




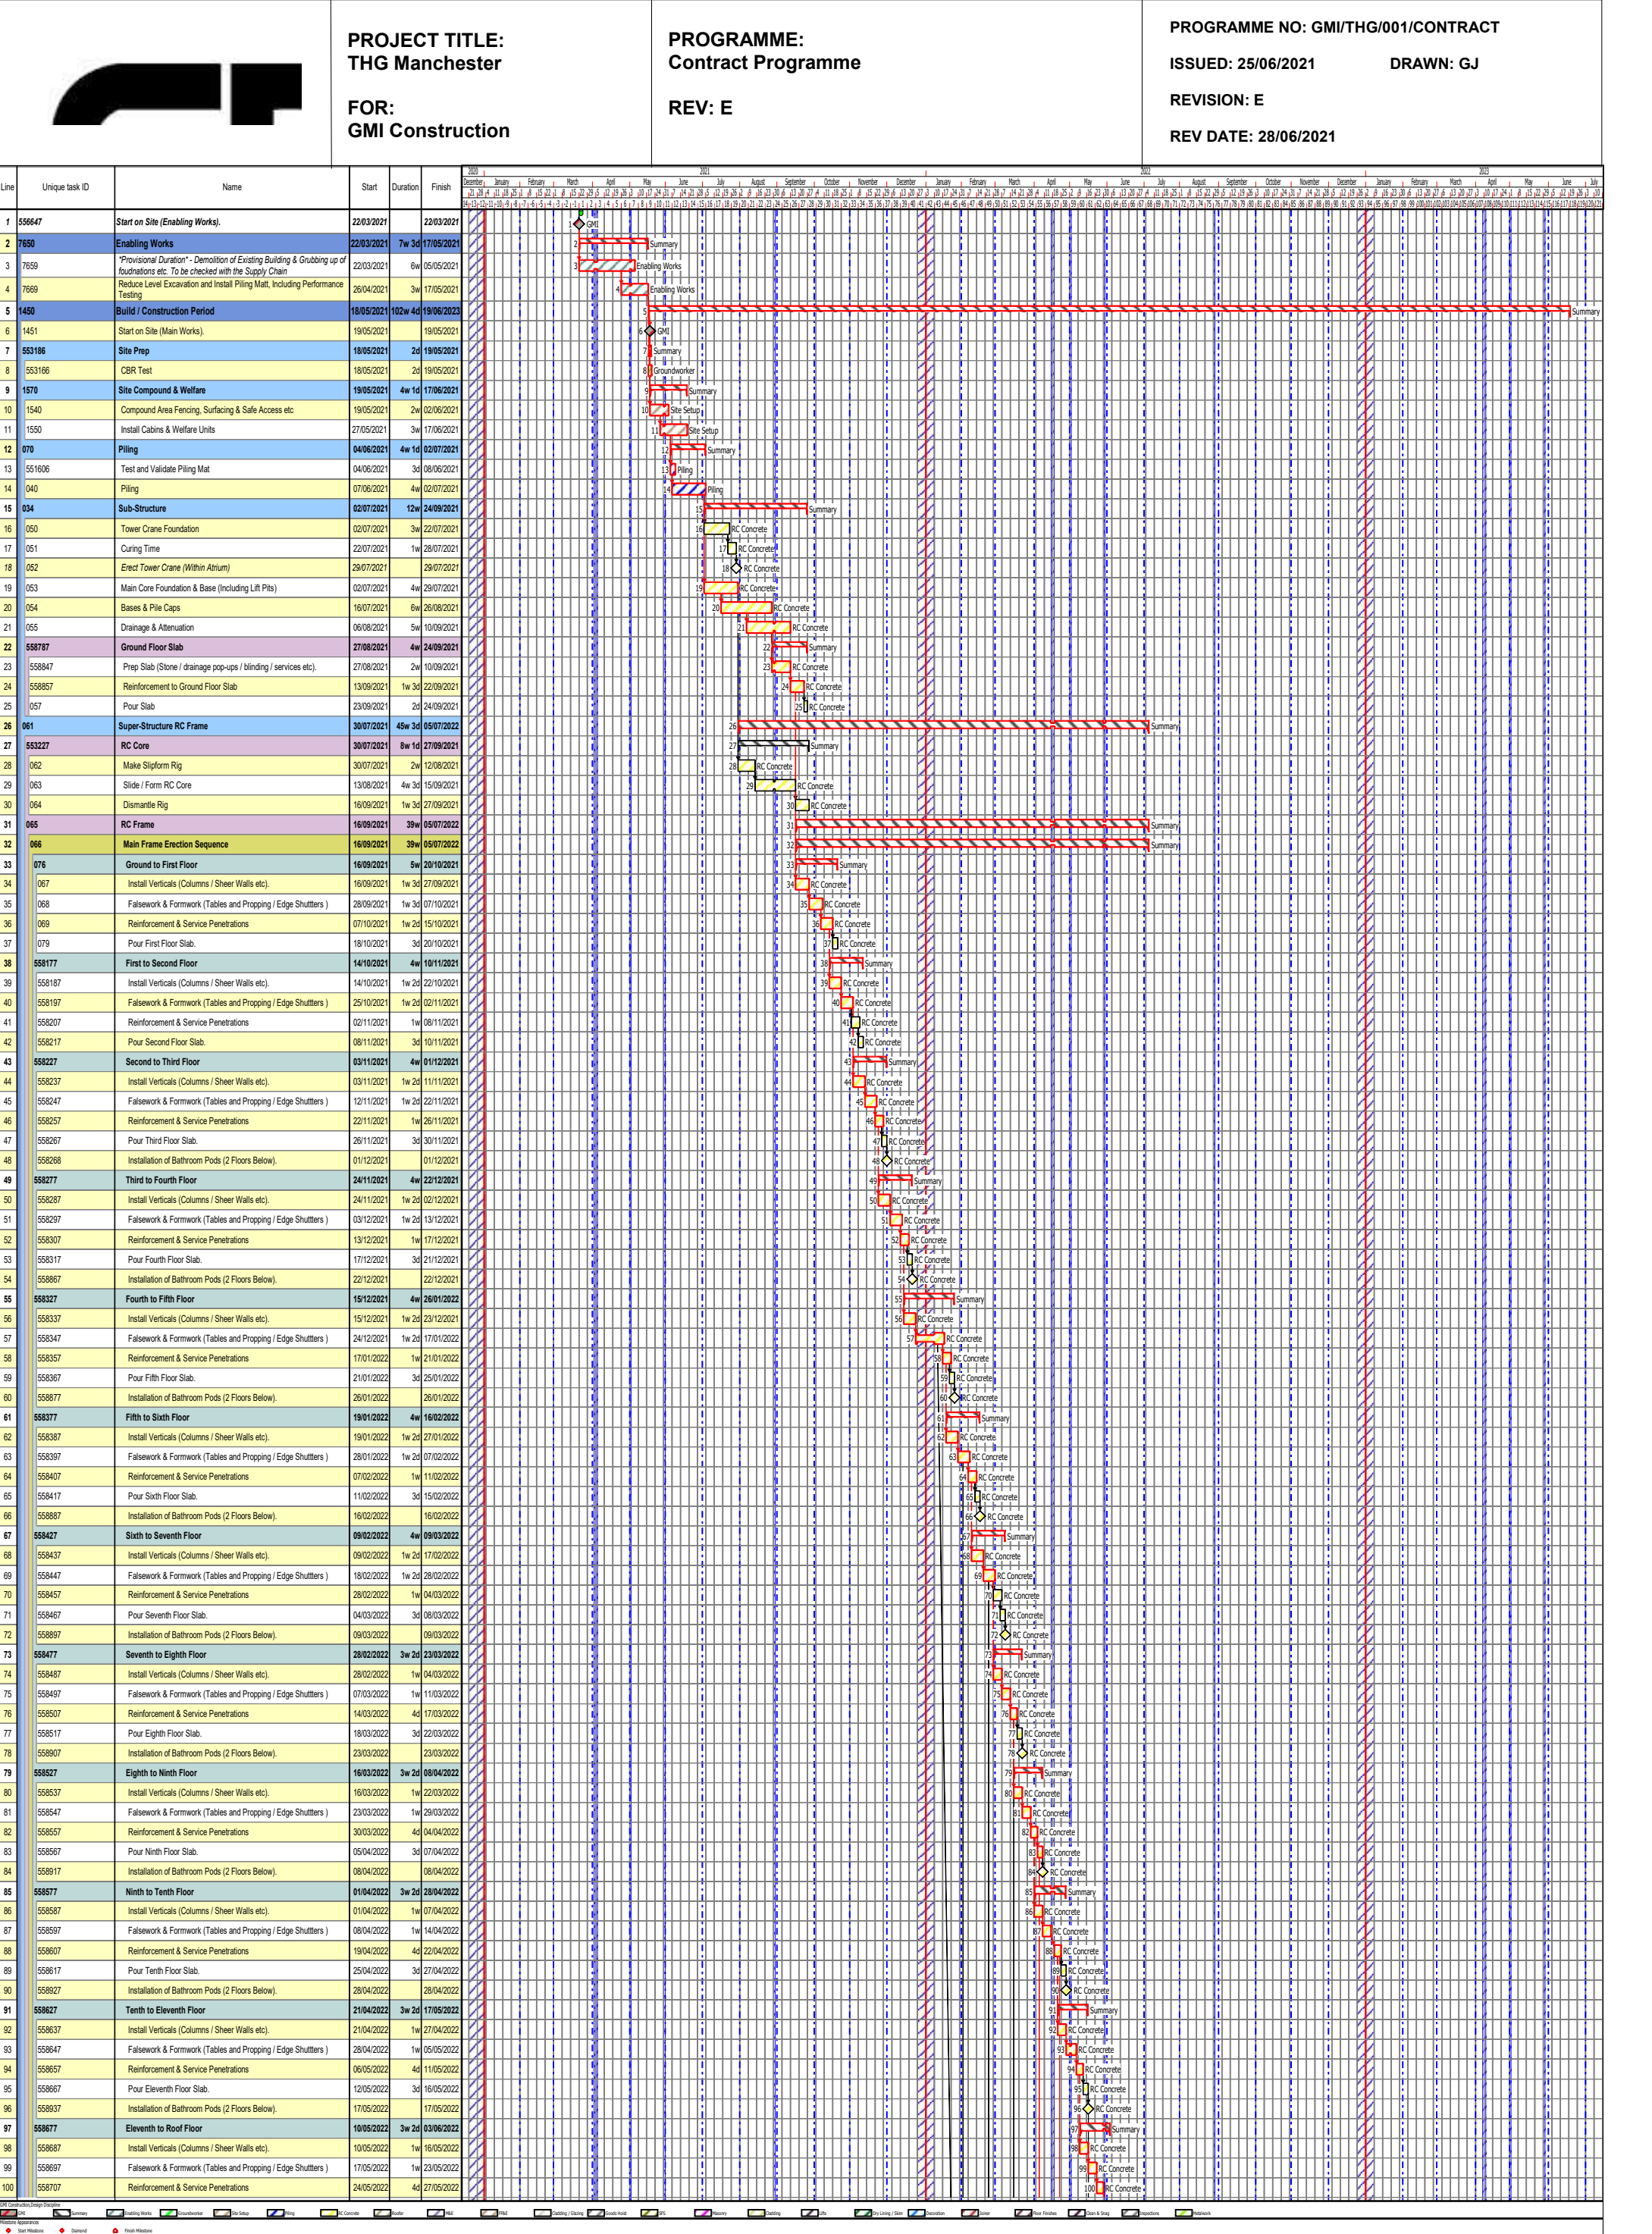

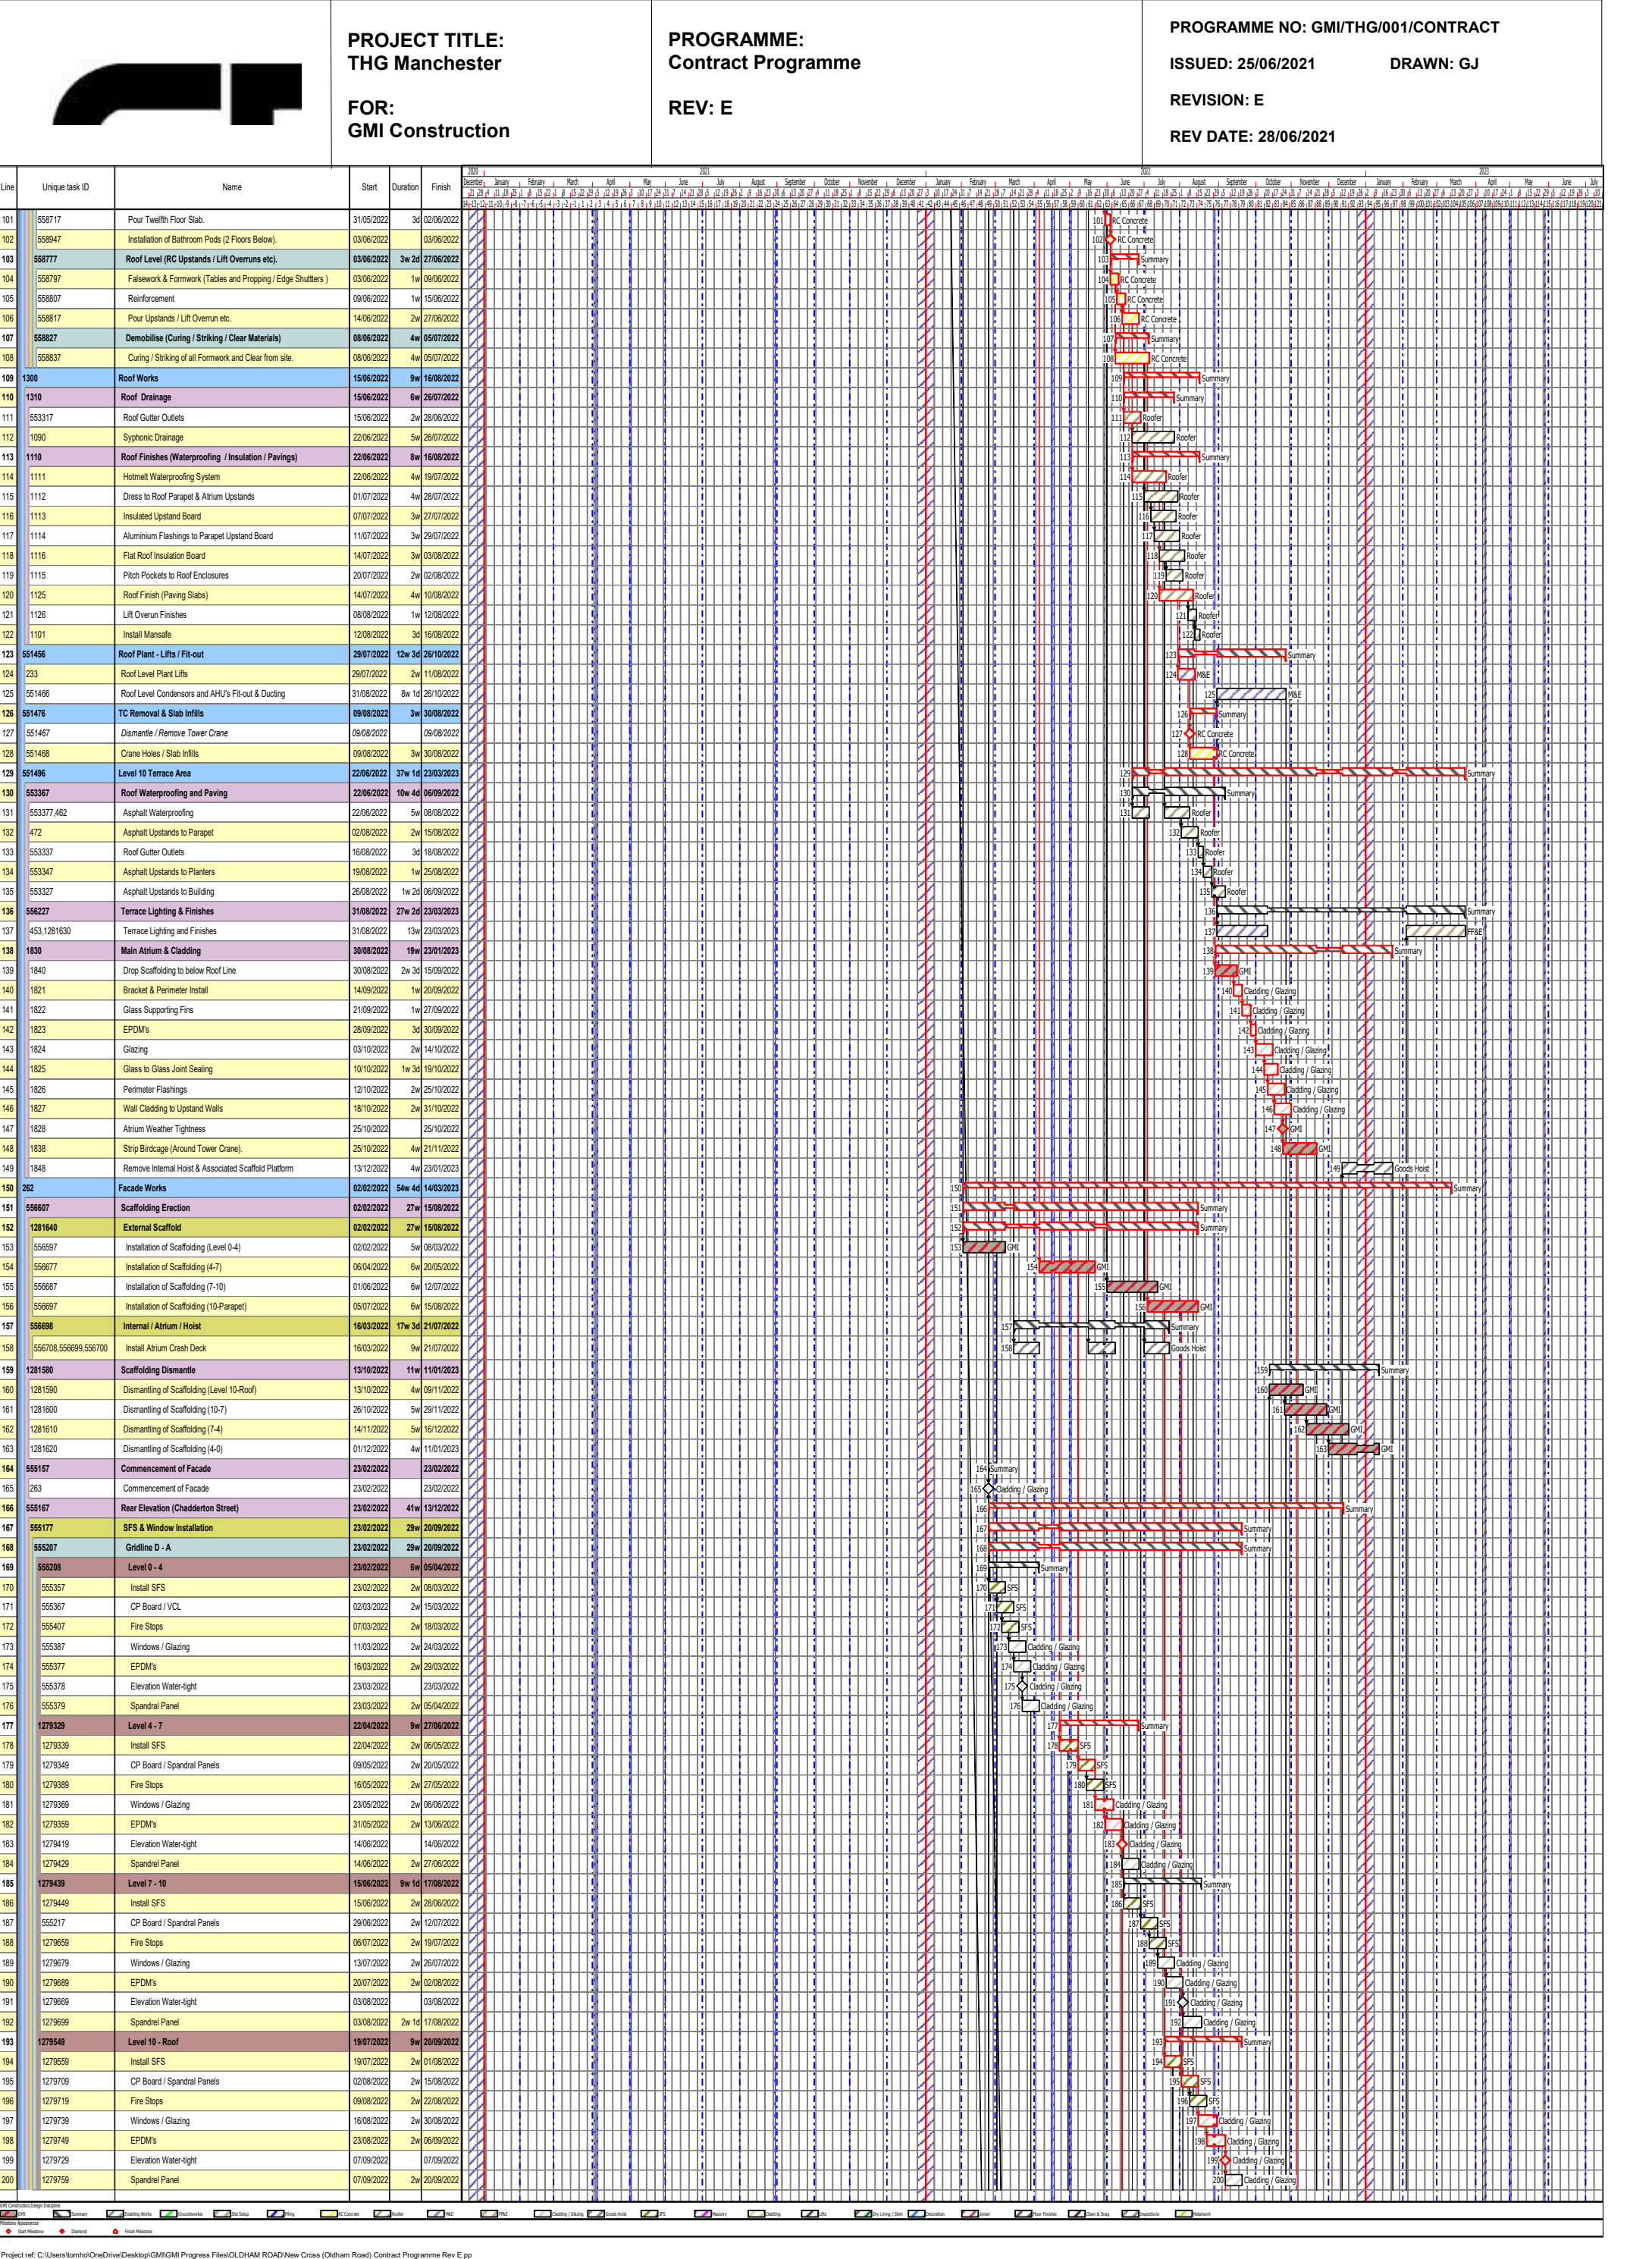

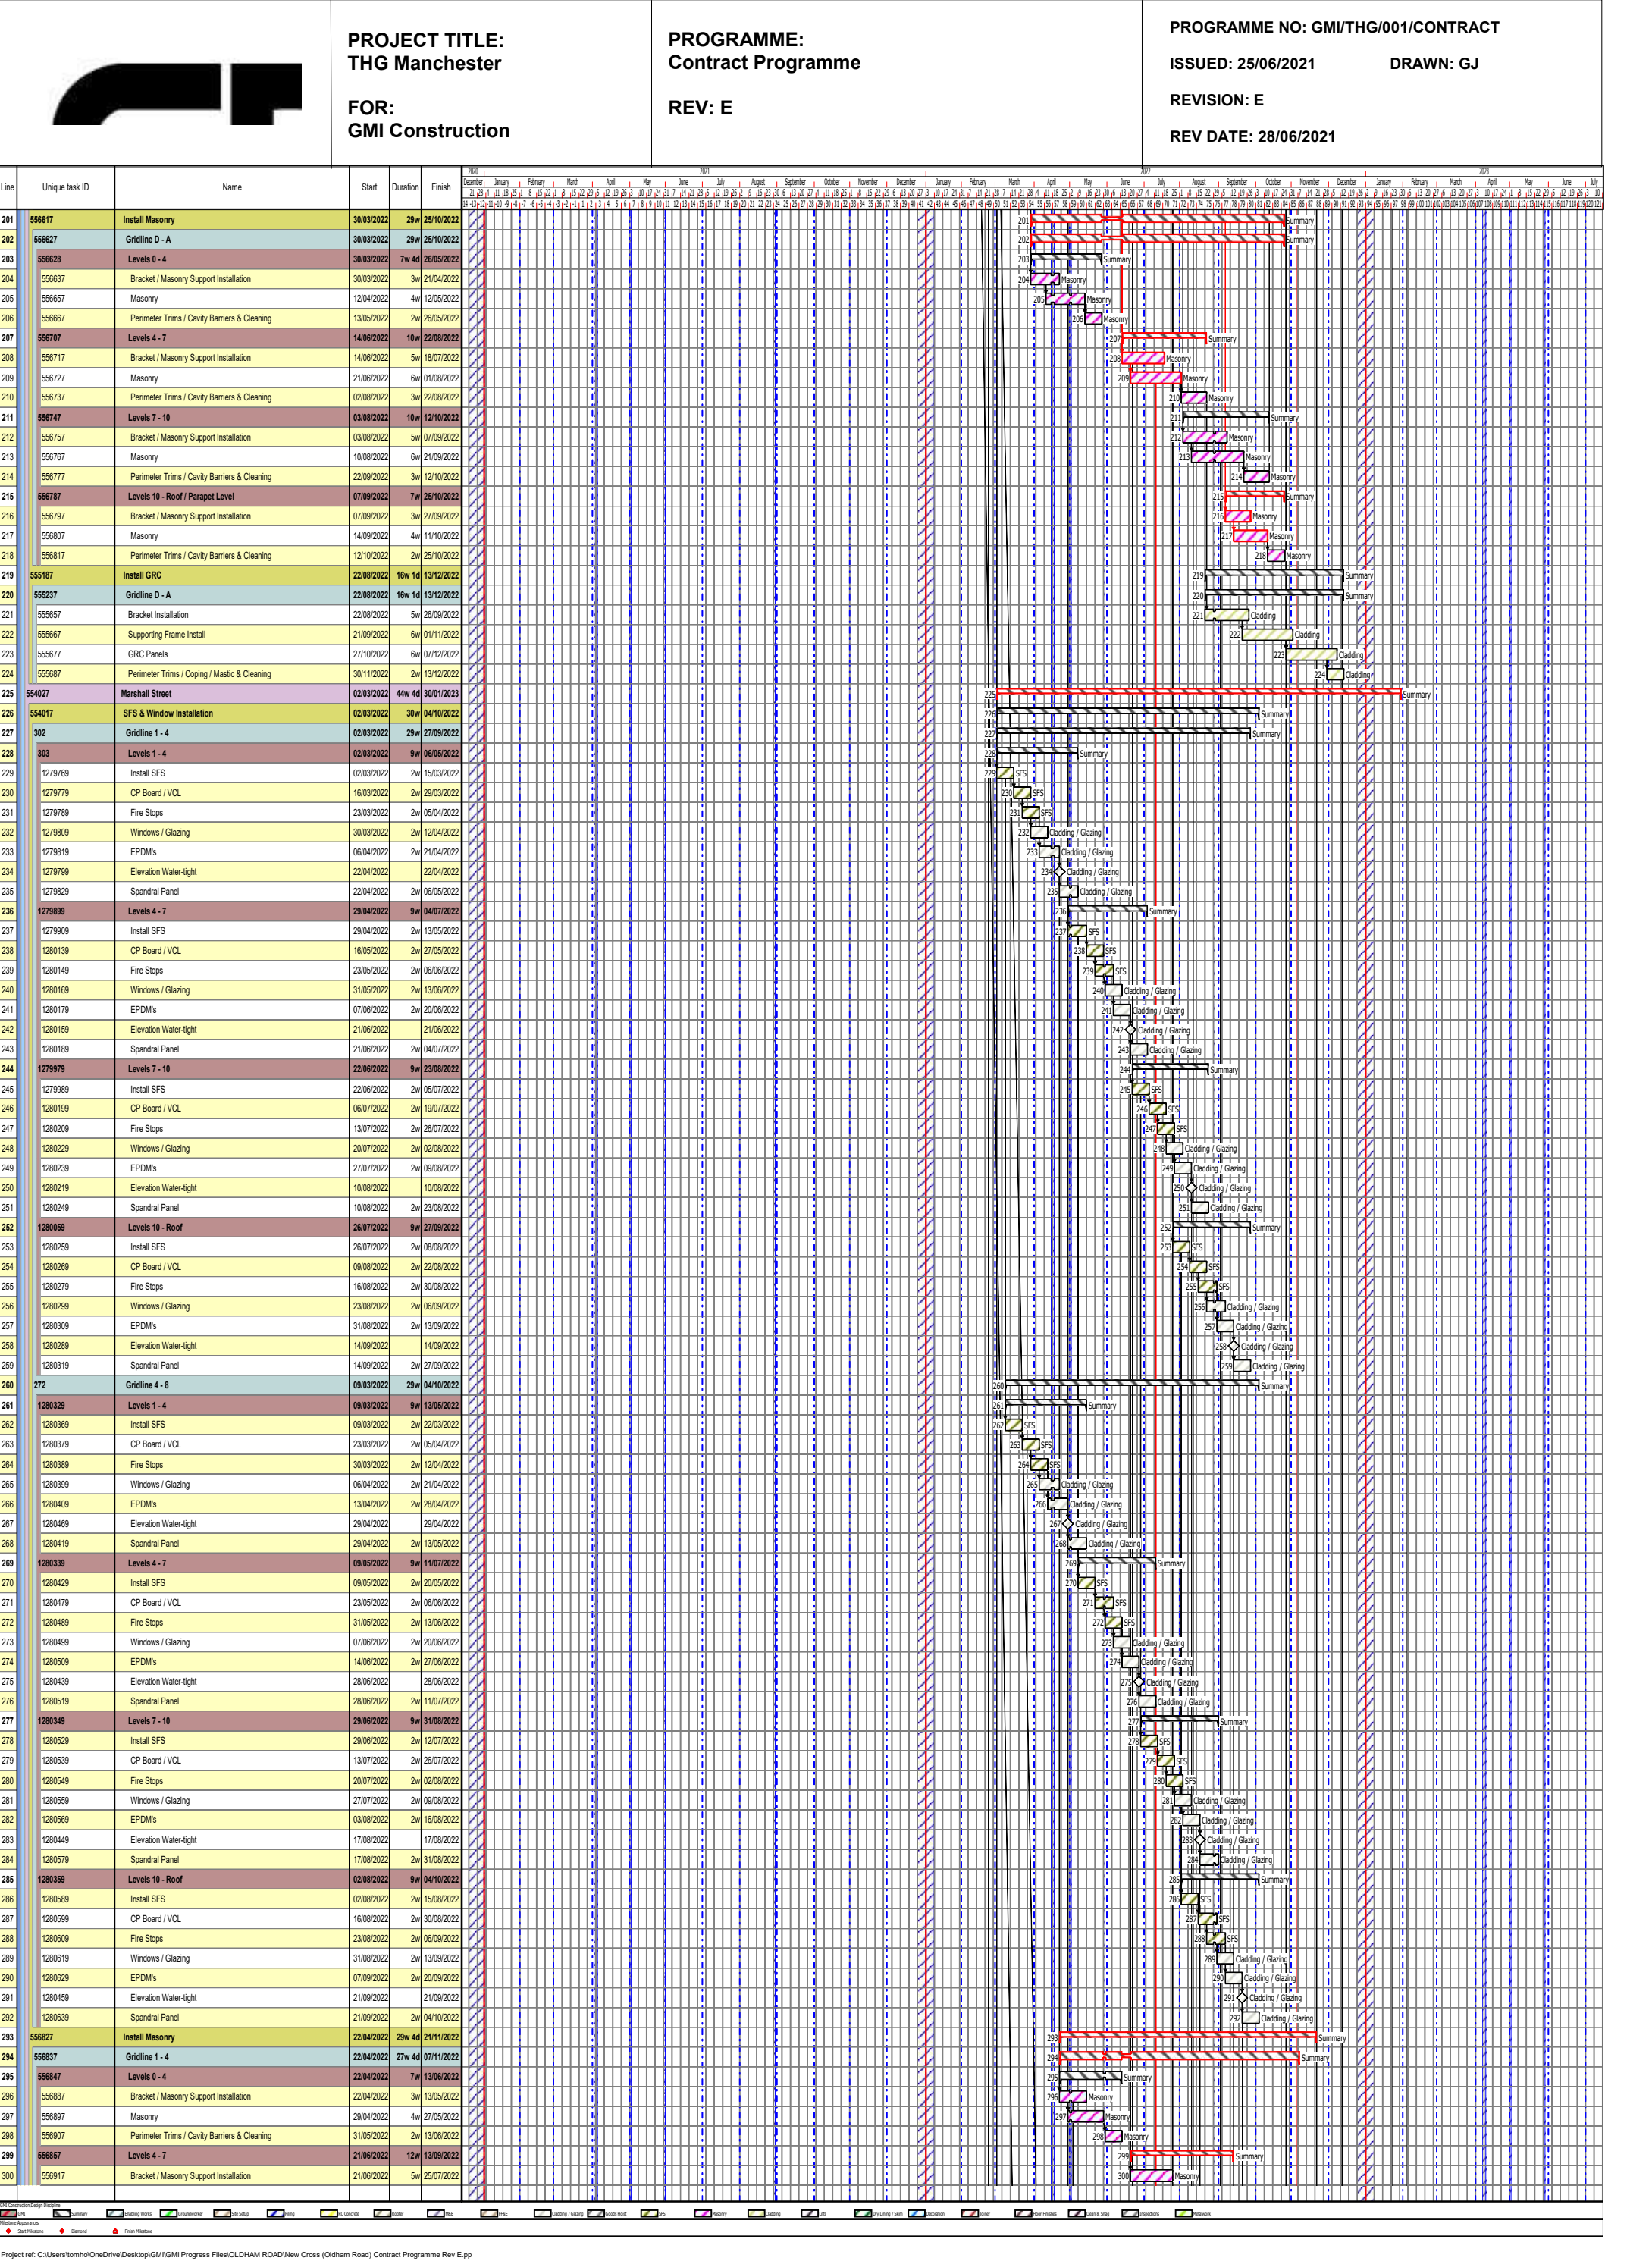

FOR:
GMI Construction

REV: E

[illegible]





PROGRAMME:
Contract Programme


REV: E


PROGRAMME NO: GMI/THG/001/CONTRACT
ISSUED: 25/06/2021 **DRAWN: GJ**
REVISION: E
REV DATE: 28/06/2021

Project ref: C:\Users\ltonhol\OneDrive\Desktop\GMI\GMI Progress Files\OLDHAM ROAD\New Cross (Oldham Road) Contract Programme Rev E.pp

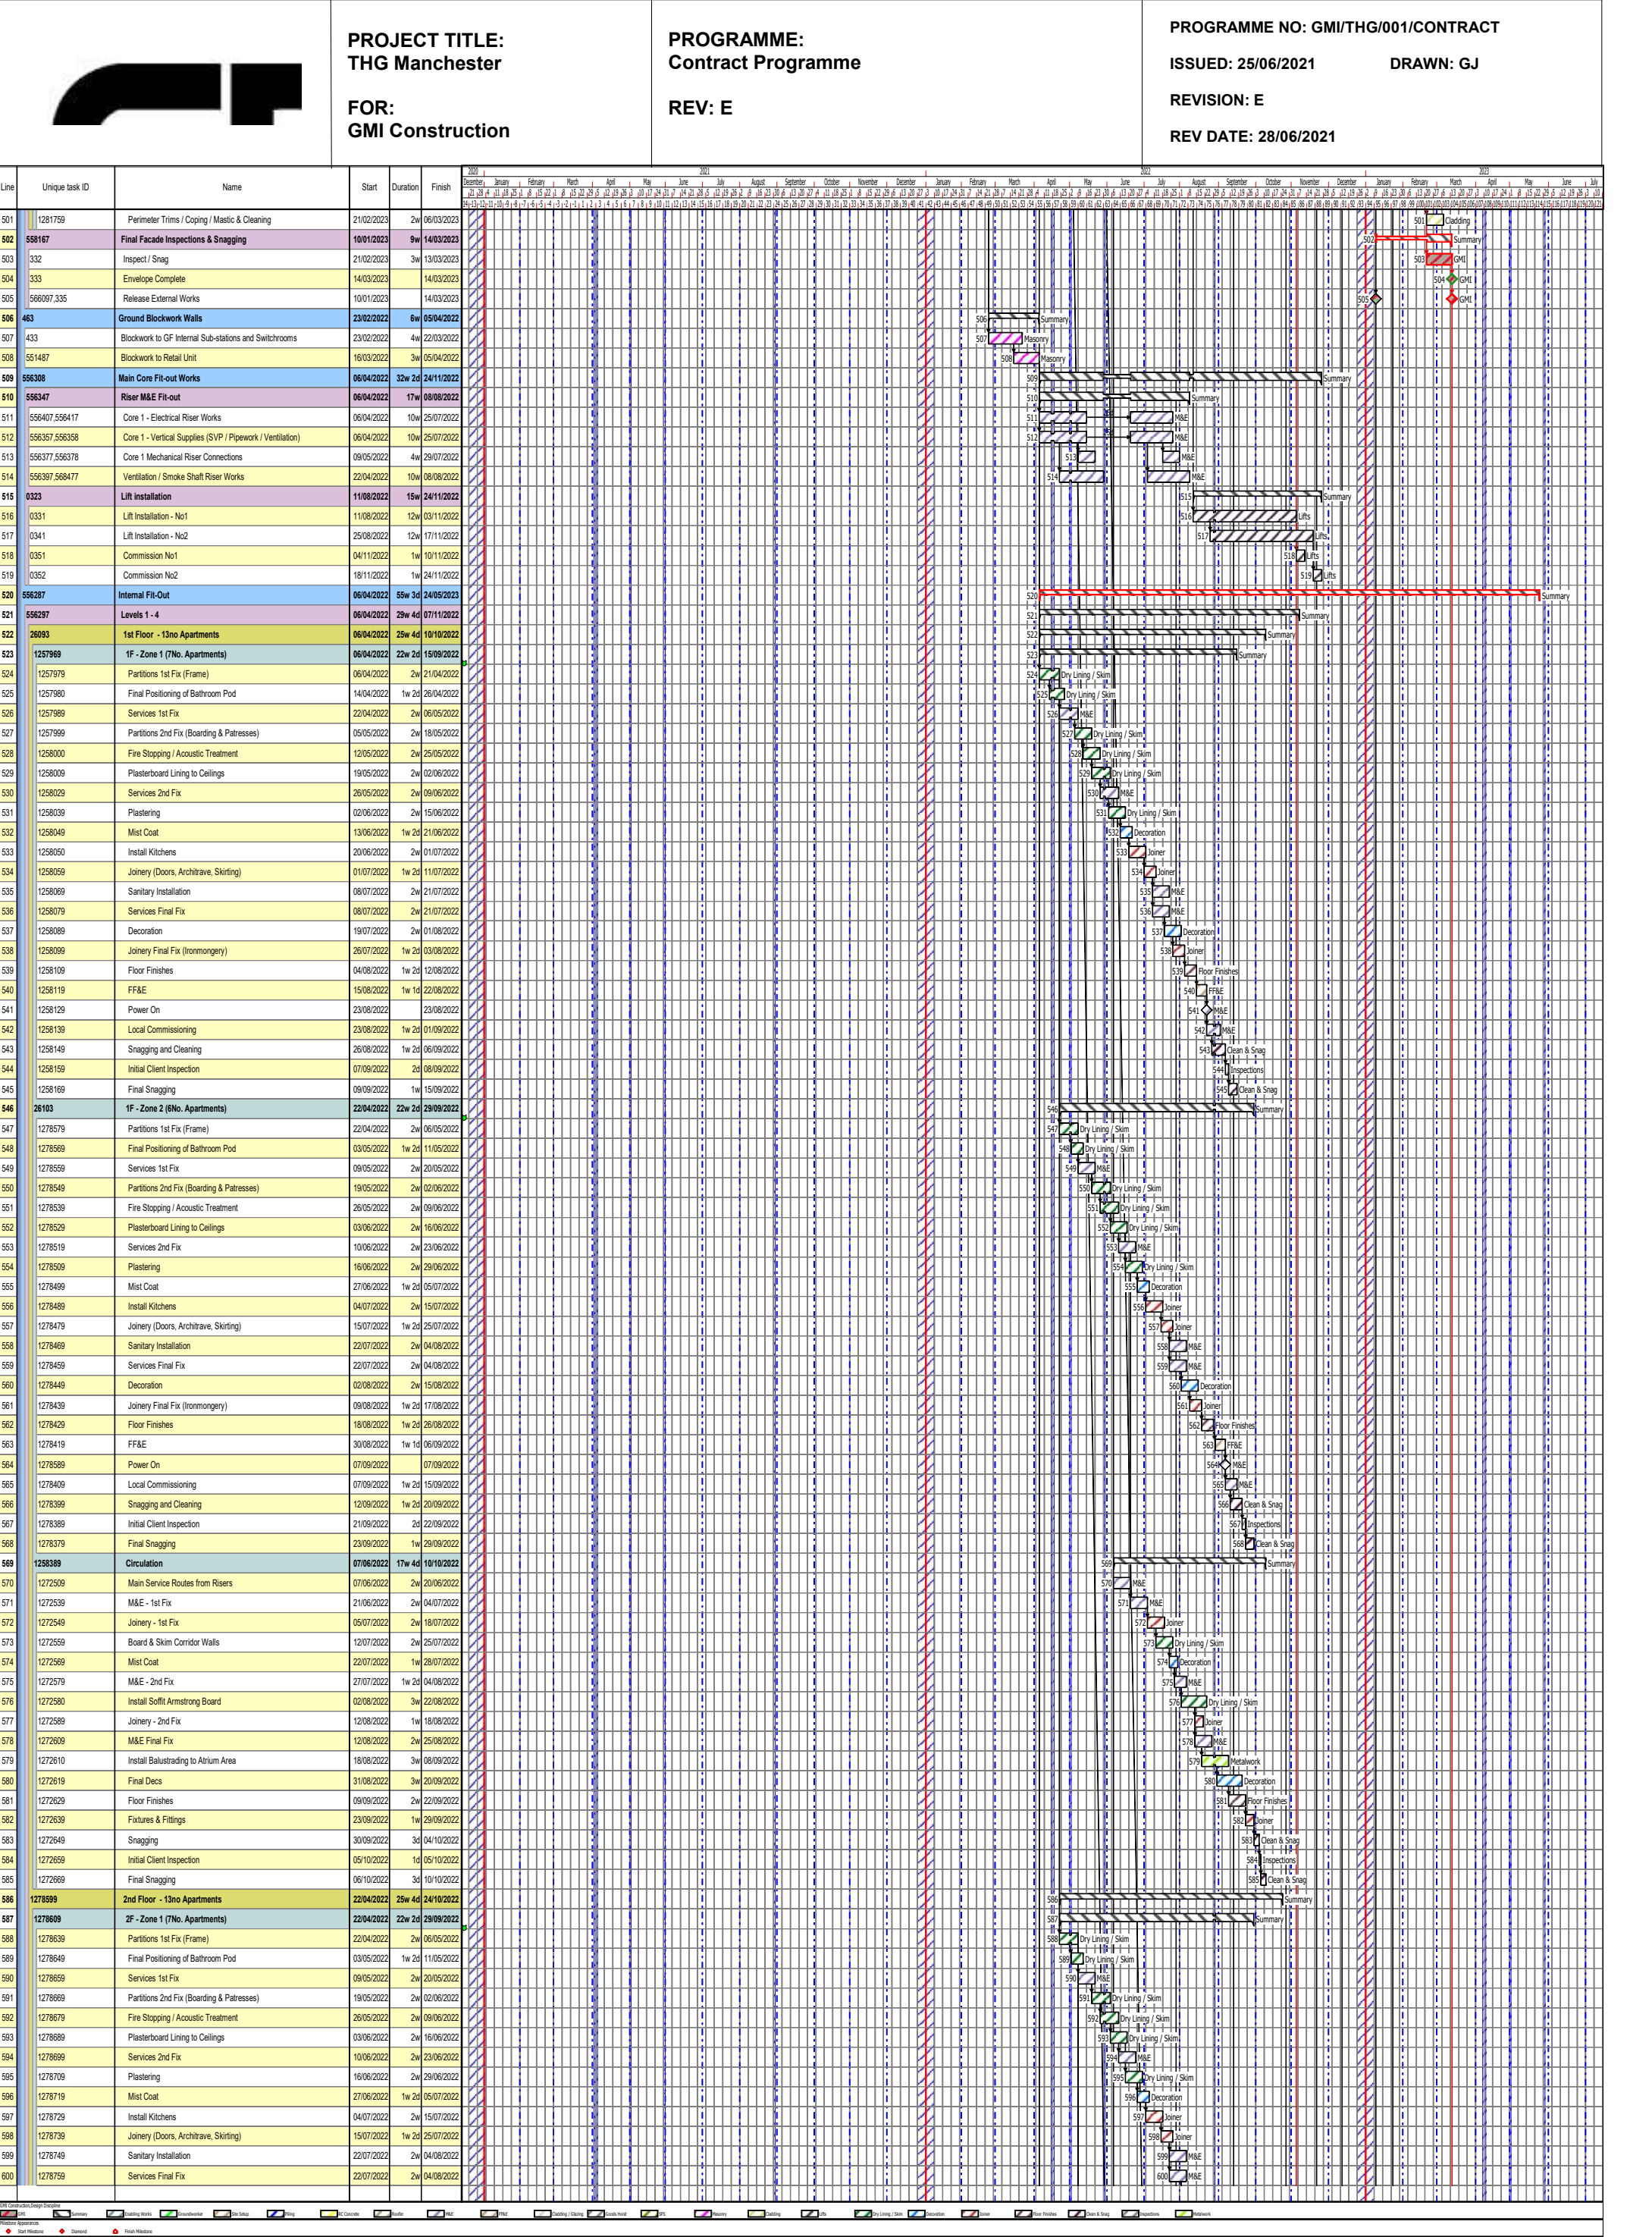

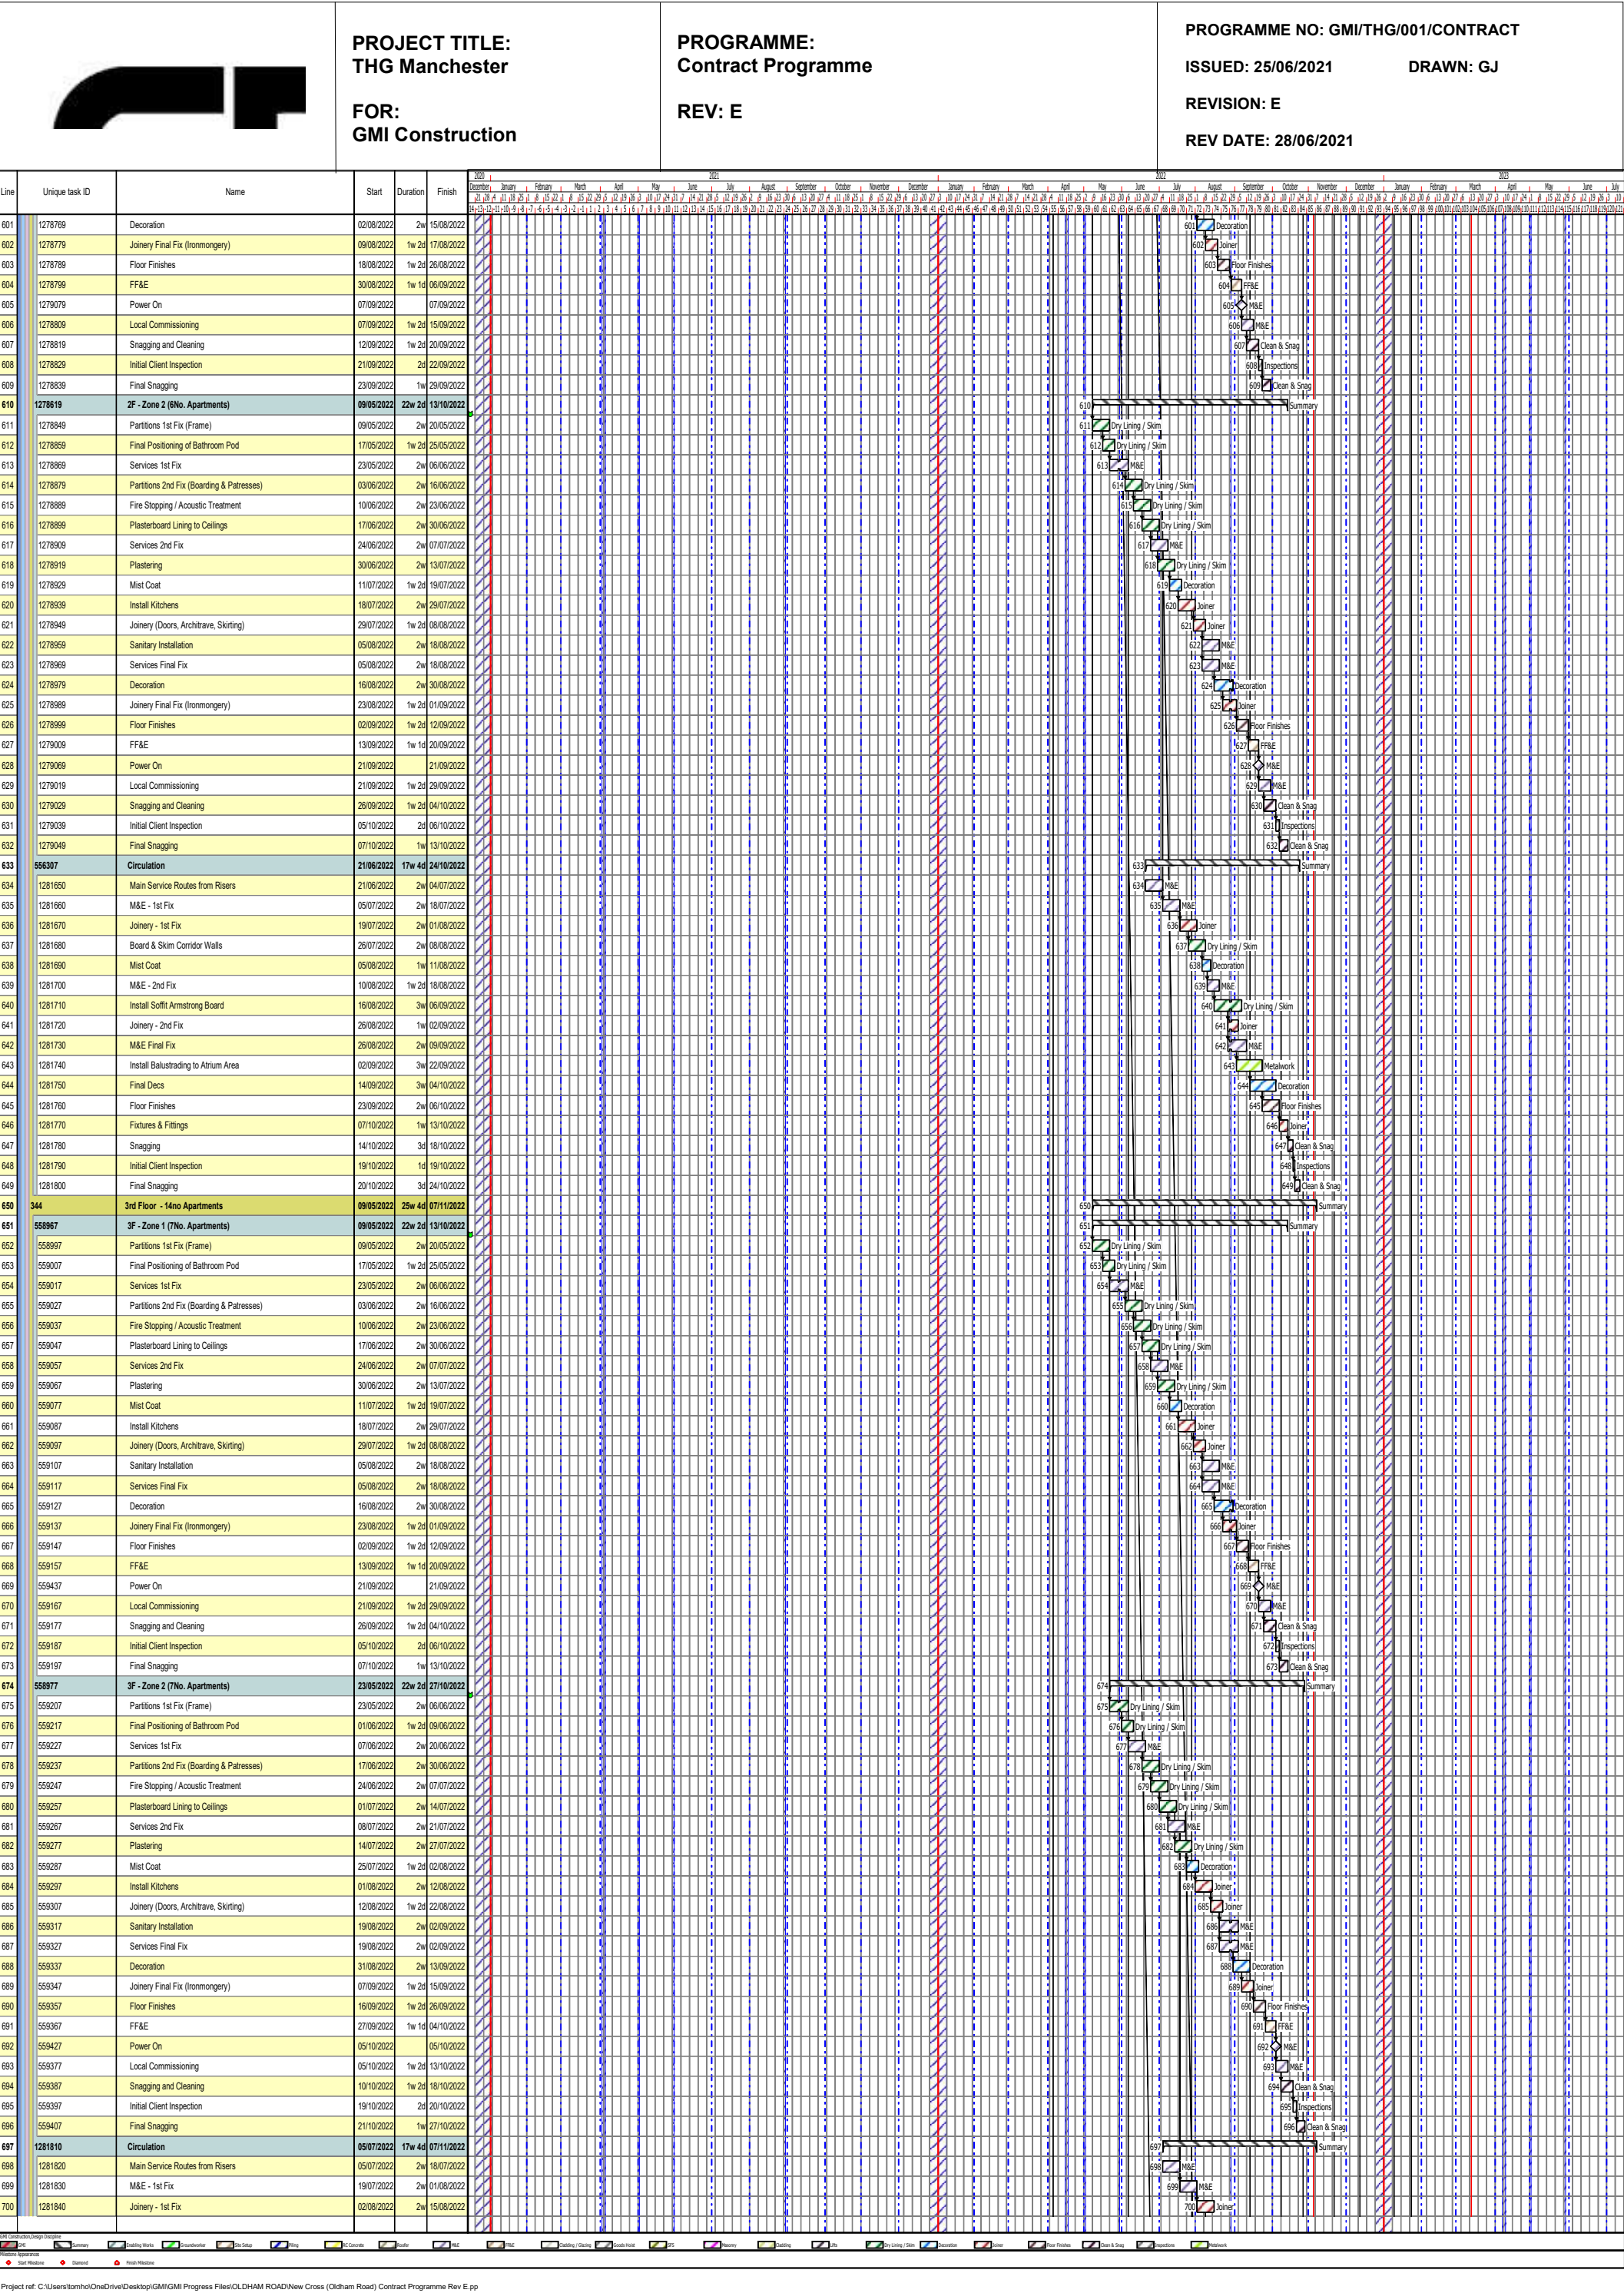

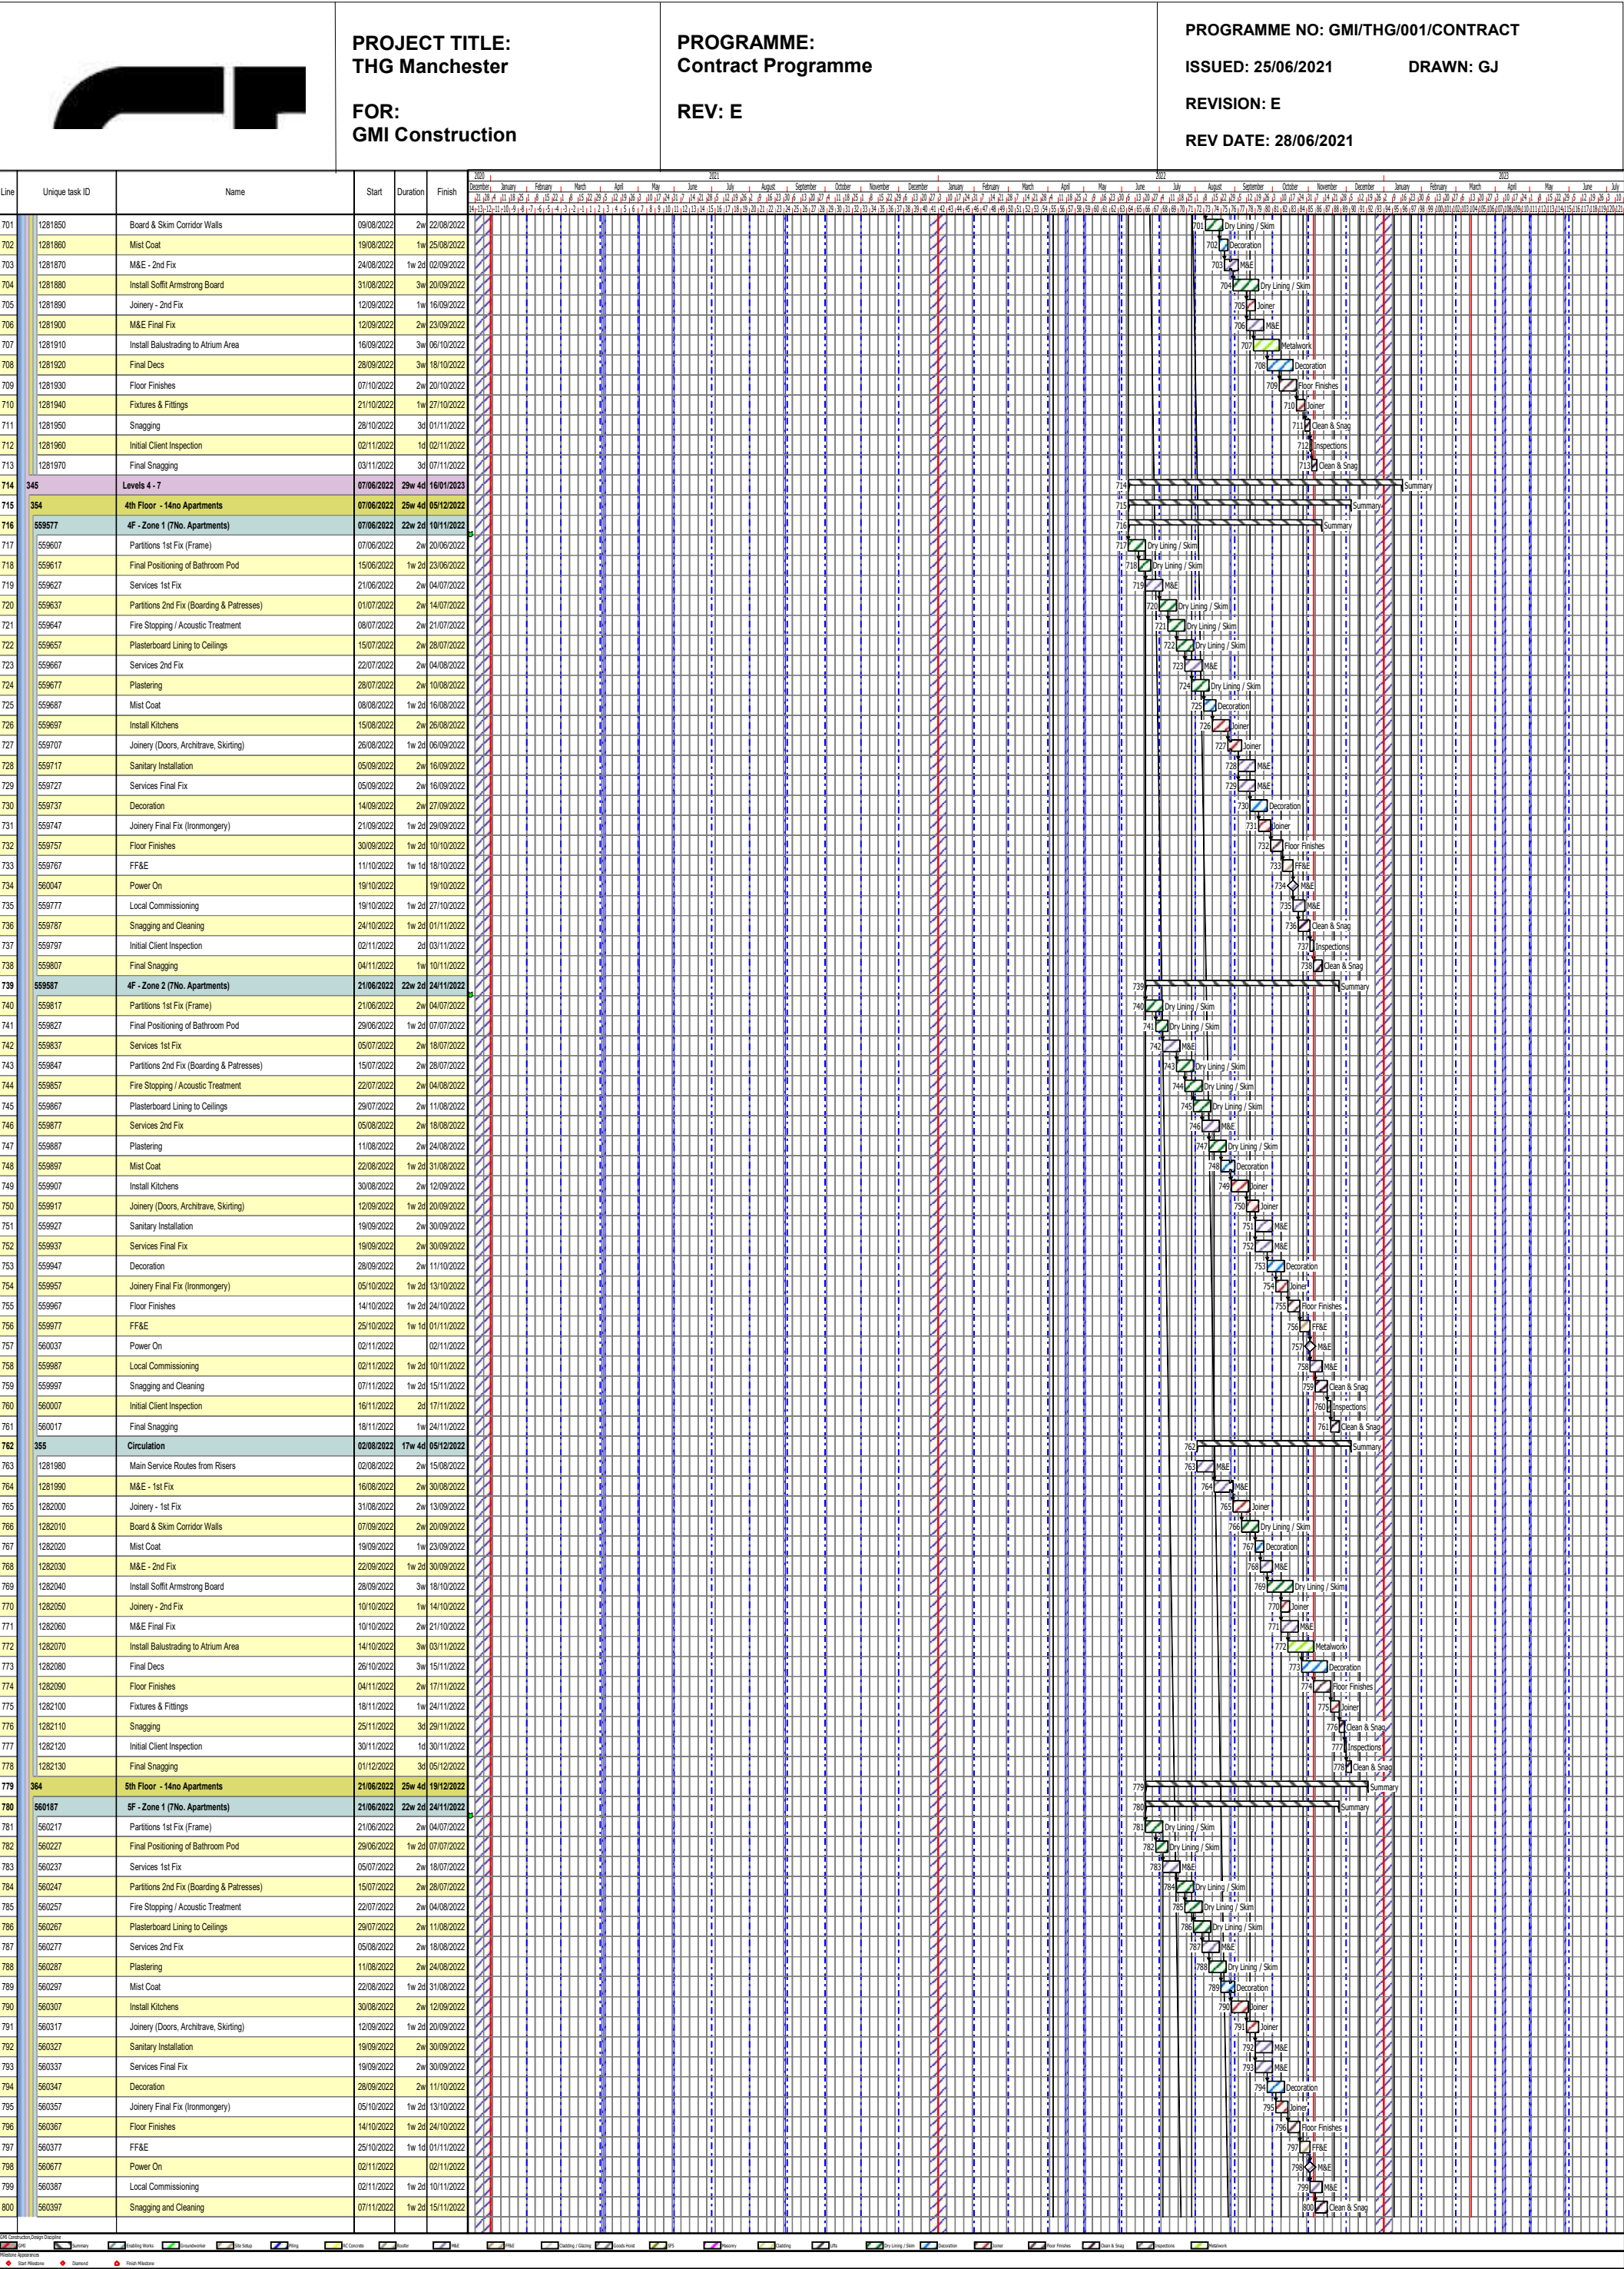


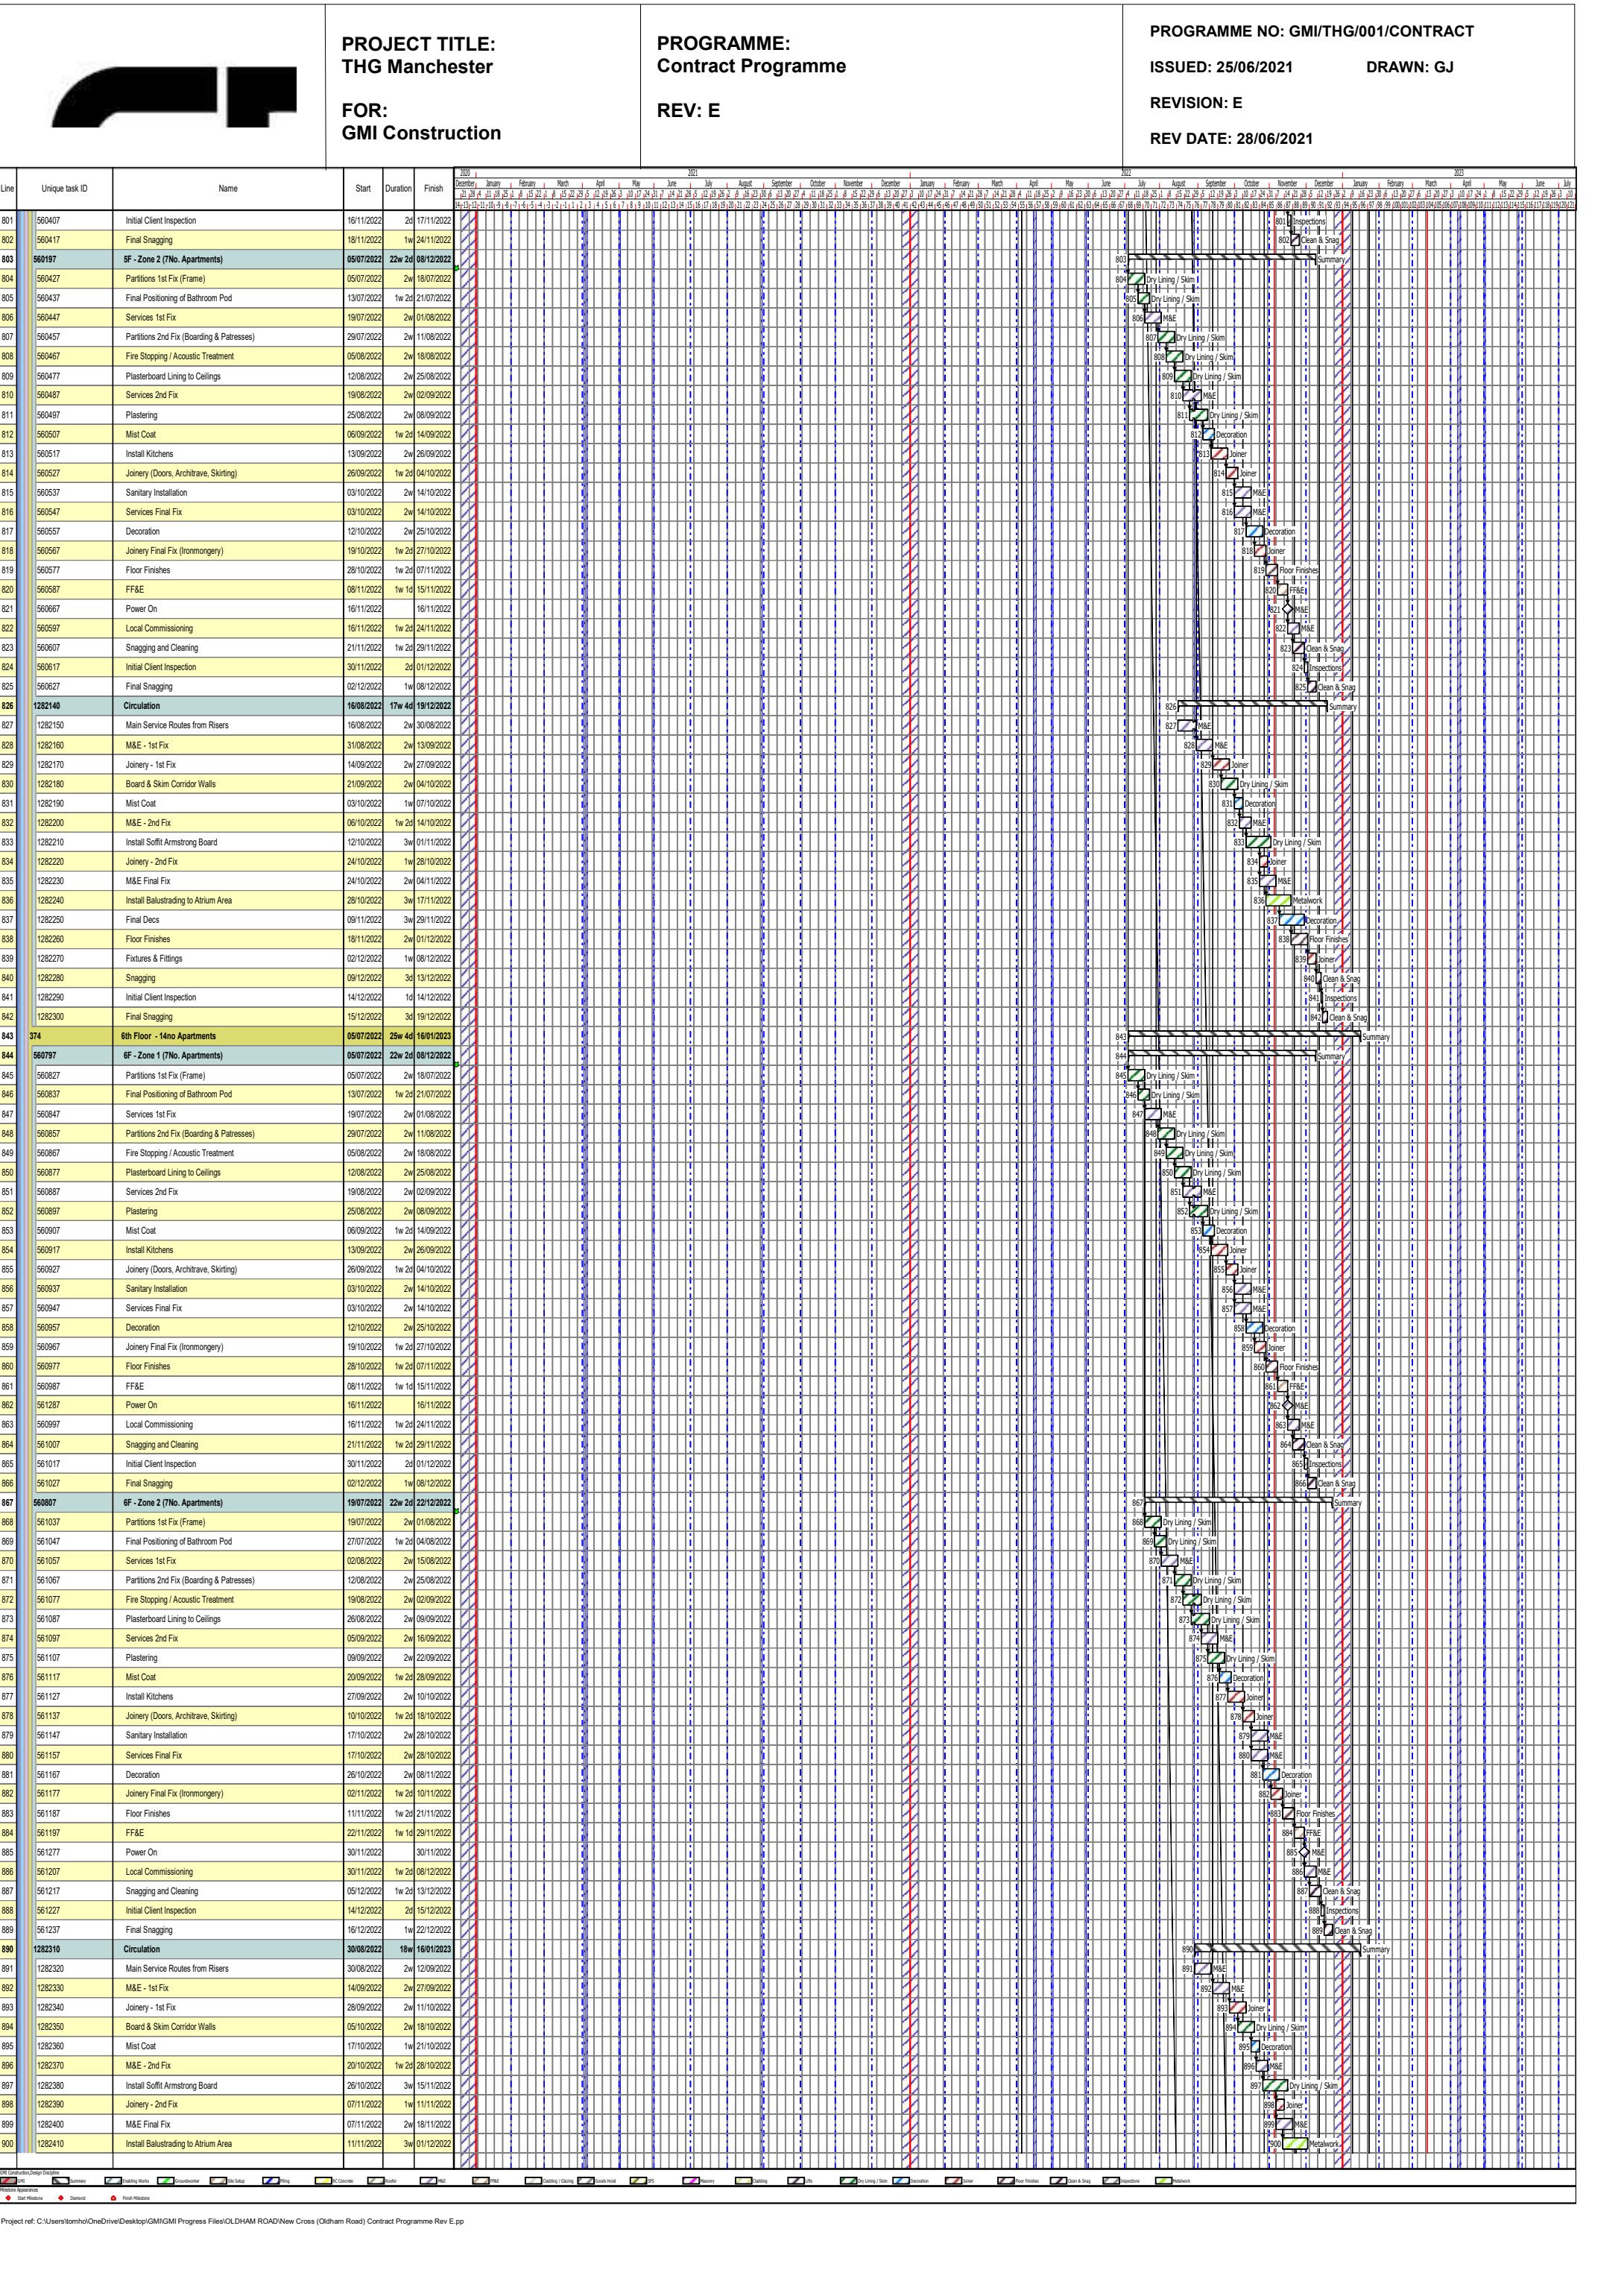





			2020												2021												2022												2023											
			December	January	February	March	April	May	June	July	August	September	October	November	December	January	February	March	April	May	June	July	August	September	October	November	December	January	February	March	April	May	June	July																
Unique task ID	Name	Start	Duration	Finish																																														
901	1282420	Final Decs	23/11/2022	3w	13/12/2022																																													
902	1282430	Floor Finishes	02/12/2022	2w	15/12/2022																																													
903	1282440	Fixtures & Fittings	16/12/2022	1w	22/12/2022																																													
904	1282450	Snagging	23/12/2022	3d	10/01/2023																																													
905	1282460	Initial Client Inspection	11/01/2023	1d	11/01/2023																																													
906	1282470	Final Snagging	12/01/2023	3d	16/01/2023																																													
907	375	Levels 7 - 10	28/07/2022	29w 4d	08/03/2023																																													
908	384	7th Floor - 14no Apartments	28/07/2022	25w 3d	07/02/2023																																													
909	561407	7F - Zone 1 (7No. Apartments)	28/07/2022	22w 2d	16/01/2023																																													
910	561437	Partitions 1st Fix (Frame)	28/07/2022	2w	10/08/2022																																													
911	561447	Final Positioning of Bathroom Pod	05/08/2022	1w 2d	15/08/2022																																													
912	561457	Services 1st Fix	11/08/2022	2w	24/08/2022																																													
913	561467	Partitions 2nd Fix (Boarding & Patresses)	23/08/2022	2w	06/09/2022																																													
914	561477	Fire Stopping / Acoustic Treatment	31/08/2022	2w	13/09/2022																																													
915	561487	Plasterboard Lining to Ceilings	07/09/2022	2w	20/09/2022																																													
916	561497	Services 2nd Fix	14/09/2022	2w	27/09/2022																																													
917	561507	Plastering	20/09/2022	2w	03/10/2022																																													
918	561517	Mist Coat	29/09/2022	1w 2d	07/10/2022																																													
919	561527	Install Kitchens	06/10/2022	2w	19/10/2022																																													
920	561537	Joinery (Doors, Architrave, Skirting)	19/10/2022	1w 2d	27/10/2022																																													
921	561547	Sanitary Installation	26/10/2022	2w	08/11/2022																																													
922	561557	Services Final Fix	26/10/2022	2w	08/11/2022																																													
923	561567	Decoration	04/11/2022	2w	17/11/2022																																													
924	561577	Joinery Final Fix (Ironmongery)	11/11/2022	1w 2d	21/11/2022																																													
925	561587	Floor Finishes	22/11/2022	1w 2d	30/11/2022																																													
926	561597	FF&E	01/12/2022	1w 1d	08/12/2022																																													
927	561897	Power On	09/12/2022		09/12/2022																																													
928	561607	Local Commissioning	09/12/2022	1w 2d	19/12/2022																																													
929	561617	Snagging and Cleaning	14/12/2022	1w 2d	22/12/2022																																													
930	561627	Initial Client Inspection	23/12/2022	2d	09/01/2023																																													
931	561637	Final Snagging	10/01/2023	1w	16/01/2023																																													
932	561417	7F - Zone 2 (7No. Apartments)	11/08/2022	22w 2d	30/01/2023																																													
933	561647	Partitions 1st Fix (Frame)	11/08/2022	2w	24/08/2022																																													
934	561657	Final Positioning of Bathroom Pod	19/08/2022	1w 2d	30/08/2022																																													
935	561667	Services 1st Fix	25/08/2022	2w	08/09/2022																																													
936	561677	Partitions 2nd Fix (Boarding & Patresses)	07/09/2022	2w	20/09/2022																																													
937	561687	Fire Stopping / Acoustic Treatment	14/09/2022	2w	27/09/2022																																													
938	561697	Plasterboard Lining to Ceilings	21/09/2022	2w	04/10/2022																																													
939	561707	Services 2nd Fix	28/09/2022	2w	11/10/2022																																													
940	561717	Plastering	04/10/2022	2w	17/10/2022																																													
941	561727	Mist Coat	13/10/2022	1w 2d	21/10/2022																																													
942	561737	Install Kitchens	20/10/2022	2w	02/11/2022																																													
943	561747	Joinery (Doors, Architrave, Skirting)	02/11/2022	1w 2d	10/11/2022																																													
944	561757	Sanitary Installation	09/11/2022	2w	22/11/2022																																													
945	561767	Services Final Fix	09/11/2022	2w	22/11/2022																																													
946	561777	Decoration	18/11/2022	2w	01/12/2022																																													
947	561787	Joinery Final Fix (Ironmongery)	25/11/2022	1w																																														

REV DATE: 28/06/2021



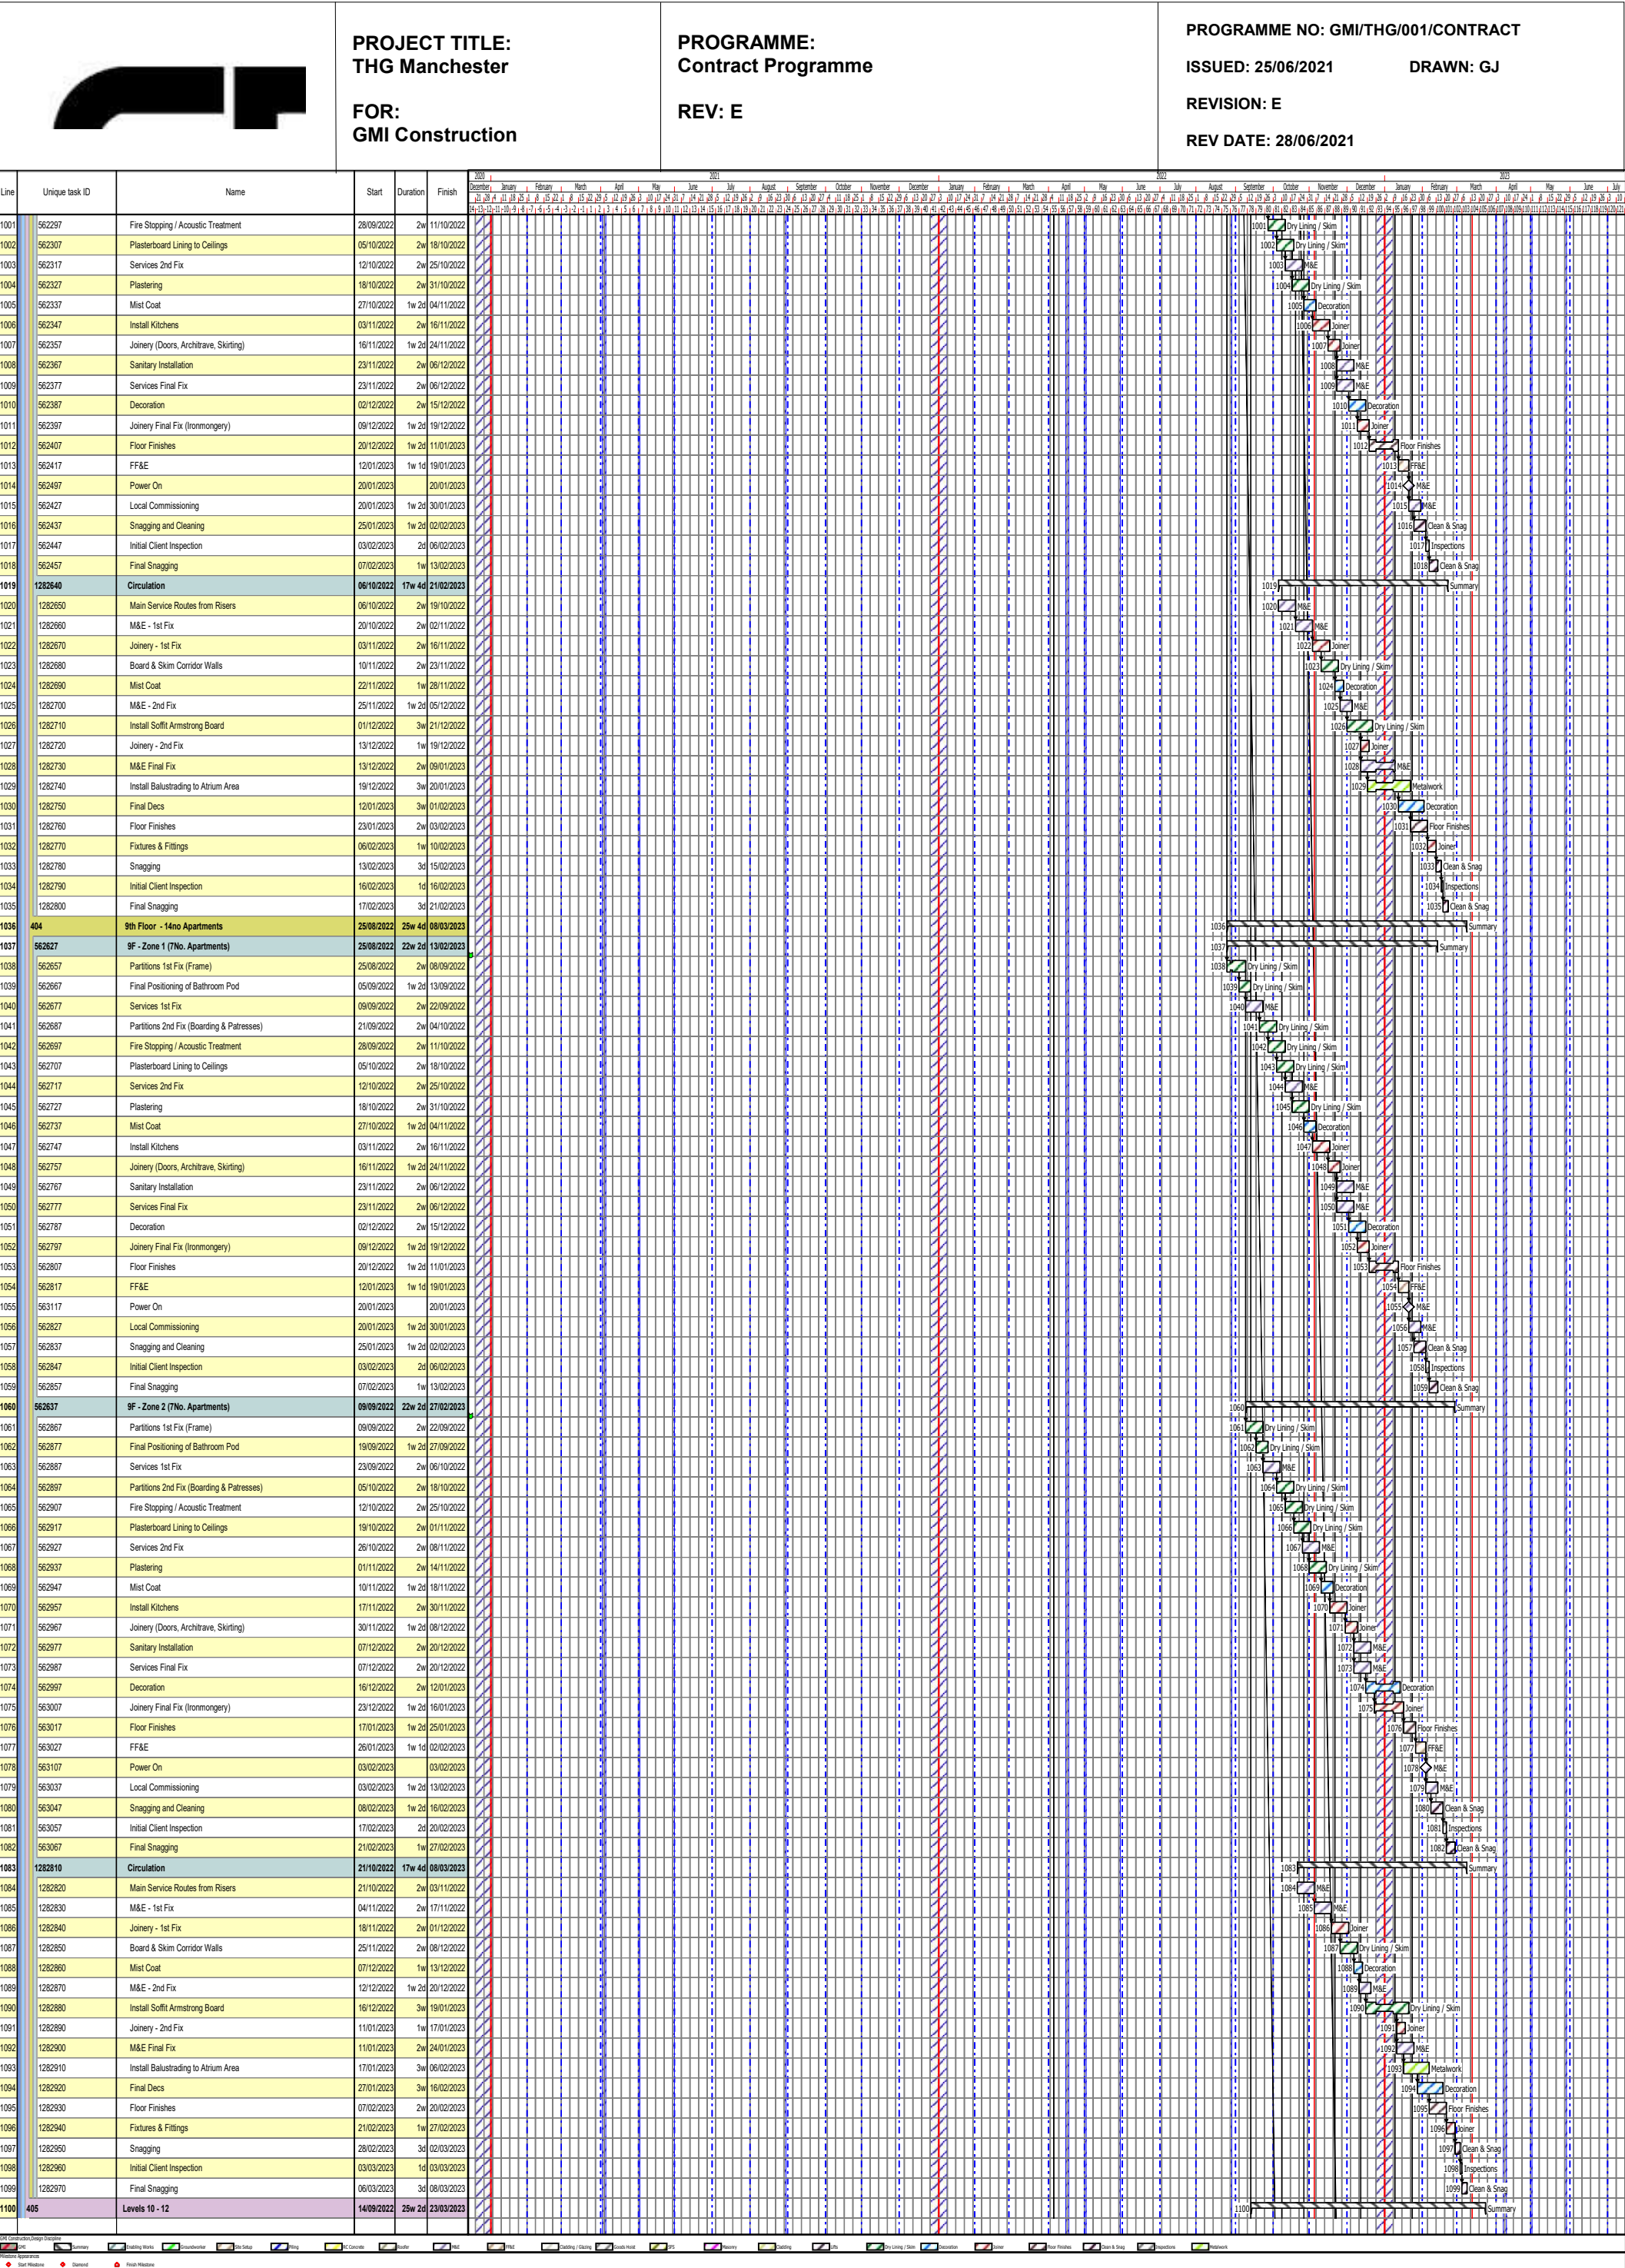

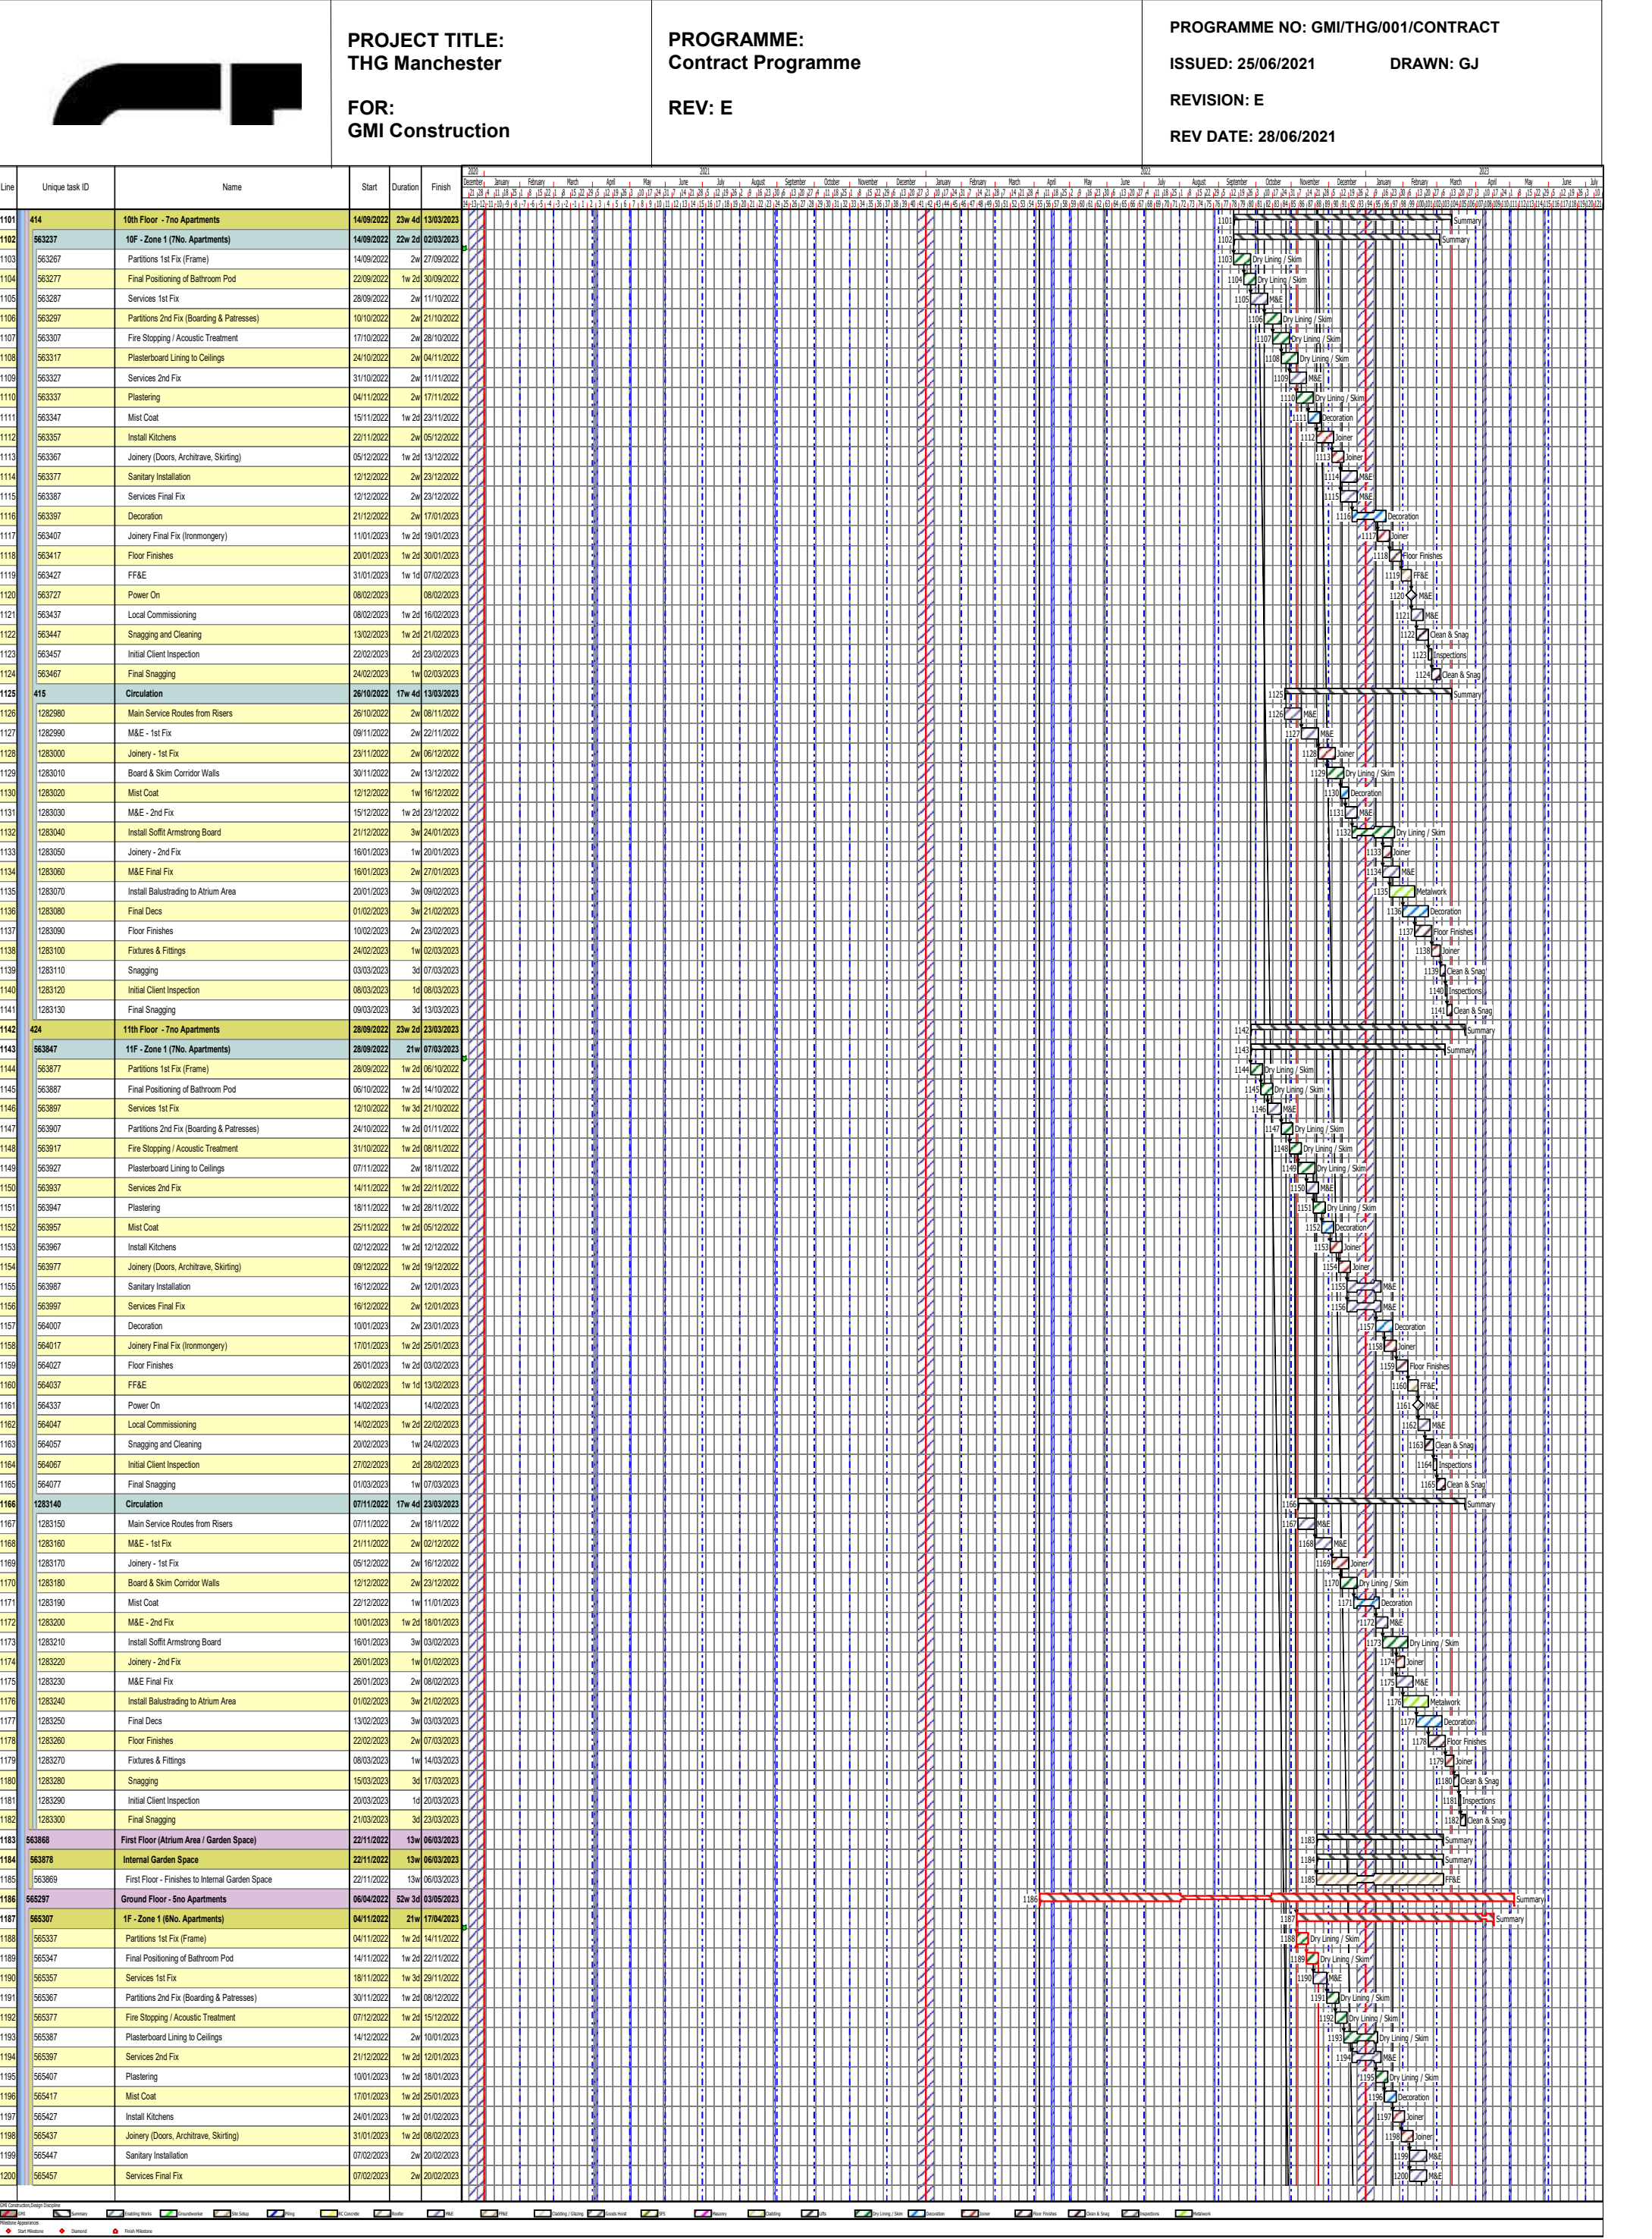



	PROJECT TITLE: THG Manchester	PROGRAMME: Contract Programme	PROGRAMME NO: GMI/THG/001/CONTRACT
	FOR: GMI Construction	REV: E	ISSUED: 25/06/2021 DRAWN: GJ
			REVISION: E
			REV DATE: 28/06/2021

	PROJECT TITLE: THG Manchester	PROGRAMME: Contract Programme	PROGRAMME NO: GMI/THG/001/CONTRACT
	FOR: GMI Construction	REV: E	ISSUED: 25/06/2021 DRAWN: GJ
			REVISION: E
			REV DATE: 28/06/2021

	PROJECT TITLE: THG Manchester	PROGRAMME: Contract Programme	PROGRAMME NO: GMI/THG/001/CONTRACT
	FOR: GMI Construction	REV: E	ISSUED: 25/06/2021 DRAWN: GJ
			REVISION: E
			REV DATE: 28/06/2021

	PROJECT TITLE: THG Manchester	PROGRAMME: Contract Programme	PROGRAMME NO: GMI/THG/001/CONTRACT
	FOR: GMI Construction	REV: E	ISSUED: 25/06/2021 DRAWN: GJ
			REVISION: E
			REV DATE: 28/06/2021

	PROJECT TITLE: THG Manchester	PROGRAMME: Contract Programme	PROGRAMME NO: GMI/THG/001/CONTRACT
	FOR: GMI Construction	REV: E	ISSUED: 25/06/2021 DRAWN: GJ
			REVISION: E
			REV DATE: 28/06/2021

	PROJECT TITLE: THG Manchester	PROGRAMME: Contract Programme	PROGRAMME NO: GMI/THG/001/CONTRACT
	FOR: GMI Construction	REV: E	ISSUED: 25/06/2021 DRAWN: GJ
			REVISION: E
			REV DATE: 28/06/2021

	PROJECT TITLE: THG Manchester	PROGRAMME: Contract Programme	PROGRAMME NO: GMI/THG/001/CONTRACT
	FOR: GMI Construction	REV: E	ISSUED: 25/06/2021 DRAWN: GJ
			REVISION: E
			REV DATE: 28/06/2021

	PROJECT TITLE: THG Manchester	PROGRAMME: Contract Programme	PROGRAMME NO: GMI/THG/001/CONTRACT
	FOR: GMI Construction	REV: E	ISSUED: 25/06/2021 DRAWN: GJ
			REVISION: E
			REV DATE: 28/06/2021

	PROJECT TITLE: THG Manchester	PROGRAMME: Contract Programme	PROGRAMME NO: GMI/THG/001/CONTRACT
	FOR: GMI Construction	REV: E	ISSUED: 25/06/2021 DRAWN: GJ
			REVISION: E
			REV DATE: 28/06/2021

[illegible]
