



Premier Inn Manchester West Didsbury
CONSTRUCTION MANAGEMENT PLAN

on behalf of Whitbread Group Plc.

2024/7847/CMP02

September 2025

www.rgp.co.uk

DOCUMENT CONTROL

Project: Premier Inn Manchester West Didsbury
Report Type: Construction Management Plan
Client: Whitbread Group Plc.
Reference: 2024/7847/CMP02

DOCUMENT REVIEW

Author:	SDH	Date:	08/09/2025
Checked by:	PJB	Date:	08/09/2025
Approved by:	NDR	Date:	08/09/2025

DOCUMENT STATUS

Issue	Date	Status	Issued by
1.	08/09/2025	Issue A	NDR
2.			
3.			
4.			
5.			

© Copyright RGP Consulting Engineers Limited 2025

No part of this publication may be reproduced by any means without the prior permission of RGP Consulting Engineers Limited.

TABLE OF CONTENTS

1	INTRODUCTION.....	1
1.1	Document Context.....	1
2	PRINCIPAL CONTRACTOR.....	2
2.1	Principal Contractor.....	2
2.2	Considerate Constructors.....	2
2.3	Phases of Construction.....	2
2.4	Procurement.....	3
2.5	Communication.....	3
2.6	Enquiries and Complaints.....	3
3	CONSTRUCTION SITE.....	4
3.1	Contractors Compound.....	4
3.2	Loading and Unloading.....	5
3.3	Site Hours.....	5
3.4	Construction Vehicle Hours.....	5
3.5	Car Parking.....	5
3.6	Incidents and Emergencies.....	6
4	CONSTRUCTION VEHICLES.....	7
4.1	Construction Vehicle Routing.....	7
4.2	Construction Vehicle Schedule.....	7
4.3	Vulnerable Road Users.....	7
4.4	Swept Path Analysis.....	8
4.5	Abnormal Load.....	8
4.6	Arrangements for Temporary Facilities.....	8
4.7	Traffic Management Measures.....	8
4.8	Wheel Washing Facilities.....	9
5	ENVIRONMENTAL MANAGEMENT.....	10
5.1	Dust.....	10
5.2	Light.....	10
5.3	Noise.....	11
5.4	Water.....	11
5.5	Terrestrial Mammals.....	12
5.6	Nesting Birds.....	12
5.7	Retained Trees.....	12
5.8	Community Relations.....	12
5.9	Summary.....	12
6	VEHICLE MANAGEMENT.....	13
6.1	Personnel Travel Plan.....	13
7	WASTE MANAGEMENT.....	15
7.1	Context.....	15
7.2	Waste Hierarchy.....	15
7.3	Waste Collections.....	16

Figures

Figure 1	Premier Inn Manchester West Disbury Hotel	1
Figure 2	Indicative Construction Site Compound (Source. Allison Pike)	4
Figure 3	Car Park Accumulation – Construction	6
Figure 4	2000 Metre Walk Catchment.....	13
Figure 5	5000 Metre Cycle Catchment.....	14
Figure 6	The Waste Hierarchy (Source. Department for Environment, Food & Rural Affairs).....	15
Figure 7	The Circular Economy (Source. Ellen MacArthur Foundation)	16

Drawings

2024/7847/001	Swept Path Analysis – Large Tipper
---------------	------------------------------------

1 INTRODUCTION

1.1 Document Context

- 1.1.1 This Construction Management Plan (document reference. 2024/7847/CMP02) is prepared by RGP Consulting Engineers Limited with consideration to approved development at Premier Inn Manchester West Didsbury hotel, Christie Fields Business Park, Derwent Avenue, West Didsbury, M21 7QS ("the site").

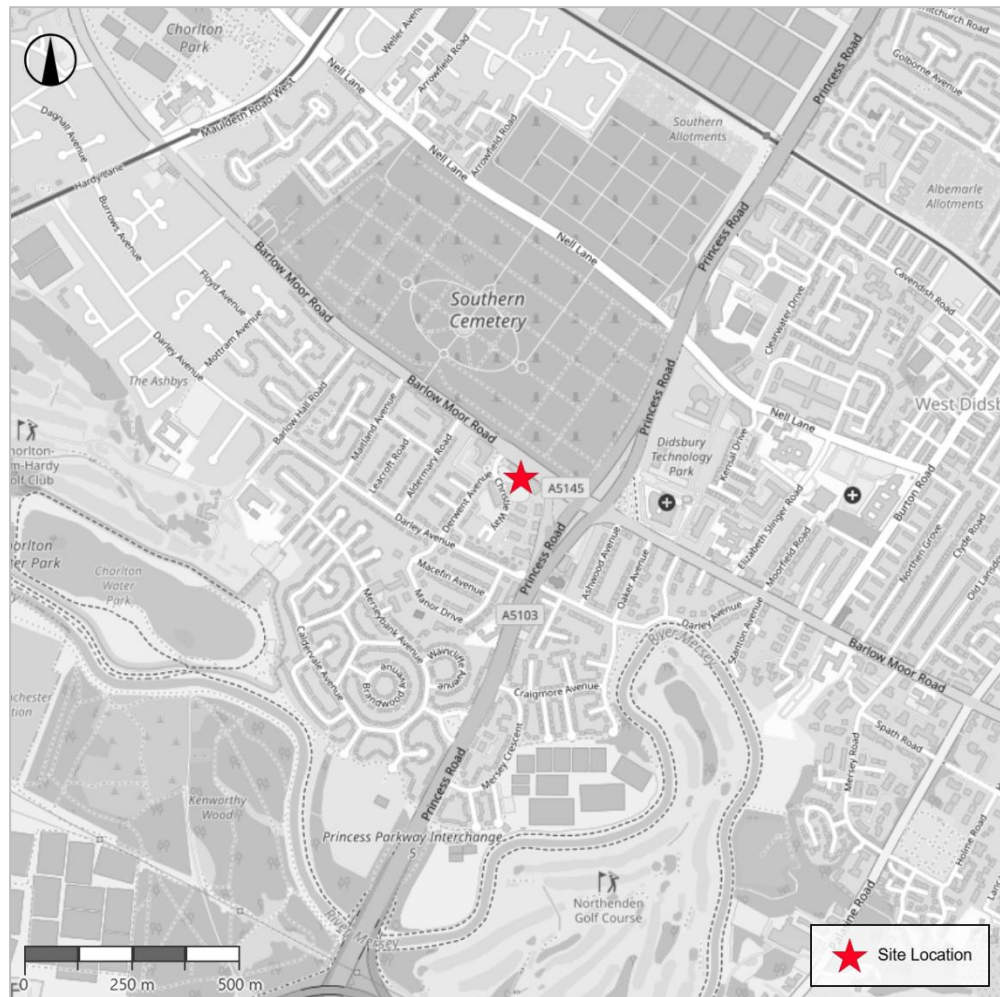


Figure 1 Premier Inn Manchester West Disbury Hotel

- 1.1.2 The development (application number. 140916/FO/2024) comprises the demolition of the existing associated branded restaurant at the site and erection of a two-storey annexe building to provide additional hotel accommodation.
- 1.1.3 This Construction Management Plan represents a new document, superseding the previously prepared Construction Management Plan (document reference. 2024/7847/CMP01) following feedback from Manchester City Council on that document and the information and assessments it contained.

2 PRINCIPAL CONTRACTOR

2.1 Principal Contractor

2.1.1 The Principal Contractor for the construction works is Medlock FRB Limited.

- Greengate Street
- Oldham
- OL4 1DG
- +44 0161 621 5200

2.1.2 Medlock will be responsible for implementing this Construction Management Plan throughout construction works. Medlock will review this Plan throughout construction works and make amendments and revisions as appropriate.

2.1.3 The contact details of the Principal Contractor will be provided on hoarding at the site, to include a twenty-four-hour emergency contact, throughout construction works – the details will be appropriately maintained to ensure they are clear and legible.

2.2 Considerate Constructors

2.2.1 Medlock FRB Limited will operate the construction sites with consideration to the Considerate Constructors Scheme. The Scheme commits Contractors to observe and implement the Code of Considerate Practice. The Code focuses on three key sections:

- Respecting the community - Constructors must manage their impact on their neighbours and the public to support a positive experience.
- Caring for the environment - Constructors must minimise their impact and enhance the natural environment.
- Valuing the workforce - Constructors must create a supportive, inclusive, and healthy workplace.

2.2.2 Medlock will ensure all on-site personnel and visitors to the construction site operate in a manner consistent with the Code.

2.3 Phases of Construction

2.3.1 Medlock FRB Limited anticipated the phases of construction will be as follows:

- Enabling works and site establishment.
- Substructure.
- Superstructure.
- Fit-Out.

- External Works.
- Miscellaneous (i.e. snagging).

2.4 Procurement

- 2.4.1 Medlock FRB Limited will explore opportunities for common procurement with other construction sites locally, this will include the delivery of supplies and collection of waste. Common procurement can positively contribute to decreased vehicle movements associated with construction sites.

2.5 Communication

- 2.5.1 This Construction Management Plan will be communicated by Medlock FRB Limited to all on-site personnel and visitors through induction training and toolbox talks throughout construction works.
- 2.5.2 Neighbouring residents and businesses will be informed of construction through a 'Letterbox Drop' prior to construction and throughout the construction works as appropriate – the contact details of the Principal Contractor will be provided on any communications.

2.6 Enquiries and Complaints

- 2.6.1 Medlock FRB Limited will aim for all construction work to be completed in a manner which has consideration to the community, environment and on-site personnel.
- 2.6.2 Nonetheless, Medlock will establish a procedure for the handling of any enquiries or complaints to include recording details of:
- The nature of the enquiry or complaint.
 - The cause of the enquiry or complaint.
 - The remedial action taken (where appropriate).
- 2.6.3 Medlock will aim to respond to any enquiry or complaint in a timely a manner as practicable and take remedial action where deliverable and justifiable.

3 CONSTRUCTION SITE

3.1 Contractors Compound

3.1.1 Medlock FRB Limited will establish a Contractors Compound on-site. An indicative construction site compound is illustrated in the figure below.

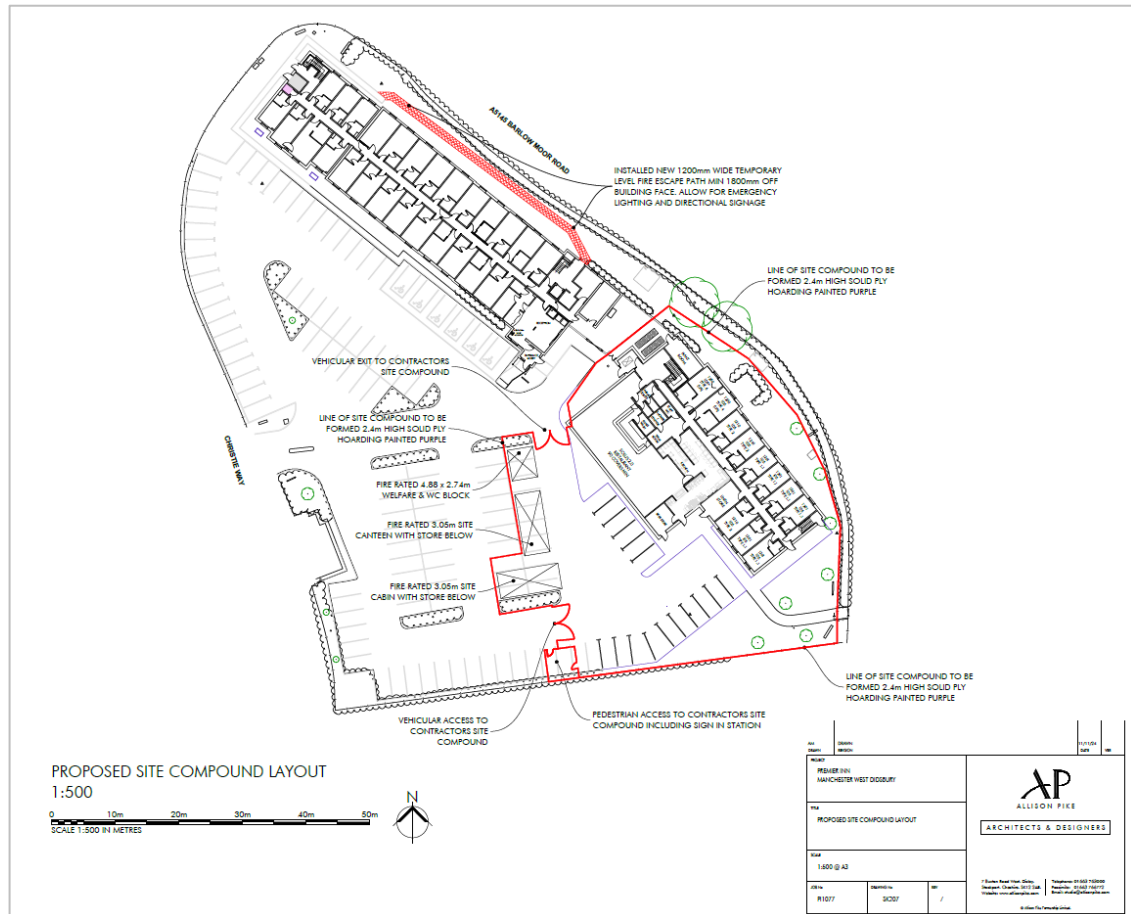


Figure 2 Indicative Construction Site Compound (Source. Allison Pike)

- 3.1.2 The Compound will be secured with plywood faced hoarding (2.4 metres in height) and heras fencing (2.0 metres in height) to prevent unauthorised access. The hoarding will be painted purple and adorned with Premier Inn graphics.
- 3.1.3 The Compound will comprise a site office and welfare facilities, additionally, provision will be made for the storage of construction materials and waste and wheel wash facilities. Cabins and containers will be stacked as appropriate to minimise the footprint of the Compound.
- 3.1.4 The composition of the Compound will be reviewed by Medlock throughout the construction programme to ensure it can contain all construction related facilities, materials and waste.

3.2 Loading and Unloading

- 3.2.1 All loading and unloading will be completed on-site / in the site compound as appropriate.

3.3 Site Hours

- 3.3.1 The construction site will be operational:

- 08:00 to 18:00 – Monday to Friday.
- 09:00 to 13:00 – Saturday.

- 3.3.2 No construction works will be undertaken on Sundays, Bank or Public Holidays.

3.4 Construction Vehicle Hours

- 3.4.1 Construction vehicle hours will be within the above construction site hours.

- 3.4.2 Construction vehicles will generally be restricted, as far as is reasonably practicable, to between 09:30 and 16:30 to minimise construction vehicle movements during peak hours on the highway network.

- 3.4.3 Construction vehicles movements will not be completed outside of the above construction site hours.

3.5 Car Parking

- 3.5.1 101 car parking spaces will be retained during construction works.

- 3.5.2 Application of the car parking accumulation data from approved RGP prepared Transport Statement confirms the site during construction could generate a peak car parking demand of 86 cars at 23:00, as illustrated in the figure below.

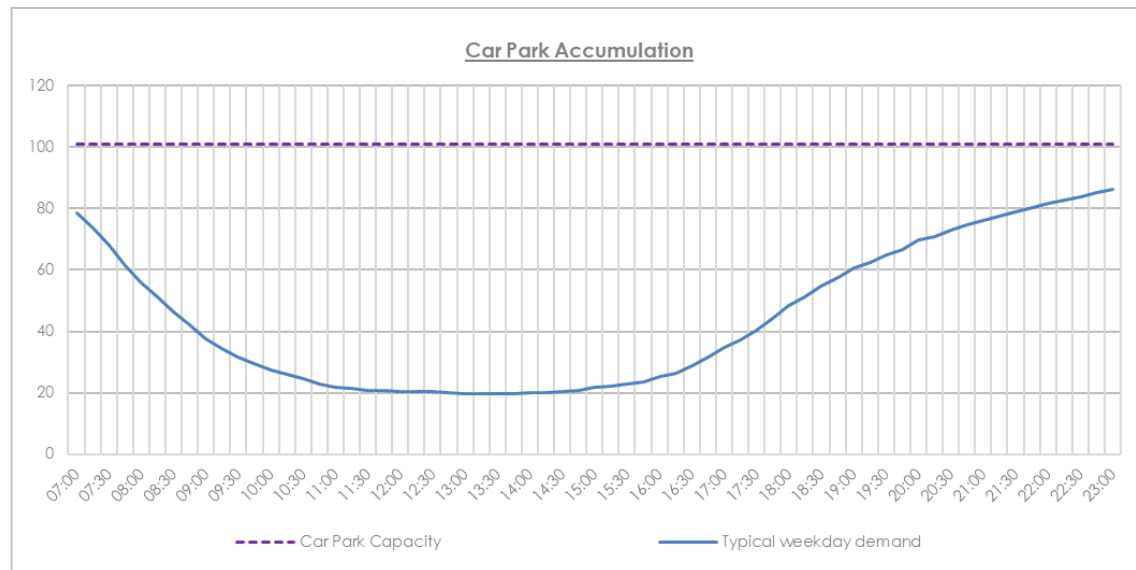


Figure 3 Car Park Accumulation – Construction

- 3.5.3 As illustrated in the figure above, the peak car parking demand would be observed overnight, as hotel guests are checked into the hotel.
- 3.5.4 Car parking demand would be lower across the course of a day when the construction site is operational, facilitating the shared use of the car park by hotel guests and construction personnel.
- 3.5.5 Nonetheless, this document provides measures to limit construction personnel and visitor car parking, in favour of sustainable travel to and from the site, as far as is reasonably practicable.

3.6 Incidents and Emergencies

- 3.6.1 Incidents and emergencies could arise where it is not possible or practicable to comply with the above construction site hours, the measures of this document or relevant planning policies.
- 3.6.2 In any such instances, Medlock FRB Limited will be permitted to complete emergency works with the Local Planning Authority advised and contacted with the details provided to the nature of the works.
- 3.6.3 Medlock will record details of any emergency works to include:
- The nature of the incident or emergency.
 - The cause of the incident or emergency.
 - The remedial action taken (where appropriate).
- 3.6.4 An Incident /Emergency Log will be kept as appropriate.

4 CONSTRUCTION VEHICLES

4.1 Construction Vehicle Routing

- 4.1.1 The site is located off the A5145, Barlow Moor Road, running between Stockport and Stretford via Chorlton-cum-Hardy and Didsbury.
- 4.1.2 The A5145 is located to the north of Junction 5 of the M60. The M60 is the Manchester orbital serving the main areas of Ashton-under-Lyne, Oldham, Stockport and Trafford Park.
- 4.1.3 While construction vehicle routing would be dependent on the origin / subsequent destination of the construction vehicle, it is considered roads close to the site are of sufficient standard to accommodate all construction vehicles.
- 4.1.4 All construction vehicles will access the site, and the construction site compound in a forward gear, manoeuvre on-site / within the construction site compound and egress the construction site compound and site in a forward gear. This arrangement is illustrated on drawing **2024/7847/001** attached hereto.

4.2 Construction Vehicle Schedule

- 4.2.1 Medlock FRB Limited will prepare a Construction Vehicle Schedule for all construction vehicle movements to ensure that only one vehicle is present at the site at any one time, and that movements are undertaken in a timely manner. As a Schedule would be prepared, it is not anticipated vehicle holding areas would be required.
- 4.2.2 Medlock will ensure all vehicle movements are booked in advance, at minimum 48 hours prior to the day of arrival. All drivers will be requested to telephone prior to their arrival at the site so the necessary steps can be undertaken to enable a smooth and efficient delivery or collection. All drivers will be notified of the intended vehicle routing prior to their arrival at the site to ensure their compliance.

4.3 Vulnerable Road Users

- 4.3.1 Medlock FRB Limited will aim for all construction vehicles to benefit from the following features to protect vulnerable road users:
- Audible warning alert (i.e. reversing or when turning left).
 - Blind spot sensors.
 - Camera monitoring.
 - Class V and VI mirrors.
 - Moving off sensors.
 - Side under-run protection.
 - Warning signage.

- 4.3.2 All construction vehicles will be supported by a suitably qualified Traffic Marshal as appropriate.

4.4 Swept Path Analysis

- 4.4.1 Swept path analysis for the largest vehicle regularly requiring access to the construction site compound is attached hereto. It is demonstrated the vehicle will access the site, and the construction site compound in a forward gear, manoeuvre on-site / within the construction site compound and egress the construction site compound and site in a forward gear. To ensure adequate space is available, some minor on-site works will be required.

4.5 Abnormal Load

- 4.5.1 An abnormal load is a vehicle with any of the following:
- weight over 44,000kg (43.3 tons)
 - an axle load of more than 10,000kg (9.84 tons) for a single non-driving axle or 11,500kg (11.31 tons) for a single driving axle
 - width over 2.9 metres (9.5 feet)
 - rigid length over 18.65 metres (61 feet)
- 4.5.2 Given the scale of construction works, it is not considered abnormal loads will be required throughout the construction works – should abnormal loads be required, Medlock FRB Limited will devise appropriate arrangements for the management of this and contact the Local Planning Authority / Local Highway Authority as appropriate.

4.6 Arrangements for Temporary Facilities

- 4.6.1 Given the scale of construction works, it is not considered there will be a requirement for temporary facilities to local public transport stops or along construction vehicle routes throughout construction works – should temporary facilities be required, Medlock FRB Limited will contact the Local Planning Authority / Local Highway Authority as appropriate.

4.7 Traffic Management Measures

- 4.7.1 Given the scale of the construction works, it is not considered any traffic management measures will be required throughout the construction works – should traffic management measures be required, Medlock FRB Limited will contact the Local Planning Authority / Local Highway Authority as appropriate.

4.8 Wheel Washing Facilities

- 4.8.1 To prevent mud and other debris being carried onto the highway, wheel washing facilities will be provided within the construction site compound. It is anticipated this will comprise the provision of a pressure washer, or similar, close to the access / egress of the construction site compound. A pressure washer is considered appropriate given the scale of the construction works.

5 ENVIRONMENTAL MANAGEMENT

5.1 Dust

- 5.1.1 Medlock FRB Limited will operate the site as per the Institute of Air Quality Management 'Guidance on the assessment of dust from demolition and construction.'

Management Measures

- 5.1.2 The following dust management measures will be employed during construction:

- Construction vehicles will not be permitted to idle, unless required.
- No materials or waste will be burned on-site.
- Plant will be low- or zero-emission.
- Plant will be maintained as per manufacture guidance.
- Plant will be oriented away from dust-sensitive receptors.
- Plant will be sited away from dust-sensitive receptors.
- Plant will have suitable dust suppression technologies.
- The site will be swept at the end of each day, or throughout the day, as required.
- Water suppression systems (i.e. handheld sprays) will be used throughout construction.

- 5.1.3 Medlock will establish a method of monitoring air quality and dust generation at the site.

5.2 Light

- 5.2.1 Medlock FRB Limited will operate the site as per the Health and Safety Executive 'Light at work' and Health and Safety Executive 'Electrical safety on construction sites'.

Management Measures

- 5.2.2 The following light management measures will be employed during construction:

- Light will be sited away from light-sensitive receptors.
- Lighting installations will be provided for the illumination of emergency exits and escape routes.
- Lighting will be designed to achieve a reasonably uniform illuminance on all relevant areas of the site.
- Lighting will be maintained as per manufacture guidance.
- Lighting will be oriented away from light-sensitive receptors.

- 5.2.3 Lighting will be designed to the minimum requirement outside of construction site hours to ensure personnel safety and site security.

5.3 Noise

- 5.3.1 Medlock FRB Limited will operate the site as per British Standard BS 5228 'Code of practice for noise and vibration control on construction and open sites'.

Management Measures

- 5.3.2 The following noise management measures will be employed during construction:

- Materials will be lowered and drop heights minimised.
- Plant will be maintained as per manufacture guidance.
- Plant will be oriented away from noise-sensitive receptors.
- Plant will be sited away from noise-sensitive receptors.
- Plant will be screened where it cannot be sited or oriented away from noise-sensitive receptors.
- Plant will have acoustic covers which will be in place when in use.
- Personnel will be provided with appropriate Personal Protective Equipment.
- Personnel will be competent in the operation of plant.

5.4 Water

- 5.4.1 Medlock FRB Limited will operate the site with consideration to best practice to ensure water management.

Management Measures

- 5.4.2 The following water management measures will be employed during construction:

- Drains within the site will be identified and measures implemented to prevent pollution.
- Drip trays will be provided for plant as appropriate.
- Emergency 'Spill Kits' will be provided.
- Hazardous construction materials will be stored in bunds.
- Plant will be maintained as per manufacture guidance.
- Processes that could generate spills will be sited away from drains.
- Water from wheel washing facilities and wash down areas will be contained.

- Water run-off will be contained.

5.5 Terrestrial Mammals

- 5.5.1 Medlock FRB Limited will operate the site with consideration to best practice to ensure the protection of terrestrial mammals.

Management Measures

- 5.5.2 The following protection of terrestrial mammal management measures will be employed during construction:
- Chemicals / pollutants will be stored and disposed of according to Control of Substances Hazardous to Health regulations.
 - Excavations will be covered overnight.
 - Excavations not covered overnight will be provided with a ramp.
 - Lighting will be designed and oriented to avoid light spill on retained habitats.

5.6 Nesting Birds

- 5.6.1 It is recommended the construction programme is undertaken outside the core breeding bird season – should this not be practicable; an inspection of surrounding vegetation should be undertaken by a suitably qualified ecologist no more than 24 hours prior to the commencement of work.

5.7 Retained Trees

- 5.7.1 Arbtech 'Arboricultural Method Statement' detailed mitigation pertaining to existing trees (where required) and it is considered any mitigation measures detailed within the Survey represent effective mitigation from an ecological perspective and should be adhered to.

5.8 Community Relations

- 5.8.1 Should there be an enquiry or complaint on any of the above environmental management measures, the Medlock FRB Limited will aim to respond in a timely a manner as practicable and take remedial action where deliverable and justifiable.

5.9 Summary

- 5.9.1 The above lists are not exhaustive, and Medlock FRB Limited are encouraged to explore further management measures.

6 VEHICLE MANAGEMENT

6.1 Personnel Travel Plan

- 6.1.1 Medlock FRB Limited will implement a Personnel Travel Plan.
- 6.1.2 The Personnel Travel Plan will promote active (walking and cycling) and sustainable (public transport) travel modes.
- 6.1.3 To support active and sustainable travel, Medlock will consider the provision of lockers on-site for construction personnel to store their goods, so they do not have to be transported to / from the site daily.

Active Travel

- 6.1.4 It is commonly accepted that distances of up to 2000 metres can be walked by reasonably fit individuals for commuting purposes. In consideration of this, the figure below illustrates a 2000 metre walk catchment.

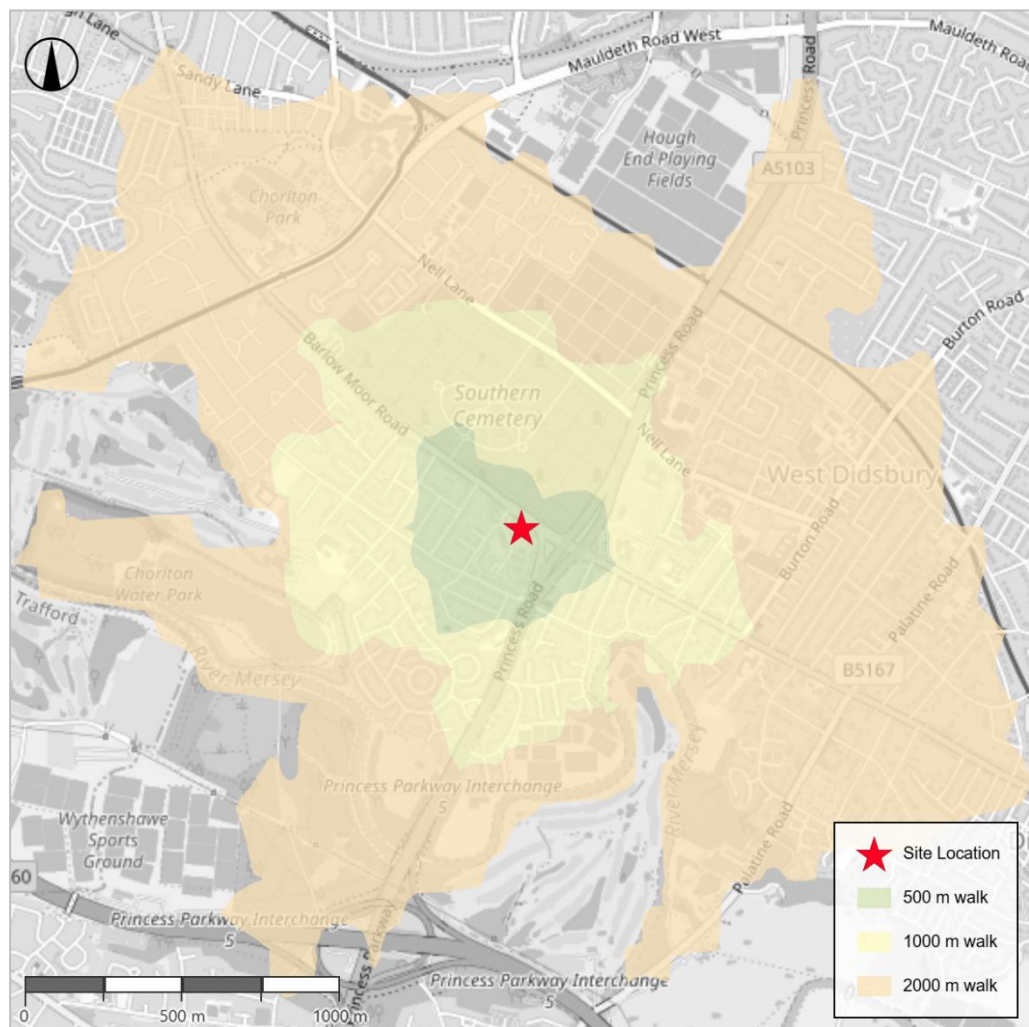


Figure 4 2000 Metre Walk Catchment

- 6.1.5 It is commonly accepted that distances of up to 5000 metres can be cycled by reasonably fit individuals for commuting purposes. In consideration of this the figure below illustrates a 5000 metre cycle catchment.

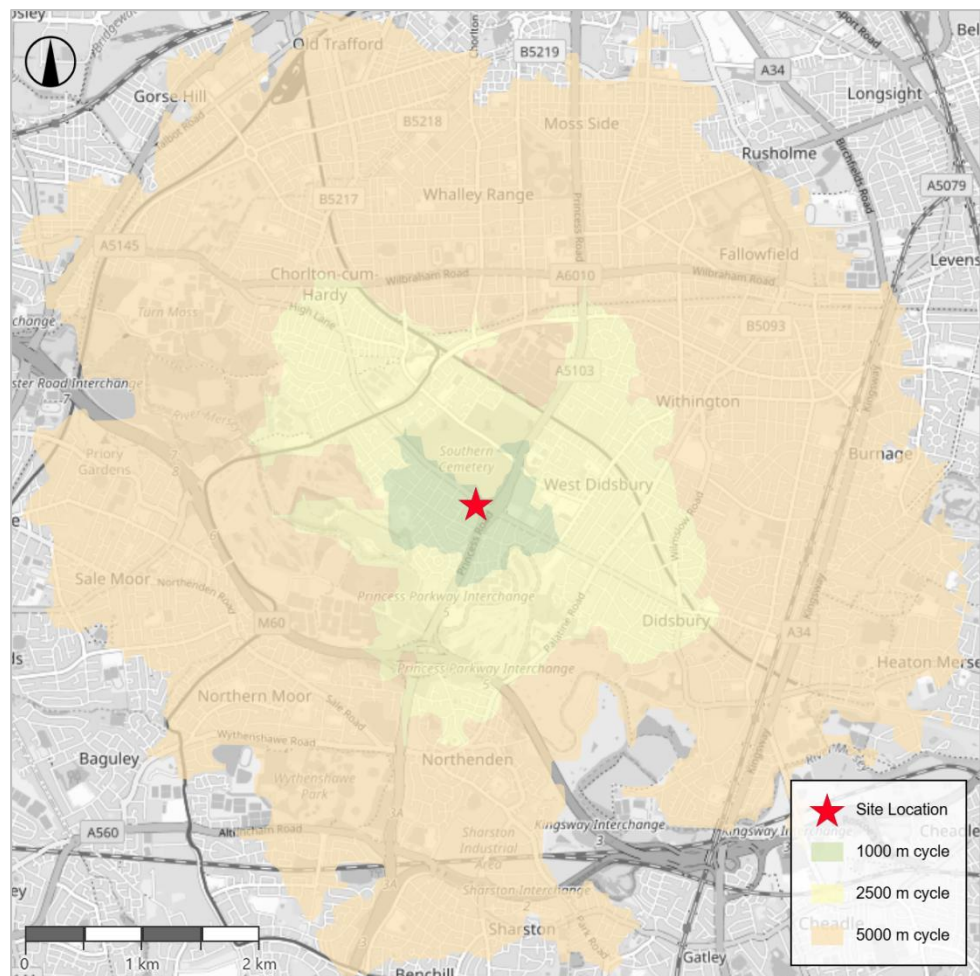


Figure 5 5000 Metre Cycle Catchment

- 6.1.6 Medlock will consider the use of personnel who reside locally so that active travel is a realistic travel choice.

Sustainable Travel

- 6.1.7 The closest bus stops to the site are located on the A5145, Barlow Moor Road. The stops are served by routes 23 (The Trafford Centre - Urmston - Stretford – Stockport) and 87 (Piccadilly Gardens - Moss Side - Withington – Chorlton). Bus route 172 (Newton Heath - Droylsden - Gorton - Didsbury – Chorlton) can be boarded on Princess Road.
- 6.1.8 Medlock will consider the use of personnel who reside locally so that sustainable travel is a realistic travel choice.

7 WASTE MANAGEMENT

7.1 Context

- 7.1.1 This Section is informed by Department for Environment, Food & Rural Affairs 'Guidance on Applying the Waste Hierarchy' (2011).

7.2 Waste Hierarchy

- 7.2.1 The Waste Hierarchy "ranks waste management options according to the best environmental outcome taking into consideration the lifecycle of the material." The Waste Hierarchy, as reproduced from the Guidance, is illustrated in the figure below.

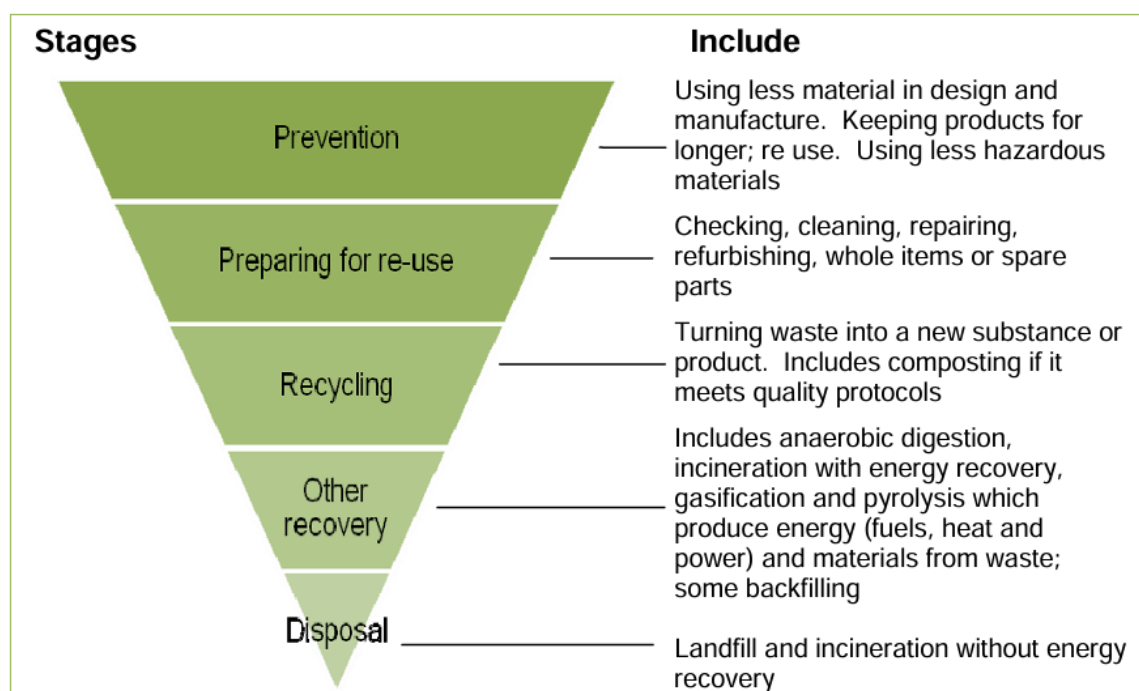


Figure 6 The Waste Hierarchy (Source. Department for Environment, Food & Rural Affairs)

- 7.2.2 As illustrated above, the Waste Hierarchy gives top priority to preventing waste, and where waste is generated, it gives top priority to preparing it for reuse, then recycling, then other recovery, prior to disposal.
- 7.2.3 Application of the Waste Hierarchy supports the move from a linear model of production, consumption and disposal towards a circular model. The Circular Economy, as reproduced from the Ellen MacArthur Foundation, is illustrated in the figure below.



7.3 Waste Collections

- Waste will be collected by an Authorised Organisation which could comprise one of the following:
 - a) Holder of an Environmental Permit.
 - b) Registered Water Carrier.
 - c) Waste Collection Authority.
 - d) Waste Disposal Authority.
- Non-Hazardous waste would be transferred under a 'Waste Transfer Note'.
- Hazardous waste will be transferred under a 'Waste Consignment Note'.

DRAWINGS



RGP - Transport Planning and Infrastructure Design Consultants

enquiries@rgp.co.uk

www.rgp.co.uk

Surrey Office Old Mill Studios, Fry's Yard, 37-40 Bridge Street, Godalming GU7 1HP
London Office 10 York Road, London SE1 7ND

T: 01483 861 681
T: 020 7078 9662

