



Phoenix Iron Works, Jersey Street, Ancoats

Construction Environmental Management Plan

Planning Condition: 137346/FO/2023 Condition 10



Contents

Introduction	
Project Team & Programme	
Site Working Hours	
Visitor and Operative Parking	
Security Hoardings	
Site Logistics and Pedestrian Access	
HGV vehicle routing plan and material deliveries	
Enabling Works	
Storage of Plant, Materials and Fuel	
Cranage	
Waste Management (recycling/disposal)	
Noise Control	
Surrounding Area	
Mitigation Measures	
Operating Methods of Noise Reduction	
Noise Reduction of Mobile Plant	
Noise Reduction of Stationary Plant and Tools	
Control of Noise Propagation on Site	
Dust Control	
Dust Assessment	
Mitigation Measures	
Further Dust Guidance	
Fire Precautions	
Light Control	
Wheel Washing Prevention of silt-laden run-off)	
Concrete wash down	
Flooding & Weather Alert	
Environmental Management Toolkit	
Environmental Pollution Emergency Response Procedures	
Network Rail	
Communication	
Considerate Constructors	
Group Communication to EWC Staff	
Communication with Operatives	
Communication with the Local Community	



Introduction

The works comprise:

Phoenix Ironworks offers an exciting opportunity to help the Poland Street Zone transform into a distinctive new neighbourhood within Manchester.

The Phoenix Ironworks brief requested designs that included

- 1, 2 and 3 bedroom apartments to provide a mixture of typologies catering for a wide variety of residential requirements
- The creation of ground floor activities through the provision of makers' spaces and commercial workspace.

Location: The site is bounded by Jersey Street, Radium Street, Naval Street & Poland Street, Ancoats, Manchester, M4 6AY and is located within the boundary of the Ancoats Conservation Area.



This document specifically targets and mitigates the issues presented from the construction of the proposed development and the associated works. For ease of reference these are separated into specific elements and covered individually.

Project Team

Manchester Life
Arcadis
PRP Architects
KODA
Urban Green

Client
Design Intent Guardian (Architect)
Architect
Structural Engineers
Landscape Architects



Emergency Contact Number

EWC Operations Manager
EWC Project Manager

Adam Pickford
Derek Mullarkey
Tel: 07990051251
Tel: Head Office 01772 698822

This document specifically targets and mitigates the issues presented from the construction of the development and the associated works. For ease of reference these are separated into specific elements and covered individually.

Project Programme

Enabling Works

3rd/4th Quarter 2025

Construction Works

Site Commencement
Project Completion

1st Quarter 2026
3rd Quarter 2028

Site Working Hours

It is proposed that site construction activities will be carried out during the following hours:


Monday to Friday	Site Open 7.30 till 18.00 Site Working hours 8.00 till 18.00.
Saturday	9.00 till 14.00
Sunday/Bank Holidays	No work unless prior arrangement is granted by MCC Environmental Health.

Visitor and Operative Parking

There will be no onsite parking for either Management Staff, Visitors and Operatives vehicles, parking is available within walking distance from the site on various City Centre Car Parks.

Prior to the placement of subcontract orders with our supply chain we will make them aware of the site restrictions, particularly the parking restrictions on and around the site. We will actively

encourage car sharing and the use of crew buses to minimise the number of vehicles coming to site

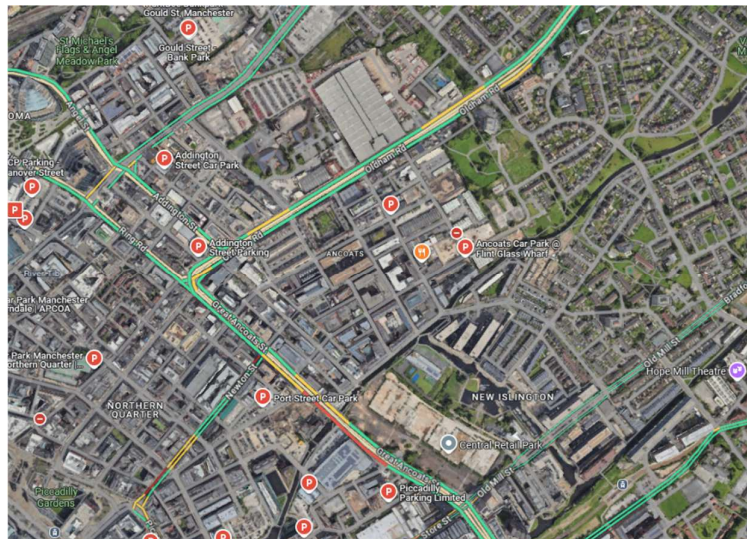



Erection and Maintenance of Security Hoarding

Hoardings will be 2.4m high solid hoarding painted pale grey (RAL 7004) with all necessary fixings and lighting to secure the works.

The Contractor shall ensure that the hoardings are kept free of graffiti and advertisements or bills. Any graffiti, advertisements or bills need to be removed by the contractor within 72 hours.


Manchester Life will apply marketing branding to the hoardings from time to time. The location will be pre-agreed with the Contractor based upon the most practical and marketable location.

Site signage and any display of any company branding should be agreed with Manchester Life in advance. Manchester Life may request that their brand be displayed alongside any company branding. This includes but is not limited to cranes and mast climbers.

Emergency contact details will be displayed on the hoardings at the main entrance points to site and at regular intervals around the site.

All hoardings will be visually inspected daily and maintained accordingly. The main entrance to the site will be branded as per the EWC hoarding standards (see below). This helps distinguish EWC sites from others and gives delivery drivers a point of reference. The main hoarding surrounding the site will be branded in accordance with the Clients Branding.


Internal access routes and storage compounds will be segregated utilising Heras type fencing panels or pedestrian barriers as appropriate.

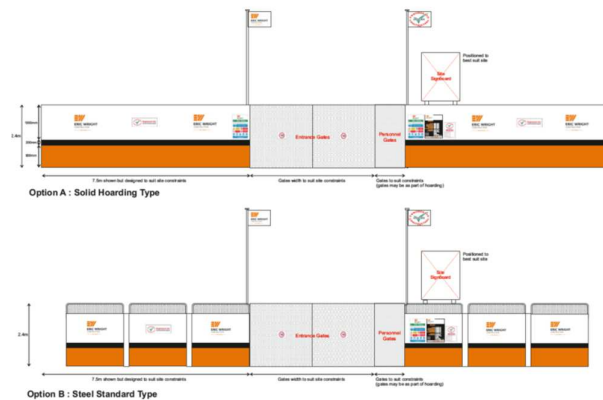


Site Accommodation and Pedestrian Access

The project is split into an Enabling Package & Main Works Package;

Enabling Works – will operate from temporary site cabins, works to be undertaken will be demolition of remaining industrial units, remediation of the site and installation of Piling Mat.

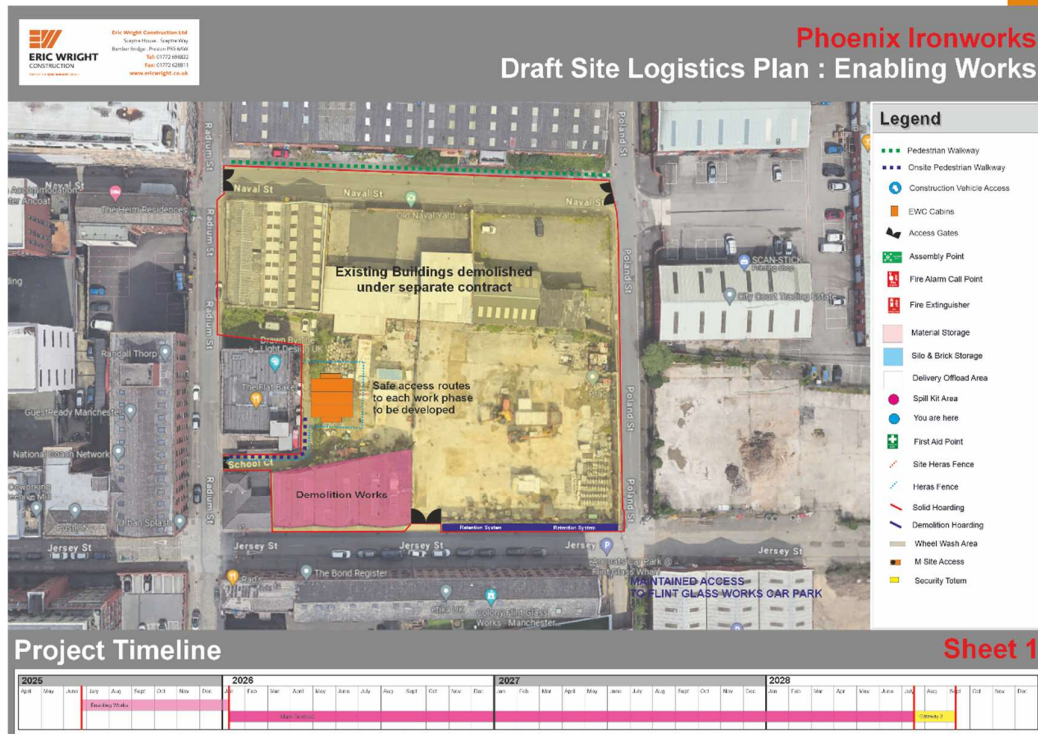

Main Works – Meeting rooms, PM’s office, QS office, open office, subcontract offices, Toilet Facilities and Kitchen facilities for management and subcontractors will be located within the newly built Eliza Yard development, with canteen, drying, toilet facilities located onsite in the area shown in either the newly constructed industrial units or temporary cabins.

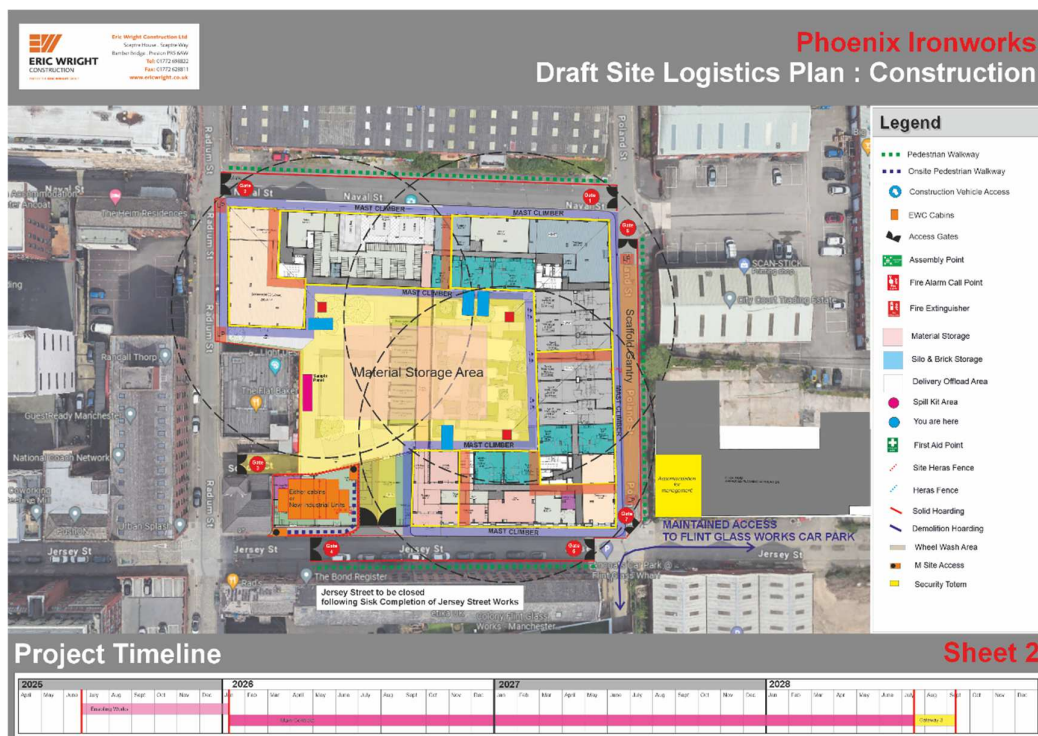



We will have biometric turnstiles to ensure that only inducted management and site operatives can access the site.

HGV Routing Plan & Material Deliveries


Vehicles will enter site immediately and gates will be manned to ensure no deliveries are kept on the highway. All subcontractors will be required to produce a procurement schedule for their materials which will be monitored at their weekly/fortnightly meetings and must book delivery slots with our Logistics manager. Efficient and accurate scheduling of deliveries will minimise storage capacity required, double handling and congestion around the site and surrounding roads and highway infrastructure.

Movement of traffic to and from site will be restricted and controlled at sensitive times, (to be developed and agreed with Highways designated representative) and in any event deliveries will be programmed so as not to conflict with peak periods of the day.


Anticipated peak traffic rates will be during the concreting works when we anticipate approximately 60 movements a day for the concrete pours.

We will utilise a booking in system, so site is ready to receive deliveries and bring them immediately within the site boundary upon arrival.

We will develop a traffic management plan with highways and agree this prior to commencement. An indicative plan is provided below;

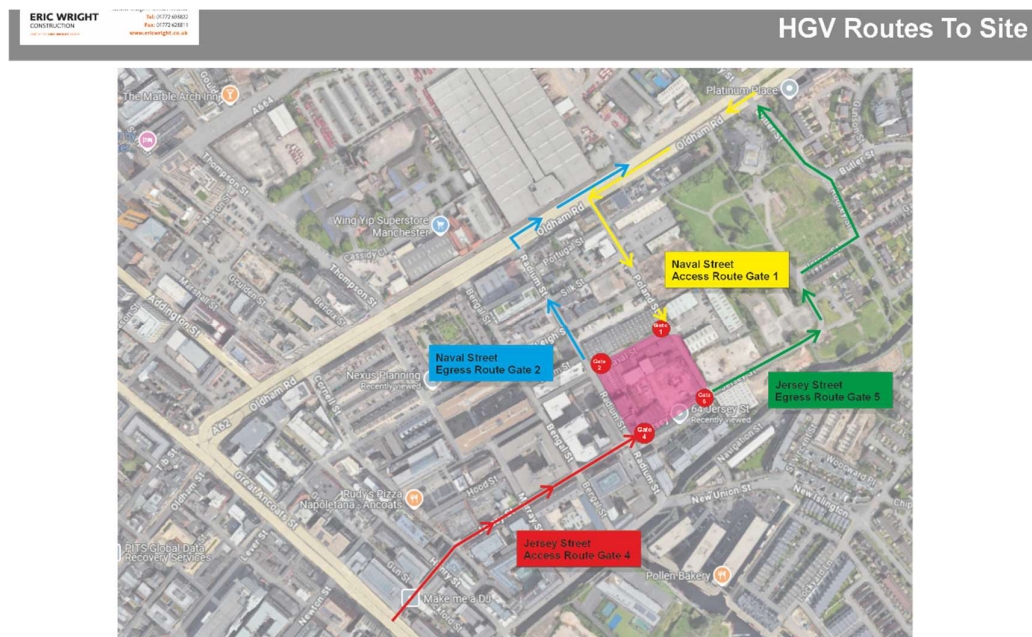

Initial Swept path analysis, larger version appended;

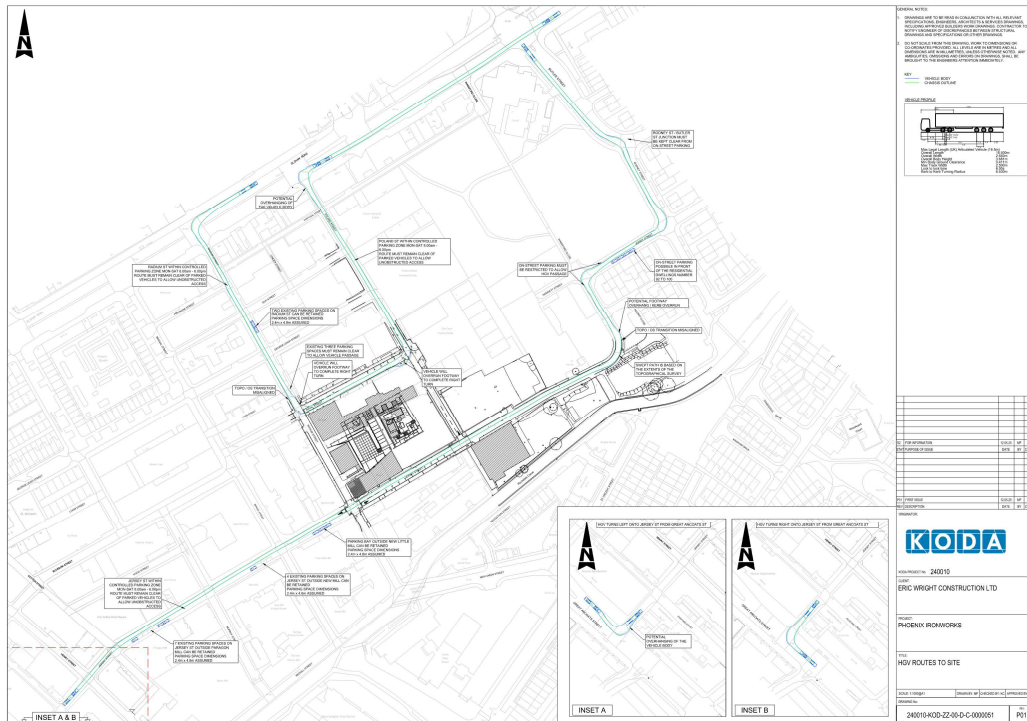

- Order the amount of materials we need as accurately as possible
- Arrange for 'just in time' deliveries to reduce storage and material losses
- Consider the source of materials.
- Consider the packaging used for materials delivered to the site -can this be reduced or recycled
- Ensure that deliveries are rejected if damaged or incomplete
- Make sure storage areas are safe, secure and weatherproof (where required)
- Store liquids away from drains, burns and in bunded areas to prevent pollution.

Wherever possible materials will be delivered shrink-wrapped and palletised to be unloaded and distributed safely by crane or hoist. Diesel fuel for site plant will be stored in sealed tanks inside bunded walls with a minimum of 110% of the capacity of the tank. The use of diesel driven plant and equipment will be kept to an absolute minimum. Wherever possible equipment and plant will be electrically powered to reduce noise and prevent emissions.



Cranage

There will be 3 number tower cranes used on the Project. Indicative location is shown on the appended logistics plan. The base for the crane will be designed by the structural engineer and checked/sign-off by our Temporary Works Engineer.



The crane will be zoned in such a way to limit oversailing of neighbouring properties but an oversail agreement will be required with MCC's highway's authority. Cranes will be operated in accordance with the requirements of BS 7171, Code of Practice for Safe Use of Cranes.

Waste Management (Recycling/Disposal)

An important part of the site management process involves site cleansing, rubbish removal and recycling. We have produced an initial Site Waste Forecast Dashboard which details our initial waste forecast.

Measures of how we intend to reduce, re-use, recycle and manage site waste include.

- Ensure that all material removed from site is taken to waste recycling stations and separated for recycling.
- Records of the waste recycling will be provided by the recycling stations.
- Enforcing good housekeeping measures e.g. proper storage of materials to minimise spillage.
- The use of raw materials as per manufacturer's instructions.
- Monitoring the generation of waste in order to identify trends and areas for further investigation.



- Identifying recyclable and salvageable materials and where feasible find secondary or alternative uses.
- Segregate waste types to facilitate recycling activities.
- Working with suppliers / subcontractors to minimise surplus material delivered to site.
- Working with suppliers to ensure only the necessary minimum of packaging is used.
- Consideration of alternative materials with lower wastage levels.
- Ensuring that all Duty of Care and other legal requirements are complied with during the disposal of wastes.
- Consulting with suppliers to determine correct / appropriate disposal routes for waste products and containers.
- Assessing the project design to identify ways in which waste generation can be minimised through raw material.
- Identify how wastage from temporary and permanent works activities can be avoided and minimised.
- Setting waste reduction targets as well as educating and informing site staff.
- Reducing usage of diesel, electricity and water on site by adopting good practices and Management procedures.

The responsibility of updating the Waste Forecast Dashboard belongs to the EWC Project manager.

Noise, Dirt/Dust & Vibration Control

Noise Control

In general, the construction phase can be viewed as intense activities of work over a short timescale.

These construction processes involve concentrated activities in a localised area.

Construction methodologies should be made as efficient as possible to minimise noise impacts to local residential areas and offices. Additionally, every opportunity should be taken to provide 'temporary' screening where it is likely to provide effective mitigation. In places where screening is recommended as part of the traffic noise mitigation plan, the early installation of these screening measures where practicable would also reduce the construction noise levels considerably.

Locations closest to the scheme are likely to be subject to the highest construction noise levels, although this will depend on topography and existing infrastructure providing natural screening. The level of impact would also vary considerably, dependent on the current ambient noise levels for given areas. Where properties are already subject to significant road traffic noise, the impact from construction noise will be less than those areas which are set further back from existing road transport corridors.

All measures to minimise construction noise would be taken according to best practicable means, as described in the mitigation measures section.

A more detailed Noise Assessment will be carried out by the Environmental Coordinator upon commencement and at regular intervals throughout the construction process.

The following table illustrates expected levels of noise from the various types of plant to be used on the project.



Plant Type	BS 5228 Reference	Sound Pressure Level Leq (dBA) at 10m
Tower crane	C4.49	77
Passenger/goods hoists	C4.62	66
Cutters, drills, and small tools	C3.35	65
Pulveriser on Excavator	C1.4	76
Fork lift truck	C4.55	70
Lorries and vans	-	73
Mobile crane	C4.46	67
Mobile lorry mounted concrete pump	C4.30	79
Poker vibrator	C4.33	78
Ready mixed concrete lorry	C4.21	77
Concrete splitters/saws	C1.6	83
Scaffolding and hydraulic access platforms	C4.58	63
Tipper lorries	C2.32	74
Flatbed articulated vehicle	-	73
Large rigid lorries	-	75
Track mounted piling rigs	C3.15	82
Water pumps	C2.45	65

Surrounding Area

The continuity of existing operations of the surrounding area will be at the heart of all our planning and delivery of the project. We will use the following hierarchy:

1. Protect and maintain all existing adjacent buildings operations and services.
2. Protect and maintain all highway and footpath operations and services contained
Within, there will be a requirement for diversions to in place during the works and these will be clearly signposted.
3. Use construction methods that are appropriate when working close to site users and staff.
4. Plan and communicate on the above basis.
5. Deliver, monitor and control activities.

The most sensitive receptors surrounding the site are.

North – Naval Street Industrial Units

East – City Court Trading Estate and newly constructed Eliza Yard Residential

South – Flint Glass Works Offices & Residential

West – Urban Splash Offices



Construction methodologies will be made as efficient as possible to minimise noise impacts to surrounding areas.

All measures to minimise construction noise will be taken according to best practicable means, as described in the mitigation measures section.

A more detailed Noise Assessment will be carried out by the Environmental Coordinator upon commencement and at regular intervals throughout the construction process.

All operatives will be given a site induction and briefed on the environmental risks that our construction activities pose to the surrounding water courses, with regular toolbox talks being given on the correct use of spill kits, wash down areas etc.

Mitigation Measures

The noise impact of the construction phases can be minimised by use of the noise control measures, as suggested in Section 8 of BS 5228-1:2009. General principles for the control of noise during the construction works are presented below.

- Appropriate choice of plant and equipment.
- Regular plant maintenance to keep plant in good working condition and reduce noise from machinery.
- Careful phasing of the proposed operations; and
- Provision of temporary barriers.

The site staff will be utilising methods of mitigation outlined, alongside regular monitoring and utilising feedback from residents.

This regular noise monitoring will be carried out by the Environmental Coordinator. This may be substituted by sub-contractor's noise readings as stated in their method of work.



Operating Methods of Noise Reduction

Ensure that all staff and operatives are briefed on the requirement to minimise nuisance from site activities, this will be mentioned within the site inductions, a programme of toolbox talks and all method statements. Any significant changes in numbers of workforce on site will force a review of the monitoring programme.

No equipment shall operate other than at the manufacturers' rated working levels; site staff shall not 'rev' equipment unnecessarily.

Use of machine-based equipment on site shall be kept to an absolute minimum and only silenced or sound models shall be used.

No plant and equipment shall be left running if not required for immediate use. Where this is not practicable, equipment shall be set to idle in the quietest manner to minimise noise emissions.

Resilient materials will be used where possible to reduce impact noise where materials are being moved or dropped e.g. lining chutes and dumpers. Materials will be lowered whenever practicable and otherwise drop heights will be kept to a minimum.

Noise Reduction of Mobile Plant

The movement of plant onto and around the site will have regard to the normal operating hours of the site and the location of any noise sensitive receptors. Audible reversing alarms will be of a type, which whilst ensuring that they give proper warning, have a minimum noise impact external to the site.

Internal haul routes will be well maintained and avoid steep gradients.

Earth moving plant will be fitted with efficient sound reduction equipment and manufacturers' enclosure panels will be kept closed.

Location of the site compound is located to minimise the noise impacts of delivery vehicles on unmade ground.

Noise Reduction of Stationary Plant and Tools

Noise reduction measures for tools are as follows:

- Use of hydraulic or electric tools where possible.
- Use of alternative quieter equipment for concrete breaking/cutting.
- Fitting suitably designed sound reduction equipment to reduce noise without impairing efficiency.
- Use of damped tool piece or saw blade.
- Enclose in a suitably designed portable or fixed acoustic enclosure with suitable ventilation (with due regard to the health and safety of operatives).

These measures will be considered for selected where appropriate by the Site Manager.

Control of Noise Propagation on Site

Temporary acoustic barriers, such as hoardings or mounds when positioned close to the source or the receiver will assist in the reduction of noise levels experienced at nearest receivers. The degree



of protection will be limited to 5-10dB(A), and care must be taken to avoid reflecting noise and increasing the problem elsewhere.


Barriers should be:

- A fairly uniform panel, free from holes with no gaps or openings at joints (uneven ground may leave gaps to be filled).
- Stable and robust enough to stand up to site conditions.
- Of a height and width more than enough to completely cut off sight of the source from the receiver, and
- Preferably at right angles to the line of sight of the receiver.

Further Noise Guidance

BS 5228 -1:2009 'Code of practice for noise and vibration control on construction and open sites – Part: Noise'

Eric Wright Sustainable Construction Toolkit (saved on the Wrightway electronic project file):

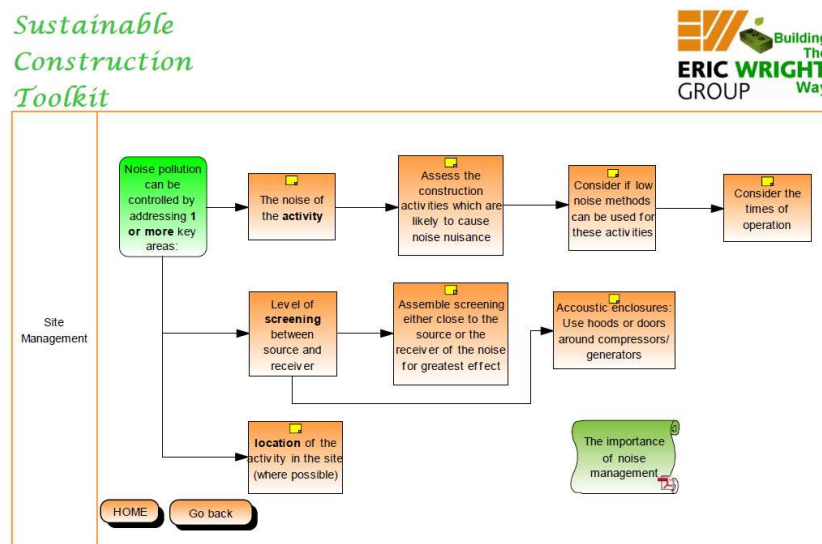

Dirt & Dust Control

The control of dust arising from the construction works will be controlled in a number of ways depending on the work source causing/providing the dust and the timing/stage at which the construction works are at.

Permits will be obtained from the EWA prior to any crushing of materials onsite.

Vehicles when removing or bringing materials to site will be sheeted.

Dirt & Dust Assessment

Environmental risk assessments are completed for every contract and particular attention is focused on statutory nuisance. Dust monitoring will take place twice a day in line with the control



methods detailed in the risk assessment. Records of this will be maintained on site and available on request. If excessive dust levels are reached, works will be temporarily suspended whilst the Environmental Coordinator is consulted, and further appropriate dust measures are implemented to enable works to recommence. This will be recorded.

Additional dust monitoring will be carried out by Eric Wright Construction Environmental Coordinator on a regular basis. Control methods as necessary will be identified.

Mitigation Measures

Measures that may be taken include, but are not limited to:

Haulage Routes, Vehicles and Construction Plant

Potential dust Source	Control Measure	Responsibility for implementation
Haul roads and traffic routes	Scheduled deliveries to avoid standing traffic on routes to site	Project Manager
Vehicle waiting areas and hard standing	Vehicles will be directed into site and unloaded. If waiting is required engines will be switched off	Gateman/Traffic controller
Vehicle and wheel washing	Wheel washing facilities easily available and signed. Gateman to be responsible.	Gateman/Traffic controller
Site traffic	Speed restrictions will be in place including signage and managed by site personnel to avoid back up.	Gateman/Traffic controller
Public roads	Gateman/Traffic controller to be aware of scheduled deliveries and coordinate traffic and operations affecting access	
Road cleaning	Road sweeper to be employed on a daily basis for cleaning access roads to site. These operations will be increased when critical activities occur	Gateman/Traffic controller
High level walkways and surfaces (Scaffolding and others)	Operatives will be briefed at induction to the requirements of dust control and suppression	Project Manager

Static and Mobile Plant Emissions

Potential dust Source	Control Measure	Responsibility for implementation
Visible exhaust smoke	All standing/waiting traffic to have engines switched off. All plant brought to site to be well maintained, and suppliers advised of this at order stage	Project Manager
Maintenance	All plant and equipment to be maintained off site	Project Manager
Servicing	All plant and equipment to be serviced off site	Project Manager
Operating time	All operations will be conducted in line with the planning conditions and all sub contractors being made aware of restrictions at order stage	Site Team
Exhaust time	Operating plant to be monitored to ensure it is not left running unnecessarily	Project Manager



Exhaust direction and heights	Exhausts from plant will be in line with manufacturers specifications and directed from ground to atmosphere	Project Manager
Location of plant and equipment	Plant and equipment operating close to other businesses and sensitive receptors will be kept to critical activities only.	Project Manager

Surfacing and Coatings

Potential dust Source	Control Measure	Responsibility for implementation
Bitumen over heating	Control of tar boilers. Ensure equipment is in good working order	Project Manager
Fume Production	Ensure protection is in place at all times while heating or maintaining heat	Project Manager
Small accidental fires	Have emergency procedures in place and brief at induction and toolbox talks. Monitor RAMS	Project Manager
Housekeeping	Monitored through regular inspections	Project Manager
Direct application of open Flames (torching)	Avoid overheating and keep to a minimum	Project Manager

Material Handling

Potential dust Source	Control Measure	Responsibility for implementation
Material Handling operations	Handling and movement of materials to be kept to a minimum through planning	Project Manager
Transport of powdery materials	Loose materials to be moved in containers or remain wrapped until use	Project Manager
Transport of aggregates	Use enclosed or sheeted vehicles	Project Manager
Handling areas	Keep areas clean and free from dust	Project Manager
Vehicle loading	Use methods that minimise the creation of dust. Damp down with water	Project Manager
Filling Skips	Use enclosed skips where possible	Project Manager
Reducing the spread of dust across the site	Use damping down methods	Project Manager

Storage of Powder Materials

Potential dust Source	Control Measure	Responsibility for implementation
Bulk Cement	To be delivered and stored in tankers/silos	Project Manager
Silos	To be kept in good condition. Regular checks for damage	Project Manager
Accidental spillage when filling or operating silos	Emergency preparedness plan in place identifying R+R	Project Manager



Dry materials > 3mm	Storage to be kept to minimum. Use materials at point of delivery	Project Manager
Dry materials < 3mm	Storage to be kept to minimum. Use materials at point of delivery	Project Manager
Storage	Store materials away from site boundaries and sensitive receptors	Project Manager

Stockpiles

Potential dust Source	Control Measure	Responsibility for implementation
Stockpiles	Stockpiles will be kept away from sensitive receptors and kept to a minimum, damping down systems	Project Manager
Building stockpiles	Ensure any stockpiling is done so that the angle of repose is not such that slippage will occur	Project Manager
Short term stockpiles	Ensure that these are kept to a minimum and avoided by use of material at source	Project Manager
Long term stockpiles	Ensure that these are kept to a minimum and avoided by use of material at source	Project Manager

Site Establishment and Restoration on Completion

Potential dust Source	Control Measure	Responsibility for implementation
Earthworks	Will be completed in sections to minimise over exposure and as programme phasing.	Project Manager
Completed earthworks	To be reinstated as soon as possible in line with programme	Project Manager
Storage mounds	Any mounding will be sealed	Project Manager
Landscaping	To be in line with programme and design. No screening to be on site	Project Manager
Transitory soil mounds	Not required	Project Manager
Crushing and screening	Crushing and screening operations to be kept away from sensitive receptors. Ensure compliance with the EPA 1990	Project Manager

Construction and Fabrication Process

Potential dust Source	Control Measure	Responsibility for implementation
Cutting, grinding, drilling, sawing etc	Consider prefabrication to avoid cutting. Quality checks to prevent errors and re-work. Use dust suppression sprays. Use exhaust ventilation. Robust design to prevent cutting.	Project Manager
Dust control exhaust ventilation	Always use diamond cutting blades and water sprays	Project Manager
Cutting roads, pavements, blocks	Always use diamond cutting blades and water sprays	Project Manager



Angle grinders	Always use diamond cutting blades and water sprays	Project Manager
Mixing of granular materials	Use premixed materials. Mix under controlled conditions. Store dry powder materials in a safe dry environment	Project Manager

Internal and External Finishing and Refurbishment


Potential dust Source	Control Measure	Responsibility for implementation
Painting and decorating	Use of suppression or extraction equipment should be used. Vacuum cleaning where possible	Project Manager
Plastering rendering, finishing and fitting out	Housekeeping to control dust related activities	Project Manager
Electrical plumbing systems requiring chasing into walls	Use of suppression or extraction equipment should be used. Vacuum cleaning where possible	Project Manager
Fireproofing and insulation	Use of suppression or extraction equipment should be used. Vacuum cleaning where possible	Project Manager
Cleaning	Avoid dry sweeping use vacuum control where possible	Project Manager

Further Dust Guidance

‘The Control of Dust from Construction and Demolition Activities’ document (BRE, 2003)

- Eric Wright Sustainable Construction Toolkit (saved on the Wrightway electronic project file):

Sustainable Construction Toolkit

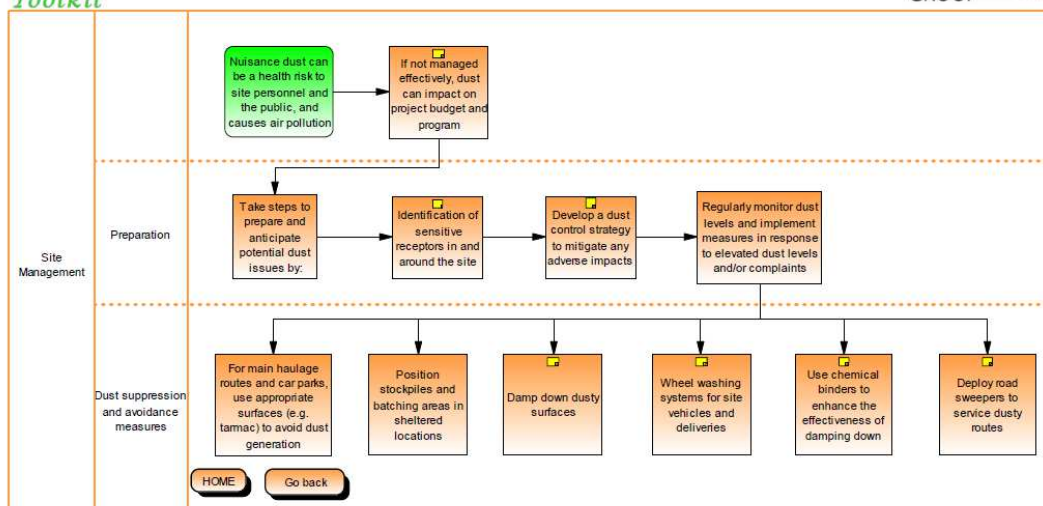



Fire Precautions

Upon the start of a contract, Eric Wright Construction's Project Manager will appoint a competent person to serve as the Fire Safety Coordinator, responsible for overseeing fire evacuation procedures and conducting muster checks.

The Project Manager, together with the Fire Safety Coordinator, will carry out a comprehensive fire risk assessment to identify potential fire hazards, assess those at risk, and review fire safety arrangements. The findings will be documented using the Fire Assessment and Arrangements Form.

After completing the Fire Assessment, the Project Manager and Fire Safety Coordinator will develop an action plan to mitigate hazards and ensure all necessary fire safety measures are implemented before occupancy.

The Project Manager and Fire Safety Coordinator will incorporate the completed Fire Assessment and Arrangements into the Contract Management Plan. The Project Manager will also integrate fire safety protocols into the site induction process to ensure all personnel understand the fire evacuation procedures. A site layout drawing showing fire safety measures will be displayed at key locations, with details recorded on a Fire Notice.

Fire Wardens will be appointed by the Project Manager, and training will be arranged, ensuring coverage during holidays or absences. The names of the Fire Wardens will be communicated and recorded on a Fire Notice. Fire Wardens will receive thorough training to understand their roles and responsibilities.

The Fire Safety Coordinator will establish a Fire Safety Inspection Record for each site, covering the entire year, to document weekly checks, evacuation drills, and annual equipment inspections. The Fire Safety Coordinator, or a designated individual, will perform weekly inspections of fire extinguishers, escape routes, fire signage, alarms, and fire brigade access points. These inspections will be documented in the Fire Safety Inspection Record.

Practice fire evacuation drills will be conducted approximately every six months at locations with a static workforce. For sites with high staff turnover, the frequency of drills will be increased. During these drills, Fire Wardens will ensure proper evacuation procedures are followed and report any issues to the Fire Safety Coordinator.

In the event of a false fire alarm, where no emergency is present, the alarm should continue, and the building evacuated to avoid confusion. This will be treated as a practice drill, and the Fire Safety Coordinator will record the incident on both the Emergency Evacuation Record and the Fire Safety Inspection Record. Any required actions will be noted on the Fire Assessment and Arrangements Form.

The Fire Safety Coordinator will ensure all fire-fighting equipment is inspected annually by a qualified individual. These inspections will be recorded in the Fire Safety Inspection Form. The Fire Assessment and Arrangements will be reviewed annually or after any significant changes, such as building alterations or changes in occupancy levels.

Light Control

Lighting must be able to provide safe working conditions for staff, and therefore the following measures will be put in place when situating & using site lighting.

- All lighting will be situated in such a manner as to provide as much lighting as is necessary for the work & no more, thereby reducing the risk of light pollution & the use of unnecessary numbers of generators.



- The lights will face downwards/sideways so that they do not shine into any nearby premises (particularly the residential receptors).
- Appropriate selection of innovative site lighting methods e.g. LED to improve the energy efficiency of the site and minimise the spread of the light beyond where required.

Wheel washing (prevention of Silt-laden run-off)

Eric Wright Group Ltd ensures that the working machinery, plant & vehicles, which may have the potential to cause an excessive dust or mud problem onto the public highway, will have the facility to wash down. This will be placed at a strategic point near to the road exit of the site, to prevent the mud being carried on to the road, with the addition of a road sweeper.



Site confines preclude the use of a permanent washdown station, we will employ a dedicated operative and plant (jet wash) to clean vehicles wheels prior to leaving site. This will be supplemented with the use of a truck mounted road sweeper which will attend site on a daily basis to ensure the access routes are kept clean.

The wheel wash measures will be implemented during the enabling works and early groundworks stages of the project.

During the enabling works we are going to tarmac access routes around the site to aid site tidiness and try and ensure the surrounding roads are kept clean.

Concrete Wash down Area

A siltbuster (or similar) concrete wash down facility will be installed in a location at the egress point from site, this self-contained treatment system will enable water to be treated, stored and re-used for wash down purposes.

- Effectively capture the concrete wash water and associated aggregate
- Aggregates are retained and any bleed waters and fine material are captured in the low-level tray.
- The alkaline waters weir out of the tray and will finally be stored, in a fully automated process, in the grey water storage tank for reuse.
- A digital pH controller constantly monitors the pH of the water, automatically neutralising the wash water with carbon dioxide (CO₂) to reduce the pH, removing risk to both the environment and to any operators.
- The treated grey water can be reused via the integrated pump and hose.
- Multi-functional with a tiny footprint and easy to transport and operate (can be shipped via conventional pallet networks)
- Enabling contractors to easily follow best environmental practise



ROADSIDE CONCRETE WASHOUT (RCW)

L: 2785mm
W: 1880mm
H: 1823mm

Design



The exact location of the concrete wash down area is to be determined.

Any on site surplus water discharge required will be discharged into the foul sewer network subject to the appropriate licences being obtained and agreeing the maximum discharge rates.

Road Sweepers


Road sweepers will be used as required to keep hard standing areas free from build up as much as reasonably practicable. All collected build up will be tipped off site.

Construction of the new drainage system following the enabling works

It is our intention to construct the new drainage system as early as possible during the construction period, so that surface water from the roofs and hardstanding's are discharged into the new systems as soon as is practicable in the construction programme.

Flooding & Weather Alert

Eric Wright Group Ltd Project Management Project Manager and Site Managers sign up to the Environmental Agency flood warning system <https://www.gov.uk/sign-up-for-flood-warnings> if the site is within a flood medium or high risk.

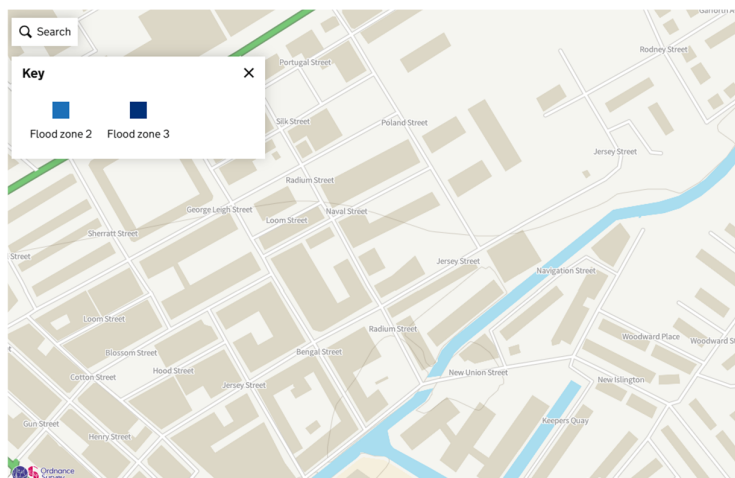



Based the Environment Agency Flood Zone Map, the Site is located within Flood Zone 1 (less than 1 in 1000 annual probability of river or sea flooding in any year) which is defined as having a low probability of flooding in the Planning Practice Guidance to the NPPF.

Weather Alerts (Surface Water Flood Risk)

Eric Wright Group Ltd Project Management Project Manager and Site Manager should sign up to the Met Office weather warning system <https://www.metoffice.gov.uk/public/weather/warnings>

Alert Level	Definition	Action	Responsibility
Yellow: Be Aware	Yellow warnings can be issued for a range of weather situations. Many are issued when it is likely that the weather will cause some low level impacts, including some disruption to travel in a few places. Other yellow warnings are issued when the weather could bring much more severe impacts to many people but the certainty of those impacts occurring is much lower. It is important to read the content of yellow warnings to determine which weather situation is being covered by the yellow warning.	Walk the site ensuring controls in place	Project Manager, Logistics/Site Manager, groundworker
Amber: Be Prepared	There is an increased likelihood of impacts from severe weather, which could potentially disrupt your works plans. This means there is the possibility of travel delays, road and rail closures, power cuts and the potential risk to life and property.	Clear slip trenches, ensure all hazardous waste stores in good order, ensure bunds are in place and clear in preparation for the weather. Ensure project specific drainage controls are in place.	Project Manager, Logistics/Site Manager, groundworker
Red: Take Action	Dangerous weather is expected and, if you haven't already done so, you should take action now to keep yourself and your works force safe from the impact of the severe weather. It is very likely that there will be a risk to life, with substantial disruption to travel, energy supplies and possibly widespread. You should avoid travelling, where possible, and follow the advice of the emergency services and local authorities.	Clear slip trenches, ensure all hazardous waste stores in good order, ensure bunds are in place and clear in preparation for the weather. Ensure project specific drainage controls are in place.	Project Manager, Logistics/Site Manager, groundworker



Environmental Management Toolkit

Over the past 25 years, the world has become increasingly aware of the plethora of environmental issues it faces, including global warming, air pollution, plastics, waste, ozone depletion, water pollution, resource depletion, biodiversity loss, environmental degradation and climate change.

As one of the least environmentally friendly industries in the world, we are central to sustainable development policies and as such, are coming under increasing pressure from government legislation, client demands, international targets, European targets and shareholders.

The construction industry has a major role to ensure that the built environment is shaped to deliver a sustainable future and reduce a number of environmental pressures, both globally and locally. The benefits to our business from improving our environmental performance are significant, from complying with law and policy, ensuring natural resources are passed to future generations, and benefitting our bottom line.

This toolkit has been created as a 'one stop shop' for environmental issues throughout all phases of a development. It includes topic specific legislative requirements, guidance documents, procedures, work instructions, checklists and best practice.

The toolkit should be used in partnership with the Quality & Environmental Department.

Toolkit Extract.

Introduction

Sustainability Tools

1. Site Establishment

2. Existing Environmental Features

3. Site Management

4. Waste

5. Procurement

6. Reporting

3. Site Management > Water Management

Useful documents / guidance

Water is a valuable commodity, especially in times of drought (an evermore common occurrence). As such, the cost of water is increasing, an already significant expense to the Group.

Reducing the amount of water we use is important both as a cost saving opportunity and to reduce carbon emissions. A recent study indicated that the industry could reduce water usage by 20% through the following:

- Installation of flow restrictors
- Installation of dual flush toilets
- Rainwater harvesting
- Changing our behaviours
- Procurement of more efficient systems
- Improved leak detection
- Fixing leaks sooner
- Carrying out water audits of owned assets
- Creating actions plans to reduce water usage
- Using treated / recycled water where viable

Report your water usage at the end of each month through either a KPI return or CSR return.



Environmental Management Toolkit

Home

Glossary

Useful Links



Contact us

Environmental Pollution Emergency Response Procedures

Together with the Environmental Management Toolkit our response flow diagrams below detail how this would be dealt with.



EWG-E-WI-038 - Environmental Emergency
Action Plan

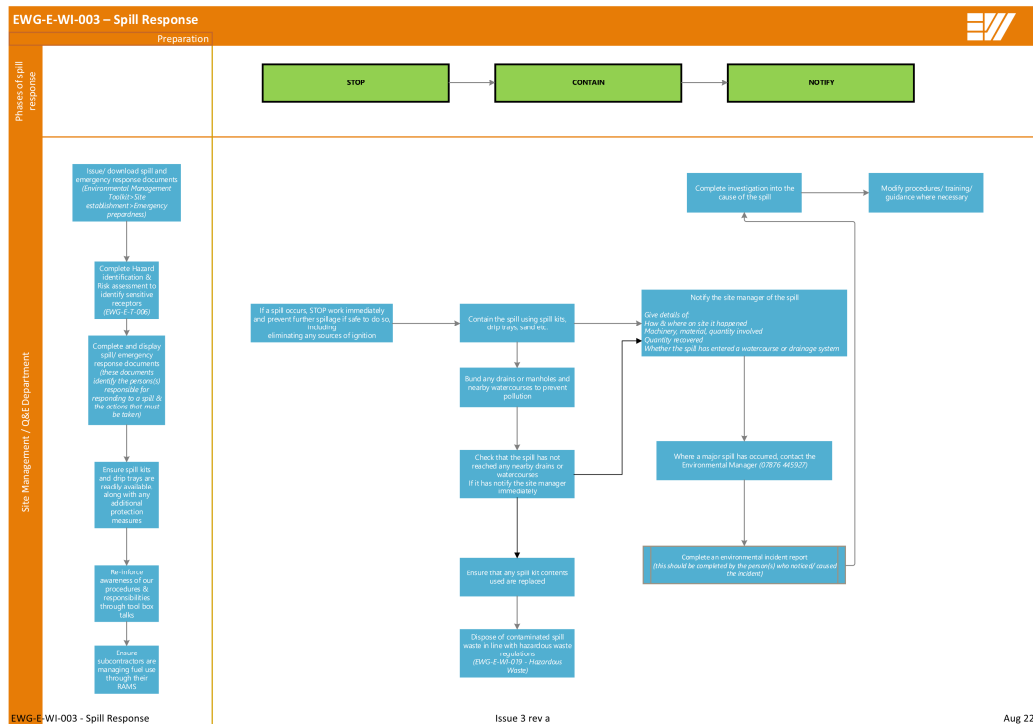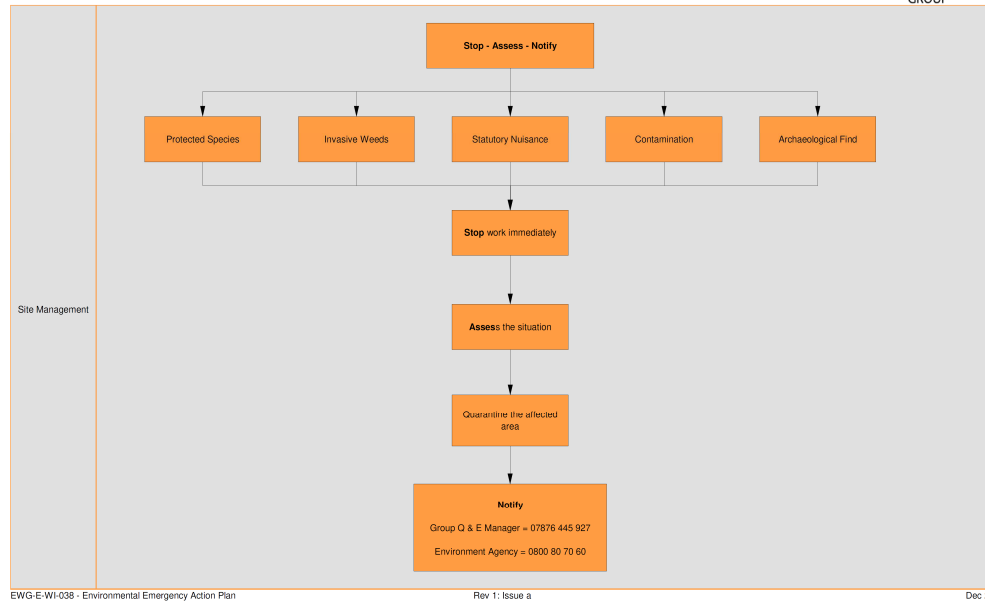



Communication

Considerate Constructors Scheme

The site will be registered with the Considerate Constructors Scheme in order to demonstrate our commitment to delivering the highest standards of construction while being a considerate neighbour to the local community. By joining the scheme, we aim to ensure that our operations are respectful, safe, and environmentally conscious, reflecting our values and responsibility. It also allows us to proactively engage with the public, reduce disruption, and maintain transparency throughout the project. Registering with the CCS reinforces our dedication to best practices and helps us build trust with residents, clients, and stakeholders across Ancoats.

Group communications to EWC Staff

Alerts are issued via a SHEQ **Bulletin** to communicate urgent environmental information. These are issued to all staff via email, and hard copies displayed in all site cabins. The Environmental Manager will contact any external body such as (Natural England, Environment Agency, Local Authority) when an imperative issue arises, thus keeping continual communication channels open.

Communication with Operatives

It will be mandatory, for all sub-contractors and operatives working on the site to undergo a formal **induction** prior to entering the site where all relevant environmental information for the site will be briefed. **Toolbox talks** will also be delivered, and records maintained.

Communication with the Local Community

To minimize disruption, local residents and businesses will receive hand-delivered newsletters with details of the project, including proposed start and completion dates and a summary of the work schedule. These letters will be distributed at least 14 days before the commencement of works and periodically throughout the project. Example below:

Brindle Road, Bamber Bridge

ERIC WRIGHT
CONSTRUCTION

Site Newsletter No. 1 - June 2014

Introduction

This is the second Brindle Road Housing newsletter.

The works comprise of the construction of 34 dwellings, 10 apartments and 24 houses.

The properties are all being built to a high degree of quality that we, at Eric Wright pride ourselves on, using the latest materials within a traditional, attractive design.

The Client is Progress Housing.

Key Dates

Start on Site:	02/06/2014
Demolition:	13/06/2014
New Building Works Begin:	09/09/2014
Building Works Complete:	15/03/2015
First Phase	04/04/2015
Second Phase	04/04/2015
External Works Complete:	04/04/2015

Architects Impression

MAPLE GROVE DEVELOPMENTS

Page 1

Brindle Road, Bamber Bridge

ERIC WRIGHT
CONSTRUCTION

Site Newsletter No. 1 - June 2014

Upcoming Works

We are currently up to roof level for plots 28-34, with the remainder of the site at first floor level to each plot.

Main drainage works to Brindle Road, adjacent to the main site entrance will commence on 15th December with a duration of 5 working days. Please be aware there may be some traffic disruption, but we will minimise this where possible.

Page 2

Working in Bamber Bridge, Preston

Eric Wright Construction have committed to using local labour and materials where possible while undertaking these works. We will be working with your local job centre to advertise any vacancies.

Please note that we have a surplus of wood, if anyone would like this for their log burner, please get in touch.

Site Contact Details

Any feedback, suggestions or requests can be directed to our site manager Joel Castles as below:

Telephone: 07825632902
Email: joelc@ericwright.co.uk

For more information on Eric Wright Construction please visit: www.ericwright.co.uk

Please follow us on:

Page 2

To minimize disruption, local residents and businesses will receive hand-delivered newsletters with details of the project, including proposed start and completion dates and a summary of the work schedule. These letters will be distributed at least 14 days before the commencement of works and periodically throughout the project. Example below:



A complaints log is maintained on site to record feedback from local residents. EWC staff are encouraged to proactively address complaints promptly and fairly. Environmental complaints will be escalated to the Environmental Coordinator to assist in formulating an appropriate response. Contact with the public may occur during and prior to construction via site notices, leaflets/letters, or in-person outreach. Sufficient notice will be provided, and contact details for Manchester City Council will be included on public consultation materials, Tel; 0161 234 5004.


Complaints Resolution

Complaints will be taken seriously and addressed by the Technical and Construction Team for site development-related matters. Their contact details will be included in public communications.

Site Noticeboard will be affixed to the hoardings, displaying:


- Contact details of the Site Manager
- The most recent newsletter
- Notifications of work opportunities
- The latest environmental dashboard, including waste and carbon data


By implementing these measures, the CEMP ensures clear communication, swift complaint resolution, and effective engagement with site neighbours.

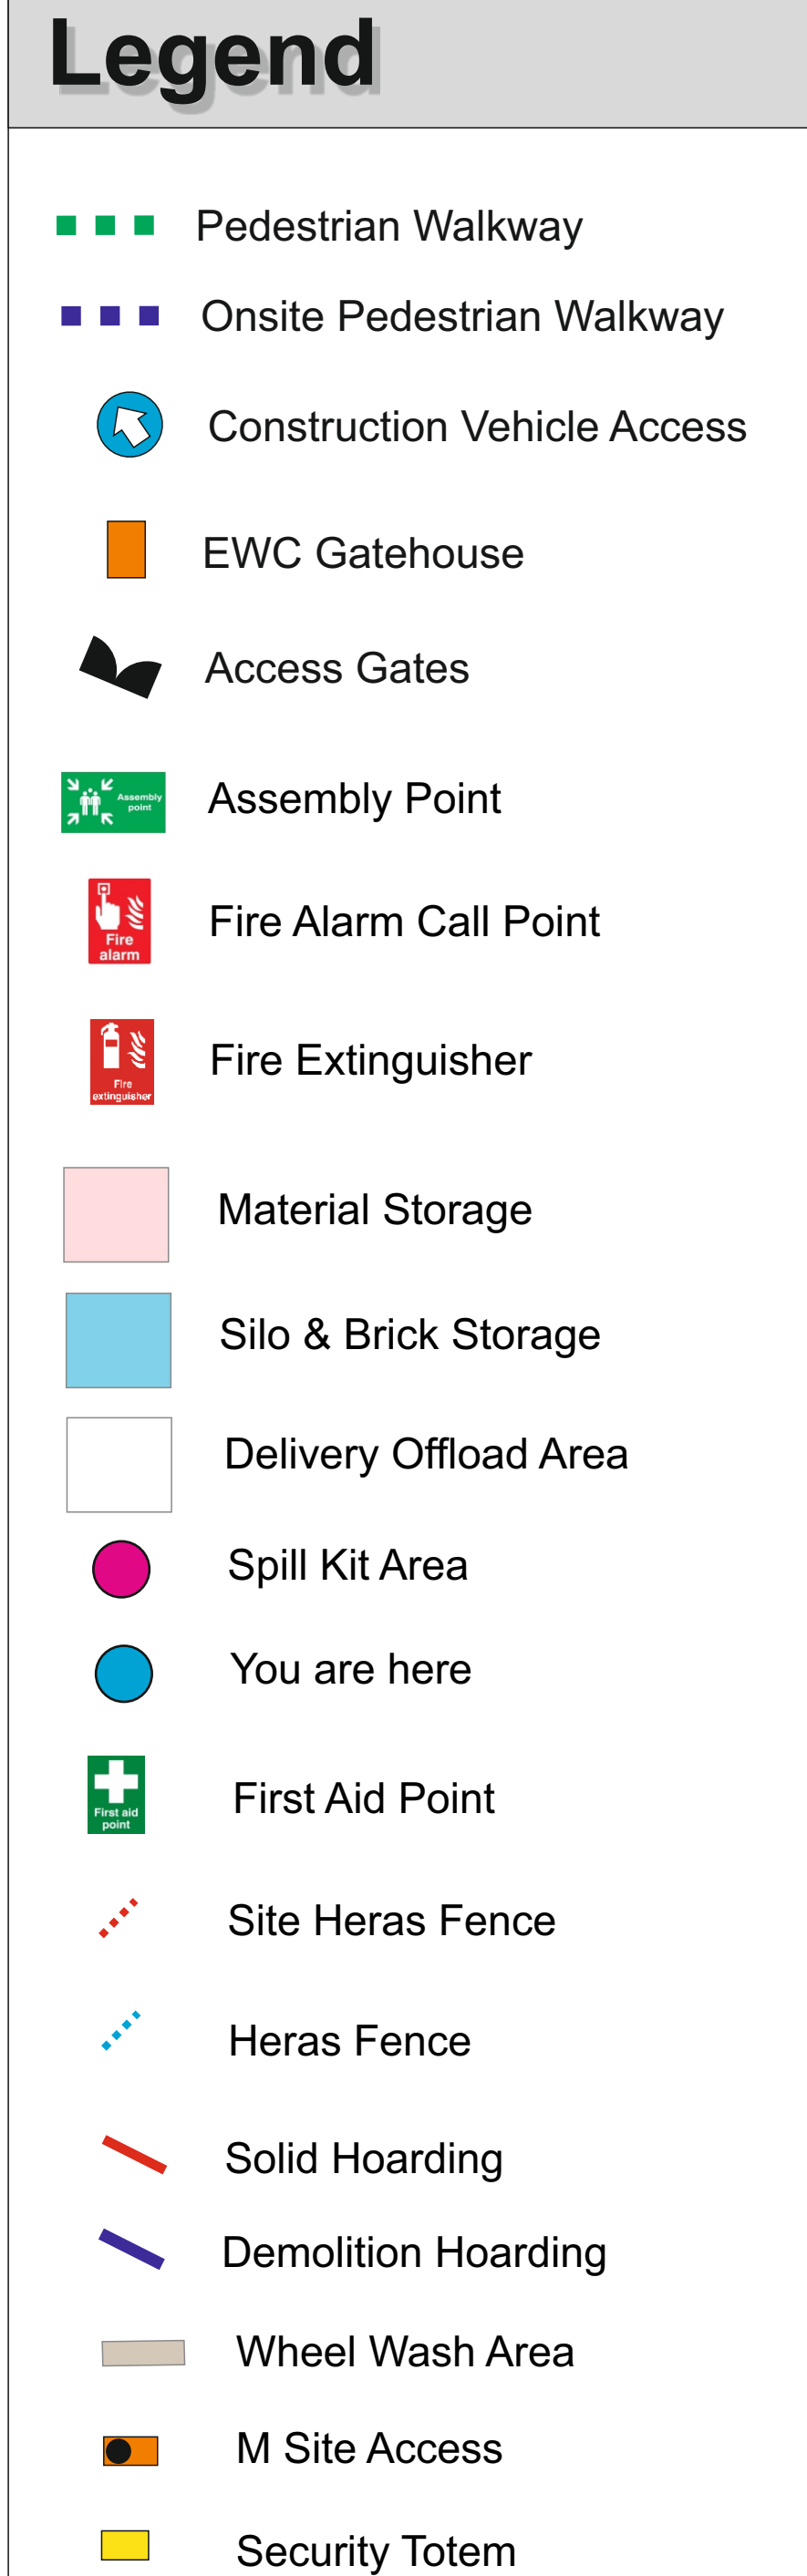

Sheet 2

[illegible]

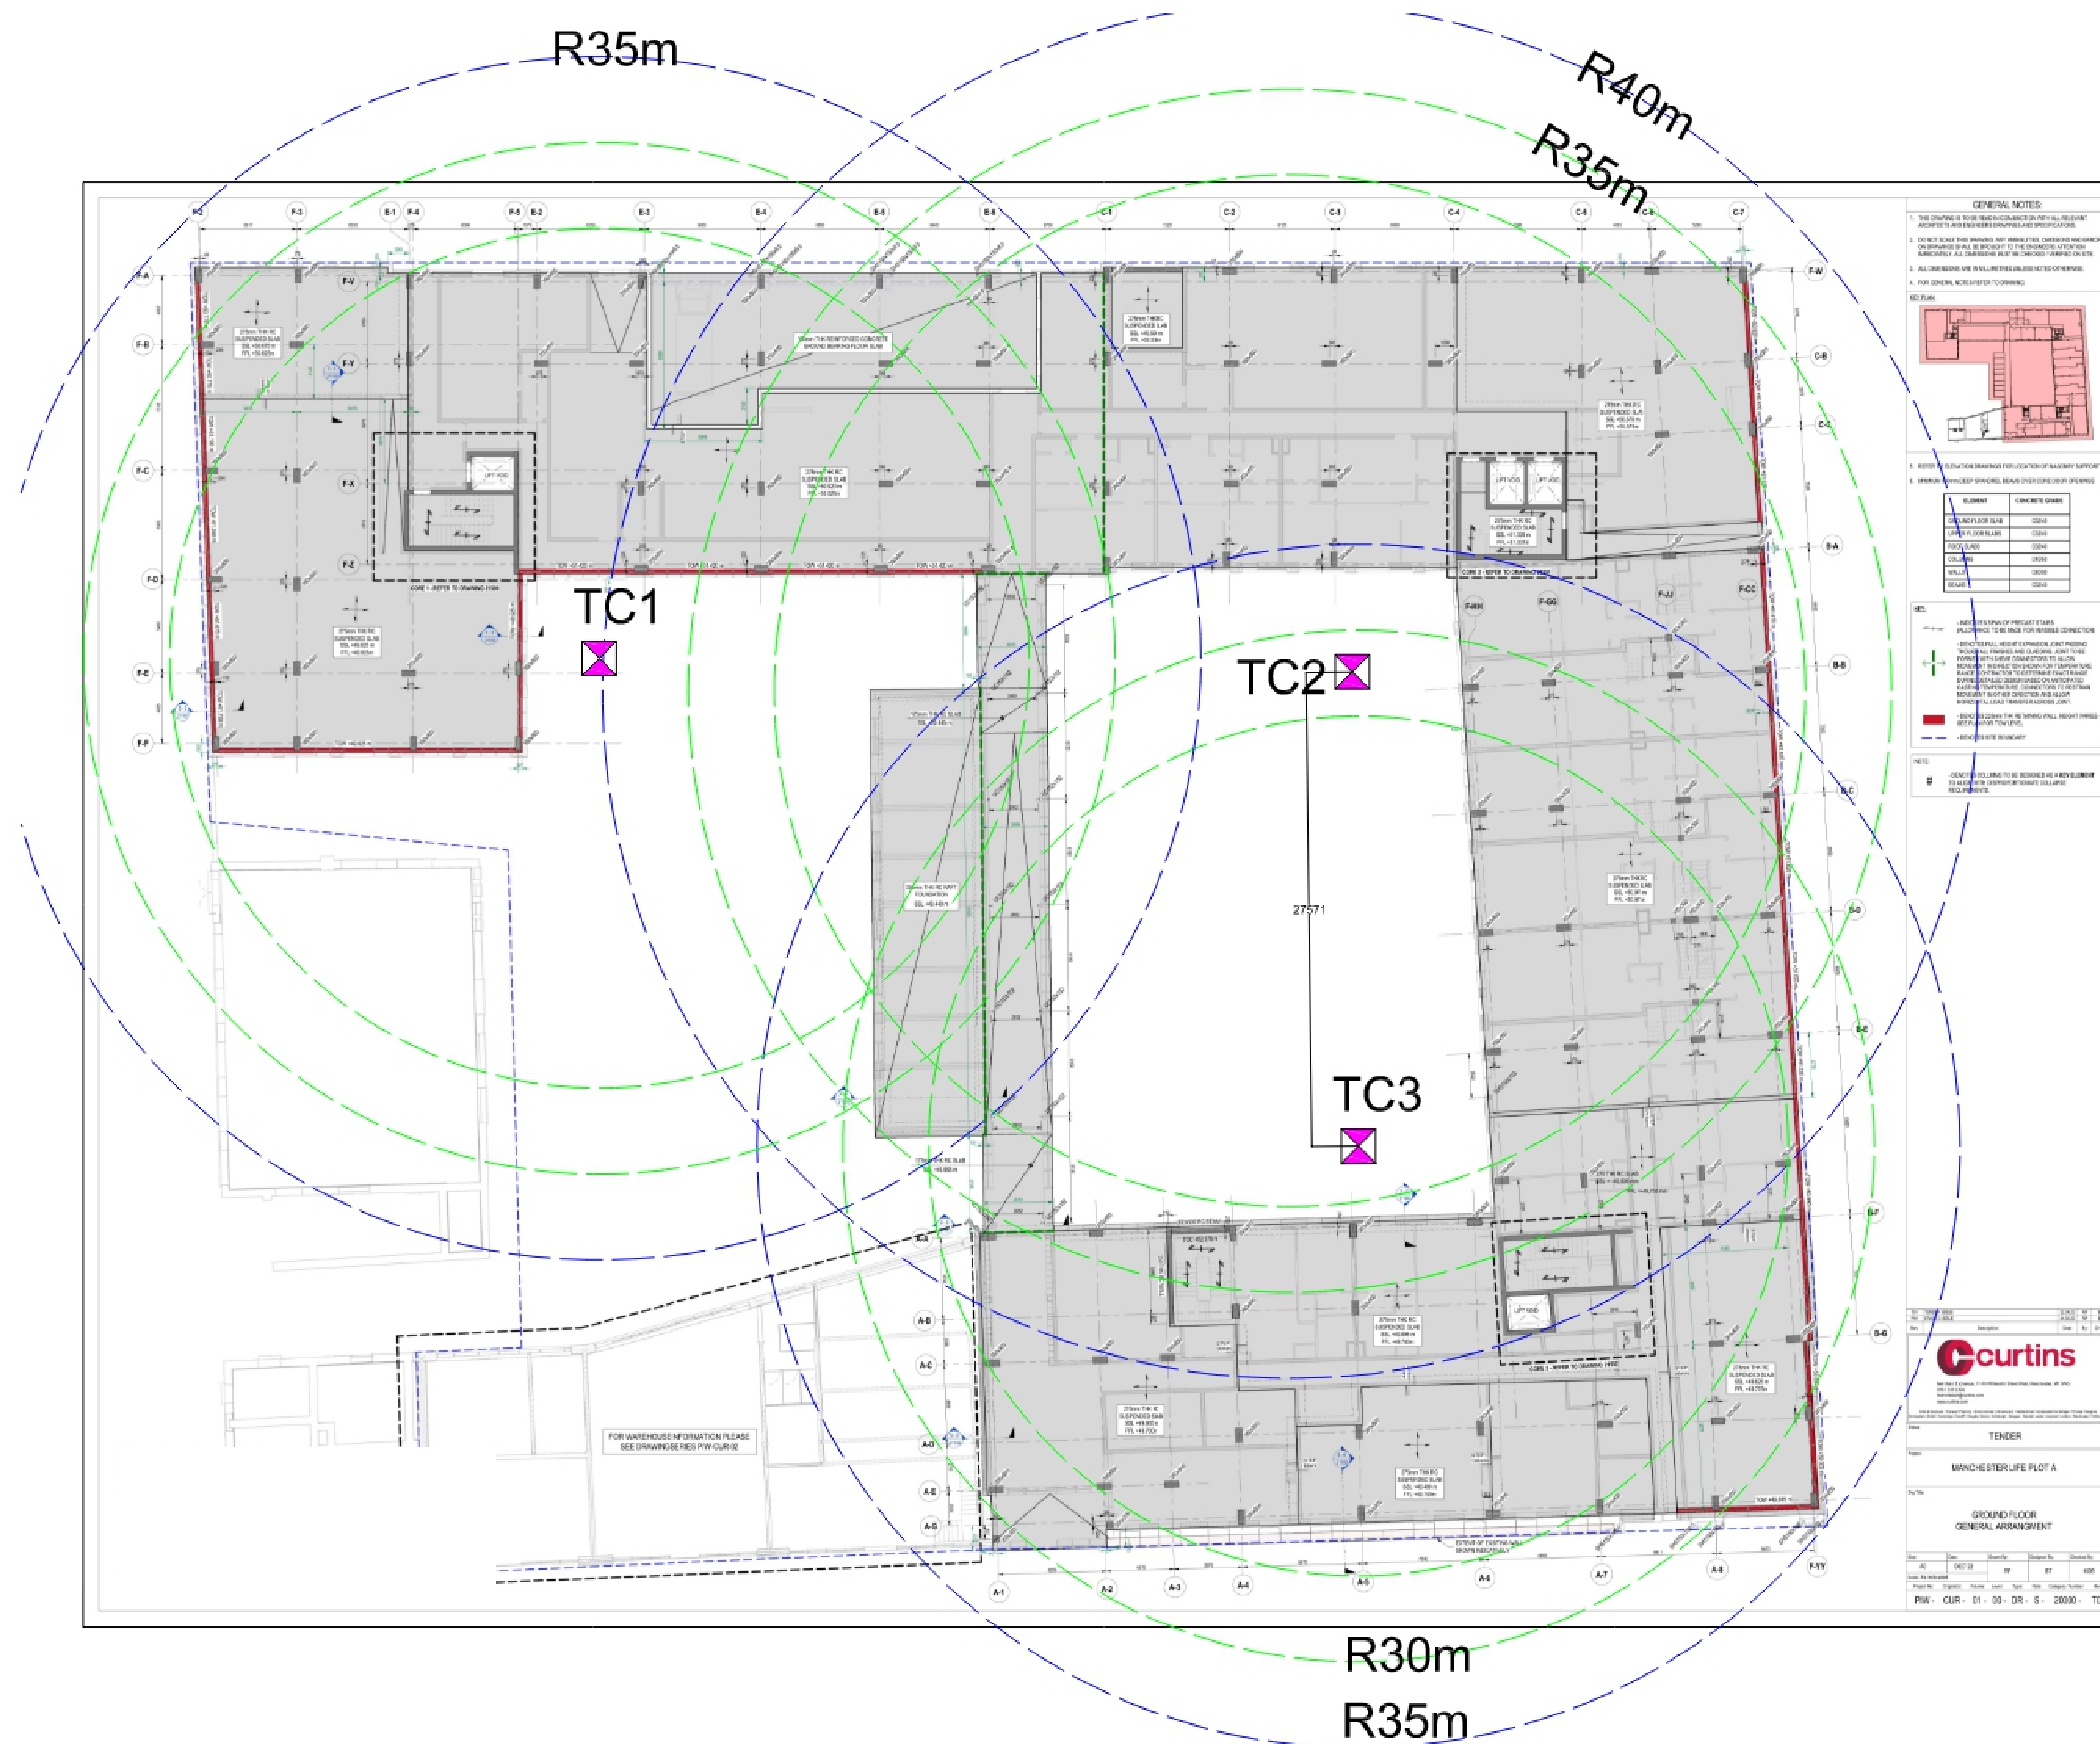

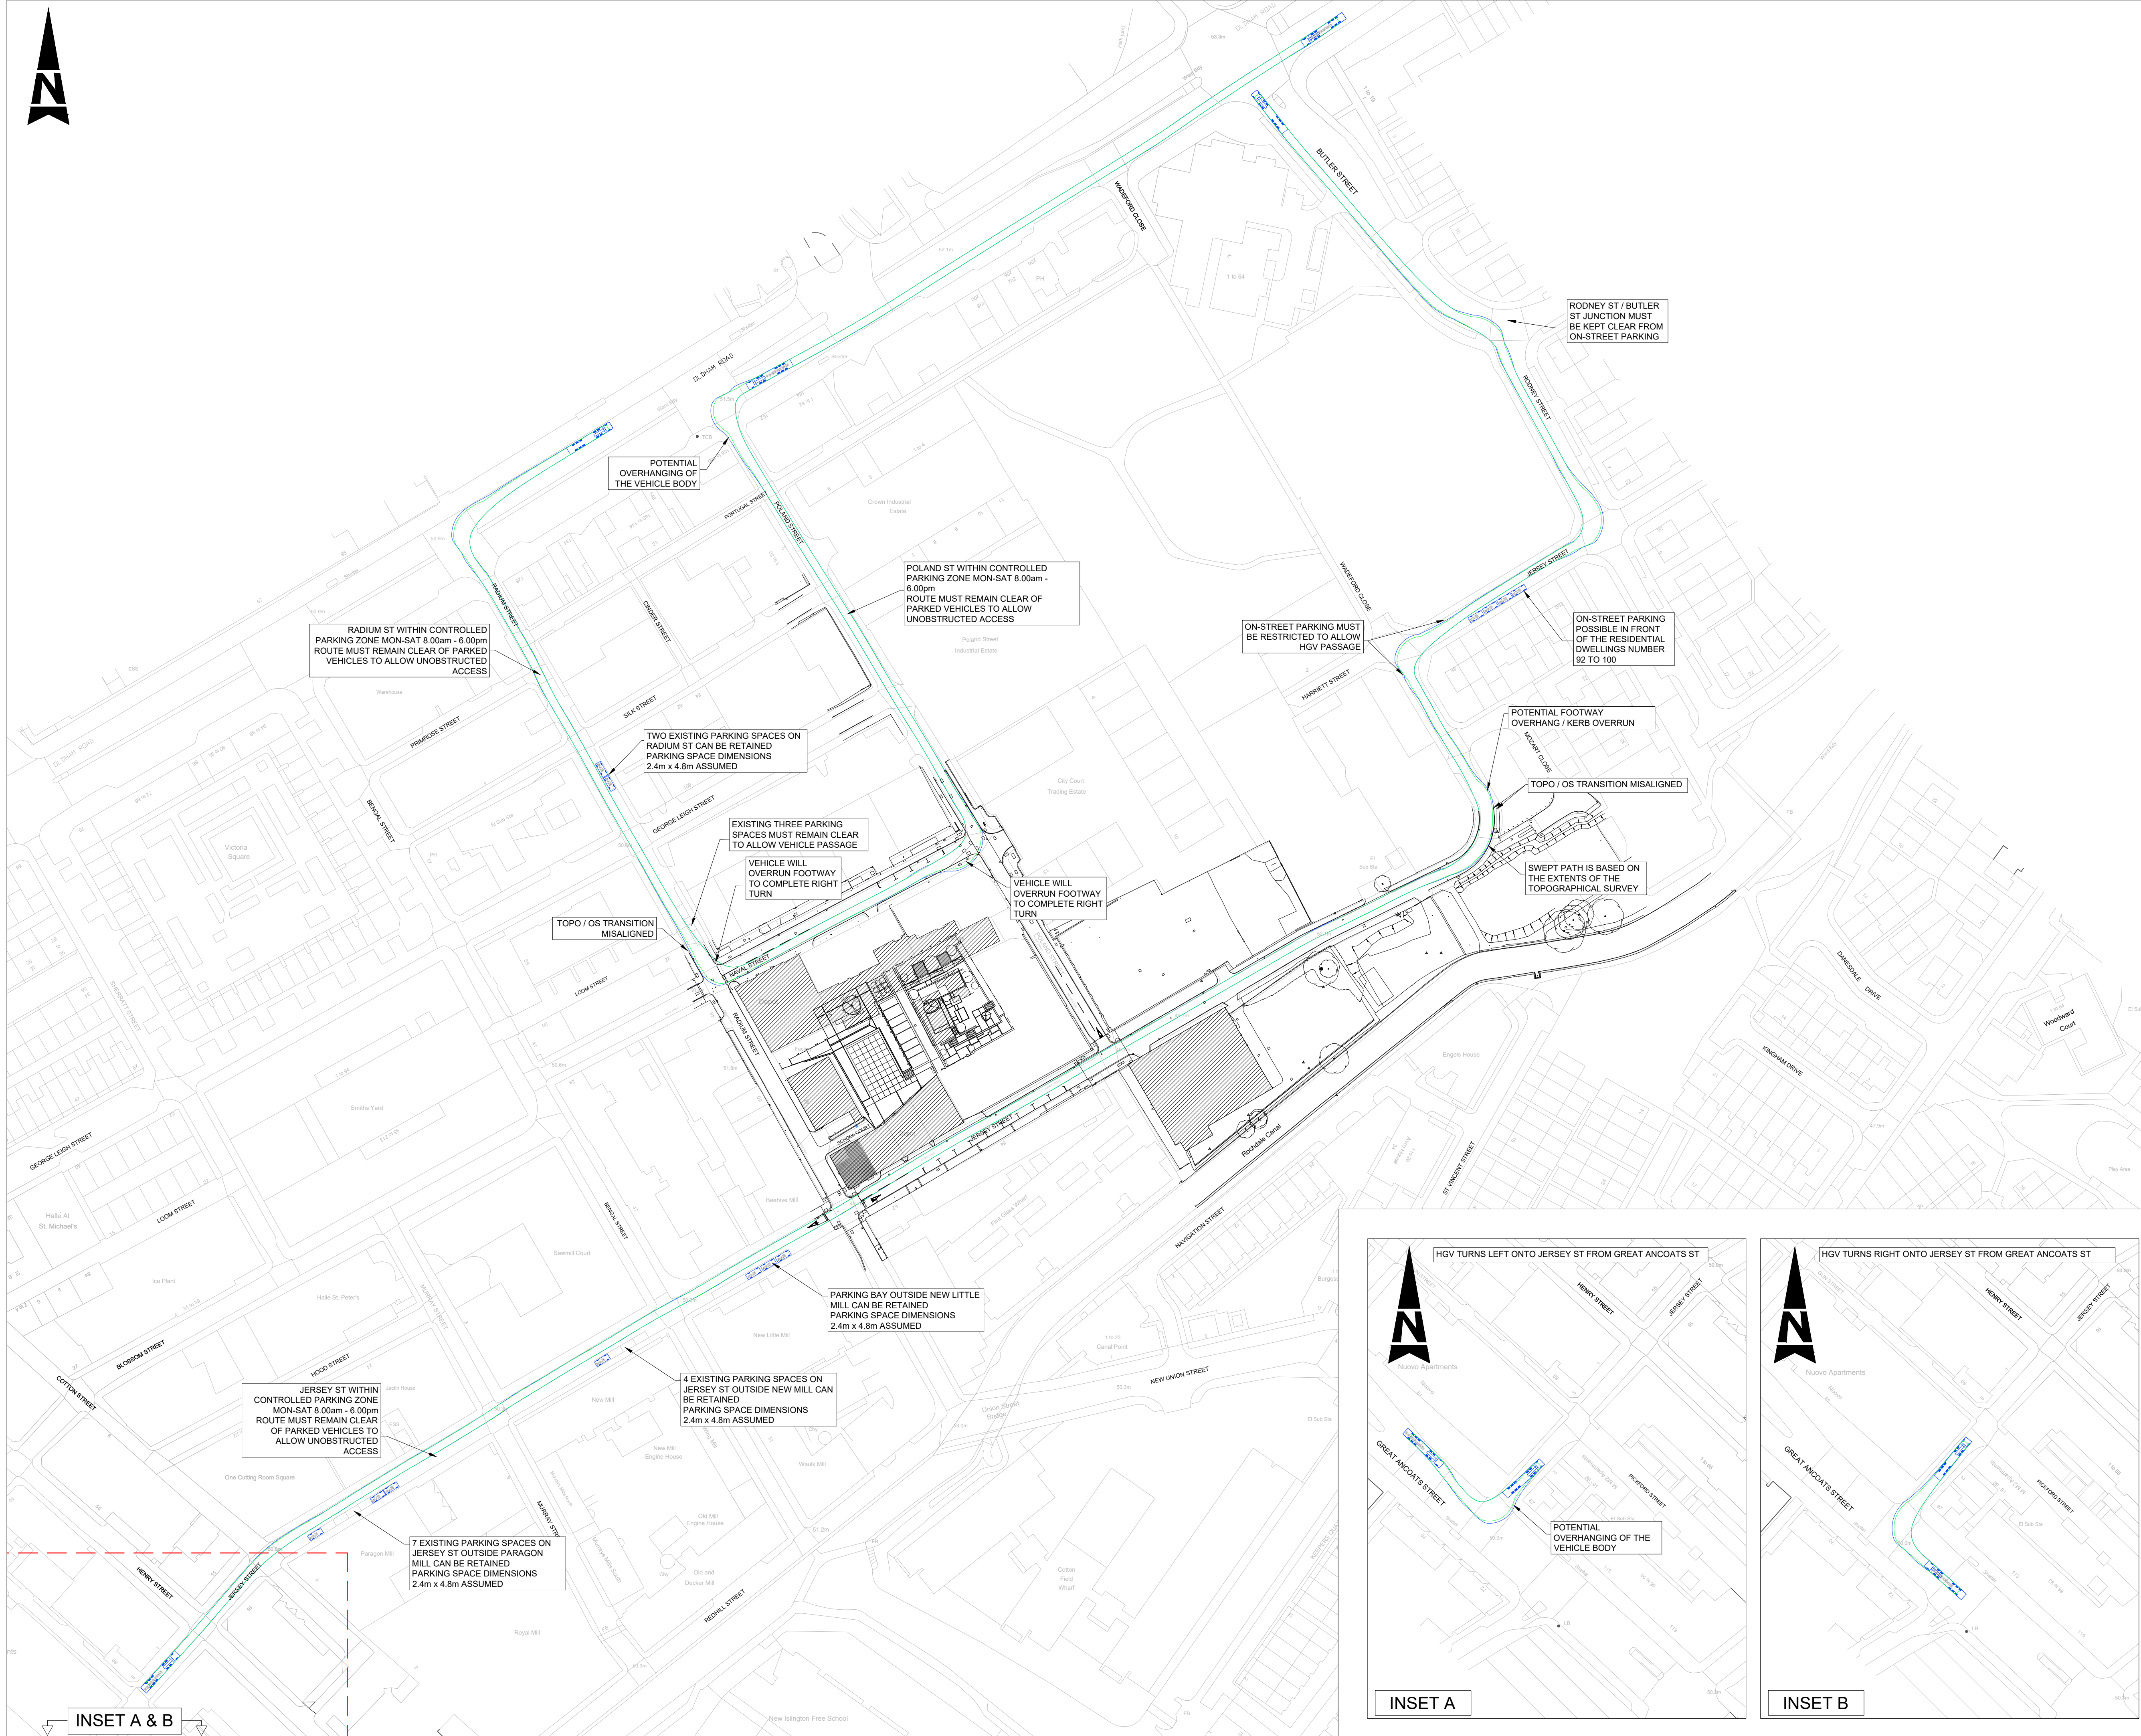

S2	FOR INFORMATION	12.05.25	MF KC
STAT	PURPOSE OF ISSUE	DATE	BY CHKD
P01	FIRST ISSUE	12.05.25	MF KC
REV	DESCRIPTION	DATE	BY CHKD

ORIGINATOR:

KODA

KODA PROJECT No: 240010

CLIENT:
ERIC WRIGHT CONSTRUCTION LTD

PROJECT:
PHOENIX IRONWORKS

TITLE:
HGV ROUTES TO SITE

SCALE: 1:1000@A1	DRAWN BY: MF	CHECKED BY: KC	APPROVED BY: KC
DRAWING No:			
240010-KOD-ZZ-00-D-C-0000051			
REV P01			
