

MOHO Façade Remediation Scheme



Issue: 01

Copy No.: Uncontrolled when printed

Prepared By:

Gareth Roberts CMIOSH AIEMA
Safety & Assurance Consultant on behalf of
H. H. Smith & Sons Ltd
Date: 12/04/23

This document is the property of H. H. Smith & Sons Ltd. It shall not be reproduced in whole or in part, nor disclosed to a third party, without the written permission of the author.

CONTENTS

- 1. KEY PROJECT INFORMATION**
 - 1.1 Contact Information
 - 1.2 Site Location
 - 1.3 Nature of Work / Introduction to Development
 - 1.4 Programme / Timings
 - 1.5 Hours of Work
 - 1.6 Development Control
- 2. COMPANY HEALTH AND SAFETY MANAGEMENT STRUCTURE**
- 3. TRAFFIC MANAGEMENT**
 - 3.1 Site Access and Restrictions
 - 3.2 Deliveries to Site / Supply Chain Management
 - 3.3 Use of alternative Modes
 - 3.4 Targets
- 4. CONSTRUCTION SITE MANAGEMENT & PROCEDURES**
 - 4.1 Unauthorised Access to Site/ Hoarding
 - 4.2 Compound Area
 - 4.3 Plant and Machinery movements
 - 4.4 PPE
 - 4.5 Security
 - 4.6 Buried Services
 - 4.7 Temporary support
 - 4.8 Permit to work
 - 4.9 Supply Chain management
 - 4.10 Intrusive site investigation works and monitoring
- 5. COMMUNICATION & MONITORING**
 - 5.1 Monitoring Arrangements
 - 5.2 Consultation and neighbourhood liaison
 - 5.3 Staff training and briefing procedures
 - 5.4 Complaint procedure
 - 5.5 Managing Change
 - 5.6 Monitoring Health and Safety Standards
- 6. WASTE MANAGEMENT**
 - 6.1 Site waste management plan
 - 6.2 Waste Disposal
 - 6.3 Asbestos

Construction Management Plan
MOHO Façade Remediation Scheme



7. ENVIRONMENTAL MANAGEMENT

- 7.1 Air Quality Monitoring
- 7.2 Control of Noise and Vibration
- 7.3 Control of Dust & debris on highways and air pollution
- 7.4 Schedule of environmental legislation and good practice
- 7.5 Register of permissions and consents required
- 7.6 Environmental Audit Programme
- 7.7 Environmental Risk Register

Appendix 1 Existing site plan

Appendix 2 Proposed site plan

Appendix 3 Site Set-up

Appendix 4 Traffic Management

1. KEY PROJECT INFORMATION

1.1 Contact Information

ROLE & RESPONSIBILITIES	ADDRESS	CONTACT DETAILS
Principal Contractor	H. H. Smith & Sons Ltd Rear of 95 Bury Old Road Whitefield Manchester M45 7AY	Role: Contracts Manager Contact: Mark Kelly Tel: 07968 151813 Email: markkelly@hhsmith.co.uk Role: SHEQ Director Contact: Juan Crous Tel: 07872952425 Email: jc@hhsmith.co.uk Role: QS Contact: Peter Birds Tel: 0161 280 3509 Email: peterbirds@hhsmith.co.uk Role: Site Manager Contact: Richard Slatem Tel: 0161 280 3509 Email: richardslatem@hhsmith.co.uk
Client	Mainstay Whittington Hall Whittington Road Worcester WR5 2ZX	Kate Magill M: 07929 610130 E: katemagill@mainstaygroup.co.uk Nigel Gaskell M: 07971 330891 E: nigelgaskell@mainstaygroup.co.uk
Client Representative	BWP 6 Hewitt Street Manchester M15 4GB	Darren Bailey M: 07867 676068 T: 0161 236 8133 E: darren.bailey@bwpconsultants.co.uk
Principal Designer	Spectra Pacific Court Pacific Road Altrincham WA14 5BJ	Stephen Wilkinson M: 07495 309 029 E: stephen.wilkinson@thespectragroup.co.uk
Architect	BTP Elizabeth House 486 Didsbury Road Stockport SK4 3BS	Vicky Saunders T: 0161 443 1221 E: vicky@btparchitects.co.uk

Client QS	Walker Sime The Corner House Fourth Avenue Trafford Park Manchester M17 1DB	Gavin Garner M: 07813 215922 T: 0161 872 9955 E: ggarner@walkersime.co.uk M: 07720 835909 E: imarsland@walkersime.co.uk
Façade Consultant	Wintech Quartz House Pendeford Business Park Wobaston Road Wolverhampton WV9 5HA	Irfan Hadhi M: 07487 823151 T: 01902 307430 E: I.Hadhi@wintech-group.com
Structural Engineer	Joule Consulting Engineers Timber Wharf 32 Worsley Street Manchester M15 4NY	Simon Waite T: 0161 832 3487 E: sw@jouleconsultingengineers.co.uk
Fire Engineers	Design Fire Consultants Ltd Suite 3.06 Jactin House 24 Hood Street Manchester M4 6WX	Neal Butterworth M: 07496 760 306 E: neal@designfireconsultants.co.uk
Building Control Inspectors	Ball and Berry Piccadilly House 49 Piccadilly Manchester M1 2AP	Richard Cymler M: 07562205664 T: 0333 0230262 E: richard@ballandberry.co.uk

1.2 Site Location

Moho Building 7 Arundel St, Manchester M15 4JP

See attached Site Plan and TMP

Current access to the site is either via traveling eastbound on the A56 Chester Road, turning left onto Hulme Hall Road and then turning right onto Ellesmere Street or, by exiting the Deansgate Interchange and taking the slip road northbound heading onto the A57(M) and turning left onto Ellesmere Street.


The current area is surrounded by a mixture of residential properties and commercial/industrial units.

Construction Management Plan


MOHO Façade Remediation Scheme



Below image; Site location plan, Phase 1 – full version in appendices.

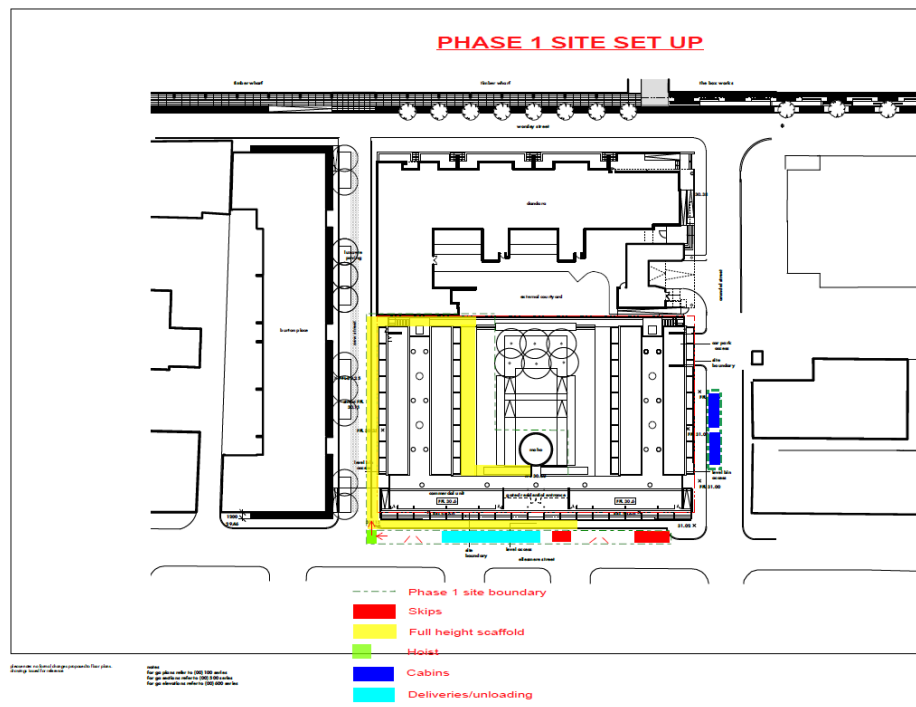

Below image; Site location plan, Phase 1 – full version in appendices.

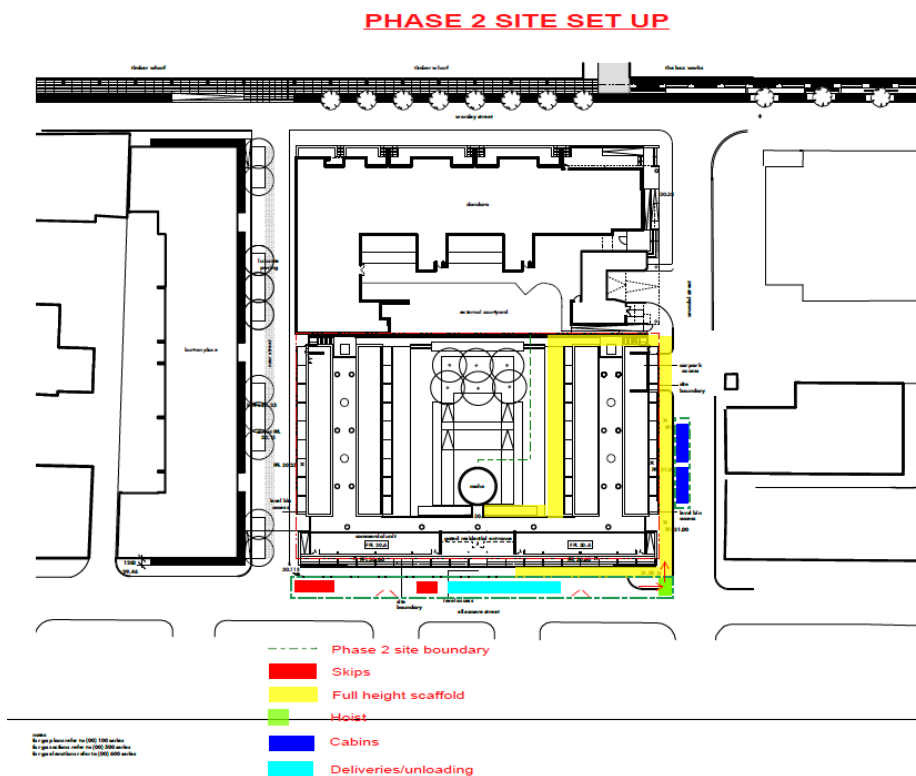

Nature of Work

The Moho (short for modular housing) apartments on Ellesmere Street is an Urban Splash development designed by the Liverpool architectural practice of Shed KM and completed in 2006 and is managed by Mainstay. The building is composed of prefabricated "living pods" built by the off-site construction specialists Yorkton. Each pod is designed around a central bathroom and kitchen area, with the living space and bedrooms either side. A large timber decked balcony allows for private outdoor space in addition to the resident's communal garden. Moho also features a convenience store, two bar/restaurants and offices on the ground floor and two floors of underground car parking.

The proposed works consist of:

- Replacement of insulated render system to all facades
- Provision of aluminium coping detail to the head of the parapet walls at roof level
- Replacement of timber decking to balconies
- Replacement of timber cladding to dining pods
- Replacement of timber louvre detail to balconies
- Replacement of timber cladding detail to the courtyard walkway façade
- Replacement of timber decking to internal walkways
- Replacement of timber cladding to the ceilings of the internal walkways
- Replacement of roof coverings to dining pods
- External decorations
- Replacement of intumescent coating system to steel beams/columns
- Replacement of balcony doors and frames

1.3 Programme / Timings

A programme setting out each particular element of the construction process to deliver the works in a safe, cost effective, sustainable manner & causing as minimum disruption has been developed. This will be issued to the design team & all other interested parties to ensure it is achievable.

1.4 Hours of Work

Working hours will be subject to a degree of flexibility, particularly where noisy activities are concerned, to minimise disturbance of the neighbours and residents.

- Monday to Friday 08:00 to 17:00
- Not work at all on Weekends, Public or Bank Holidays

Any work necessary outside of these hours must be by prior consent in writing from the Client & local authority.


The Site Manager and Project Manager will make regular contact with the affected residents to agree times and restrictions to ensure minimal disruptions to both parties.

Deliveries will be scheduled for outside of peak congestion hours on the surrounding busy roads.

1.5 Development Control

HH Smith & Sons Co Ltd notes that through outlining the proposals included within this document the local authority planning requirements with respect to Construction Logistics Plans will be followed.


2. PROJECT HEALTH AND SAFETY MANAGEMENT STRUCTURE

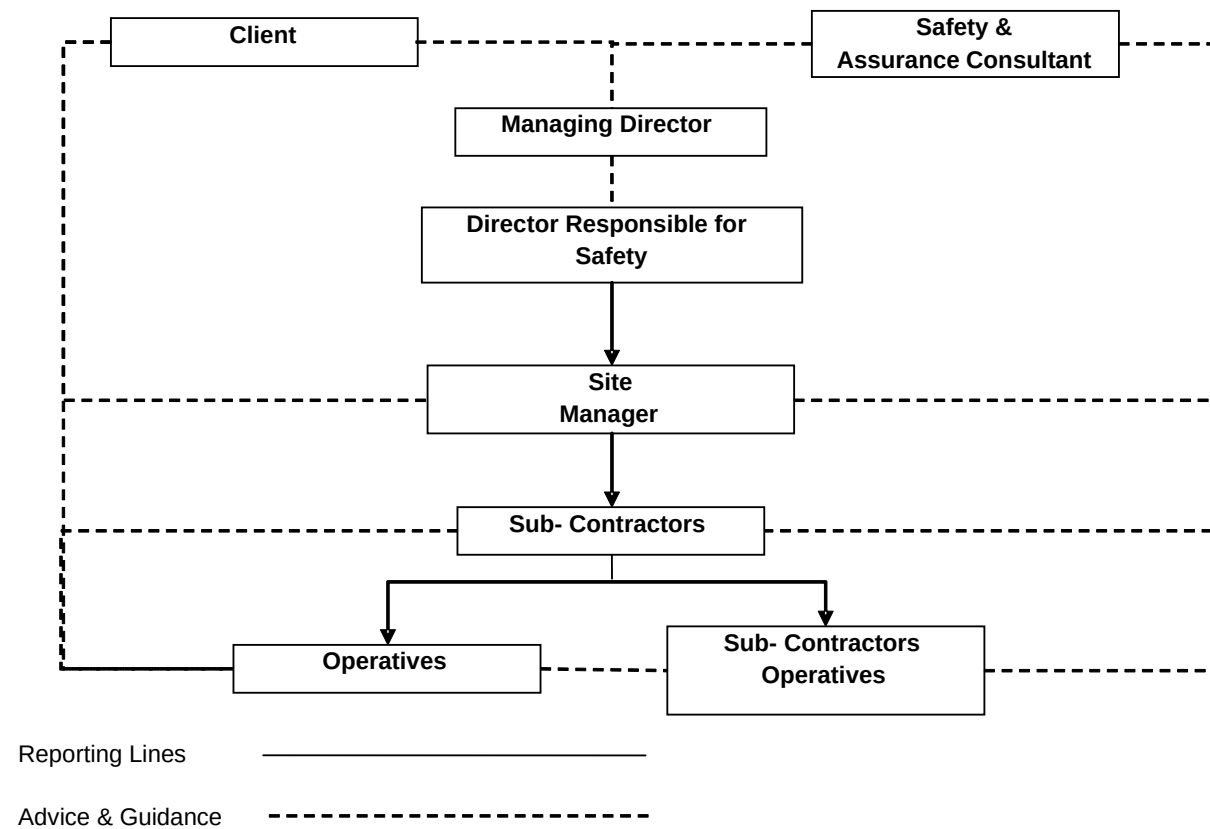

3. TRAFFIC MANAGEMENT, SITE ACCESS AND RESTRICTIONS

3.1 Vehicle access to site


Below image; traffic management plan – full version in appendices.

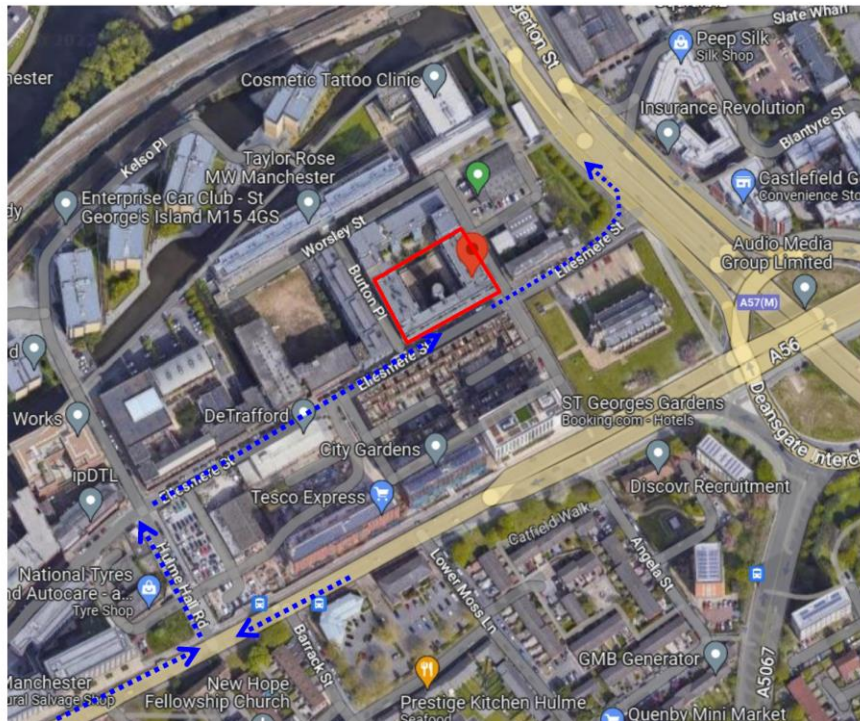

Key	
—	Site, Fenced off.
→	Main vehicle route into and out of site.

Proposal/ NOTES

- Delivery times will be restricted to avoid busy traffic periods at the start & end of the day.
- No deliveries to site between:
08:00 to 09:00 and 16:00 to 17:00
Or as agreed with highways.
- Delivery restriction in place to avoid disruptions to local business, schools & surrounding residents.
- All contract/ operative deliveries MUST be arranged & agreed with the site manager or site supervisors.
- Prior to deliveries accessing the site suitable arrangements will be made for the vehicle to be guided to & from site by banks man.
- Delivery procedure will be issued to entire supply chain that may be involved in the project.
- A copy of the plan will be issued to the council, highways & rail services for comments.
- All vehicles must access site as shown and leave site via Ellesmere Street and A57M.

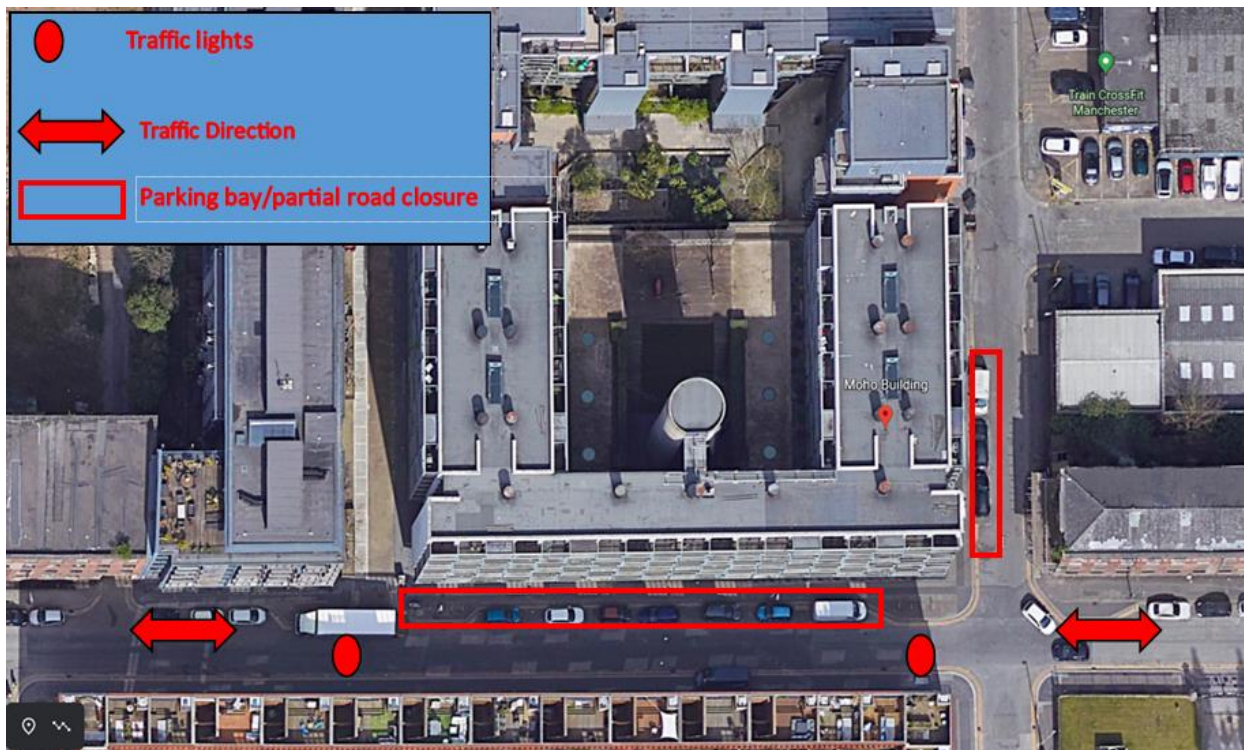

Construction Management Plan

MOHO Façade Remediation Scheme



All vehicle movements and manouvering on site, will be supervised by a banksman at all times with a strict 5mph speed limit. The Site Manager and banksman will ensure vehicle movements are clear of and not obstructing access for residents and local business customers so far as possible.

Access for public and emergency services must be maintained at ALL times.

Parking

HH Smith will take into account any parking / unloading restrictions imposed by the local authorities or police and will restrict construction traffic parking and unloading to the site as far as practicable. Parking for site staff will be available on the surrounding streets in authorised parking bays however given the location vehicle sharing and use of public transport will be encouraged

On site traffic

Movement of on-site vehicles and MEWP's will be closely monitored and suitable and trained banks man employed. Risk Assessments will be done where the movement of vehicles on site affects other site activities.

Suitable demarcation will be maintained by the HH Smith & contractors to separate vehicle and pedestrian routes at all times throughout the duration of the project.

Construction Traffic Speed Signage

Signs will be posted in visible locations to remind drivers that the speed limit for construction traffic on Trinity Street and around site is strictly 5 mph.

Pedestrian access

A dedicated pedestrian entrance/ turnstile with biometric recognition into the site compound area will be utilised as shown in the Site Plan.

The entrance will be segregated from the construction activities & vehicle movements with barriers from the site entrance to the site office to allow visitors & all operatives to access the office/ welfare without the need of PPE. A pedestrian gate leading onto construction areas from the compound will be controlled with a biometric lock.

Please see appendix 3 of this document for the site set up plans.

Preservation of Existing Footways and Carriageways

Prior to works commencing a photographic dilapidation survey of the footpaths and carriageways in the surrounding area will be carried out to ensure that any damage or unreasonable wear and tear on this infrastructure caused by construction activities can be remediated in full.

3.2 Deliveries to Site / Supply Chain Management

The site access point for deliveries will be as shown in the Site Plan and Traffic Management Plan.

The primary contact for all deliveries is the Site Manager who is based on site throughout all operations. The single point of contact for deliveries will be in place throughout. An alternative contact in case of unavailability or emergencies is available at HH Smith & Sons Site Offices.

All contract/ operative deliveries MUST be arranged & agreed with the site manager or site supervisors in advance. All deliveries no matter the size MUST be booked in on HH Smith's Delivery booking IN form on site at least 24 hours prior to the delivery.

Any delivery attempted to site and **NOT** booked in WILL be turned away from site.

Delivery routes/ entrance for unloading/ unloading areas will be highlighted with signs.

Deliveries to site will be arranged to avoid peak traffic times of the day within normal working hours to ensure minimal disruption to local business users, residents, and traffic movements.

Deliveries are not permitted between: **8:00 – 9:30 am and 16:00 –17:30** in order to avoid the peak congestion periods.

Any deliveries attempted outside the agreed delivery times, or in contravention of the booking in system will not be allowed to enter site and will be turned away. All sub-contractors and suppliers will be advised that non-compliance with the agreed delivery schedule will result in an appropriate sanction which will be identified in all contracts and purchase orders.

Delivery drivers must contact the site manager or site supervisor before entering site. Arrangements will be made for the vehicle to be guided to & from site by banks man.

Deliveries and collections should also be planned to de-conflict with those related to the normal operation of the Site.

Unloading & loading of deliveries & plant.

On arrival at the site, a banksman will guide the vehicle into site, the driver must stop and report to the site office.

Drivers **MUST** not park or leave vehicles in areas that obstruct the local highways & footpaths. Access for public must be maintained at ALL times.

Prior to deliveries accessing the construction areas/ delivery off load areas HH Smith will make suitable arrangements for the vehicle to be guided to & from site by banks man.

Banks man will guide the vehicle safely to the project offload area, including overseeing any reversing, and his instructions must be followed accordingly.

A telehandler will be used on site to unload vehicles & distribute materials around site to and from storage and construction areas.

All delivery drivers must have full PPE (i.e., hard hat, safety footwear, hi-vis vest or jacket and suitable gloves) before entering CDM construction areas

Reversing of vehicles on highways or site should be avoided. If reversing cannot be avoided suitable controls must be implemented; exclude pedestrians, use suitable number of banks man to guide/ control movements, vehicle audible warning when reversing, enough space to manoeuvre etc.

The TMP will be issued to all suppliers & contractors to ensure the agreed routes & procedures are followed to create minimum disruption on site and on local highways.

3.3 Use of Alternative Modes of transport & deliveries

The design Team currently anticipates that all materials transported to and from the site will be carried out by road.



3.4 Delivery Targets

Appropriate targets will be determined on appointment of sub-contractors and suppliers with the aim of reducing the number and frequency of deliveries thereby reducing the impacts of the construction phase on the college and local businesses.

These targets will be monitored monthly and reports issued to the supply chain where possible to drive improvement.

3.5 Wheel Washing

It is not anticipated mud from the construction site tracking onto nearby roads will be an issue given that all surfaces on site are paved or tarmac.

4. CONSTRUCTION SITE MANAGEMENT & PROCEDURES

4.1 Unauthorised Access to Site/ Hoarding and Signage

A heras fence hoarding will be maintained.

The site entrance will be kept closed at all times and signs will be erected around the perimeter of the site. Pedestrian access to the site will be through the authorised access point only and will be controlled through the booking in system and with the use of biometric locks. Information boards will be sited at entrances to identify access procedures and contact telephone numbers.

Fencing and gates will be fitted with signage to warn of the construction site danger and unauthorised access is prohibited. At the site gate a sign reminding operatives of the minimum site PPE requirements will be posted.

4.2 Compound Area

A permanent site office, canteen, drying room & WC facilities will be set up prior to works commencing.

For details of access to the site compound, plant and materials storage areas, please see Proposed Site Set Up Plan on page 5 of this document.

Security arrangements will comprise of a CCTV system installed to view strategic areas which will be remotely monitored during times when the site is non-operational. Out of hours security will be utilised due to the city centre location of the site.

4.3 Plant and Machinery movements

All necessary steps will be taken to reduce noise levels from plant, machinery and work activities in accordance with the Noise at Work Regulations 2005. Where reasonably practicable, noise levels will be reduced at source to their lowest reasonable level.

If necessary the Site Manager will carry out noise assessments with guidance from the Health & Safety Manager, where considered necessary and appropriate measures taken to protect site operatives, residents and members of the public from site noise.

Any possible excessive noisy work activities will be carried out at times that will cause least possible disturbance to the local residents, surrounding business or schools etc.

Noisy plant & equipment will be placed as far as possible from areas that may be affected from the noise. Noise dampening measure will be taken if required to reduce noise reaching sensitive buildings.

Banks man will guide plant if crossing pedestrian routes, highways or any other area where plant may come into contact with public or pedestrians.

4.4 PPE

All PPE will be in compliance with the HH Smith & Sons, H & S requirements, which are included as an appendage to the Health & Safety Plan. As a minimum, hard hat, high visibility vest and safety shoes must be worn at all times on site, and in addition, operatives must wear long trousers and short sleeve shirts as a minimum to protect them from UV radiation. HH Smith & Sons Co Ltd will make sun cream freely available to operatives in hot weather.

PPE requirements for specific high-risk tasks are included in the relevant risk assessments and method statements.

4.5 Security

Security arrangements will comprise of security staff out of site hours and a CCTV system installed to view strategic areas which will be remotely monitored during times when the site is non-operational.

No authorised access to site will be allowed, particularly by children. The site will be left secure at the end of each working day.

All of the Site workforce and visitors will sign in and out of the site as per the induction briefing on a daily basis.

All of the site workforce & visitors must wear company branded Hi Visibility Vests this will enable easy identification by client representatives, staff etc.

4.6 Buried Services

No groundworks are involved in the scope but should this change no breaking ground will take place until all services have been identified, proven as isolated back to source and capped off by a competent contractor with certificate of isolation held.

Services & utility surveys will be carried out before works start copies will be issued to all contractors that may be affected. Hard copies will be kept on site.

Prior to any task where ground will be broken with equipment or tools existing drawings or plans will be checked by the site manager for any possible services within the proposed work area, if no drawings or information is available a buried services survey will be carried out & findings recorded on the PF004.3 Survey for Buried Services survey.

A CAT scan & genny will be used by a competent operative with the relevant qualifications to carry out the buried services survey. If any services are found, they will be exposed and reported to contract administrator.

Prior to excavations works commencing a dig permit to work must be issued by the site manager.

4.7 Temporary support

All temporary works will be designed by competent person.

A Structural engineer has been employed to survey and issue any requirements for temporary support during the construction phase.

The temporary design will be issued to a competent person with qualifications relevant to structural work required to review & amendments made if any is required.

Once the design has been agreed a competent contractor will install/ erect the temporary support as per the design. The temporary works will be installed/ erected using the materials/ equipment specified as per the manufacturer instruction guidelines & design.

Once the temporary works have been installed/ erected a competent person will inspect the installation to check if it has been installed as per the temporary design.

Once the installation has been signed off work can commence.

No person can alter or dismantle the temporary support installed unless instructed or advised by a competent person.

4.8 Permit to work

A permit to work system will be in operation for the following hazardous activities within the site demise

- Working in occupied flats
- Works involving Hot Works
- Works on Electrical Systems/ services
- Works in Confined Spaces
- Works involving Hazardous Substances
- Works at Height
- Work in any occupied areas
- Works involving breaking ground

4.9 Supply Chain management

All traffic management plans & site logistic plans will be issued to supply chain.

Items to be sourced locally or from the same supplier to reduce the number of deliveries to site. Suppliers must follow procedures to avoid Deliveries during peak time traffic.

HH Smith & Sons Co Ltd will operate a delivery booking system. Deliveries can only be made by prior appointment and must be carried out under this agreement.

4.10 Intrusive site investigation works and monitoring

Various geotechnical and land surveys have been carried out by the client during the planning of the construction.

The reports and their findings will reviewed before construction work start to ensure any recommendation or protection measure works is carried out and briefed to the project management team & contractors. A copy of the plan will be held on site and will be included in the site Construction Phase Health & Safety Plan.

5. COMMUNICATION & MONITORING

5.1 Monitoring Arrangements

All procedures and proposals identified in this CEMP will be monitored and data collected as required to ensure that actual activities can be monitored and compared against the targets set.

Monitoring meetings will be held on a quarterly basis to review findings against targets.

All data identified in the CEMP will be collected by the site manager and will be reviewed on a weekly basis to ensure that targets are being achieved, or to agree measures required to rectify issues identified. The results of the data monitoring will be presented at site progress meetings on a fortnightly basis.

Data to be monitored should include the following:

Noise

Delivery / collection accuracy compared to schedule

Breaches & complaints

- Vehicle routing
- Unacceptable queuing
- Unacceptable parking
- Supplier FORS accreditation
- LEZ compliance
- Contractual conditions compliance

Safety

- Logistics related accidents
- Record of associated fatalities and serious injuries
- Ways staff are travelling to site
- Vehicles and operations not meeting safety requirements

Effectiveness of waste plan

- Percentage of recycled materials used in the development
- Percentage of materials re-used on site
- Percentage of waste recycled

5.2 Consultation and neighbourhood liaison

Prior to commencing works on site a letter drop will be done around the area notifying the residents & local business of the works start date & expected programme of the works.

The site manager's contact details will be included within the letter and will be encouraged to contact him for any feedback positive or negative.

The proposed site traffic management plans & delivery plans will be agreed with the local council and highways to ensure suitable routes is agreed so minimum disruption is caused to the local highways. Deliveries to site will be arranged to avoid peak traffic times of the day within normal working hours to ensure minimal disruption to the college, local business users, residents and traffic movements.

Prior to any abnormal deliveries due to size or number of vehicles i.e. muck shift wagons, concrete wagons for foundation & slab pours, steel deliveries to site on articulated wagons a leaflet/ letter drop will be done to notify the Neighbours & local business of this.

5.3 Staff training and briefing procedures

General Training

There is a commitment to ensure the training needs of all employees & contractors is reviewed on a regular basis and providing initial and refresher training for all of employees to ensure that adequate safety standards are met and maintained.

Employees will be given information on the risks to their health & safety. Training is linked to capabilities to ensure that anyone given a specific task is capable of carrying this out in the prescribed manner.

In addition, employees and sub-contractors will be provided with adequate health and safety training through induction briefings prior to commencement and “Tool box” talks aimed to make employees aware of the risks and necessary controls prior to commencing an operation.

Site Specific

All personnel employed on the site will receive a Site-Specific Induction before commencing work on site.

Site Liaison

Regular site meetings will be held with all Operatives, Client Representatives and major suppliers, at which the company will present the following information in relation to health, safety & environmental:

- A report on any accident along with any comments, lessons learnt and a copy of the accident report.
- Notes of any meeting between the client/local managers/police/emergency services.

Arrangements for co-operation and co-ordination between the on-site Operatives and major suppliers will be discussed and methods agreed for ensuring that all health and safety decisions will be passed between all parties and to the site operatives.

Meetings to discuss health and safety will be held as and when required either by the Client, the Principal Designer or HH Smith & Sons Co Ltd.

Any unforeseen eventualities during the execution of the works, which could have implications on health and safety, will be brought to the attention of the company’s Safety & Assurance Consultant immediately.

Any of the following events will be reported to the Client, Principal Designer and the Site Manager immediately.

- Accident/incident/Near Miss
- Visit to site by any Enforcement Agency.
- Improvement or Prohibition Notices issued by an Enforcement Agency
- Any formal warning issued to Operatives

5.4 Complaint procedure

A Complaint is defined as: A complaint by a stakeholder during or after the delivery of the service or product.

Receipt and Registration of complaints

HHS operate a QR Code based compliant system that allows anyone with a smart phone to lodge a complaint including photographs quickly and easily, and anonymously if they wish. Posters of the QR code will be displayed around site.

The recipient of a complaint shall, without any undue delay, acknowledge the receipt of the complaint and pass the details onto the Quality Representative.

The Quality Representative will record the details of the complaint assign a reference number.

Appropriate corrective actions and responses will be decided on as detailed below then recorded in a report.

Investigation and response to complaints

Where the recipient of a complaint identifies the complaint as being associated with a specific client order or area of work, which is under the control of a specific Contract Manager/Supervisor, it should be referred to him for the initial investigation and provision of a report to the Managing Director.

All other complaints shall be referred to the Managing Director who will forward it to the relevant Manager/Partner for action or if relevant deal with it himself. He may also pass the Customer Complaint Report to the Managing Director if necessary.

Details of any investigation and subsequent actions shall be recorded on the PF039 Feedback Log by the investigating Manager and on issue of a written response the Stakeholder Complaint Report shall be closed.

Where the action includes the issuing of a Non-conformance Report, the stakeholder shall be informed of its subsequent satisfactory closure.

Once closed the Feedback Log will be updated to show the date the issue was closed and who verified the close out.

5.5 Managing Change

The procedure set out below should be included within the construction phase health and safety plan which should be issued to all contractors & suppliers of the project to incorporate any procedures along with any other documentation produced for the project.

The Site Manager will act as the point of contact for the Principal Designer, Contract Administrator and the Client. If this appointment changes, all parties involved will be notified.

Procedures for considering the health, safety & environmental implications of design elements of the HH Smith & Sons packages.

Where a change in design is required then HH Smith & Sons Co Ltd will consult with the Designer to consider safety implications of possible design changes; for example:

What new hazards arise from the design changes

How these hazards can be designed out or minimised and any additional safety measures that may be required.

Procedures for dealing with unforeseen eventualities during the project execution (resulting in substantial design change and which may affect resources).

HH Smith & Sons Co Ltd will consult with the Designer to consider:

- Safety implications of the proposed design changes
- What new hazards arise from the proposed design changes
- How these hazards can be designed out or minimised and any additional safety measures that may be required.

Liaison with any Sub-contractor who may be involved or possibly manufacturers/supplier may be necessary during consultations, but in all cases the Contract Administrator/Principal Designer will be advised on the outcome and the effect upon this Health and Safety Plan.

Monitoring of Health & Safety Standards

Regular visits will be made by H. H. Smith & Sons Ltd representatives who will carry out site inspections and prepare reports, drawing any non-compliance to the Site Manager's immediate attention. The Site Manager will also carry out ad-hoc safety tours of the site. Any serious situations or continuing non-compliance will be reported to the Managing Director and the Client.

6. WASTE MANAGEMENT

6.1 Site waste management plan

An environmental plan along with a site-specific site waste management plan will be developed for the project.

The construction contract will result in a variety of wastes arising that shall be minimised as far as practicable, and the remainder managed in keeping with UK and international legislation. This plan provides detailed guidance to ensure that waste minimisation and effective waste management is practised. Additionally, resource management and storage & ordering procedures are a crucial element of waste minimisation and thus are included in this plan. Waste practices specified are also designed to achieve the client and HH Smith & Sons aims and objectives for waste management.

The Client Waste Objectives and Targets

The Client's waste objectives and targets should be obtained during the planning stage of the contract/project and incorporated into HH Smith & Sons waste objectives and targets for the duration of the contract/project.

- Reduction of wastes from services;
- Restricting or suspending use of hazardous substances; and
- Identification of areas where energy savings can be made;

HH Smith & Sons Waste Objectives and Targets

- Quantify all significant waste streams and their disposal routes
- Investigate and report on reuse or recycling possibilities for all wastes;
- Set reduction targets for all wastes going to landfill
- Review facilities for management of the creation, storage and disposal of hazardous wastes
- 90% of waste materials recycled via waste transfer station with remaining 10% diverted from landfill to waste to energy.

6.2 Waste Disposal

The waste disposal process will be in line with site waste management developed specifically for the project.

Rubbish, debris, redundant materials, etc will be collected regularly from the work area, placed into segregated skips and not allowed to accumulate. Skips will be lockable and placed on skids to prevent damage to existing surfaces.

Arrangements will be made with a locally licensed Waste Disposal Contractor who will collect the skips regularly for disposal at an appropriately licensed disposal station.

6.3 Asbestos

Given that the building was constructed in 2006 it is reasonable to assume no asbestos will be present in the structure.

7. ENVIRONMENTAL MANAGEMENT

7.1 Air Quality Monitoring

The air quality will be monitored where there is evidence of airborne hazardous materials or there is a risk of fumes or dust affecting the local area and take the required corrective actions.

7.2 Control of Noise and Vibration

All necessary steps will be taken to reduce noise levels from plant, machinery and work activities in accordance with the Noise at Work Regulations 2005. Where reasonably practicable, noise levels will be reduced at source to their lowest reasonable level and PPE must only be employed as the last resort.

If necessary the Site Manager will carry out noise assessments with guidance from the Health & Safety Manager, where considered necessary and appropriate measures taken to protect site operatives, residents and members of the public from site noise.

Any possible excessive noisy work activities will be carried out at times that will cause least possible disturbance to the local residents, surrounding business or schools etc.

It is not likely that the scope of works will cause significant noise levels, but the client will be given prior notice should this change.

7.3 Control of Dust & debris on highways and air pollution

The existing tarmac road areas leading onto site & car park areas that will be used as delivery areas will be retained during the construction period thus minimise the risk of dust or debris on the highways.

All necessary precautions will be taken to protect the college staff, pupils, members of the public and site operatives from the effects of the inhalation of respirable dust that may be caused by the works.

All operations that may create dust will include a type of dust suppression technique, such as damping down or mechanical dust extraction. This applies specially to cutting or grinding operations. All operatives will be issued with and required to wear suitable goggles and masks or respirators, wherever this type of work is being carried out.

Vehicles transporting aggregates or waste to & from site will be suitable covered.

Where there is a stockpile of soil these areas shall be damped down to reduce the risk of dust emissions. The handling of spoil should be kept to a minimum to reduce the emission of dust.

No materials will be burned on site.

The site manager will arrange for the surrounding highways to be swept with a road sweep as and when required.

Emissions from plant will be controlled by ensuring plant is in good order by regular services & maintenance. Plant must not be left running for long periods when not used.

The reuse of materials on site will be encouraged.

Plant used on site to crush materials should be done with an environmental permit issued from the local authority. The works must be done as per the procedures within the permit. Where plant is used to recycle materials the appropriate Environmental Permit from the environmental agency shall be obtained.

7.4 Schedule of environmental legislation and good practice

A Register of Legislation applicable to all the activities and operations, which have an effect upon the environment will be included within the site environmental plan.

In addition, where relevant a current record of the various agreements, commitments and conditions associated with obtaining planning approvals, licences and consents have been developed.

In order to ensure that the legal requirements placed upon individuals undertaking specific tasks are communicated at the appropriate point, all environmental procedures, work instructions produced within Environmental Management System will carry a section detailing the legislation, requirements and impact.

7.5 Register of permissions and consents required

Street works – alterations to highways, entrance to site.
Partial Road closure and Pavement Closure

7.6 Environmental Audit Programme

The monitoring and measurement of the activities and operations carried out at the site, which pose significant risks to the environment, and the recording of information to track performance and conformance with the Environmental Policy, Legislation, Assurance Objectives/targets and this Management Plan, will be undertaken through the following:

- Weekly work-place Environmental and Safety Tours by the Site Manager
- Monthly Inspections undertaken by the SHEQ Manager initiating corrective action when appropriate.
- Reports to Senior Management via the management review.
- Periodic review of legislation, the register of significant environmental aspects & impacts
- Third Party Audits and Inspections

The Site Manager will ensure that the monitoring takes place within the specified timescales with guidance and assistance provided by the SHEQ Manager.

Activity or Subject	Responsibility
Monthly Inspection & production of report	SHEQ Manager
6 Monthly Inspections & Production of report and NCRs if applicable	SHEQ Manager
Third Party Audits	Responsible 3 rd Party i.e. Client's Representative with assistance from Site manager &/or SHEQ maaher
Review of Inspection Reports	Managing Director & SHEQ Manager
Close out of NCR	Recipient of NCR
Management Review	Managing Director Responsible Manager Management Team

7.7 Environmental Risk Register

HH Smith & Sons Co Ltd is committed to implementing appropriate strategies and processes that identify, analyse and manage the risks associated with these internal & external influences as a means of minimising the impact of undesired and unexpected events on our business activities.

We will therefore via; the Aspects and Impacts Register, Risks and Opportunities Register, Business Objectives, Commercial Risk Register and the Business Continuity Plan:

- Identify business objectives that reflect the environmental interests of all our stakeholders
- Identify both the environmental threats to the achievement of our business objectives and possible opportunities
- Control and manage our exposure to environmental risk by appropriate risk reduction and mitigation actions
- Regularly review our exposure to all forms of risk and reduce it as far as reasonably practicable or achievable
- Apply robust risk management processes as part of a wider management system
- Educate and train our managers in environmental risk management
- Regularly review the environmental risks we face as a result of our business activities and of the business and economic climate in which we operate
- Identify cost effective risk treatment options
- Identify and regularly measure key risk indicators and take appropriate action to reduce our risk exposure

This Construction Environmental Management Plan (CEMP) specific to the Project & will be designed in response to BS EN ISO 14001: 2015 Environmental Management Systems, HH Smith & Sons Co. Ltd' own environmental policy and Assurance objectives and targets. The CEMP will be utilised throughout the life of the project and will be regularly reviewed by the Safety & Assurance Advisor to ensure its ongoing suitability to the work undertaken at the site.

A Sustainability Risk Assessment & Mitigation register is intended to ensure that environmental, social and economic (sustainability) issues are assessed, understood and managed in all key procurement decisions that relate to the procurement of goods (products) for the project. This register involves the identification of key impacts on the environment, society and the economy.



Appendix 1 Proposed site plan



Appendix 2 Site Set-up



Appendix 3 Traffic Management Plan
