

Arboricultural Impact Assessment (AIA)

August 2021

Arcadia Library and Leisure Centre

Yew Tree Avenue

Levenshulme

Manchester

M19 3PH

U R B A N
G R E E N

QUALITY MANAGEMENT

Project No.:	UG1207			
Project:	Arcadia Library and Leisure Centre			
Location:	Arcadia Library and Leisure Centre, Yew Tree Avenue, Levenshulme, Manchester, M19 3PH			
Title:	Arboricultural Impact Assessment			
Document Type:	BS 5837			
Date:	10/08/21			
Prepared By:	Elizabeth Anderson			
Checked By:	Robert Hickey			
Approved By:	Katie Bird			
Revision Status:				
Rev:	Date:	Issue/Purpose/ Comment:	Prepared:	Checked:

CONTENTS

1. Executive Summary	1
2. Introduction	2
2.1. Instructions and references	2
2.2. Scope.....	3
2.3. Documents provided.....	3
2.4. Limitations	3
3. Legislation.....	4
3.1. Tree protection status	4
3.2. Wildlife	4
4. Arboricultural Impact Assessment (AIA)	5
4.1. Summary of the development.....	5
4.2. Tree constraints	5
4.3. Root Protection Areas (RPAs) explained.....	5
4.4. Impacts of development	5
4.5. Tree surgery works	5
4.6. Protective fencing.....	6
4.7. Boundary treatments.....	6
4.8. Temporary site cabins	6
4.9. Utilities	7
4.10. Recommendations	7

Appendix 1 – Tree Data Schedule

Appendix 2 – Tree Schedule Definition of Terms

Appendix 3 – Tree Retention Categories

Appendix 4 – Site Plans

1. Executive Summary

- 1.1.1. Urban Green has been instructed by Ameresco to carry out an Arboricultural Survey to British Standard 5837:2012 guidelines at Arcadia Library and Leisure Centre, Yew Tree Avenue, Manchester, M19 3PH and produce our findings in a report.
- 1.1.2. It is proposed to develop an air heat source pump. Full details of the proposed site layout can be seen on the plans included in Appendix 4.
- 1.1.3. The proposed development necessitates the removal of 3 trees and 2 groups of trees within the site boundary. However, it is noted that the majority of these are of low value. It is recommended that this tree loss is mitigated for by replacement tree planting and the production of a robust soft landscaping scheme.
- 1.1.4. Before any tree works are carried out trees should first be assessed for their suitability for protected species by a suitably qualified and experienced ecologist.
- 1.1.5. Information regarding the layout of new utilities and drainage and final site levels should be submitted to the Arboricultural Consultant so that the impact of these on the retained trees can be assessed.

2. Introduction

2.1. Instructions and references

- 2.1.1. We have been instructed by Ameresco to carry out a Arboricultural Impact Assessment (AIA) in accordance with BS 5837:2012 Trees in relation to design, demolition and construction – Recommendations at the site location and produce our findings in a report to be submitted with a detailed planning application.
- 2.1.2. All trees, regardless of their statutory status, are a material consideration in a planning application. BS 5837 recognises the potential conflict between trees and development. The standard sets out to assist those concerned with trees in relation to construction and aid with decision making. This is achieved by providing impartial and balanced information on trees and their potential impacts.
- 2.1.3. Due to the nature of the site, it was decided that the survey methodology would include broadly grouping trees that share very similar characteristics. This method is in line with point 4.4.2.3 of BS 5837:2012 that states ‘Trees forming groups...should be identified and considered as groups where the arboriculturist determines that this is appropriate... It may be appropriate to assess the quality and value of trees as a whole, rather than individuals.’
- 2.1.4. The site is located in the area shown in Figure 1.



Figure 1 – Site Location Plan

2.2. Scope

- 2.2.1. The AIA takes into account any potential impacts on existing trees including the effect of any tree loss required to implement the design and recommendation for the establishment of new trees.
- 2.2.2. The AIA will also assess any potentially damaging activities proposed in the vicinity of retained trees and the effect that the retained trees may have on the development such as potential nuisance caused by excessive leaf/fruit litter, lighting levels and potential damage to structures.

2.3. Documents provided

- 2.3.1. A scaled plan has been provided with tree positions already plotted. Any extra trees found on site that were not included on the original plan have been plotted according to measurements taken on site and/or using aerial photography.
- 2.3.2. Tree locations which have been estimated are illustrated on the Tree Protection Plan in Appendix 4. The exact locations of these trees must be verified, and any discrepancies discussed with the Arboricultural Consultant before starting works on site.
- 2.3.3. The position of the air heat source pump has been shown by the client on the PDF.

2.4. Limitations

- 2.4.1. The report is based upon a visual inspection. The consultant shall not be responsible for events that happen after the date of the report due to factors that were not apparent at the time, and the acceptance of this report constitutes an agreement with the guidelines and the terms listed in this report.
- 2.4.2. The consultant accepts no liability in respect of the trees unless the recommendations of this report are carried out under his supervision.
- 2.4.3. Assessing the potential influence of trees upon load bearing soils, beneath existing and proposed structures resulting from water abstraction by trees or rehydration of shrinkable soils was not included in the contract brief and is therefore not considered in the report. The consultant cannot be held responsible for damage arising from such action.
- 2.4.4. Trees are living organisms whose health, condition and structure can change over time. The contents of this report are valid for a period of one year from the date of the report.
- 2.4.5. Potentially hazardous trees are highlighted, and appropriate recommendations are made. However, this report is not a substitute for a full tree risk assessment or management plan which are specifically designed to minimise risk and liability associated with responsibility for trees.

3. Legislation

3.1. Tree protection status

- 3.1.1. A Tree Preservation Order (TPO) is an order made by a Local Authority to protect specific trees, groups of trees or woodlands in the interests of amenity. A TPO prohibits the cutting down, topping, lopping, uprooting and wilful damage or destruction of trees without the Local Authority's written consent.
- 3.1.2. At the time of writing the report, we have not yet received a response from the Local Planning Authority to our request regarding the status of trees on or adjacent to the site.
- 3.1.3. It is recommended that the Local Authority is consulted before any tree works are undertaken, as new TPOs may have been created since the time of enquiry, and heavy fines exist for unauthorised works to protected trees.
- 3.1.4. All works to trees covered by a TPO require permission from the Local Authority, including any pruning. However, this does not include trees that are dead or have become dangerous. The removal of dead branches is also excluded from a TPO. Although the above exceptions exist, it is advisable to give the Local Authority five days' notice in writing of any intended removal. Permission is not needed where tree work is required to implement an approved planning application.
- 3.1.5. In a Conservation Area, all trees greater than 75mm in diameter at 1.5m above ground level are protected. Where tree work is required in a Conservation Area, a Section 211 notice of intent must be submitted to the Local Planning Authority who have six weeks to decide to either make a TPO or allow the work to proceed.
- 3.1.6. The proposed work can proceed after six weeks as it is presumed that the Local Authority consents if they have not responded in that time.
- 3.1.7. It is an offence to remove more than 5m³ of timber in any one calendar quarter without having first obtained a felling licence from the Forestry Commission. It must be noted, however, that this excludes sites where planning permission has already been granted.

3.2. Wildlife

- 3.2.1. Prior to the commencement of any tree works, the trees should be assessed for the presence of species which are subject to protection under the *Wildlife and Countryside Act 1981* (as amended) and the *Conservation of Habitats and Species Regulations 2017*.
- 3.2.2. Where there is evidence that bats, birds or other protected species are present, the advice of a suitably qualified ecologist should be sought.
- 3.2.3. If tree works are carried out during the bird nesting season (March to September inclusive), trees would need to be inspected by a qualified ecologist no more than 48 hours prior to the commencement of works.

4. Arboricultural Impact Assessment (AIA)

4.1. Summary of the development

- 4.1.1. It is proposed to develop an air heat source pump. Full details of the proposed site layout can be seen on the plans included in Appendix 4.

4.2. Tree constraints

- 4.2.1. BS 5837:2012 recognises that conflicting requirements of the planning system for development means that trees are only one factor which need to be taken into consideration. Although there may be certain specimens that can pose significant constraints to development due to their importance, it is essential that inappropriate tree retention is avoided.
- 4.2.2. Trees can be adversely affected on development sites if their protection is not factored into the wider project management of onsite operations. We have transposed the tree survey plan over plans detailing current proposals in order to assess the impact on surveyed trees.
- 4.2.3. It is essential that roots are protected from construction works including physical damage from excavation and changes in soil structure from compaction and changes in ground levels.

4.3. Root Protection Areas (RPAs) explained

- 4.3.1. The RPA is an area of ground around the base of a retained tree, which is calculated in relation to the stem diameter, where disturbance should be kept to a minimum and avoided if at all possible.
- 4.3.2. The majority of tree roots grow within the upper 600mm of the soil profile where most nutrients are available as the result of the decomposition of organic matter close to the surface. Rooting conditions become less favourable at depth as the soil density increases, creating anaerobic conditions.

4.4. Impacts of development

- 4.4.1. The site contains 13 trees and groups of which 6 category B, 6 category C and 1 category U.
- 4.4.2. 3 trees and 2 groups, require removal to facilitate the container for the development. These are of low-quality trees which are semi mature and can be replaced.
- 4.4.3. The trees that are removed are to replant with suitable native species at a rate of 1:3, on other parts of the site to mitigate the loss of the trees.

4.5. Tree surgery works

- 4.5.1. Tree works that are recommended within the Tree Works Schedule (Appendix 4) are works required to facilitate development and also include details or remedial works. Tree works stated in the Tree Data Schedule (Appendix 1) are of a general maintenance nature and can be carried out at any time as per recommendations.

- 4.5.2. Tree works required to facilitate the development will be carried out prior to the commencement of any onsite operations. This should allow sufficient space for approved construction to be carried out.
- 4.5.3. Any unforeseen tree works that become apparent during the construction process will require written consent from the Local Authority Tree Officer.

4.6. Protective fencing

- 4.6.1. Temporary protective fencing will need to be installed at the alignment indicated on the Tree Protection Plan in Appendix 4, prior to the commencement of any construction activities on site including the delivery of materials and site facilities.
- 4.6.2. Any fencing that is damaged so that it is no longer able to protect retained trees must be replaced/repared immediately with appropriate fencing.
- 4.6.3. The required specification for protective fencing is illustrated in the Tree Protection Plan (Insert 1).
- 4.6.4. The 'in-ground' system involves driving vertical scaffold poles approximately 0.6m into the ground onto which are affixed horizontal scaffold poles and bracing struts. 2m high anti-climb weldmesh panels are then wired to the scaffold framework. The vertical scaffold poles should be at a maximum of 3m apart.
- 4.6.5. No fixing shall be made to any tree and all possible precautions shall be taken to prevent damage to the tree roots when locating uprights.
- 4.6.6. A 600mm x 300mm warning sign reading "TREE PROTECTION AREA KEEP OUT" shall be fixed to every 10m of protective fencing, as illustrated on the Tree Protection Plan (Insert 2).

4.7. Boundary treatments

- 4.7.1. Where fencing is to be installed within RPAs of retained trees, post holes will be excavated by hand and kept as narrow as possible. Trial holes will be dug using a manually operated soil augur in order to position post holes to avoid major roots.
- 4.7.2. Exploratory post holes will be dug before committing to positions. If any roots in excess of 25mm are encountered they are to remain intact and the post hole will be relocated to avoid them. The fencing system must permit such flexibility (i.e. where fixed panel widths are used, all post holes must be excavated before committing to the final location)
- 4.7.3. All post holes will be excavated by hand and kept as narrow as possible (maximum diameter 300mm).

4.8. Temporary site cabins

- 4.8.1. All storage facilities and deliveries will make use of existing hard surfaces to avoid unnecessary compaction within RPAs. The locations will be agreed in writing with the LPA prior to delivery and will remain in the agreed locations unless approved by the LPA.

- 4.8.2. If storage facilities require siting within RPAs, every effort will be made to ensure that any damage to aerial parts of retained trees is avoided and that appropriate footings are used to avoid root damage or compaction of the soil.

4.9. Utilities

- 4.9.1. At the time of writing Urban Green have not been made aware of any new utilities or service runs that will be associated with the development. Information regarding the layout of new utilities and drainage and final site levels should be submitted to the Arboricultural Consultant so that the impact of these on the retained trees can be assessed.

4.10. Recommendations

- 4.10.1. All operations that could affect trees on and adjacent to the site must be considered as part of the project management of the Proposed Development. It is therefore recommended that an Arboricultural Consultant is appointed as part of the design and management team to advise on pre-development issues and supervise on-site operations.
- 4.10.2. The Arboricultural Consultant may also have an advisory role in the preparation of site including tree surgery works and the protection of trees during demolition processes.
- 4.10.3. The Arboricultural Consultant shall be responsible for inspecting all protective fencing prior to the commencement of all onsite activity.

Appendix 1 - Tree Data Schedule

The following pages contain information gathered during the site survey. The reader should refer to Appendices 2 and 3 in order to correctly interpret the tree data.

Reference T= Tree G = Group H = Hedge W = Woodland	Age & Species	Height (m)	Crown Ht (m)	DBH (mm)	Crown Spread (m) N W S E	Notes	Recommendations		Physiological Condition	Life Expectancy (yrs)	RPA Radius	
							Priority	Inspect Freq (yrs)	Structural Condition	Retention Category	(m)	
T1	Mature Ash Fraxinus excelsior	20	6	800	6 8 8	1: Offsite with restricted access and limited inspection. 2: Canopy to north overhanging into site. 3: Failed scaffold branch at approximately 9m above ground level, large torn branch stub remaining. 4: Localized canopy dieback to upper crown.	Monitor condition.		Fair	20-40	B	9.60
	Moderate						1	Fair				
T2	Early-Mature Hawthorn Crataegus monogyna	5	2	350	3 3 2	1: Offsite with restricted access and limited inspection. 2: Canopy to north overhanging into site could be pruned back if required. 3: Bifurcated stem.	No action required.		Good	40+	B	4.20
	n/a						3	Good				
T3	Semi-Mature Ash Fraxinus excelsior	4	1.5	120	2 1 2	1: Offsite with restricted access and limited inspection. 2: Topped with regrowth. 3: Acceptable condition at present.	No action required.		Good	10-20	C	1.44
	n/a						3	Fair				
T4	Early-Mature Ash Fraxinus excelsior	9	2	250	3 2 3	1: Offsite with restricted access and limited inspection. 2: Canopy to north overhanging into site could be pruned back if required. 3: Large dead hawthorn adjacent. 4: Chainsaw cut to hawthorn has damaged ash tree although structural stability doesn't appear compromised.	Remove adjacent dead hawthorn and monitor condition of ash.		Good	10-20	C	3.00
	High						1	Fair				
T5	Young Maidenhair Tree Ginkgo biloba	4.5	2	80	1 1 1	1: New planting. 2: Acceptable condition at present.	No action required.		Good	10-20	C	0.96
	n/a						3	Good				
T6	Early-Mature Hawthorn Crataegus monogyna	8	4	270	2 2 3	1: Offsite with restricted access and limited inspection. 2: Canopy to south east encroaching onto adjacent dwelling. 3: Decay column from ground level to approximately 2m above ground level appears to have compromised structural integrity. 4: Sparce canopy growth.	Remove.		Fair	<10	U	3.24
	Moderate						1	Poor				

Reference T= Tree G = Group H = Hedge W = Woodland	Age & Species	Height (m)	Crown Ht (m)	DBH (mm)	Crown Spread (m) N W E S	Notes	Recommendations		Physiological Condition	Life Expectancy (yrs)	RPA Radius (m)
							Priority	Inspect Freq (yrs)			
G7	Semi-Mature Ash Fraxinus excelsior	av 8	av 1.5	av 120	av 3 3 3 each	1: Offsite with restricted access and limited inspection. 2: Natural colonisation abutting boundary fence. 3: Some adhoc pruning to lower stem and base. 4: Canopies to north overhanging into the site could be pruned back if required.	No action required.		Good Fair	20-40 C	1.44
							n/a	3			
G8	Semi-Mature Turkish Hazel Corylus colurna	av 5	av 2	av 100	av 1 1 1 each	1: Ornamental planting. 2: Staked, ties recently cut. 3: Acceptable condition at present.	No action required.		Good Good	40+ B	1.20
							n/a	3			
G9	Semi-Mature Mixed Species	av 2	2	av 80	av 1 1 1 each	1: Dogwood and elder. 2: Ornamental planting staked and tied. 3: Acceptable condition at present.	No action required.		Good Fair	10-20 C1.2	0.96
							n/a	3			
T10	Semi-Mature Field Maple Acer campestre	6	2	120	3 2 3 2	1: Established ornamental planting. 2: Excellent specimen.	No action required.		Good Good	40+ B	1.44
							n/a	3			
T11	Semi-Mature Field Maple Acer campestre	4	1.5	100	2 2 1 1	1: Ornamental planting staked, tie removed.	No action required.		Good Good	40+ B	1.20
							n/a	3			
T12	Young Maidenhair Tree Ginkgo biloba	3.5	1.5	80	1 0.5 0.5	1: Recent ornamental planting staked and tied.	No action required.		Good Fair	20-40 C	0.96
							n/a	3			

Reference T= Tree G= Group H= Hedge W= Woodland	Age & Species	Height (m)	Crown Ht (m)	DBH (mm)	Crown Spread (m) N W E S	Notes	Recommendations		Physiological Condition	Life Expectancy (yrs)	RPA Radius
							Priority	Inspect Freq (yrs)	Structural Condition	Retention Category	(m)
T13	Semi-Mature					1: Established ornamental planting. 2: Adequate clearance from adjacent building.	No action required.		Good	40+	1.80
	Red Oak	5	1.5	150	3 3 3				Good	B	
	Quercus rubra						n/a	3			

Appendix 2 - Tree Schedule Definition of Terms

Tree Referencing	Individual Trees T (+number) Grouped Trees G (+number) Hedgerows H (+number) Woodlands W(+number)
Age Category	Young Usually <15 years Semi-mature Significant growth expected, approximately one third of life expectancy complete Early-Mature Full height achieved with further significant growth possible, up to two thirds of life expectancy complete Mature Full height has been achieved with possible spreading of the canopy, usually past two thirds of overall life expectancy Veteran Usually a tree of significant age with characteristics that give additional cultural, landscape and conservation benefits, Over-mature A tree declining due to age as indicated by deterioration in the health and condition of its crown and trunk.
Species	Botanical Name conforming to the International Code of Nomenclature for algae, fungi, and plants (ICN). For universal plant recognition. Common Name commonly used names usually on a local and national scale.
Tree Height	The vertical distance between the base of the tree (where soil and buttress meet) and the tip of the highest branch on the tree.
Crown Height	Measured from ground level to the height at which the main crown begins.
Stem Diameter (DBH)	Stem diameter is measured at 1.5 m above ground level
Crown	Measurements taken from all four cardinal points in metres.
Notes	Notes are made to inform of any possible defects, peculiarities or points of interest that may relate to the trees position, physiology, safety and possible effects on developments.
Recommendations	Recommendations are made in accordance to good arboricultural practice. Recommendations are made regardless to the end usage of the site.
Priority Scale	Priority is given dependant on the perceived threat and the likelihood of failure given to a possible hazard. The priority of work is given regardless of the end usage of the site. Urgent To be carried out as soon as possible. Very High To be carried out within 1 month. High To be carried out within 3 months. Moderate To be carried out within 1 year. Low To be carried out within 3 years.
Physiological Condition:	Good Usually healthy with no symptoms of poor health or disease. Fair Exhibiting signs of poor health or minor disease infections that are not considered to be hazardous. Poor Disease present in considerable quantities or with very poor physiological vigour. Very Poor Tree is in a moribund state in extremely poor condition, usually with little chance of recovery.
Structural Condition:	Good A tree with no significant structural defects. Fair Minor defects may have been observed but are not considered to be immediately hazardous. Poor Significant defects found. Tree requires monitoring or remedial works. Very Poor Major defects that require immediate remedial work or the removal of the tree.
Life Expectancy:	The estimated number of years before the tree may require removal should no unexpected mechanical or environmental impacts occur to the tree.
Retention Category:	Please refer to Tree retention categorisation table on the next page.

Appendix 3 - Tree Retention Category

The following table provides an explanation of retention categories used.		
Trees to be removed		Colour on Plan
Category U Includes trees of very low quality that offer little or no amenity value.	Trees that are in such a condition that they should be removed as a matter of good arboricultural practice regardless of given proposals.	RED
Trees to be considered for retention		
Category A Trees of a high quality, with an estimated life of expectancy of at least 40 years	Trees that are excellent examples of their species, usually mature, especially if rare or unusual including veteran trees. Category A trees are likely to enhance a development and should be retained wherever possible.	GREEN
Category B Trees of moderate quality with an estimated remaining life expectancy of at least 20 years.	Trees that are good examples of their species. B category trees are usually mature or younger trees with the potential to reach A category in the future. Although the retention of these trees is desirable, some losses may be acceptable.	BLUE
Category C Trees of low quality with an estimated remaining life expectancy of at least 10 years, or young trees with a stem diameter below 150 mm.	Unremarkable trees of very limited merit or such impaired condition that they do not qualify in higher categories.	GREY
NOTE: Trees that are viewed as borderline and do not fit neatly into either of the categories are given a plus or minus rating (+/-) in the tree data schedule. Therefore, C+ would denote a tree being borderline C/B although C is deemed to be the most appropriate category. Similarly, B- would denote a tree being borderline B/C with B seen as the most appropriate category.		



Appendix 4 - Site Plans

The site plans referred to in the report follow this page which include the following:

- Tree Constraints Plan
- Tree Removal Plan
- Tree Works Schedule
- Tree Protection Plan
- Tree Protection Inserts

Although included plans are usually to scale, they are only intended to indicate positions of surveyed trees and dimensions should not be taken from these drawings.



Notes:-

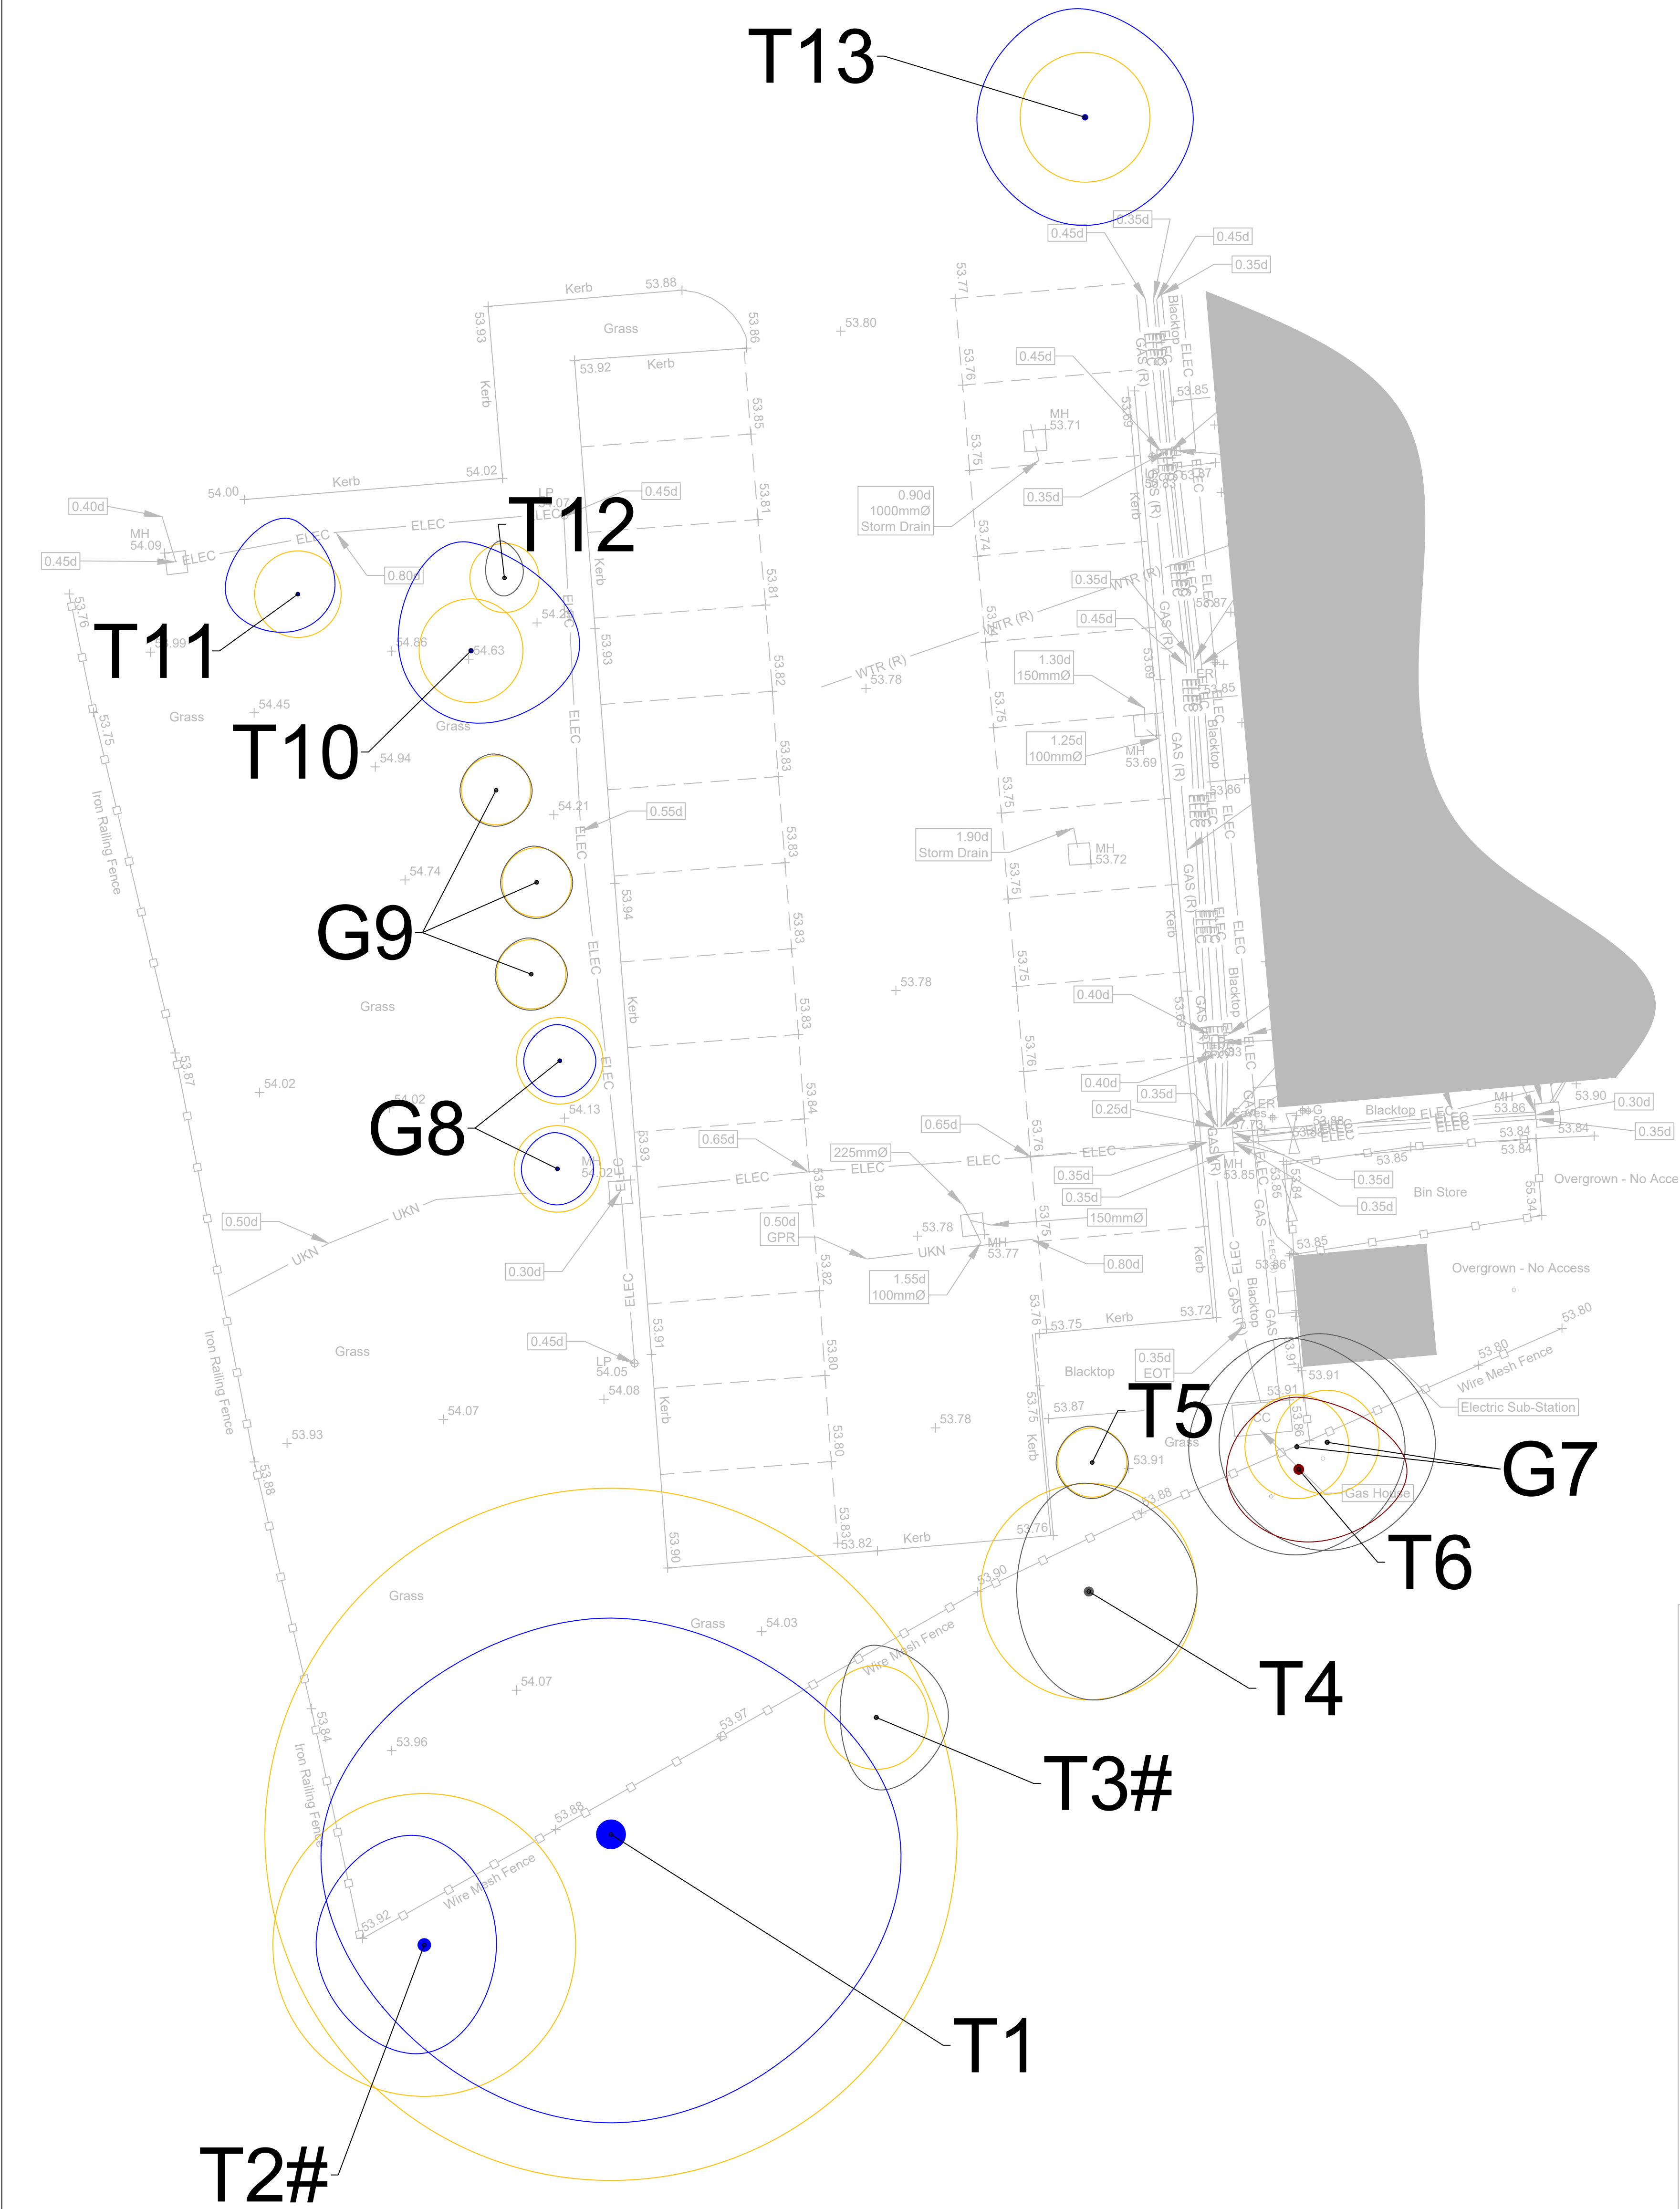

	Category A tree, group or hedge
	Category B tree, group or hedge
	Category C tree, group or hedge
	Category U tree, group or hedge
	Root Protection Area (RPA)
	Position estimated on site

Client:	Project:	Drawn:	Checked:	Approved:	Date:	
AMERESCO	ARCADIA LIBRARY AND LEISURE CENTRE	EA	RH	EA	09/08/21	
Issue:	Title:	Dwg No:	Scale @ A1:	Revision:		
PLANNING	TREE CONSTRAINTS PLAN	UG_1207_ARB_TCP_01	1:100	00		
						URBAN GREEN A: Ground Floor, The Tower, Deva City Office Park, Trinity Way, Manchester M3 7BF T: +44 (0) 161 312 3131 weareurbangreen.co.uk

Notes:-

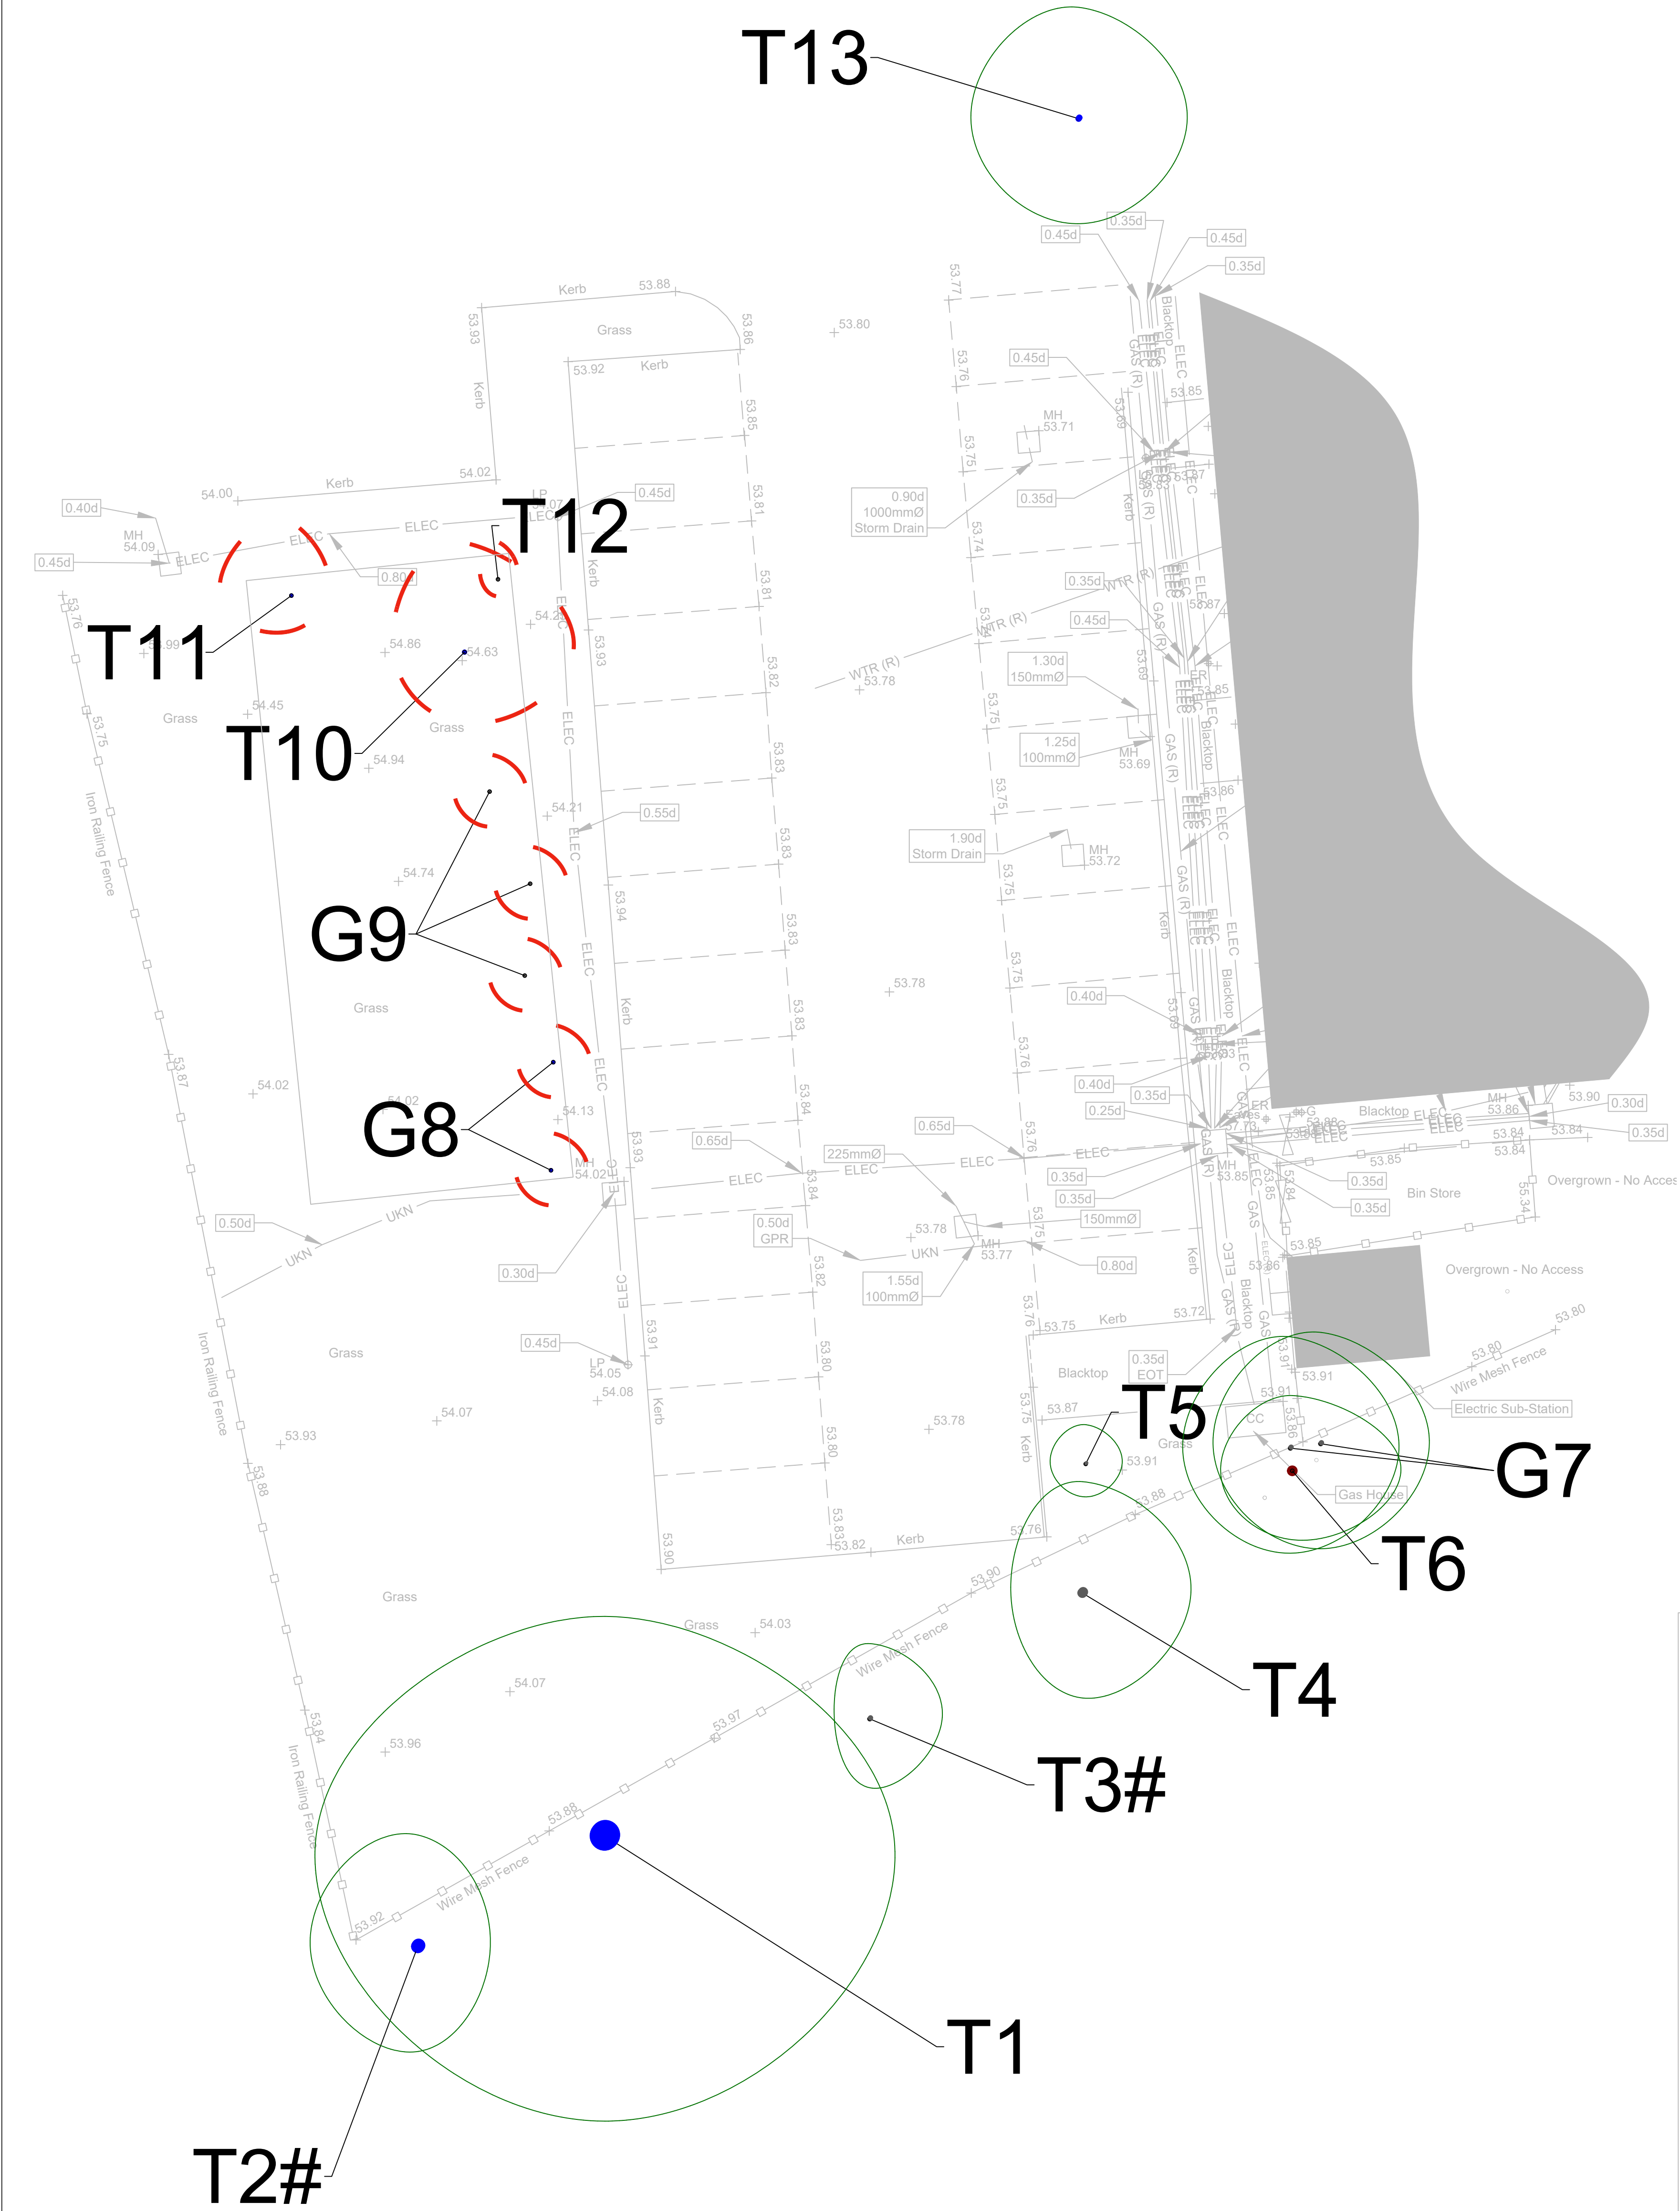

	Category A tree, group or hedge
	Category B tree, group or hedge
	Category C tree, group or hedge
	Category U tree, group or hedge
	Retained tree
	Removed tree
	Extents of pruning
	Position estimated on site

Client:	Project:	Drawn:	Checked:	Approved:	Date:	
AMERESCO	ARCADIA LIBRARY AND LEISURE CENTRE	EA	RH	EA	13/08/21	
Issue:	Title:	Dwg No:	Scale @ A1:	Revision:		
PLANNING	TREE REMOVAL PLAN	UG_1207_ARB_TRP_01	1:100	00		
						URBAN GREEN A: Ground Floor, The Tower, Deva City Office Park, Trinity Way, Manchester M3 7BF T: +44 (0) 161 312 3131 weareurbangreen.co.uk

Tree Works Schedule

Tree Number	Species	Works Required	Reason
G8	Turkish Hazel	Removal	To facilitate the development
G9	Mixed species		
T10	Field maple		
T11			
T12	Maidenhair Tree		

REV.

DATE

DESCRIPTION

DRAWN

CHK'D

U R B A N
G R E E N

A: Ground Floor, The Tower,
Deva City Office Park, Trinity Way,
Manchester M3 7BF

T: +44 (0) 161 312 3131

weareurbangreen.co.uk

Client:

AMERESCO

Project:

ARCADIA LIBRARY AND
LEISURE CENTRE

Title:

TREE WORKS SCHEDULE

Issue:

PLANNING

Drawn:

EA

Checked:

RH

Approved:

EA

Project:

UG1207

Scale @ A1:

NTS

Date:

13/08/21



Dwg No:

UG_1207_ARB_TWS_01

Revision:

00


Notes:-

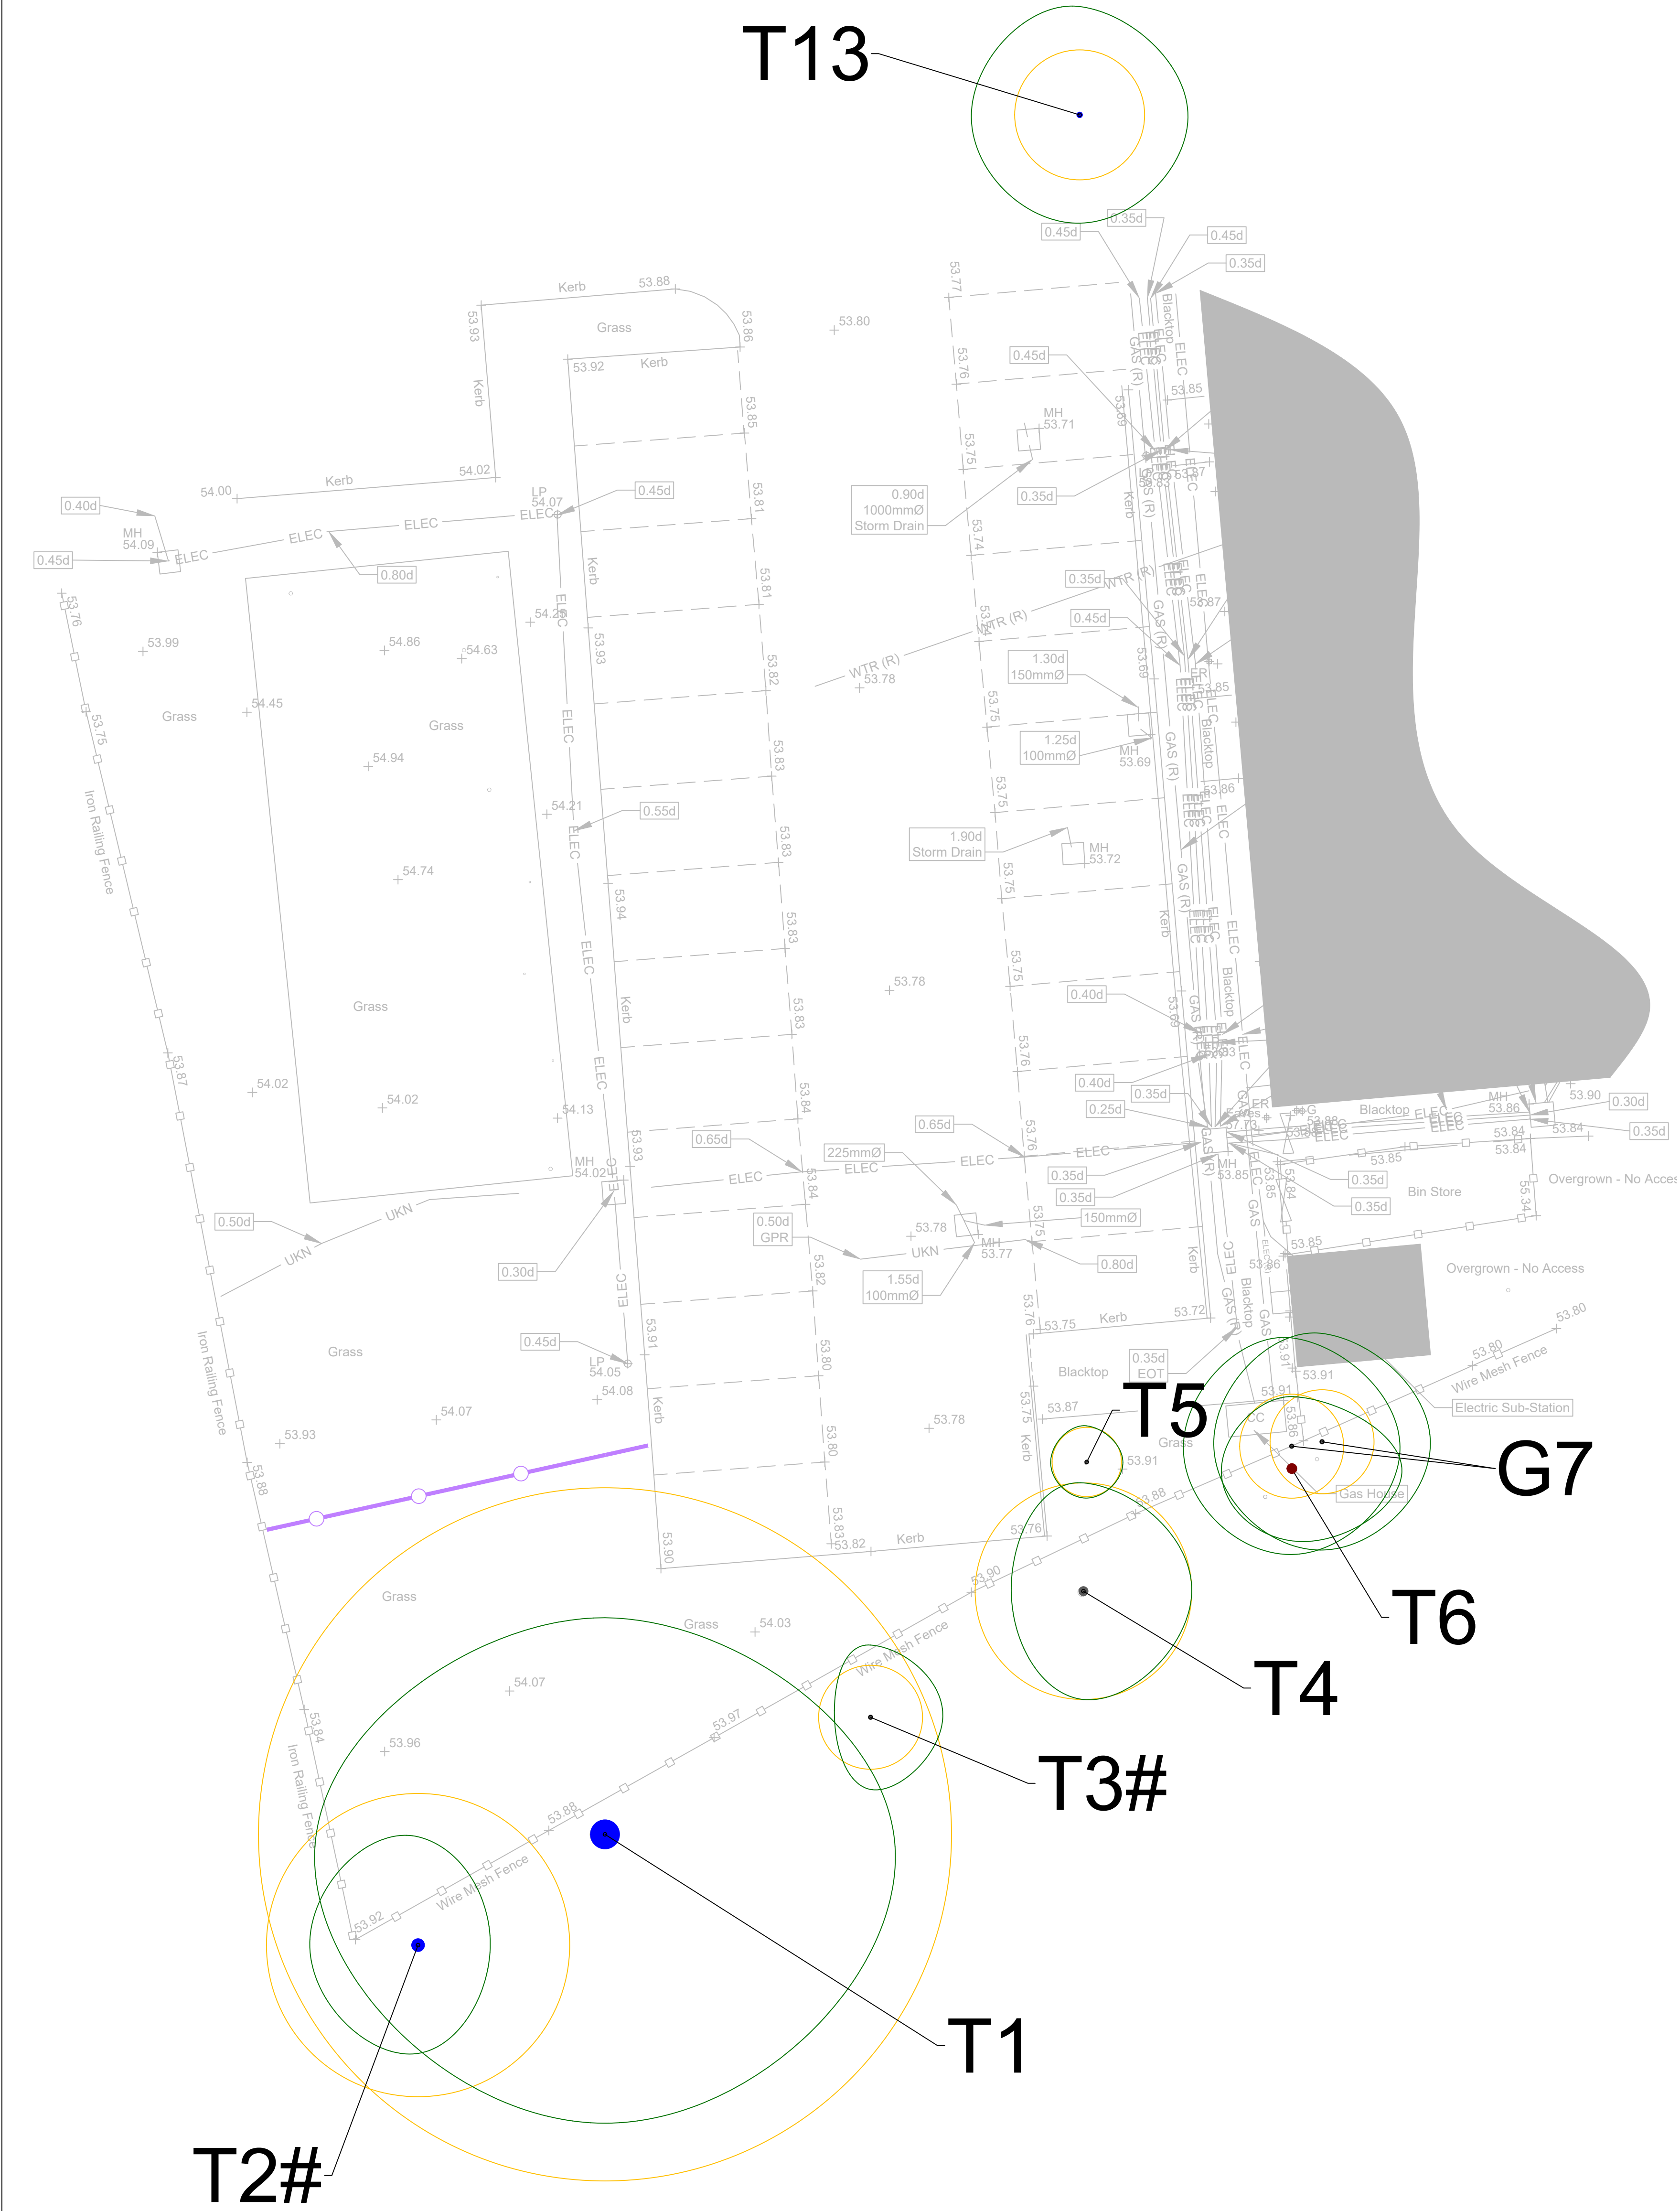


- Category A tree, group or hedge
- Category B tree, group or hedge
- Category C tree, group or hedge
- Category U tree, group or hedge
- Retained tree
- Root Protection Area (RPA)
- # Position estimated on site
- Protective fencing (See Insert 1 & Insert 2)

Client:	Project:	Drawn:	Checked:	Approved:	Date:	
AMERESCO	ARCADIA LIBRARY AND LEISURE CENTRE	EA	RH	EA	13/08/21	
Issue:	Title:	Dwg No:	Scale @ A1:	Revision:		
PLANNING	TREE PROTECTION PLAN	UG_1207_ARB_TPP_01	1:100	00		
						URBAN GREEN A: Ground Floor, The Tower, Deva City Office Park, Trinity Way, Manchester M3 7BF T: +44 (0) 161 312 3131 weareurbangreen.co.uk


Insert 1: Tree protective fencing specification

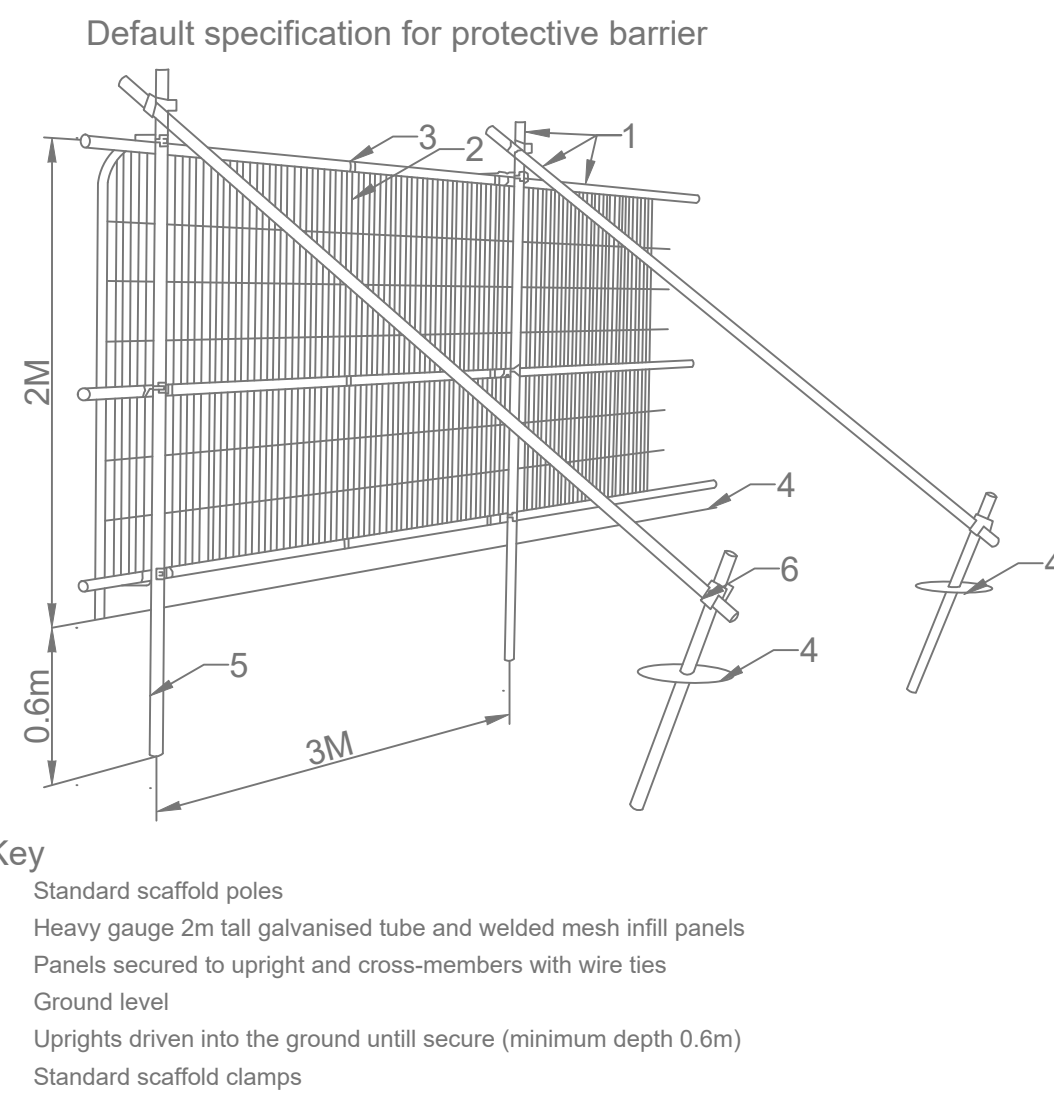


Back-stay support

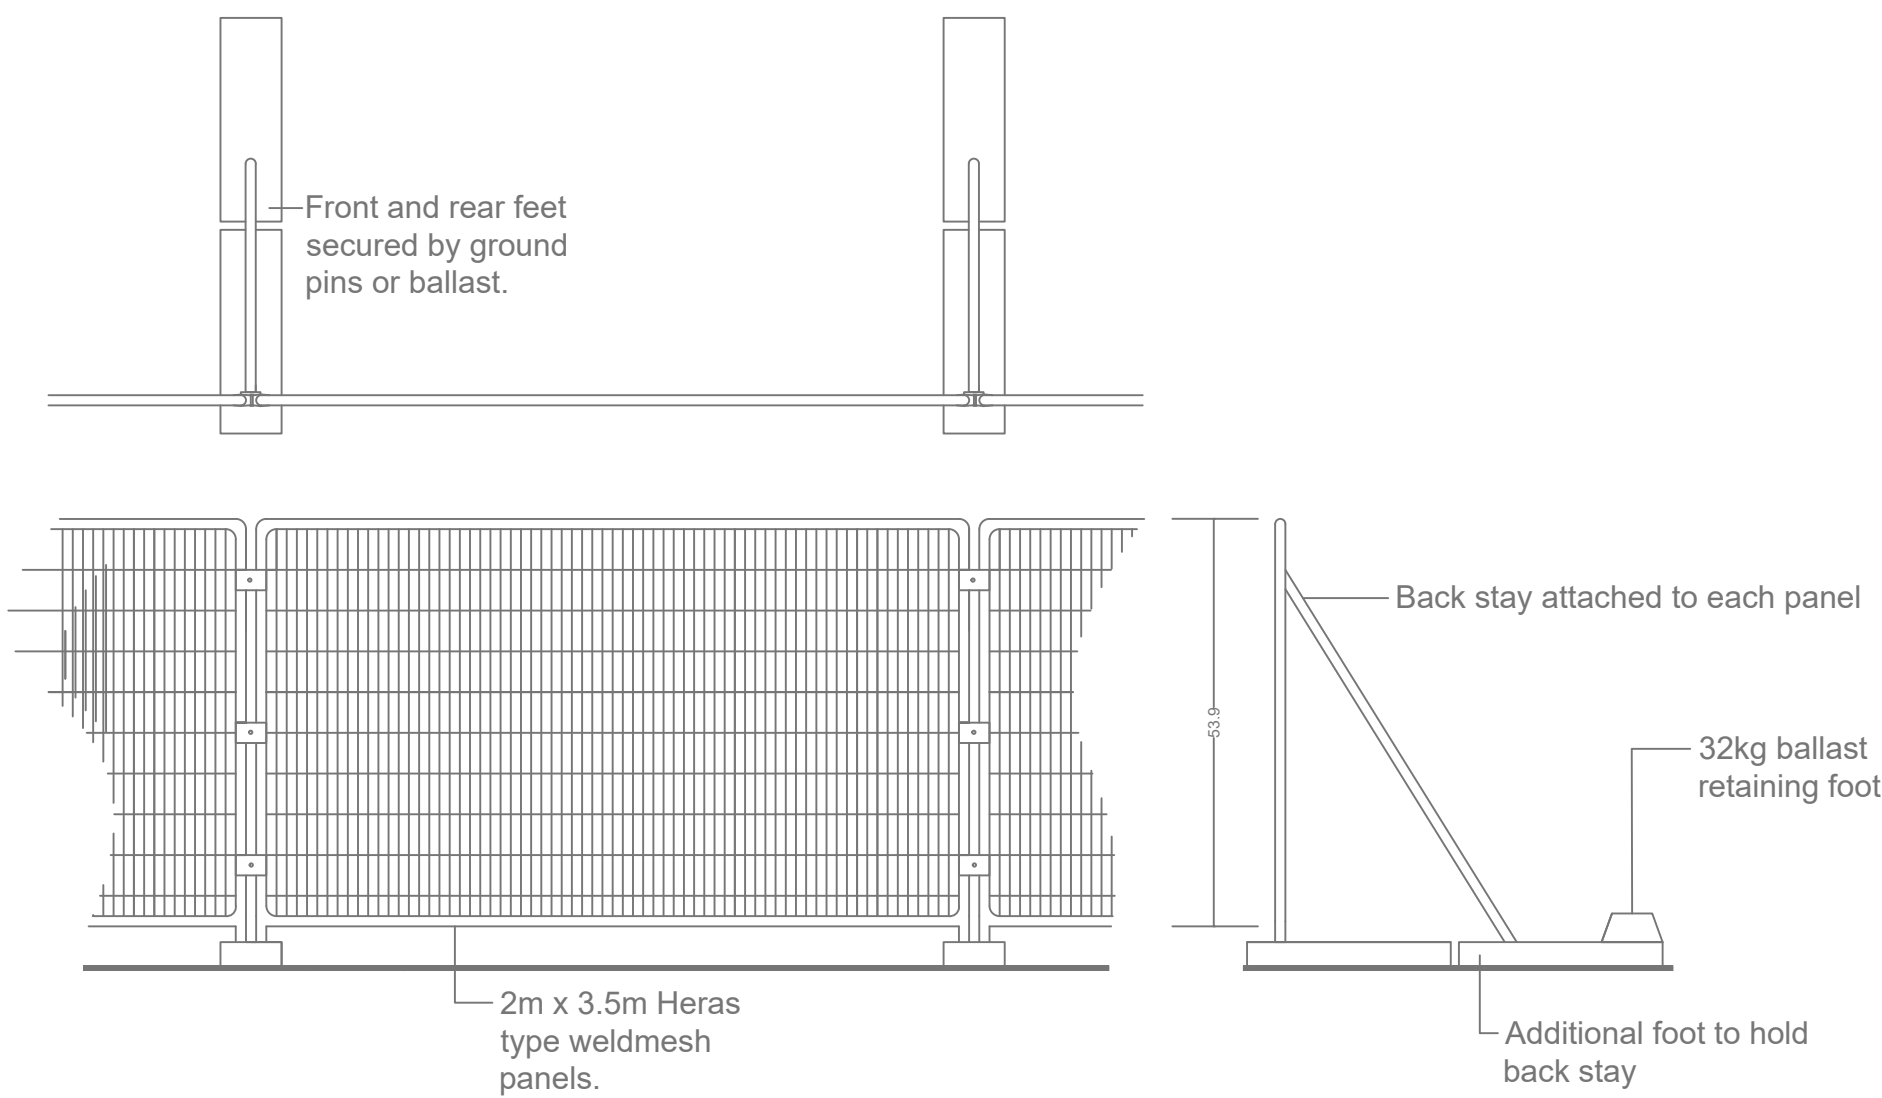

Temporary tree guard specification

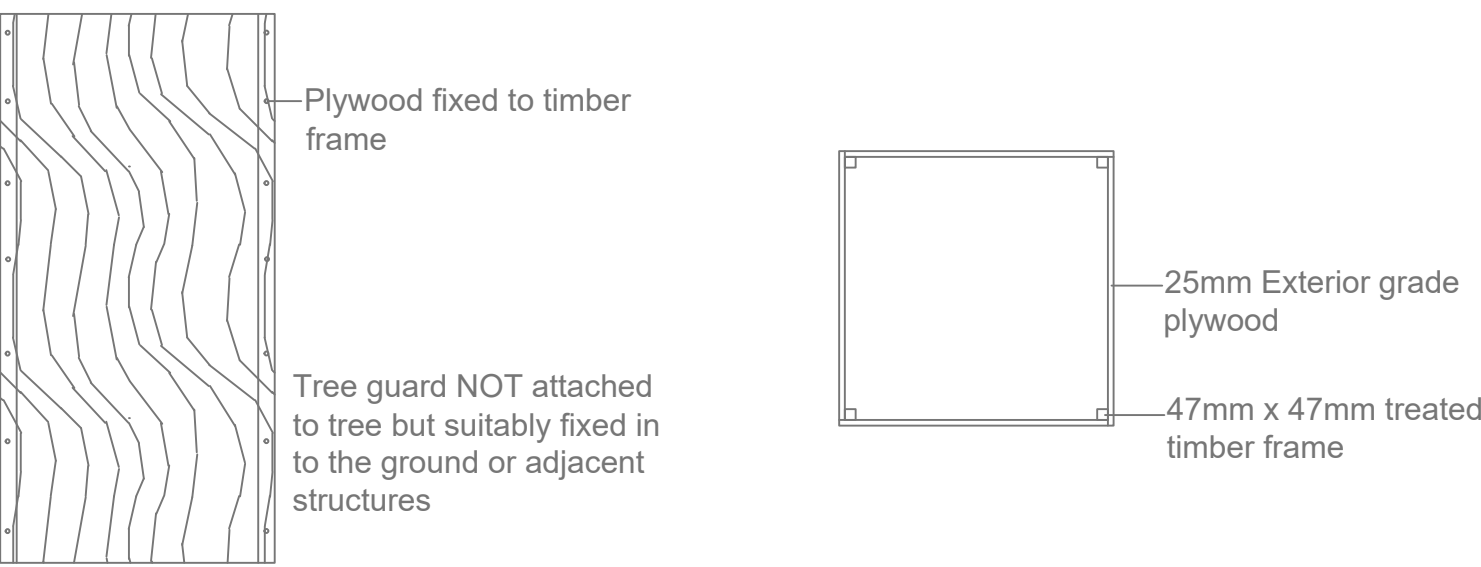


Barrier mesh specification

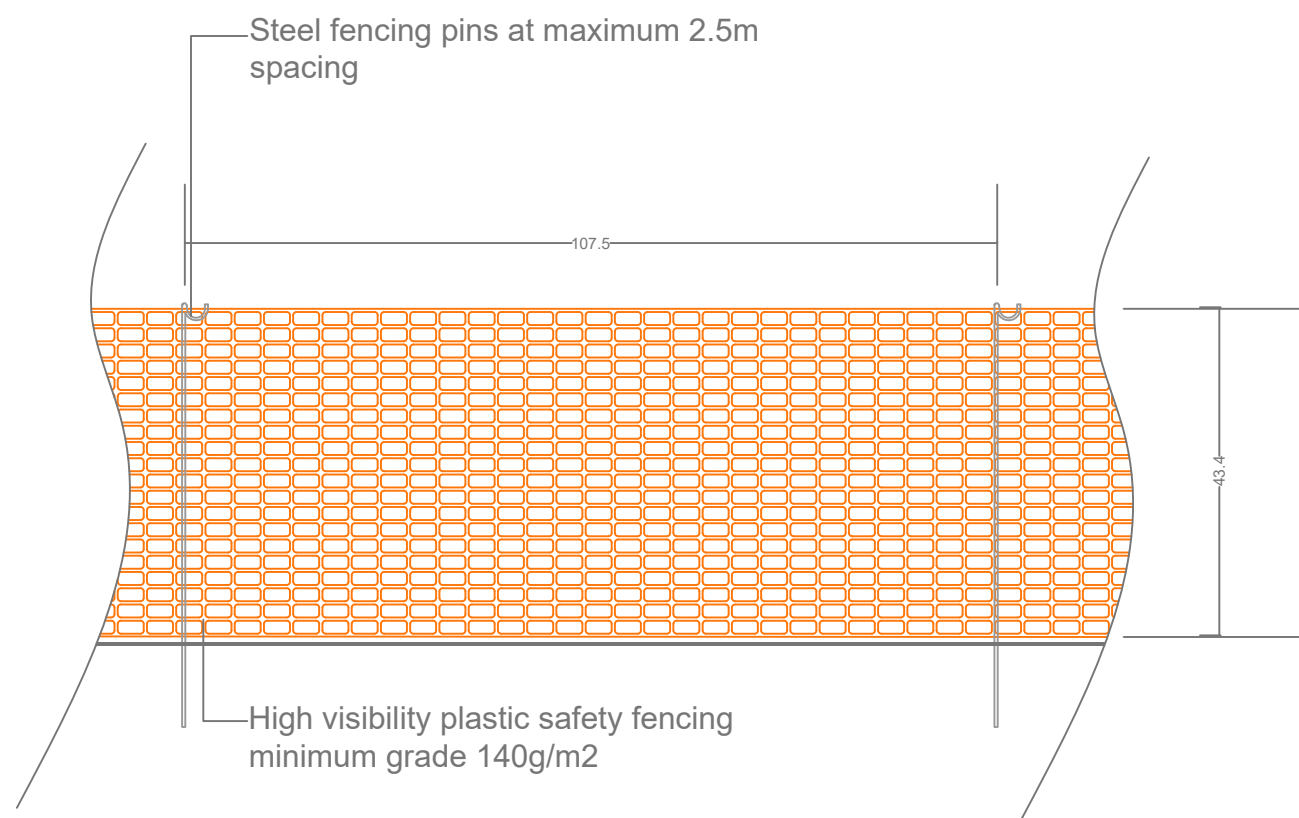

Insert 2: Tree protection notice




Insert 3: Ground protection specification

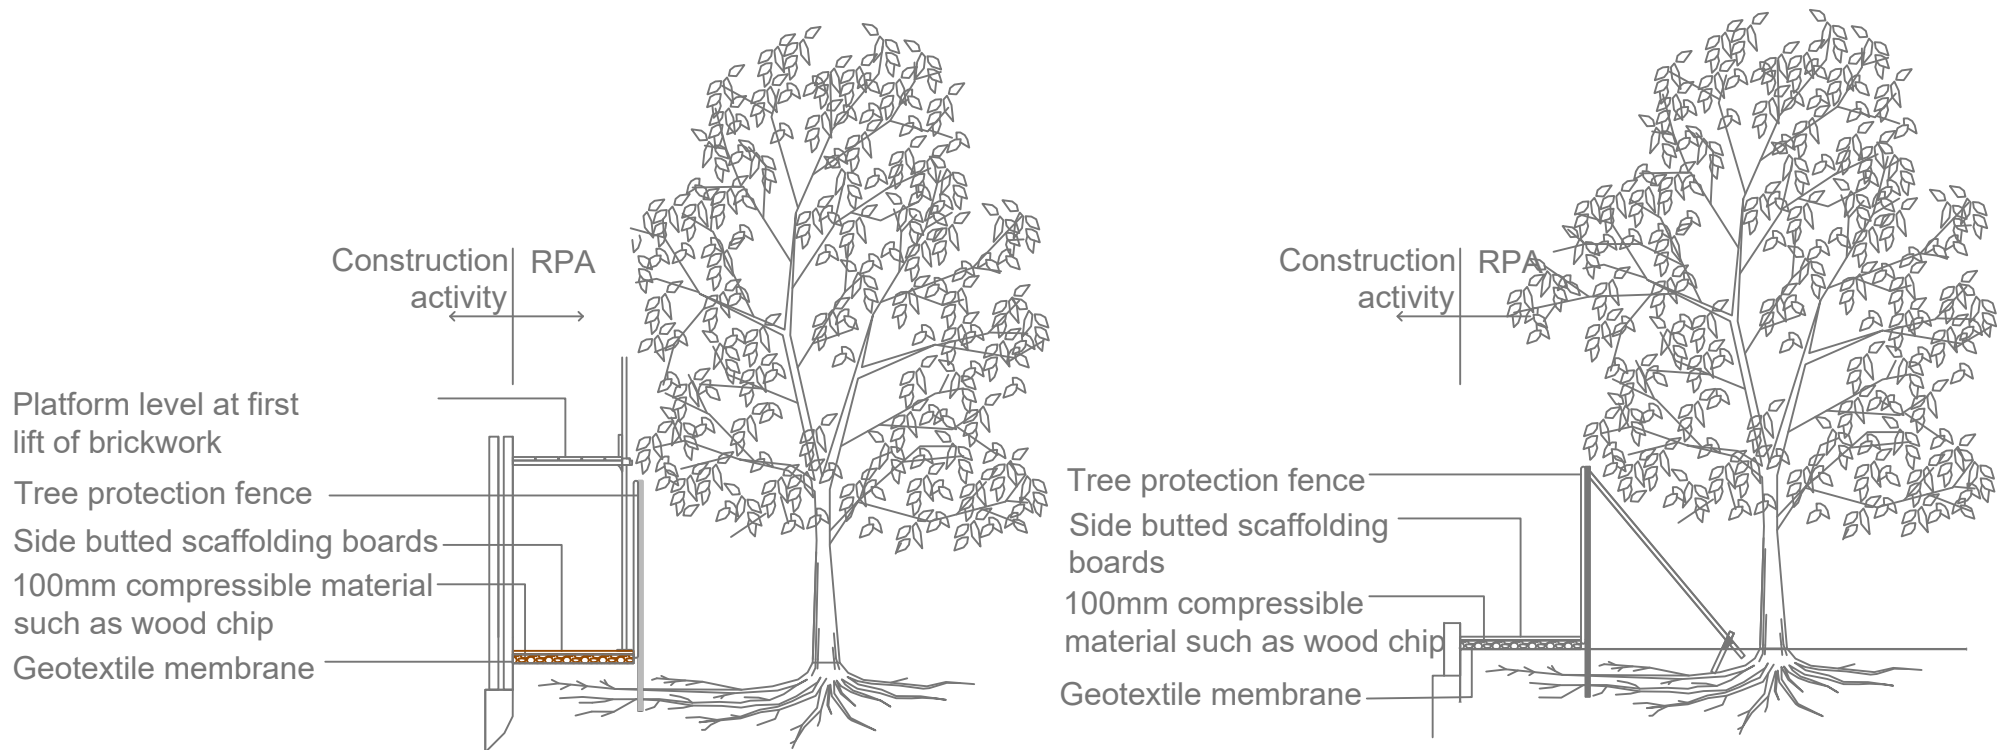

Do not scale this drawing (printed or electronic version).
Contractors must check all dimensions from site.
This drawing is copyright and is for use on this site only. This drawing should be read in conjunction with all relevant consultants drawings and specialist subcontractors / supply chain drawings and specifications.
All works to be carried out in accordance with the latest British Standards / Codes of Practice unless specifically directed otherwise in the specification.
Responsibility for the reproduction of this drawing in paper form, or issued in electronic format, lies with the recipient to check that all information has been replicated in full and is correct when compared to the original paper or electronic image.
Graphical representations of equipment on this drawing have been co-ordinated, but are approximations only. Please refer to the specifications and / or details for actual sizes and / or specific contractor construction information.

Notes:-



REV.	DATE	DESCRIPTION	DRAWN	CHK'D
URBAN GREEN A: Ground Floor, The Tower, Deva City Office Park, Trinity Way, Manchester M3 7BF T: +44 (0) 161 312 3131 weareurbangreen.co.uk				
Client:		AMERESCO		
Project:		ARCADIA LIBRARY AND LEISURE CENTRE		
Title:		TREE PROTECTION INDEX		
Issue:		PLANNING		
Drawn:	EA	Checked:	RH	Approved: EA
Project:	UG1207	Scale @ A1:	NTS	Date: 13/08/21
Dwg No:	UG_1207_ARB_TPI_01	Revision:	00	
