


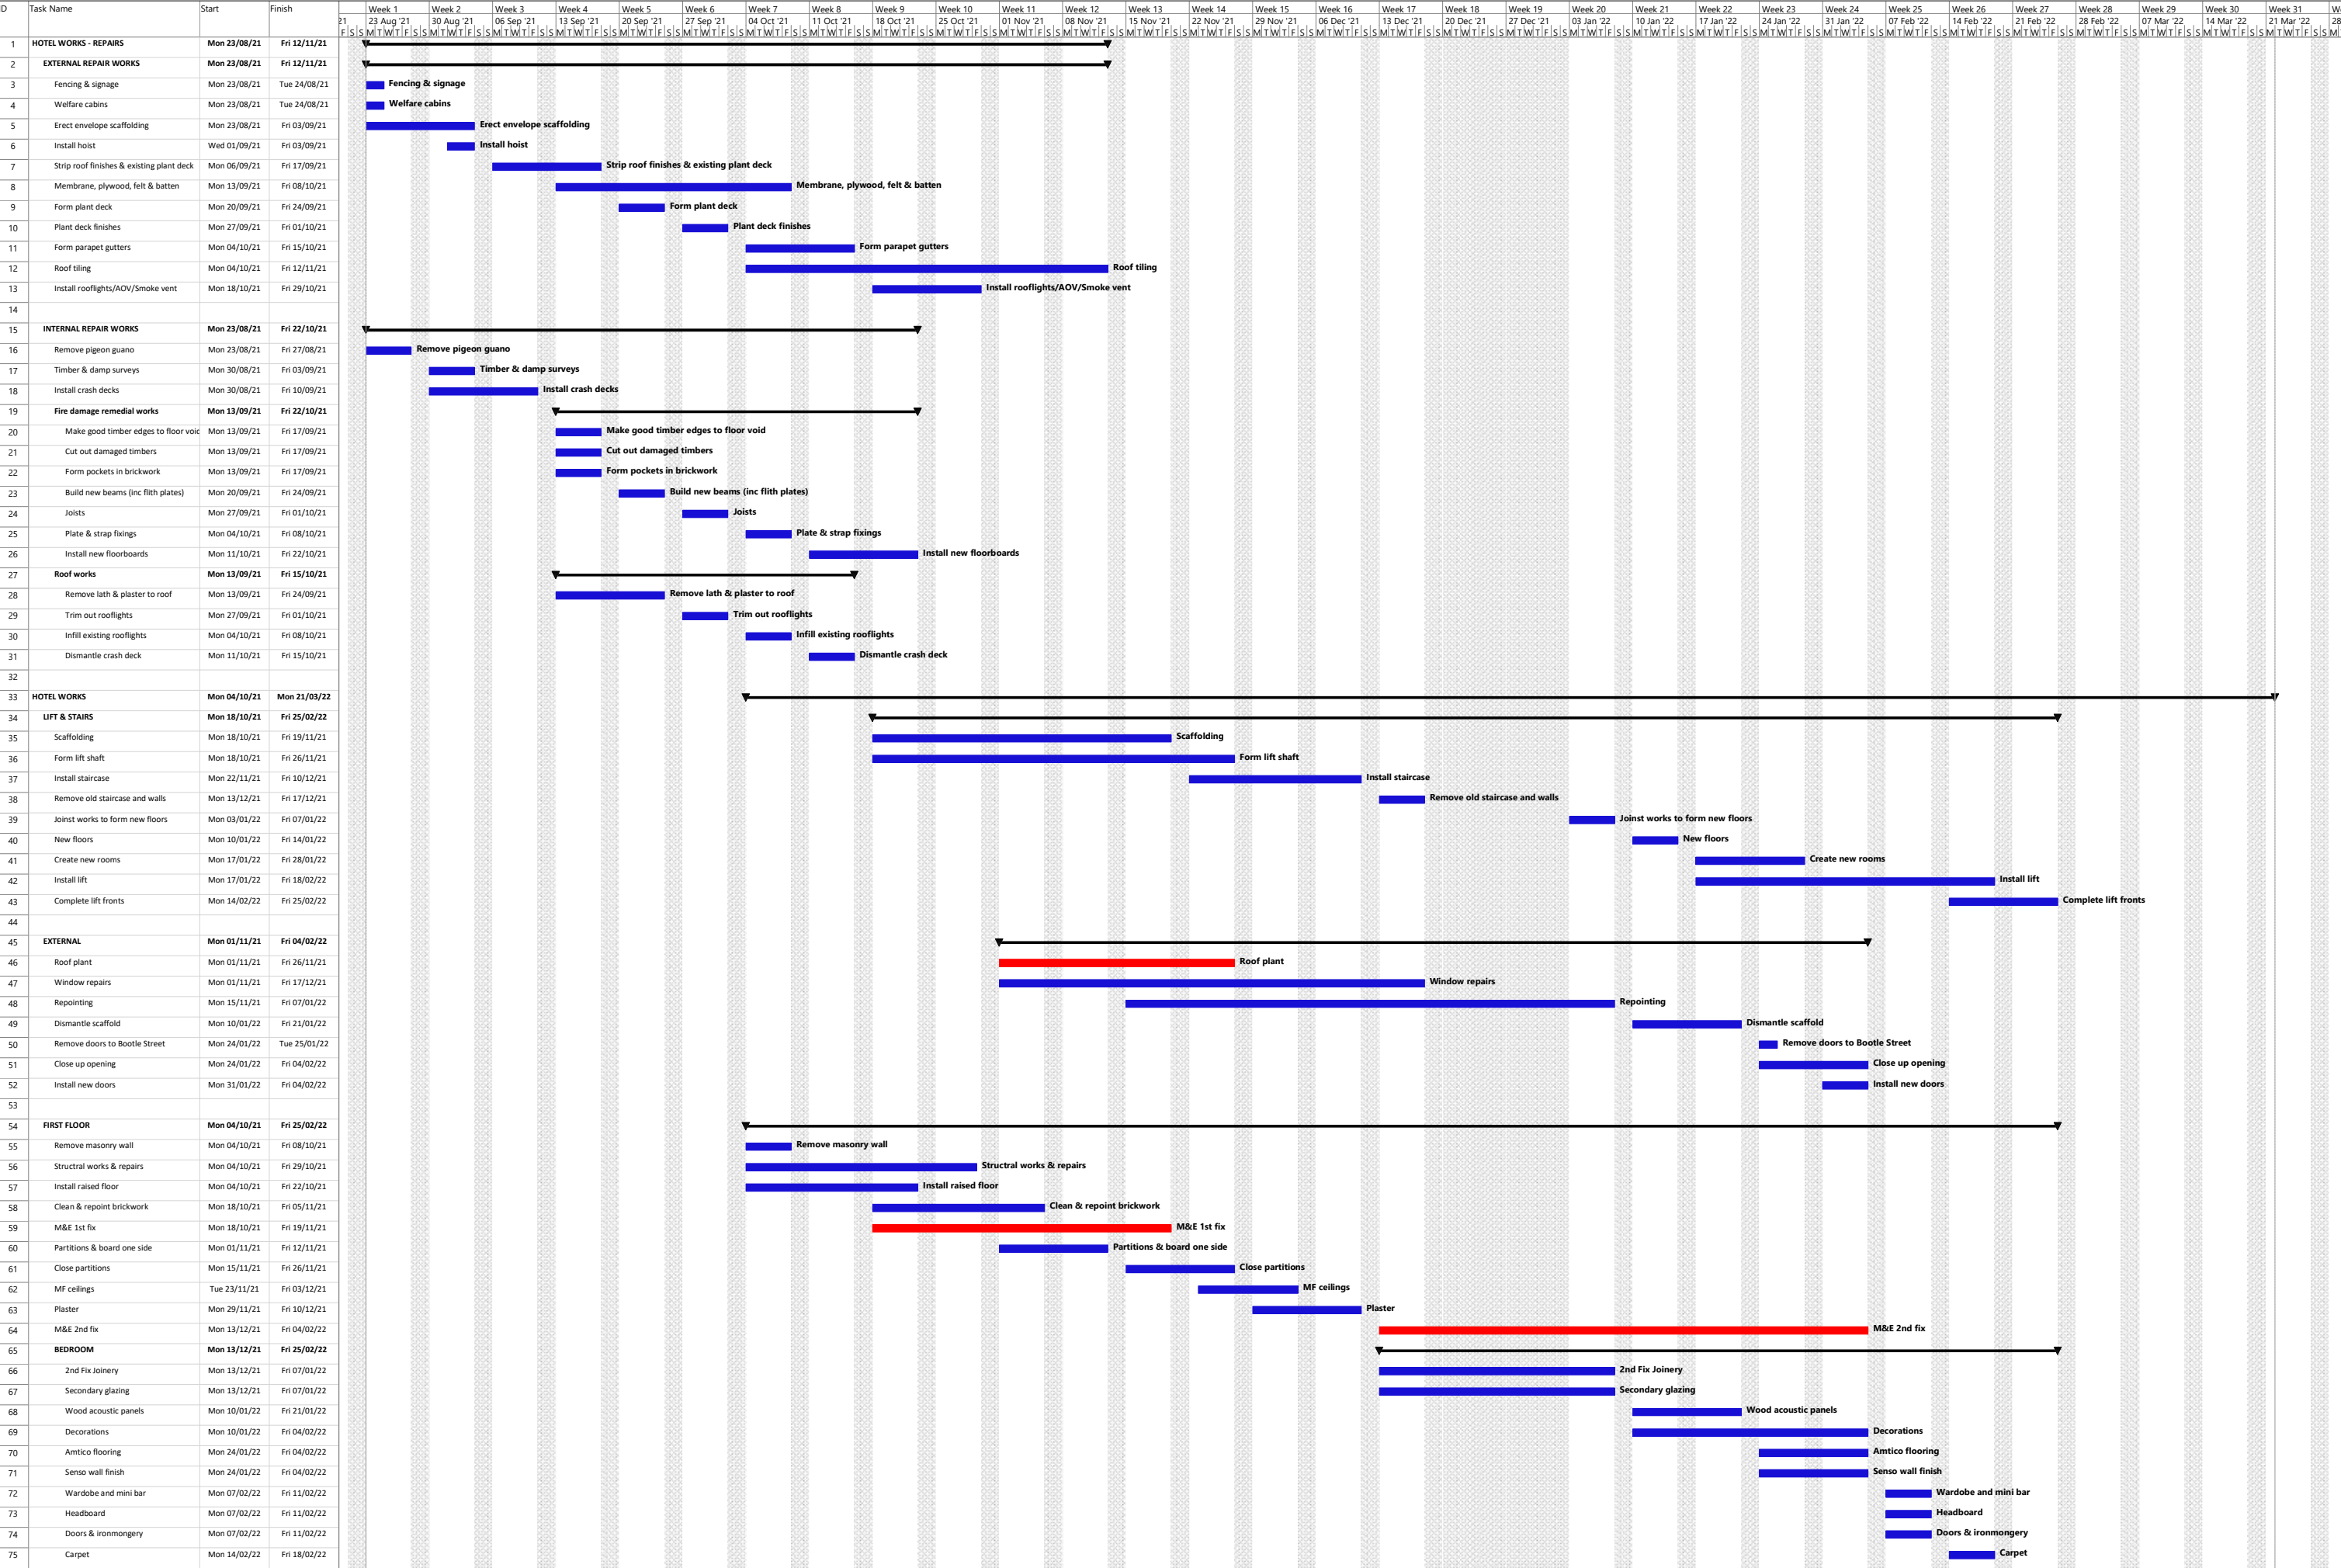

[illegible]

Task Name	Start	Finish	Week 1 23 Aug '21	Week 2 30 Aug '21	Week 3 06 Sep '21	Week 4 13 Sep '21	Week 5 20 Sep '21	Week 6 27 Sep '21	Week 7 04 Oct '21	Week 8 11 Oct '21	Week 9 18 Oct '21	Week 10 25 Oct '21	Week 11 01 Nov '21	Week 12 08 Nov '21	Week 13 15 Nov '21	Week 14 22 Nov '21	Week 15 29 Nov '21	Week 16 06 Dec '21	Week 17 13 Dec '21	Week 18 20 Dec '21	Week 19 27 Dec '21	Week 20 03 Jan '22	Week 21 10 Jan '22	Week 22 17 Jan '22	Week 23 24 Jan '22	Week 24 31 Jan '22	Week 25 07 Feb '22	Week 26 14 Feb '22	Week 27 21 Feb '22	Week 28 28 Feb '22	Week 29 07 Mar '22	Week 30 14 Mar '22	Week 31 21 Mar '22	Week 32 28 Mar '22	
151	BATHROOM	Mon 03/01/22	Fri 25/02/22																																
152	M&E 1st fix	Mon 03/01/22	Fri 28/01/22																																
153	Sanitaryware 1st fix	Mon 24/01/22	Fri 28/01/22																																
154	Wall tiling to bathroom	Mon 31/01/22	Fri 04/02/22																																
155	Vanity unit	Mon 07/02/22	Fri 11/02/22																																
156	Floor tiling to bathroom	Mon 14/02/22	Fri 18/02/22																																
157	Sanitaryware 2nd fix	Mon 21/02/22	Fri 25/02/22																																
158																																			
159	LGF BAR	Mon 03/01/22	Fri 04/03/22																																
160	Strip out & Demolition	Mon 03/01/22	Wed 05/01/22																																
161	Structural Alterations	Mon 03/01/22	Tue 11/01/22																																
162	Kitchen extract remedial work	Mon 03/01/22	Fri 07/01/22																																
163	Drylining	Mon 10/01/22	Tue 11/01/22																																
164	Plaster & Polished Plaster	Wed 12/01/22	Fri 14/01/22																																
165	M&E works	Mon 10/01/22	Fri 11/02/22																																
166	Ceiling rafts & making good to existing beams	Mon 17/01/22	Tue 18/01/22																																
167	Bar & Backfitting	Mon 17/01/22	Fri 21/01/22																																
168	Vinyl flooring	Mon 24/01/22	Mon 24/01/22																																
169	Wall Panelling	Mon 24/01/22	Tue 25/01/22																																
170	Window mesh	Wed 26/01/22	Wed 26/01/22																																
171	Joinery (Skirts/ Doors/ Architraves)	Wed 26/01/22	Thu 27/01/22																																
172	Make good existing brickwork	Wed 26/01/22	Fri 28/01/22																																
173	Mirrors	Mon 31/01/22	Mon 31/01/22																																
174	Remedial works to rear staircase	Mon 31/01/22	Thu 03/02/22																																
175	Decoration	Mon 31/01/22	Fri 11/02/22																																
176	Wallpaper	Mon 14/02/22	Wed 16/02/22																																
177	Feature light fittings	Mon 14/02/22	Wed 23/02/22																																
178	Timber flooring	Wed 16/02/22	Fri 18/02/22																																
179	Pocket sliding door	Mon 21/02/22	Wed 23/02/22																																
180	Sliding wall system	Mon 21/02/22	Wed 23/02/22																																
181	Snagging	Thu 24/02/22	Wed 02/03/22																																
182	FF&E and Furniture	Mon 28/02/22	Tue 01/03/22																																
183	Cleaning & Mastic	Mon 28/02/22	Fri 04/03/22																																
184																																			
185	RESTAURANT	Mon 03/01/22	Fri 04/02/22																																
186	Strip Out & Demolition	Mon 03/01/22	Fri 07/01/22												</																				
