



GAS MEMBRANE VALIDATION

Site Name: Belle Vue Stadium	Project Number: 12-123
Company Name: Countryside	Date: 25-05-2022
Project Manager: O. Jackson	E3P Engineer: R. Webster
PM Qualifications : BSc FGS AMIEnvSc	Engineer Qualifications: Verification of Gas Protection Systems Dec 2017
Ground Gas Risk Assessment: Amber 1	
<p>Overview:</p> <p>The membrane comprised a Visqueen HC Blok gas membrane (Gold) resistant to radon, carbon dioxide and low levels of methane. E3P can confirm there were no holes or rips at the time of inspection. Upon being laid the membrane is to be covered with a Celotex (closed Cell) floor insulation material which is considered to provide a high degree of protection.</p> <p>All external joints were inspected and E3P can confirm that the membrane was overlapped and double taped to external and internal gas resistant DPM. The membrane was taped to the gas resistant DPM using a double-sided jointing tape.</p> <p>Each unit has a service duct located to the front and outer edge of the property. E3P inspected each one and can confirm that the top-hats have been adequately sealed against the membrane.</p> <p>Based on the information provided within this report, the site inspections and validation checklists, E3P can confirm that Plots 89-91 have been installed with gas protection measures in accordance with Amber 1 to an acceptable level of workmanship.</p>	
Membrane Specification: Visqueen HC Blok (Gold)	
	




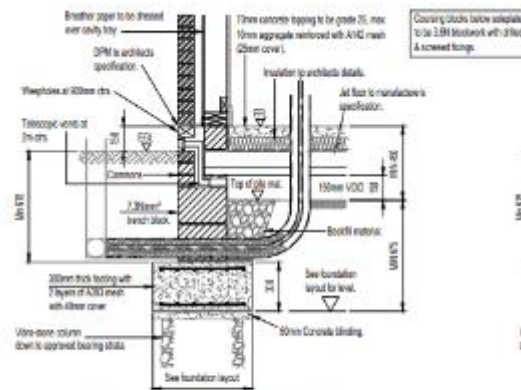

**EXTERNAL FOOTING VIBRO DETAIL
 (PERPENDICULAR FLOOR)**
 (SCALE 1:20)

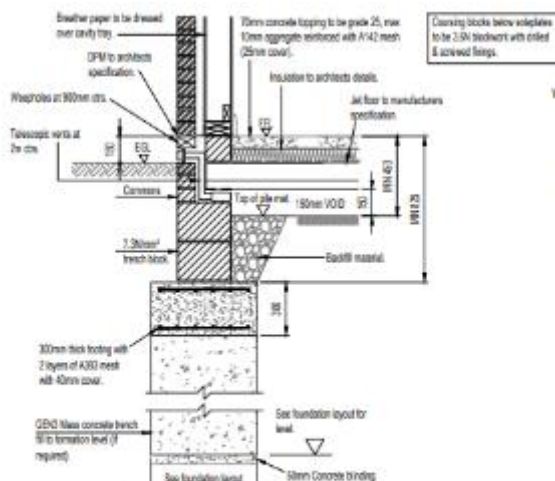

**EXTERNAL TRENCH/STRIP
 FOOTING DETAIL**
 (SCALE 1:20)

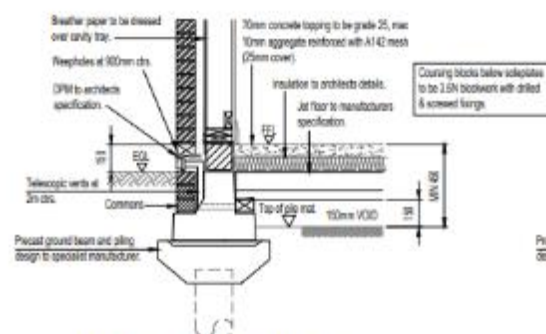

**EXTERNAL FOOTING PILE DETAIL
 (PERPENDICULAR FLOOR)**
 (SCALE 1:20)



Plot - 89

General Condition of Membrane-Good Condition



Verification of Joints and Seals-Overlapped and sealed correctly



Verification of Service Penetrations-Good Condition



Verification of Ventilation-Good Condition



Plot - 90


General Condition of Membrane-Good Condition



Verification of Joints and Seals-Overlapped and sealed correctly



Verification of Service Penetrations-Good Condition

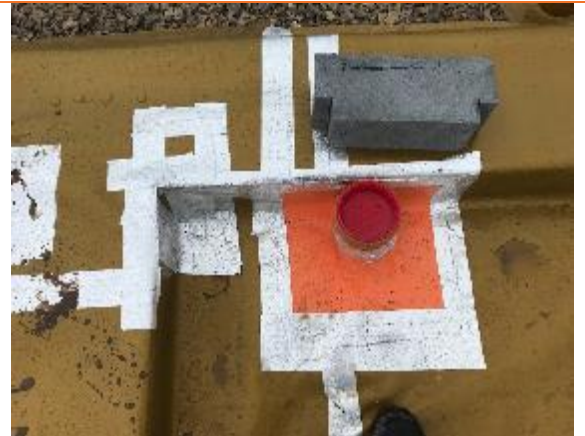

Verification of Ventilation-Good Condition



Plot - 91

General Condition of Membrane-Good Condition



Verification of Joints and Seals-Overlapped and sealed correctly



Verification of Service Penetrations-Good Condition



Verification of Ventilation-Good Condition



Gas Protection Validation Site Record

Inspection date/time: 25/5	Inspected by: R. Webster	Photographed: ✓/x
Type of development: Belle Vue	Plot number: 89	Developer:

Notes/recommendations

Membrane Type	gold
Extent of Coverage	fully extend
Underside of Membrane	
Slab / membrane condition (is membrane clear of debris or insulation)	Good
Type of joints	☒ Tape Joint ☐ Welded Joint ☐ Other (please state)
Service entries – Jubilee clips, Top hats installed correctly	yes
External Wall Air bricks Present?	yes
Corners inspected?	yes
Membrane joints inspected has Double –sided butyl tape been used?	yes
Folds in membrane inspected?	yes
Has the membrane been installed as per the design detail drawing?	yes

This Plot has **PASSED/FAILED*** inspection. (Any proposed remedial works will be noted in the "Remarks" column on this form). An additional inspection visit IS/IS NOT* required for this Plot

Inspected by: R. Webster

Signed: [Redacted Signature]



Gas Protection Validation Site Record

Inspection date/time:	25/5	Inspected by:	R. Wooster	Photographed:	✓/x ✓
Type of development:	Bellevue	Plot number:	90	Developer:	

Notes/recommendations

Membrane Type	Comments
Extent of Coverage	gold
Underside of Membrane	fully extends
Slab / membrane condition (is membrane clear of debris or insulation)	Good
Type of joints	☒ Tape Joint ☐ Welded Joint ☐ Other (please state)
Service entries - Jubilee clips, Top hats installed correctly	yes
External Wall Air bricks Present?	yes
Corners inspected?	yes
Membrane joints inspected has Double -sided butyl tape been used?	yes
Folds in membrane inspected?	yes
Has the membrane been installed as per the design detail drawing?	yes

This Plot has **PA** ~~SSD~~ **FAILED*** inspection. (Any proposed remedial works will be noted in the "Remarks" column on this form). An additional inspection visit IS/IS NOT* required for this Plot.
Inspection by: R. Wooster Signed: [Redacted]



Gas Protection Validation Site Record

Inspection date/time:	25/5	Inspected by:	R. Waosker	Photographed:	✓/x ✓
Type of development:	Beltline	Plot number:	91	Developer:	

Notes/recommendations

Comments

Membrane Type

gold

Extent of Coverage

fully extends

Underside of Membrane

Slab / membrane condition (is membrane clear of debris or insulation)

Good

Type of joints

☒ Tape Joint

☐ Welded Joint

☐ Other (please state)

Service entries – Jubilee clips, Top hats installed correctly

yes

External Wall Air bricks Present?

yes

Corners inspected?

yes

Membrane joints inspected has Double –sided butyl tape been used?

yes

Folds in membrane inspected?

yes

Has the membrane been installed as per the design detail drawing?

yes

This Plot has **PA** **SS2D/FAILED*** inspection. (Any proposed remedial works will be noted in the "Remarks" column on this form). An additional inspection visit is **NOT** required for this Plot.
Inspection by: R. Waosker Signed: [Redacted]
