


Tree Protection Plan

SCALE : 1 : 500	@ A3	DATE : 07/05/2025	
MAP FILENAME : Blackley Crem			

Map data shown may contain Ordnance Survey @ products supplied by
Pear Technology Services Ltd; Email: info@peartechology.co.uk
© Crown Copyright and database rights from date shown above
Ordnance Survey @ licence number 100023148

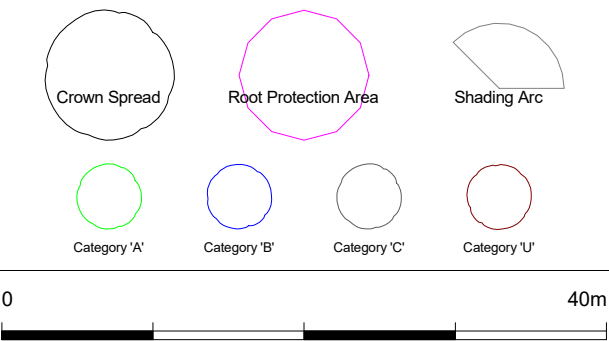

Arboricultural Supervision

The arboricultural consultant will be required to attend site to directly supervise all demolition and construction works that have to be undertaken within the root protection areas. This will include:

1. Pre-commencement site meeting.
2. Location of protective measures.
3. Supervised demolition of walls, fencing or hard surfaces within or RPAs of retained trees
4. Manual excavation within RPAs of retained trees.
- For installation of new services
5. Any excavations within or adjacent to RPAs, hard surfacing or underground services
6. Removal of protective measures and sign off.

Proposed ASHP

Proposed Solar Panel

Proposed Solar Panel

T005A


T001

T002A

G004A

T003A

Crematorium



Prohibition

- Mechanical digging or scraping is not permitted within a defined root protection area or within areas cordoned off by protective barrier fencing.
- No access will be permitted within the protected areas.
- No materials, equipment or debris will be stored within any of the fenced areas, or against the fencing.
- Fires are not permitted within 10m of any vegetation.
- Leaning objects against or attaching of objects to a tree is not permitted.
- Machinery, plant and vehicles are not permitted to be washed down within 10m of vegetation. Chemicals and materials are not to be transported, stored, used or mixed within a root protection area or within areas cordoned off by protective barrier fencing.
- Cement silos, mixing site to be situated within a bunded area to prevent pillage/leaking of chemicals harmful to trees. These areas are to be sited well clear of protected trees.
- Refuelling of plant or machinery is prohibited within 10m of the construction exclusion zones. It is essential that allowance should be made for the slope of the ground so that damaging materials such as concrete washings, mortar or diesel oil cannot run towards trees.
- Where machinery is to be used within 5m of retained tree canopies a banks man will be required at all times whilst setting up, moving or operating within this distance of retained trees canopies.
- Storage of all caustic material and chemicals are to be situated well clear of protected areas and preferably on lower ground if slopes are present, or to be situated within a bonded area to prevent any spills or leaks entering the ground.
