



Antaeus Graffiti Ltd TA Global Street Art
Global Street Art, Telephone house,
69-77 Paul Street, London, EC2A 4NW.

GLOBAL STREET ART

SINCE

H+S DOCUMENT

2012



globalstreetart.com
Company Registration Number: 07251502

MISSION: LIVE IN PAINTED CITIES

WORK PACKAGE PLAN [Version 2] – 31.07.2024

Doc Ref: WPP-001

12 PICCADILLY MANCHESTER DATE TBC (MEWP)

Please fill in using black ink all non-shaded cells throughout this form

REFERENCE

Job Ref:	TBC	Wall Ref:	12 PICCADILLY
Start Date:	TBC	Reset/Buf Date:	(TBC)

THE BASICS (IN BRIEF)

Who will be carrying out the works?	Global Street Art - Staff (ARTISTS) and Sub-contractors SMITHS HIRE
Works to be covered in these RAMS	BUFF, POUNCE & PAINTING OF MURAL OUTDOORS
Proposed dates of works	MEWP IN – TBC PAINTING TO START – TBC PAINTING AIMS TO BE COMPLETE – TBC CONTINGENCY DAYS – TBC MEWP CLEARED FROM SITE – TBC
Pre-start meeting details NB: Pre-start meetings are required for all works deemed HIGH RISK	Painting of high walls – PRE START MEETING REQUIRED DATE TBC
Landlord Name:	See Phil Hulme or Joy Ahmed
Location of Works	12 Piccadilly, Manchester M1 3AN Whatwords: ///spins.olive.branded
ADDITIONAL READING / APPENDIX ATTACHED	COSHH

12 PICCADILLY MANCHESTER DATE TBC (MEWP)



Antaeus Graffiti Ltd TA Global Street Art
Global Street Art, Telephone house,
69-77 Paul Street, London, EC2A 4NW.

GLOBAL STREET ART

SINCE

H+S DOCUMENT

2012




globalstreetart.com
Company Registration Number: 07251502

MISSION: LIVE IN PAINTED CITIES

RAMS GUIDANCE ONLY

WALL TEMPLATE - 10% SCALE (APPROX. BASED ON NIMBUS +/- 10% MARGIN FOR ERROR) 12 PICCADILLY MANCHESTER

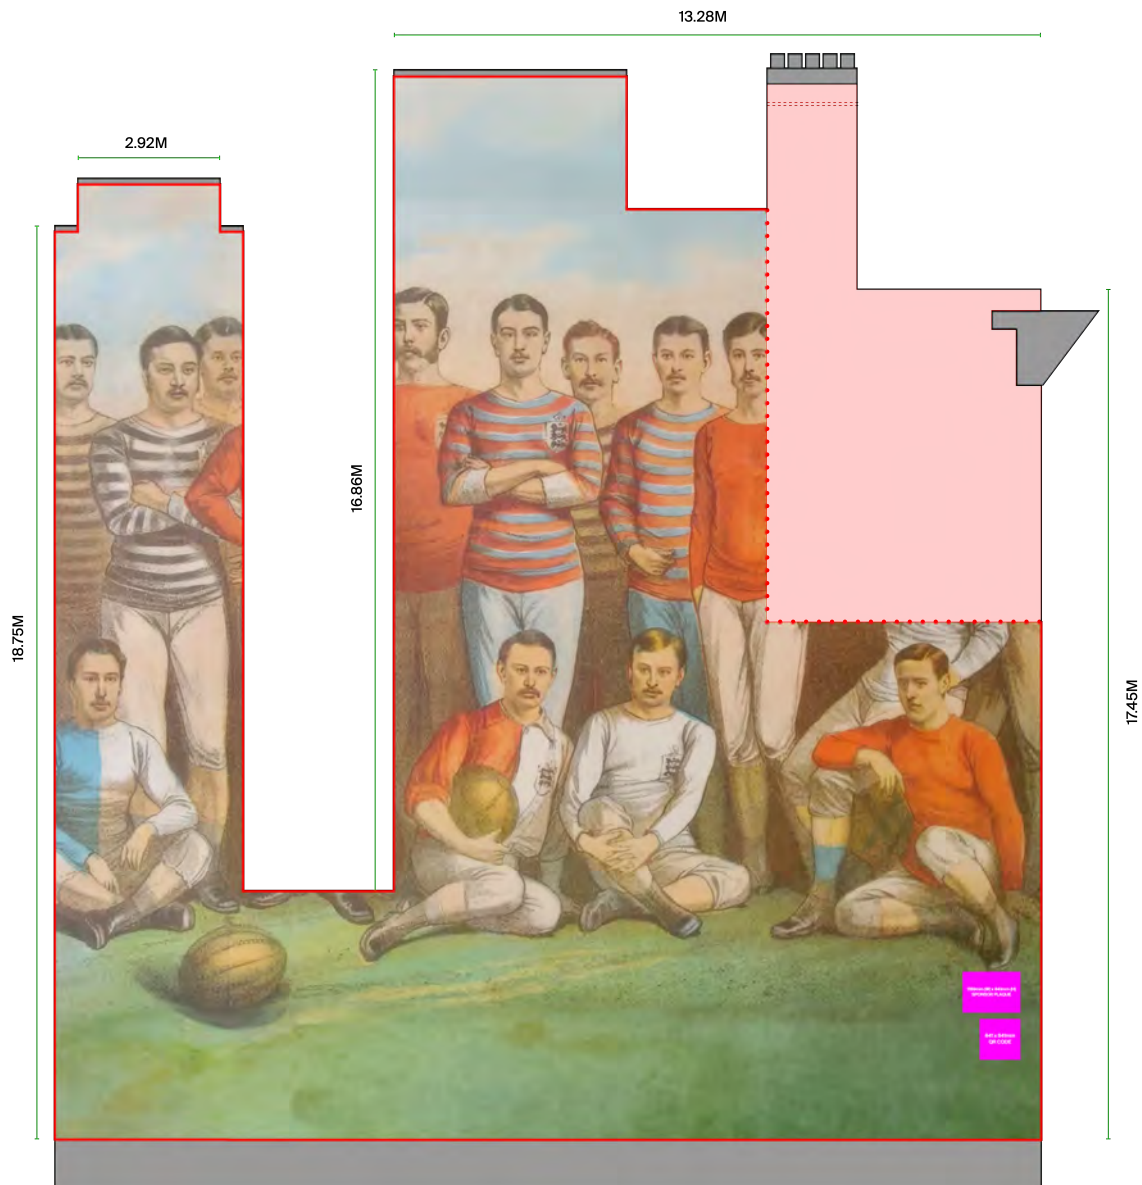

KEY:




Painted Artwork
Area



Protected Stone Area



This area can not be painted,
avoid text or key elements.



12 PICCADILLY MANCHESTER DATE TBC (MEWP)



GLOBAL STREET ART.™



Antaeus Graffiti Ltd TA Global Street Art
Global Street Art, Telephone house,
69-77 Paul Street, London, EC2A 4NW.

GLOBAL STREET ART

SINCE

H+S DOCUMENT

2012



globalstreetart.com
Company Registration Number: 07251502

MISSION: LIVE IN PAINTED CITIES

COMMUNICATION & CONTACT DETAILS

Enter details below of persons that will be carrying out the works

Name	TBC	Role	GSA Lead Artist
Name	TBC	Role	GSA Artist
Name	TBC	Role	GSA Artist
Name	TBC	Role	GSA Floor person
Name	TBC	Role	GSA Videographer

**Team members might be substituted last minute due to changed circumstances or availabilities. New members would have similar qualifications needed for the job*

PERSONNEL AND TRAINING

Detail the operatives involved in the project and list their relevant competencies (e.g., CSCS, IPAF, PASMA, 18th Edition Electrician)

		Training Requirements	TBC	TBC	TBC	TBC	TBC
Required	Training / certification / permit						
1	First Aider	YES	-	-	-	-	-
All	Working At Height	YES	YES	YES	YES	YES	YES
All	Manual handling	YES	YES	YES	YES	YES	YES
1	Asbestos awareness	-	-	-	-	-	-
1	MEWP	YES	YES	YES	YES	YES	TBC
TBC	PASMA	N/A	N/A	N/A	N/A	N/A	N/A

12 PICCADILLY MANCHESTER DATE TBC (MEWP)



Antaeus Graffiti Ltd TA Global Street Art
Global Street Art, Telephone house,
69-77 Paul Street, London, EC2A 4NW.

GLOBAL STREET ART

SINCE

H+S DOCUMENT

2012



globalstreetart.com
Company Registration Number: 07251502

MISSION: LIVE IN PAINTED CITIES

PLANT AND EQUIPMENT

Detail the tools, plant and equipment required for the project

Chapter 8 barriers

Signage

Stencils

Paint and Brushes

Ladders

Steps

MEWP – EXACT SPEC TBC

First Aid Kit

DELIVERY OF MATERIALS / TRAVELLING TO WORKSITE METHODOLOGY

Outline how you will be delivering materials or travelling to your worksite. This should be site and job specific and go into as much detail as possible. Enter details on how materials are to be moved to the worksite location, parking and barrier and signage.

Step 1.	Arrive at site (light loads, walking with trolley – heavy loads via van) and put materials in a non-obstructing manner as advised by the site supervisor. All work equipment, materials and tools will be kept within the defined works area at all times, site will not be left unattended.
Step 2.	Agree limits of worksite with GSA representative.
Step 3.	Set up worksite, Solid Physical barriers to be used.

WORKING METHODOLOGY

List every task to be covered in this proposal and state how you will be safely conducting the works. This should be site and job specific and go into as much detail as possible.

Set up worksite, the works will be carried out within the confines of an enclosure and work area.

The site supervisor will ensure that walking routes for members of the public will be set up using chapter 8 barriers.

Set up with appropriate signage, positioned to ensure Members of the public are not exposed to any risk during the work activities

Cables will be routed as not to create a trip hazard.

No equipment will be left unattended during the works and left over night in an unsafe condition.

When MEWP is not in operation / parked, boom arm to be dropped and not left in the air



Antaeus Graffiti Ltd TA Global Street Art
Global Street Art, Telephone house,
69-77 Paul Street, London, EC2A 4NW.

GLOBAL STREET ART

SINCE

H+S DOCUMENT

2012



globalstreetart.com
Company Registration Number: 07251502

MISSION: LIVE IN PAINTED CITIES

Pre-Works Methodology

Prior to work commencing the supervisor shall carry out a briefing to advise all technicians of work procedures which are to be carried out on site and to discuss any changes in safety issues and amendments to the RAMS.

The survey report provided by GSA to be referred to, and job sheets to ensure the correct works are carried out.

During works:

Only IPAF operators to use MEWPS where applicable and Scaffold contractors to amend scaffold

Keep a solid SWA and if anyone enters the SWA please stop works until they leave.

Take fresh air breaks and wear all RPE and PPE as per COSHH attached

Be clean and tidy to stop paint rolling into road

We will have a floor person on the ground to monitor works while the MEWP is in operation.

Post works:

All removed components and waste materials will then be removed from site. The waste will be transported back to the GSA depot for disposal by a licensed waste carrier.

Site supervisor to fully assess the area to ensure all PPE and waste has been removed from the work site.

When MEWP is not in operation / parked, boom arm to be dropped and not left in the air

WORKING AT HEIGHT METHODOLOGY

The area around and below where you are working must be cordoned off using Solid Physical barriers to protect other personnel and members of the public.

All tools are to be secured by lanyard. No loose objects are to be left at high level when you are not working in the area. Access equipment to all high level works must be secured at all times.

NB: Working at Height must be avoided where practicable.

Are you able to avoid working at height through the use of readily available equipment?

NO

Will you be working on an even and flat surface?

If no your access equipment must be of a type to ensure the working platform is level and secure.

MEWP - by SMITH HIRE **EXACT SPEC TBC**

What access equipment will you be using?

MEWP - **EXACT SPEC TBC**

Is this access equipment the most suitable for the proposed work activity in the proposed working environment?

YES

Does the access equipment prevent the risk of falls from height?

YES - MEWP with metal railings





Antaeus Graffiti Ltd TA Global Street Art
Global Street Art, Telephone house,
69-77 Paul Street, London, EC2A 4NW.

GLOBAL STREET ART

SINCE

H+S DOCUMENT

2012



globalstreetart.com
Company Registration Number: 07251502

MISSION: LIVE IN PAINTED CITIES

If no to the last question, what equipment will be used to reduce the consequence of a fall from height?	Lanyards and harnesses
Are all staff trained and competent in the safe use of access equipment?	Yes – IPAF trained
Are maintenance records available for all access equipment?	Yes
Will pre use checks be undertaken prior to access equipment being used?	Yes
Detail your system of working below:	
Ladders inspected prior to works commencing and fully restrained where possible, in accordance with working at height training and information sheets available from GSA. RESCUE PLAN – ALWAYS HAVE TWO WORKERS SO IF ONE PASSES OUT THE OTHER RESCUES	

MANUAL HANDLING METHODOLOGY

The area around where you are working must be cordoned off using Solid Physical barriers to protect other personnel and members of the public.

Have you undertaken and recorded relevant assessments of manual handling operations?	Yes
Where practicable will mechanical means of lifting and transporting items be used?	Van / Barrow
Where mechanical means is impracticable will you ensure sufficient persons are made available to lift loads, taking into account the size, shape and weight?	Yes
Are all operatives trained and competent in manual handling techniques?	Yes
Will you ensure access areas are clear of obstacles and that lighting is sufficient?	Yes
What PPE will be used by the operatives as highlighted by your risk assessment?	Boots, gloves, head protection
Will you ensure sharp edges are protected?	Yes
Will items be stored such that heaviest loads are in the most convenient position for the operative to lift?	Yes
Detail your system of working below:	



Antaeus Graffiti Ltd TA Global Street Art
Global Street Art, Telephone house,
69-77 Paul Street, London, EC2A 4NW.

GLOBAL STREET ART

SINCE

H+S DOCUMENT

2012



globalstreetart.com
Company Registration Number: 07251502

MISSION: LIVE IN PAINTED CITIES


All tools and equipment to be carried in secure bags not overloaded trolley and barrow

WASTE STORAGE AND DISPOSAL METHODOLOGY

The area around where you are working must be cordoned off using Solid Physical barriers to protect other personnel and members of the public.

ALL WASTE ARISING FROM THE WORKS MUST BE REMOVED DIRECTLY FROM SITE.

No waste or waste bags are to be left unattended at any time.





Antaeus Graffiti Ltd TA Global Street Art
Global Street Art, Telephone house,
69-77 Paul Street, London, EC2A 4NW.

GLOBAL STREET ART

SINCE

H+S DOCUMENT

2012



globalstreetart.com
Company Registration Number: 07251502

MISSION: LIVE IN PAINTED CITIES

TRAFFIC MANAGEMENT AND PEDESTRIAN PROTECTION METHODOLOGY

Adequate measures should be used to control traffic as road users including pedestrians, cyclists and push chair users should not be put at risk, they should be able to see the extent and nature of any obstruction well before they reach it.

The contractor should pay particular attention to the needs of disabled people and should also consider other vulnerable groups such as the elderly, children and those with push chairs.

Solid barriers should be used for all works, if the site is being left overnight, Strongfence/Heras type barriers will be required. A continuous barrier should be constructed with all fencing fastened together with clips.

All Traffic Management must be planned and Risk Assessed with drawings and/or diagrams attached to this Works Package Plan.

What Barriers will be used?

Chapter 8 cordoning off a safe working area around MEWPS

What Signage will be used?

Construction site

For long duration works will barriers/fencing be inspected on a daily basis to ensure they are still safe for passers-by and other road users?

Inspected daily

Will copies of all checks be maintained for inspection by GSA?

Recorded on daily logs

Detail your system of working below:

MEWP positioned in front of wall by IPAF staff.

Set up SWA around MEWP the works will be carried out within the confines of an enclosure and work area.

The site supervisor will ensure that walking routes for members of the public will be set up using chapter 8 barriers.

Set up with appropriate signage, positioned to ensure Members of the public are not exposed to any risk during the work activities

Cables will be routed as not to create a trip hazard.

No equipment will be left unattended during the works and left over night in an unsafe condition.

Use of generator will be required to power tools

If a generator is to be used, consideration will be given to noise levels and the generator will meet current noise regulations.

PPE will be worn at all times when handling a generator and it will be transported using a two-person lift at all times maintaining it horizontally.

The location of the generator will be sited within the barriered area so as not to interfere with the workplace and that any cable/leads do not pose a trip hazard.

The Generator will be placed on sturdy, flat even ground to ensure stability.

The Generator will be fully filled with fuel prior to works commencement off site and should not require refuelling. In the event of refuelling becoming necessary, the generator will be switched off ensuring that there are no other sources of ignition in the area, and allowed to cool sufficiently. Suitable gloves will be worn when carrying out this process.



Antaeus Graffiti Ltd TA Global Street Art
Global Street Art, Telephone house,
69-77 Paul Street, London, EC2A 4NW.

GLOBAL STREET ART

SINCE

H+S DOCUMENT

2012



globalstreetart.com
Company Registration Number: 07251502

MISSION: LIVE IN PAINTED CITIES

The fuel would be brought in an approved 5 litre container. After re-fuelling the fuel can lid will be secured and removed from site before re-starting the generator. The generator must be allowed to “cool” down prior to re-filling.

Fire extinguishers and spill kits available, staff trained to use.

A RCD circuit protection device will be used at all times, tested each time electrical equipment is to be used.

ONLY USE A GENERATOR OUTDOOR DUE TO CARBON MONOXIDE POISONING

MEWP TO BE CHARGED OVERNIGHT BY A TRANSPORTER

Pre-Works Methodology

Prior to work commencing the supervisor shall carry out a briefing to advise all technicians of work procedures which are to be carried out on site and to discussed any changes in safety issues and amendments to the RAMS.

The survey report provided by GSA to be referred to and job sheets to ensure the correct works are carried out.

All removed components and waste materials will then be loaded on a vehicle. The waste will be transported back to the GSA depot for disposal by a licensed waste carrier.

Site supervisor to fully assess the area to ensure all PPE and waste has been removed from the work site.

WELFARE ARRANGEMENTS

Detail Welfare Arrangements for these works below:

Welfare facilities will be sourced locally from coffee shops in short walking distance

ENVIRONMENTAL CONTROLS

Detail Environmental issues and Controls for these works below:

Spill kits available and staff trained – bring all waste spray cans back to GSA for removal by approved waste carriers.



Antaeus Graffiti Ltd TA Global Street Art
Global Street Art, Telephone house,
69-77 Paul Street, London, EC2A 4NW.

GLOBAL STREET ART

SINCE

H+S DOCUMENT

2012



globalstreetart.com
Company Registration Number: 07251502

MISSION: LIVE IN PAINTED CITIES


EMERGENCY ARRANGEMENTS

All accidents, incidents and near misses must be reported immediately to GSA .

Keep EYE WASH handy

In the event of an emergency, personnel are advised to:


- Raise the alarm;
- Make the working area safe, with solid barriers;
- Vacate the site to a safe location as instructed by manager;
- All plant and equipment should be left within the boundaries of the site;
- Ensure the Contractor is notified and any losses reported;
- Notify the GSA Project Manager with all the details;
- Only return to site if emergency services say it is safe to do so;
- Do not restart work without permission from GSA;



HOSPITAL LOCATION, THE NEAREST HOSPITAL WITH ACCIDENT AND EMERGENCY DEPARTMENT:

Details of the Nearest Hospital with Accident and Emergency Department:

The nearest A&E is at
Manchester Royal Infirmary, Oxford Rd, Manchester M13 9WL
12-14 MIN DRIVE

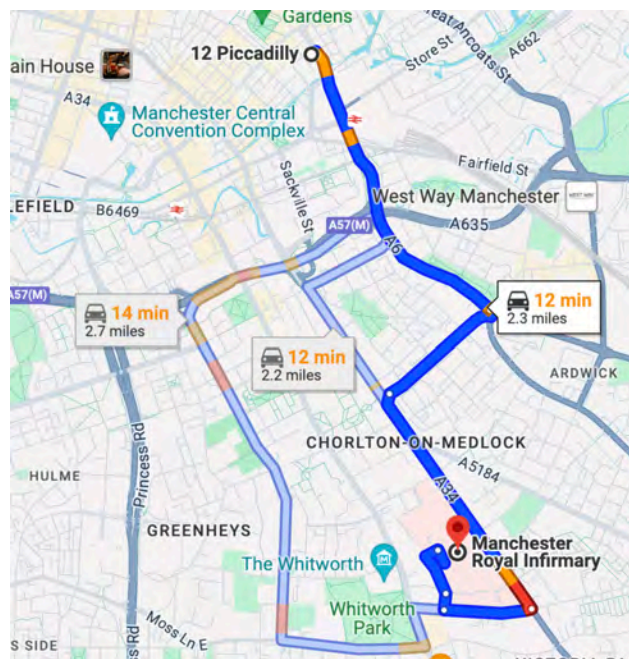

12 PICCADILLY MANCHESTER DATE TBC (MEWP)



Antaeus Graffiti Ltd TA Global Street Art
Global Street Art, Telephone house,
69-77 Paul Street, London, EC2A 4NW.

GLOBAL STREET ART

SINCE

H+S DOCUMENT

2012



globalstreetart.com
Company Registration Number: 07251502

MISSION: LIVE IN PAINTED CITIES

EMERGENCY CONTACT NUMBERS

Emergency Services

999

CONTRACTOR APPROVAL AND RISK ASSESSMENT

Risk Assessed

Yes

Approved By

Sam Simpson (IOSH)

Contractor Company Name

GLOBAL STREET ART

Date of Approval

31.07.24

Signature

Sam Simpson

The acceptance of these documents by Global Street Art does not in any way absolve the Sub-Contractor, staff and suppliers on site from their responsibility,





Antaeus Graffiti Ltd TA Global Street Art
Global Street Art, Telephone house,
69-77 Paul Street, London, EC2A 4NW.

GLOBAL STREET ART

SINCE

H+S DOCUMENT

2012



globalstreetart.com
Company Registration Number: 07251502

MISSION: LIVE IN PAINTED CITIES

APPENDIX A: FORM – Risk Assessment

DEATH – 5	L/5	M/10	M/15	H/20	H/25
MAJOR INJURY – 4	L/4	L/8	M/12	H/16	H/20
LOST TIME INJURY – 3	L/3	L/6	M/9	M/12	M/15
FIRST AID INJURY – 2	L/2	L/4	L/6	L/8	M/10
MINOR INJURY- 1	L/1	L/2	L/3	L/4	L/5
SEVERITY/LIKELIHOOD	VERY UNLIKELY – 1	UNLIKELY – 2	FAIRLY LIKELY – 3	LIKELY – 4	VERY LIKELY – 5

HAZARDS	PERSONS AFFECTED	CONTROL MEASURES	RISK RATING		
			S	L	R
Interface with third parties	Contractor, Members of the public Other workers	Works areas to be segregated off. Designated safe walking routes to be set Signage to be display on approach routes. Safe passage available for other third parties Information/instruction/training TPE will not be left un-attended	4	1	4
Ladders Fall from height	Contractor	Information/instruction/training Full PPE Work area to be clear of unauthorised personnel Ladder to be placed on boards if ground is not secure Pre inspection of equipment Harness and lanyard to be used Ladder restrained at all times 3 points of contact Do not over-reach Don't swing on scaffold poles or fool about!	5	1	5
Struck by moving vehicles (both site and road traffic)	Contractor, Members of the public Other workers	Information/instruction/training Use of banksman Barrier off work area Safe parking Operatives not to step beyond the exclusion zone PPE Hi-visibility clothing to be worn	5	1	5
Uneven ground/debris - slip, trip or fall	Contractor Members of the public	Information/instruction/training Barriers and safe walking routes Site assessments prior to working	3	1	3

12 PICCADILLY MANCHESTER DATE TBC (MEWP)



Antaeus Graffiti Ltd TA Global Street Art
Global Street Art, Telephone house,
69-77 Paul Street, London, EC2A 4NW.

GLOBAL STREET ART

SINCE

H+S DOCUMENT

2012



globalstreetart.com
Company Registration Number: 07251502

MISSION: LIVE IN PAINTED CITIES

HAZARDS	PERSONS AFFECTED	CONTROL MEASURES	RISK RATING		
			S	L	R
	Other workers	Good housekeeping Site monitoring (management) Safety boots Remove debris Cables and leads routed safely			
Falling objects – struck by	Members of the public Other workers	Exclusion zone set-up for working at height operations. All work materials to be handled with due care and attention. Tethered tools. SWL of MEWP MEWP not overloaded Good communication between operatives Access restricted to authorised persons PPE - hard hat	5	1	5
Electricity	Contractor	Pre works checks on the circuit to ensure that it has been isolated. 110v tools PAT tagged and in date RCD Pre use inspection of equipment Safe working practices PAT testing regime in place	5	1	5
Manual handling – strains/sprains	Contractor	Site based manual handling assessment supervisor Mechanical lifting aids where practicable Manual handling assessment Works vehicle to be parked adjacent to worksite Team lifting for loads Rest breaks at suitable intervals. Suitable PPE including rigger gloves to be provided. Information/instruction/training	3	2	6
Adverse weather conditions	Contractor	Information/instruction/training Welfare facilities Work/rest routine PPE – wet weather clothing/boots	3	1	3
Power tools	Contractor	Information/instruction/training Trained and authorised operatives Safety procedures Appropriate PPE Guards fitted Routine inspections and maintenance PAT tested Fitted safety systems (RCD breaker) Vibration assessments	3	2	6



Antaeus Graffiti Ltd TA Global Street Art
Global Street Art, Telephone house,
69-77 Paul Street, London, EC2A 4NW.

GLOBAL STREET ART

SINCE

H+S DOCUMENT

2012



globalstreetart.com
Company Registration Number: 07251502

MISSION: LIVE IN PAINTED CITIES

HAZARDS	PERSONS AFFECTED	CONTROL MEASURES	RISK RATING		
			S	L	R
		Job rotation			
Time of day	Contractor Members of the public	Information/instruction/training Out of hours working Team working	2	1	2
Hidden discarded needles or sharps Biological Hazards	Contractor	Visual inspection prior to commencing works. Proceed with caution and constant observation. Do not touch any needles or sharps – report immediately to Line Manager. Suitable PPE including rigger gloves to be provided. Information/instruction/training Sharps container and tongs Tool box talks	4	1	4
Spillages – slip/trip/fall	Contractor Member of the Public	Information/instruction/training Safety procedures Spillage management Barrier off work area Safety boots Environmental TBT	3	1	3
Assault - by third party when working.	Contractor	Information/instruction/training Park in designated area Avoid confrontation, walk away Be aware when taking photographs Barrier off the work area.	4	1	4
Fatigue	Contractor	Information/instruction/training Job rotation Regular breaks/welfare facilities Do not drive or work at height if fatigued. Driving assessments	4	1	4
Fire/explosion - Petrol	Contractor	Generator to be filled up prior to attending site COSHH assessment available on site Spillage kit on site Generator to be placed on a level surface Generator placed away from combustible materials SPRAY PAINTS away from combustible materials	5	1	5



Antaeus Graffiti Ltd TA Global Street Art
Global Street Art, Telephone house,
69-77 Paul Street, London, EC2A 4NW.

GLOBAL STREET ART

SINCE

H+S DOCUMENT

2012



globalstreetart.com
Company Registration Number: 07251502

MISSION: LIVE IN PAINTED CITIES

HAZARDS	PERSONS AFFECTED	CONTROL MEASURES	RISK RATING		
			S	L	R
Struck by – particles – eye injury	Contractor	Information/instruction/training Safety procedures Eye protection worn at all times Equipment inspections/maintenance Trained operative	4	2	8
Hazardous substances	Contractor	COSHH assessment briefed to operatives. Minimal level of exposure. Good personal hygiene. Suitable PPE to include chemical resistant gloves. Information/instruction/training First aid kit with eyewash on vehicle. Spill kit to contain and clean up any spillages. RPE to be worn at all times FFP3 Face fit assessments	4	1	4
Biological hazards Sharps, Leptospirosis (contact with rats) Contact with blood/faeces Contact with pigeon guano	Contractor	Information/instruction and training Large quantities of sharps contact office Welfare facilities Personal hygiene (wash hand before eating, drinking and smoking) Eating/drinking/smoking only in designated areas PPE gloves/ goggles and RPE if required Overalls	3	2	6
Noise, hand/power tools Noise induced hearing lost	Contractor	Information/ instruction and training Mandatory hearing protection to be worn when daily exposure is 85db or above Noise assessments/exposure limits Segregation of high noise activities (grinding) barrier area advise other workers and contractors Approved hearing protection suitable for the task When hearing protection is worn it must be compatible with other PPE Job rotation Regular breaks	3	2	6





Antaeus Graffiti Ltd TA Global Street Art
Global Street Art, Telephone house,
69-77 Paul Street, London, EC2A 4NW.

GLOBAL STREET ART

SINCE

H+S DOCUMENT

2012



globalstreetart.com
Company Registration Number: 07251502

MISSION: LIVE IN PAINTED CITIES

SITE BASED RISK ASSESSMENT

(*PLEASE ADD SPECIFIC RISKS FOR THIS SITE IN PARTICULAR)

WORK DESCRIPTION: PAINTING OF MURALS ON
TABERNACLE RD

Site / Location: [12 Piccadilly,](#)
[Manchester M1 3AN](#)

JOB REFERENCE:
AS ABOVE



Antaeus Graffiti Ltd TA Global Street Art
Global Street Art, Telephone house,
69-77 Paul Street, London, EC2A 4NW.

GLOBAL STREET ART

SINCE

H+S DOCUMENT

2012



globalstreetart.com
Company Registration Number: 07251502

MISSION: LIVE IN PAINTED CITIES



WARNING FALLING FROM HEIGHT - PLEASE TAKE CARE AND FOLLOW WORKING AT HEIGHT TRAINING



WARNING - STOP SPRAY CANS ROLLING INTO THE ROAD



BE AWARE OF BROKEN GLASS AND POTENTIAL SHARPS (SUCH AS RUSTY METAL SHARDS ETC).



SAFETY BOOTS MUST BE WORN AT ALL TIMES WHEN ONE SITE.



PERSONS AFFECTED

STATUS OF EXPOSED PERSONS

STAFF		SUB CONTRACTOR		PUBLIC		VISITORS		OTHER PARTIES	
-------	--	----------------	--	--------	--	----------	--	---------------	--

TASK, EQUIPMENT & SUBSTANCES

12 PICCADILLY MANCHESTER DATE TBC (MEWP)



Antaeus Graffiti Ltd TA Global Street Art
Global Street Art, Telephone house,
69-77 Paul Street, London, EC2A 4NW.

GLOBAL STREET ART

SINCE

H+S DOCUMENT

2012



globalstreetart.com
Company Registration Number: 07251502

MISSION: LIVE IN PAINTED CITIES

If no other risk assessment in place - Identify the tasks and all hazards which workers or others may be exposed to.

If generic risk assessment in place - list any additional (site specific) tasks, hazards and associated risks

THESE WORKS ARE COVERED by RISK ASSESSMENT PAGE 11

Residual Risk Agreed By (Name)	Position/Title	Signature	Date
	Site Supervisor / Team Leader		





Antaeus Graffiti Ltd TA Global Street Art
Global Street Art, Telephone house,
69-77 Paul Street, London, EC2A 4NW.

GLOBAL STREET ART

SINCE

H+S DOCUMENT

2012



globalstreetart.com
Company Registration Number: 07251502

MISSION: LIVE IN PAINTED CITIES

APPENDIX B: FORM - Staff Briefing Sheet

PROJECT: BUFF SDJ PAINTING STAR WARS 122 Tabernacle St (27.05.23)

 Day 1 Staff Briefing: Time: _____ Date: _____

I confirm that I have been briefed by Management/the Site Supervisor on the detail of the work to be carried out and my responsibilities. I have been given the opportunity to ask any question and raise any health and safety concerns that I may have. I fully understand the requirements set out in this method statement and agree to comply with them.

 Name: _____ Signed: _____ Dated _____

Name: _____ Signed: _____ Dated _____

Name: _____ Signed: _____ Dated _____

Name: _____ Signed: _____ Dated _____

Name: _____ Signed: _____ Dated _____

Name: _____ Signed: _____ Dated _____

Name: _____ Signed: _____ Dated _____

Name: _____ Signed: _____ Dated _____

Name: _____ Signed: _____ Dated _____

GSA TEAM LEADER Declaration:

I confirm that I have briefed each member of the team on the detail of the work to be carried out and their responsibilities. They have been given the opportunity to ask any question and raise any health and safety concerns.

 Name: _____ Signed: _____ Dated _____
