



Dixon's Academy,
Newall Green HS,
Greenbrow Rd,
Manchester,
M23 2SX

Arboricultural Method Statement

February 2024
Rev D



Ref: 23-10490

QUALITY STANDARDS CONTROL

The signatories below verify that this document has been prepared in accordance with our quality control requirements. These procedures do not affect the content and views expressed by the originator.

This document must only be treated as a draft unless it has been signed by the originators and approved by a director.

Revision	-	A	B	C
Date	8/12/2023	15/12/2023	05/02/2024	07/02/2024
Prepared by	C. Salisbury	C. Salisbury	C. Salisbury	C. Salisbury
Checked by	R. Quintana	A. Stuart	A. Stuart	A. Stuart
Authorised by	A. Stuart	A. Stuart	A. Stuart	A. Stuart

Revision	D
Date	16/02/2024
Prepared by	C. Salisbury
Checked by	R. Quintana
Authorised by	A. Stuart

LIMITATIONS

Syntegra Consulting Ltd ("SC") has prepared this report for the sole use of **the client, Morgan Sindall Construction & Infrastructure Ltd** in accordance with the agreement under which our services were performed. No other warranty, expressed or implied, is made as to the professional advice included in this report or any other services provided by SC.

The conclusions and recommendations contained in this report are based upon information provided by others and upon the assumption that all relevant information has been provided by those parties from whom it has been requested and that such information is accurate. Information obtained by SC has not been independently verified by SC, unless otherwise stated in the report.

The methodology adopted and the sources of information used by SC in providing its services are outlined in this report. The work described in this report was undertaken in **December 2023** and is based on the conditions encountered and the information available during the said period of time. The scope of this report and the services are accordingly factually limited by these circumstances.

Where assessments of works or costs identified in this report are made, such assessments are based upon the information available at the time and where appropriate are subject to further investigations or information which may become available.

SC disclaim any undertaking or obligation to advise any person of any change in any matter affecting the report, which may come or be brought to SC's attention after the date of the report.

Certain statements made in the report that are not historical facts may constitute estimates, projections or other forward-looking statements and even though they are based on reasonable assumptions as of the date of the report, such forward-looking statements by their nature involve risks and uncertainties that could cause actual results to differ materially from the results predicted. SC specifically does not guarantee or warrant any estimate or projections contained in this report.

Costs may vary outside the ranges quoted. Whilst cost estimates are provided for individual issues in this report these are based upon information at the time which can be incomplete. Cost estimates for such issues may therefore vary from those provided. Where costs are supplied, these estimates should be considered in aggregate only. No reliance should be made in relation to any division of aggregate costs, including in relation to any issue, site or other subdivision.

No allowance has been made for changes in prices or exchange rates or changes in any other conditions which may result in price fluctuations in the future. Where assessments of works or costs necessary to achieve compliance have been made, these are based upon measures which, in SC's experience, could normally be negotiated with the relevant authorities under present legislation and enforcement practice, assuming a proactive and reasonable approach by site management.

Forecast cost estimates do not include such costs associated with any negotiations, appeals or other non-technical actions associated with the agreement on measures to meet the requirements of the authorities, nor are potential business loss and interruption costs considered that may be incurred as part of any technical measures.

Copyright

© This report is the copyright of SC. Any unauthorised reproduction or usage by any person other than the addressee is strictly prohibited.

Table of Contents

QUALITY STANDARDS CONTROL	2
LIMITATIONS	3
1.0 DISCUSSION	5
2.0 METHOD STATEMENT.....	7
APPENDIX 1: TREE PLAN.....	8

1.0 DISCUSSION

- 1.1** The majority of the root system, of a tree, is in the surface 600mm of the soil, extending radially for distances frequently in excess of the trees height. Beyond the main structural roots (close to the base of the trunk), the root system rapidly sub-divides into smaller diameter roots: off this main system, a mass of fine roots develops.
- 1.2** The shape of the main structural roots develops in response to the need for the tree to have physical stability. Beyond these major roots, root growth and development is influenced by the availability of water and nutrients. Unless conditions are uniform around the tree, which would be unusual, the extent of the root system will be very irregular and difficult to predict. It will not generally show the symmetry seen in the branch system.
- 1.3** The parts of the root system, which are active in water and nutrient uptake, are very fine, typically less than 0.5mm diameter. They are short lived, developing in response to the needs of the tree, with the majority dying each winter. It is essential that conditions in the soil remain conducive to the healthy growth of these fine roots so that the water and nutrients necessary for healthy tree growth can be absorbed.
- 1.4** All parts of the root system, but especially the fine roots, are vulnerable to damage. Once they are damaged, water and nutrient uptake will be restricted until new roots have regenerated. Vigorous young trees will be capable of rapid regeneration but over mature trees will respond slowly, if at all.
- 1.5** In order to live and grow, roots need oxygen from the soil. Respiration by the roots and other soil organisms depletes this oxygen and increases carbon dioxide levels in the soil; a correct balance of these gases is normally maintained by diffusion between the soil and the atmosphere. Anything, which disturbs this balance, will affect the condition of the root system.
- 1.6** The factors that most commonly affect this diffusion adversely, and therefore damage roots, are the following:
1. Compaction of the ground, which reduces the space between soil particles. This is particularly important on clay soils. A single passage by heavy equipment on clay soils or storage of heavy materials can cause significant damage.
 2. Changing soil levels, even for a few weeks.
 3. Covering the root area with impervious surfaces.
 4. A rise in the level of the water table. Roots can tolerate submersion for short periods. But a permanent rise will deplete the soil of oxygen.
- 1.7** Serious damage is often caused during preliminary site works by stripping the topsoil. For this reason, such works should be avoided until protective fencing has been erected.
- 1.8** Excavations in the rooting area can sever roots. As the majority of roots are in the surface 600mm, even shallow excavations can cause damage.

- 1.9** Excavations for foundations, landscaping or service trenches are usually sufficiently deep to sever most of the roots, and it should therefore be assumed that all parts of the root system beyond the excavation would no longer serve the tree.
- 1.10** Excavation or soil stripping which severe or damage the roots may impair the stability of the tree and make it dangerous.

2.0 METHOD STATEMENT

Before any form of development commences on the site the following works should be undertaken:

2.1 Tree Works

Tree No.	Proposed Works
G2	Fell 4 trees as shown on the enclosed plan
Hedges	Remove hedges as shown on the enclosed plan

All tree works are to be undertaken outside of the bird-nesting period.


2.2 Protective Fencing

Due to the nature of the development it is felt that protective fencing is not required on this occasion.

2.3 Additional Precautions

- 2.3.1** Oil, bitumen, cement or other material likely to cause damage to the tree will not be stacked or discharged within 10m of the trees stem or within the protective area. Also materials in general will not be stacked or discharged within the exclusion zone.
- 2.3.2** Concrete mixing and washing will not be carried out within 10m of any retained trees.
- 2.3.3** Fires will not be lit beneath the foliage or in a position where the flames could extend to within 5m of the foliage, branches or trunk. If the fire is large then this may necessitate a distance of at least 20m.
- 2.3.4** Trees that are to be retained will not be used as anchorage for equipment.
- 2.3.5** Notice boards, telephone cables, or other services will not be attached to any part of the retained tree.
- 2.3.6** Care should be taken when using cranes or other equipment near the canopy of the retained trees. Also any trees to be felled in proximity to the retained trees should be done so with particular care.

2.4 Summary of Methodology for the Protection of the Trees

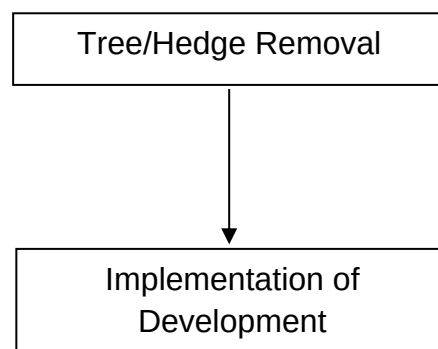

APPENDIX 1: Tree Plan

- Existing Trees Retained

Existing Trees Removed

Root Protection Area
