

Wind and Watertight Repairs

CUBED Property Advisors Limited

26 Oct 2023

<http://www.cubedltd.co.uk>


Project manager	
Project dates	1 Dec 2023 - 10 Apr 2025
Completion	0%
Tasks	27
Resources	0

Mr George Demetrious
27-29 Church Street
Manchester
M4 1PE

Tasks

Name	Begin date	End date
Party wall negotiation	01/12/2023	11/01/2024
START	22/01/2024	22/01/2024
ERECT SCAFFOLD Front	23/01/2024	05/02/2024
ERECT SAFFOLD RHS	06/02/2024	19/02/2024
ERECT SAFFOLD LHS	20/02/2024	04/03/2024
ERECT SAFFOLD Rear	05/03/2024	18/03/2024
Sheet scaffold	19/03/2024	25/03/2024
Strip roof	26/03/2024	26/03/2024
Sarking Battens	26/03/2024	22/04/2024
Line parapet and valley	27/03/2024	07/05/2024
New tiles and slates	08/05/2024	04/06/2024
Parapet caps	05/06/2024	02/07/2024
Roof top Brickwork	03/07/2024	30/07/2024
Measure windows	26/03/2024	08/04/2024
Design windows	09/04/2024	20/05/2024
Window Manufacture	21/05/2024	22/07/2024
Window install	23/07/2024	16/09/2024
Repoint Rear	17/09/2024	21/10/2024
Hack render	22/10/2024	09/12/2024
Render Front	10/12/2024	30/12/2024
Render RHS	31/12/2024	20/01/2025
Render LHS	21/01/2025	10/02/2025
Escape Stair repair	11/02/2025	10/03/2025
Decoration	11/02/2025	24/03/2025
Snagging	25/03/2025	25/03/2025
Strike SCAFFOLD	26/03/2025	08/04/2025
COMPLETE	09/04/2025	09/04/2025

Gantt Chart

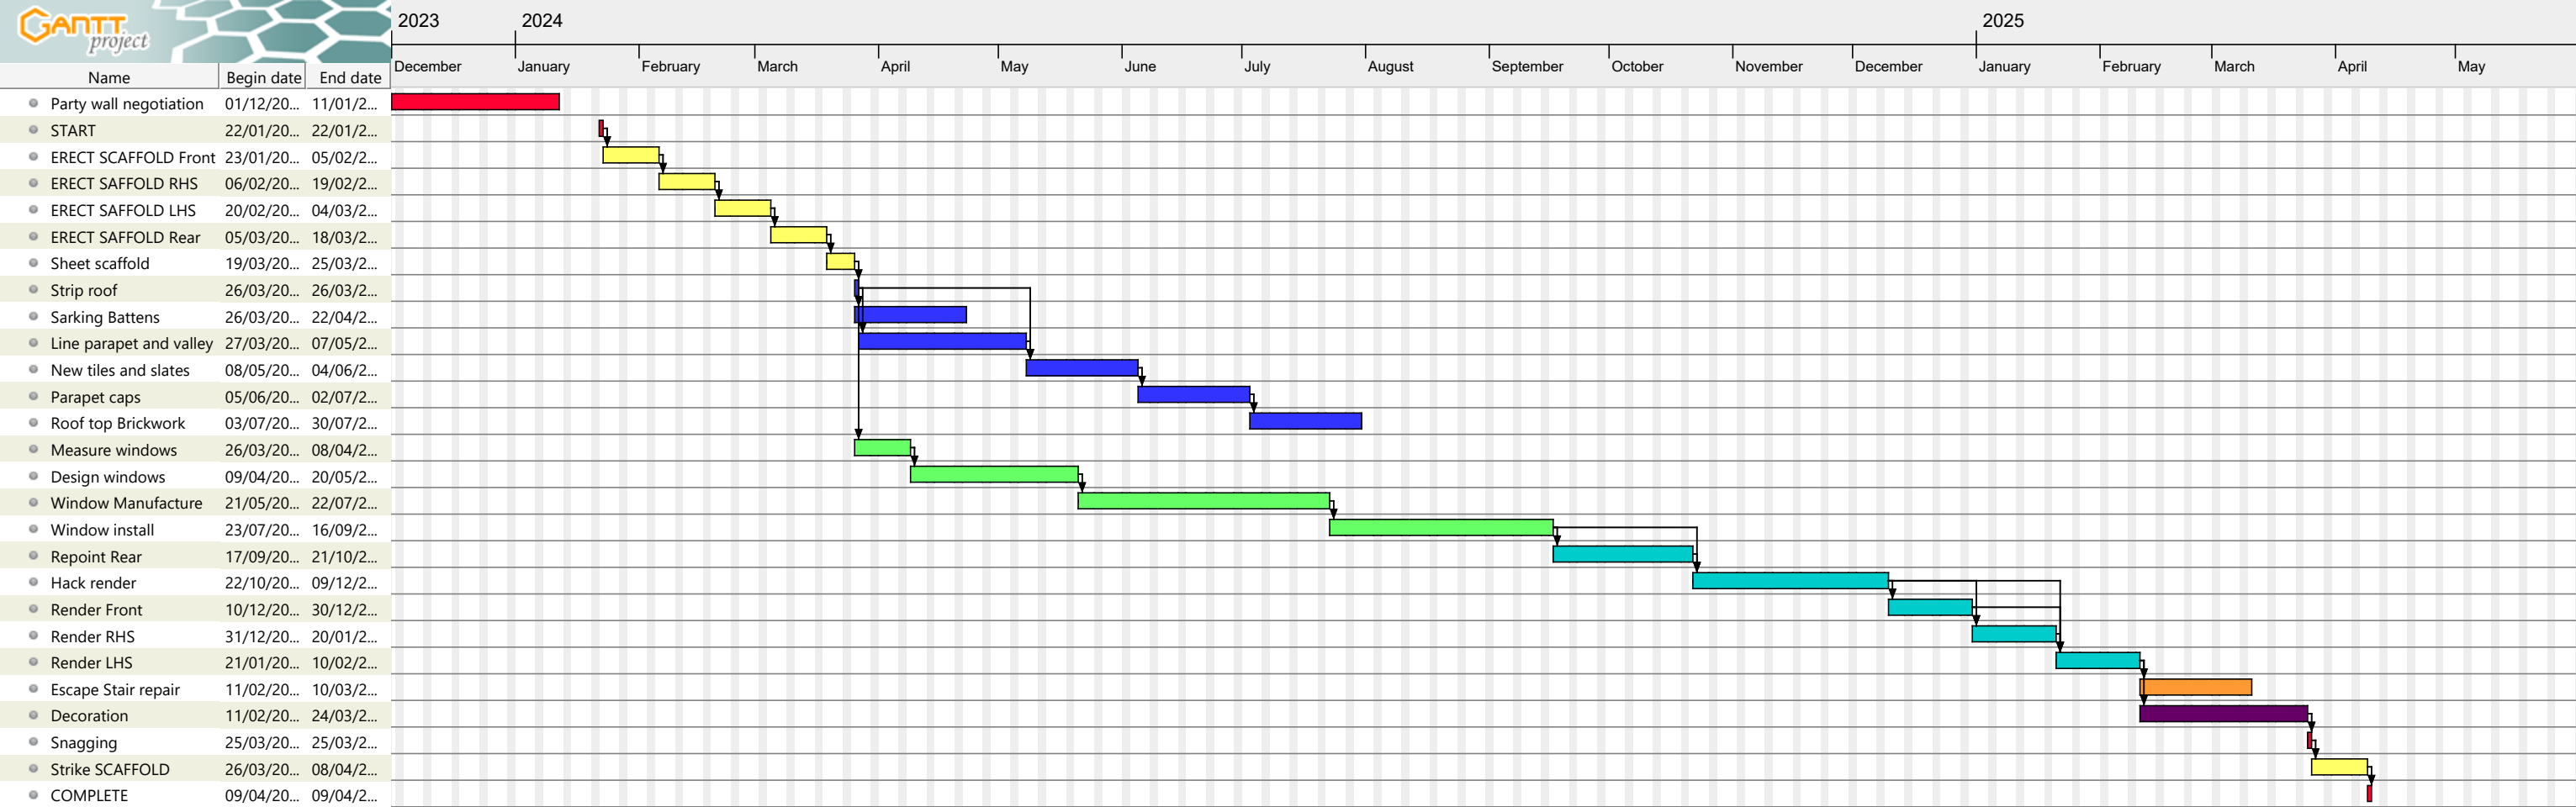

Resources Chart

		2023		2024		2025															
Name		Default role		December	January	February	March	April	May	June	July	August	September	October	November	December	January	February	March	April	May
