

Form detail

#181: Concrete Slab Installation Checklist



Forms

Location

Form date Jun 29, 2022

Description

Due date

Submitted by John Carroll

Status Closed

Last update Jul 8, 2022, 8:21 AM BST

Last updated by John Carroll

Included references Assets | Files | Forms | Issues | Photos

1. Pre-Pour Items

1.1 Project Name
Mal1.2 Date
Jun 30, 20221.3 Location / Area / GL Ref
external slab1.4 Specification / Drawing Reference
Ground1.5 All drainage pop-ups (RWP/SS), Ducting, Services installed to correct setting out
☒ Yes ☐ No ☐ N/A

Photos (1)



20220629_082813_photo

Taken on Jun 29, 2022, 8:28 AM BST**Added on** Jun 30, 2022, 8:03 AM BST**Added by** John Carroll

1.6 HOLD POINT: All drainage air tested and witnessed by the client



Yes



No



N/A

1.7 HOLD POINT: All drainage air tested and witnessed by the client (Insert Name)

Kate Miller

HOLD POINT: All drainage air tested and witnessed by the client (Insert Signature)

**Name**

Kate miller

Date and time

Jun 30, 2022 at 11:46 AM BST

1.8 Sub-Base installed as specified and to correct levels



Yes



No



N/A

Photos (2)



20220624_084617_photo

Taken on Jun 24, 2022, 8:46 AM BST**Added on** Jun 24, 2022, 11:20 AM BST**Added by** John Carroll

20220620_141448_photo

Taken on Jun 20, 2022, 2:14 PM BST**Added on** Jun 21, 2022, 11:11 AM BST**Added by** John Carroll

1.9 Blinding (Sand/Concrete) installed as specified to the correct level

☐

Yes

☐

No

☒

N/A

1.10 Waterproofing Installed as specified

☒

Yes

☐

No

☐

N/A

Photos (2)



20220624_141507_photo

Taken on Jun 24, 2022, 2:15 PM BST**Added on** Jun 24, 2022, 2:24 PM BST**Added by** John Carroll

20220623_075916_photo

Taken on Jun 23, 2022, 7:59 AM BST**Added on** Jun 24, 2022, 11:20 AM BST**Added by** John Carroll

- 1.11 HOLD POINT: Works signed off by Client prior to next Stage (Insert Name)
Kate Miller

HOLD POINT: Works signed off by Client prior to next Stage (Insert Signature)

Name	Date and time
Kate miller	Jun 30, 2022 at 11:46 AM BST

- 1.12 Insulation Installed as specified



Yes



No



N/A

Photos (4)



20220629_082917_photo

Taken on Jun 29, 2022, 8:29 AM BST**Added on** Jun 30, 2022, 8:04 AM BST**Added by** John Carroll

20220629_082907_photo

Taken on Jun 29, 2022, 8:29 AM BST**Added on** Jun 30, 2022, 8:04 AM BST**Added by** John Carroll

20220629_082821_photo

Taken on Jun 29, 2022, 8:28 AM BST**Added on** Jun 30, 2022, 8:03 AM BST**Added by** John Carroll

20220621_154610_photo

Taken on Jun 21, 2022, 3:46 PM BST**Added on** Jun 24, 2022, 11:20 AM BST**Added by** John Carroll

1.13 Reinforcement installed as specified



Yes



No



N/A

Photos (8)



20220629_082949_photo

Taken on Jun 29, 2022, 8:29 AM BST**Added on** Jun 30, 2022, 8:04 AM BST**Added by** John Carroll

20220629_082917_photo

Taken on Jun 29, 2022, 8:29 AM BST**Added on** Jun 30, 2022, 8:04 AM BST**Added by** John Carroll

20220629_082907_photo

Taken on Jun 29, 2022, 8:29 AM BST**Added on** Jun 30, 2022, 8:04 AM BST**Added by** John Carroll

20220629_082855_photo

Taken on Jun 29, 2022, 8:28 AM BST**Added on** Jun 30, 2022, 8:04 AM BST**Added by** John Carroll



20220629_082839_photo

Taken on Jun 29, 2022, 8:28 AM BST**Added on** Jun 30, 2022, 8:04 AM BST**Added by** John Carroll

20220629_082821_photo

Taken on Jun 29, 2022, 8:28 AM BST**Added on** Jun 30, 2022, 8:03 AM BST**Added by** John Carroll

20220629_082813_photo

Taken on Jun 29, 2022, 8:28 AM BST**Added on** Jun 30, 2022, 8:03 AM BST**Added by** John Carroll

20220629_082742_photo

Taken on Jun 29, 2022, 8:27 AM BST**Added on** Jun 30, 2022, 8:03 AM BST**Added by** John Carroll

1.14 Perimeter Shuttering installed to correct line and level



Yes



No



N/A

Photos (4)



20220629_083023_photo

Taken on Jun 29, 2022, 8:30 AM BST

Added on Jun 30, 2022, 8:04 AM BST

Added by John Carroll



20220629_082949_photo

Taken on Jun 29, 2022, 8:29 AM BST

Added on Jun 30, 2022, 8:04 AM BST

Added by John Carroll



20220624_084617_photo

Taken on Jun 24, 2022, 8:46 AM BST

Added on Jun 24, 2022, 11:20 AM BST

Added by John Carroll



20220624_084558_photo

Taken on Jun 24, 2022, 8:45 AM BST

Added on Jun 24, 2022, 11:20 AM BST

Added by John Carroll

1.15 All column/pop-ups boxed out as agreed and reinforcement around box outs installed as specified



Yes



No



N/A

Photos (1)



20220630_112955_photo

Taken on Jun 30, 2022, 11:29 AM BST

Added on Jun 30, 2022, 11:46 AM BST

Added by John Carroll

1.16 Any troughs / Recesses in slabs shuttered and checked for alignment and level



Yes



No



N/A

Photos (4)



20220629_083023_photo

Taken on Jun 29, 2022, 8:30 AM BST**Added on** Jun 30, 2022, 8:04 AM BST**Added by** John Carroll

20220629_082949_photo

Taken on Jun 29, 2022, 8:29 AM BST**Added on** Jun 30, 2022, 8:04 AM BST**Added by** John Carroll

20220629_082917_photo

Taken on Jun 29, 2022, 8:29 AM BST**Added on** Jun 30, 2022, 8:04 AM BST**Added by** John Carroll

20220629_082839_photo

Taken on Jun 29, 2022, 8:28 AM BST**Added on** Jun 30, 2022, 8:04 AM BST**Added by** John Carroll

1.17 All isolation details against existing structures installed as specified

☒

Yes

☐

No

☐

N/A

1.18 Any design joints installed as specified and checked for alignment

☐

Yes

☐

No

☒

N/A

2. Approval to Pour

2.1 All steel columns wrapped in cling film / existing structures or surfaces protected

☐

Yes

☐

No

☒

N/A

2.2 Waterbar/Hydrophilic Strips Installed to all construction joints and stop ends where required

☐

Yes

☐

No

☒

N/A

2.3 Cover to Reinforcement checked and correct

☒

Yes


☐

No

☐

N/A

Photos (2)

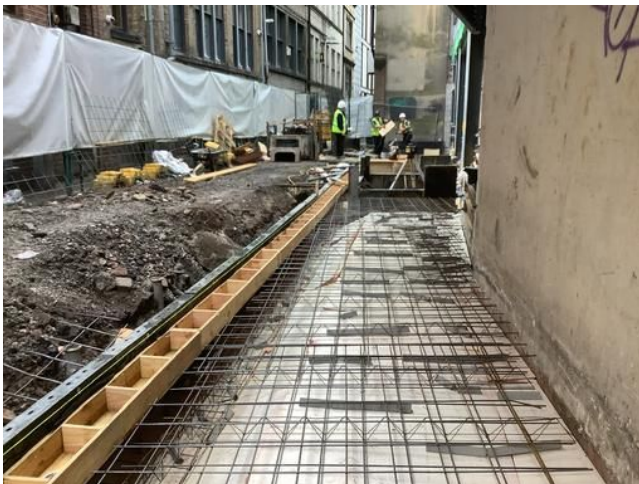

20220629_082949_photo

Taken on Jun 29, 2022, 8:29 AM BST

Added on Jun 30, 2022, 8:04 AM BST

Added by John Carroll



20220629_082917_photo

Taken on Jun 29, 2022, 8:29 AM BST

Added on Jun 30, 2022, 8:04 AM BST

Added by John Carroll

2.4 Previously installed concrete surfaces scabbled / jet washed and suitable for key

☐

Yes

☐

No

☒

N/A

2.5 All Pop-ups / ducting / services capped using appropriate caps

☐

Yes

☐

No

☒

N/A

2.6 Slab cleaned prior to pour and free from debris

☒

Yes

☐

No

☐

N/A

Photos (1)



20220629_082907_photo

Taken on Jun 29, 2022, 8:29 AM BST

Added on Jun 30, 2022, 8:04 AM BST

Added by John Carroll

2.7 HOLD POINT: Pour signed off by Client (Insert Name)

Kate miller

HOLD POINT: Pour signed off by Client (Insert Signature)

Name

Kate miller

Date and time

Jun 30, 2022 at 11:46 AM BST

3. Post Pour Items

3.1 Slab Finish acceptable

☐

Yes

☐

No

☒

N/A

3.2 Level Surveys / Straight edge Surveys completed and surveys uploaded (attach photo of survey book)

☐

Yes

☐

No

☒

N/A
