

## Bituminous Interim Inspection

# BAUDER

|                               |                                                                 |                     |                |
|-------------------------------|-----------------------------------------------------------------|---------------------|----------------|
| <b>PROJECT NUMBER</b>         | B190846/1                                                       | <b>AREA MANAGER</b> | John Wilkinson |
| <b>PROJECT NAME</b>           | Paterson Building - Christie Hospital                           |                     |                |
| <b>PROJECT ADDRESS</b>        | Christie Hospital, Wilmslow Road, MANCHESTER Lancashire M20 4DJ |                     |                |
| <b>APPROVED CONTRACTOR</b>    | Primeseal Roofing Ltd                                           |                     |                |
| <b>TEL</b>                    | 0161 620 7557                                                   |                     |                |
| <b>SITE CONTACT FOR ABOVE</b> | Stephen Duffy (0161 620 7557)                                   |                     |                |

| Roof No. | Roof(s) Inspected | % Complete | Roof Area Name | Size    | System | ID (Office Use Only) |
|----------|-------------------|------------|----------------|---------|--------|----------------------|
| RA 1     | X                 | 20         | RT09_01        | 1020.00 | BTRS   | 940                  |

### Products (Kit List)

| Part                                    | RA 1 |  |  |  |  |  |  |  |  |
|-----------------------------------------|------|--|--|--|--|--|--|--|--|
| VB4-EXPAL                               | X    |  |  |  |  |  |  |  |  |
| PIR FA fp 160mm                         | X    |  |  |  |  |  |  |  |  |
| KSA DUO                                 | X    |  |  |  |  |  |  |  |  |
| G4E                                     | X    |  |  |  |  |  |  |  |  |
| K5K Charcoal Grey                       | X    |  |  |  |  |  |  |  |  |
| Fibre prot mat FSM600                   | X    |  |  |  |  |  |  |  |  |
| Filterfleece                            | X    |  |  |  |  |  |  |  |  |
| Quick Dry Bitumen Primer                | X    |  |  |  |  |  |  |  |  |
| PU Insulation Adhesive - Twin Cartridge | X    |  |  |  |  |  |  |  |  |
| Activator-Primer - Canister             | X    |  |  |  |  |  |  |  |  |

|                      |                   |              |            |
|----------------------|-------------------|--------------|------------|
| <b>INSPECTED BY:</b> | Anthony Symondson | <b>Date:</b> | 26-01-2022 |
|----------------------|-------------------|--------------|------------|

### Questions

| If No is answered to any of the following questions, please add comments in area below                                      | YES | NO |
|-----------------------------------------------------------------------------------------------------------------------------|-----|----|
| Are the correct materials on site?                                                                                          | X   |    |
| Are the materials being stored correctly and safely?                                                                        | X   |    |
| Are there the correct tools and equipment on site?                                                                          | X   |    |
| Is there a copy of a specification, drawings and tapered scheme (if required) on site?                                      | X   |    |
| Is the workmanship consistent with Bauder's requirements for the guarantee?                                                 | X   |    |
| Has the installation been carried out in accordance with the specification?                                                 | X   |    |
| Do the roof areas correspond with the specification?                                                                        | X   |    |
| If Yes is answered to any of the following questions, please add comments in area below                                     | YES | NO |
| Did any discussions take place whilst on site that need recording?                                                          | X   |    |
| Did you notice any unsafe roof installation practices?                                                                      |     | X  |
| Are you aware of any damage to the roof?                                                                                    |     | X  |
| Are you aware of any activity that has the possibility to damage the roof and will require provision of surface protection? |     | X  |

### Actions Required By Technical

### Actions & Comments

Progress to date as follows, ROOF 9 SECTION 1 is approximately 100% AVCL, 90% insulation, underlay and 50% cap sheet installed.

Discussed with operatives that underlay will need cleaning prior to cap sheet being installed due to dust and dirt build up from trafficking

Workmanship is to a good standard with no other issues to report.

Please See Below For Relevant Photographs

| Approved Operative Name | Badge No. |
|-------------------------|-----------|
| Anthony Hickey          | 13-0246   |
| Alin Chifor             | 19-0128   |



Photo 1 - View of progress to section 1



Photo 2 - Overview of section 1



**Photo 3 - View of up stand to section 1**



**Photo 4 - View of up stand to level 9**



**Photo 5 - View of progress to level 9**



**Photo 6 - View of cap sheet to level 9**




**Photo 7 - View of level 9**



**Photo 8 - View of two layer underlay up stand**



**Photo 9 - View of steel support**

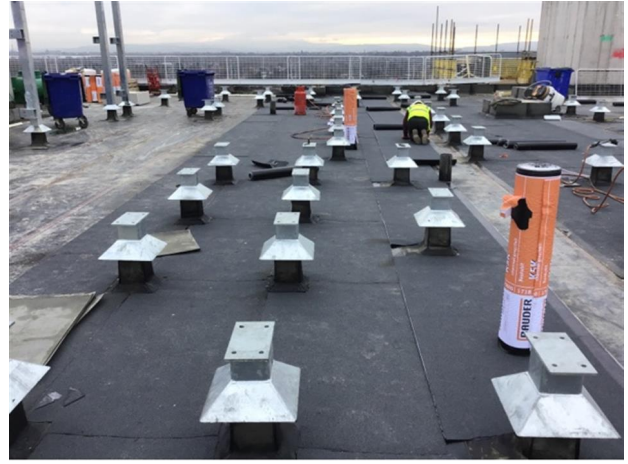

**Photo 10 - View of cap sheet to level 9**



**Photo 11 - View of underlay as comments**



**Photo 12 - View of cap sheet to level 9**
