

Bituminous Interim Inspection

BAUDER

PROJECT NUMBER	B190846/1	AREA MANAGER	John Wilkinson
PROJECT NAME	Paterson Building - Christie Hospital		
PROJECT ADDRESS	Christie Hospital, Wilmslow Road, MANCHESTER Lancashire M20 4DJ		
APPROVED CONTRACTOR	Primeseal Roofing Ltd		
TEL	0161 620 7557		
SITE CONTACT FOR ABOVE	Stephen Duffy (0161 620 7557)		

Roof No.	Roof(s) Inspected	% Complete	Roof Area Name	Size	System	ID (Office Use Only)
RA 1	X	90	RT09_01 - Section 1	340.00	BTRS	940
RA 2	X	20	RT10_03	175.00	BTRS	940

Products (Kit List)

Part	RA 1	RA 2									
VB4-EXPAL	X	X									
PIR FA fp 160mm	X	X									
KSA DUO	X	X									
G4E	X	X									
K5K Charcoal Grey	X	X									
Fibre prot mat FSM600	X	X									
Filterfleece	X	X									
Quick Dry Bitumen Primer	X	X									
PU Insulation Adhesive - Twin Cartridge	X	X									
Activator-Primer - Canister	X	X									

INSPECTED BY:	Anthony Symondson	Date:	04-02-2022
----------------------	-------------------	--------------	------------

Questions

If No is answered to any of the following questions, please add comments in area below	YES	NO
Are the correct materials on site?	X	
Are the materials being stored correctly and safely?	X	
Are there the correct tools and equipment on site?	X	
Is there a copy of a specification, drawings and tapered scheme (if required) on site?	X	
Is the workmanship consistent with Bauder's requirements for the guarantee?	X	
Has the installation been carried out in accordance with the specification?	X	
Do the roof areas correspond with the specification?	X	
If Yes is answered to any of the following questions, please add comments in area below	YES	NO
Did any discussions take place whilst on site that need recording?	X	
Did you notice any unsafe roof installation practices?		X
Are you aware of any damage to the roof?		X
Are you aware of any activity that has the possibility to damage the roof and will require provision of surface protection?		X

Actions Required By Technical

Actions & Comments

Progress to date as follows, ROOF 9 SECTION 1 is 95% complete with perimeter detail and plinth details to finish. SECTION 2 is 10% AVCL installed. SECTION 3 is approximately 70% AVCL installed

SECTION 1 is passed for landscaping

Workmanship is to a good standard with no issues to report.

Please See Below For Relevant Photographs

Approved Operative Name	Badge No.
Anthony Hickey	13-0246
Alin Chifor	19-0128



Photo 1 - View of progress to section 3

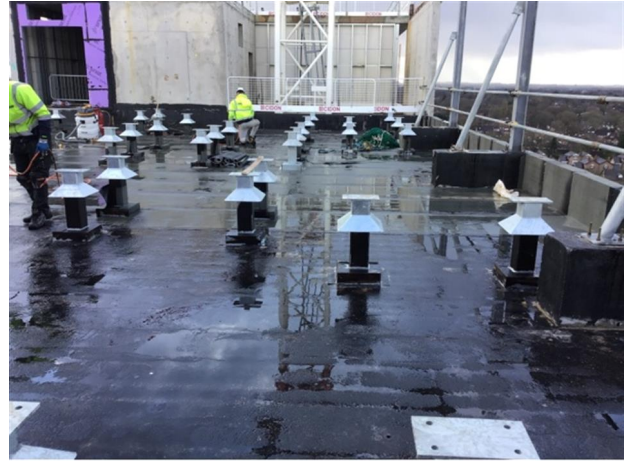


Photo 2 - View of section 3



Photo 3 - View of AVCL to section 3



Photo 4 - View of AVCL to section 3

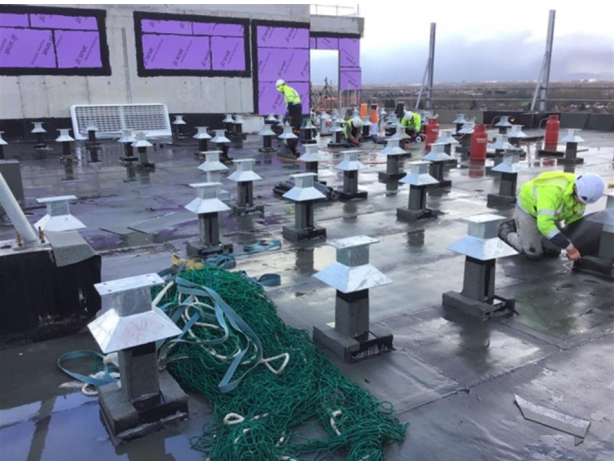


Photo 5 - View of post details to section 3



Photo 6 - Overview of section 1



Photo 7 - View of section 1



Photo 8 - View of SVP detail to section 1



Photo 9 - View of post details to section 1

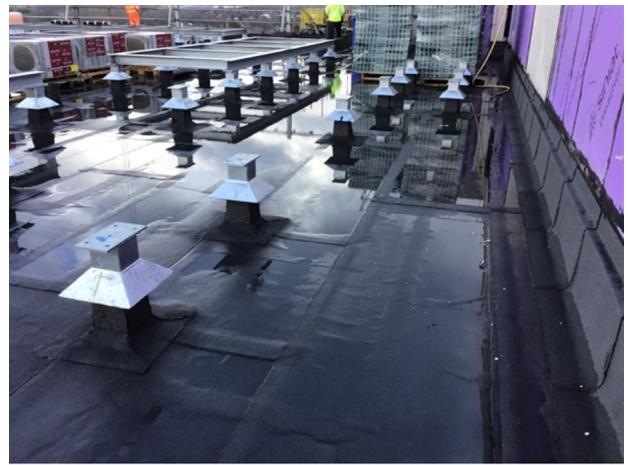


Photo 10 - View of section 1



Photo 11 - View of perimeter plinths to be completed



Photo 12 - View of SVP detail



Photo 13 - View of section 1

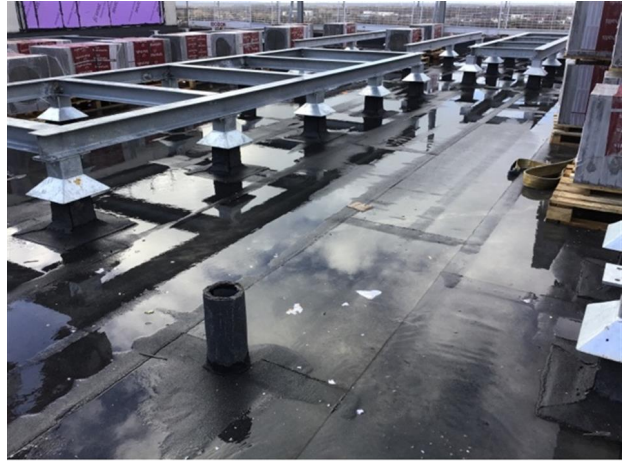


Photo 14 - View of section 1

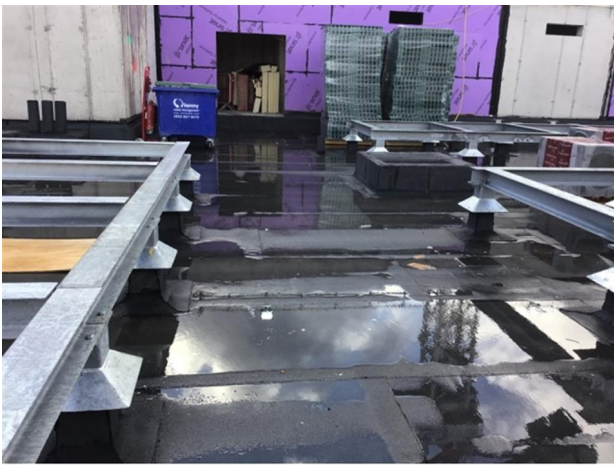


Photo 15 - View of section 1 that is passed for landscaping



Photo 16 - View of section 2
