

ASSOCIATED DOCUMENTS :

This Tree Constraints Plan should be read in conjunction with the Arboricultural Implications Assessment Proposed Development At New Street, Altrincham (3rd November, 2021) produced by Mulberry Tree Management which details tree condition, life expectancy and it's contribution to amenity.

TREE WORKS NOTES:

All felling and tree surgery is to be carried out by an Arboricultural Association approved contractor. All operations are to be carried out in accordance with BS3998:2010 Recommendations for tree work and N.P.T.C certification guidelines.

METHOD STATEMENT:

Tree felling and surgery works are to be carried out prior to the commencement of main construction works. Once complete, approved hoarding is to be erected around the construction area. This hoarding is to be sited outside the canopy extents of retained trees and is to remain outside the canopies throughout the contract period. This fencing shall not be removed or repositioned without the prior written permission of the LPA.

Under no circumstances should materials, vehicles, equipment, diesel or spoil be stored within the canopy of retained trees. Similarly no excavations for services or other construction activities are to be carried out within the protected zone unless approved in writing from the LPA.

Note:-

- Tree felling should not be undertaken through the months of March to August unless agreed with the local planning authority due to the nesting birds season.

- If the program of works clashes with these dates then any trees in question should be heavily pruned to reduce the chance of nesting during the above months.

- All tree removal and excavation works should be undertaken in accordance with Amenity Tree Care's Preliminary Tree Survey.

6.1 Arboricultural method statement



6.1.1 A precautionary approach towards tree protection should be adopted and any operations, including access, proposed within the RPA (or crown spread where this is greater) should be described within an arboricultural method statement, in order to demonstrate that the operations can be undertaken with minimal risk of adverse impact on trees to be retained.

6.2 Barriers and ground protection

6.2.1 General
6.2.1.1 All trees that are being retained on site should be protected by barriers and/or ground protection (see 5.5) before any materials or machinery are brought onto the site, and before any demolition, development or stripping of soil commences. Where all activity can be excluded from the RPA, vertical barriers should be erected to create a construction exclusion zone. Where, due to site constraints, construction activity cannot be fully or permanently excluded in this manner from all or part of

6.2.2 Barriers

6.2.2.1 Barriers should be fit for the purpose of excluding construction activity and appropriate to the degree and proximity of work taking place around the retained tree(s). Barriers should be maintained to ensure that they remain rigid and complete.

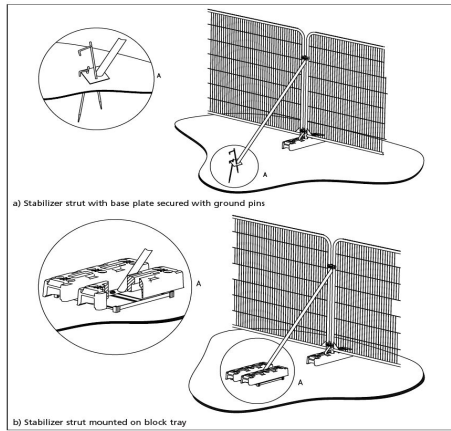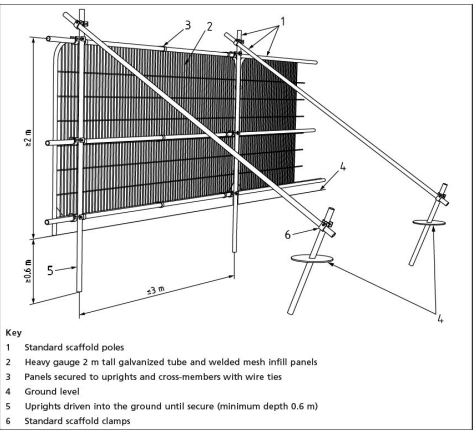

6.2.3 Ground protection during demolition and construction

6.2.3.1 Where construction working space or temporary construction access is justified within the RPA, this should be facilitated by a set-back in the alignment of the tree protection barrier. In such areas, suitable existing hard surfacing that is not proposed for re-use is part of the finished design should be retained to act as temporary ground protection during construction, rather than being removed during demolition. The suitability of such surfacing for this purpose should be evaluated by the project arboriculturist and an engineer as appropriate.

6.2.3.2 Where the set-back of the tree protection barrier would expose unmade ground to construction damage, new temporary round protection should be installed as part of the implementation of physical tree protection measures prior to work starting on site.

6.2.3.3 New temporary ground protection should be capable of supporting any traffic entering or using the site without being distorted or causing compaction of underlying soil.

7.2 Avoiding physical damage to the roots during demolition or construction

7.2.1 To avoid damage to tree roots, existing ground levels should be retained within the RPA. Intrusion into soil (other than for piling) within the RPA is generally not acceptable, and topsoil within it should be retained in situ. However, limited manual excavation within the RPA might be acceptable, subject to justification. Such excavation should be undertaken carefully, using hand-held tools and preferably by compressed air soil displacement.

7.3 Tree protection during demolition

7.3.1 Where demolition is proposed on a site where trees are to be retained, access facilitation pruning should be undertaken as necessary to prevent injurious contact between demolition plant and the tree(s). In some cases, working space may be provided by temporarily tying back tree branches. Pruning or tying should be undertaken in accordance with a specification prepared by an arboriculturist.
NOTE The local authority will be able to advise whether the trees are under statutory protection such that consent for tree works might be required.

7.3.2 When demolishing a structure (including underground structures) within what would otherwise be the RPA, barriers should be erected, and ground protection installed (see 6.2.3), to protect the underlying soil to the edge of the existing structure.

7.3.4 Where trees stand adjacent to structures to be removed, the demolition should be undertaken inwards within the footprint of the existing building (often referred to as "top down, pull back")

Existing trees to be pruned back as required to provide sufficient room for construction of new apartment block. Trees to have canopy thinned and crown lifted. Works to existing trees subject to site review with tree surgeon to agree final scope. Method statement to be provided by contractor for approval by Landscape Architect prior to works being undertaken. All works to existing trees to be undertaken outside bird nesting season (March- August).



THIS DRAWING IS COPYRIGHT PROTECTED AND MAY NOT BE REPRODUCED IN WHOLE OR PART WITHOUT WRITTEN AUTHORITY FROM THE OWNER.

NOTES:

1. Do not scale from this drawing.
2. Always work to noted dimensions.
3. All dimensions are in millimetres unless otherwise stated.
4. All setting out, levels and dimensions to be agreed on site.
5. The dimensions of all materials must be checked on site before being laid out.
6. This drawing must be read with the relevant specification clauses and detail drawings.
7. Order of construction and setting out to be agreed on site.

Existing Trees
To be removed

Existing Trees
To be retained

Root Protection Area of Retained Trees

Category B
(moderate Quality)

Category C
(low Quality)

Category U
(unsuitable for Retention)

T3 Tree Reference Code To Tree Survey

Tree Condition Survey
Refer to:
Arboricultural Impact Assessment Overview Plots 2 & 3,
Angel Square, Manchester-Bowland Tree Consultancy Ltd
(June, 2022)

Revision	Date	Description	Drawn	Apprvd.
S2-P01	23-06-22	For review and comment	EKH	MS

Planit I.E. Limited
E: info@planit-ie.com W: planit-ie.com
MANCHESTER
2 Back Grafton St, Altrincham, WA14 1DY
T: 0161 928 9281
LEEDS
No.1 Aire Street, Leeds Station, Leeds, LS1 4PR
T: 0113 824 6413
LIVERPOOL
Tempest 5.3, 12 Tithebarn Street, Liverpool, L2 2DT
T: 0151 363 1230
LONDON
Unit 6 Waterside, 44-48 Wharf Road, London, N1 7UX
T: 0207 253 5678
STANDISH
Standish Gatehouse, Stonehouse, Gloucestershire, GL10 3BZ
T: 0145 360 7080

Client MEPC

Project 2&3 Angel Square

Drg Title Tree Retention and Removal

Created on 23/06/2022 Created by LB Approved by MS

Scale 1:250 Size A1 Workstage Stage 2

Drg No. PL2190.1-PLA-XX-DR-L-1002 Suitability S2 Revision P01
