
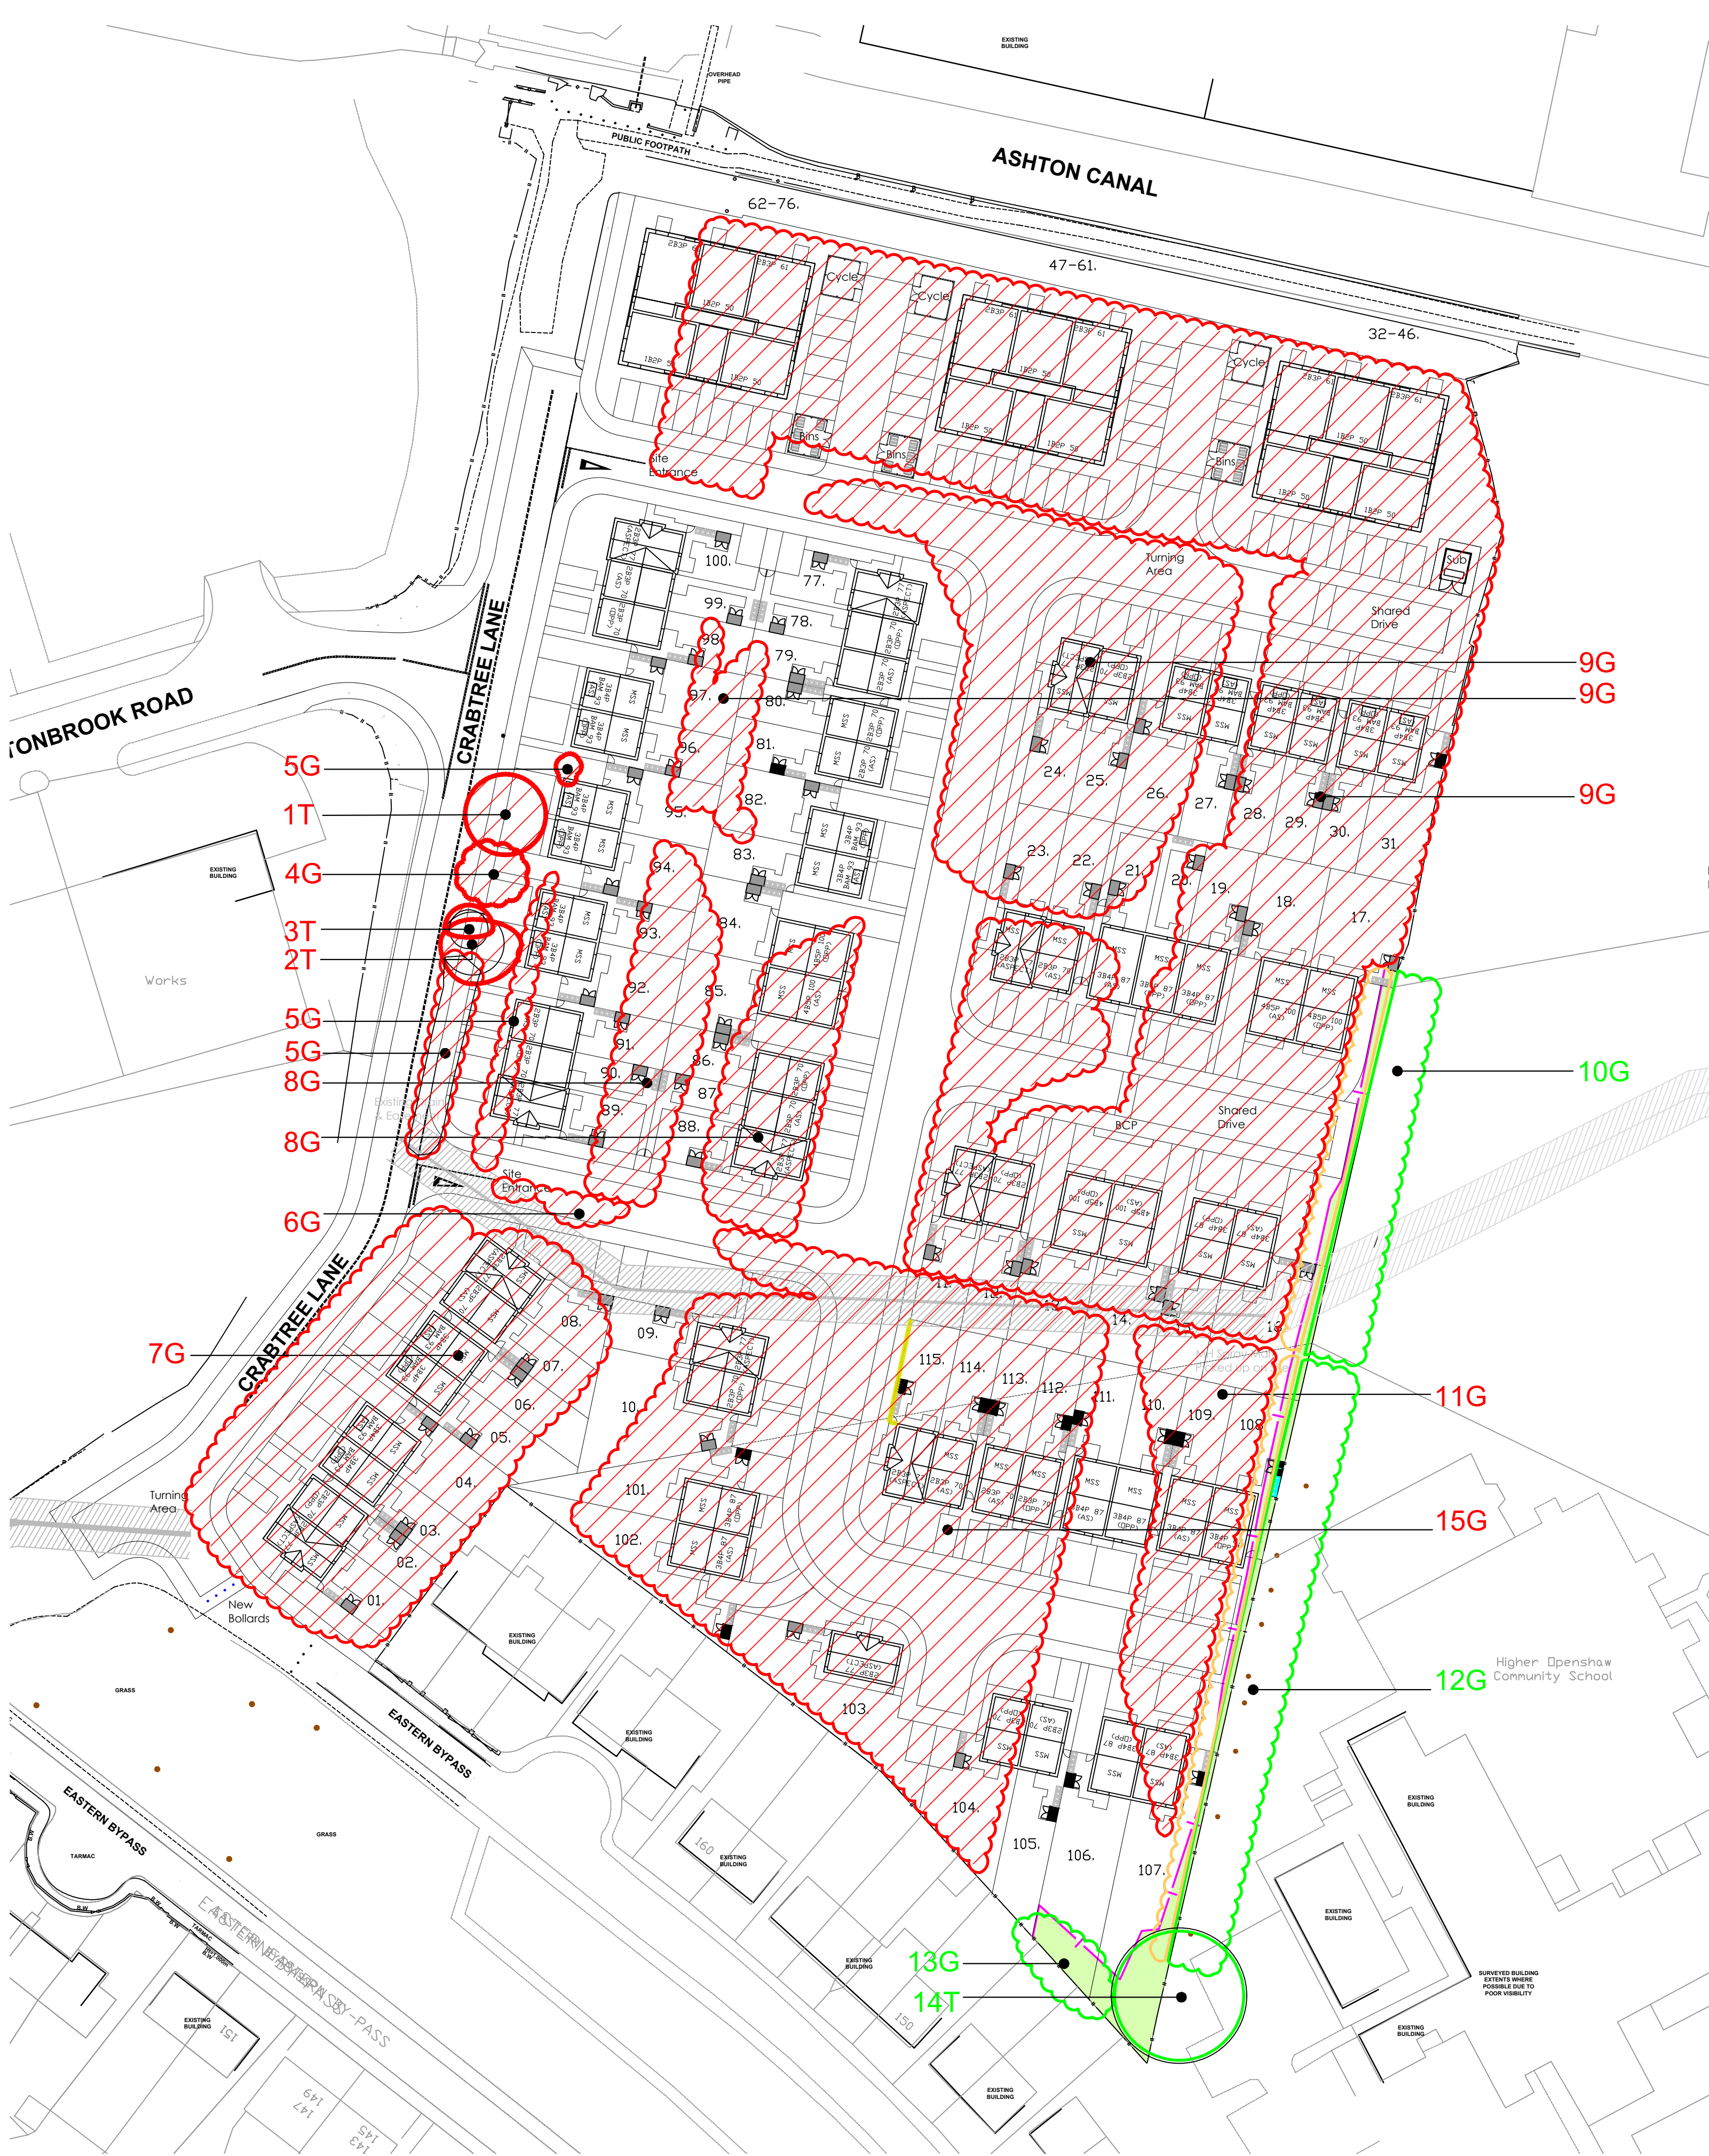










Tree Schedule			
Tree Number	Species	RPA Radius	Category
1T	Sycamore	4.8m	B2
2T	Sycamore	3.9m	C1
3T	Swedish Whitebeam	2.4m	C1
4G	Sycamore, Norway Maple and Silver Birch		B2
5G	Ash, Silver Birch, Elderberry, Goat Willow, Buddleia, Wild Cherry and Norway Maple		C3
6G	Group of Sycamore		C3
7G	Goat Willow, Silver Birch and Buddleia		C3
8G	Silver Birch, Buddleia, Wild Cherry and Sycamore		C3
9G	Silver Birch, Buddleia, Wild Cherry, Goat Willow, Alder.		C2
10G	Goat Willow, Alder and Wild Cherry		C1
11G	Goat Willow, Sycamore and Ash		C1
12G	Norway Maple and Swedish Whitebeam		B2
13G	2x Wild Cherry and 1x Elderberry		C1
14T	Weeping Willow	8.4m	B2
15G	Goat Willow, Silver Birch and Buddleia		C2

Phase	Requirements	Method																														
1 Prior to erection of protective fencing.	Undertake tree and vegetation removal and pruning works Trees/vegetation to be removed:  Trees/vegetation to be pruned: 	Refer to section 5.5 of AIA/MS report. All tree works to be carried out to BS3998: 2010: by suitably qualified and insured professional tree surgeons. The following tree felling must be undertaken at this Phase: <table><thead><tr><th colspan="2">Items requiring removal:</th></tr></thead><tbody><tr><td>1T</td><td>Sycamore</td></tr><tr><td>2T</td><td>Sycamore</td></tr><tr><td>3T</td><td>Swedish Whitebeam</td></tr><tr><td>4G</td><td>Sycamore, Norway Maple and Silver Birch</td></tr><tr><td>5G</td><td>Ash, Silver Birch, Elderberry, Goat Willow, Buddleia, Wild Cherry and Norway Maple</td></tr><tr><td>6G</td><td>Group of Sycamore</td></tr><tr><td>7G</td><td>Goat Willow, Silver Birch and Buddleia</td></tr><tr><td>8G</td><td>Silver Birch, Buddleia, Wild Cherry and Sycamore</td></tr><tr><td>9G</td><td>Silver Birch, Buddleia, Wild Cherry, Goat Willow, Alder.</td></tr><tr><td>11G</td><td>Goat Willow, Sycamore and Ash</td></tr><tr><td>15G</td><td>Goat Willow, Silver Birch and Buddleia</td></tr></tbody></table> The following tree pruning must be undertaken at this Phase: <table><thead><tr><th colspan="2">Items requiring pruning:</th></tr></thead><tbody><tr><td>10G</td><td>Goat Willow, Alder and Wild Cherry. Prune back lateral westerly branch spread to close the edge of the side boundary</td></tr><tr><td>12G</td><td>Norway Maple & Swedish Whitebeam. Prune back lateral westerly branch spread by approximately 2m in length to provide clearance.</td></tr></tbody></table>	Items requiring removal:		1T	Sycamore	2T	Sycamore	3T	Swedish Whitebeam	4G	Sycamore, Norway Maple and Silver Birch	5G	Ash, Silver Birch, Elderberry, Goat Willow, Buddleia, Wild Cherry and Norway Maple	6G	Group of Sycamore	7G	Goat Willow, Silver Birch and Buddleia	8G	Silver Birch, Buddleia, Wild Cherry and Sycamore	9G	Silver Birch, Buddleia, Wild Cherry, Goat Willow, Alder.	11G	Goat Willow, Sycamore and Ash	15G	Goat Willow, Silver Birch and Buddleia	Items requiring pruning:		10G	Goat Willow, Alder and Wild Cherry. Prune back lateral westerly branch spread to close the edge of the side boundary	12G	Norway Maple & Swedish Whitebeam. Prune back lateral westerly branch spread by approximately 2m in length to provide clearance.
Items requiring removal:																																
1T	Sycamore																															
2T	Sycamore																															
3T	Swedish Whitebeam																															
4G	Sycamore, Norway Maple and Silver Birch																															
5G	Ash, Silver Birch, Elderberry, Goat Willow, Buddleia, Wild Cherry and Norway Maple																															
6G	Group of Sycamore																															
7G	Goat Willow, Silver Birch and Buddleia																															
8G	Silver Birch, Buddleia, Wild Cherry and Sycamore																															
9G	Silver Birch, Buddleia, Wild Cherry, Goat Willow, Alder.																															
11G	Goat Willow, Sycamore and Ash																															
15G	Goat Willow, Silver Birch and Buddleia																															
Items requiring pruning:																																
10G	Goat Willow, Alder and Wild Cherry. Prune back lateral westerly branch spread to close the edge of the side boundary																															
12G	Norway Maple & Swedish Whitebeam. Prune back lateral westerly branch spread by approximately 2m in length to provide clearance.																															
2 Prior to any construction works on site	Erection of protective fencing: To retain throughout the duration of the development: 	Protective fencing is to be erected in accordance with 5.6 of AIA/MS report. The fencing must comply with the positions shown in the Tree Protection Plan. A scale copy of the Tree Protection Plan must be used as reference and fencing positions measured from the Plan using a scale rule and/or using the provided distances where shown. No works, no storage of materials, no access, or any ground disturbance is to take place within the Tree Protection Barrier Fencing other than works specified within the Arboricultural Method Statement. Fenced areas are to be treated as Construction Exclusion Zones. Warning signs to be placed on all protective fencing. For large sections of fencing the signs must be placed at 20m intervals. Signs must be laminated and securely attached at all corners. Two signs are to be placed side by side; copies of which are attached within Appendix A.																														
3 Verifying quality of protective barriers	Verify that the location and quality of tree protection barriers is adequate prior to onset of main site works.	Site visit with Arboricultural Consultant and Site Manager. Tree Officer to be pre-informed of visit. In order for set works to proceed the pro-forma in Appendix B. of the AIA/MS report is to be completed and passed on to the local planning authority: If the protective barriers are not adequately, work is not to proceed until rectified.																														

Phase	Requirements	Method
4 Ongoing	Maintain protective fencing	The tree protective barrier fencing is to remain in situ during all construction works.
5 External works within Construction Exclusion Zones	Details of ground level changes and appropriate engineering solutions near retained trees to be established within identified Construction Exclusion Zones: 	Full consideration of tree impacts can only be determined once external works information is available. A specification can then be determined for ground works adjacent trees, following consultation between engineers and the project arboriculturalist.

- **TREES/GROUPS TO BE RETAINED**
- **TREES/GROUPS TO BE REMOVED**
- **SECTIONS OF LATERAL CANOPIES OF GROUPS 10G AND 13G THAT REQUIRE PRUNING BACK**
- **FULL SPECIFICATION TREE PROTECTION BARRIER FENCING. TO REMAIN IN SITU THROUGHOUT DEVELOPMENT PROCESS**
- **CONSTRUCTION EXCLUSION ZONES. NOTE: FULL ENGINEERING SPECIFICATION ON FINAL LEVEL REQUIREMENTS ARE NEEDED PRIOR TO FINAL DETERMINATION OF IMPACTS**

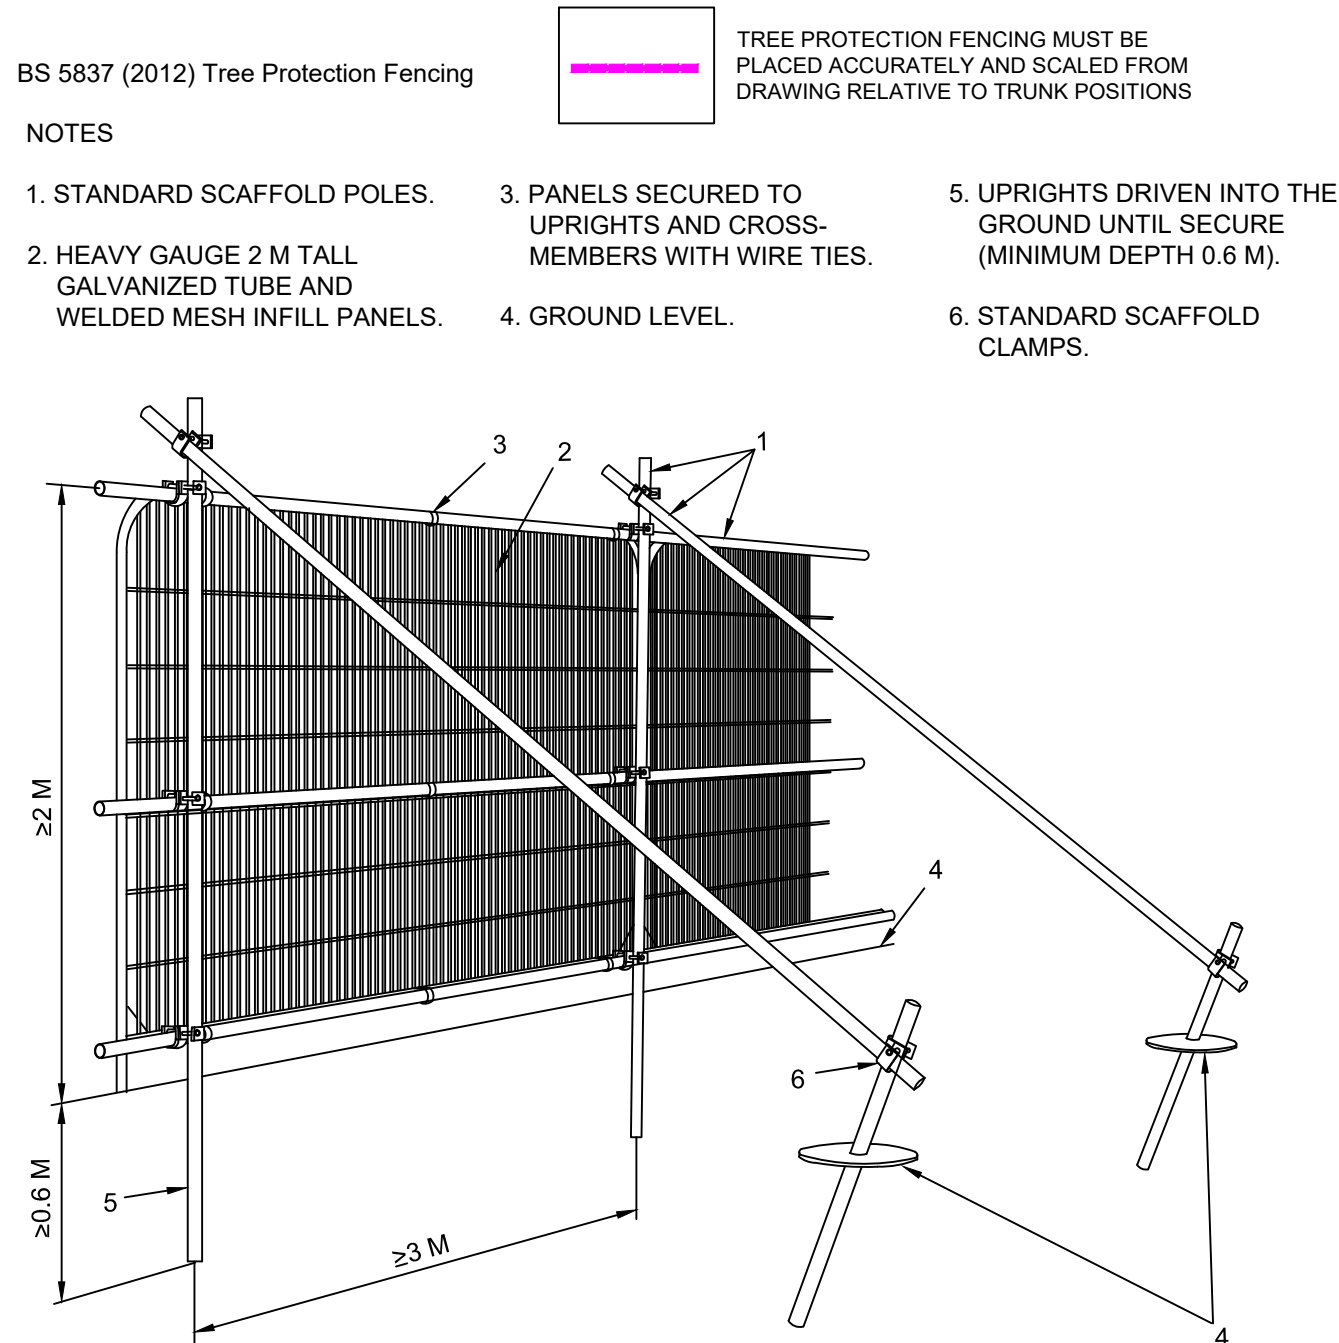


THIS DRAWING MUST BE VIEWED
IN COLOUR AND READ IN
CONJUNCTION WITH
ARBORICULTURAL IMPACT
ASSESSMENT AND METHOD
STATEMENT

No permission to be scaled from this drawing
© copyright reserved

Date

Dwn

Rev



Landscape Architecture

Trevor Bridge Associates Ltd
Ashton Old Baths
Stanford Street West
Ashton-under-Lyne
Lancs OL6 7FW
Tel: 0161-804 2099
E-mail: info@trevorbridge.co.uk

Project
TREE PROTECTION PLAN

Title
LAND AT CRABTREE LANE, OPENSRAW,
MANCHESTER.
MCI DEVELOPMENTS

Date	Scale(s)	Dwg no	Rev
JUL 22	1:500	6696.03	
Dwn	Chgd	@ A0	
MG			
