



Arboricultural Method Statement

Premier Modular

**The Stirling Centre,
Scotland Hall Road,
Newton Heath,
Manchester,
M40 2RE**

09 March 2026

Jon Hartley BSc(Hons) MArbor A

Table of Contents

Introduction	4
Tree Survey	5
Arboricultural Impact Assessment	6
Trees to be Removed	7
Arboricultural Method Statement	8
Sequencing of works	8
Tree Work	10
Protected Species (general informative for tree works)	11
Protective Measures	13
Demolition	17
Construction	18
Prohibition	25
Site Management	26
Services	27
Landscaping	28
Monitoring and Supervision	29
Appendices	31
Appendix 1: Tree Schedule	32
Appendix 2: Arboricultural Impact Assessment	34
Appendix 3: Tree Protection Plan	36
Appendix 4: Tree Protection Notice	38
Appendix 5: Contact Details	40
Document Production Record	42

Table 1: Documents referred to	4
Table 2: Impacts upon the RPAs of retained trees	6
Table 3: Number of individual trees to be removed	7
Table 4: Number of groups to be removed.....	7
Table 5: Sequencing of works	8
Table 6: Summary of tree works	10
Figure 1: Example of protective barrier fencing constructed with a scaffold frame (BS5837)	15
Figure 2: Example of protective barrier fencing with above-ground stabilising system (BS5837).....	16
Figure 3: Example cross-section for multi-dimensional confinement system using kerb edging.....	21
Figure 4: Example cross-section for multi-dimensional confinement system using timber edging.....	21
Figure 5: Example cross-section of a “road deck” system.....	23

Introduction

Instruction

Arbtech Consulting Limited (Arbtech) received written instruction from Richard Keeting at Premier Modular to attend The Stirling Centre, Scotland Hall Road, Newton Heath, Manchester, M40 2RE; grid reference SJ 88141 99642 to undertake an arboricultural survey to BS5837:2012 guidance to assess trees, hedges and major shrub groups growing on and within influencing distance of the site and to produce a Schedule of Trees and Tree Constraints Plan (TCP), Arboricultural Impact Assessment (AIA), Arboricultural Method Statement (AMS) and Tree Protection Plan (TPP).

Executive Summary

A tree survey guided by British Standard 5837:2012 'Trees in relation to design, demolition and construction – Recommendations' ("BS5837") was carried out to include all trees within influencing distance of the proposed area for development.

This report has subsequently been produced, balancing the layout of the proposed development against the competing needs of retained trees. This report comprises all of the requisite elements of an arboricultural implications assessment, method statement, and any required supporting plans.

It is the conclusion of this report that if followed, the overall quality and longevity of the amenity contribution provided for by retained trees within and adjacent to the site will not be adversely affected as a result of the local planning authority consenting to the proposed development.

Table 1: Documents referred to

Document	Originator	Reference Number	Title
Survey base drawing	Vaughan Architecture Ltd.	40693-PML-00-DR-A-000020	Existing Site Plan
Proposed layout drawing	Vaughan Architecture Ltd.	40693-PML-00-DR-A-000021	Prioposed Site Plan
Tree Schedule (TS)	Arbtech Consulting Ltd	Arbtech TS 01	Tree Schedule
Arboricultural Impact Assessment (AIA)	Arbtech Consulting Ltd	Arbtech AIA 01	Arboricultural Impact Assessment
Tree Protection Plan (TPP)	Arbtech Consulting Ltd	Arbtech TPP 01	Tree Protection Plan

Tree Survey

An arboricultural survey guided by British Standard 5837:2012: Trees in Relation to Design, Demolition and Construction - Recommendations of all trees within impacting distance of the site was undertaken by Andrew Davies on 28 February 2026.

A total of 9No. individual trees were surveyed.

For full details of all the trees surveyed, see Appendix 1: Tree Schedule.

Survey Limitations

The survey was made at ground level using visual observation only. Detailed examinations, such as climbing inspections and advanced decay detection equipment, were not employed, though they may form part of the survey's management recommendations. Measurements were taken using specialist tapes, lasers, and GPS devices. Where this was not possible, measurements are estimated. Inaccessible trees will have the best estimates made about their location, physical dimensions, and characteristics. Trees have been grouped where BS5837 guides us that it is expedient to do so. Trees have been excluded from the survey if they are found by us to be sufficiently far away from the proposed developable area or if they are outside of the red line boundary plan showing the expectations of our client for the extent of the survey.

Scope

Pre-development tree surveys make arboricultural management recommendations based exclusively upon the condition of the individual tree or group of trees relative to their present context (*i.e., not in relation to the proposed development*).

Legal Status

No statutory protection check has been performed. BS5837 does not draw any distinction between trees subject to statutory protection, such as a Tree Preservation Order ("TPO"), and those trees without, starting at Annex B:

The potential effect of development on trees, whether statutorily protected (e.g. by a tree preservation order or by their inclusion within a conservation area) or not, is a material consideration that is taken into account in dealing with planning applications. Consequently, we do not seek to offer any comparison between or infer any difference in the quality or importance of TPO trees and other trees.

Arboricultural Impact Assessment

An Arboricultural Impact Assessment (AIA) guided by British Standard 5837:2012: Trees in Relation to Design, Demolition and Construction - Recommendations was undertaken by Jon Hartley on 06 March 2026 to determine the potential conflicts between the proposed development scheme and existing trees located on and near the site and has subsequently produced this Arboricultural Method Statement to demonstrate how the proposed scheme can be successfully implemented without causing harm to retained trees.

Several issues may need to be addressed in an Arboricultural Impact Assessment between the trees and the proposed development; these are as follows:

- The effect and extent of the proposed development within the root protection areas (RPAs) of retained trees;
- The potential conflicts of the proposed development with canopies of retained trees and;
- The likelihood of any future remedial works to retained trees beyond those that would have been scheduled as part of usual management.

Table 2: Impacts upon the RPAs of retained trees

Tree Number	Species	Structure	Incursion	
			(m ²)	(%)
T01	Common whitebeam	Hard surface	12.1	15.2
T01	Common whitebeam	Foundation	5.7	7.1
T02	Common ash	Hard surface	6.9	16.9
T02	Common ash	Foundation	3	7.4
T03	Common ash	Hard surface	8.8	15.0
T03	Common ash	Foundation	6.6	11.3
T04	Common ash	Hard surface	9	13.8
T04	Common ash	Foundation	0.8	1.2
T06	Common whitebeam	Hard surface	1.6	2.4

These impacts can be seen on the Arboricultural Impact Assessment (Arbtech AIA 01). See Appendix 2: Arboricultural Impact Assessment.

Trees to be Removed

The implementation of the proposed development is not predicated upon the removal of existing trees.

A breakdown of all tree works can be seen in Table 6: Summary of tree works.

Table 3: Number of individual trees to be removed

U	A	B	C
0	0	0	0

Table 4: Number of groups to be removed

U	A	B	C
0 (0)	0 (0)	0 (0)	0 (0)

0 = partial removal of a group

Arboricultural Method Statement

This Arboricultural Method Statement (Arbtech AMS 01) demonstrates how any aspect of the development that could potentially result in tree loss or damage may be implemented and provides an adequate level of protection for trees that are to be retained during the proposed works.

Details of key site personnel, including the Site/Project Manager, will be submitted to the Council's Tree Officer before site works commence. This Arboricultural Method Statement (Arbtech AMS 01) is to be approved and agreed to in writing by all key personnel before the commencement of any site works.

No site personnel are to be present, and no demolition, site clearance, building work, or material delivery is to occur until the protective measures are in accordance with this Arboricultural Method Statement (Arbtech AMS 01) and the Tree Protection Plan (Arbtech TPP 01). Unless otherwise specified, protective measures will remain unaltered and in situ for the entire duration of the construction.

Sequencing of works

A logical sequence of events is to be observed and shall be phased as follows:

Table 5: Sequencing of works

Stage	Event
Stage 1.	Undertake and complete tree works as specified within Table 6: Summary of tree works
Stage 2.	Installation of protective measures in accordance with the approved Tree Protection Plan(s) (Arbtech TPP 01).
Stage 3.	Pre-commencement site meeting.
Stage 4.	Undertake and complete ground works.
Stage 5.	Undertake and complete construction works
Stage 6.	Undertake and complete external landscaping outside of the construction exclusion zones (CEZs).
Stage 7.	Removal of all machinery and materials from the site.
Stage 8.	Dismantle and removal of protective tree measures.
Stage 9.	Undertake and complete external landscaping within the construction exclusion zones (CEZs).

Stage 10.	Site completion and sign-off from Project Arboriculturalist.
-----------	--



Tree Work

For reasons of public safety, all tree works referred to herein must be carried out before site personnel commence work or building materials are delivered.

Table 6: Summary of tree works

Tree Number	Species	Works	Category
T01	Common whitebeam	Prune: Crown lift locally to achieve 3m clearance over the proposed hard surface and 1m clearance to the proposed structure.	B
T02	Common ash	Prune: Crown lift locally to achieve 3m clearance over the proposed hard surface and 1m clearance to the proposed structure.	B
T03	Common ash	Prune: Crown lift locally to achieve 3m clearance over the proposed hard surface and 1m clearance to the proposed structure.	B
T04	Common ash	Prune: Crown lift locally to achieve 3m clearance over the proposed hard surface and 1m clearance to the proposed structure.	B

Notes

All tree work is to be undertaken in accordance with British Standard BS 3998:2010 - Recommendations for tree work. All arising's are to be removed, and the site is to be left as found. Care is to be taken of the ground around retained trees to make sure that it does not become compacted as a result of tree surgery operations. No equipment or vehicles such as timber Lorries, tractors, excavators, or cranes shall be parked or driven beneath the crowns of any retained trees to prevent subsequent compaction and root death.

Protected Species (general informative for tree works)

Conservation Status of British Bats

The consensus in Britain and Europe is that virtually all bat species are declining and vulnerable. Our understanding of population status is poor as there is very little historical data for most bat species. Certain species, such as the horseshoe bats, are better understood and have well-documented contractions in range and population size. Given this general picture of decline in the UK Government, the UK Biodiversity Action Plan has designated five species of bats as priority species (greater and lesser horseshoe bats, barbastelle, Bechstein's, and pipistrelle). These plans provide an action pathway for investigating the maintenance and restoration of the former populations' levels.

Legal Status of British Bats

Given the above position, all British bats, as well as their breeding sites and resting places, enjoy national and international protection. All bat species in the UK are fully protected under the Wildlife and Countryside Act 1981 (as amended) through inclusion in Schedule 5. All bats are also listed in Annex IV (and some in Annex II) of the EC Habitats Directive, giving further European protection. Taken together, the Act and Conservation of Habitats and Species Regulations 2012 (as amended)* make it an offence to intentionally or deliberately kill, injure or capture (take) bats;

- Deliberately disturb bats (whether in a roost or not);
- Damage, destroy or obstruct access to bat roosts;
- Possess or transport a bat or any part of a bat unless acquired legally;
- Sell, barter or exchange bats or parts of bats

Although the legislation does not strictly protect foraging grounds, it does protect roost sites. Bat roosts are protected at all times of the year, whether or not bats are present. Any disturbance of a roost due to development must be licenced.

**the regulations that delivered by the UK's commitments to the Habitats Directive.*

Breeding Birds

All nesting birds are protected under the Wildlife and Countryside Act (as amended) 1981, which makes it an offence to intentionally kill, injure or take any wild bird or take, damage or destroy its nest whilst in use or being built, or take or destroy its eggs. Furthermore, several birds enjoy further protection under that Act and are listed on Schedule 1 of the Act. These further protected birds are also protected from disturbance and it may be necessary to operate "no-go" buffer zones around such nests – typically out to 100m. Planning policy guidance on the treatment of species identified as priorities under the biodiversity action programme suggests that local authorities should take measures to protect the habitats of these species from further decline through policies in local development documents and should ensure that they are protected from the adverse effects of development, where appropriate, by using planning conditions or obligations.

The conservation of these species should be promoted through the incorporation of beneficial biodiversity designs within developments.

Protective Measures

Protective measures are to be installed immediately following the completion of the tree works and sited and aligned in accordance with the Tree Protection Plan (Arbtech TPP 01) before the commencement of any works or the introduction of any machinery or material to the site.

Upon installing the protective measures around the retained trees, the client will instruct on a pre-commencement site meeting, during which the Project Arboriculturist will visit the site to inspect and document the position and specifications of the protective measures.

If the protective measures and their positions do not comply with this Arboricultural Method Statement (Arbtech AMS 01) dated: 09 March 2026 and Tree Protection Plan (Arbtech TPP 01), the Project Arboriculturist shall inform the client and Fencing Contractor so adjustments can be made.

When the protective measures comply with this Arboricultural Method Statement (Arbtech AMS 01) and Tree Protection Plan (Arbtech TPP 01), the Project Arboriculturist will sign off the protective measures in writing to the Client for which a copy can be sent to the Fencing Contractor, Site Agent, and Local Authority Tree Officer.

If the protective measures become damaged or there is an accident or emergency involving trees, these areas are to be cordoned off immediately with high-visibility plastic mesh fencing. The site agent is to photograph and document the damage and inform the Project Arboriculturist immediately after the incident. All work within this area is to cease until the Project Arboriculturist has visited the site. Any damaged sections of protective measures shall be replaced within 48 hours of the initial incident.

The protected area is sacrosanct and will not be invaded by the storage of materials, the mixing of concrete or other products, the access of machinery, equipment, or pedestrians, or in any other way disturbed by construction activity.

The protective measures will remain in place until the completion of Stage 7 (see Table 5: Sequencing of works) thereafter, they will be carefully dismantled only with the agreement of the Project Arboriculturist and or the Local Authority Tree Officer.

The existing site boundary measures are to be retained for the duration of the development. If, for any reason, the existing boundary measures are not to be used, protective barrier fencing is to be installed along the line of the boundaries and is only to be removed upon the written permission of the Project Arboriculturist upon the completion of the development or immediately before the installation of the permanent boundary measures.

The proposed hard surfacing is to be installed immediately to act as ground protection. Where it is decided that this is not a viable option, these areas are to be covered by ground boarding as designed by the Project Engineer to cope with any likely loading.

No equipment, vehicles, or plant shall operate beyond the tree protection fencing. Booms, hoists, and rigs should be kept as far away from the canopies of retained trees as possible at all times. Where it is necessary to operate within 5m of a tree canopy, it will be done with the utmost caution and under the control of a banksman. Damage to trees will be considered a breach of this Tree

Protection Plan and Arboricultural Method Statement, which in turn could be a breach of planning permission.

Construction Exclusion Zone

A construction exclusion zone (CEZ), generally designated by the protective barrier fencing, is an area where there is to be no construction activity. Access to the area for construction personnel or machinery is strictly prohibited unless detailed in the tree protection plan, and there is no scope for materials or waste storage, welfare facilities, etc. There may be some construction activities planned for these areas (e.g. the installation of service trenches) these activities will be undertaken under the direct supervision of the Project Arboriculturalist.

Protective Barrier Fencing

Protective barrier fencing should be appropriate for the intensity and proximity of the development to protect trees where development activity is nearby.

The protective barrier fencing will be fixed with signage denoting the words “tree protection area” at 5.0m intervals. See Appendix 4: Tree Protection Notice

Option 1: The fence will comprise either a 2.4m wooden site hoarding or a 2.3m high scaffold framework, well-braced to resist impacts. The uprights will be spaced at a maximum of 3.0m intervals and driven into the ground by a minimum of 600mm. Standard anti-climb welded mesh panels will be securely fixed to each other with at least two scaffold clamps and to the scaffold framework with wire.

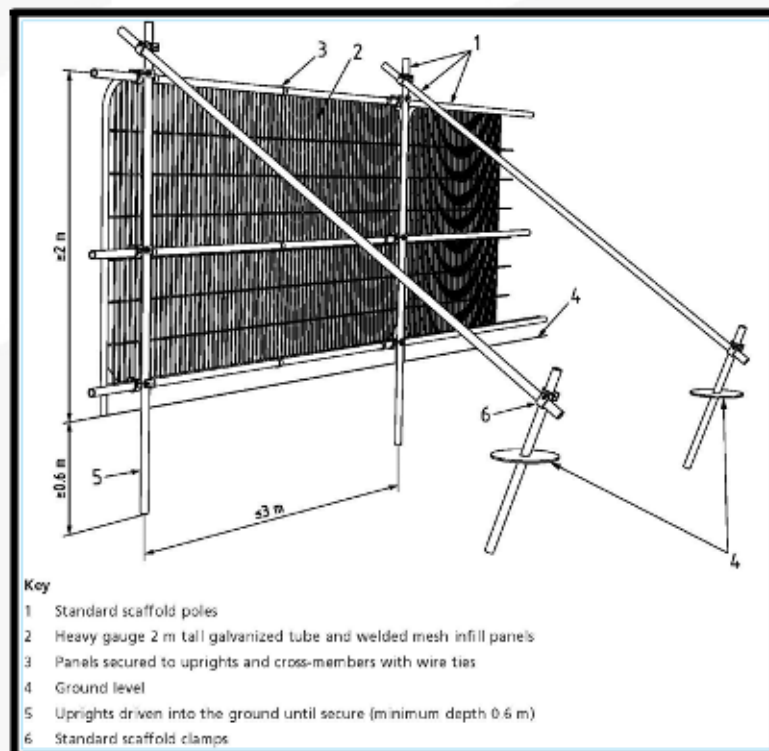


Figure 1: Example of protective barrier fencing constructed with a scaffold frame (BS5837)

Option 2: The fence will comprise 2m tall welded mesh panels on rubber or concrete feet. The panels are to be joined together using a minimum of two anti-tamper couplers installed so that they can only be removed from inside the fence. The panels will be supported on the inner side by stabiliser struts, which will be attached to a base plate and secured with ground pins.

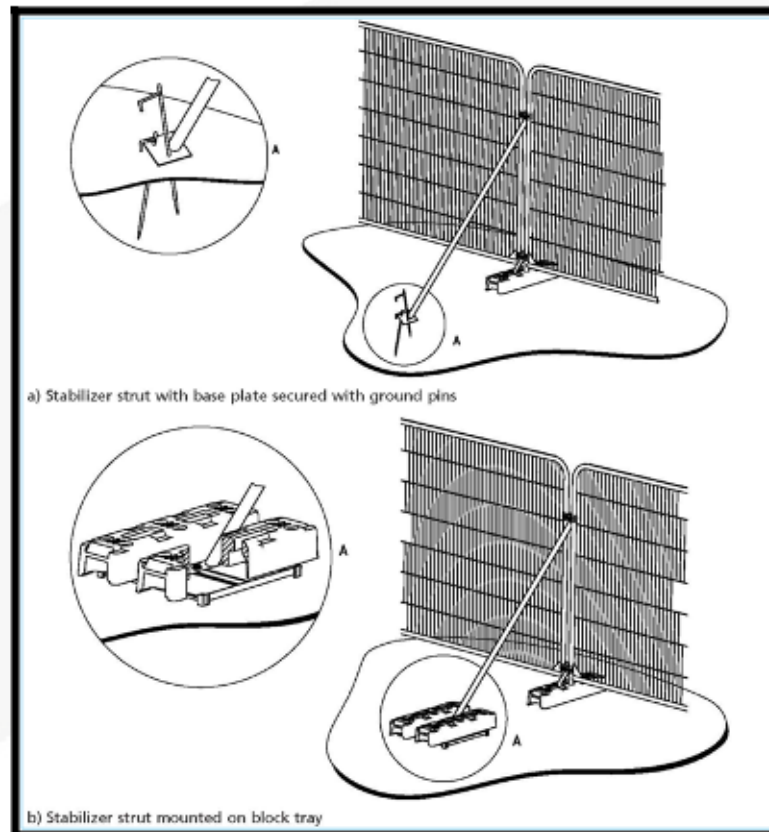


Figure 2: Example of protective barrier fencing with above-ground stabilising system (BS5837)

Demolition

Before the demolition of the existing site features, all tree works are to have been completed, tree protection measures are to be in place as per Tree Protection Plan document (Arbtech TPP 01) and have been signed-off, and a copy of the demolition method statement submitted and approved by the Project Arboriculturist to ensure that there is no conflict with this Arboricultural Method statement.

All demolition work within or immediately adjacent to RPAs or canopies of retained trees is to be undertaken under the direct supervision of the Project Arboriculturist.

Existing Underground Services

Existing services within the site should be retained wherever possible. Where existing services within RPAs of retained trees require upgrading, the utmost care must be taken to minimise disturbance. Trenchless techniques should be employed where feasible, and open excavations should be considered only where necessary.

Construction

Before the proposed development is constructed, a copy of the construction method statement will be submitted and approved by the Project Arboriculturist to ensure that it does not conflict with this Arboricultural Method Statement.

All excavations and construction work within or immediately adjacent to the RPAs or canopies of retained trees is to be undertaken under the direct supervision of the Project Arboriculturist.

Foundations Design

New foundations for buildings, structures, and hard surfacing situated within the RPAs of retained trees are to be designed in conjunction with arboricultural advice to accommodate the structure's likely loading. The foundations will be designed to limit the amount of excavation required within RPAs to retain significant roots, as identified during the site investigations.

The foundation design for the structure within the RPAs of retained trees T01, T02, T03 & T04 is to be designed to minimise the adverse impact upon trees and should pay particular attention to the existing ground levels and proposed finished floor level. Foundation design will be undertaken using site-specific information in conjunction with the Project Arboriculturist and Engineer.

The use of traditional strip foundations can result in excessive root loss and as such should be avoided.

Designs for foundations that would minimize the adverse impact upon trees should include particular attention to the existing levels, proposed finished levels and cross sectional details. Site specific and specialist advice should be sought from the project engineers and arboriculturist.

Root damage can be minimised by using:

- Piles with site investigation used to be determined their optimal location whilst avoiding damage to roots important for the stability of the tree, by means of hand tools or compressed air soil displacement, to a minimum depth of 600mm;
- Beams laid at or above ground level, and cantilevered as necessary to avoid tree roots identified by site investigation.
- Capping slab laid at or above ground level, and cantilevered as necessary to avoid tree roots identified by site investigation.

Where a slab for minor structures (e.g. shed base) is to be formed within the RPA, it should bear on the existing ground level, and should not exceed an area greater than 20% of the existing unsurfaced ground.

Where piling is to be installed near to trees, the smallest practical pile diameter should be used, as this reduces the possibility of striking major tree roots, and reduces the size of the rig required to sink the piles. If a piling mat is required, this should conform to the parameters for ground boarding. Use of the smallest practical piling rig is also important where piling within the

branch spread is proposed, as this can reduce the need for access facilitation pruning. The pile type should be selected bearing in mind the need to protect the soil and adjacent roots from the potentially toxic effects of uncured concrete, e.g. sleeved bored piles or screw piles.

Hard Surfacing

New hard surfacing situated within the RPAs of retained trees is to be designed in conjunction with advice from the Project Engineer and Arboriculturalist to ensure it can accommodate the likely loading required. The design will not require excavation; however, the removal of the turf layer or other surface vegetation may be acceptable if necessary. Ideally, the construction will be situated entirely above the existing ground level.

Appropriate options for the sub-base of hard surfacing situated within the RPAs of retained trees include multi-dimensional confinement systems (CellWeb™ or similar). Alternatively, piles, pads or elevated beams can be used to bridge over the RPAs or, following exploratory investigations to determine location, provide support within the RPAs while allowing retention of roots of 25mm or greater in diameter.

An exploratory investigation is to be undertaken manually under arboricultural supervision using hand tools (See Manual excavation).

Before the installation of the hard surfacing within the RPAs, vegetation may be removed using hand tools or sprayed with an approved non-residual herbicide such as 'Glyphosate'.

NOTE: *The use of a multi-dimensional confinement system will raise the finished level of the hard surfacing, which needs to be considered when designing foundations and setting the finished floor level of adjacent buildings.*

Multi-dimensional confinement system: If a multi-dimensional confinement system (such as CellWeb™ or similar) is to be used, it is to be laid entirely above the existing soil surface over a geotextile membrane and or a bi-axel geo-grid (such as Tensar TriAx). Prior to this, any small hollows on the surface may be filled with clean, sharp sand (not builders' sand) to a maximum depth of 150mm. The 'CellWeb' is to be backfilled by hand with a no-fines aggregate of 20mm – 30mm. The use of an excavator/machinery to fill the confinement system may be possible at the discretion of the Project Arboriculturist.

The area of 'CellWeb' shall be covered with permeable geotextile fabric, and the finished wearing course shall be laid on top. The wearing course shall be permeable to both water and air to comply with 'SUDS' regulations.

Edge supports of an appropriate size and strength will be set above ground level and will be secured with either haunching or steel pins driven into the ground. The outer edge of the supports may be banked up with clean topsoil.

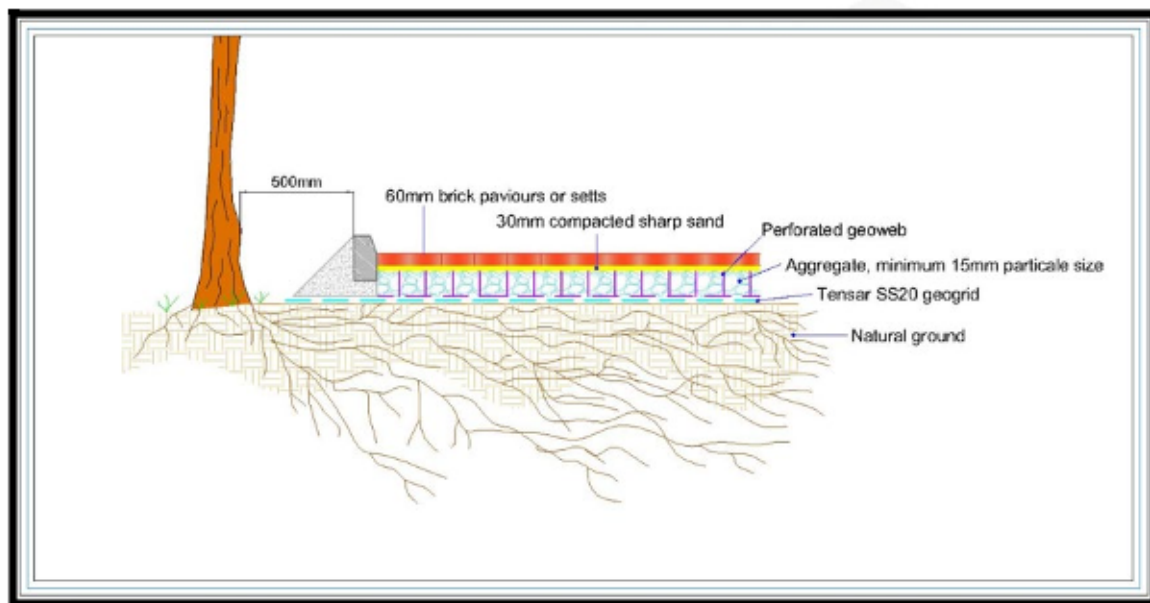


Figure 3: Example cross-section for multi-dimensional confinement system using kerb edging

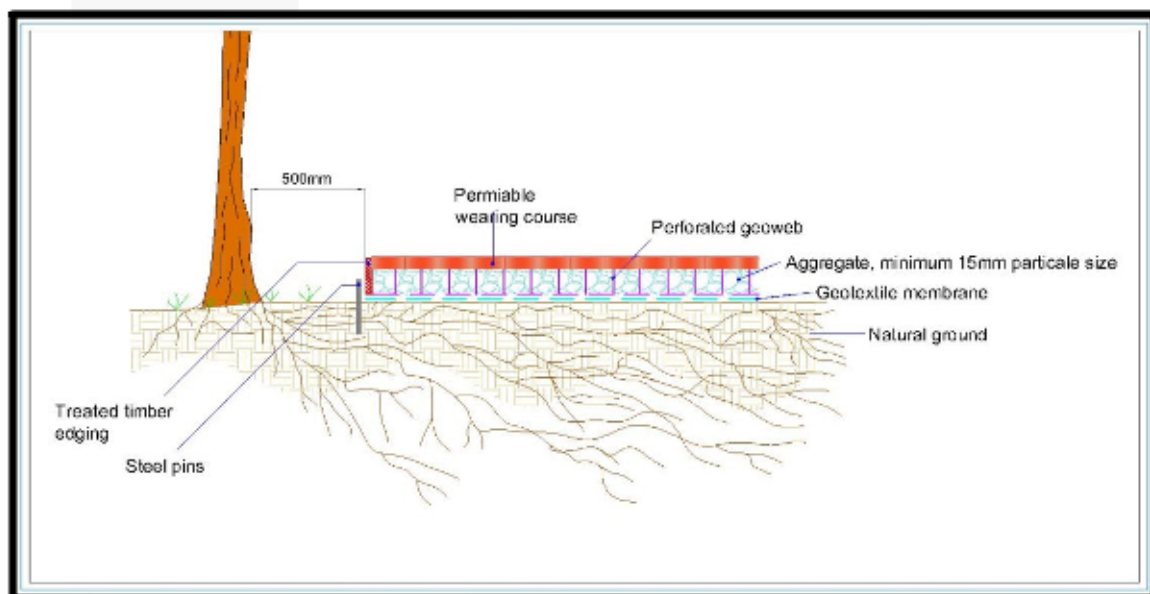


Figure 4: Example cross-section for multi-dimensional confinement system using timber edging

Based on the design of the hard surfacing, the proposed use is for a footpath (pedestrian access) and a road (vehicular access); Geosynthetics Limited recommends, within the product data sheet 'CellWeb® TRP weight capabilities', that a cell depth of 75mm (pedestrian use) to 200mm (vehicular access to include emergency access vehicles and HGVs) of their product CellWeb® TRP would possibly be suitable for the proposed use.

As a part of the design process and to allow Geosynthetics Limited to be able to calculate the exact correct depth of CellWeb® TRP please contact the Geosynthetics engineers.

Installation of a multi-dimensional confinement system

a) Prepare the surface

- Remove any surface rocks and debris;
- Create a level surface by filling in any hollows with clean, angular stone or sharp sand;
- Do not level off any high spots or compact the soil through rolling.

b) Layout Geotextile membrane

- Layout the permeable Geotextile membrane, overlaying the edges of the required area by 300mm;
- Overlap any joints by 300mm or more.

c) Layout multi-dimensional confinement system (MDC)

- Layout the collapsed MDC system on top of the Geotextile membrane;
- Place one steel pin into the centre cell at one end of the panel and secure it into the ground;
- Pull out the MDC to its full length (see manufacturer specifications), place a steel pin in the centre at the opposite end and secure it into the ground;
- Pull out the MDC to its full width (see manufacturer specifications), and secure each corner into the ground with steel pins;
- Create a panel of the correct size using the required number of steel pins (as per the manufacturer's specifications);
- Make sure all cells are fully extended (as per manufacturer specifications);
- Staple adjacent panels together (as per manufacturer specifications);
- If a curved shape is required, the panels are to be cut down to the required size and shape (once the MDC is pinned out. Do not curve or bend panels into place).

d) Infill with clean angular stone

- The infill material must be a clean (no fines) angular stone (as per manufacturer specifications)
- Do not use M.O.T type 1 or crushed stone with fines within or adjacent to RPAs;
- Infill the MDC cells with clean angular stone, working towards the tree using the infilled panels as a platform;
- The infill does not require compaction. Do not use a whacker plate, roller, or any other means of compaction.

e) Edge restraints

- All kerb edging will be situated on top of the MDC within RPAs; do not excavate within RPAs to install kerb edging;
- Where edging is required for light structures, a peg and treated timber board edging is normally acceptable;
- Other options include wooden sleepers, plastic, or metal edging;
- The outer edges of the supports may be banked up with clean topsoil and or mulch.

f) Wearing course

- Install a permeable geotextile membrane, overlapping any joints by 300mm before laying the wearing course;
- Surfaces can include block paving, asphalt, loose gravel, resin-bound gravel, concrete, etc.;
- Within RPAs, the wearing course shall be permeable to both water and air.

Road deck / Engineered system:

The design, material choices and methodology of a 'road deck' are to be undertaken to an engineering specification in conjunction with the advice of the Project Engineer and Arboriculturalist to ensure it accommodates the likely loading to which the 'road deck' will be subjected.

The following principles will be followed during the design process:

- The road deck is to be suspended entirely above the existing ground level to create a void between the underneath of the 'road deck' and the natural ground.
- Design of ground protection suitable to support and distribute the likely loading from the piling rig and associated construction machinery that will allow the hole to be removed so the pile may be installed through the ground protection (the use of a multi-dimensional confinement system may be suitable).
- Prevention of the void being inhabited by rodents or other small mammals.
- A watering system to either capture rainwater or direct it onto the soil below the 'road deck' or for the 'road deck' to be permeable. These systems must take into account that if the surface is to be subjected to de-icing salt, an impermeable barrier or filtration system will be required to prevent contamination of the rooting area.
- Pile locations are to be designed based on the advice of the Project Arboriculturist and, as identified during the site investigations, to allow for the retention of roots that are important to the tree's stability.
- Piles should be lined and the ground protected to prevent contamination of the rooting environment by concrete effluent runoff.

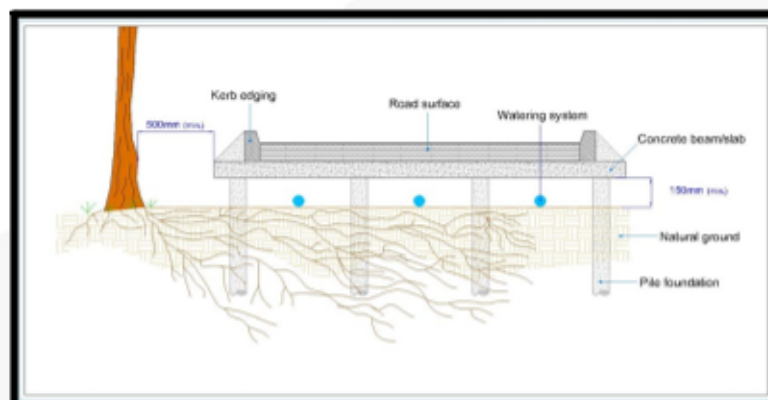


Figure 5: Example cross-section of a "road deck" system

Concrete use within RPAs

Before concrete is poured within or immediately adjacent to the RPAs of retained trees, the excavation is to be lined and sealed to prevent any leaching of the concrete into the soil and causing desiccation of retained roots by concrete runoff.

Manual excavation

Excavation within RPAs will be undertaken by hand under the direct supervision of the Project Arboriculturalist to the required depth of the foundations or to a minimum of 600mm deep of any excavation, whether for proposed foundations, hard surfacing, or underground services. The Project Arboriculturalist will determine the total depth of the manual excavation while on site.

The soil is to be loosened with a fork or pickaxe and then cleared with an air spade, air vac, or shovel. The Project Arboriculturalist will cleanly sever any roots found with either a hand saw or secateurs.

The Project Arboriculturalist shall cleanly sever any roots found with a diameter of less than 25mm. Roots of 25mm and above shall be excavated around without damaging them; the Project Arboriculturalist shall decide if it is feasible or necessary to retain the root; if not, it shall be severed.

The edge of the excavation closest to the trees will be covered with damp hessian to prevent soil collapse or contamination by concrete.

The soil beneath the depth may be sheet piled, regular piled, or excavated deeper. Machinery may be used for this, provided that it is situated outside of the RPAs of retained trees or has appropriate ground protection in place to move around and work upon.

Prohibition

- Mechanical digging or scraping is not permitted within a defined root protection area or areas cordoned off by protective barrier fencing.
- No access will be permitted within the protected areas;
- No materials, equipment or debris will be stored within any of the fenced areas or against the fencing;
- Fires are not permitted within 10m of any vegetation.
- Leaning objects against or attaching objects to a tree is not permitted.
- Machinery, plant, and vehicles are not permitted to be washed down within 10m of vegetation.
- Chemicals and materials are not to be transported, stored, used, or mixed within a root protection area or areas cordoned off by protective barrier fencing.
- Cement silos and mixing sites are to be situated within a bunded area to prevent spillage/leaking of chemicals harmful to trees. These areas are to be sited well clear of protected trees.
- Refuelling of plant or machinery is prohibited within 10m of the construction exclusion zones.
- An allowance must be made for sloping ground so that damaging materials such as concrete washings, mortar, or diesel oil cannot run towards trees.
- Where machinery is to be used within 5m of retained tree canopies, a banks man will be required at all times while setting up, moving, or operating within this distance of retained tree canopies.
- All caustic material and chemicals must be stored well clear of protected areas and preferably on lower ground if slopes are present or within a bonded area to prevent spills or leaks from entering the ground.

Site Management

The Site Manager will be responsible for briefing and inducting all personnel who will be working on any stage of this development, especially those who will be working within or adjacent to the canopies or RPAs of retained trees, and will make them aware of and provide a copy of this Arboricultural Method Statement (Arbtech AMS 01) and Tree Protection Plan (Arbtech TPP 01); this is to include but not exclusively the movement and or operation of plant, excavations, unloading deliveries, mixing and or pouring of cement and concrete.

The Site Manager will be responsible for the day-to-day running and protection of all retained trees and for liaising with the Project Arboriculturalist about any tree-related matters and before any works that may or will affect the RPAs or canopies of retained trees; this is to include but not exclusively the movement and or operation of plant, excavations, unloading deliveries, mixing, pouring and storage of all caustic materials that may cause harm to retained trees.

The Site Manager will document any incidents of damage to retained trees or tree protection measures. Then, the Site Manager will report these incidents to the Project Arboriculturalist immediately and ensure that works within this area cease until the Project Arboriculturalist has had an opportunity to inspect the damage and, where appropriate, agree on a mitigation plan with the Local Planning Authority Tree Officer.

The Site Manager may designate another person to take charge of the briefing and inducting process of new site personnel or visitors in his absence.

If the Site Manager is replaced or is absent from the site for more than three consecutive working days, the Project Arboriculturalist will be informed, and a new pre-start meeting will be held with the new or acting Site Manager.

It is the responsibility of the Site Manager to ensure that the planning conditions attached to any granted planning consent are adhered to at all times and that a monitoring regime and supervision of any works within or adjacent to the RPAs are adopted.

If pruning works other than those previously approved are required at any time, permission must be sought from the Local Authority Tree Officer. Once permission is granted, they are to be carried out by a suitably qualified person in accordance with BS3998:2010 Tree work—Recommendations.

Services

Detailed drawings of proposed underground services are not available at this time; hence it is not possible to identify any specific potential impacts associated with the scheme at this stage.

Existing services within the site will be retained wherever possible. Where existing services within RPAs require upgrading, the utmost care must be taken to minimise disturbance. Where feasible, trenchless techniques are to be employed, and only where necessary should open excavations be considered.

Where new services are to be introduced into the site, they will be located outside of RPAs so that they do not interfere with tree roots. If any excavations are required within the RPAs, all trenches are to be excavated by hand radially to the tree trunks under the direct supervision of the Project Arboriculturalist and carried out under NJUG guidelines.

The final positions of any proposed services will be verified and approved by the Project Arboriculturalist and Local Authority Tree Officer before implementation.

New Underground services

Trenching for the installation of underground services and drainage routes could sever any roots that may be present and, as such, adversely affect the tree's health. For this reason, particular care will be taken in routing and installation methods of all underground services. All underground services and drainage routes will be located so that no excavations are required within RPAs.

Where underground services have been impossible to prevent from passing through RPAs or within proximity to trees, these sections are to be installed in one of three ways and under the direct supervision of the Project Arboriculturalist and in accordance with the National Joint Utilities Group guidelines (NJUG 4).

Trenchless Techniques

There are three main types of trenchless techniques: guided and unguided boring and pipe replacement by lining or bursting. These techniques allow for the installation, maintenance, or renewal of underground services without disturbing soil in which roots are likely to grow. Starting and receiving pits for the boring machinery are to be located outside of the RPAs of any retained trees, with the bore depth maintained at a minimum depth of 600mm below the existing ground level. Techniques involving external lubrication of the equipment shall use only water, as other lubricants (e.g., oil, bentonite, etc.) could contaminate the soil.

Broken Trench – Hand Dug

This technique combines both trenchless techniques and manual excavation, where excavation is unavoidable. Excavations will be limited to where there is clear access around and below the roots. All trenches shall be excavated by hand with the same precautions taken as for manual excavation. The open section of the trench will only be large enough to allow access for linking to the next section.

Manual Excavation

Excavation within RPAs will be undertaken by hand under the direct supervision of the Project Arboriculturalist to the required depth of the foundations or to a minimum of 600mm deep of any excavation, whether for proposed foundations, hard surfacing, or underground services. The Project Arboriculturalist will determine the total depth of the manual excavation while on site.

The soil is to be loosened with a fork or pickaxe and then cleared with an air spade, air vac, or shovel. The Project Arboriculturalist will cleanly sever any roots found with either a hand saw or secateurs.

The Project Arboriculturalist shall cleanly sever any roots found with a diameter of less than 25mm. Roots of 25mm and above shall be excavated around without damaging them; the Project Arboriculturalist shall decide if it is feasible or necessary to retain the root; if not, it shall be severed.

The edge of the excavation closest to the trees will be covered with damp hessian to prevent soil collapse or contamination by concrete.

The soil beneath the depth may be sheet piled, regular piled, or excavated deeper. Machinery may be used for this, provided that it is situated outside of the RPAs of retained trees or has appropriate ground protection in place to move around and work upon.

Landscaping

Landscaping, such as planting, turfing, fencing, etc., around retained trees may only be carried out once all tree protection measures have been removed.

All excavations within the RPAs of retained trees shall be undertaken by hand and without reducing current ground levels unless it is agreed in writing with the Local Planning Authority. At no time is the use of a rotavator permitted within the RPAs of retained trees.

Any tree roots discovered will be left in situ and shall not be cut or otherwise damaged. Where possible, the soil structure within the RPA shall be preserved.

No works will be carried out within the RPAs of any trees if the soil moisture is at a level where soil compaction may be likely. Should the soil become compacted or have a poor structure that would hinder the development of the existing trees and plants or any new plantings, the arboriculturalist will be consulted about soil decompaction techniques.

Monitoring and Supervision

Where trees have been identified within this Arboricultural Method Statement (Arbtech AMS 01) and Tree Protection Plan (Arbtech TPP 01) for retention, there will be an auditable system of arboricultural monitoring. This is to extend to arboricultural supervision whenever demolition or construction activity is to take place within or adjacent to any canopy or RPA.

The development's tree protection measures are to be monitored, and all demolition and construction works are to be undertaken within or adjacent to the RPAs of retained trees. The Project Arboriculturist will supervise the work and record and report observations to the Council at appropriate intervals.

Pre-commencement site meeting

Before the commencement of any works or machinery and materials arriving on site, a pre-commencement site meeting involving the Project Arboriculturalist, Landowner or Agent, Site Manager, contractors and Engineer (as appropriate) and the relevant Local Planning Authority Officers will be held to ensure that all aspects of the Arboricultural Method Statement and Tree Protection Plan are understood and for all parties to swap contact details. See Appendix 5: Contact Details.

Monitoring and supervision schedule

The initial monitoring visit will check that the tree protection measures are in the correct location and as specified within the approved Arboricultural Method Statement, and if so, to sign off on their installation.

Thereafter, monitoring visits are to take place at regular intervals to ensure that tree protection measures are in place and are functioning as designed or whenever necessary to undertake works to be carried out under arboricultural supervision. The frequency of the monitoring visits is to be agreed upon with the Local Authority Tree Officer at the pre-commencement site meeting.

A record of all arboricultural monitoring and supervision visits will be kept, and any faults will be logged; this will then be copied to the Site Agent, Developer, and Local Planning Authority in a digital format.

If areas must be redesigned during the development so that they would require changes to the approved Arboricultural Method Statement or Tree Protection Plan and so affect retained trees, the Project Arboriculturalist and Local Authority Tree Officer will be invited to attend a site meeting with all relevant parties. Before any changes are implemented, they must have been approved in writing by the Local Authority Tree Officer.

Supervision

The Project Arboriculturist will be required to attend the site to directly supervise all demolition and construction works that are to be undertaken within or adjacent to the RPAs of all retained trees and will be advised a minimum of 72 hours before the commencement of any works that require his attendance; these will include:

1. Pre-commencement site meeting.
2. Location of protective measures.
3. Supervised excavations for site investigations to inform foundation design within the RPAs of trees T01, T02, T03 & T06.
4. Installation of 'No Dig' sub-base within the RPAs of trees T01, T02, T03, T04 & T06.
5. Any demolition and or excavations within or adjacent to RPAs, including foundations, hard surfacing or underground services (a non-exhaustive list).
6. Arboricultural sign off and removal of protective measures.

Completion meeting

Once all construction works have been completed and all materials and machinery have been removed from the site, the Project Arboriculturalist shall be informed and will invite the Local Authority Tree Officer to meet on-site to discuss the process, final remedial works that may be required and sign the development off so that the protective measures may be removed.

Appendices

The following documents were released to the Client as appendices to this report:

- Appendix 1: Tree Schedule
- Appendix 2: Arboricultural Impact Assessment
- Appendix 3: Tree Protection Plan
- Appendix 4: Tree Protection Notice
- Appendix 5: Contact Details

If you require clarification of the information contained herein, please do not hesitate to contact us via 01244 661170.

Yours Sincerely,

Jon Hartley BSc(Hons) MArborA
Principal Arboricultural Consultant
07860951396
jh@arbtech.co.uk

A large, light gray decorative graphic in the background, consisting of two large, stylized chevrons pointing upwards, one above and one below the section header.


Appendix 1: Tree Schedule

Client	Premier modular
Project	The Stirling Centre
Date	28Feb26
Surveyor	Andrew Davies
Weather Conditions	Dry & clear




Ref No.	Common Name Scientific Name	Age Class	Height	Stem Diameter	Crown Spread	Crown Clearance	Condition		RPA		Comments	Remaining Life Expectancy	Category / Sub-category
							Structural	Physiological	Area (m ²)	Radius (m)			
T01	Sorbus aria Common whitebeam	Mature	11	420	N - 4.5 E - 4.5 S - 4.5 W - 4	2	Fair	Good	79	5.00	Growing alongside boundary fenceline stem is approx. 100mm from fence. Historic bark wounds to lower stem which have almost fully occluded.	20+ Years	B1
T02	Fraxinus excelsior Common ash	Early Mature	16	300	N - 2 E - 3.5 S - 3.5 W - 4	4	Fair	Fair	41	3.60	Minor deadwood within crown consistent with age and species. Stem bifurcates at 3.5m	20+ Years	B1
T03	Fraxinus excelsior Common ash	Early Mature	16	360	N - 3.5 E - 4 S - 2.5 W - 3.5	2	Fair	Fair	58	4.30	Minor deadwood within crown consistent with age and species.	20+ Years	B1
T04	Fraxinus excelsior Common ash	Early Mature	16	380	N - 5 E - 5 S - 4 W - 3.5	2	Fair	Fair	66	4.60	Minor deadwood within crown consistent with age and species. Exposed root system	20+ Years	B1
T05	Sorbus aria Common whitebeam	Mature	14	440	N - 3.5 E - 3.5 S - 4.5 W - 3	2	Fair	Good	88	5.30	Asymmetric crown heavily reduced away from telecoms lines. Crown bias towards car park area in front of building. Large flush cut pruning wound at 2m on NW side of stem around union.	20+ Years	B1
T06	Sorbus aria Common whitebeam	Mature	15	380	N - 3 E - 3.5 S - 3 W - 3	2	Fair	Good	66	4.60	Asymmetric crown heavily reduced away from telecoms lines. Crown bias towards open space in front of building.	20+ Years	B1
T07	Acer pseudoplatanus Sycamore	Early Mature	16	460	N - 4 E - 4 S - 4 W - 5	2	Good	Good	95	5.50	3rd party tree RPA close to site main entrance driveway.	20+ Years	B1
T08	Acer pseudoplatanus Sycamore	Early Mature	16	640	N - 5 E - 6 S - 5 W - 6	2	Good	Good	186	7.70	3rd party tree RPA close to site main entrance driveway.	20+ Years	B1


T09	Sorbus aucuparia Rowan	Early Mature	7	280	N - 3 E - 2.5 S - 3 W - 2.5	2	Good	Good	36	3.40	Growing close to fenceline stem is almost touching brick pillar. Stem bifurcates at 1.8m	20+ Years	B1
-----	---------------------------	--------------	---	-----	--------------------------------------	---	------	------	----	------	--	-----------	----

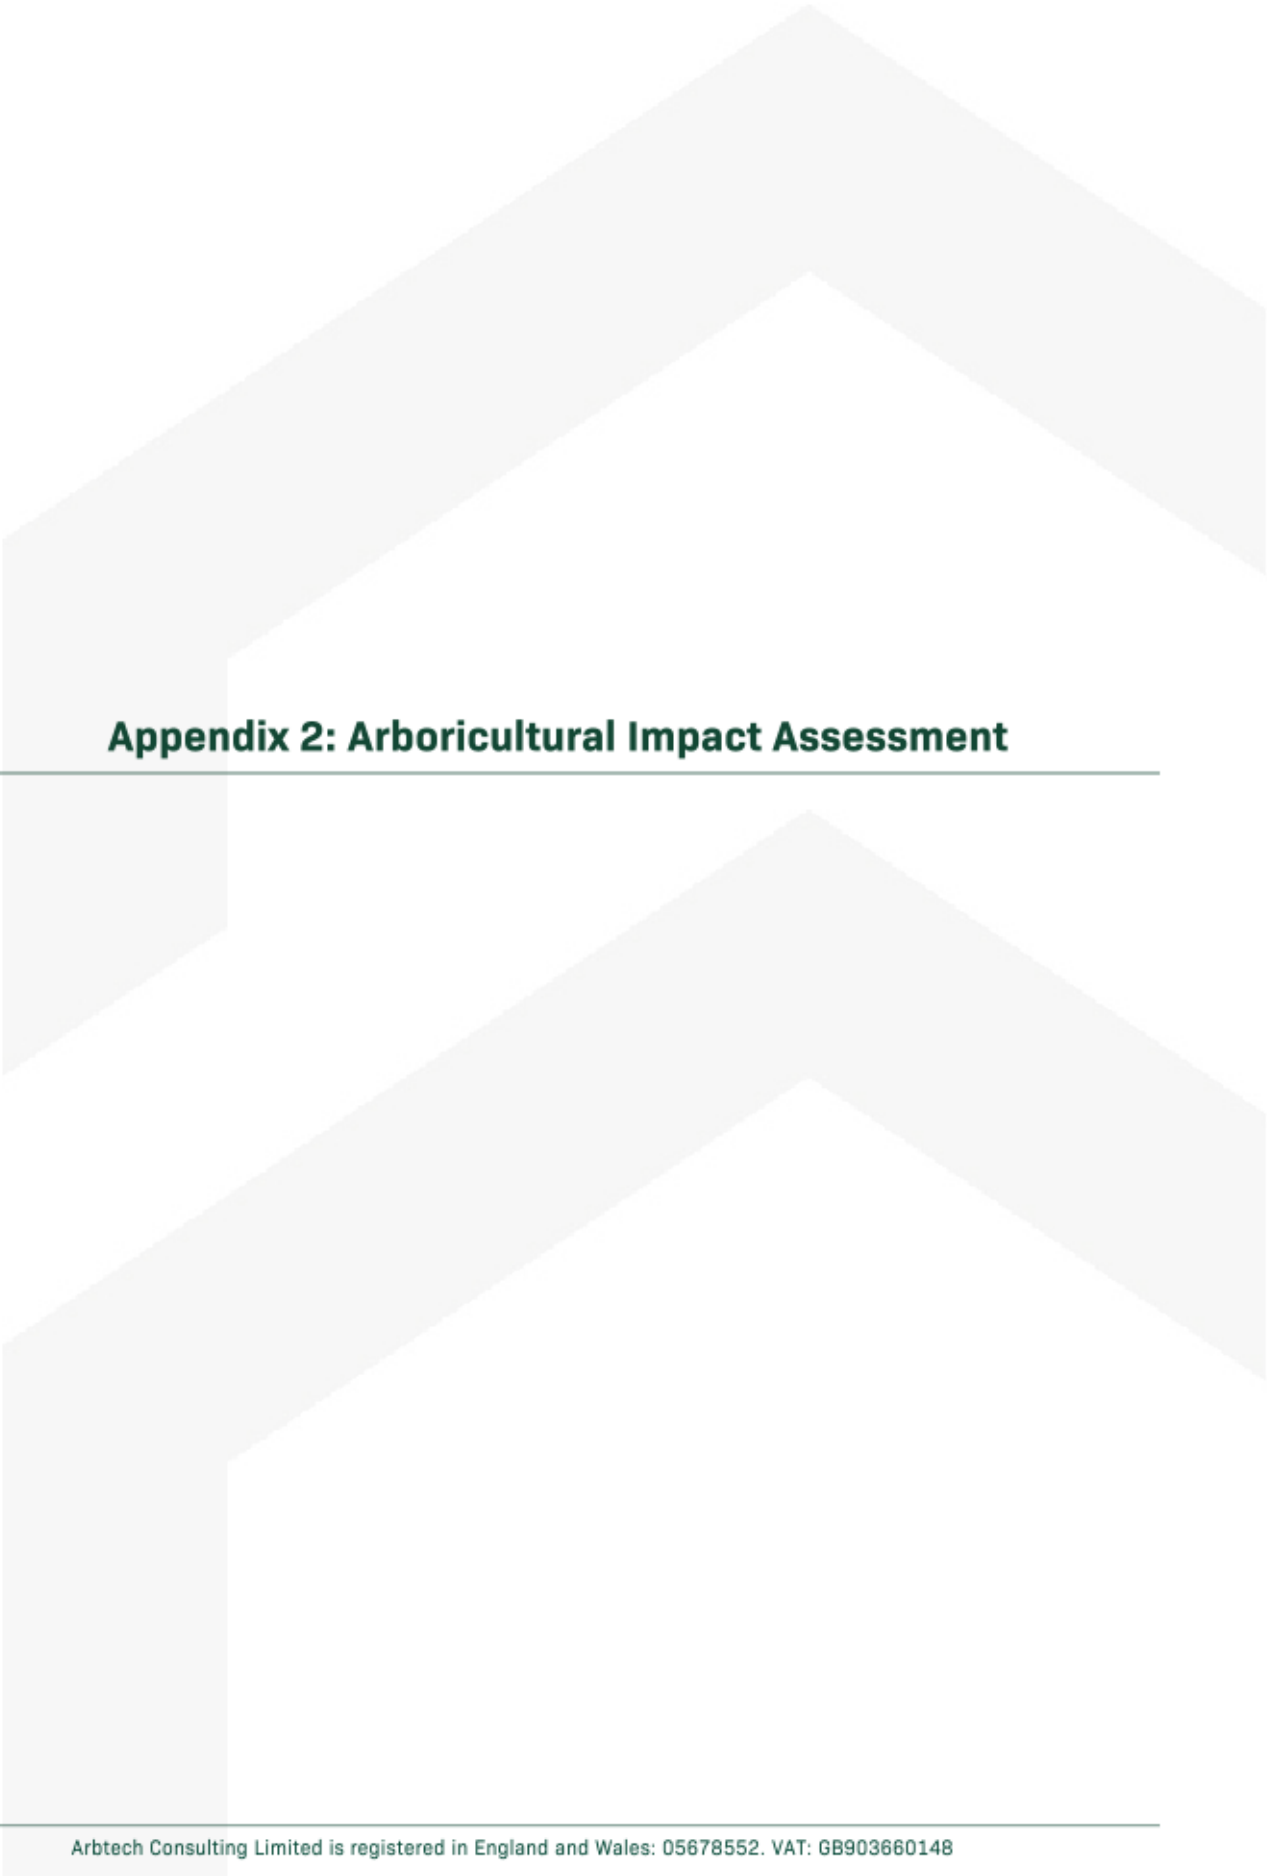

Appendix 2: Arboricultural Impact Assessment

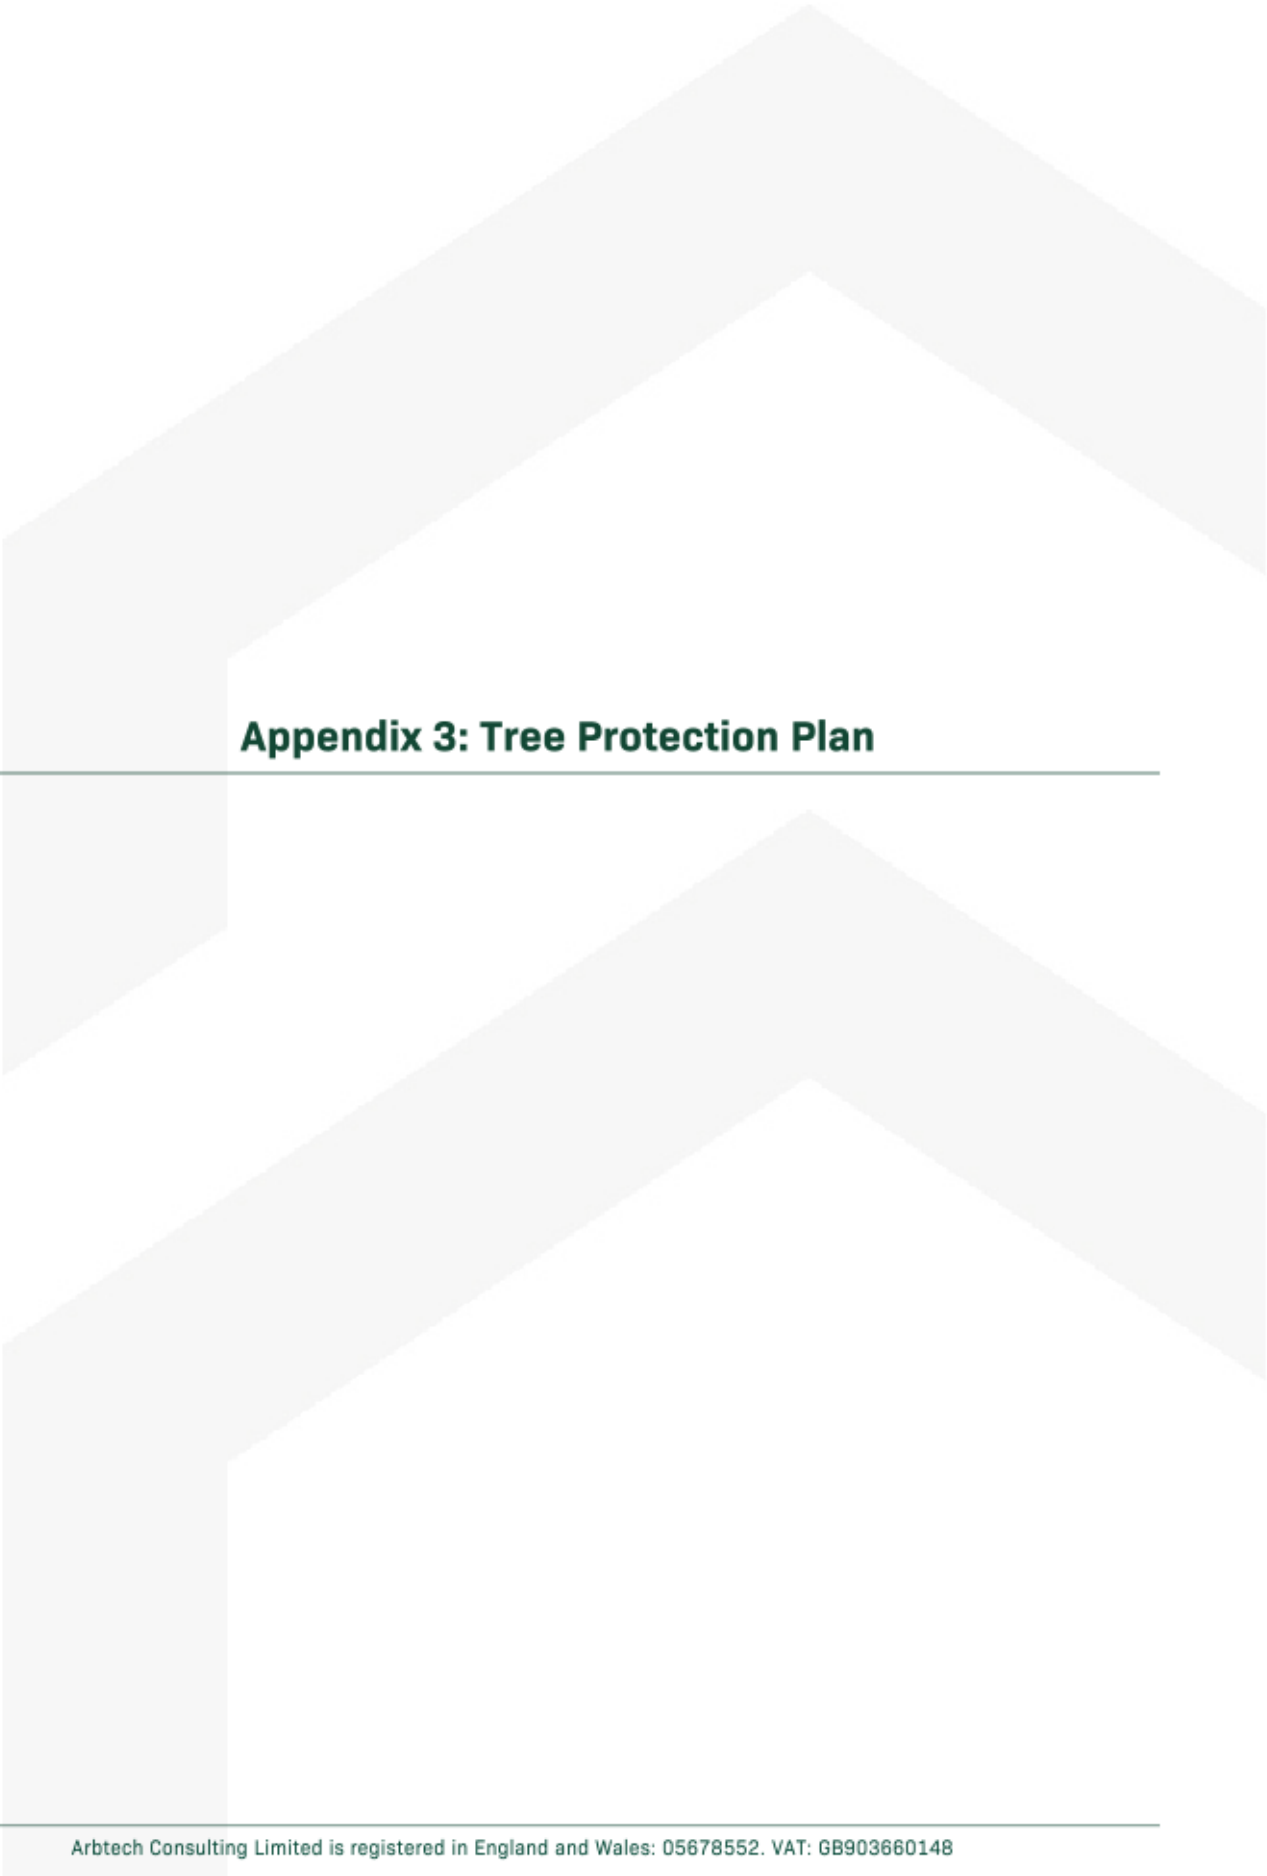

Appendix 3: Tree Protection Plan



Appendix 4: Tree Protection Notice

Tree Protection Area

KEEP OUT

Do not move this fence

(TOWN & COUNTRY PLANNING ACT 1990)

**TREES ENCLOSED BY THIS FENCE ARE PROTECTED BY PLANNING CONDITIONS AND/OR
ARE THE SUBJECT OF A TREE PRESERVATION ORDER.**

**CONTRAVENTION OF A TREE PRESERVATION ORDER MAY LEAD TO CRIMINAL
PROSECUTION**

**ANY INCURSION INTO THE PROTECTED AREA MUST BE WITH THE WRITTEN PERMISSION
OF THE LOCAL PLANNING AUTHORITY**



Arbtech Consulting Limited.
Unit 3, Well House Barn, Chester Road, Chester, CH4 0DH
<https://arbtech.co.uk> - 01244 661170



Appendix 5: Contact Details

Name	Position	Company	Contact
	Client		
	Agent / Project Manager		
	Tree Officer		
	Project Arboriculturist	Arbtech Consulting Ltd.	01244 661170 https://arbtech.co.uk
	Site Manager		
	Main contractor		

Document Production Record

Document number	Editor	Signature	Position	Issue number	Date
Arbtech AMS 01	Jon Hartley		Principal Arboricultural Consultant	01	09/03/26

Report Limitations

Arbtech Consulting Ltd has prepared this report for the sole use of the above-named Client/Agent in accordance with our terms of business, under which our services were performed. No other warranty, expressed or implied, is made as to the professional advice included in this report or any other services provided by us. This report may not be relied upon by any other party without the prior and express written agreement of Arbtech Consulting Ltd. The assessments made assume that the sites and facilities will continue to be used for their current purpose without significant change. The conclusions and recommendations contained in this report are based upon information provided by others and upon the assumption that all relevant information has been provided by those parties from whom it has been requested. Information obtained from third parties has not been independently verified by Arbtech Consulting Ltd.

Copyright

© This Report is the copyright of Arbtech Consulting Ltd. Any unauthorised reproduction or usage by any person other than the addressee is strictly prohibited.
