



GAS MEMBRANE VALIDATION


Site Name: Belle Vue Stadium	Project Number: 12-123
Company Name: Countryside	Date: 29-03-2022
Project Manager: O. Jackson	E3P Engineer: R. Webster
PM Qualifications : BSc FGS AMIEnvSc	Engineer Qualifications: Verification of Gas Protection Systems Dec 2017
Ground Gas Risk Assessment: Amber 1	
<p>Overview: The membrane comprised a Visqueen low permeability gas membrane (Yellow) resistant to radon, carbon dioxide and low levels of methane. E3P can confirm there were no holes or rips at the time of inspection. Upon being laid the membrane is to be covered with a Celotex (closed Cell) floor insulation material which is considered to provide a high degree of protection.</p> <p>All external joints were inspected and E3P can confirm that the membrane was overlapped and double taped to external and internal gas resistant DPM. The membrane was taped to the gas resistant DPM using a double-sided jointing tape.</p> <p>Each unit has a service duct located to the front and outer edge of the property. E3P inspected each one and can confirm that the top-hats have been adequately sealed against the membrane.</p> <p>Based on the information provided within this report, the site inspections and validation checklists, E3P can confirm that Plots 4-5 have been installed with gas protection measures in accordance with Amber 1 to an acceptable level of workmanship.</p>	
Membrane Specification: Visqueen Gas Membrane (Yellow)	
	



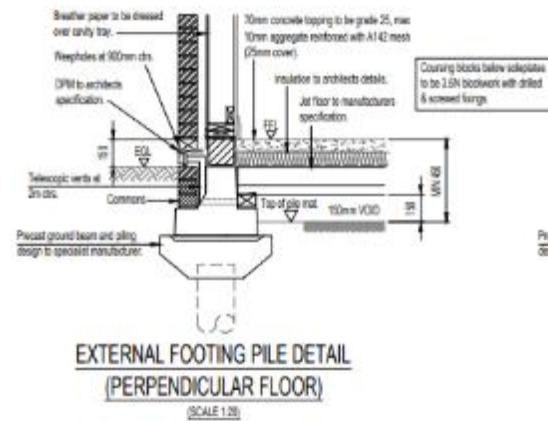


Plot - 4


General Condition of Membrane-Good Condition

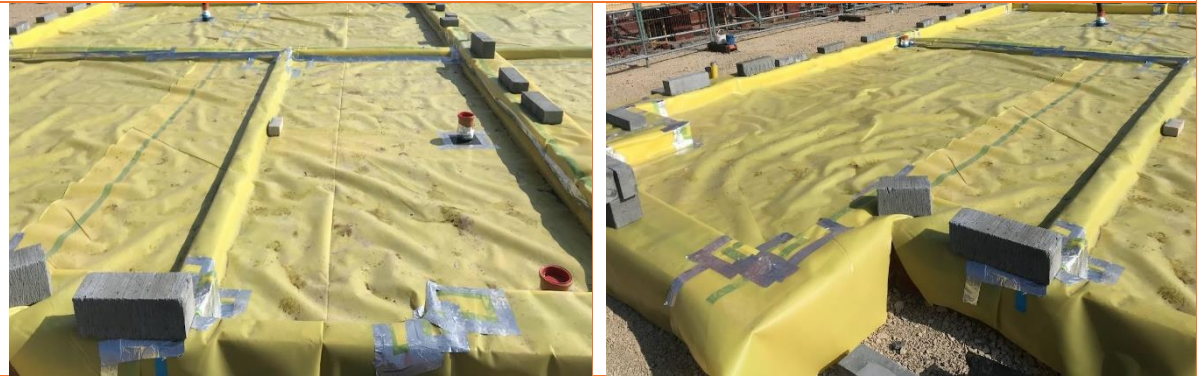

Verification of Joints and Seals-Overlapped and sealed correctly

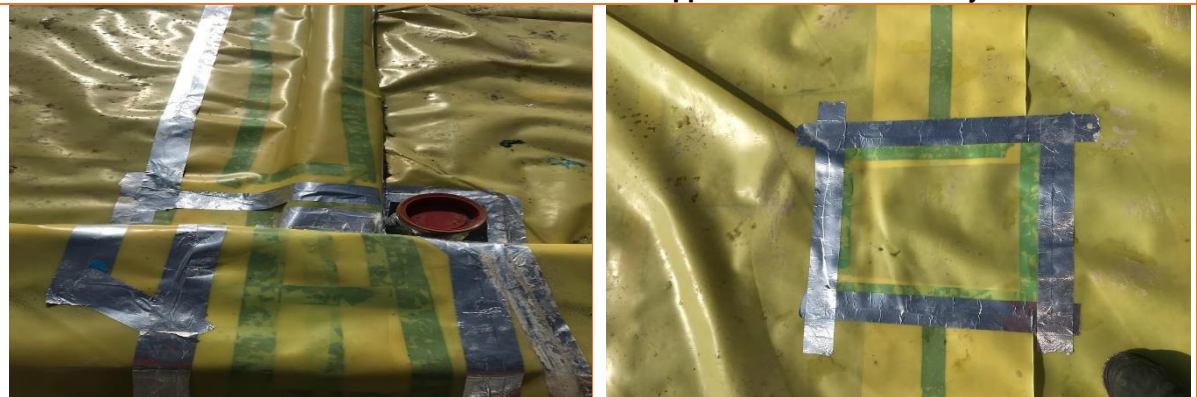

Verification of Service Penetrations-Good Condition

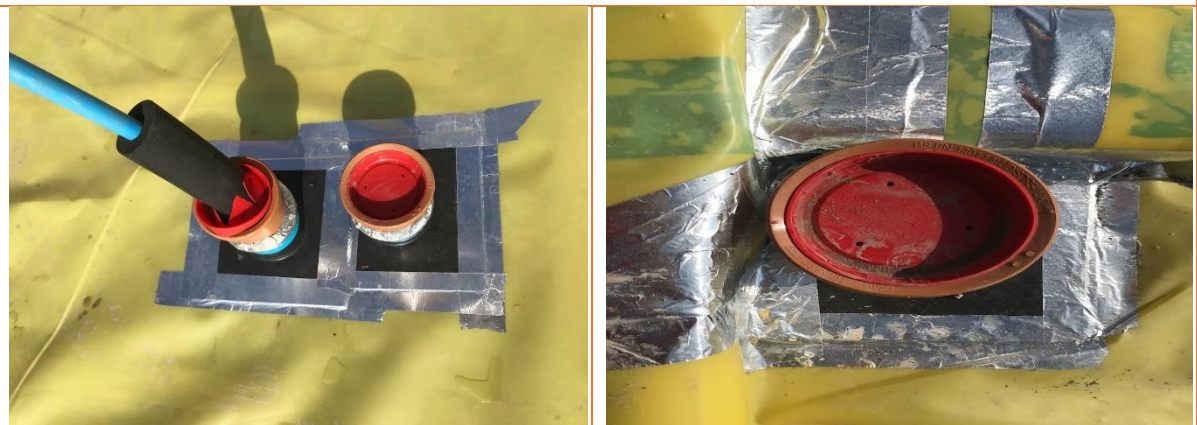


Verification of Ventilation-Good Condition



Plot - 5



General Condition of Membrane-Good Condition

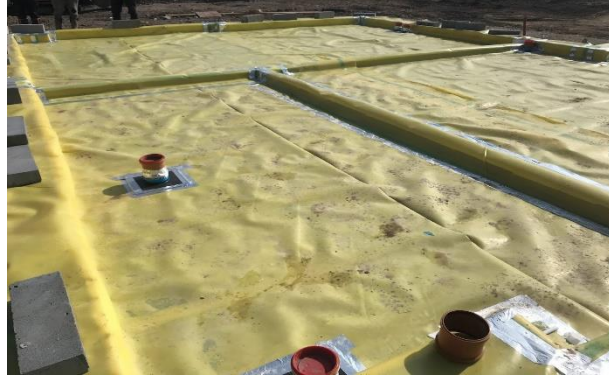

Verification of Joints and Seals-Overlapped and sealed correctly



Verification of Service Penetrations-Good Condition

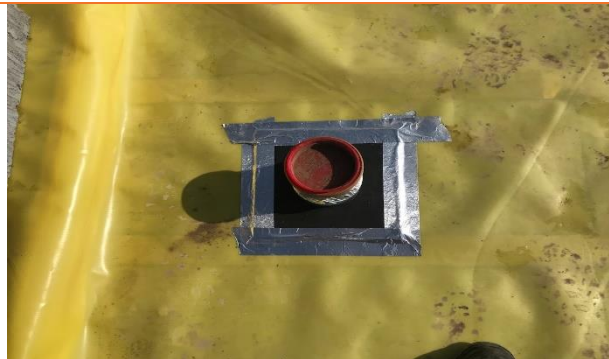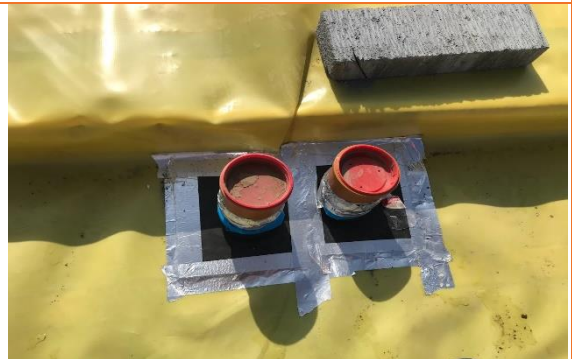

Verification of Ventilation-Good Condition




Gas Protection Validation Site Record

Inspection date/time:	29/3	Inspected by:	R. Webster	Photographed:	✓
Type of development:	Belle Vue	Plot number:	4	Developer:	

Notes/recommendations	Comments
Membrane Type	Visqueen yellow
Extent of Coverage	fully extend
Underside of Membrane	
Slab / membrane condition (is membrane clear of debris or insulation)	Good
Type of joints	☒ Tape Joint ☐ Welded Joint ☐ Other (please state)
Service entries – Jubilee clips, Top hats installed correctly	yes
External Wall Air bricks Present?	yes
Corners inspected?	yes
Membrane joints inspected has Double –sided butyl tape been used?	yes
Folds in membrane inspected?	yes
Has the membrane been installed as per the design detail drawing?	yes

This Plot has **PASSED/FAILED*** inspection. (Any proposed remedial works will be noted in the "Remarks" column on this form). An additional inspection will be required for this Plot.

Inspection by: *R. Webster* Signed: [REDACTED]




Gas Protection Validation Site Record

Inspection date/time:	29/3	Inspected by:	R Webster	Photographed:	✓/x ✓
Type of development:	Belle Vue	Plot number:	5	Developer:	
Notes/recommendations					
Membrane Type	Comments				
Extent of Coverage	Visqueen yellow				
Underside of Membrane	fully exposed				
Slab / membrane condition (is membrane clear of debris or insulation)	Good				
Type of joints	☒ Tape Joint ☐ Welded Joint ☐ Other (please state)				
Service entries – Jubilee clips, Top hats installed correctly	yes				
External Wall Air bricks Present?	yes				
Corners inspected?	yes				
Membrane joints inspected has Double –sided butyl tape been used?	yes				
Folds in membrane inspected?	yes				
Has the membrane been installed as per the design detail drawing?	yes				

Plot has PASSED/FAILED* inspection. (Any proposed remedial works will be noted in the "Remarks" column on this form). An additional inspection visit is required for this Plot.

Inspection by: R Webster Signed: [Redacted Signature]



