

GAS MEMBRANE VALIDATION

Site Name: Belle Vue Stadium	Project Number: 12-123
Company Name: Countryside	Date: 15-07-2022
Project Manager: O. Jackson	E3P Engineer: P. Lavelle
PM Qualifications : BSc FGS AMIEnvSc	Engineer Qualifications: Verification of Gas Protection Systems Dec 17

Overview:

The membrane comprised a Visqueen gas membrane (yellow) resistant to radon, carbon dioxide and low levels of methane. E3P can confirm there were no holes or rips at the time of inspection. Upon being laid the membrane is to be covered with a Celotex (closed Cell) floor insulation material which is considered to provide a high degree of protection.

All external joints were inspected and E3P can confirm that the membrane was overlapped and double taped to external and internal gas resistant DPM. The membrane was taped to the gas resistant DPM using a double-sided jointing tape.

Each unit has a service duct located to the front and outer edge of the property. E3P inspected each one and can confirm that the top-hats have been adequately sealed against the membrane.

Based on the information provided within this report, the site inspections and validation checklists, E3P can confirm that **Plots 141-142** have been installed with gas protection measures in accordance with Amber 1 to an acceptable level of workmanship.





Plot – 141


General Condition of Membrane-Good Condition



Verification of Joints and Seals-Overlapped and sealed correctly



Verification of Service Penetrations-Good Condition

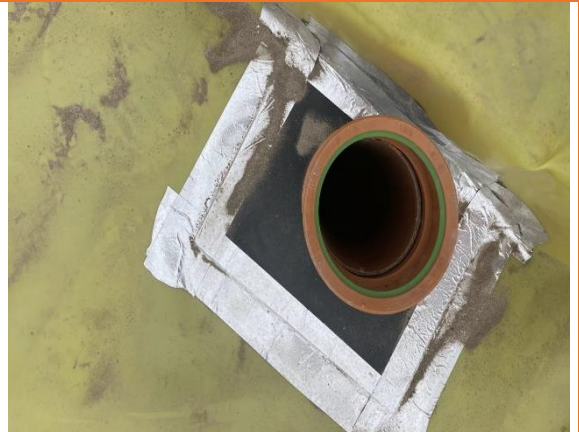

Verification of Ventilation-Good Condition




Plot – 142


General Condition of Membrane-Good Condition



Verification of Joints and Seals-Overlapped and sealed correctly

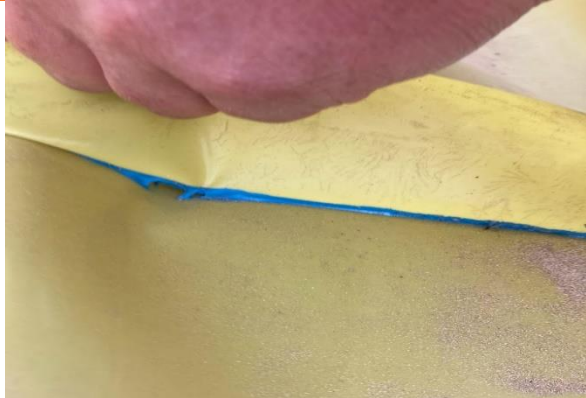

Verification of Service Penetrations-Good Condition

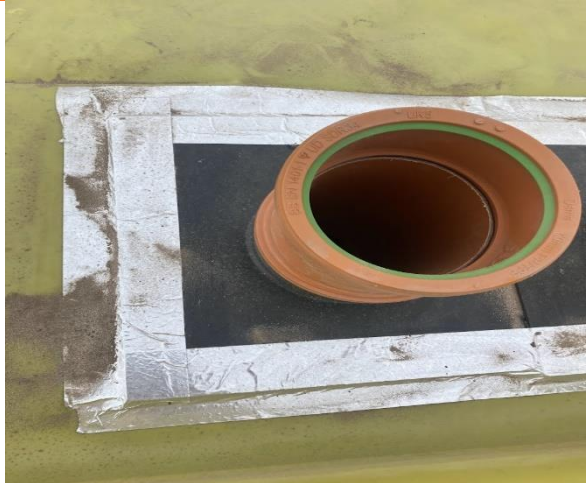

Verification of Ventilation-Good Condition





Gas Protection Validation Site Record

Inspection date/time:	15/7/22	Inspected by:	[Redacted]	Photographed:	☒
Type of development:	Residential	Plot number:	141	Developer:	

Notes/recommendations	Comments
Membrane Type	Yellow VIS guleon
Extent of Coverage	Full coverage
Underside of Membrane	Clear
Slab / membrane condition (is membrane clear of debris or insulation)	Clear
Type of joints	☒ Tape Joint ☐ Welded Joint ☐ Other (please state)
Service entries - Jubilee clips, Top hats installed correctly	yes
External Wall Air bricks Present?	yes
Corners inspected?	yes
Membrane joints inspected has Double -sided butyl tape been used?	yes
Folds in membrane inspected?	yes
Has the membrane been installed as per the design detail drawing?	yes

This Plot has PASSED/FAILED* inspection. (Any proposed remedial work should be noted in the "Remarks" column on this form). An additional inspection visit IS/IS NOT* required for t [Redacted]
Inspection by: [Redacted] Signed: [Redacted]

Gas Protection Validation Site Record

Inspection date/time:	15/7/22	Inspected by:	[Redacted]	Photographed:	☒ x
Type of development:	Residential	Plot number:	142	Developer:	

Notes/recommendations

Comments

Membrane Type	hollow Visqueen Full coverage Clear Clear
Extent of Coverage	
Underside of Membrane	
Slab / membrane condition (is membrane clear of debris or insulation)	
Type of joints	
Service entries – Jubilee clips, Top hats installed correctly	☒ Tape Joint ☐ Welded Joint ☐ Other (please state)
External Wall Air bricks Present?	yes
Corners inspected?	yes
Membrane joints inspected has Double –sided butyl tape been used?	yes
Folds in membrane inspected?	yes
Has the membrane been installed as per the design detail drawing?	yes

This Plot has PA [Redacted]	Any proposed rer [Redacted]	column on this form). An additional inspection visit IS/IS
NOT* required for [Redacted]		
Inspection by: [Redacted]	Signed: [Redacted]	
