




Our Town Hall Project : Programme G19.2 (ACCEPTED PROGRAMME)


OTH-LLC-TH-XX-RPT-W-0230

Status: S2
Rev: P01
Document Type: Report
Date: 4/11/2021


Issue History:

Revision Nr	Details	Date	Created By	Check by
P01	Document Created	4/11	IF	

Our Town Hall Project : Programme G19.2 (ACCEPTED PROGRAMME)

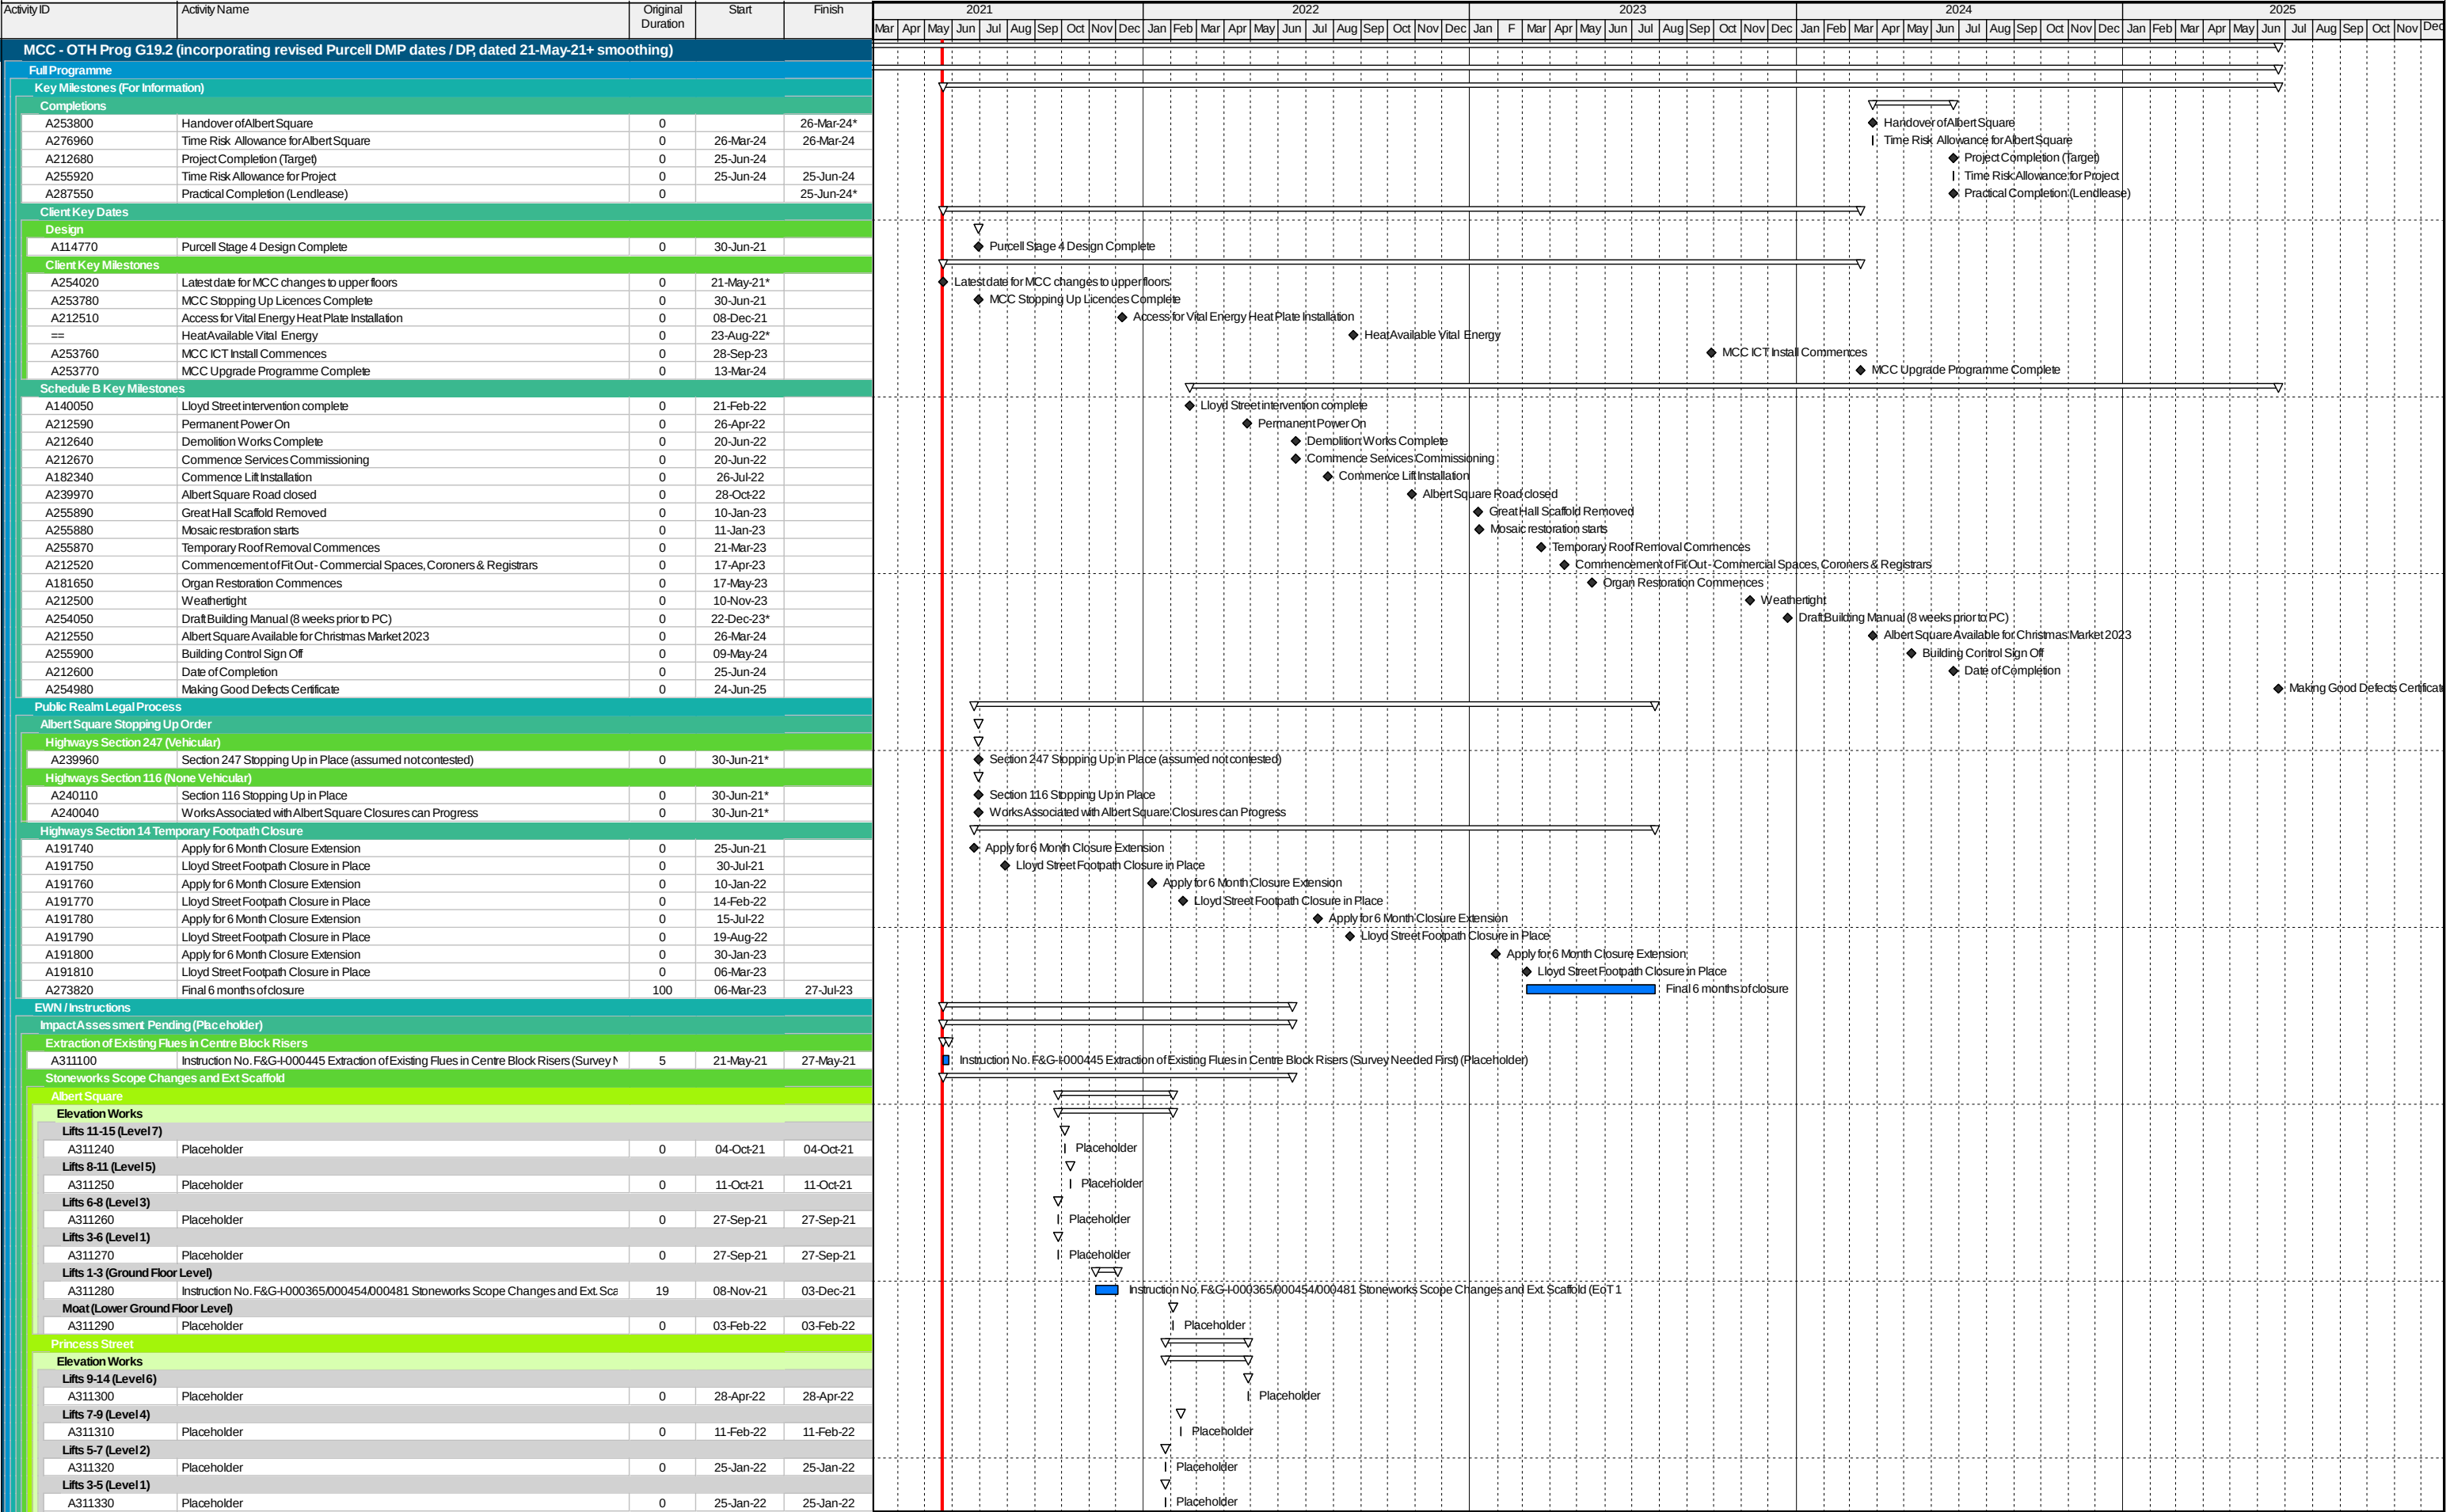

Our Town Hall Project : Programme G19.2 (ACCEPTED PROGRAMME)

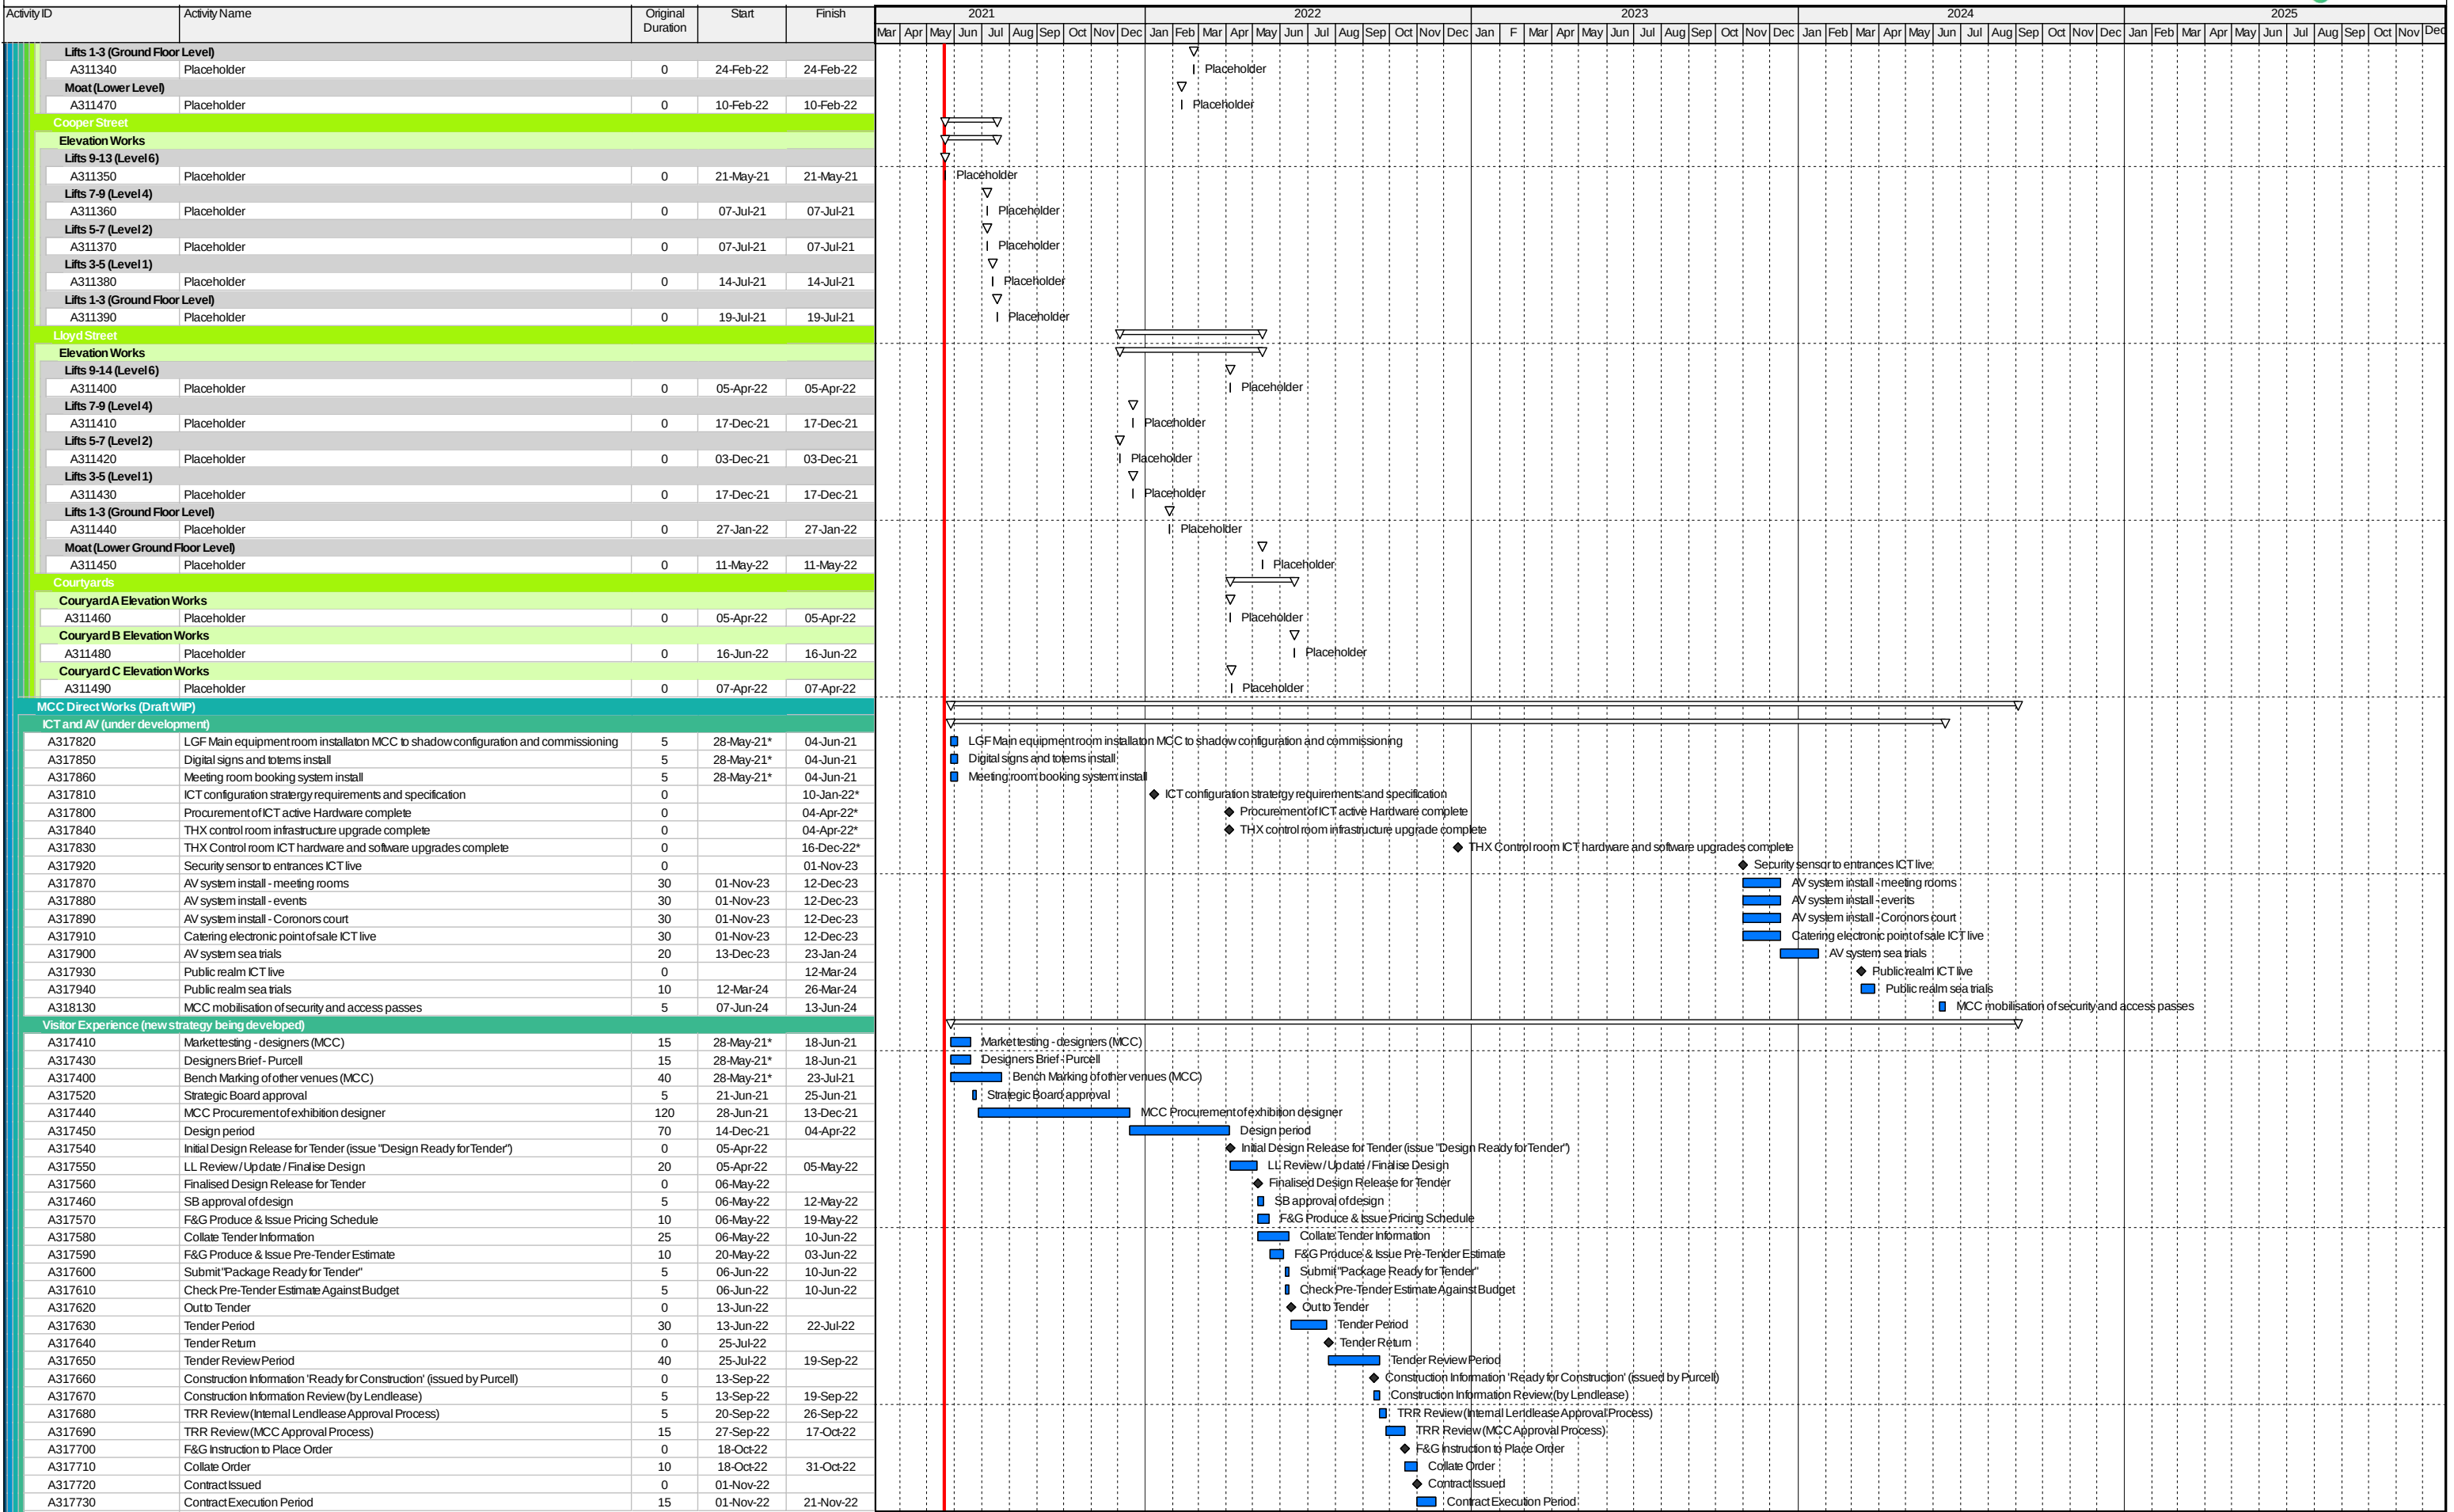



Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]


Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

4 of 96

Our Town Hall Project : Programme G19.2 (ACCEPTED PROGRAMME)

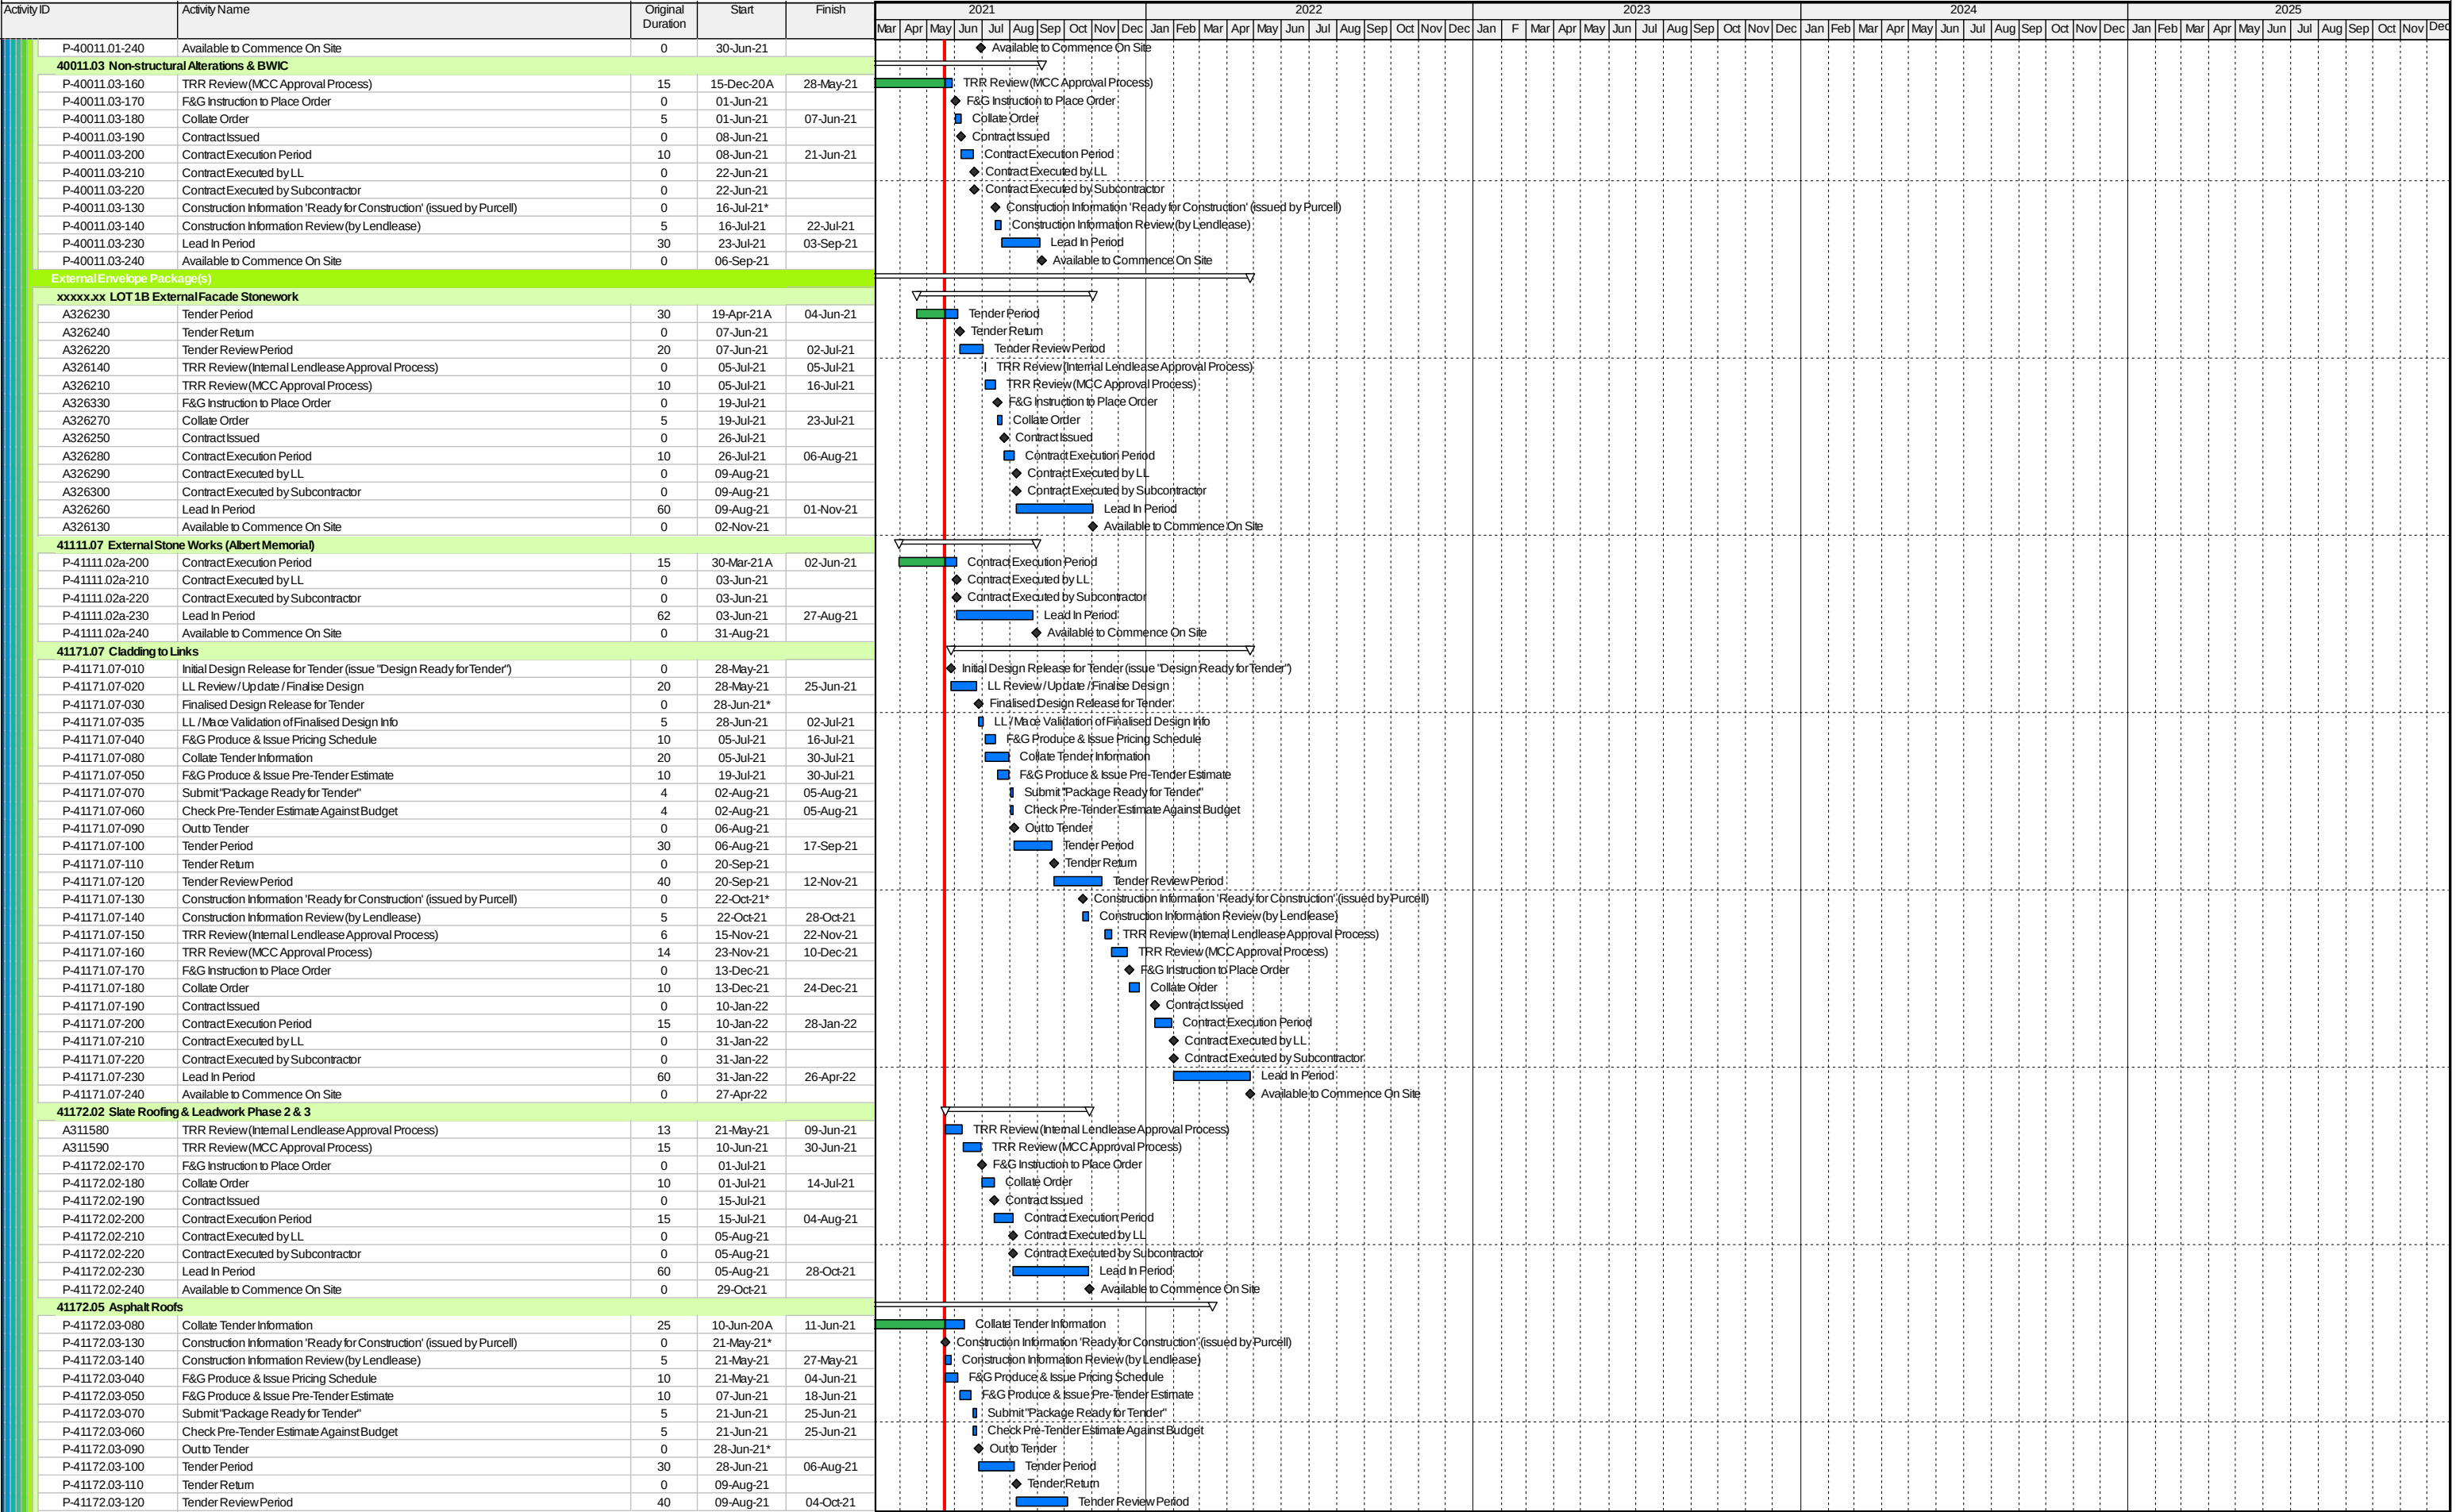

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]


Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

6 of 96

Our Town Hall Project : Programme G19.2 (ACCEPTED PROGRAMME)

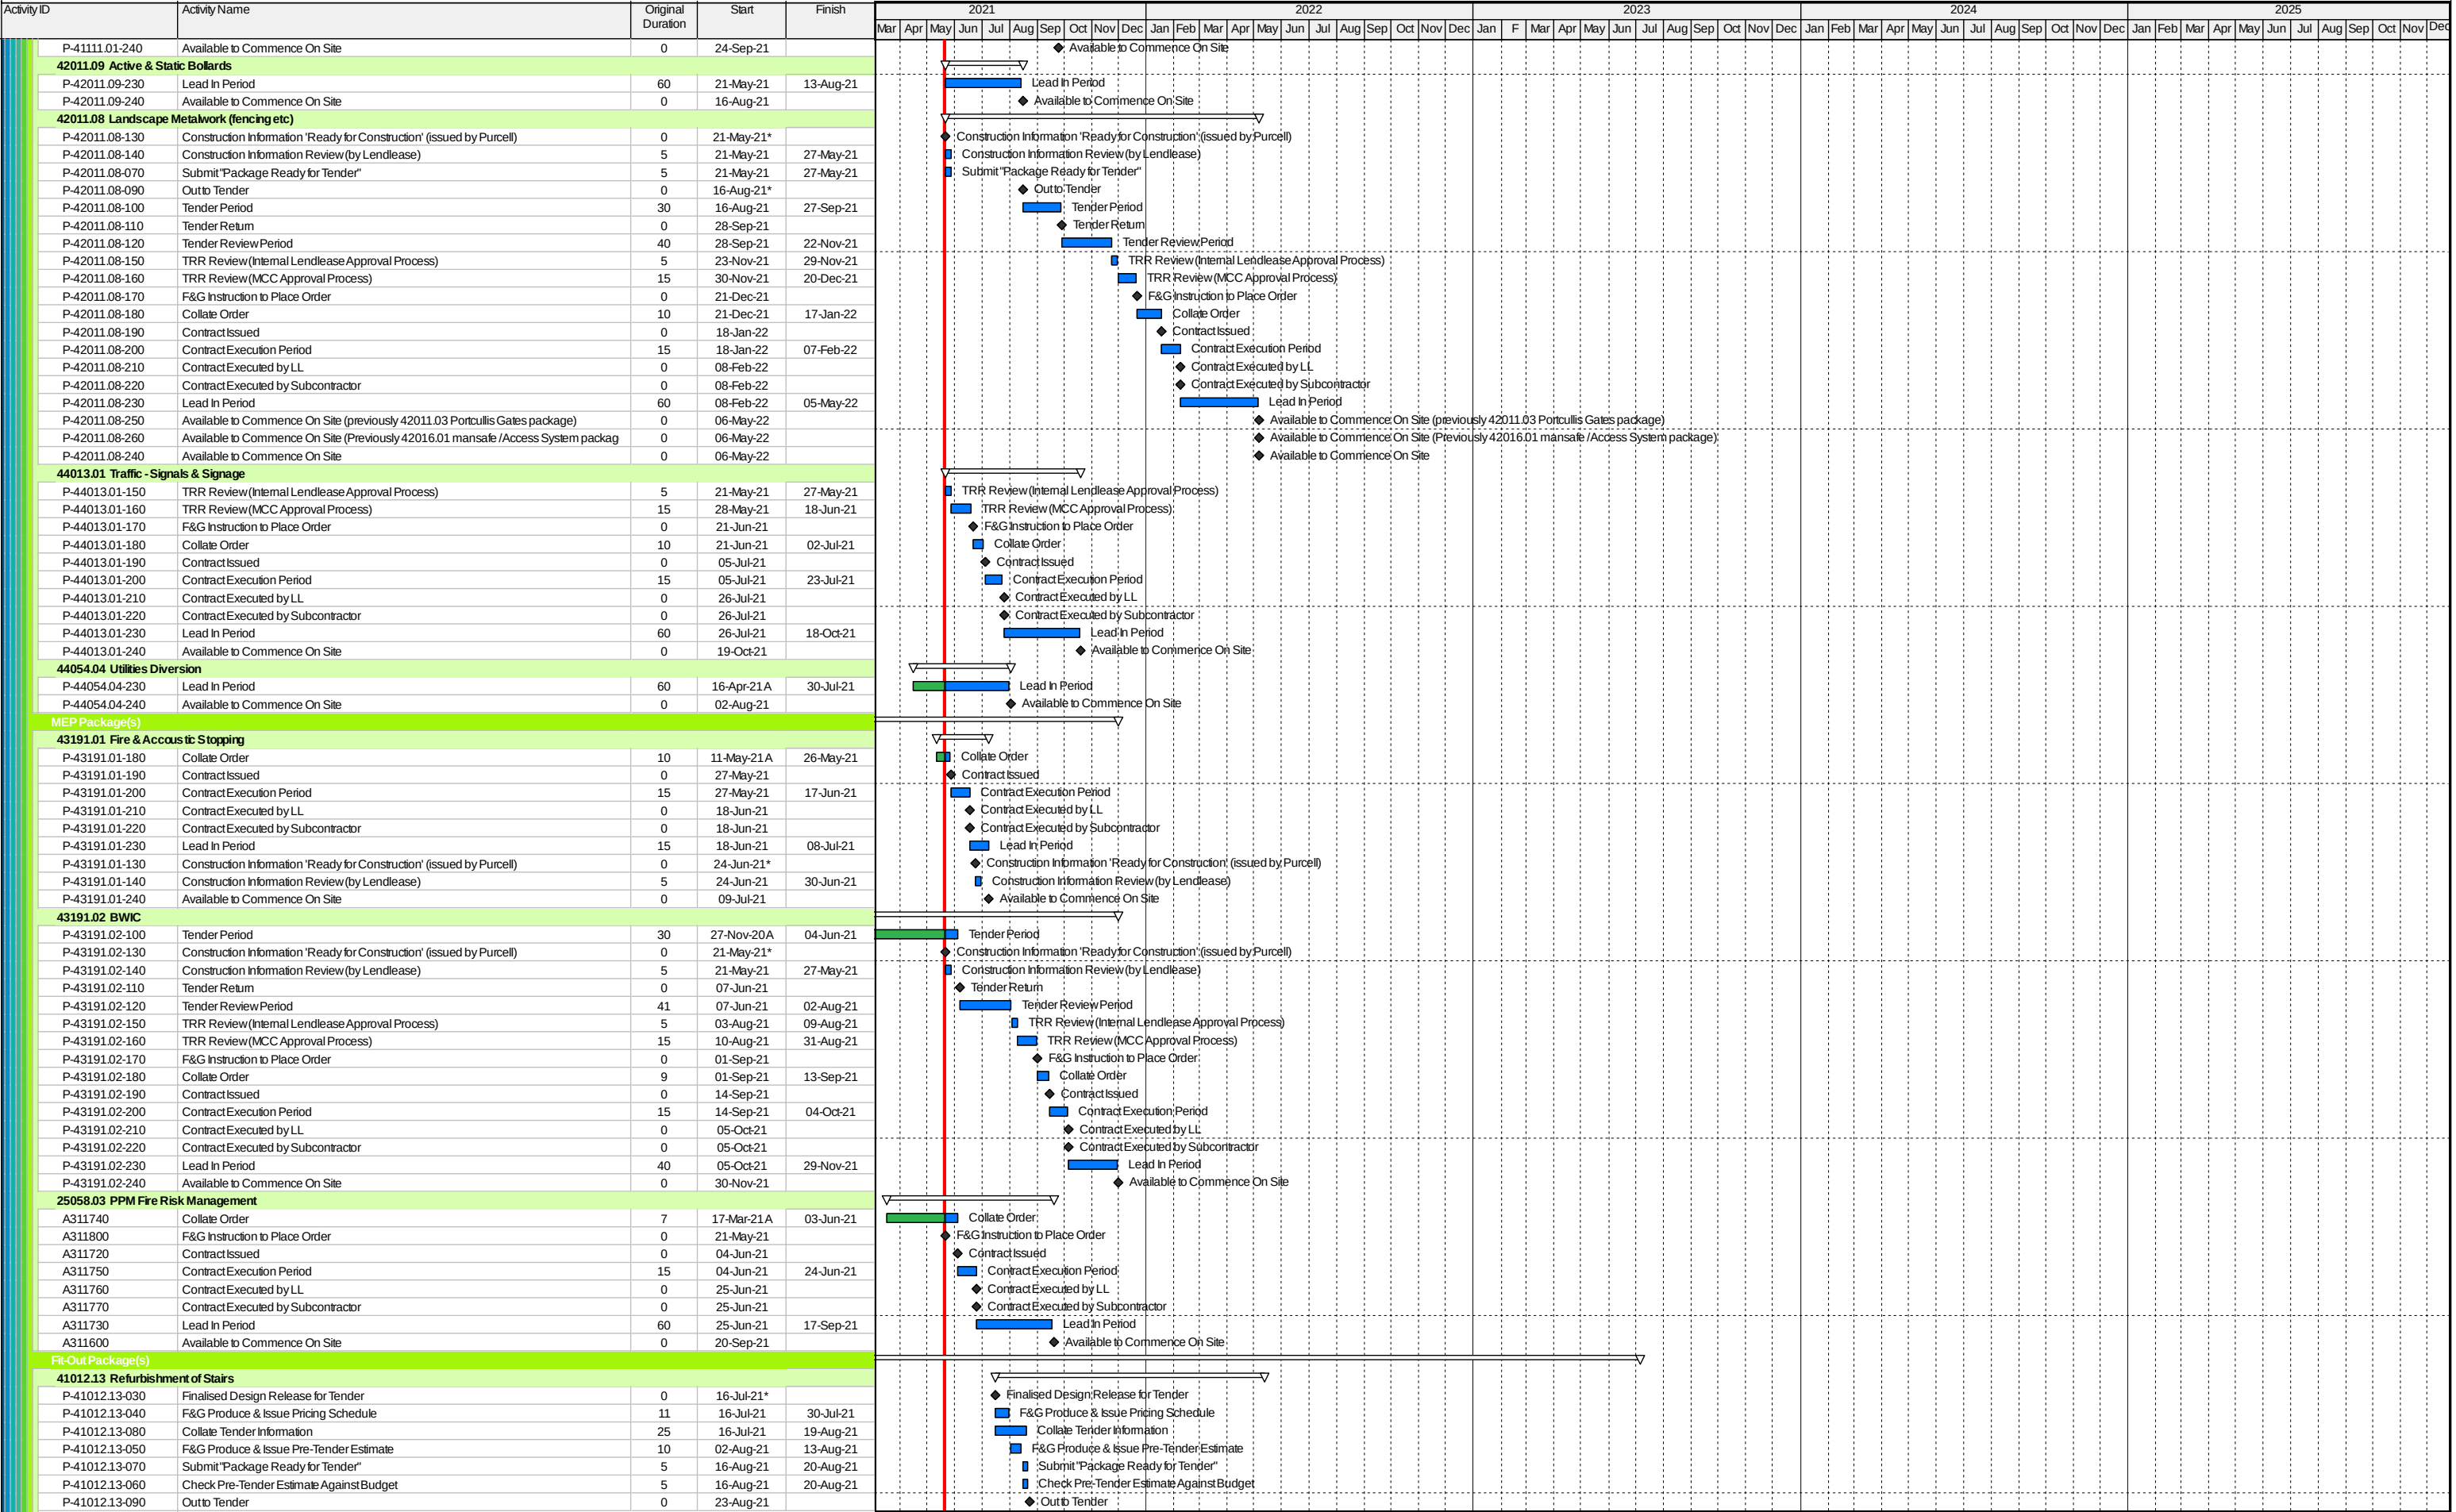

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

7 of 96

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

8 of 96

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

9 of 96

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

10 of 96

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

11 of 96

Intermittent Work Completed Work Remaining Work Critical Remaining Work	◆ Milestone ▽ Summary	<table><tr><th colspan="4">Programme Revision:</th></tr><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approv...</th></tr><tr><td>11-Jun-21</td><td>G19.2 - Accepted</td><td>RJH / ST</td><td>AM</td></tr><tr><td colspan="4"></td></tr></table>	Programme Revision:				Date	Revision	Checked	Approv...	11-Jun-21	G19.2 - Accepted	RJH / ST	AM					Delivery / Contract Programme	Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21) Layout: OTH - G19.2 General Layout [RJH] Data Date: 21-May-21 Print Date: 24-Aug-21	Page: 12 of 96
Programme Revision:																					
Date	Revision	Checked	Approv...																		
11-Jun-21	G19.2 - Accepted	RJH / ST	AM																		

Intermittent Work Completed Work Remaining Work Critical Remaining Work	◆ Milestone ▽ Summary	<table><tr><th colspan="4">Programme Revision:</th></tr><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approv...</th></tr><tr><td>11-Jun-21</td><td>G19.2 - Accepted</td><td>RJH / ST</td><td>AM</td></tr><tr><td colspan="4"></td></tr></table>	Programme Revision:				Date	Revision	Checked	Approv...	11-Jun-21	G19.2 - Accepted	RJH / ST	AM					Delivery / Contract Programme	Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21) Layout: OTH - G19.2 General Layout [RJH] Data Date: 21-May-21 Print Date: 24-Aug-21	Page: 13 of 96
Programme Revision:																					
Date	Revision	Checked	Approv...																		
11-Jun-21	G19.2 - Accepted	RJH / ST	AM																		

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21


Print Date: 24-Aug-21

Page:

14 of 96

Intermittent Work Completed Work Remaining Work Critical Remaining Work	◆ ◆ Milestone ▽ Summary	<table><tr><th colspan="4">Programme Revision:</th></tr><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approv...</th></tr><tr><td>11-Jun-21</td><td>G19.2 - Accepted</td><td>RJH / ST</td><td>AM</td></tr><tr><td colspan="4"></td></tr></table>	Programme Revision:				Date	Revision	Checked	Approv...	11-Jun-21	G19.2 - Accepted	RJH / ST	AM					Delivery / Contract Programme	Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21) Layout: OTH - G19.2 General Layout [RJH] Data Date: 21-May-21 Print Date: 24-Aug-21	Page: 15 of 96
Programme Revision:																					
Date	Revision	Checked	Approv...																		
11-Jun-21	G19.2 - Accepted	RJH / ST	AM																		

Our Town Hall Project : Programme G19.2 (ACCEPTED PROGRAMME)

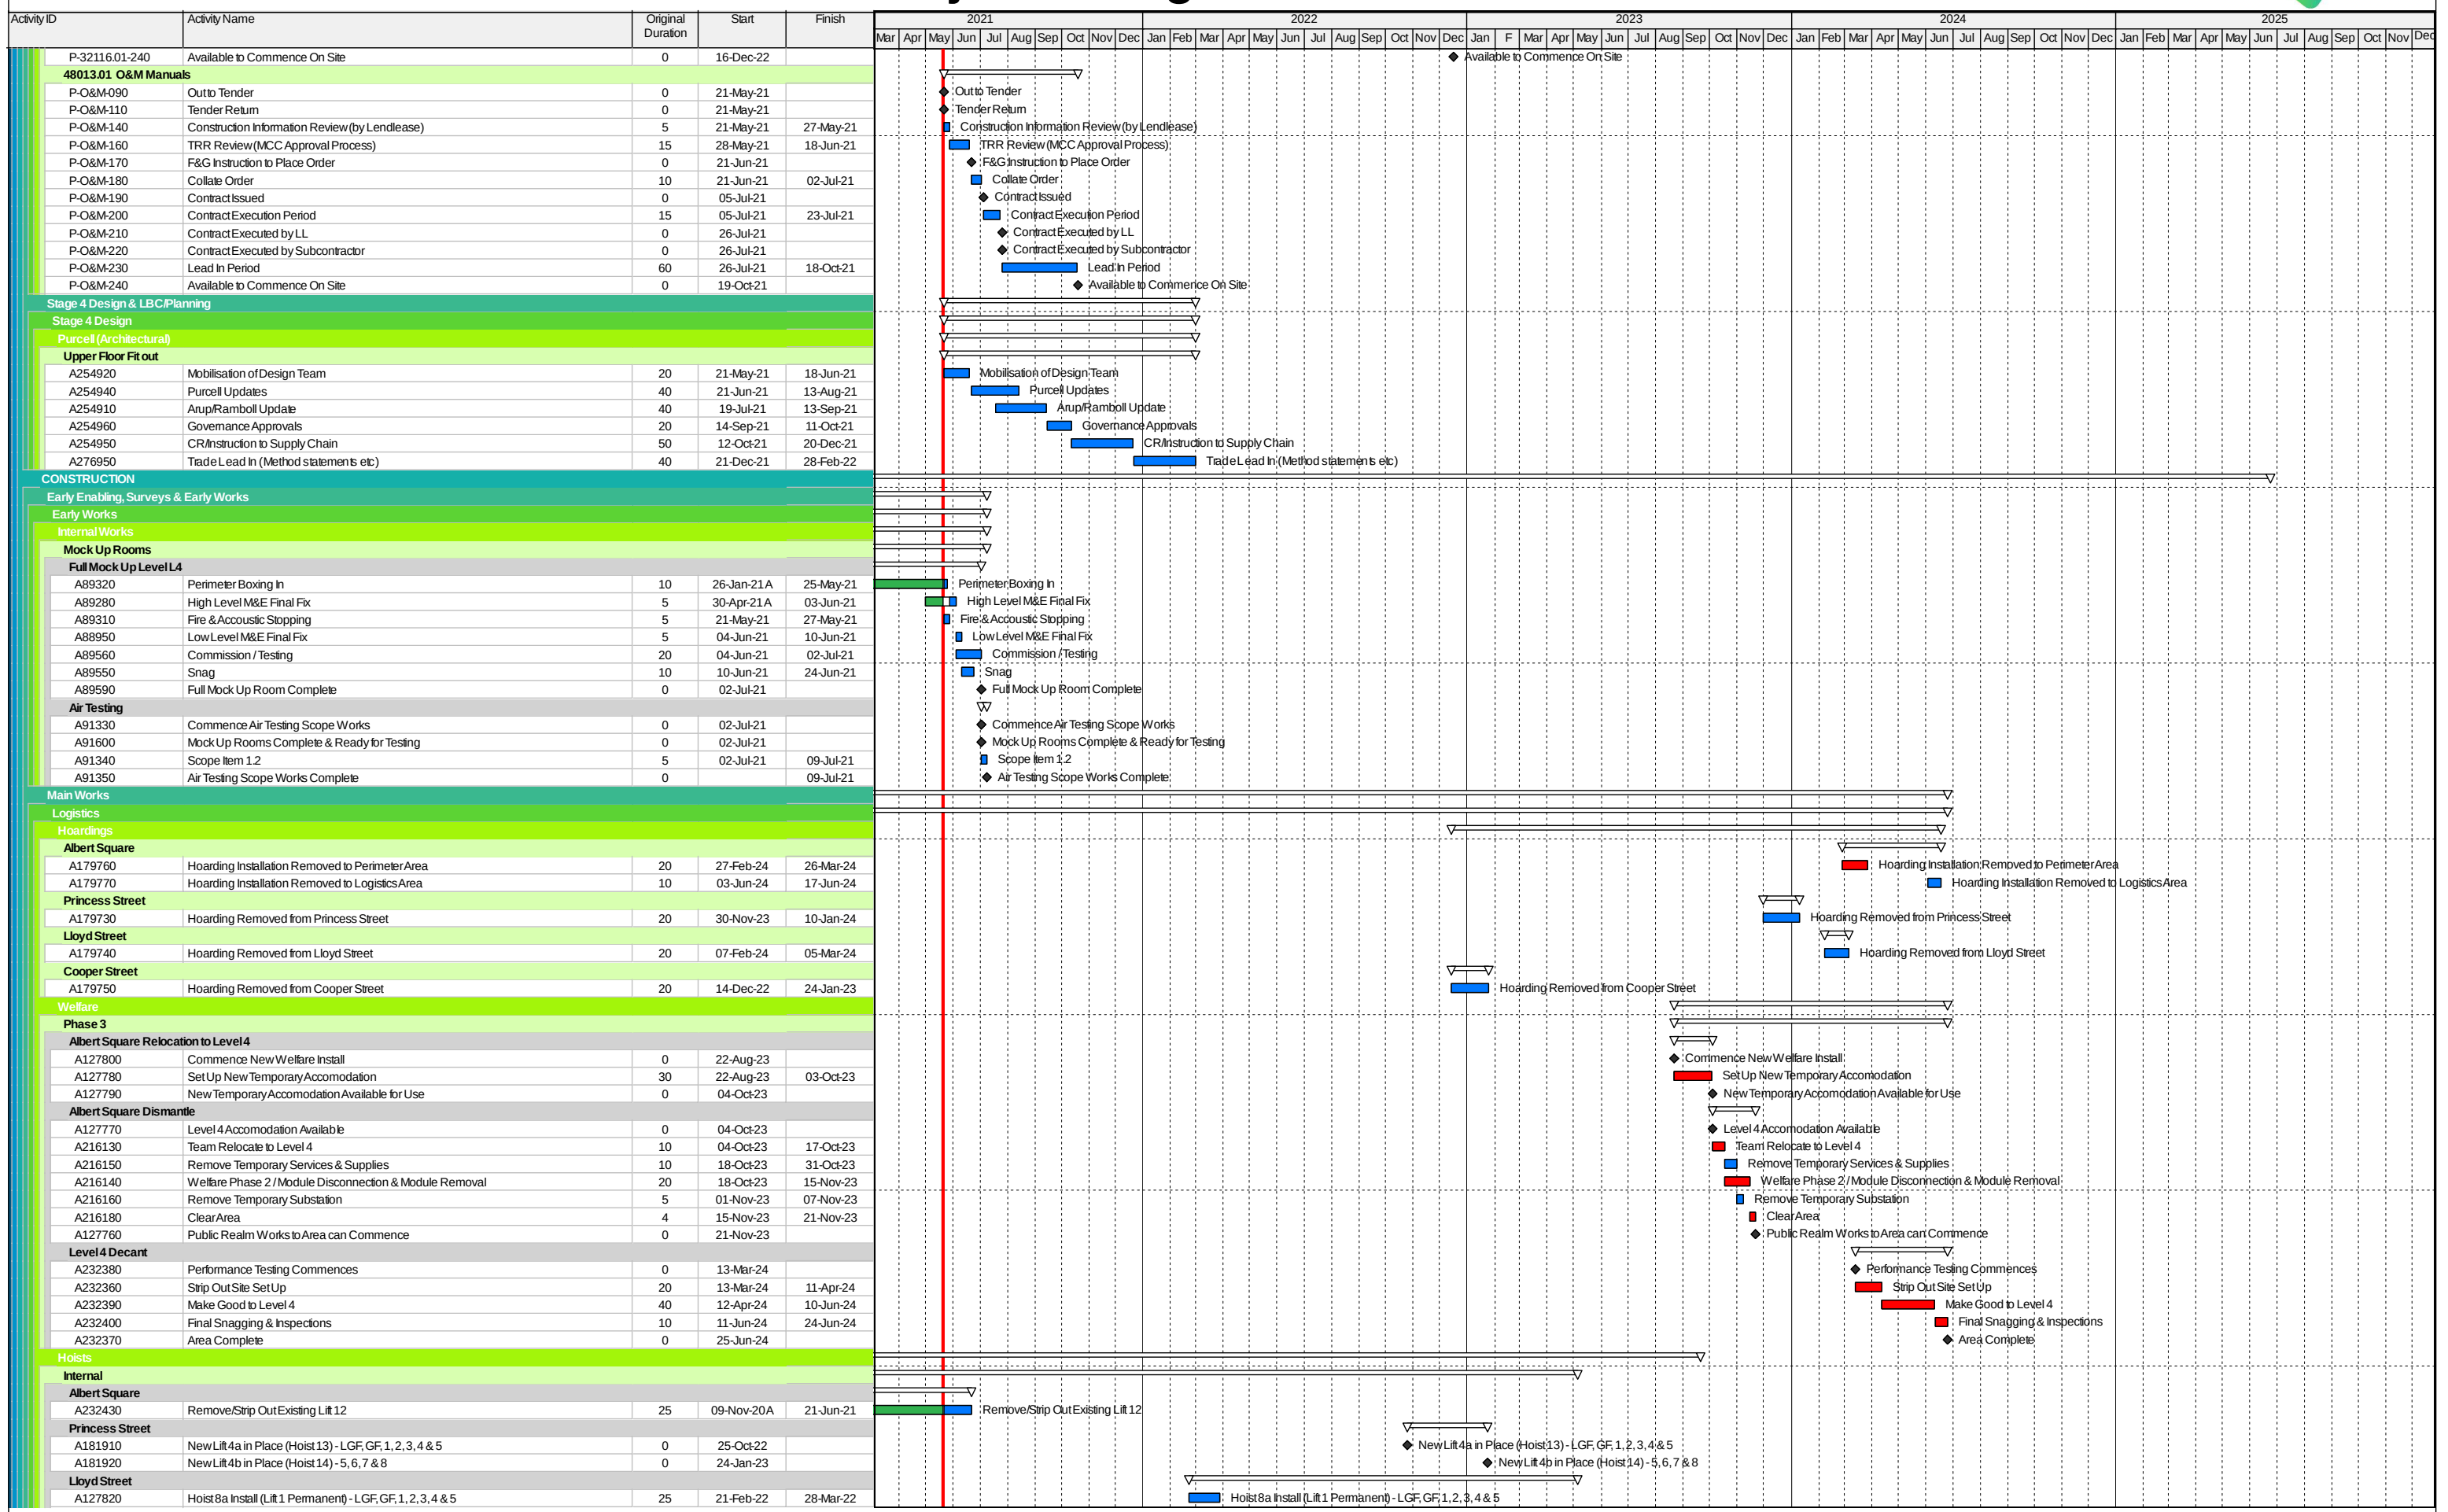

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

17 of 96

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]


Data Date: 21-May-21

Print Date: 24-Aug-21


Page:

18 of 96


Our Town Hall Project : Programme G19.2 (ACCEPTED PROGRAMME)

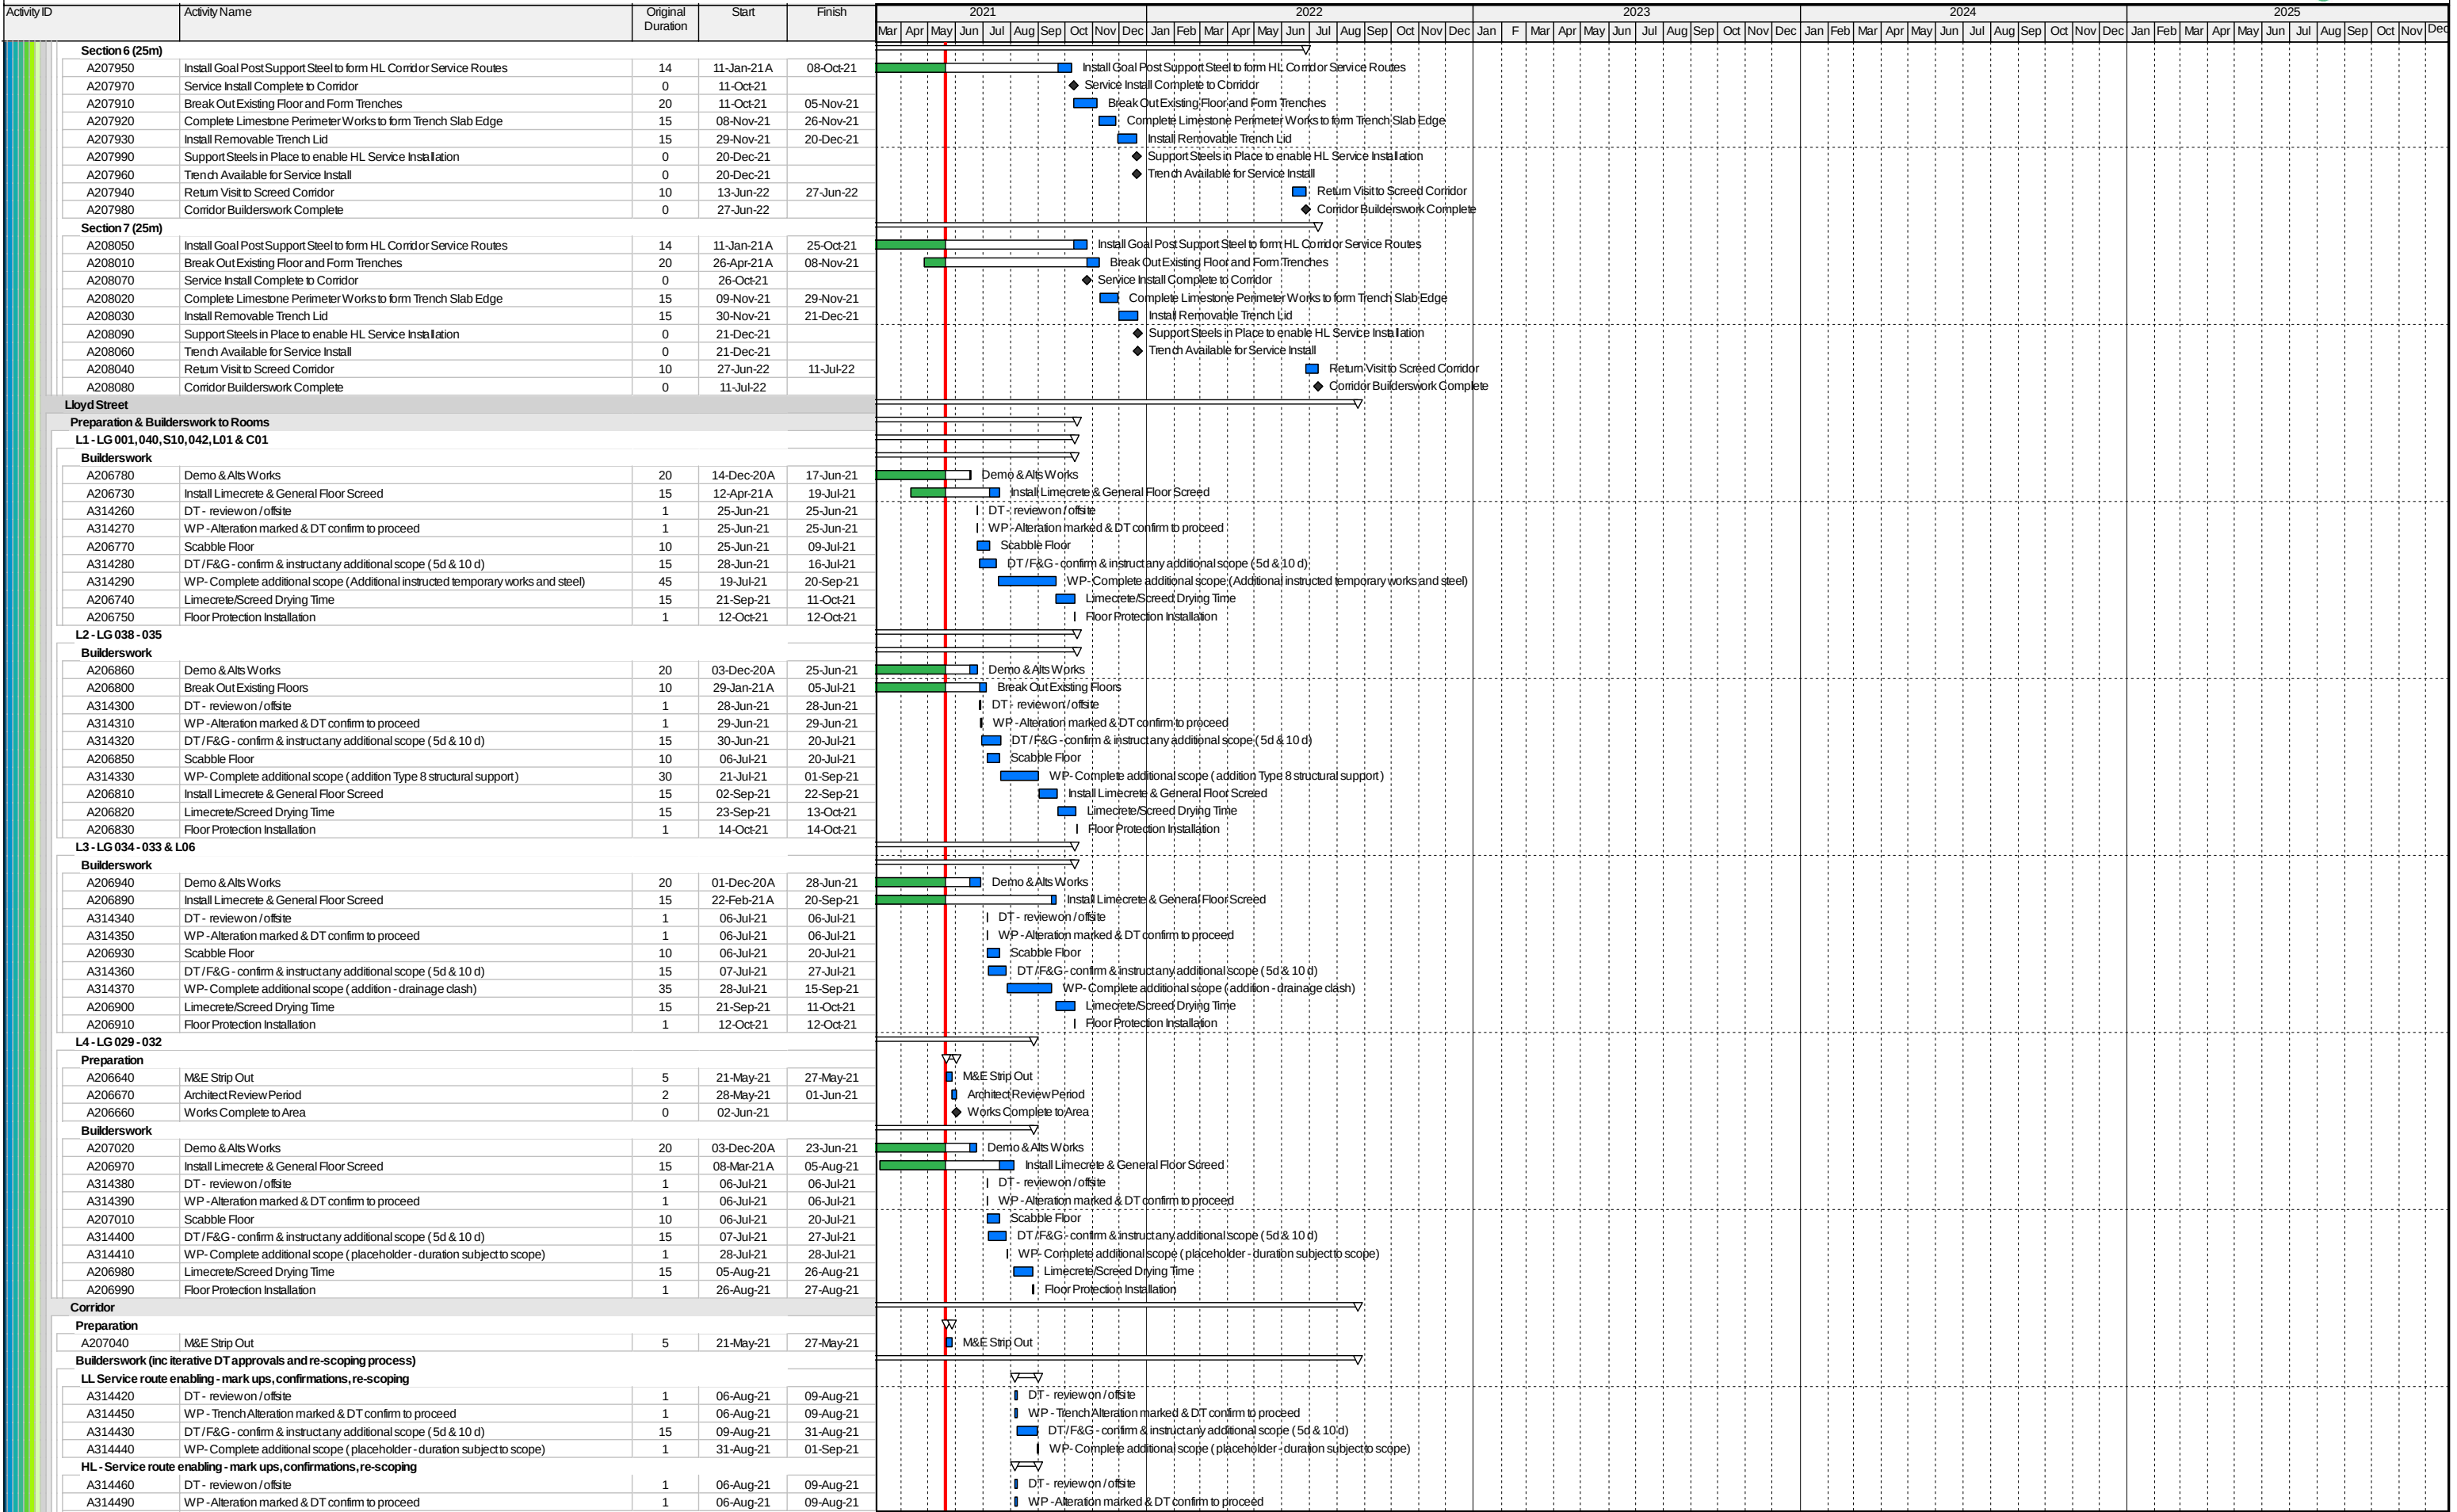

Our Town Hall Project : Programme G19.2 (ACCEPTED PROGRAMME)

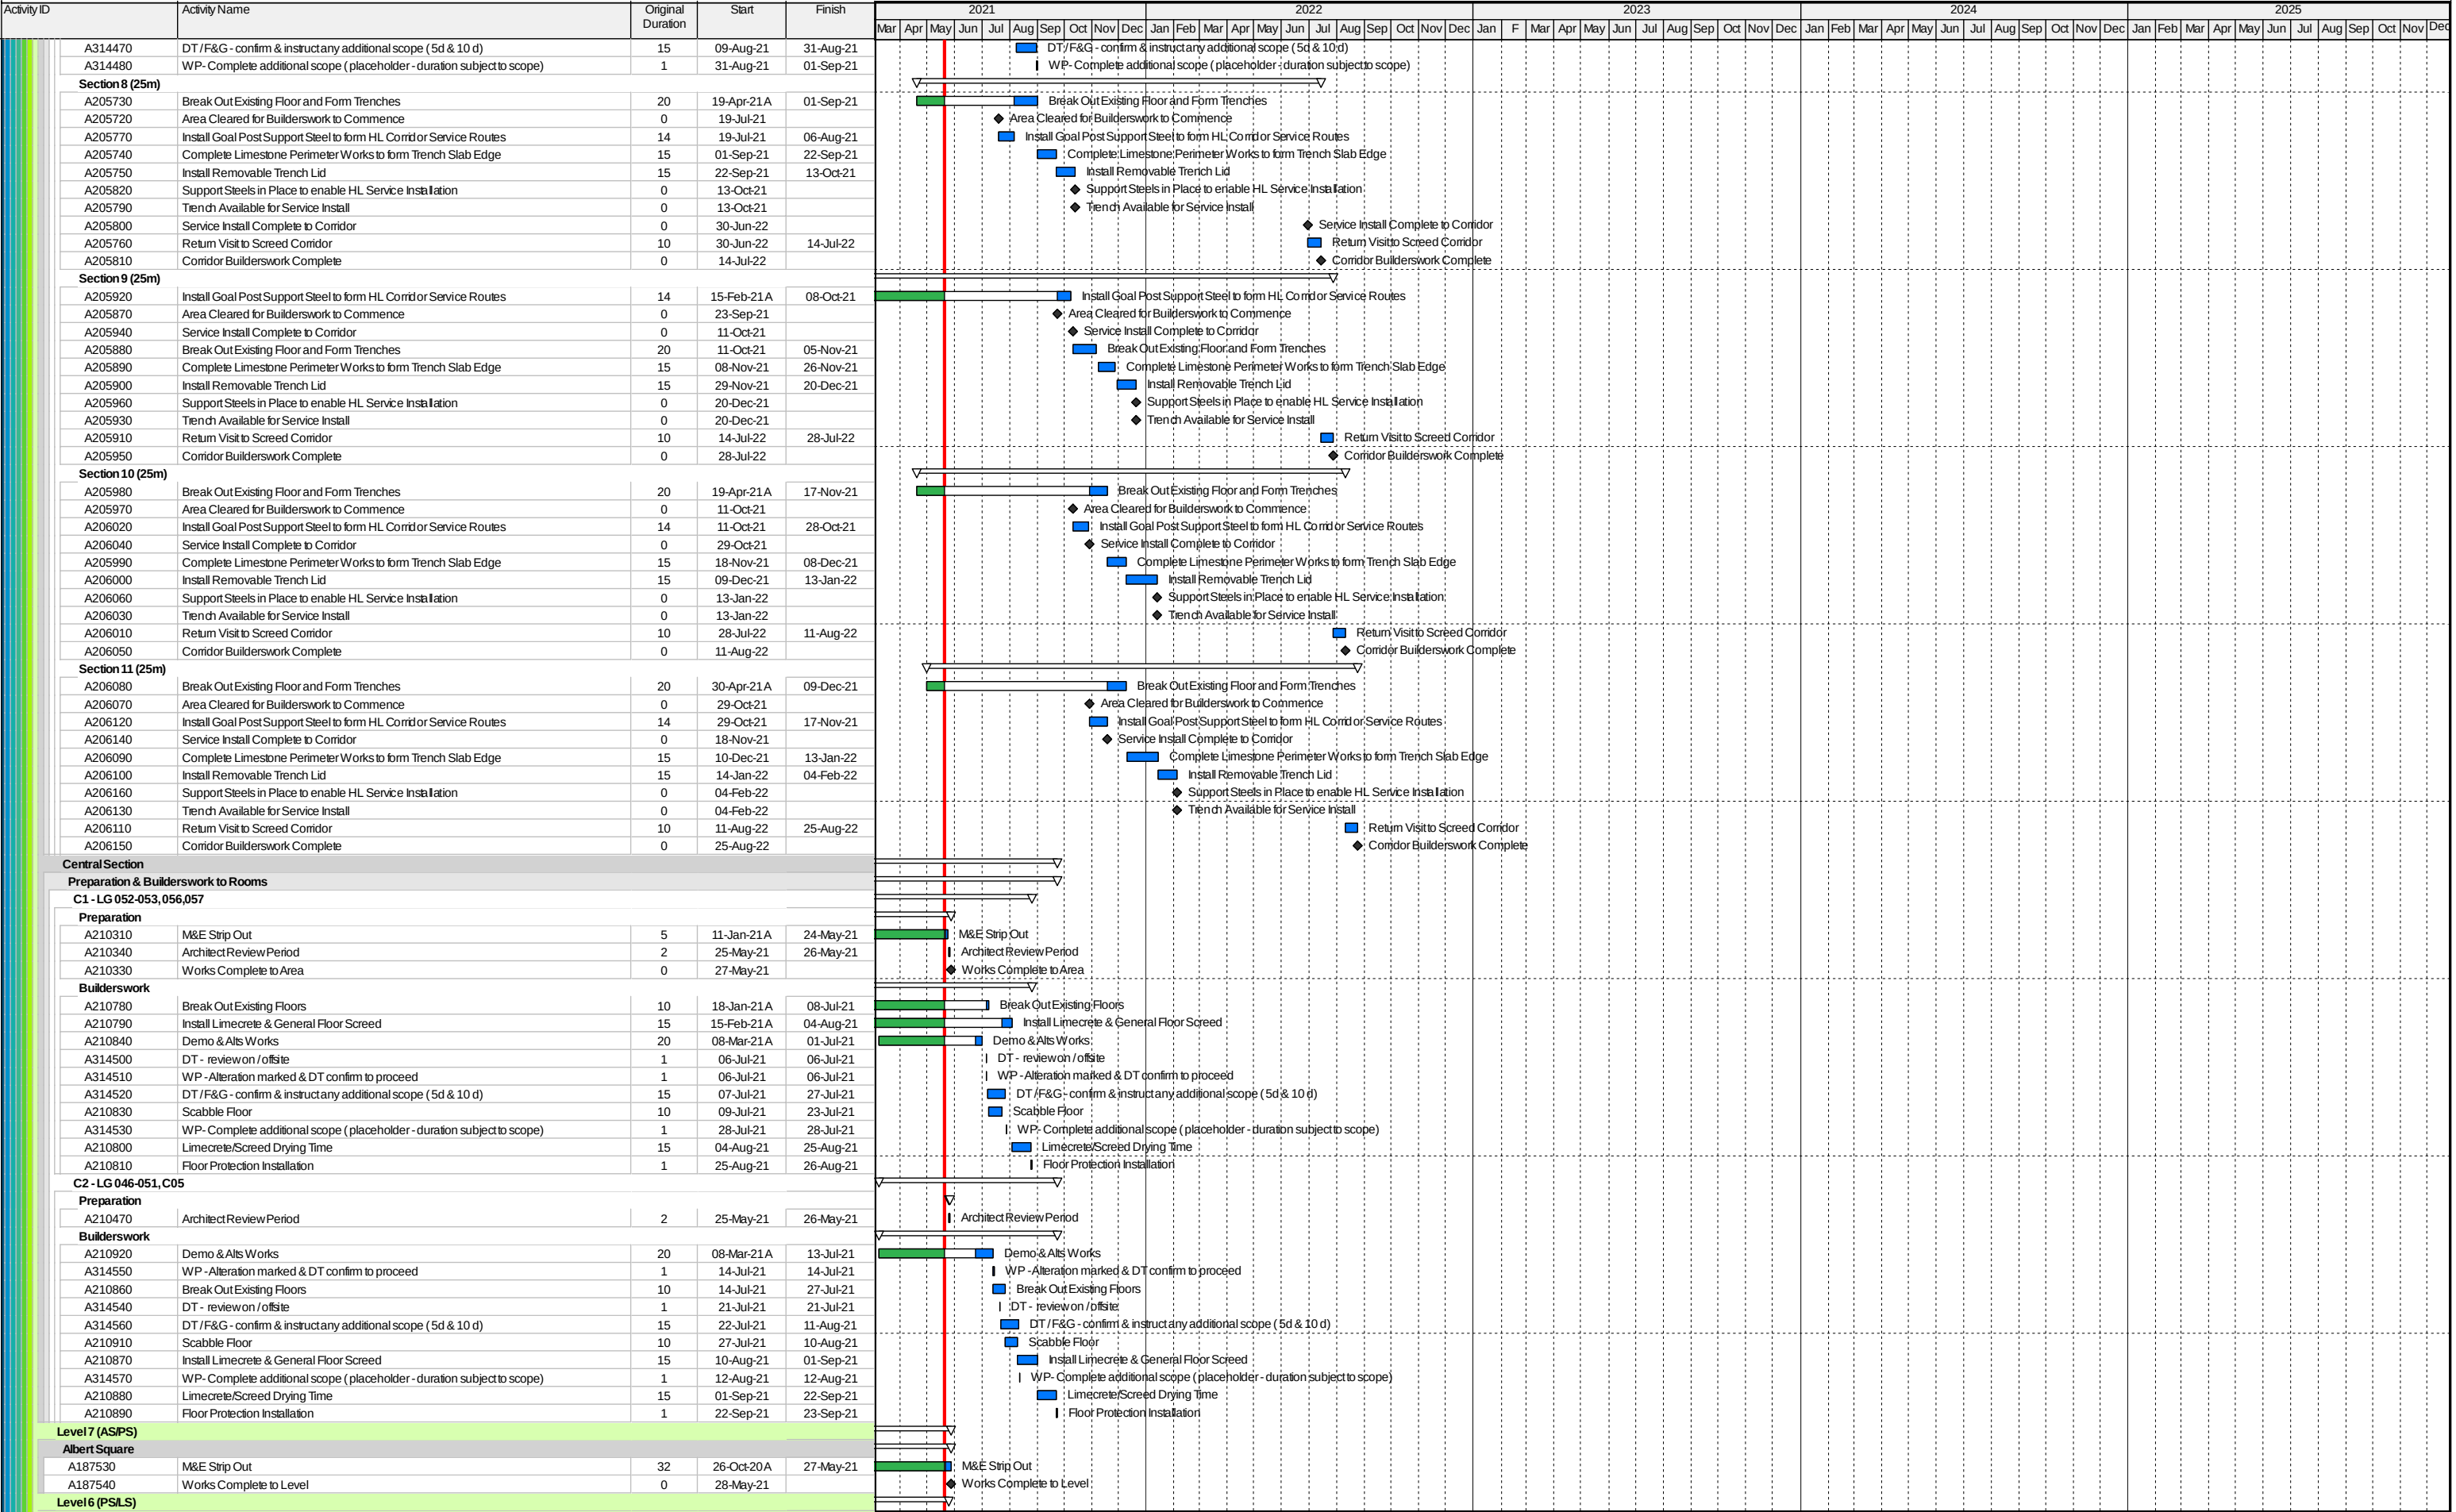

Our Town Hall Project : Programme G19.2 (ACCEPTED PROGRAMME)

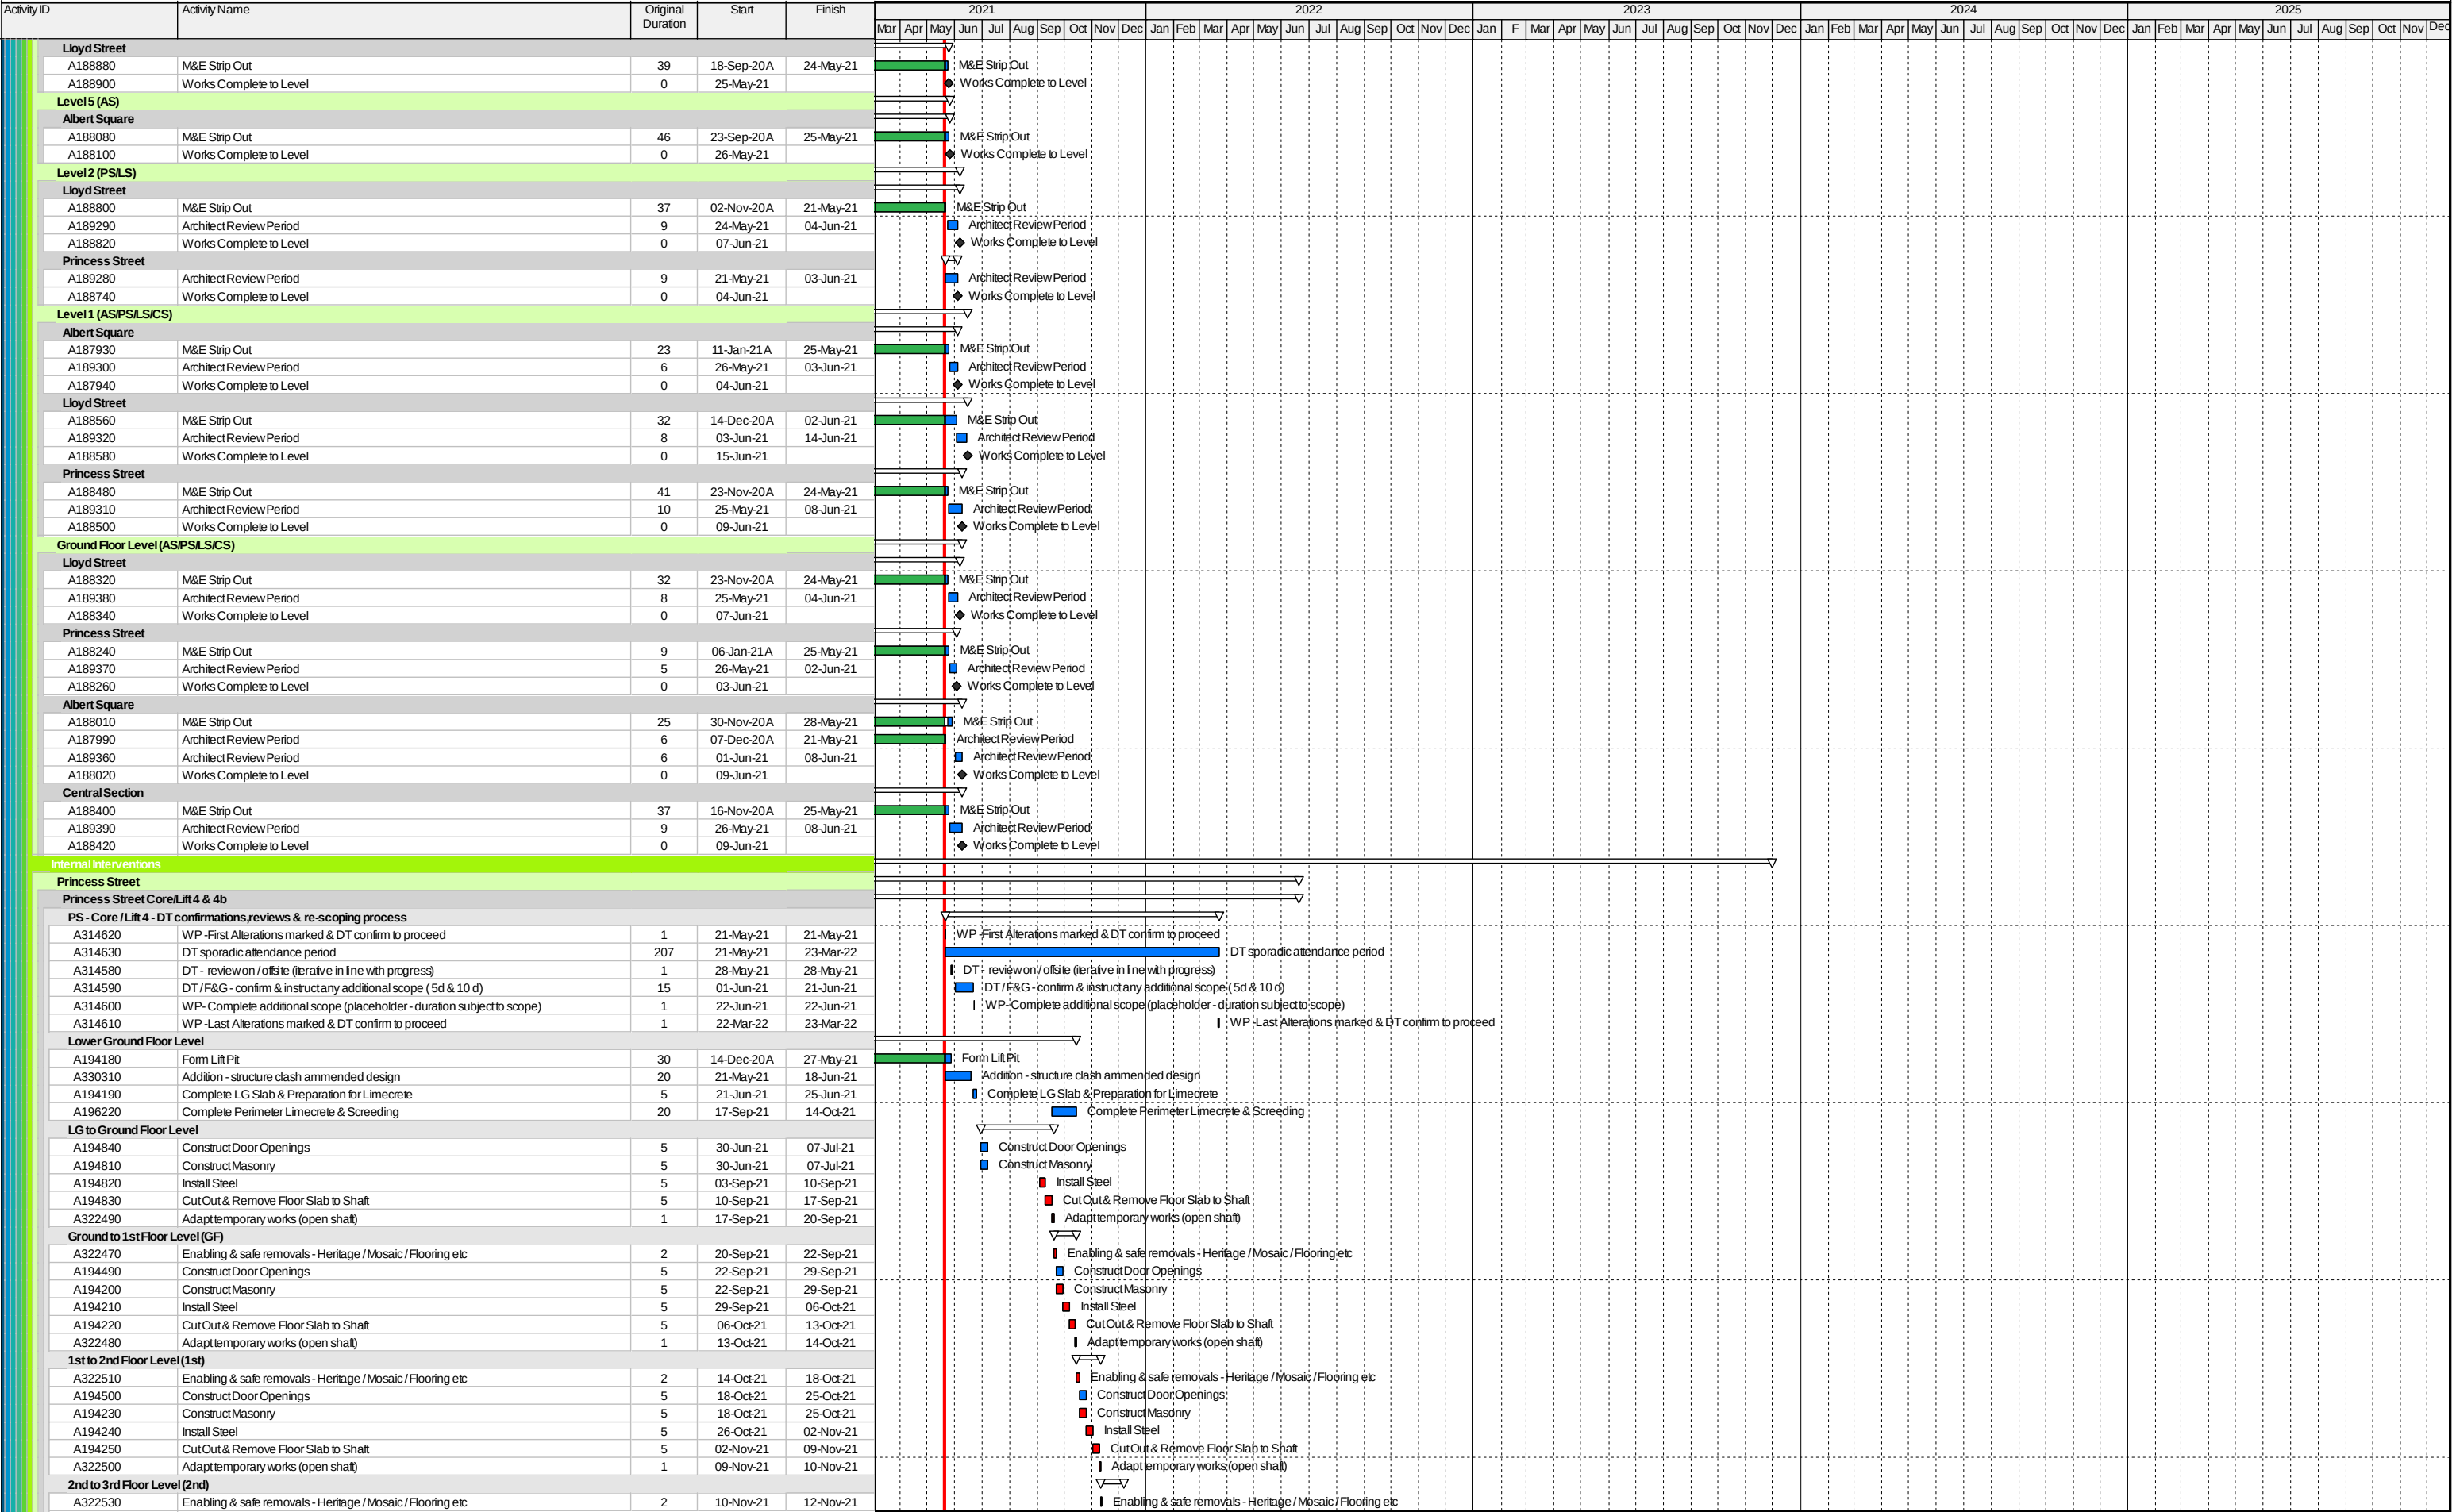

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

◆

Milestone

▽

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID:

UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout:

OTH - G19.2 General Layout [RJH]

Data Date:

21-May-21


Print Date:

24-Aug-21

Page:

22 of 96

Our Town Hall Project : Programme G19.2 (ACCEPTED PROGRAMME)

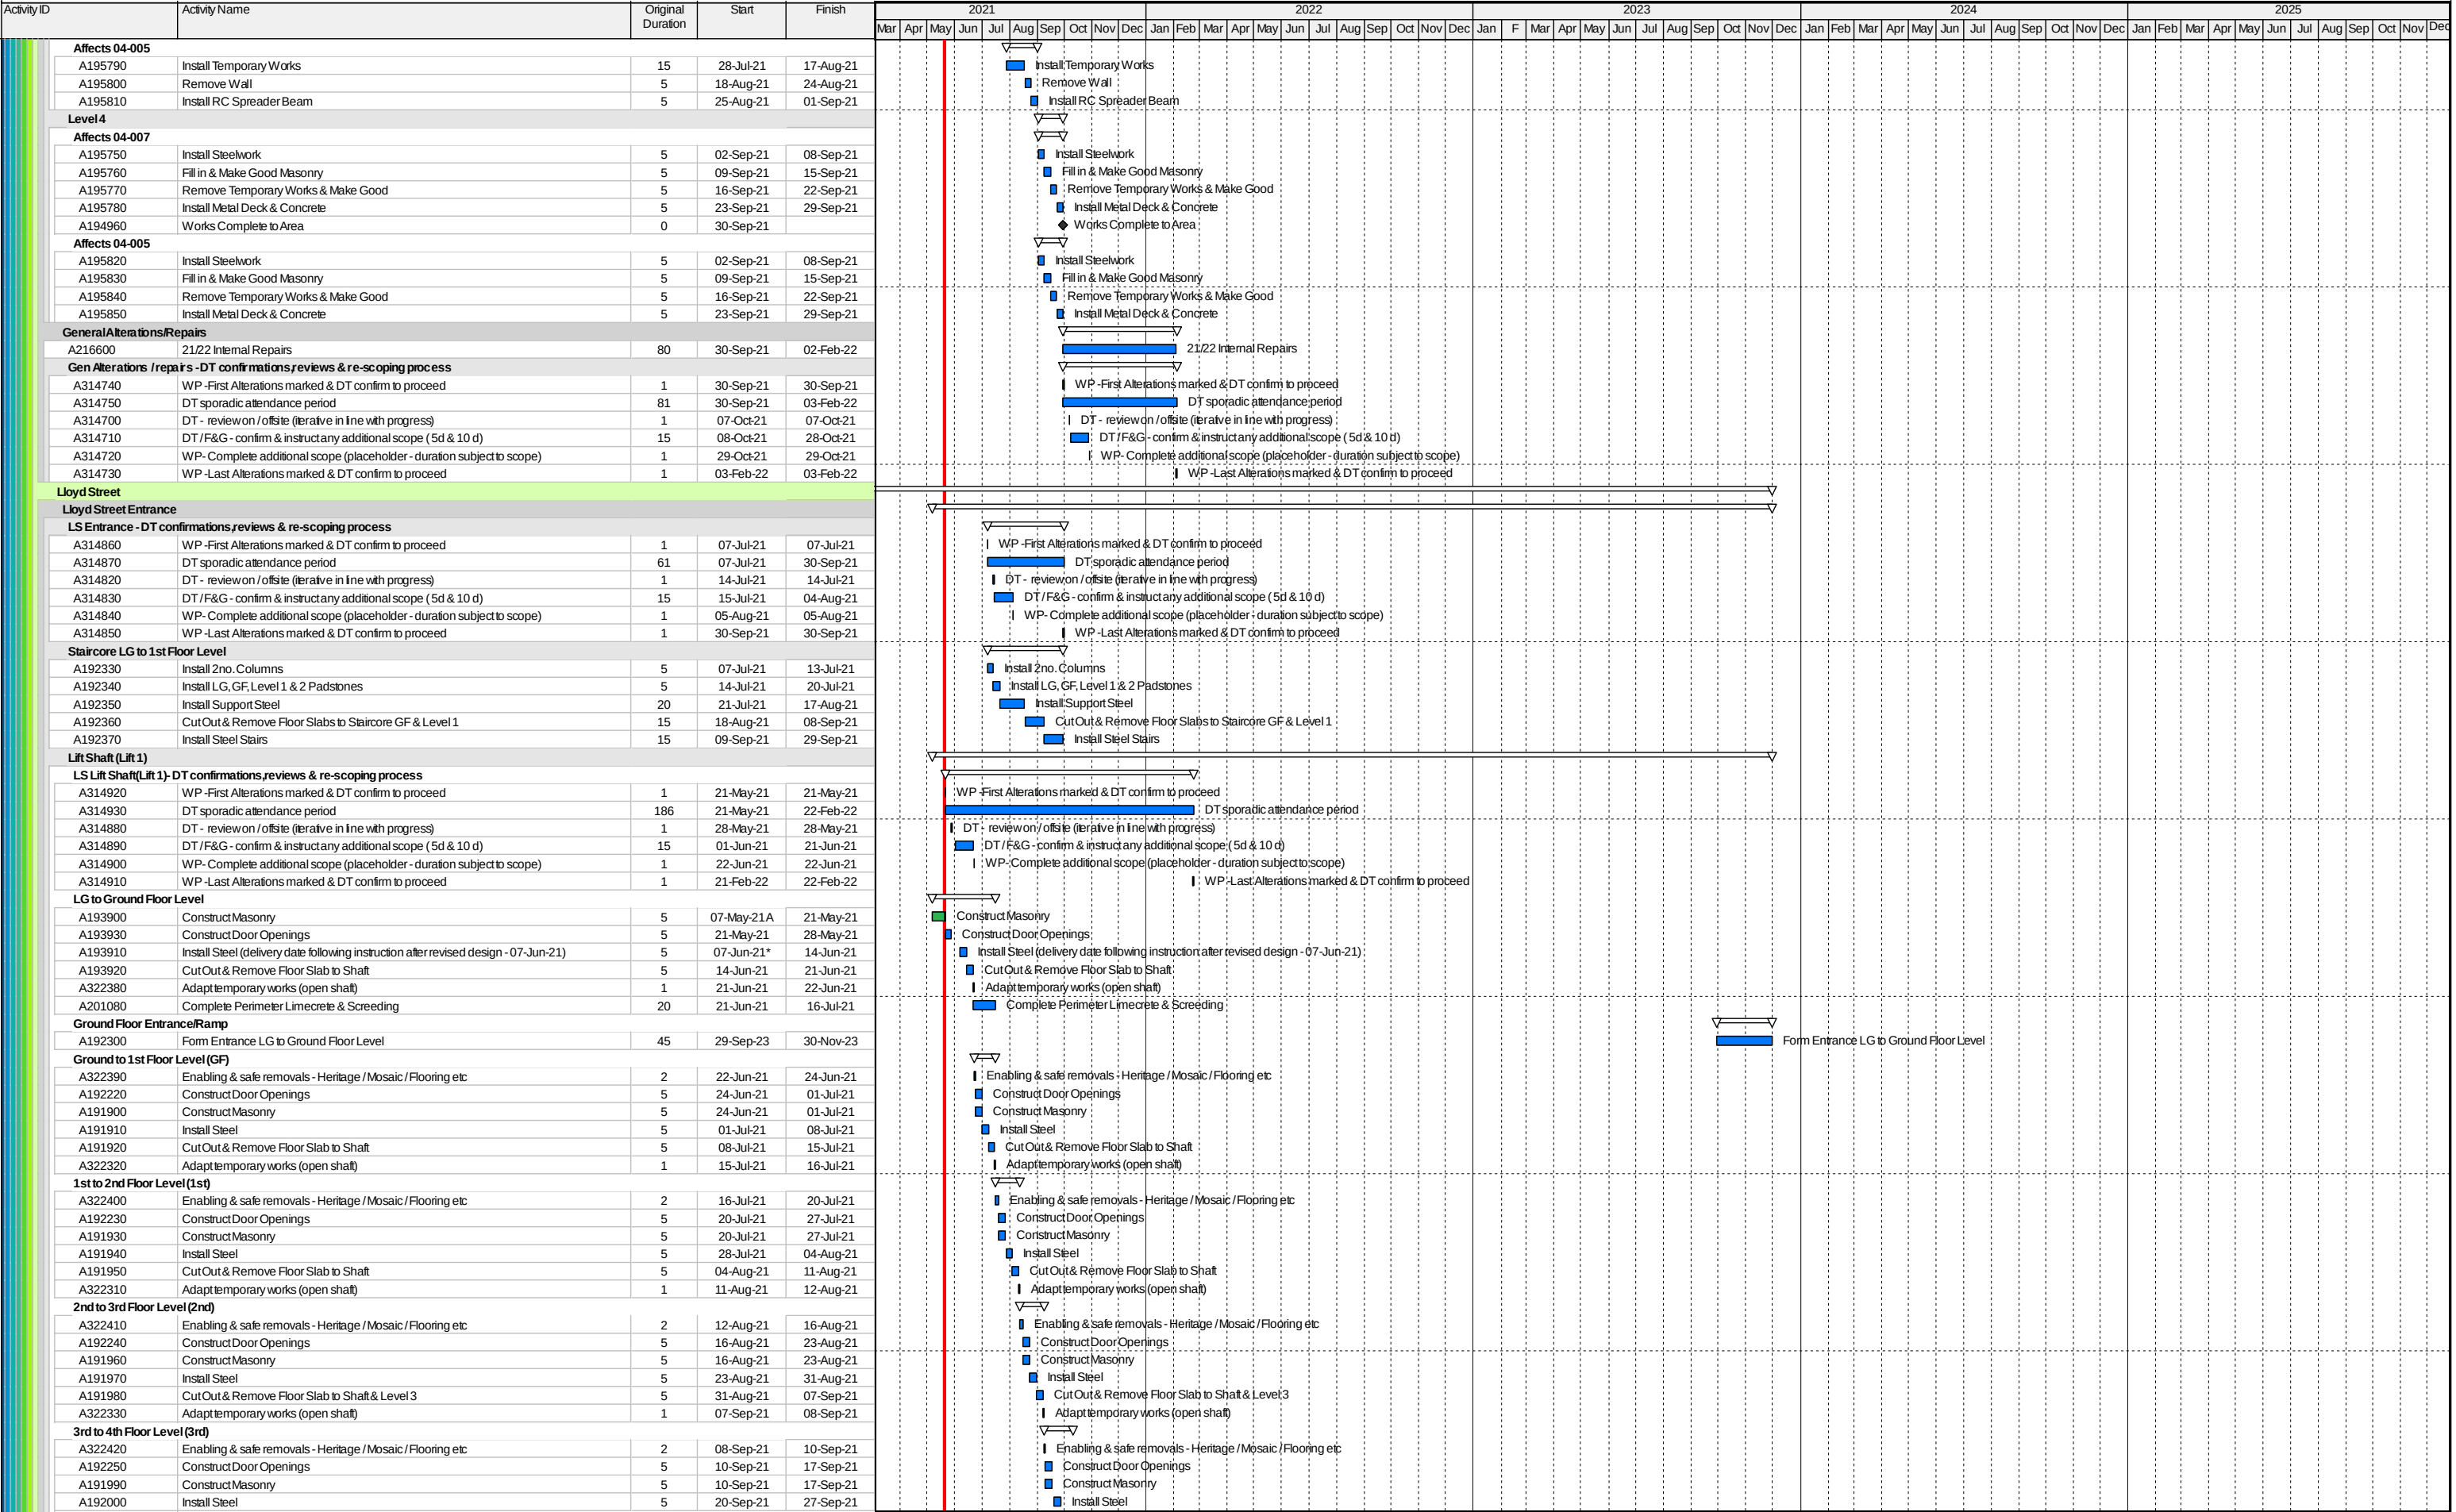

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

◆

Milestone

▽

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

24 of 96

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]


Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

25 of 96

Our Town Hall Project : Programme G19.2 (ACCEPTED PROGRAMME)

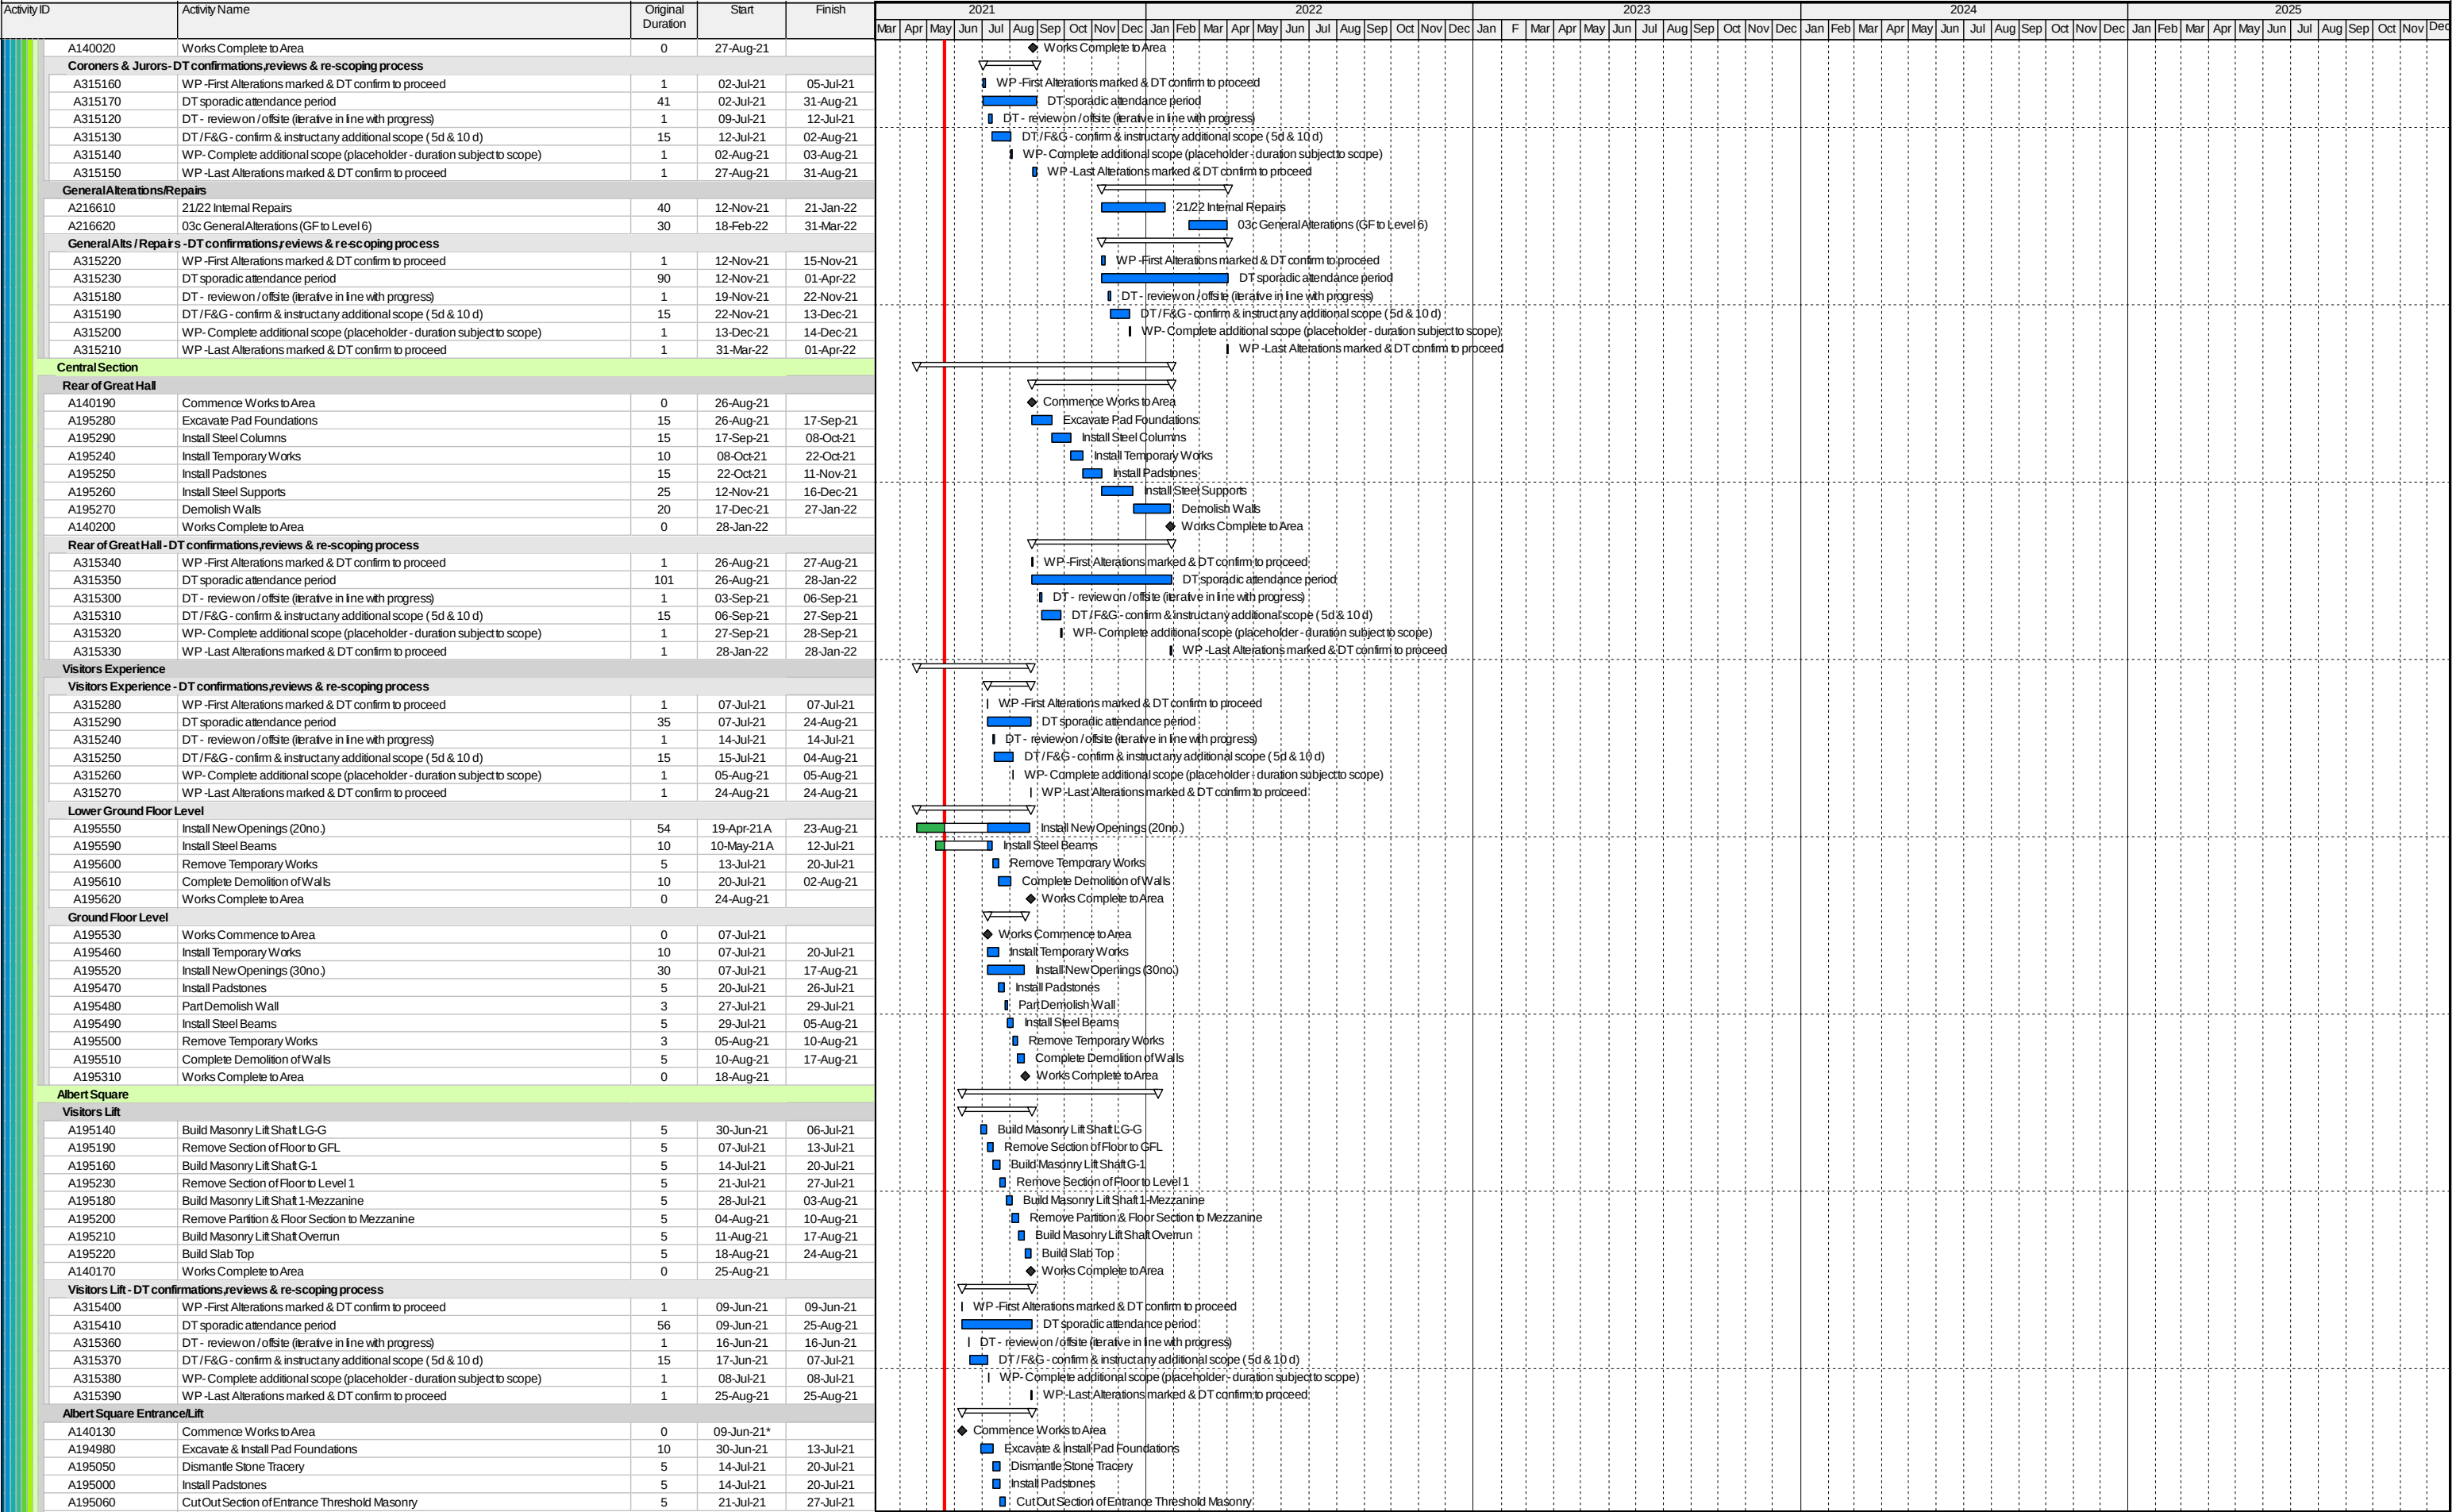

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]


Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

27 of 96

Our Town Hall Project : Programme G19.2 (ACCEPTED PROGRAMME)

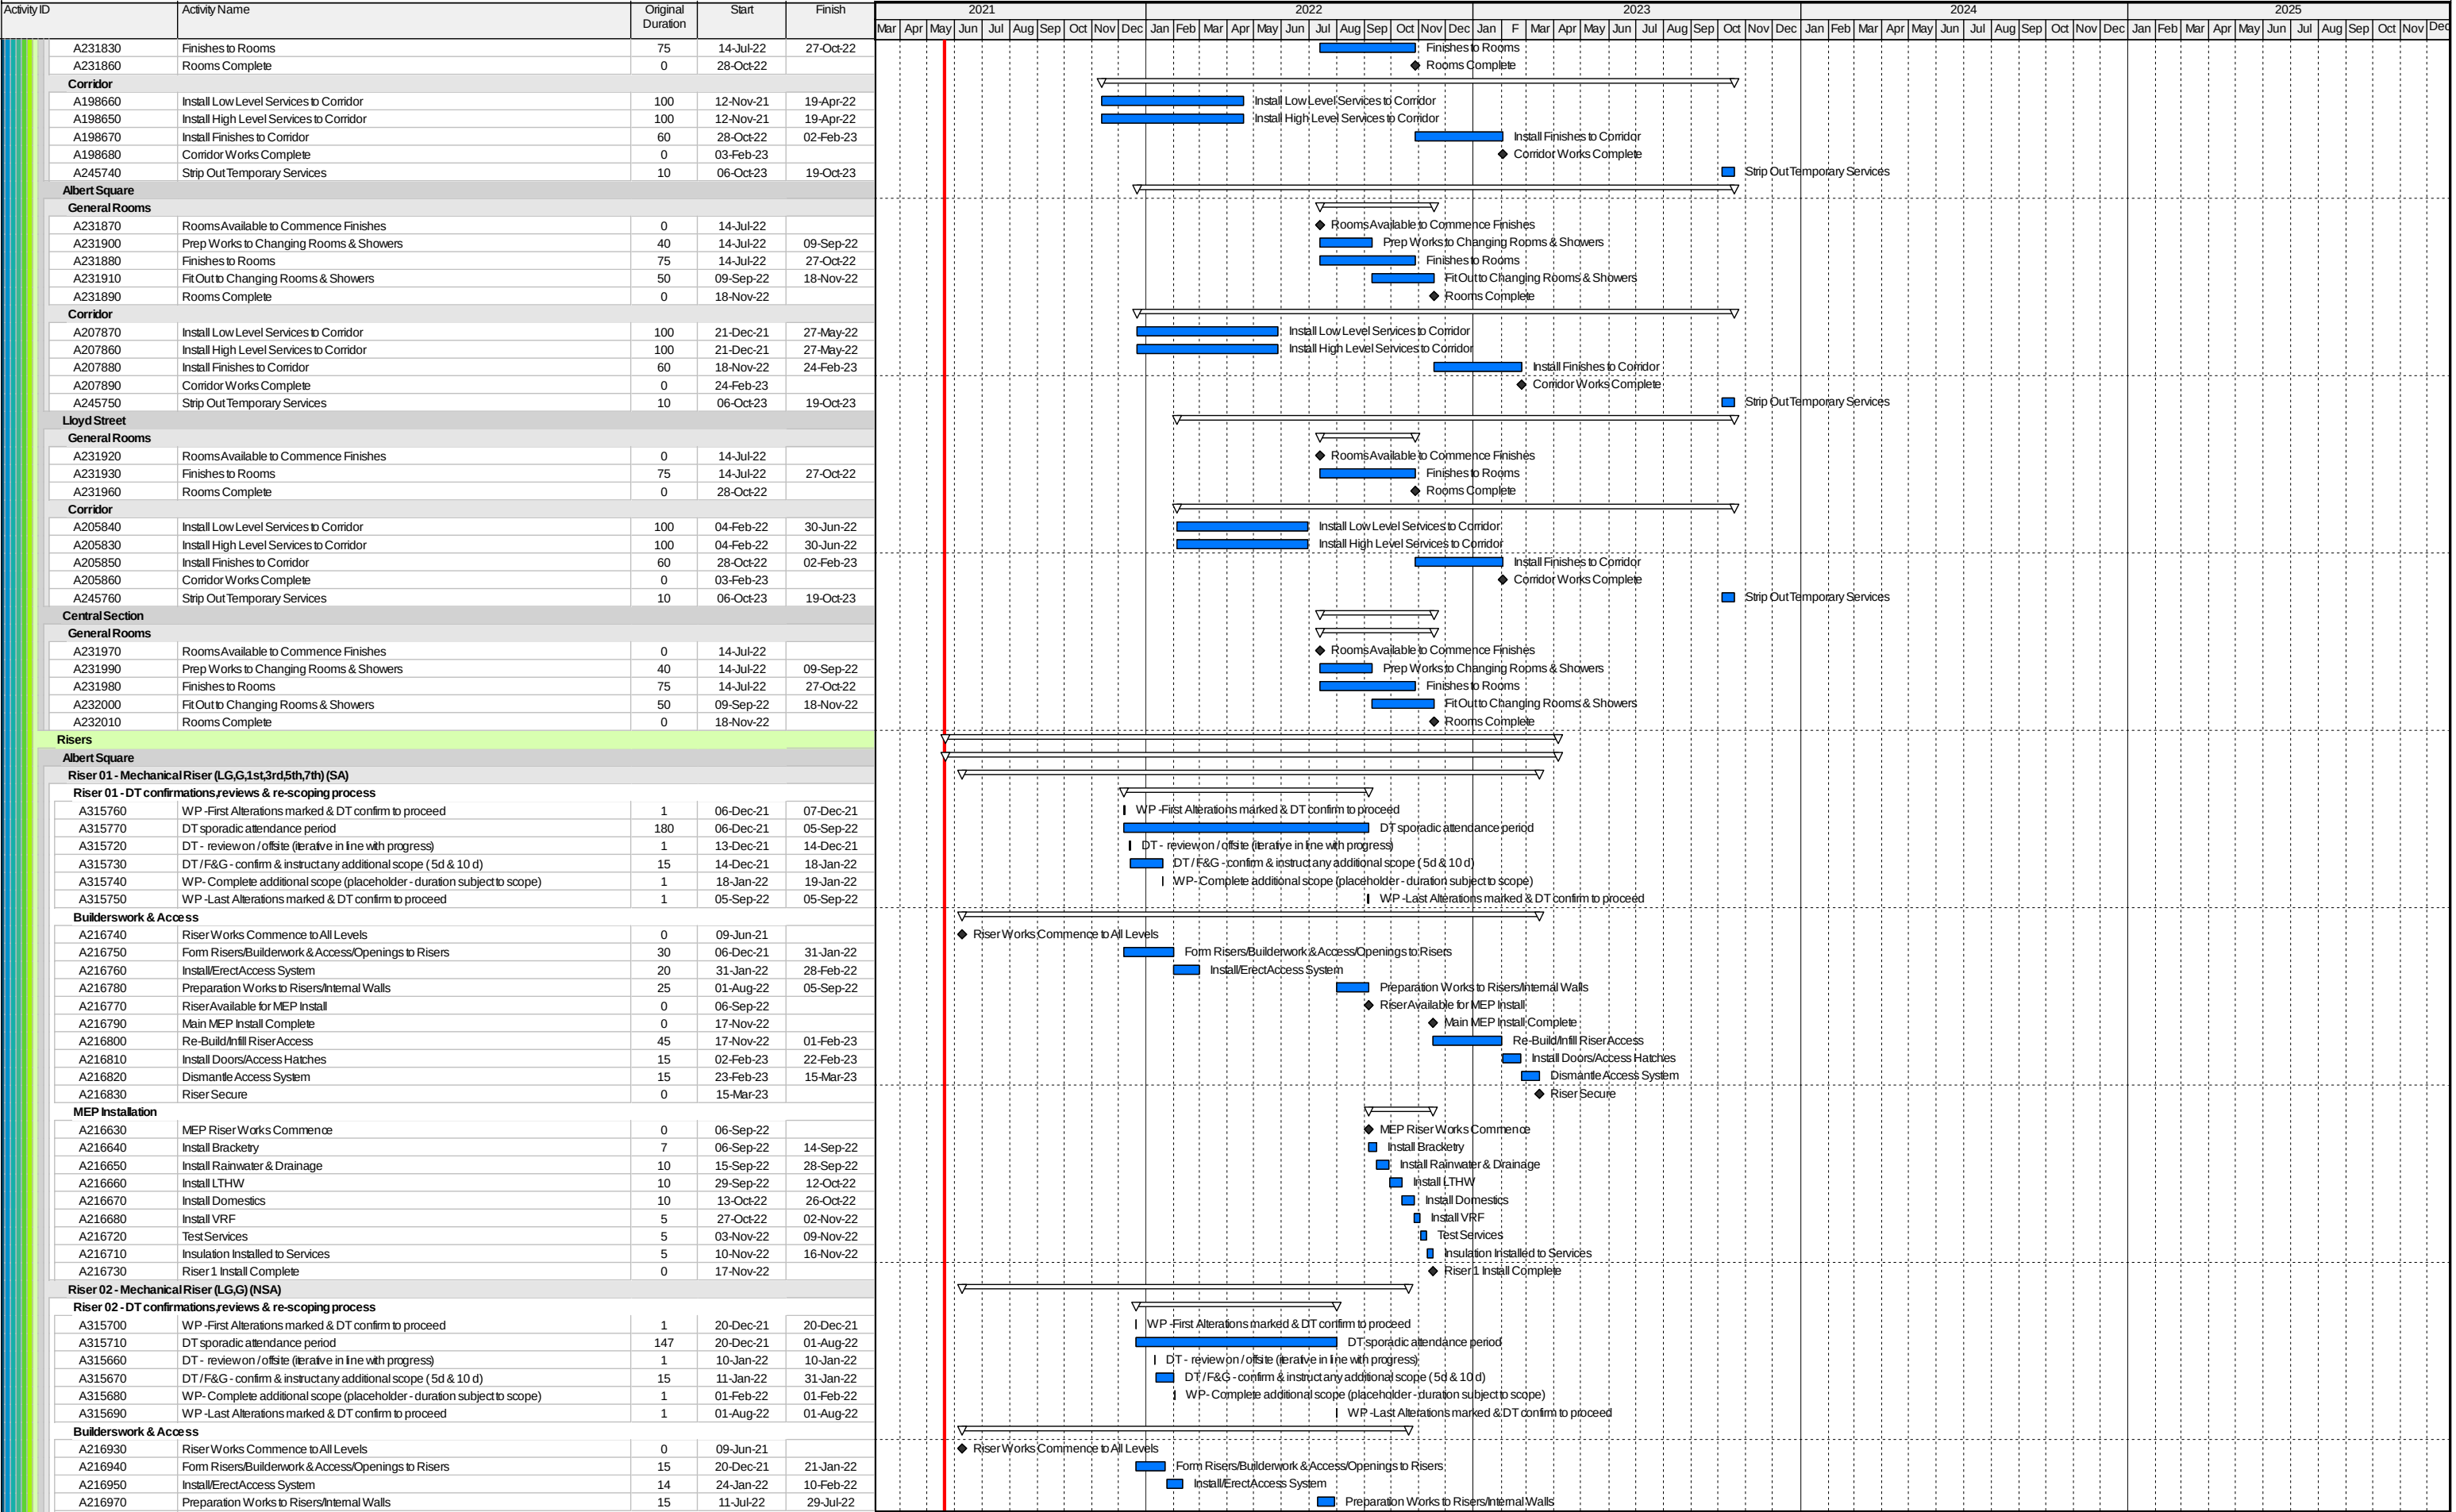

Intermittent Work Completed Work Remaining Work Critical Remaining Work	◆ Milestone ▽ Summary	<table><tr><th colspan="4">Programme Revision:</th></tr><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approv...</th></tr><tr><td>11-Jun-21</td><td>G19.2 - Accepted</td><td>RJH / ST</td><td>AM</td></tr><tr><td colspan="4"></td></tr></table>	Programme Revision:				Date	Revision	Checked	Approv...	11-Jun-21	G19.2 - Accepted	RJH / ST	AM					Delivery / Contract Programme	Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21) Layout: OTH - G19.2 General Layout [RJH] Data Date: 21-May-21 Print Date: 24-Aug-21	Page: 29 of 96
Programme Revision:																					
Date	Revision	Checked	Approv...																		
11-Jun-21	G19.2 - Accepted	RJH / ST	AM																		

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

30 of 96

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)


Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:
31 of 96

Our Town Hall Project : Programme G19.2 (ACCEPTED PROGRAMME)

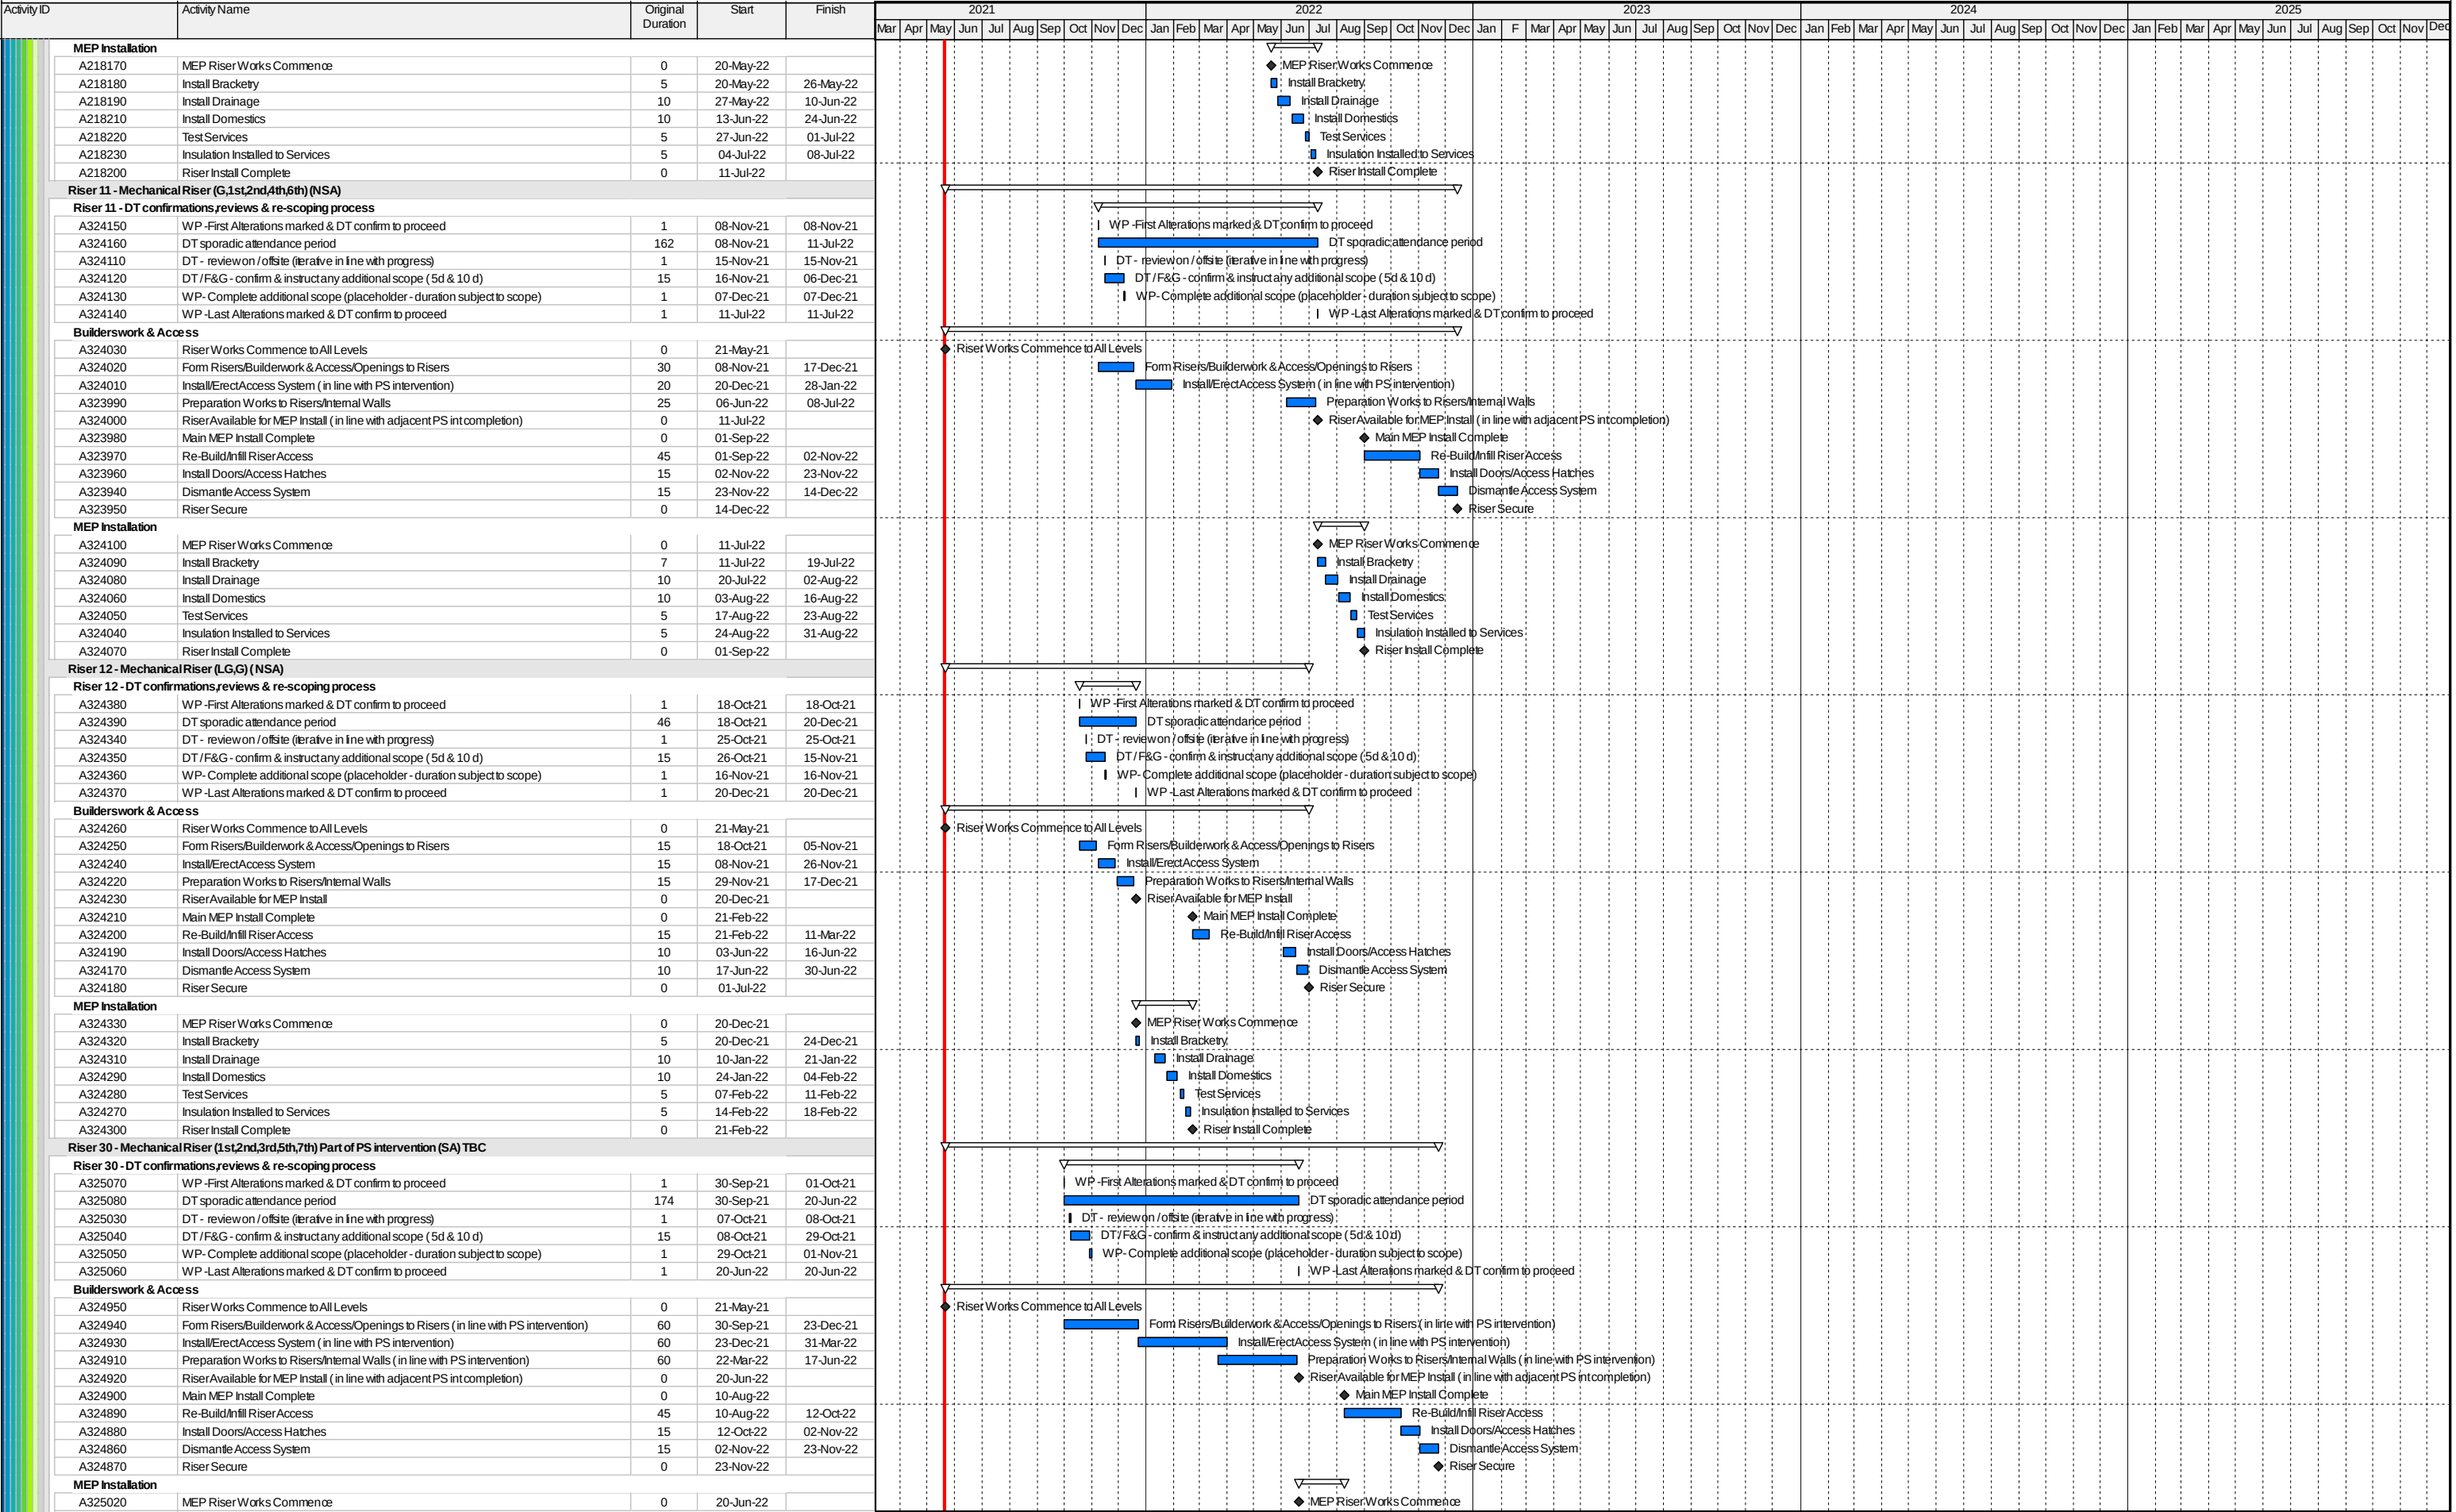

Intermittent Work Completed Work Remaining Work Critical Remaining Work	◆ Milestone ▽ Summary	<table><tr><th colspan="4">Programme Revision:</th></tr><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approv...</th></tr><tr><td>11-Jun-21</td><td>G19.2 - Accepted</td><td>RJH / ST</td><td>AM</td></tr><tr><td colspan="4"></td></tr></table>	Programme Revision:				Date	Revision	Checked	Approv...	11-Jun-21	G19.2 - Accepted	RJH / ST	AM					Delivery / Contract Programme	Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21) Layout: OTH - G19.2 General Layout [RJH] Data Date: 21-May-21 Print Date: 24-Aug-21	Page: 33 of 96
Programme Revision:																					
Date	Revision	Checked	Approv...																		
11-Jun-21	G19.2 - Accepted	RJH / ST	AM																		

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

34 of 96

Intermittent Work Completed Work Remaining Work Critical Remaining Work	◆ Milestone ▽ Summary	<table><tr><th colspan="4">Programme Revision:</th></tr><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approv...</th></tr><tr><td>11-Jun-21</td><td>G19.2 - Accepted</td><td>RJH / ST</td><td>AM</td></tr><tr><td colspan="4"></td></tr></table>	Programme Revision:				Date	Revision	Checked	Approv...	11-Jun-21	G19.2 - Accepted	RJH / ST	AM					Delivery / Contract Programme	Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21) Layout: OTH - G19.2 General Layout [RJH] Data Date: 21-May-21 Print Date: 24-Aug-21	Page: 35 of 96
Programme Revision:																					
Date	Revision	Checked	Approv...																		
11-Jun-21	G19.2 - Accepted	RJH / ST	AM																		

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Date

Revision

Checked

Approv...

11-Jun-21

G19.2 - Accepted

RJH / ST

AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

36 of 96

Intermittent Work Completed Work Remaining Work Critical Remaining Work ◆ Milestone ▽ Summary	<table border="1"> <tr> <th colspan="4">Programme Revision:</th> </tr> <tr> <th>Date</th> <th>Revision</th> <th>Checked</th> <th>Approv...</th> </tr> <tr> <td>11-Jun-21</td> <td>G19.2 - Accepted</td> <td>RJH / ST</td> <td>AM</td> </tr> </table>	Programme Revision:				Date	Revision	Checked	Approv...	11-Jun-21	G19.2 - Accepted	RJH / ST	AM	Delivery / Contract Programme Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21) Layout: OTH - G19.2 General Layout [RJH] Data Date: 21-May-21 Print Date: 24-Aug-21	Page: 37 of 96
Programme Revision:															
Date	Revision	Checked	Approv...												
11-Jun-21	G19.2 - Accepted	RJH / ST	AM												

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

38 of 96

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

39 of 96

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

40 of 96

Intermittent Work Completed Work Remaining Work Critical Remaining Work	◆ ◆ Milestone ▽ Summary	<table><tr><th colspan="4">Programme Revision:</th></tr><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approv...</th></tr><tr><td>11-Jun-21</td><td>G19.2 - Accepted</td><td>RJH / ST</td><td>AM</td></tr><tr><td colspan="4"></td></tr></table>	Programme Revision:				Date	Revision	Checked	Approv...	11-Jun-21	G19.2 - Accepted	RJH / ST	AM					Delivery / Contract Programme	Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21) Layout: OTH - G19.2 General Layout [RJH] Data Date: 21-May-21 Print Date: 24-Aug-21	Page: 41 of 96
Programme Revision:																					
Date	Revision	Checked	Approv...																		
11-Jun-21	G19.2 - Accepted	RJH / ST	AM																		

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:
42 of 96

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

43 of 96

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

44 of 96

Intermittent Work Completed Work Remaining Work Critical Remaining Work	◆ Milestone ▽ Summary	<table><tr><th colspan="4">Programme Revision:</th></tr><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approv...</th></tr><tr><td>11-Jun-21</td><td>G19.2 - Accepted</td><td>RJH / ST</td><td>AM</td></tr><tr><td colspan="4"></td></tr></table>	Programme Revision:				Date	Revision	Checked	Approv...	11-Jun-21	G19.2 - Accepted	RJH / ST	AM					Delivery / Contract Programme	Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21) Layout: OTH - G19.2 General Layout [RJH] Data Date: 21-May-21 Print Date: 24-Aug-21	Page: 45 of 96
Programme Revision:																					
Date	Revision	Checked	Approv...																		
11-Jun-21	G19.2 - Accepted	RJH / ST	AM																		

Intermittent Work Completed Work Remaining Work Critical Remaining Work	◆ Milestone ▽ Summary	<table><tr><th colspan="4">Programme Revision:</th></tr><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approv...</th></tr><tr><td>11-Jun-21</td><td>G19.2 - Accepted</td><td>RJH / ST</td><td>AM</td></tr><tr><td colspan="4"></td></tr></table>	Programme Revision:				Date	Revision	Checked	Approv...	11-Jun-21	G19.2 - Accepted	RJH / ST	AM					Delivery / Contract Programme	Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21) Layout: OTH - G19.2 General Layout [RJH] Data Date: 21-May-21 Print Date: 24-Aug-21	Page: 46 of 96
Programme Revision:																					
Date	Revision	Checked	Approv...																		
11-Jun-21	G19.2 - Accepted	RJH / ST	AM																		

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]


Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

47 of 96

Our Town Hall Project : Programme G19.2 (ACCEPTED PROGRAMME)

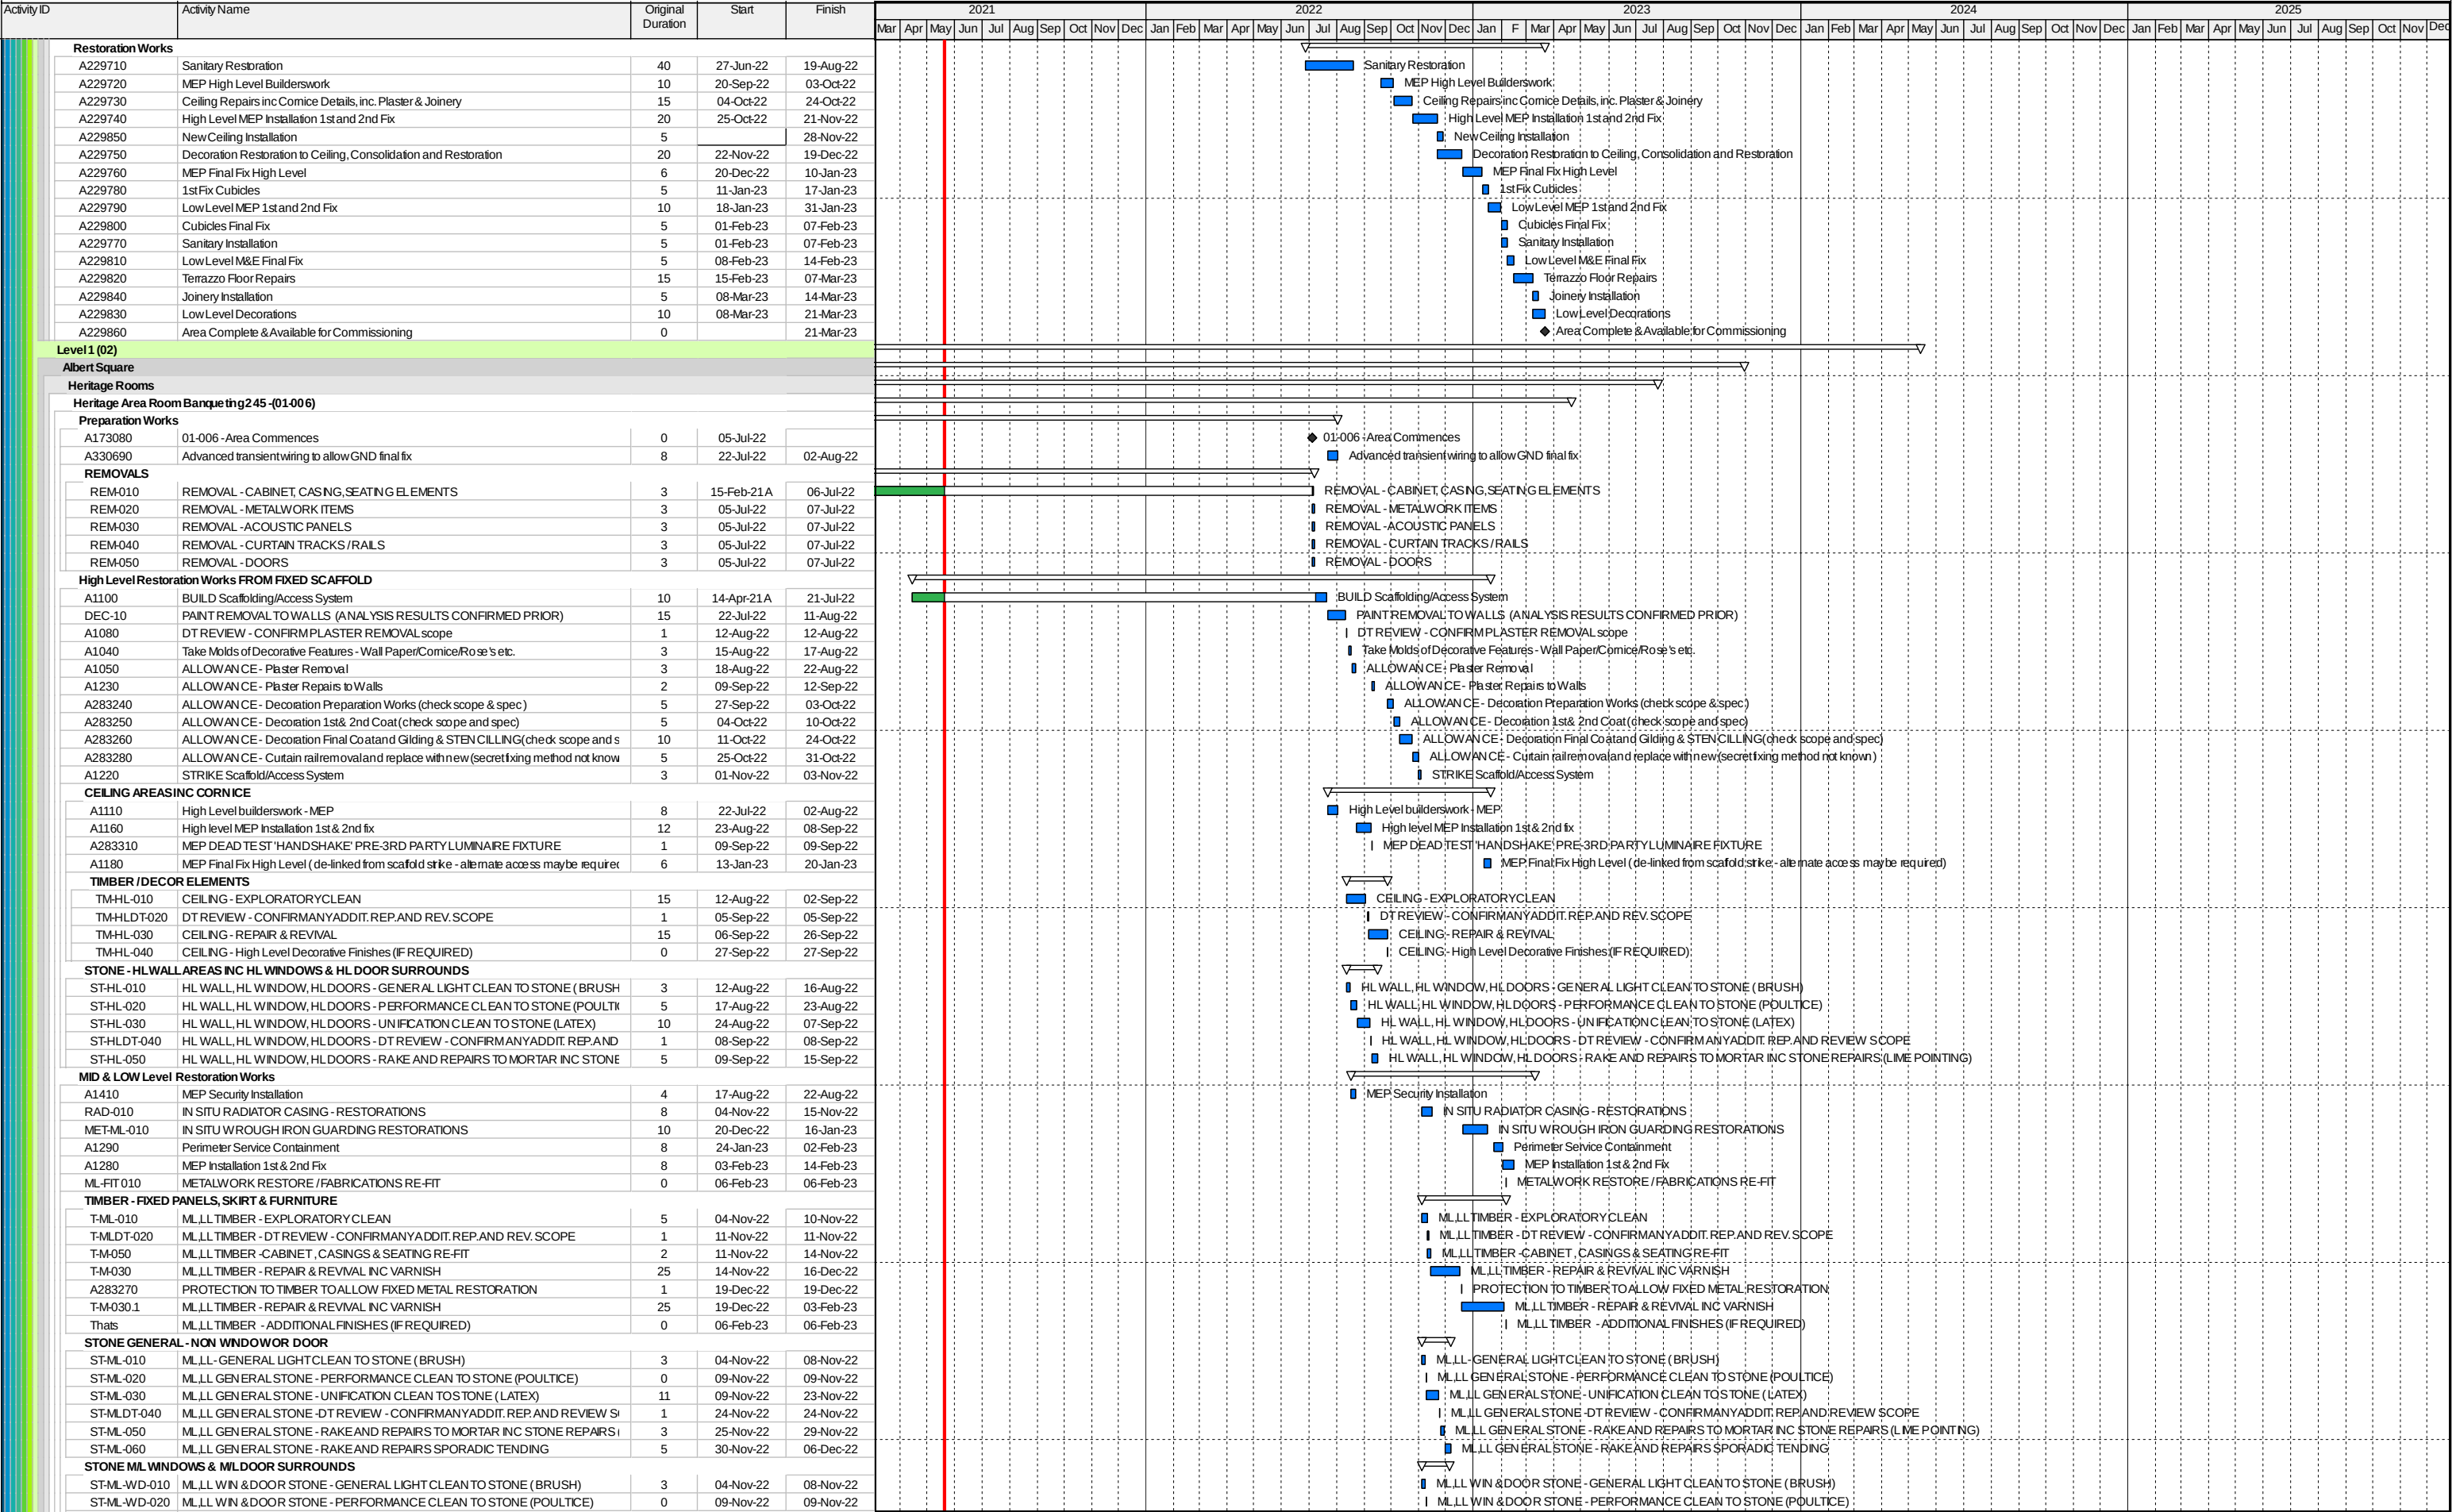

Our Town Hall Project : Programme G19.2 (ACCEPTED PROGRAMME)

[illegible]

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

50 of 96

Intermittent Work Completed Work Remaining Work Critical Remaining Work ◆ ◆ Milestone ▽ Summary	<table border="1"> <tr> <th colspan="4">Programme Revision:</th> </tr> <tr> <th>Date</th> <th>Revision</th> <th>Checked</th> <th>Approv...</th> </tr> <tr> <td>11-Jun-21</td> <td>G19.2 - Accepted</td> <td>RJH / ST</td> <td>AM</td> </tr> </table>	Programme Revision:				Date	Revision	Checked	Approv...	11-Jun-21	G19.2 - Accepted	RJH / ST	AM	Delivery / Contract Programme Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21) Layout: OTH - G19.2 General Layout [RJH] Data Date: 21-May-21 Print Date: 24-Aug-21	Page: 51 of 96
Programme Revision:															
Date	Revision	Checked	Approv...												
11-Jun-21	G19.2 - Accepted	RJH / ST	AM												

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:

Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

52 of 96

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID:

UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout:

OTH - G19.2 General Layout [RJH]

Data Date:

21-May-21

Print Date:

24-Aug-21

Page:

53 of 96

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21


Print Date: 24-Aug-21

Page:

54 of 96

Intermittent Work Completed Work Remaining Work Critical Remaining Work	◆ Milestone ▽ Summary	<table><tr><th colspan="4">Programme Revision:</th></tr><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approv...</th></tr><tr><td>11-Jun-21</td><td>G19.2 - Accepted</td><td>RJH / ST</td><td>AM</td></tr><tr><td colspan="4"></td></tr></table>	Programme Revision:				Date	Revision	Checked	Approv...	11-Jun-21	G19.2 - Accepted	RJH / ST	AM					Delivery / Contract Programme	Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21) Layout: OTH - G19.2 General Layout [RJH] Data Date: 21-May-21 Print Date: 24-Aug-21	Page: 55 of 96
Programme Revision:																					
Date	Revision	Checked	Approv...																		
11-Jun-21	G19.2 - Accepted	RJH / ST	AM																		

Our Town Hall Project : Programme G19.2 (ACCEPTED PROGRAMME)

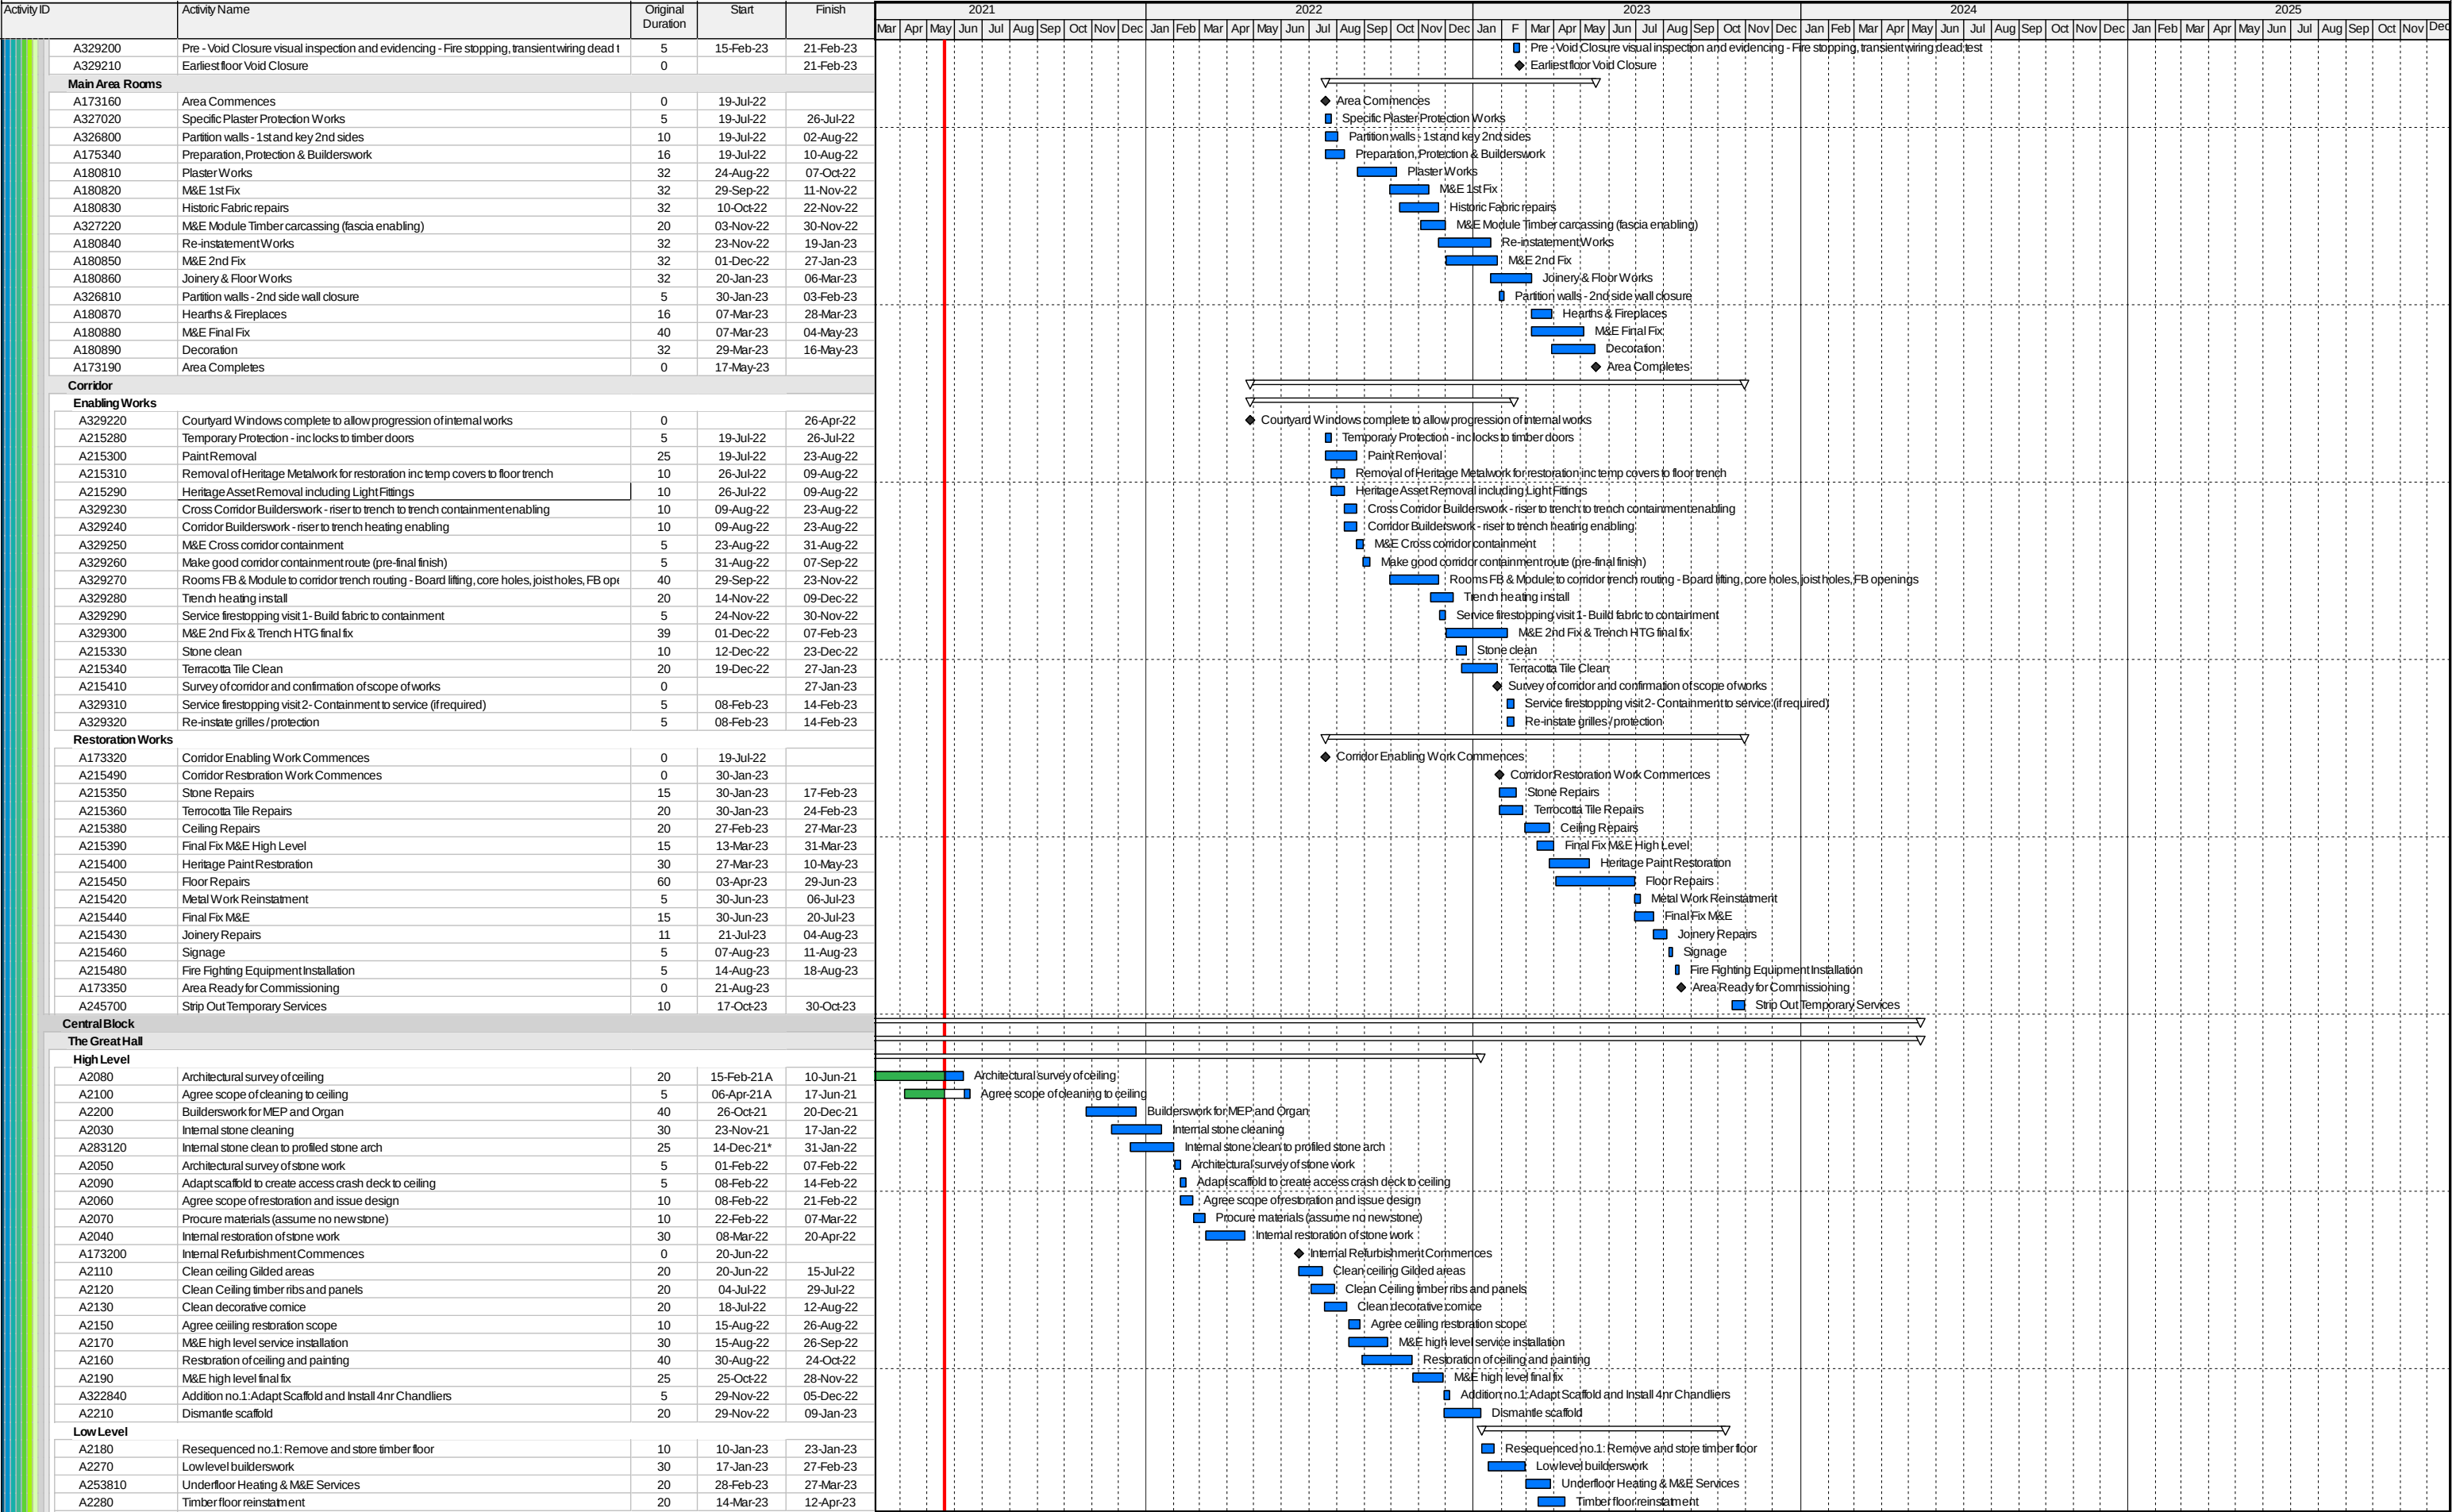

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

57 of 96

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID:

UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout:

OTH - G19.2 General Layout [RJH]

Data Date:

21-May-21

Print Date:

24-Aug-21

Page:

58 of 96

Intermittent Work Completed Work Remaining Work Critical Remaining Work Milestone Summary	<table border="1"> <tr> <th colspan="4">Programme Revision:</th> </tr> <tr> <th>Date</th> <th>Revision</th> <th>Checked</th> <th>Approv...</th> </tr> <tr> <td>11-Jun-21</td> <td>G19.2 - Accepted</td> <td>RJH / ST</td> <td>AM</td> </tr> <tr> <td colspan="4"> </td> </tr> </table>	Programme Revision:				Date	Revision	Checked	Approv...	11-Jun-21	G19.2 - Accepted	RJH / ST	AM					Delivery / Contract Programme	Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21) Layout: OTH - G19.2 General Layout [RJH] Data Date: 21-May-21 Print Date: 24-Aug-21 Page: 59 of 96
Programme Revision:																			
Date	Revision	Checked	Approv...																
11-Jun-21	G19.2 - Accepted	RJH / ST	AM																

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

60 of 96

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

61 of 96

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

62 of 96

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

63 of 96

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

◆

Milestone

↔

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID:

UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout:

OTH - G19.2 General Layout [RJH]

Data Date:

21-May-21

Print Date:

24-Aug-21

Page:

64 of 96

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

65 of 96

Intermittent Work Completed Work Remaining Work Critical Remaining Work	◆ Milestone ▽ Summary	<table><tr><th colspan="4">Programme Revision:</th></tr><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approv...</th></tr><tr><td>11-Jun-21</td><td>G19.2 - Accepted</td><td>RJH / ST</td><td>AM</td></tr><tr><td colspan="4"></td></tr></table>	Programme Revision:				Date	Revision	Checked	Approv...	11-Jun-21	G19.2 - Accepted	RJH / ST	AM					Delivery / Contract Programme	Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21) Layout: OTH - G19.2 General Layout [RJH] Data Date: 21-May-21 Print Date: 24-Aug-21	Page: 66 of 96
Programme Revision:																					
Date	Revision	Checked	Approv...																		
11-Jun-21	G19.2 - Accepted	RJH / ST	AM																		

Intermittent Work Completed Work Remaining Work Critical Remaining Work	◆ ◆ Milestone ▽ Summary	<table><tr><th colspan="4">Programme Revision:</th></tr><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approv...</th></tr><tr><td>11-Jun-21</td><td>G19.2 - Accepted</td><td>RJH / ST</td><td>AM</td></tr><tr><td colspan="4"></td></tr></table>	Programme Revision:				Date	Revision	Checked	Approv...	11-Jun-21	G19.2 - Accepted	RJH / ST	AM					Delivery / Contract Programme	Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21) Layout: OTH - G19.2 General Layout [RJH] Data Date: 21-May-21 Print Date: 24-Aug-21	Page: 67 of 96
Programme Revision:																					
Date	Revision	Checked	Approv...																		
11-Jun-21	G19.2 - Accepted	RJH / ST	AM																		

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

◆ Milestone

▽ Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page: 68 of 96

Intermittent Work Completed Work Remaining Work Critical Remaining Work	◆ Milestone ▽ Summary	<table><tr><th colspan="4">Programme Revision:</th></tr><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approv...</th></tr><tr><td>11-Jun-21</td><td>G19.2 - Accepted</td><td>RJH / ST</td><td>AM</td></tr><tr><td colspan="4"></td></tr></table>	Programme Revision:				Date	Revision	Checked	Approv...	11-Jun-21	G19.2 - Accepted	RJH / ST	AM					Delivery / Contract Programme	Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21) Layout: OTH - G19.2 General Layout [RJH] Data Date: 21-May-21 Print Date: 24-Aug-21	Page: 69 of 96
Programme Revision:																					
Date	Revision	Checked	Approv...																		
11-Jun-21	G19.2 - Accepted	RJH / ST	AM																		

Intermittent Work Completed Work Remaining Work Critical Remaining Work	◆ Milestone ▽ Summary	<table><tr><th colspan="4">Programme Revision:</th></tr><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approv...</th></tr><tr><td>11-Jun-21</td><td>G19.2 - Accepted</td><td>RJH / ST</td><td>AM</td></tr><tr><td colspan="4"></td></tr></table>	Programme Revision:				Date	Revision	Checked	Approv...	11-Jun-21	G19.2 - Accepted	RJH / ST	AM					Delivery / Contract Programme	Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21) Layout: OTH - G19.2 General Layout [RJH] Data Date: 21-May-21 Print Date: 24-Aug-21	Page: 70 of 96
Programme Revision:																					
Date	Revision	Checked	Approv...																		
11-Jun-21	G19.2 - Accepted	RJH / ST	AM																		

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]


Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

71 of 96

Our Town Hall Project : Programme G19.2 (ACCEPTED PROGRAMME)

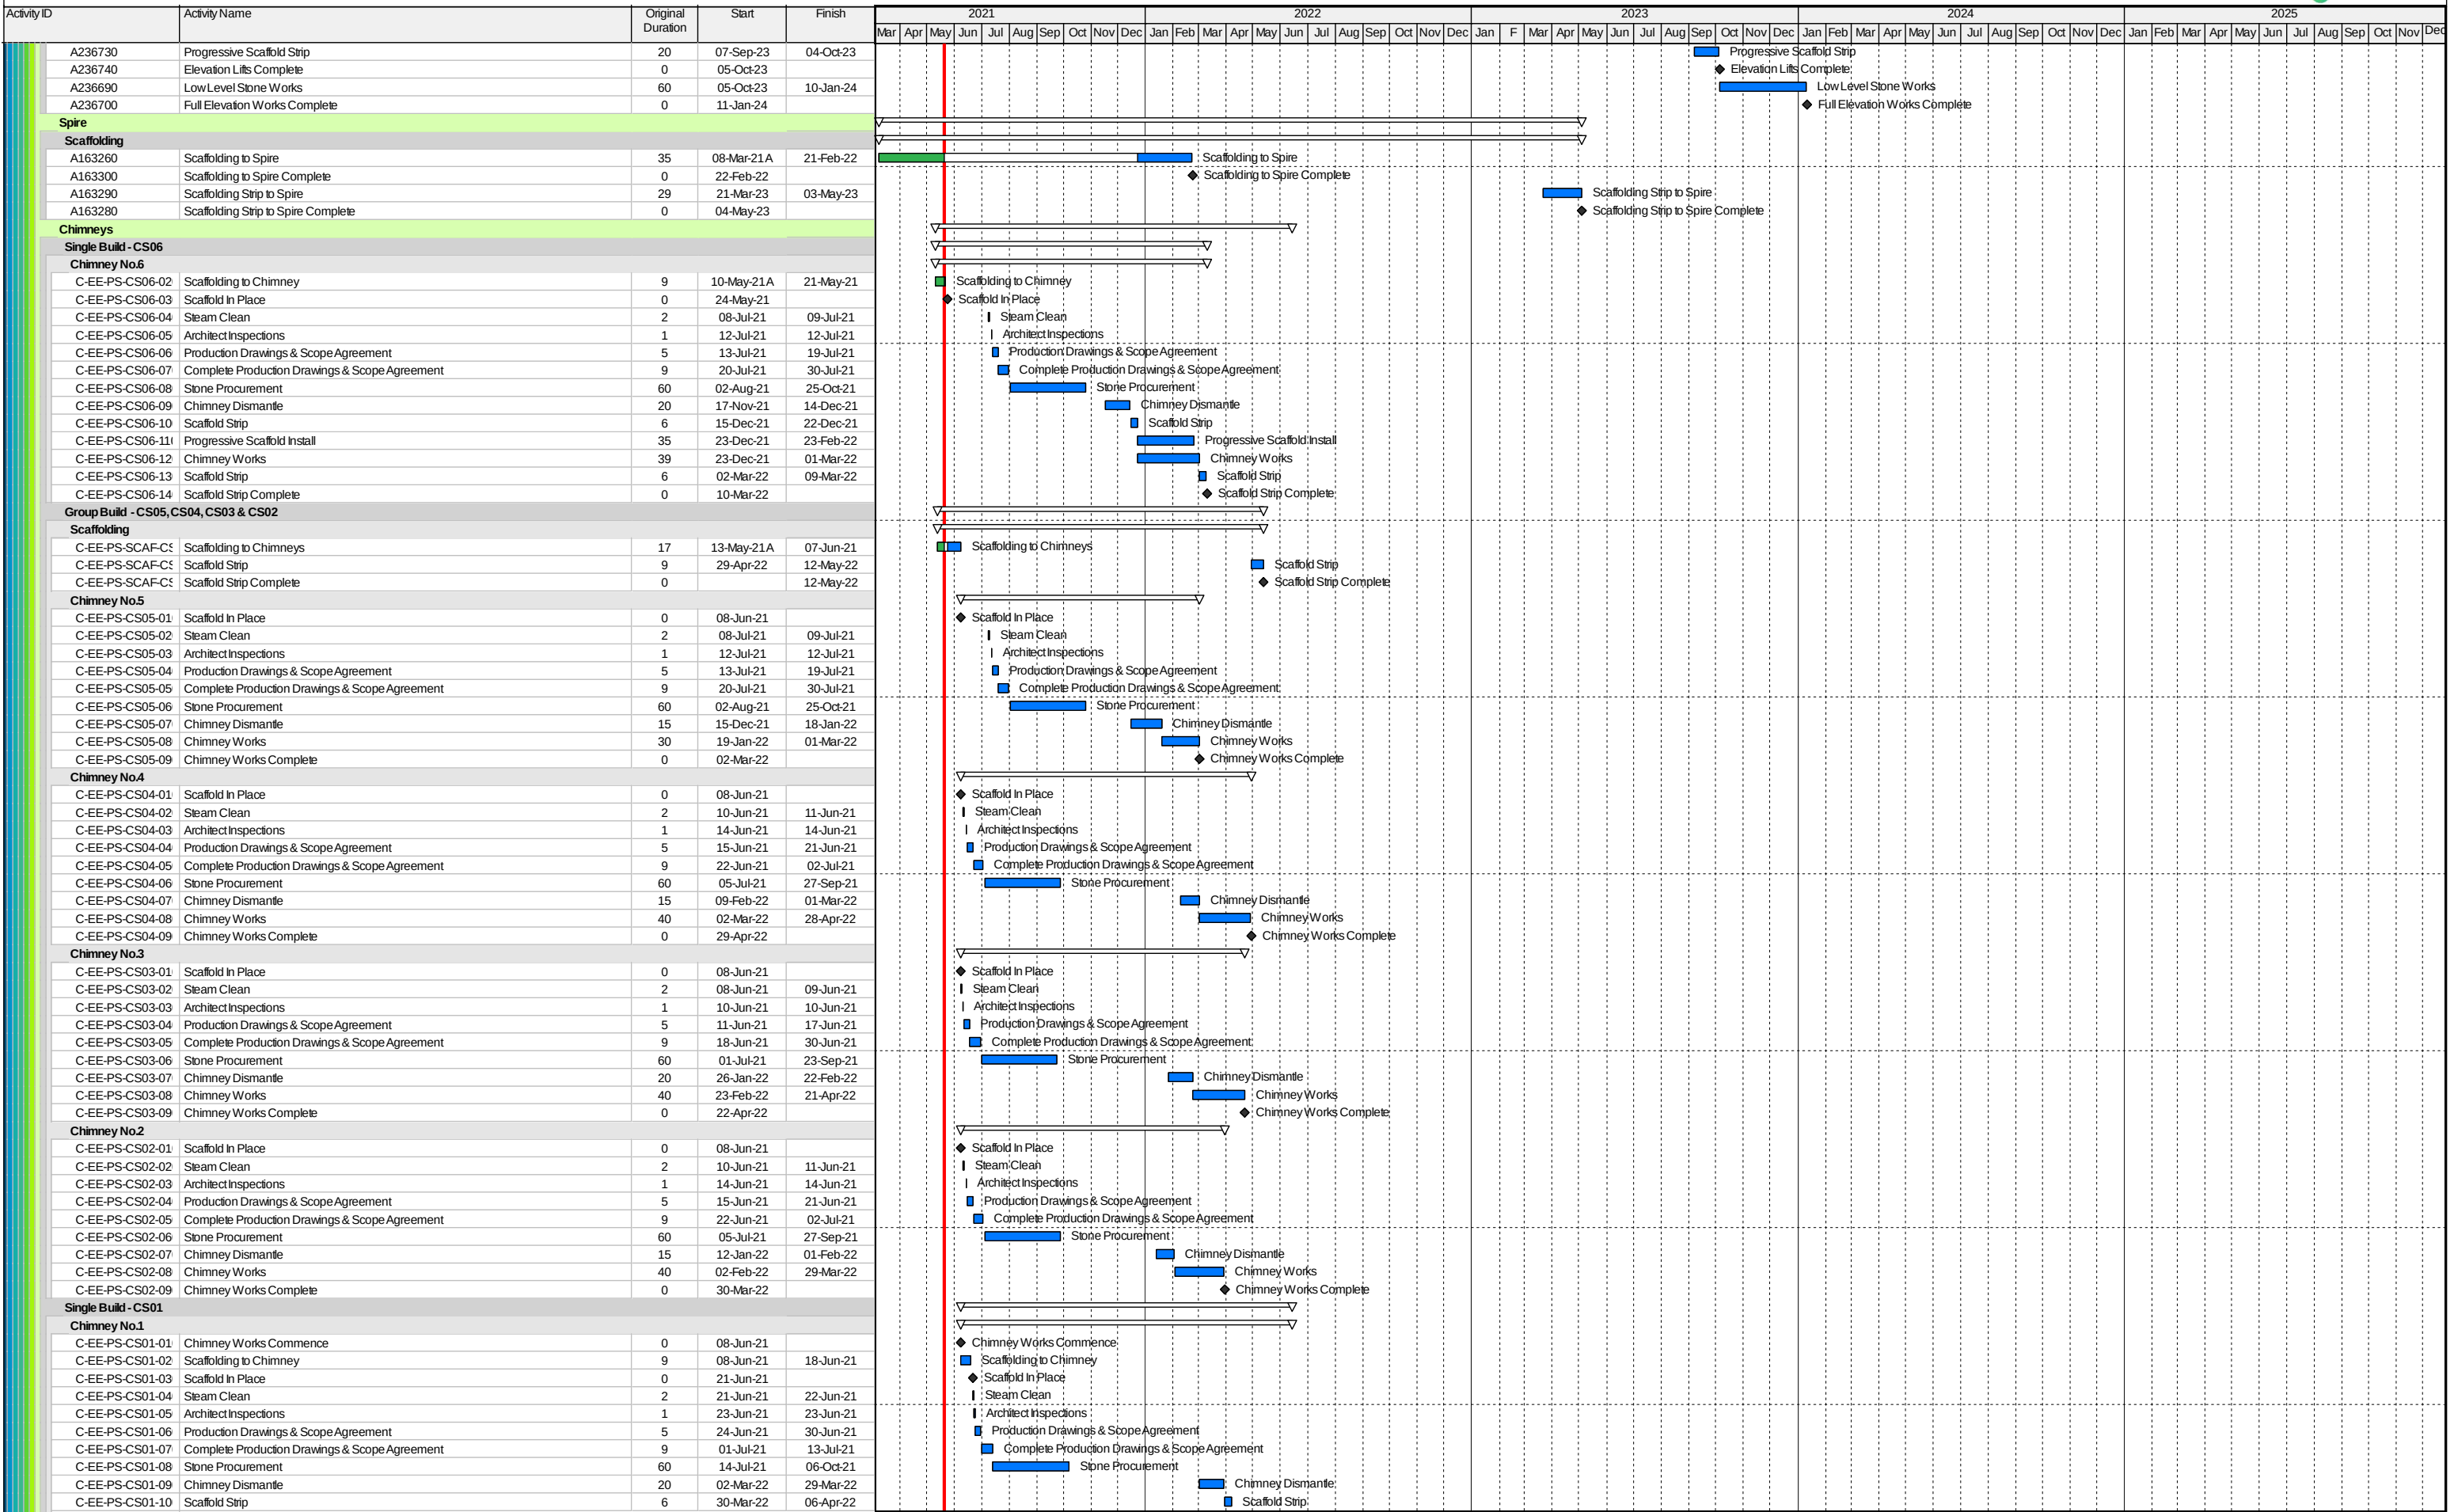

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

◆

Milestone

↔

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID:

UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout:

OTH - G19.2 General Layout [RJH]

Data Date:

21-May-21


Print Date:

24-Aug-21


Page:

73 of 96

Our Town Hall Project : Programme G19.2 (ACCEPTED PROGRAMME)

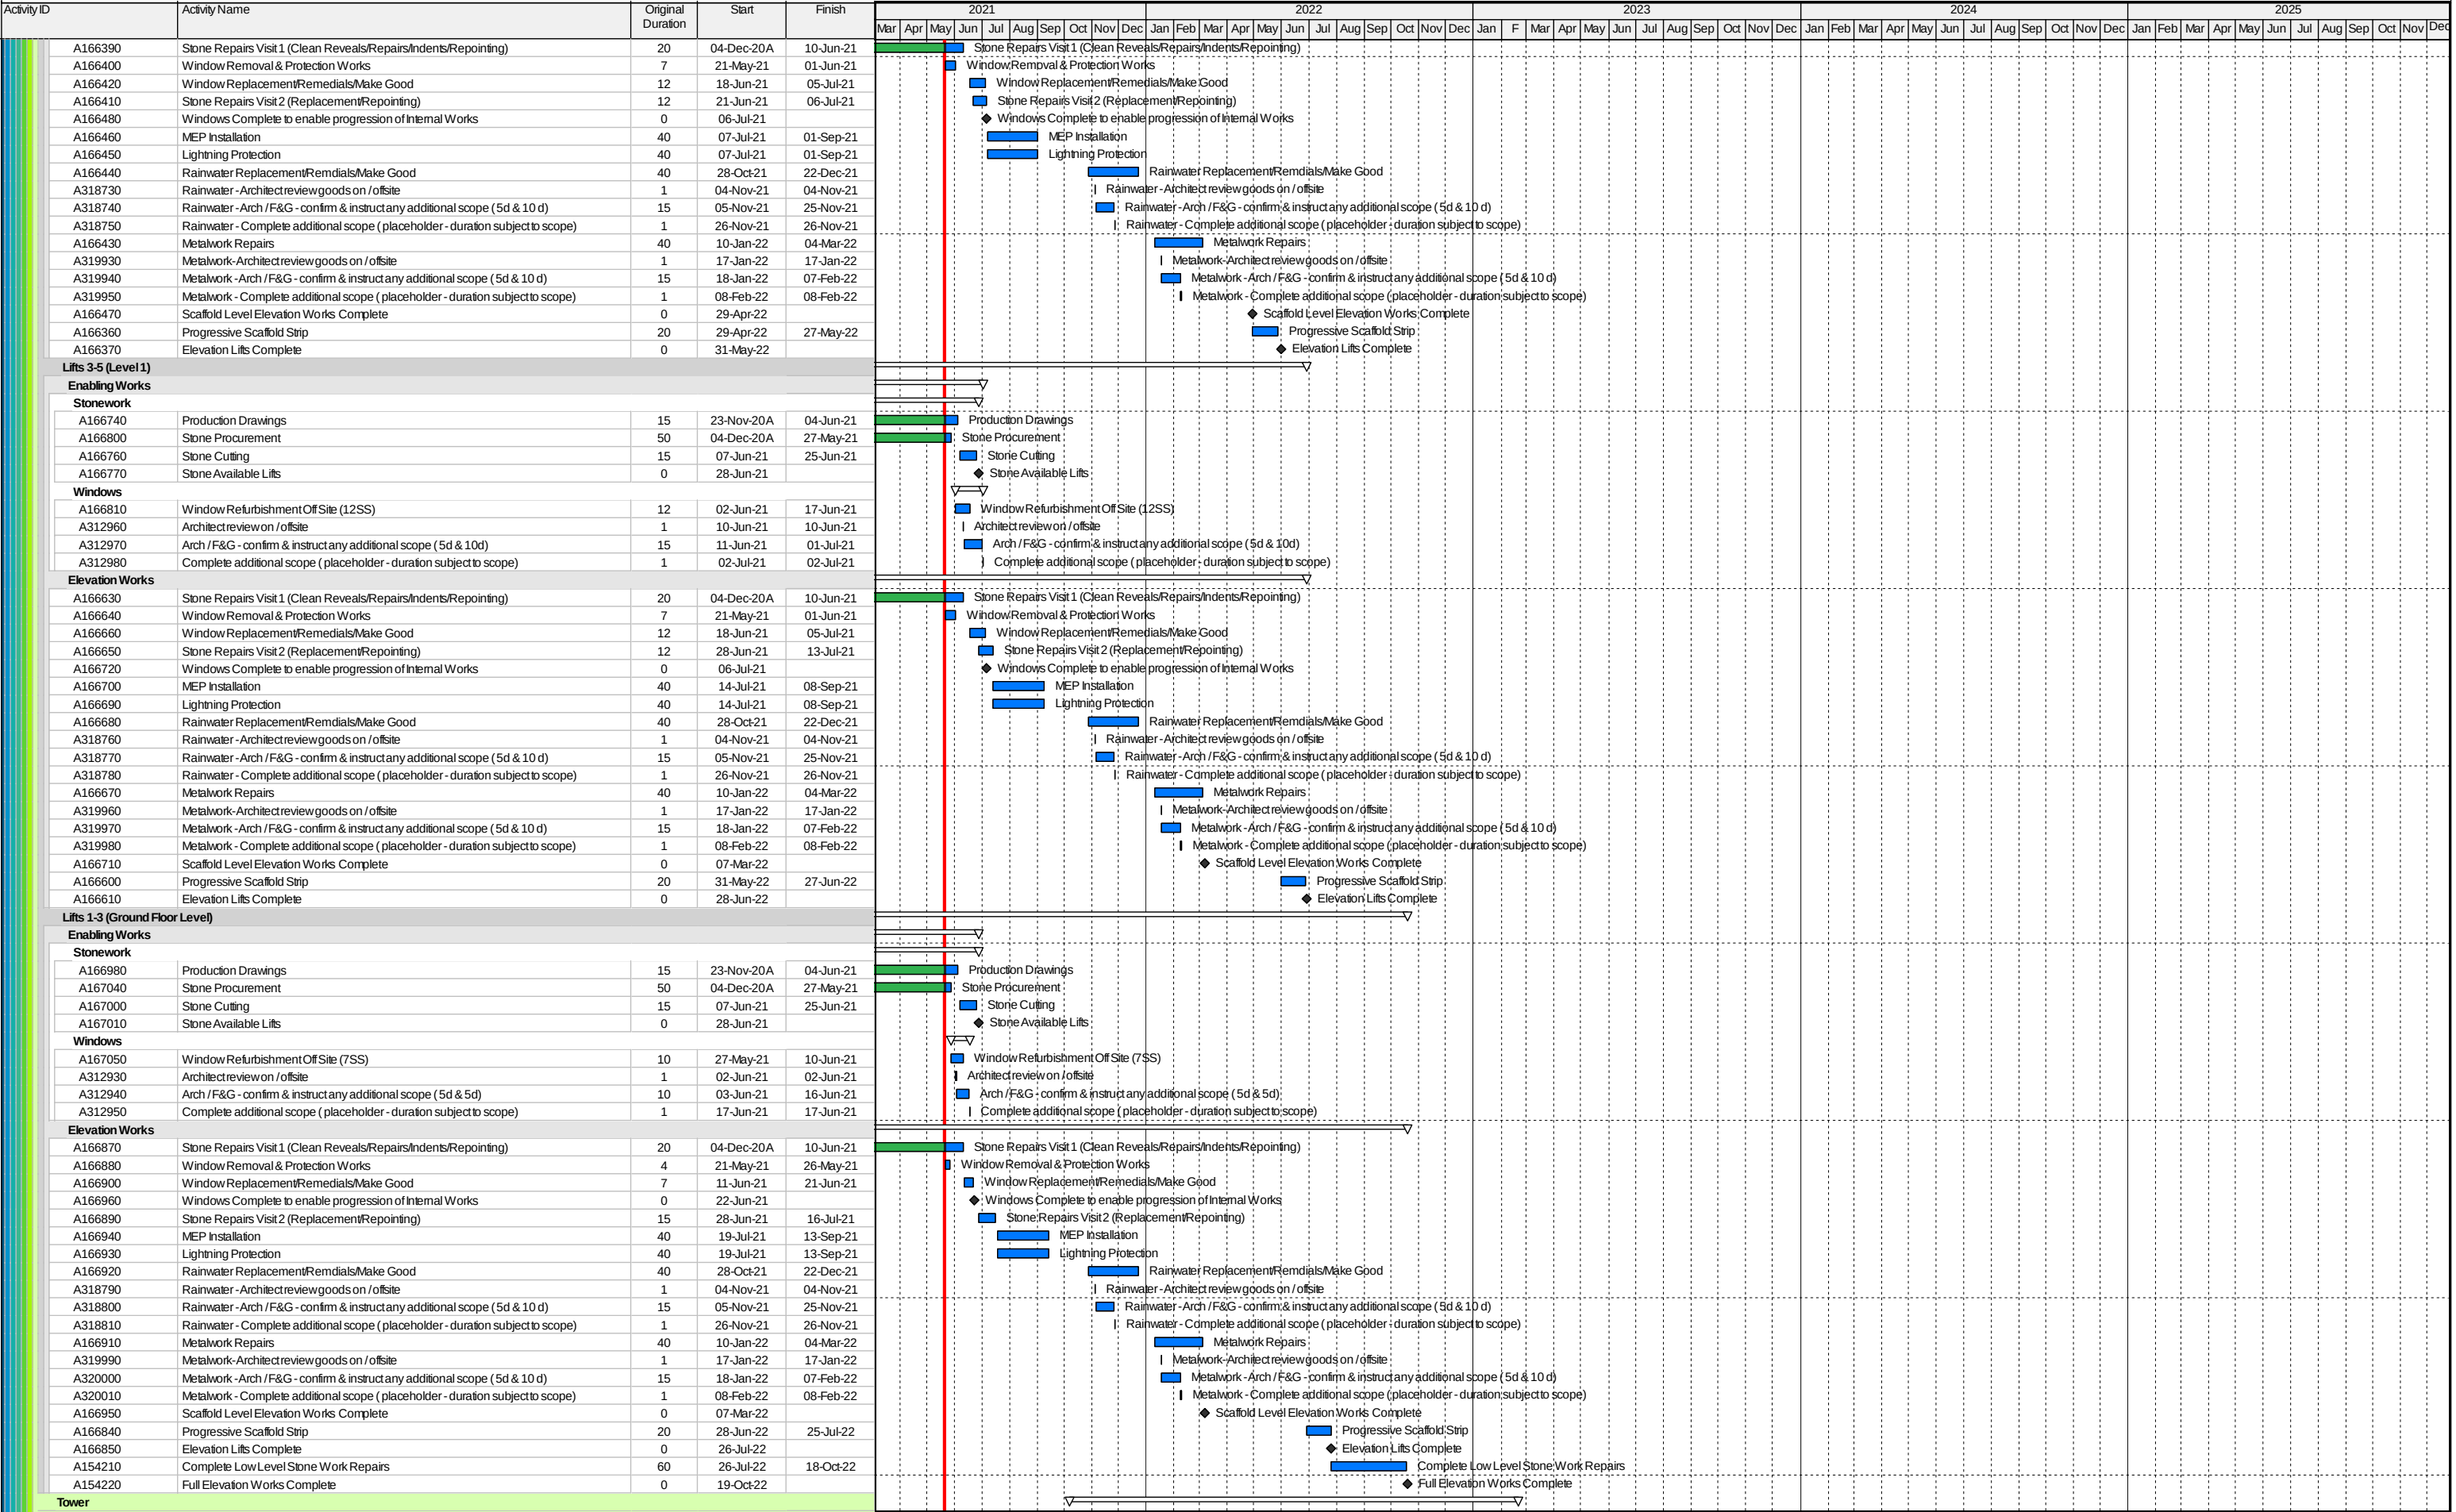

Our Town Hall Project : Programme G19.2 (ACCEPTED PROGRAMME)

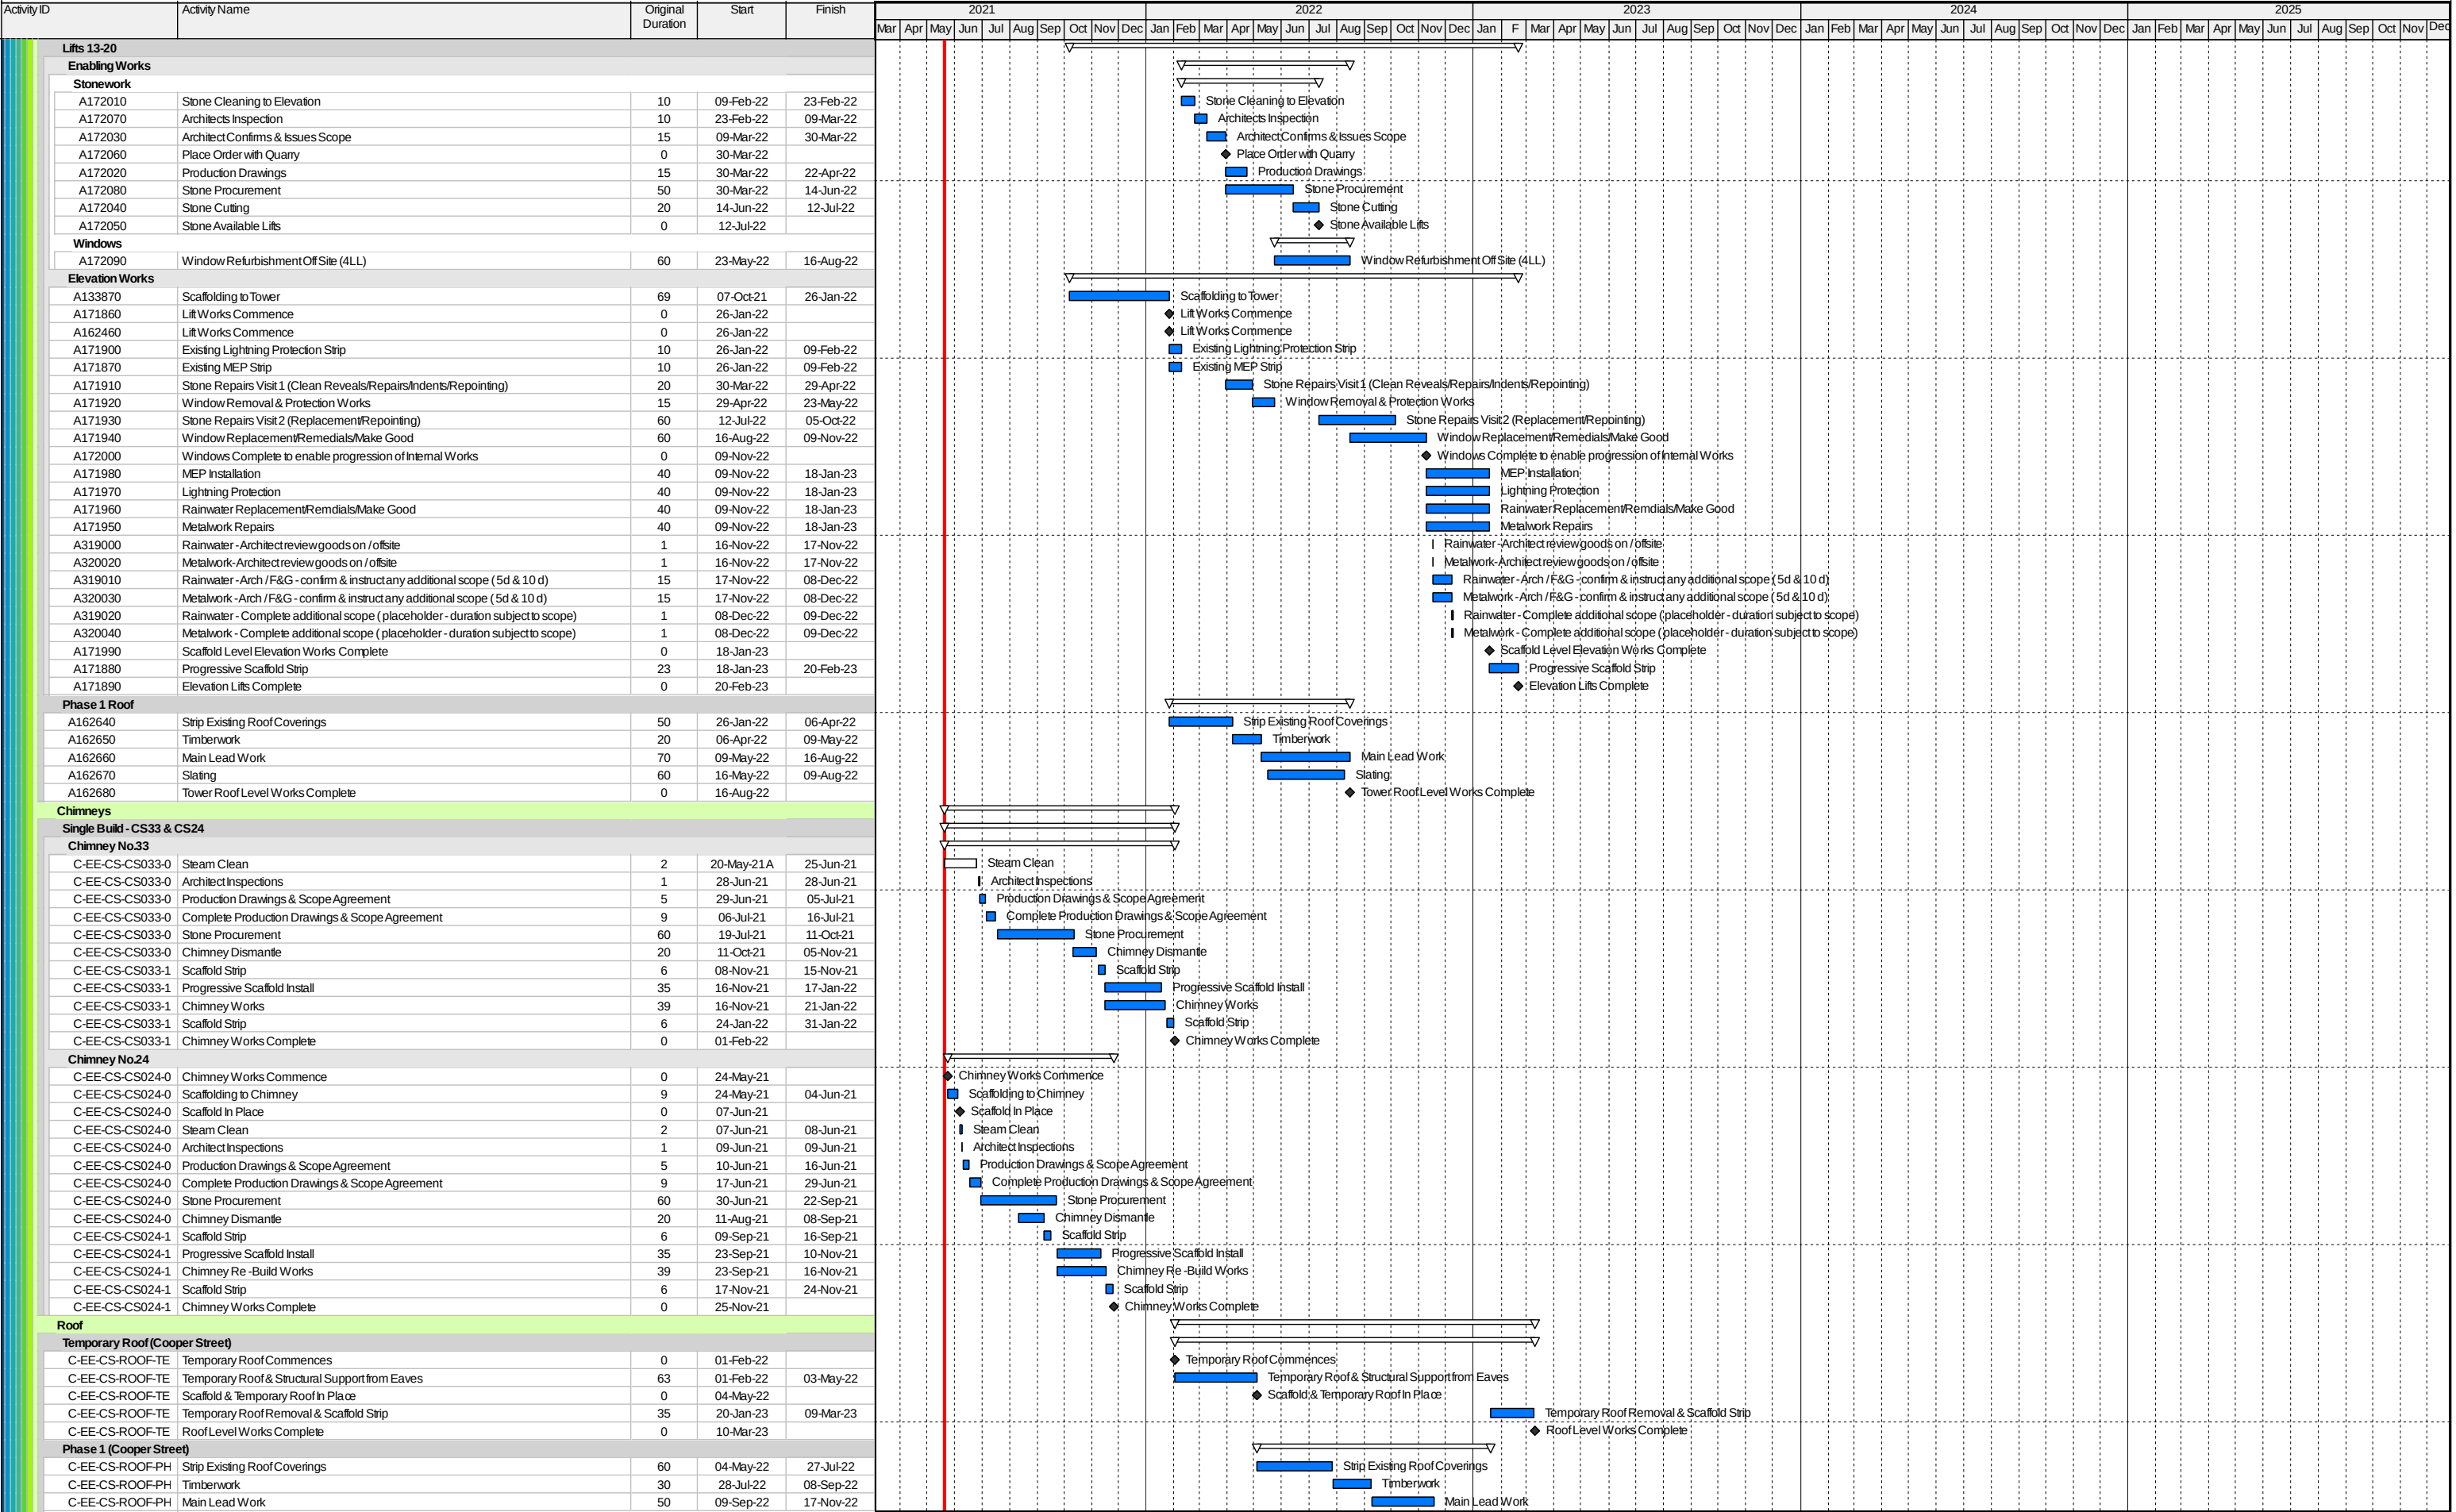

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

76 of 96

Intermittent Work Completed Work Remaining Work Critical Remaining Work	◆ Milestone ↔ Summary	<table><tr><th colspan="4">Programme Revision:</th></tr><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approv...</th></tr><tr><td>11-Jun-21</td><td>G19.2 - Accepted</td><td>RJH / ST</td><td>AM</td></tr><tr><td colspan="4"></td></tr></table>	Programme Revision:				Date	Revision	Checked	Approv...	11-Jun-21	G19.2 - Accepted	RJH / ST	AM					Delivery / Contract Programme	Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21) Layout: OTH - G19.2 General Layout [RJH] Data Date: 21-May-21 Print Date: 24-Aug-21	Page: 77 of 96
Programme Revision:																					
Date	Revision	Checked	Approv...																		
11-Jun-21	G19.2 - Accepted	RJH / ST	AM																		

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]


Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

78 of 96

Our Town Hall Project : Programme G19.2 (ACCEPTED PROGRAMME)

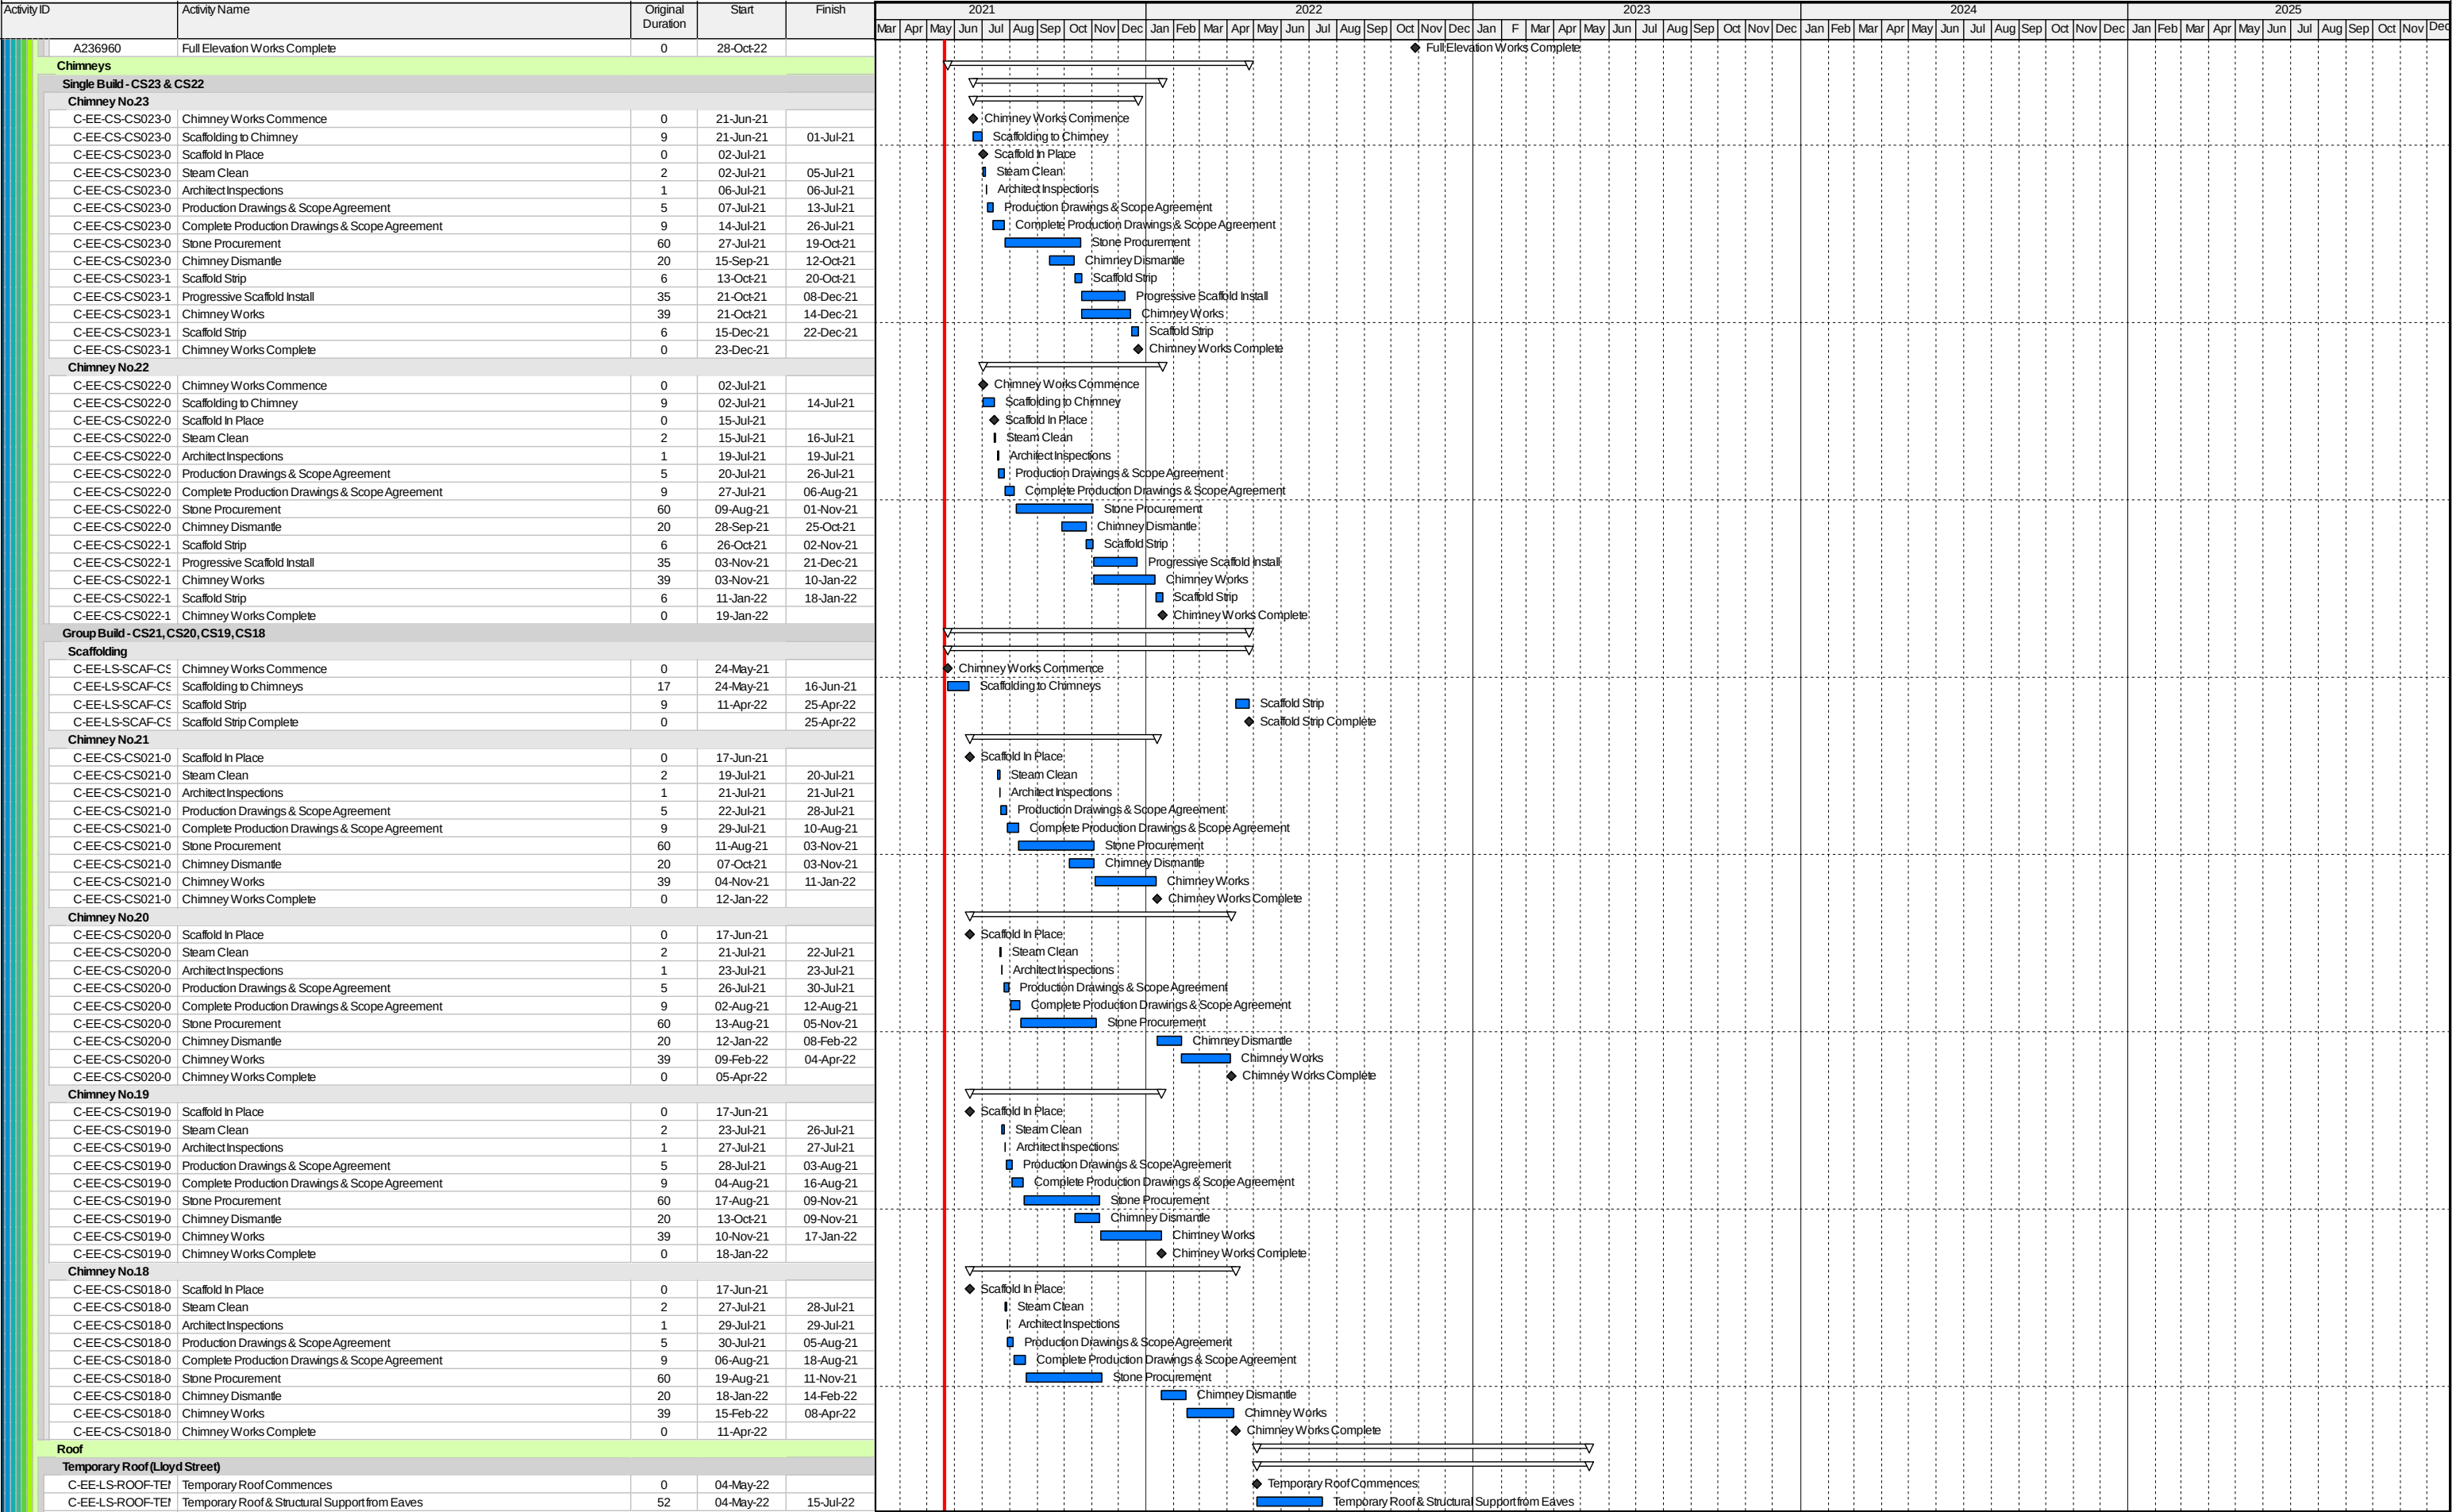

Intermittent Work Completed Work Remaining Work Critical Remaining Work	◆ ◆ Milestone ▽ Summary	<table><tr><th colspan="4">Programme Revision:</th></tr><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approv...</th></tr><tr><td>11-Jun-21</td><td>G19.2 - Accepted</td><td>RJH / ST</td><td>AM</td></tr></table>	Programme Revision:				Date	Revision	Checked	Approv...	11-Jun-21	G19.2 - Accepted	RJH / ST	AM	Delivery / Contract Programme	Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21) Layout: OTH - G19.2 General Layout [RJH] Data Date: 21-May-21 Print Date: 24-Aug-21	Page: 80 of 96
Programme Revision:																	
Date	Revision	Checked	Approv...														
11-Jun-21	G19.2 - Accepted	RJH / ST	AM														

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

◆

Milestone

▽

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID:

UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout:

OTH - G19.2 General Layout [RJH]

Data Date:

21-May-21

Print Date:

24-Aug-21

Page:

81 of 96

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

82 of 96

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

◆

Milestone

▽

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID:

UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout:

OTH - G19.2 General Layout [RJH]

Data Date:

21-May-21

Print Date:


24-Aug-21

Page:

83 of 96

Intermittent Work Completed Work Remaining Work Critical Remaining Work	◆ Milestone ▽ Summary	<table><tr><th colspan="4">Programme Revision:</th></tr><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approv...</th></tr><tr><td>11-Jun-21</td><td>G19.2 - Accepted</td><td>RJH / ST</td><td>AM</td></tr></table>	Programme Revision:				Date	Revision	Checked	Approv...	11-Jun-21	G19.2 - Accepted	RJH / ST	AM	Delivery / Contract Programme	Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21) Layout: OTH - G19.2 General Layout [RJH] Data Date: 21-May-21 Print Date: 24-Aug-21	Page: 84 of 96
Programme Revision:																	
Date	Revision	Checked	Approv...														
11-Jun-21	G19.2 - Accepted	RJH / ST	AM														

Our Town Hall Project : Programme G19.2 (ACCEPTED PROGRAMME)

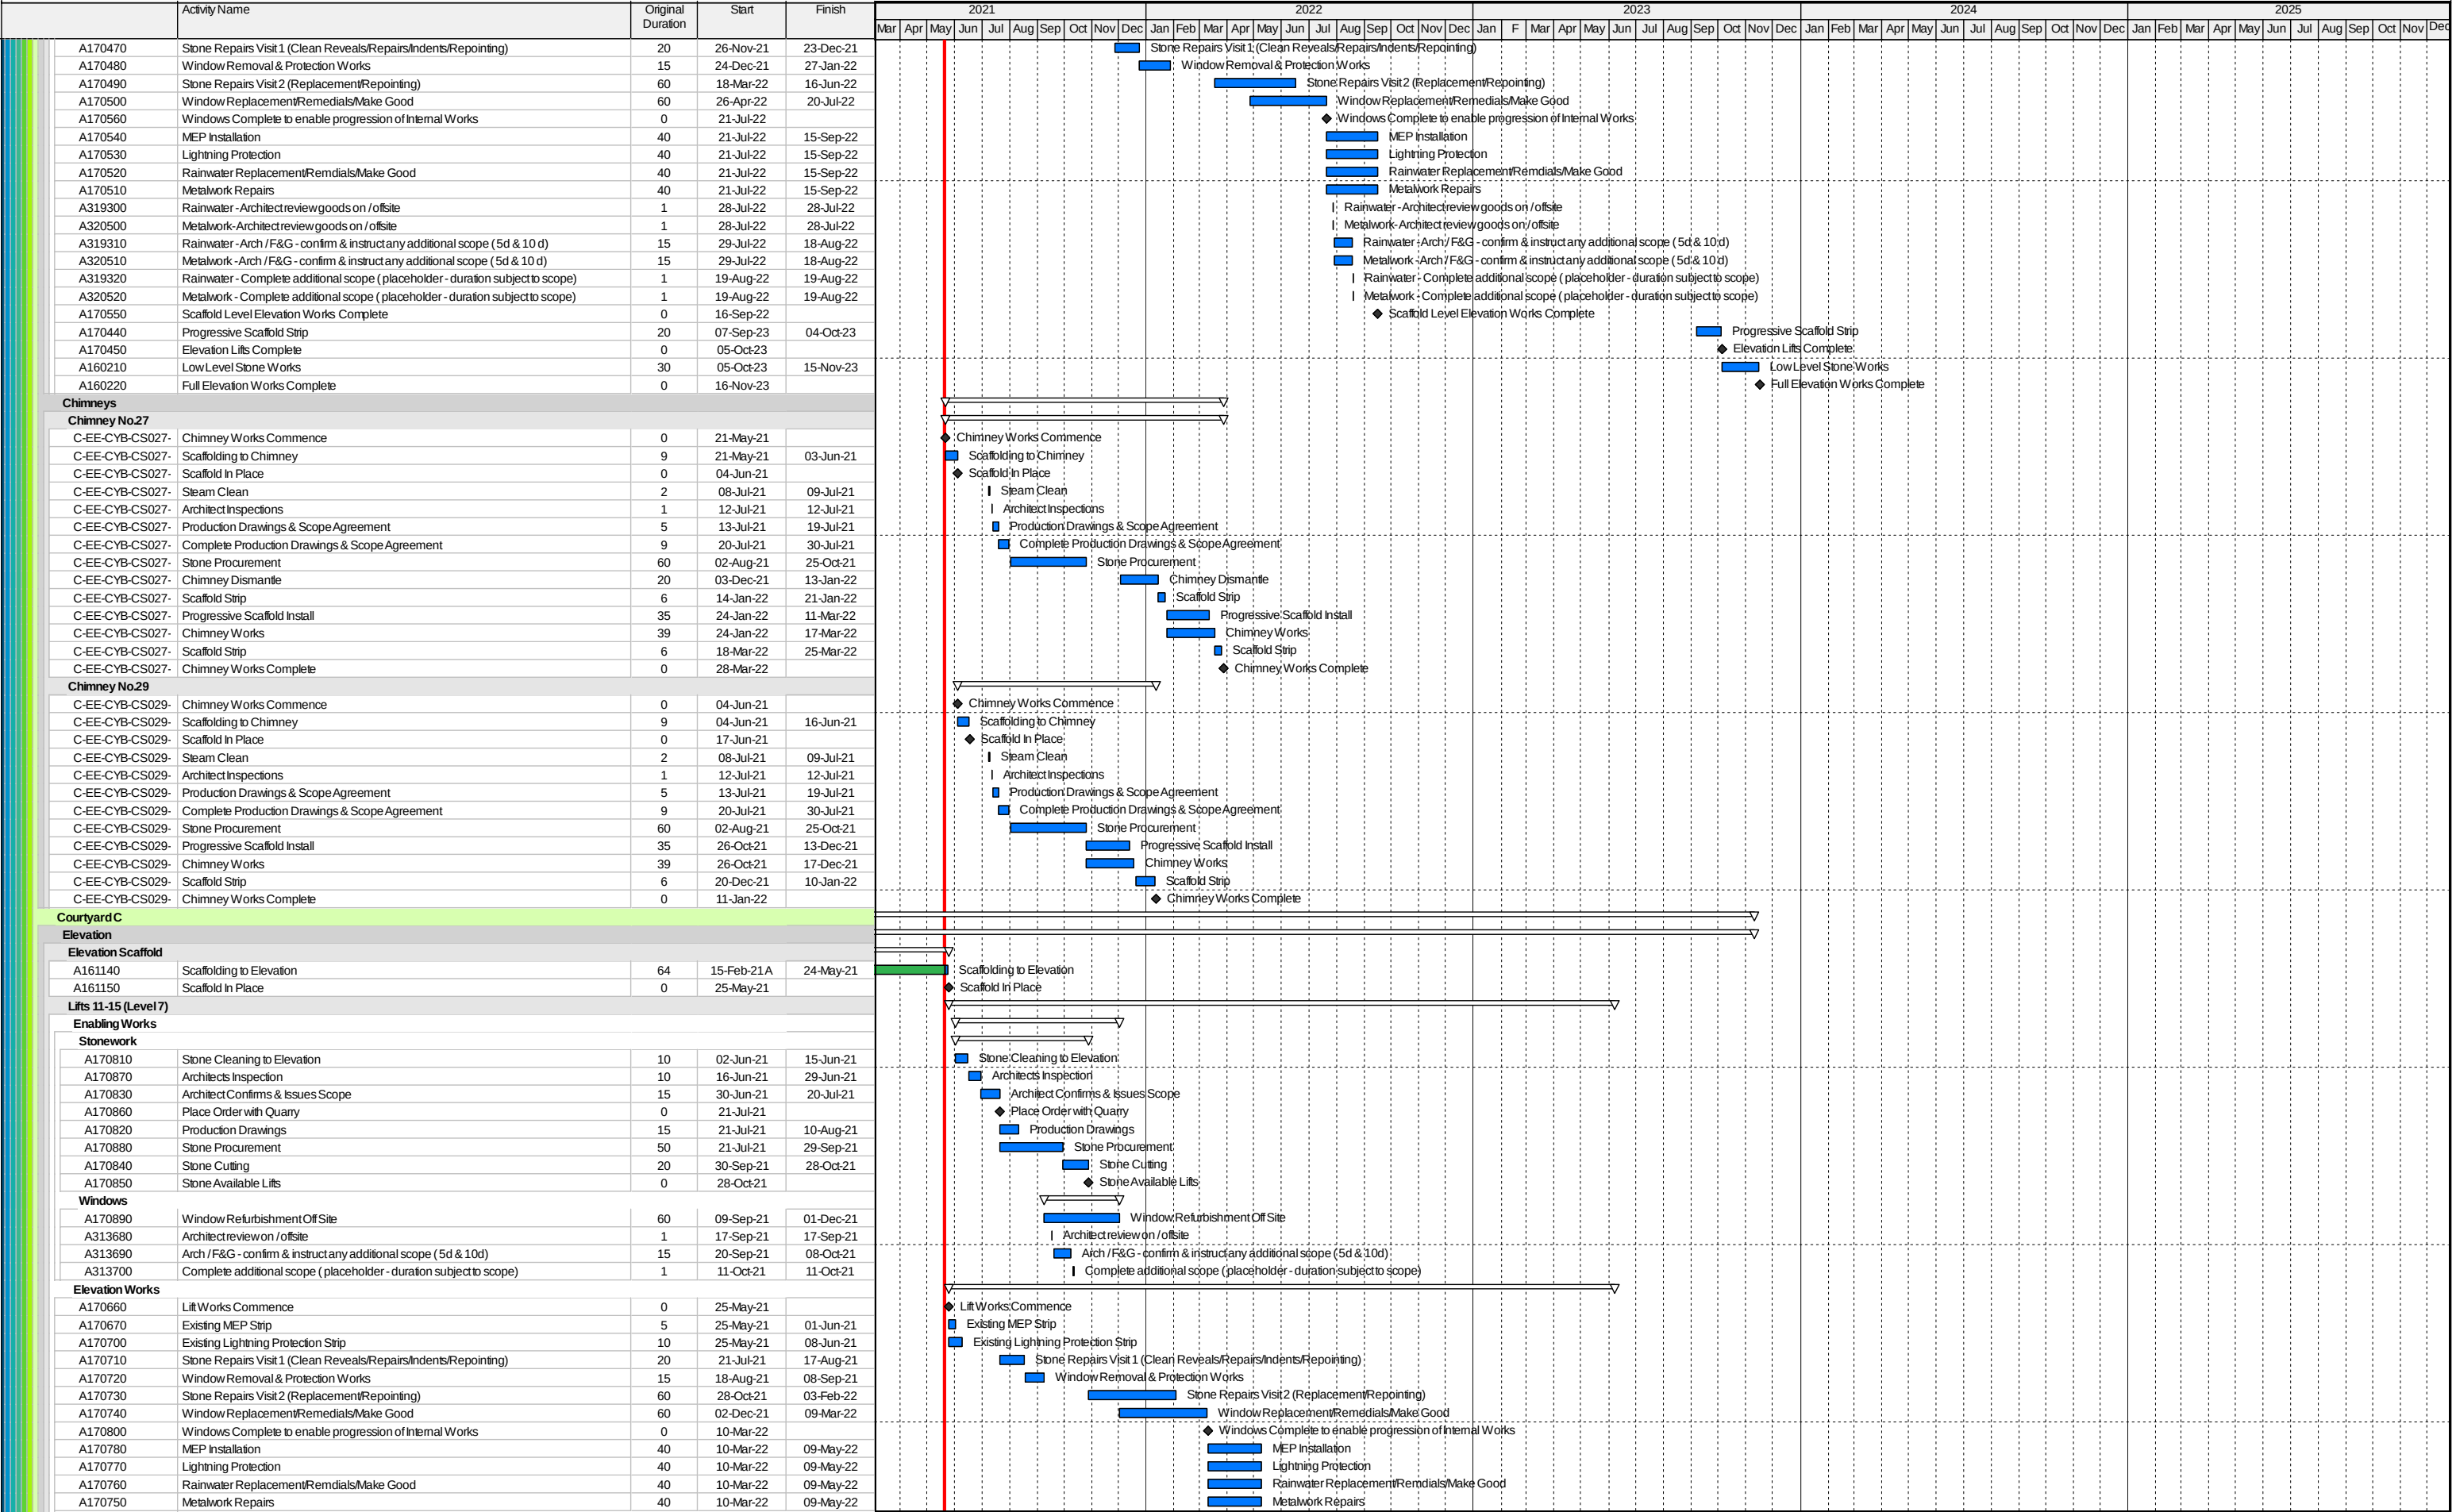

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

86 of 96

Intermittent Work Completed Work Remaining Work Critical Remaining Work	◆ Milestone ▽ Summary	<table><tr><th colspan="4">Programme Revision:</th></tr><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approv...</th></tr><tr><td>11-Jun-21</td><td>G19.2 - Accepted</td><td>RJH / ST</td><td>AM</td></tr><tr><td colspan="4"></td></tr></table>	Programme Revision:				Date	Revision	Checked	Approv...	11-Jun-21	G19.2 - Accepted	RJH / ST	AM					Delivery / Contract Programme	Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21) Layout: OTH - G19.2 General Layout [RJH] Data Date: 21-May-21 Print Date: 24-Aug-21	Page: 87 of 96
Programme Revision:																					
Date	Revision	Checked	Approv...																		
11-Jun-21	G19.2 - Accepted	RJH / ST	AM																		

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

◆

Milestone

↔

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID:

UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout:

OTH - G19.2 General Layout [RJH]

Data Date:

21-May-21

Print Date:

24-Aug-21

Page:

88 of 96

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID:

UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout:

OTH - G19.2 General Layout [RJH]

Data Date:

21-May-21

Print Date:

24-Aug-21

Page:

89 of 96

Intermittent Work Completed Work Remaining Work Critical Remaining Work	◆ Milestone ↔ Summary	<table><tr><th colspan="4">Programme Revision:</th></tr><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approv...</th></tr><tr><td>11-Jun-21</td><td>G19.2 - Accepted</td><td>RJH / ST</td><td>AM</td></tr><tr><td colspan="4"></td></tr></table>	Programme Revision:				Date	Revision	Checked	Approv...	11-Jun-21	G19.2 - Accepted	RJH / ST	AM					Delivery / Contract Programme	Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21) Layout: OTH - G19.2 General Layout [RJH] Data Date: 21-May-21 Print Date: 24-Aug-21	Page: 90 of 96
Programme Revision:																					
Date	Revision	Checked	Approv...																		
11-Jun-21	G19.2 - Accepted	RJH / ST	AM																		

Intermittent Work Completed Work Remaining Work Critical Remaining Work	◆ Milestone ▽ Summary	<table><tr><th colspan="4">Programme Revision:</th></tr><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approv...</th></tr><tr><td>11-Jun-21</td><td>G19.2 - Accepted</td><td>RJH / ST</td><td>AM</td></tr><tr><td colspan="4"></td></tr></table>	Programme Revision:				Date	Revision	Checked	Approv...	11-Jun-21	G19.2 - Accepted	RJH / ST	AM					Delivery / Contract Programme	Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21) Layout: OTH - G19.2 General Layout [RJH] Data Date: 21-May-21 Print Date: 24-Aug-21	Page: 91 of 96
Programme Revision:																					
Date	Revision	Checked	Approv...																		
11-Jun-21	G19.2 - Accepted	RJH / ST	AM																		

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

92 of 96

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

93 of 96

Intermittent Work Completed Work Remaining Work Critical Remaining Work	◆ Milestone ▽ Summary	<table><tr><th colspan="4">Programme Revision:</th></tr><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approv...</th></tr><tr><td>11-Jun-21</td><td>G19.2 - Accepted</td><td>RJH / ST</td><td>AM</td></tr></table>	Programme Revision:				Date	Revision	Checked	Approv...	11-Jun-21	G19.2 - Accepted	RJH / ST	AM	Delivery / Contract Programme	Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21) Layout: OTH - G19.2 General Layout [RJH] Data Date: 21-May-21 Print Date: 24-Aug-21	Page: 94 of 96
Programme Revision:																	
Date	Revision	Checked	Approv...														
11-Jun-21	G19.2 - Accepted	RJH / ST	AM														

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Programme Revision:

Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID: UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout: OTH - G19.2 General Layout [RJH]

Data Date: 21-May-21

Print Date: 24-Aug-21

Page:

95 of 96

Intermittent Work

Completed Work

Remaining Work

Critical Remaining Work

◆

Milestone

▽

Summary

Programme Revision:			
Date	Revision	Checked	Approv...
11-Jun-21	G19.2 - Accepted	RJH / ST	AM

Delivery / Contract Programme

Project ID:

UK-R-MCC-OTH-H-G19.2 (21-May-21)

Layout:

OTH - G19.2 General Layout [RJH]

Data Date:

21-May-21

Print Date:

24-Aug-21

Page:

96 of 96
