

33 - 35 Piccadilly gardens

27 Oct 2022

Trafalgar Leisure Limited

<http://www.cubedltd.oc.uk>

Project manager

Project dates

7 Nov 2022 - 23 May 2023

Completion

0%

Tasks

23

Resources


0

Roof and Façade Repairs
33-35 Piccadilly Gardens
MANCHESTER
M1 1AF

Tasks

Name	Begin date	End date
Start on site	07/11/2022	07/11/2022
Site set up	08/11/2022	08/11/2022
Erect Scaffold front	09/11/2022	22/11/2022
Erect scaffold Side	23/11/2022	06/12/2022
Erect scaffold Rear	07/12/2022	20/12/2022
Hoarding	23/11/2022	29/11/2022
Sheet scaffold	30/11/2022	02/12/2022
Structural Eng Inspection	05/12/2022	16/12/2022
Structural design Repair	19/12/2022	23/12/2022
Concrete Struct Repair	26/12/2022	30/12/2022
Brickwork crack repair	02/01/2023	13/01/2023
Strip roof	16/01/2023	27/01/2023
Lay new asphalt	30/01/2023	24/02/2023
Perimeters Asphalt	27/02/2023	24/03/2023
Copings and cappings	27/03/2023	14/04/2023
Parapet renders	17/04/2023	21/04/2023
Parapet brick	24/04/2023	05/05/2023
Roof wall repoint	08/05/2023	19/05/2023
Plant room joinery	27/03/2023	07/04/2023
Window Repairs	27/02/2023	31/03/2023
External Decoration	03/04/2023	05/05/2023
Scaffolding and banner removal	08/05/2023	19/05/2023
Snagging and completion	22/05/2023	22/05/2023

Gantt Chart

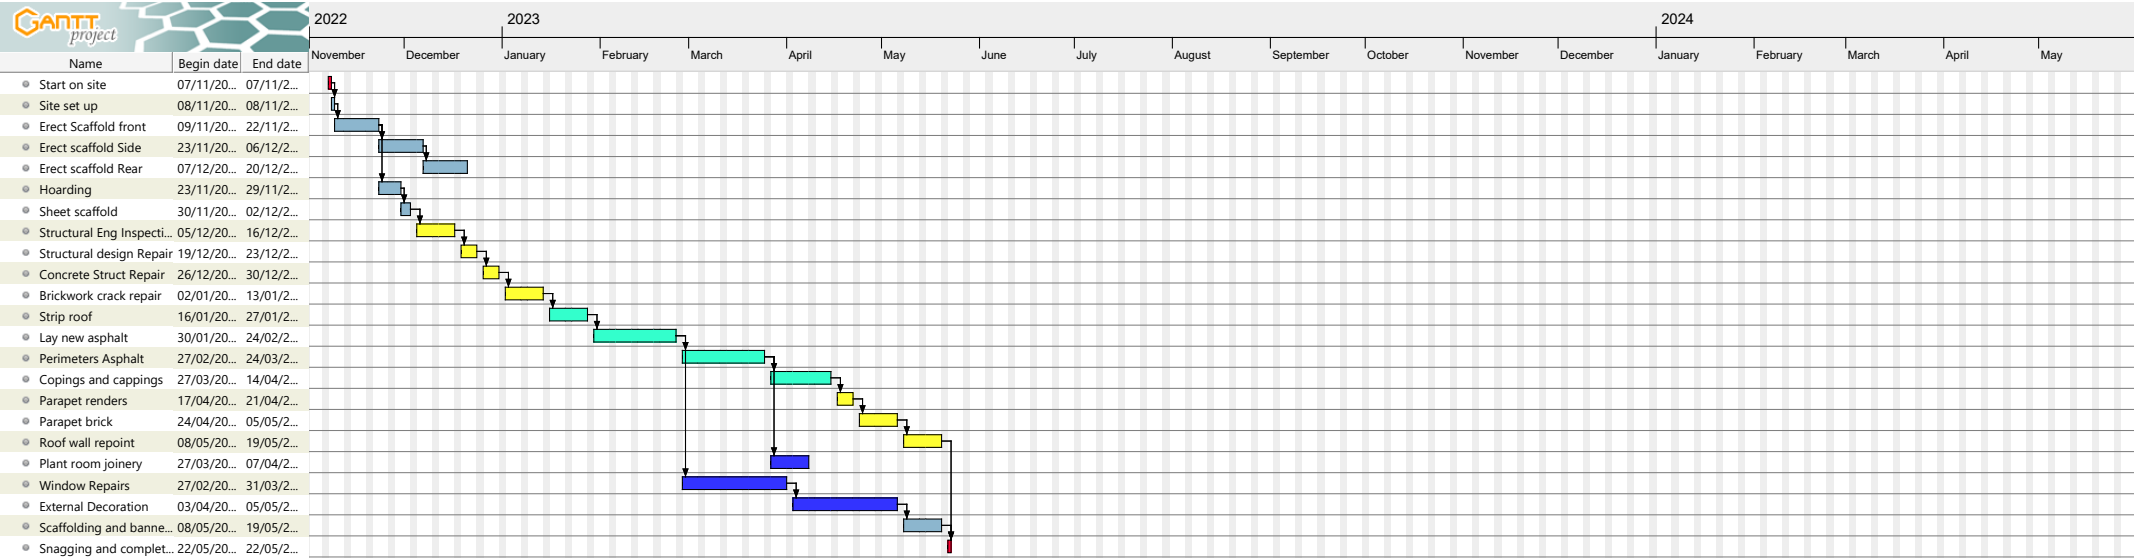

Resources Chart

