

33 - 35 Piccadilly gardens

30 Jun 2022

Trafalgar Leisure Limited

<http://www.cubedltd.oc.uk>

Project manager

Project dates

1 Aug 2022 - 28 Apr 2023

Completion

0%

Tasks

22

Resources

0


Roof and Façade Repairs
33-35 Piccadilly Gardens
MANCHESTER
M1 1AF

Tasks

2

Name	Begin date	End date
Start on site	01/08/2022	01/08/2022
Site set up	02/08/2022	02/08/2022
Erect Scaffold front	03/08/2022	16/08/2022
Erect scaffold Side	17/08/2022	30/08/2022
Erect scaffold Rear	31/08/2022	13/09/2022
Hoarding	14/09/2022	20/09/2022
Sheet scaffold	21/09/2022	04/10/2022
Structural Eng Inspection	05/10/2022	18/10/2022
Structural design Repair	19/10/2022	25/10/2022
Concrete Struct Repair	26/10/2022	01/11/2022
Brickwork crack repair	02/11/2022	15/11/2022
Strip roof	16/11/2022	29/11/2022
Lay new asphalt	30/11/2022	27/12/2022
Perimeters Asphalt	28/12/2022	24/01/2023
Copings and cappings	25/01/2023	14/02/2023
Parapet renders	15/02/2023	21/02/2023
Parapet brick	22/02/2023	07/03/2023
Roof wall repoint	08/03/2023	21/03/2023
Plant room joinery	25/01/2023	07/02/2023
Window Repairs	28/12/2022	31/01/2023
External Decoration	22/03/2023	25/04/2023
Removal of Scaffolding (subject to completion of works)	25/04/2023	26/05/2023

Gantt Chart

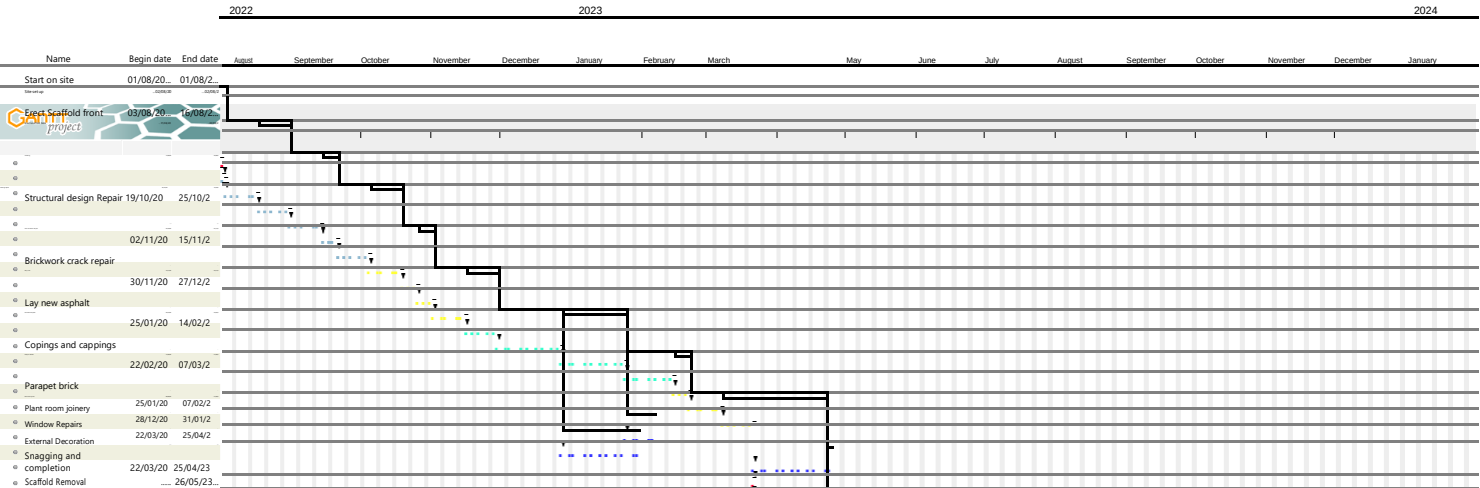

Resources Chart

																									
		2022																							
Name		Default role		August	September	October	November	December	2023	January	February	March	April	May	June	July	August	September	October	November	December	2024	January		
