



Manox Enabling Works – Phasing Proposed Layout

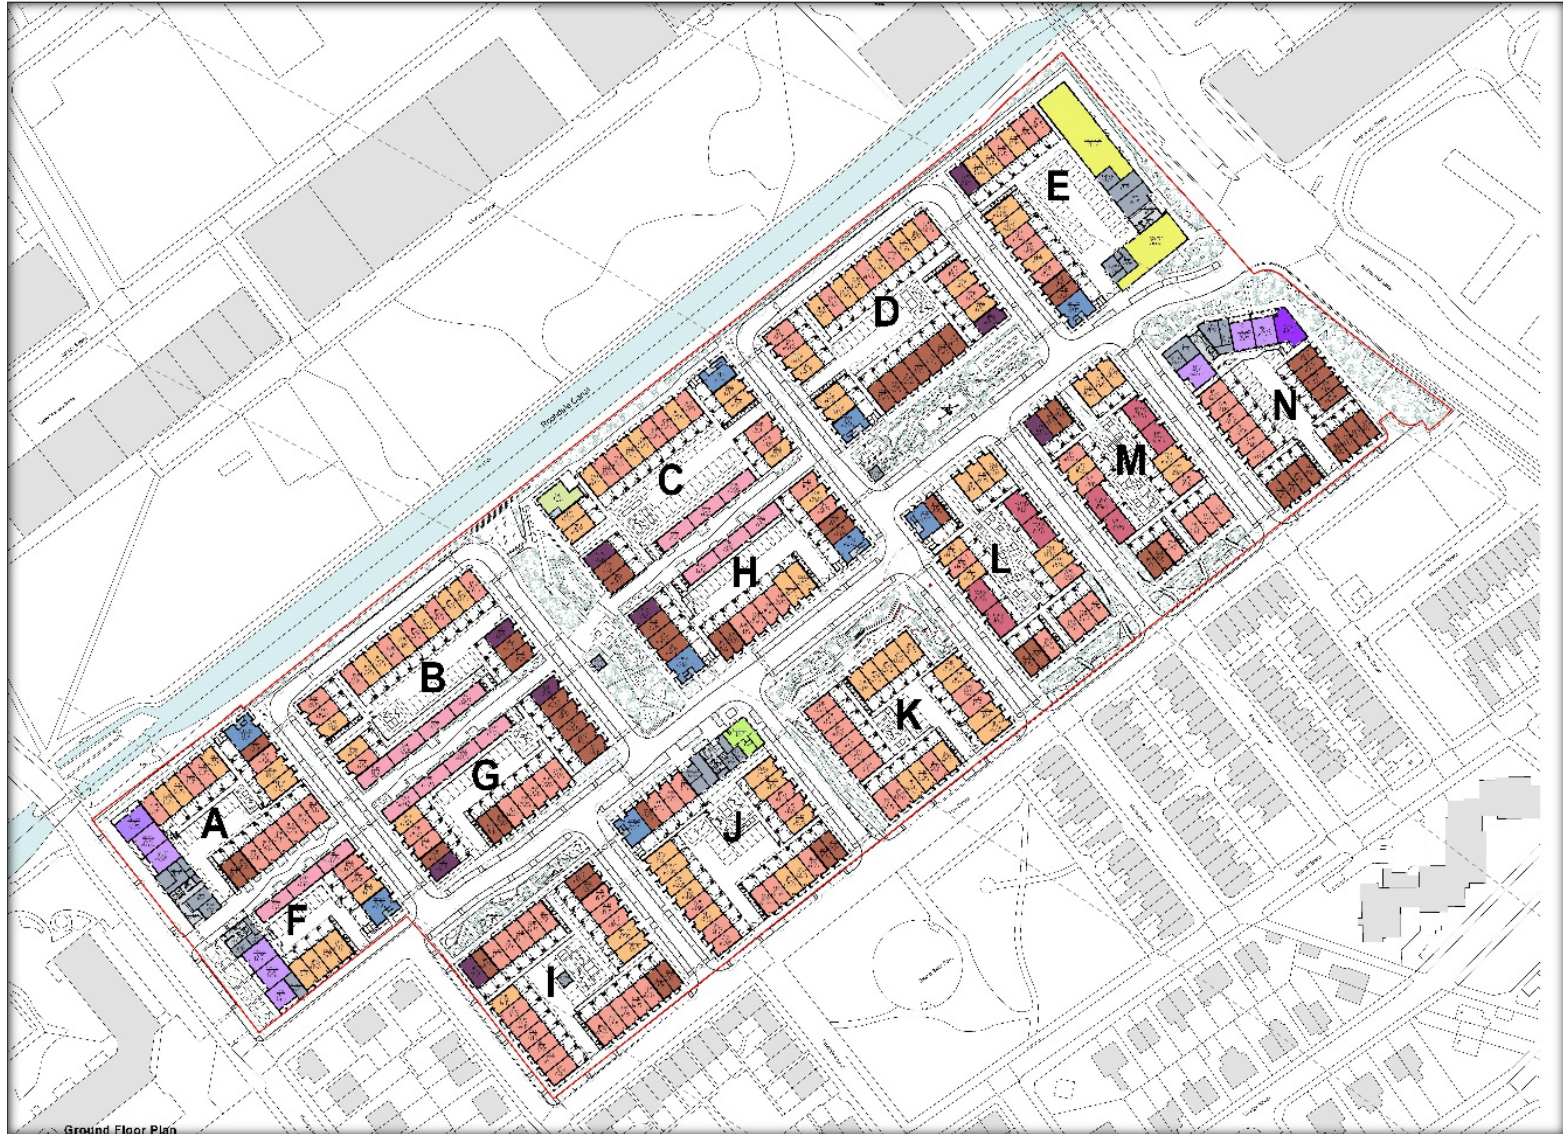

Manox Enabling Works – Phasing

Current T=0 weeks



Manox Enabling Works – Phasing

Current T=0-5 weeks – Site Set up and Clearance



Manox Enabling Works – Phasing

Current T=5-10 weeks – Hot Spot Removal



Manox Enabling Works – Phasing

Current T=9-17 weeks – Mine Working Remediation



Manox Enabling Works – Phasing

Current T=17-26 weeks – Sheet Piling and Earthworks



Manox Enabling Works – Phasing

Current T=27-31 weeks – Remediation and Archaeology.



Manox Enabling Works – Phasing

Current T=32-59 weeks – Remediation and Earthworks



Manox Enabling Works – Phasing

Current T=60-62 weeks – Remediation and Earthworks.



Manox Enabling Works – Phasing

Current T=63-77 weeks – Remediation and Earthworks.



Manox Enabling Works – Phasing

Current T=78 weeks – Remediation and Earthworks.



Hotspot Location Plan

