



OPENINGS TO BE CHECKED AND
TEMPORARY SUPPORT DETERMINED BY
STRUCTURAL ENGINEER

STAIRCASE TO BE SUPPORTED TO ENGINEER'S
DETAIL AND MANUALLY REMOVED TO
ENSURE THERE IS NOT CONSEQUENT
DAMAGE TO ADJACENT SURFACES

IMAGE 001 - INTERNAL - Junction between retained and demolished



4m MIN TO BE DISMANTLED MANUALLY

ALL CONNECTING BEAMS AND JOISTS
CONNECTING TO THE EXISTING BUILDING
TO BE REMOVED MANUALLY AND IN
SEQUENCE. ALLOW TO PIECE IN BRICKWORK
IN LIME MORTAR TO ENSURE WORK
REMAINS STABLE

OPENINGS TO BE CHECKED AND
TEMPORARY SUPPORT DETERMINED BY
STRUCTURAL ENGINEER

IMAGE 002- Internal - Junction between retained and demolished - Lightwell



ALL CONNECTING BEAMS AND JOISTS
CONNECTING TO THE EXISTING BUILDING
TO BE REMOVED MANUALLY AND IN
SEQUENCE. ALLOW TO PIECE IN BRICKWORK
IN LIME MORTAR TO ENSURE WORK
REMAINS STABLE

OPENINGS TO BE CHECKED AND
TEMPORARY SUPPORT DETERMINED BY
STRUCTURAL ENGINEER

4m MIN TO BE DISMANTLED MANUALLY


IMAGE 003- INTERNAL - Junction between retained and demolished - Warehouse

REVISION	DATE	DESCRIPTION
-	29/04/2022	ISSUED FOR DISCHARGE OF CONDITION

READ IN CONJUNCTION WITH PLAN NOTES

KEY

DEMOLITION

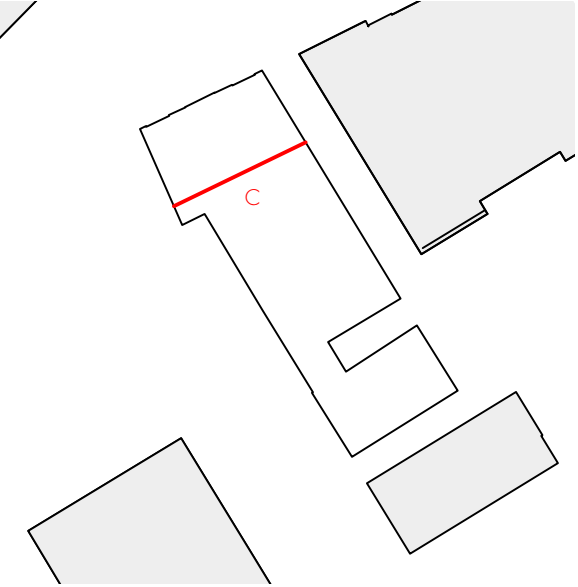

OMIArchitects

31 Blackfriars Road, Salford, Manchester, M3 7AQ
+44(0)161 832 3242 / info@omiarchitects.com / www.omiarchitects.com

PROJECT	LAYSTALL STREET						
DRAWING	DEMOLITION IMAGES INTERNAL						
DATE	FEB' 22	DRAWN BY	RP	SCALE	NTS	@A3	
JOB NO.	1383	DWG.NO.	1383-OMI-00-ZZ-DR-A-L0217--				
