
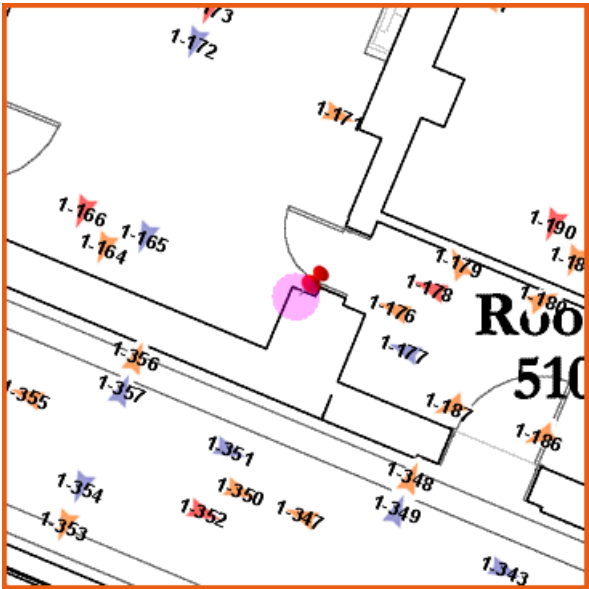


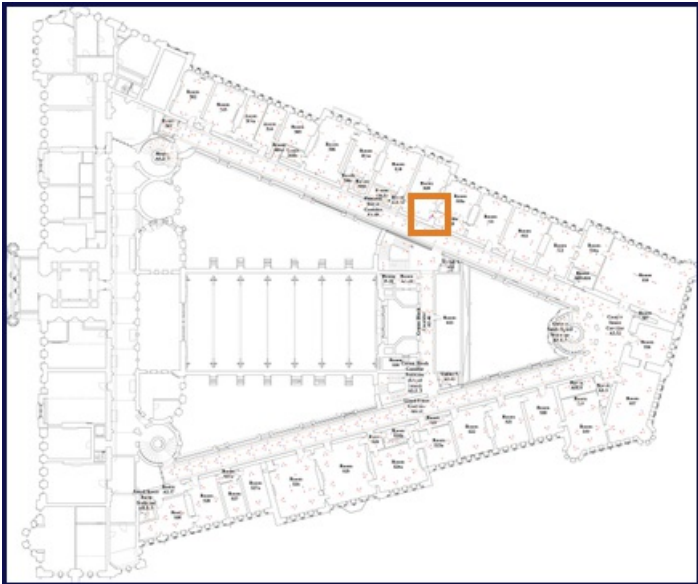

Michael Twiss	Sequence of removal to be agreed by S.Hannon	Sep 05, 2019
Michael Twiss	• Firstly we would start with running a small blade/scrapper down each side to remove any sealing material e.g. Paint, varnish etc. • Then working up in size from a small chisel to a more larger pry bar gently pry the architrave off the casing until its r	Sep 06, 2019
Michael Twiss	Sequence agreed by S.Hannon	Sep 06, 2019

Lendlease - Manchester Town Hall OTH
Michael Twiss - September 5 2019
