



Project

Project Name: 123 LEVENSHULME ROAD GORTON (SURFACE WATER)

Project Date: 10/05/2025

Inspection Standard: MSCC5 Sewers & Drainage GB (SRM5 Scoring)



Table of Contents

Project Name	Project Number	Project Date
123 LEVENSHULME ROAD GORTON (SURFACE WATER)		10/05/2025

Project Information	P-1
Section Item 1: S1RE > S2 (S1REX)	1
Section Item 2: S2 > S4 (S2X)	2
Section Item 3: S3RE > S4 (S3REX)	3
Section Item 4: S4 > S6 (S4X)	4
Section Item 5: S5RE > S6 (S5REX)	5
Section Item 6: BRANCHA > S7 (BRANCHAX)	6
Section Item 7: BRANCHB > S7 (BRANCHBX)	7
Section Item 8: S8RE > S9 (S8REX)	8
Section Item 9: S9 > S10 (S9X)	9
Section Item 10: S6 > S10 (S6X)	10
Section Item 11: S7 > S10 (S7X)	11
Section Item 12: S10 > S12 (S10X)	12
Section Item 13: BRANCHA(1 > S13 (BRANCHA(1X)	13
Section Item 14: S13 > S14 (S13X)	14
Section Item 15: S14 > S15 (S14X)	15
Section Item 16: S15 > SUBMAIN (S15X)	16
Section Item 17: BRANCHA(2 > S17 (BRANCHA(2X)	17
Section Item 18: BRANCHB(1 > S17 (BRANCHB(1X)	18
Section Item 19: BRANCHC > S17 (BRANCHCX)	19
Section Item 20: S17 > S18 (S17X)	20
Section Item 21: S18 > S19 (S18X)	21
Section Item 22: BRANCHA(2 > S19 (BRANCHA(2X)	22
Section Item 23: BRANCHA(3 > S21 (BRANCHA(3X)	23
Section Item 24: S21 > S22 (S21X)	24
Section Item 25: BRANCHA(4 > S22 (BRANCHA(4X)	25
Section Item 26: BRANCHB(2 > S22 (BRANCHB(2X)	26
Section Item 27: S22 > S23 (S22X)	27
Section Item 28: BRANCHA(5 > S11 (BRANCHA(5X)	28



Project Information

Project Name	Project Number	Project Date
123 LEVENSHULME ROAD GORTON (SURFACE WATER)		10/05/2025



Section Inspection - 10/05/2025 - S1 REX

Item No. 1	Insp. No. 1	Date 10/05/25	Time 10:07	Client's Job Ref Not Specified	Weather Not Specified	Pre Cleaned Not Specified	PLR S1 REX
Operator Not Specified		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Not Specified	Alternative ID Not Specified

Town or Village:	Inspection Direction: Upstream	Upstream Node: S1 RE
Road:	Inspected Length: 1.58 m	Upstream Pipe Depth:
Location:	Total Length: 1.58 m	Downstream Node: S2
Surface Type:	Joint Length:	Downstream Pipe Depth:
Use: Surface water	Pipe Shape: Circular	
Type of Pipe:	Dia/Height: 150 mm	
Flow Control:	Material: Polyvinyl chloride	
Year Constructed: Not Specified	Lining Type: No Lining	
Inspection Purpose:	Lining Material: No Lining	

Comments:
Recommendations:

Scale: 1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
	0.00	MH	Start node, manhole, reference: S2			
	1.58	REF	Finish node, rodding eye, reference: S1 RE: RODDING EYE			

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Inspection - 10/05/2025 - S2X

Item No. 2	Insp. No. 1	Date 10/05/25	Time 10:09	Client`s Job Ref Not Specified	Weather Not Specified	Pre Cleaned Not Specified	PLR S2X
Operator Not Specified		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Not Specified	Alternative ID Not Specified

Town or Village:	Inspection Direction: Downstream	Upstream Node: S2
Road:	Inspected Length: 10.25 m	Upstream Pipe Depth:
Location:	Total Length: 10.25 m	Downstream Node: S4
Surface Type:	Joint Length:	Downstream Pipe Depth:
Use: Surface water	Pipe Shape: Circular	
Type of Pipe:	Dia/Height: 150 mm	
Flow Control:	Material: Polyvinyl chloride	
Year Constructed: Not Specified	Lining Type: No Lining	
Inspection Purpose:	Lining Material: No Lining	

Comments:

Recommendations:

Scale: 1:89 Position [m] Code Observation MPEG Photo Grade

Depth: m

S2

0.00

MH Start node, manhole, reference: S2

1.40

CN Connection other than junction at 11 o'clock, 150mm dia

10.10

CN Connection other than junction at 12 o'clock, 150mm dia

10.25

MHF Finish node, manhole, reference: S4

S4

Depth: m

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Inspection - 10/05/2025 - S3 REX

Item No. 3	Insp. No. 1	Date 10/05/25	Time 10:11	Client's Job Ref Not Specified	Weather Not Specified	Pre Cleaned Not Specified	PLR S3 REX
Operator Not Specified		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Not Specified	Alternative ID Not Specified

Town or Village:		Inspection Direction: Upstream		Upstream Node: S3 RE	
Road:		Inspected Length: 9.21 m		Upstream Pipe Depth:	
Location:		Total Length: 9.21 m		Downstream Node: S4	
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use: Surface water			Pipe Shape: Circular		
Type of Pipe:			Dia/Height: 150 mm		
Flow Control:			Material: Polyvinyl chloride		
Year Constructed: Not Specified			Lining Type: No Lining		
Inspection Purpose:			Lining Material: No Lining		

Comments:

Recommendations:

Scale: 1:80 Position [m] Code Observation MPEG Photo Grade

Depth: m
S4



0.00

MH

Start node, manhole, reference: S4

8.89

CN

Connection other than junction at 3 o'clock, 100mm dia

9.21

REF

Finish node, rodding eye, reference: S3 RE: RODDING EYE

S3 RE

Depth: m

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Inspection - 10/05/2025 - S4X

Item No. 4	Insp. No. 1	Date 10/05/25	Time 10:12	Client's Job Ref Not Specified	Weather Not Specified	Pre Cleaned Not Specified	PLR S4X
Operator Not Specified		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Not Specified	Alternative ID Not Specified

Town or Village:	Inspection Direction: Upstream	Upstream Node: S4
Road:	Inspected Length: 15.36 m	Upstream Pipe Depth:
Location:	Total Length: 15.36 m	Downstream Node: S6
Surface Type:	Joint Length:	Downstream Pipe Depth:
Use: Surface water	Pipe Shape: Circular	
Type of Pipe:	Dia/Height: 150 mm	
Flow Control:	Material: Polyvinyl chloride	
Year Constructed: Not Specified	Lining Type: No Lining	
Inspection Purpose:	Lining Material: No Lining	

Comments:

Recommendations:

Scale: 1:133 Position [m] Code Observation MPEG Photo Grade

Depth: m


S6



0.00

MH

Start node, manhole, reference: S4



15.36

MHF

Finish node, manhole, reference: S6

S4

Depth: m

Construction Features

Miscellaneous Features

Structural Defects

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Inspection - 10/05/2025 - S5 REX

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
5	1	10/05/25	10:15	Not Specified	Not Specified	Not Specified	S5 REX
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
Not Specified		Not Specified		Not Specified	Not Specified	Not Specified	Not Specified

Town or Village:	Inspection Direction: Upstream	Upstream Node: S5 RE
Road:	Inspected Length: 11.64 m	Upstream Pipe Depth:
Location:	Total Length: 11.64 m	Downstream Node: S6
Surface Type:	Joint Length:	Downstream Pipe Depth:
Use: Surface water	Pipe Shape: Circular	
Type of Pipe:	Dia/Height: 150 mm	
Flow Control:	Material: Polyvinyl chloride	
Year Constructed: Not Specified	Lining Type: No Lining	
Inspection Purpose:	Lining Material: No Lining	

Comments:
Recommendations:

Scale:	1:101	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: m S6 0.00 10.62 11.64 S5 RE Depth: m							
MH	Start node, manhole, reference: S6						
CN	Connection other than junction at 11 o'clock, 100mm dia						
REF	Finish node, rodding eye, reference: S5 RE: RODDING EYE						

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Inspection - 10/05/2025 - BRANCH AX


Item No. 6	Insp. No. 1	Date 10/05/25	Time 10:24	Client's Job Ref Not Specified	Weather Not Specified	Pre Cleaned Not Specified	PLR BRANCH AX
Operator Not Specified		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Not Specified	Alternative ID Not Specified

Town or Village:		Inspection Direction: Upstream		Upstream Node: BRANCH A	
Road:		Inspected Length: 0.71 m		Upstream Pipe Depth:	
Location:		Total Length: 0.71 m		Downstream Node: S7	
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use: Surface water			Pipe Shape: Circular		
Type of Pipe:			Dia/Height: 100 mm		
Flow Control:			Material: Polyvinyl chloride		
Year Constructed: Not Specified			Lining Type: No Lining		
Inspection Purpose:			Lining Material: No Lining		

Comments:

Recommendations:

Scale: 1:50 Position [m] Code Observation MPEG Photo Grade

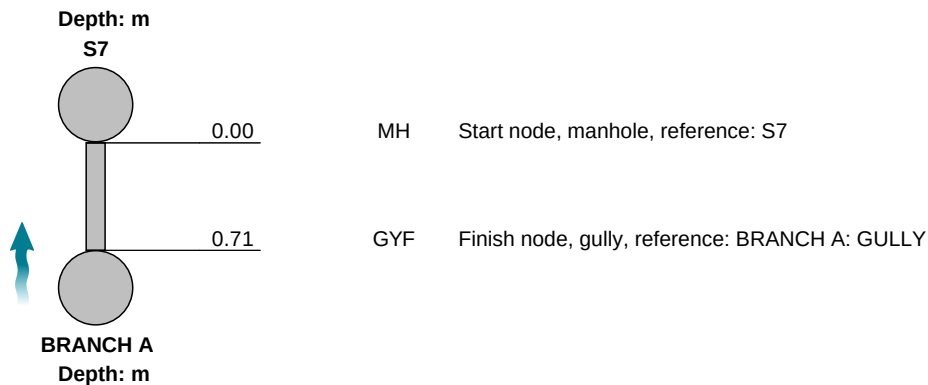

Construction Features

Miscellaneous Features

Structural Defects

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Inspection - 10/05/2025 - BRANCH BX

Item No. 7	Insp. No. 1	Date 10/05/25	Time 10:25	Client's Job Ref Not Specified	Weather Not Specified	Pre Cleaned Not Specified	PLR BRANCH BX
Operator Not Specified		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Not Specified	Alternative ID Not Specified

Town or Village:	Inspection Direction: Upstream	Upstream Node:	BRANCH B
Road:	Inspected Length: 0.74 m	Upstream Pipe Depth:	
Location:	Total Length: 0.74 m	Downstream Node:	S7
Surface Type:	Joint Length:	Downstream Pipe Depth:	
Use: Surface water	Pipe Shape: Circular		
Type of Pipe:	Dia/Height: 100 mm		
Flow Control:	Material: Polyvinyl chloride		
Year Constructed: Not Specified	Lining Type: No Lining		
Inspection Purpose:	Lining Material: No Lining		

Comments:
Recommendations:

Scale: 1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
	0.00	MH	Start node, manhole, reference: S7			
	0.74	GYF	Finish node, gully, reference: BRANCH B: GULLY			

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Inspection - 10/05/2025 - S8 REX

Item No. 8	Insp. No. 1	Date 10/05/25	Time 10:26	Client's Job Ref Not Specified	Weather Not Specified	Pre Cleaned Not Specified	PLR S8 REX
Operator Not Specified		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Not Specified	Alternative ID Not Specified

Town or Village:	Inspection Direction: Upstream	Upstream Node: S8 RE
Road:	Inspected Length: 11.48 m	Upstream Pipe Depth:
Location:	Total Length: 11.48 m	Downstream Node: S9
Surface Type:	Joint Length:	Downstream Pipe Depth:
Use: Surface water	Pipe Shape: Circular	
Type of Pipe:	Dia/Height: 150 mm	
Flow Control:	Material: Polyvinyl chloride	
Year Constructed: Not Specified	Lining Type: No Lining	
Inspection Purpose:	Lining Material: No Lining	

Comments:
Recommendations:

Scale: 1:100	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: m S9						
	0.00	MH	Start node, manhole, reference: S9			
	9.47	CN	Connection other than junction at 3 o'clock, 100mm dia			
	11.48	REF	Finish node, rodding eye, reference: S8 RE: RODDING EYE			
S8 RE Depth: m						

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Inspection - 10/05/2025 - S9X

Item No. 9	Insp. No. 1	Date 10/05/25	Time 10:28	Client's Job Ref Not Specified	Weather Not Specified	Pre Cleaned Not Specified	PLR S9X
Operator Not Specified		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Not Specified	Alternative ID Not Specified

Town or Village:	Inspection Direction: Downstream	Upstream Node: S9
Road:	Inspected Length: 13.36 m	Upstream Pipe Depth:
Location:	Total Length: 13.36 m	Downstream Node: S10
Surface Type:	Joint Length:	Downstream Pipe Depth:
Use: Surface water	Pipe Shape: Circular	
Type of Pipe:	Dia/Height: 150 mm	
Flow Control:	Material: Polyvinyl chloride	
Year Constructed: Not Specified	Lining Type: No Lining	
Inspection Purpose:	Lining Material: No Lining	

Comments:

Recommendations:

Scale: 1:116 Position [m] Code Observation MPEG Photo Grade

Depth: m
S9



0.00

MH

Start node, manhole, reference: S9

5.80

CN

Connection other than junction at 1 o'clock, 150mm dia

13.36

MHF

Finish node, manhole, reference: S10

S10
Depth: m



Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations


STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Inspection - 10/05/2025 - S6X

Item No. 10	Insp. No. 1	Date 10/05/25	Time 10:29	Client's Job Ref Not Specified	Weather Not Specified	Pre Cleaned Not Specified	PLR S6X
Operator Not Specified		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Not Specified	Alternative ID Not Specified

Town or Village:		Inspection Direction: Upstream		Upstream Node: S6	
Road:		Inspected Length: 13.69 m		Upstream Pipe Depth:	
Location:		Total Length: 13.69 m		Downstream Node: S10	
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water			Pipe Shape:	Circular
Type of Pipe:				Dia/Height:	150 mm
Flow Control:				Material:	Polyvinyl chloride
Year Constructed:	Not Specified			Lining Type:	No Lining
Inspection Purpose:				Lining Material:	No Lining
Comments:					
Recommendations:					

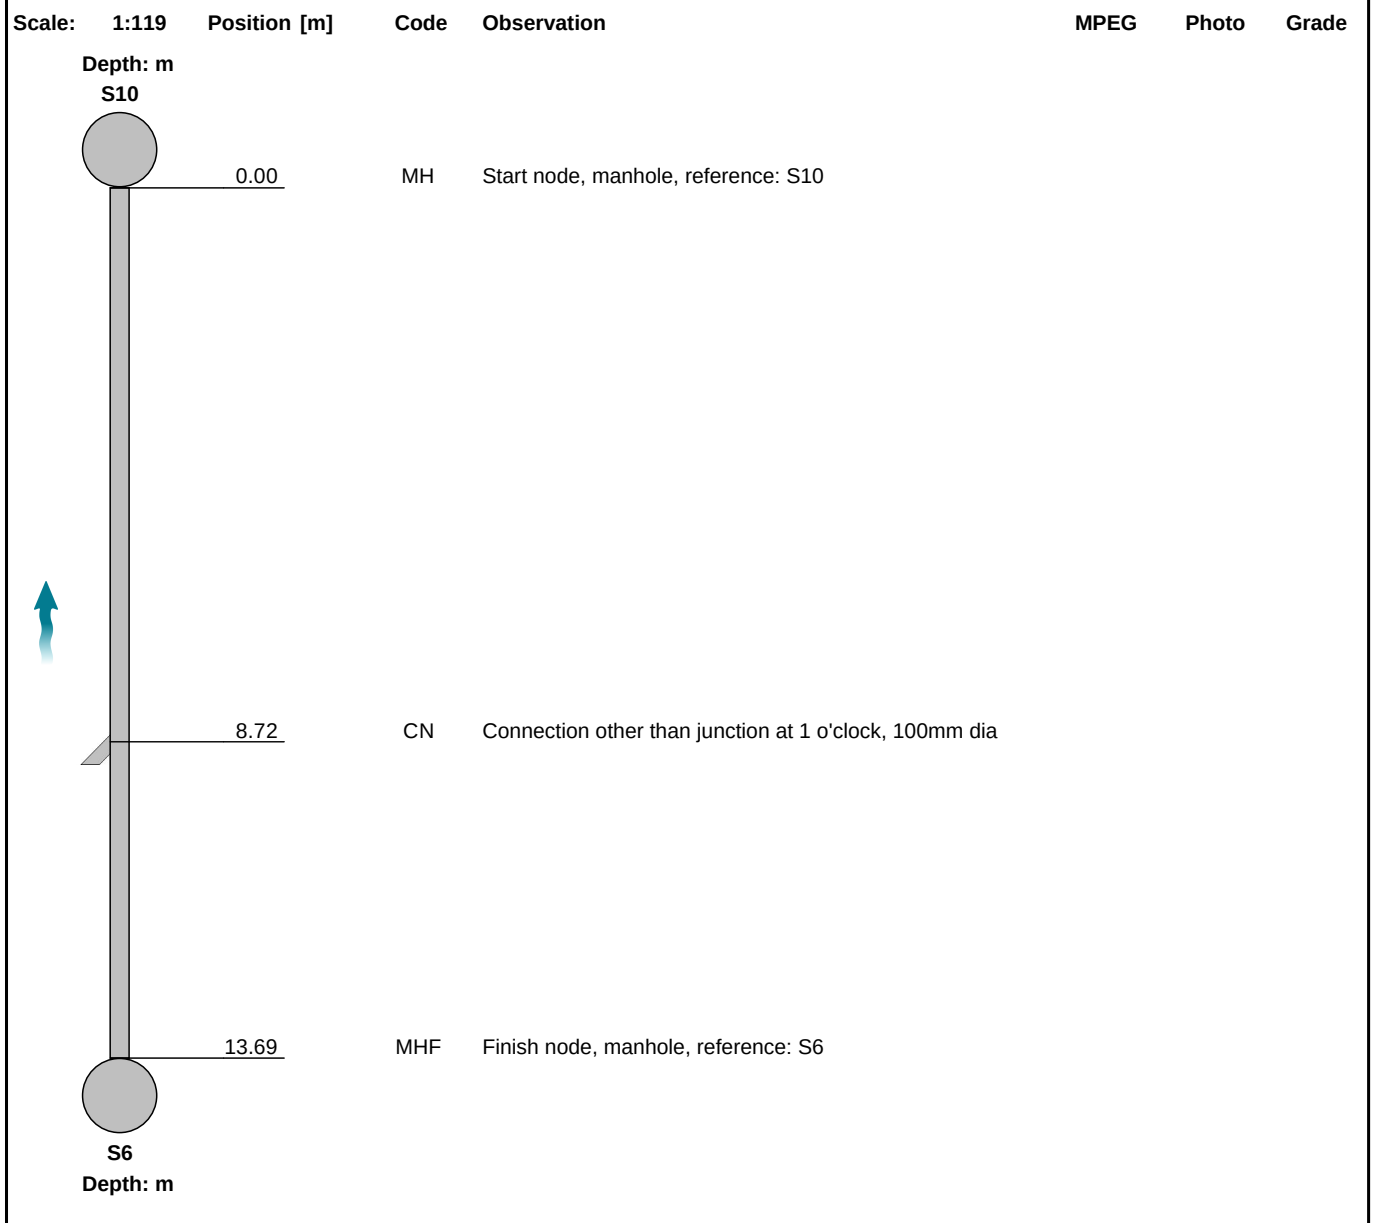

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Inspection - 10/05/2025 - S7X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
11	1	10/05/25	10:31	Not Specified	Not Specified	Not Specified	S7X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
Not Specified		Not Specified		Not Specified	Not Specified	Not Specified	Not Specified

Town or Village:		Inspection Direction: Upstream		Upstream Node: S7	
Road:		Inspected Length: 10.37 m		Upstream Pipe Depth:	
Location:		Total Length: 10.37 m		Downstream Node: S10	
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use: Surface water			Pipe Shape: Circular		
Type of Pipe:			Dia/Height: 150 mm		
Flow Control:			Material: Polyvinyl chloride		
Year Constructed: Not Specified			Lining Type: No Lining		
Inspection Purpose:			Lining Material: No Lining		

Comments:
Recommendations:

Scale:	1:90	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: m S10 0.00 MH Start node, manhole, reference: S10							
4.95 CN Connection other than junction at 11 o'clock, 100mm dia							
5.17 CN Connection other than junction at 1 o'clock, 100mm dia							
10.37 MHF Finish node, manhole, reference: S7							
S7 Depth: m							

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Inspection - 10/05/2025 - S10X

Item No. 12	Insp. No. 1	Date 10/05/25	Time 10:33	Client's Job Ref Not Specified	Weather Not Specified	Pre Cleaned Not Specified	PLR S10X
Operator Not Specified		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Not Specified	Alternative ID Not Specified

Town or Village:	Inspection Direction: Downstream	Upstream Node: S10
Road:	Inspected Length: 3.45 m	Upstream Pipe Depth:
Location:	Total Length: 3.45 m	Downstream Node: S12
Surface Type:	Joint Length:	Downstream Pipe Depth:
Use: Surface water	Pipe Shape: Circular	
Type of Pipe:	Dia/Height: 150 mm	
Flow Control:	Material: Polyvinyl chloride	
Year Constructed: Not Specified	Lining Type: No Lining	
Inspection Purpose:	Lining Material: No Lining	

Comments:
Recommendations:

Scale: 1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: m S10 0.00 MH Start node, manhole, reference: S10						
3.45 MHF Finish node, manhole, reference: S12						
S12 Depth: m						

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Inspection - 10/05/2025 - BRANCH A(1X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
13	1	10/05/25	10:34	Not Specified	Not Specified	Not Specified	BRANCH A(1X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
Not Specified		Not Specified		Not Specified	Not Specified	Not Specified	Not Specified

Town or Village:		Inspection Direction: Upstream		Upstream Node: BRANCH A(1	
Road:		Inspected Length: 0.77 m		Upstream Pipe Depth:	
Location:		Total Length: 0.77 m		Downstream Node: S13	
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use: Surface water			Pipe Shape: Circular		
Type of Pipe:			Dia/Height: 100 mm		
Flow Control:			Material: Polyvinyl chloride		
Year Constructed: Not Specified			Lining Type: No Lining		
Inspection Purpose:			Lining Material: No Lining		

Comments:
Recommendations:

Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
		0.00	MH	Start node, manhole, reference: S13			
		0.77	GYF	Finish node, gully, reference: BRANCH A(1: GULLY			

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Inspection - 10/05/2025 - S13X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
14	1	10/05/25	10:35	Not Specified	Not Specified	Not Specified	S13X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
Not Specified		Not Specified		Not Specified	Not Specified	Not Specified	Not Specified

Town or Village:	Inspection Direction: Downstream	Upstream Node: S13
Road:	Inspected Length: 14.86 m	Upstream Pipe Depth:
Location:	Total Length: 14.86 m	Downstream Node: S14
Surface Type:	Joint Length:	Downstream Pipe Depth:
Use: Surface water	Pipe Shape: Circular	
Type of Pipe:	Dia/Height: 150 mm	
Flow Control:	Material: Polyvinyl chloride	
Year Constructed: Not Specified	Lining Type: No Lining	
Inspection Purpose:	Lining Material: No Lining	

Comments:
Recommendations:

Scale: 1:129	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: m						
S13						
	0.00	MH	Start node, manhole, reference: S13			
	6.70	CN	Connection other than junction at 12 o'clock, 150mm dia			
	14.86	MHF	Finish node, manhole, reference: S14			
S14						
Depth: m						

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0




Section Inspection - 10/05/2025 - S14X

Item No. 15	Insp. No. 1	Date 10/05/25	Time 10:37	Client's Job Ref Not Specified	Weather Not Specified	Pre Cleaned Not Specified	PLR S14X
Operator Not Specified		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Not Specified	Alternative ID Not Specified

Town or Village:	Inspection Direction: Downstream	Upstream Node: S14
Road:	Inspected Length: 17.51 m	Upstream Pipe Depth:
Location:	Total Length: 17.51 m	Downstream Node: S15
Surface Type:	Joint Length:	Downstream Pipe Depth:
Use: Surface water	Pipe Shape: Circular	
Type of Pipe:	Dia/Height: 150 mm	
Flow Control:	Material: Polyvinyl chloride	
Year Constructed: Not Specified	Lining Type: No Lining	
Inspection Purpose:	Lining Material: No Lining	

Comments:
Recommendations:

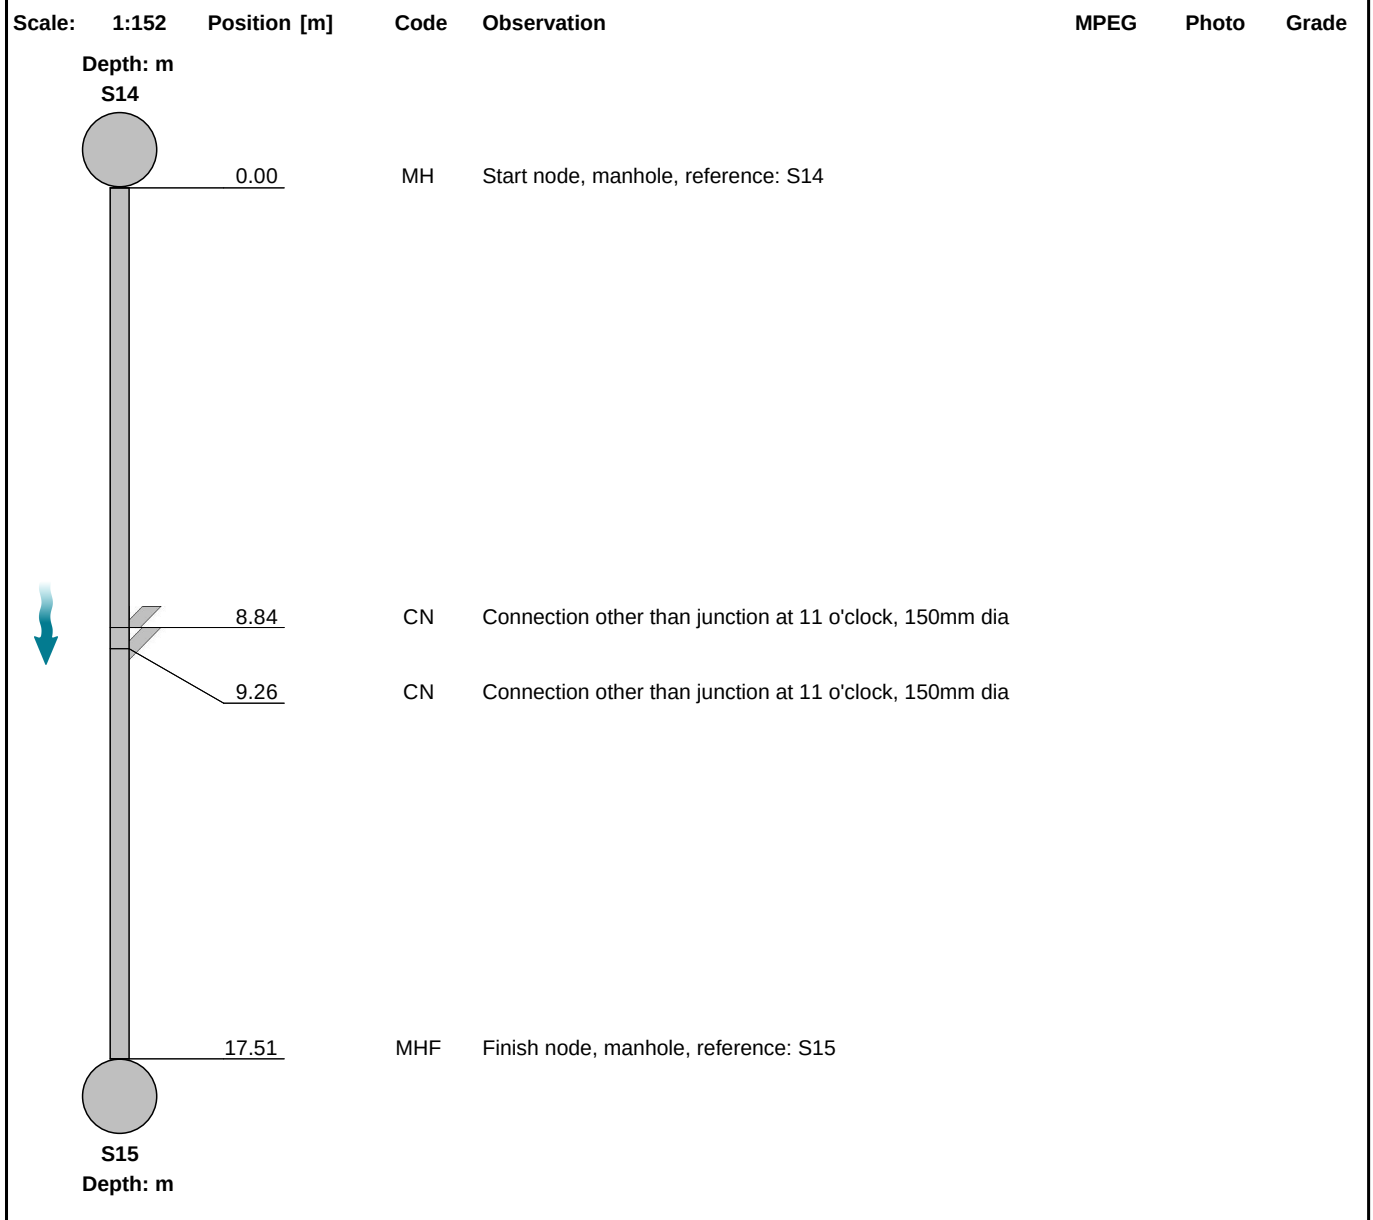


Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Inspection - 10/05/2025 - S15X

Item No. 16	Insp. No. 1	Date 10/05/25	Time 10:39	Client's Job Ref Not Specified	Weather Not Specified	Pre Cleaned Not Specified	PLR S15X
Operator Not Specified		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Not Specified	Alternative ID Not Specified

Town or Village:	Inspection Direction: Downstream	Upstream Node: S15
Road:	Inspected Length: 5.14 m	Upstream Pipe Depth:
Location:	Total Length: 5.14 m	Downstream Node: SUBMAIN
Surface Type:	Joint Length:	Downstream Pipe Depth:
Use: Surface water	Pipe Shape: Circular	
Type of Pipe:	Dia/Height: 150 mm	
Flow Control:	Material: Polyvinyl chloride	
Year Constructed: Not Specified	Lining Type: No Lining	
Inspection Purpose:	Lining Material: No Lining	
Comments:		
Recommendations:		

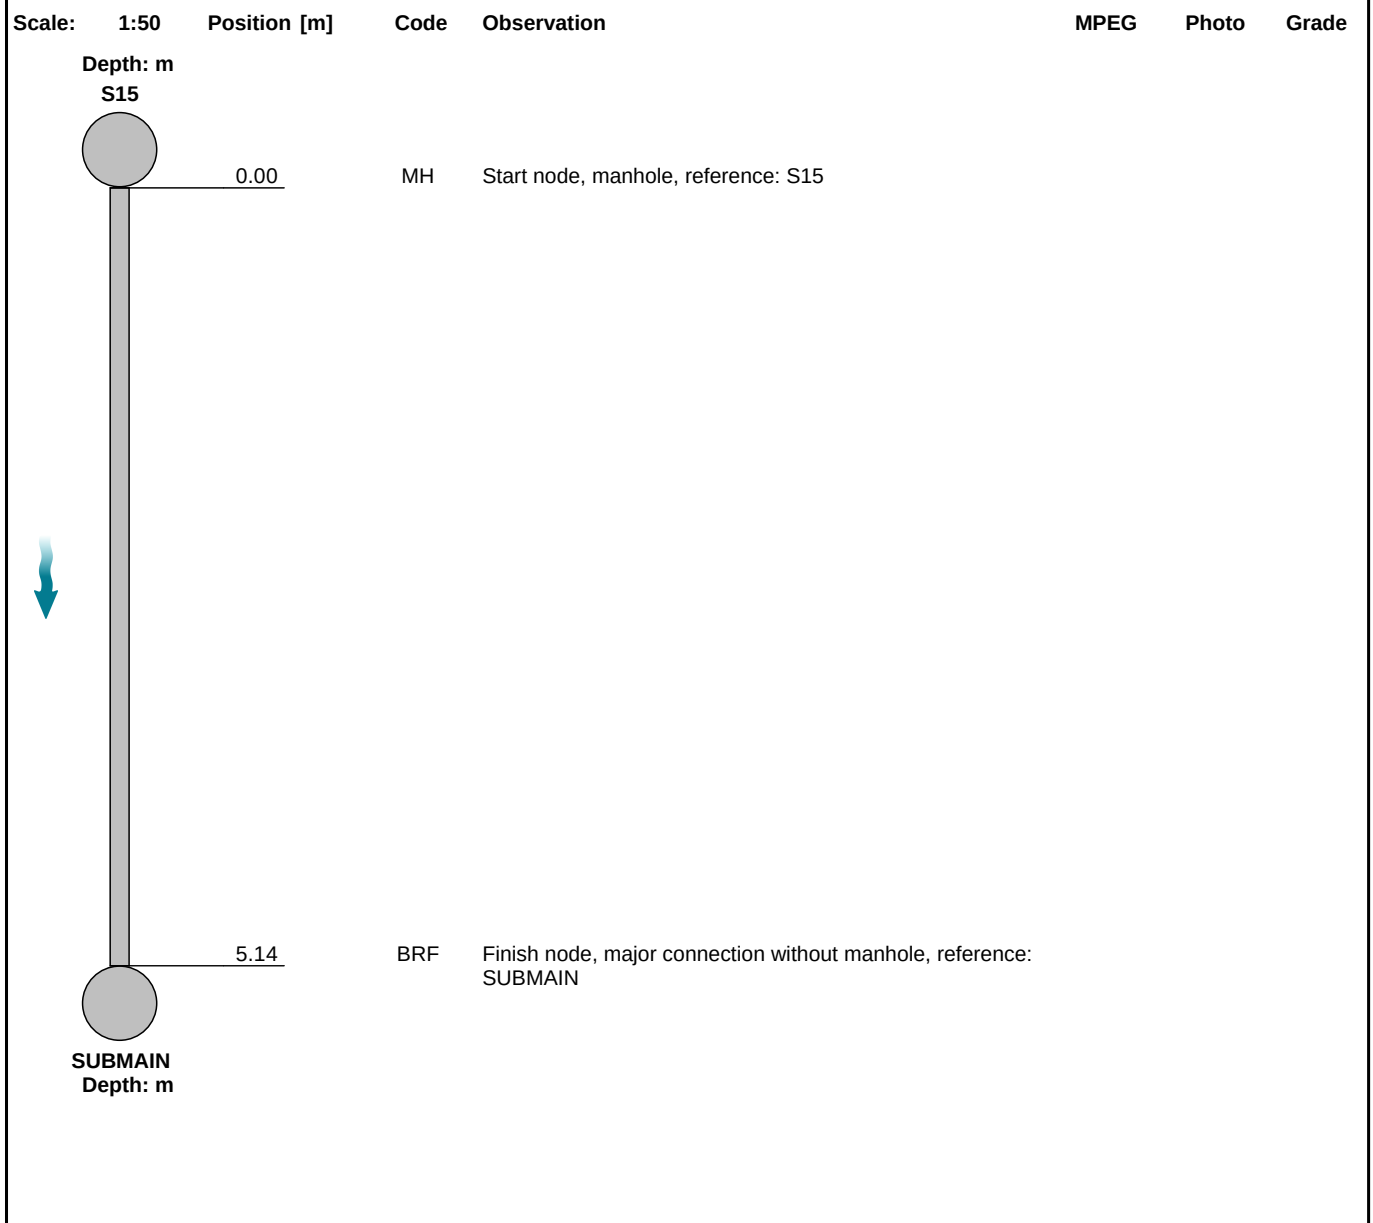

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Inspection - 10/05/2025 - BRANCHA (2X)

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
17	1	10/05/25	10:41	Not Specified	Not Specified	Not Specified	BRANCHA (2X)
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
Not Specified		Not Specified		Not Specified	Not Specified	Not Specified	Not Specified

Town or Village:		Inspection Direction: Upstream		Upstream Node: BRANCHA (2	
Road:		Inspected Length: 1.00 m		Upstream Pipe Depth:	
Location:		Total Length: 1.00 m		Downstream Node: S17	
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use: Surface water		Pipe Shape: Circular			
Type of Pipe:		Dia/Height: 100 mm			
Flow Control:		Material: Polyvinyl chloride			
Year Constructed: Not Specified		Lining Type: No Lining			
Inspection Purpose:		Lining Material: No Lining			

Comments:
Recommendations:

Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: m							
S17							
	0.00		MH	Start node, manhole, reference: S17			
	1.00		GYF	Finish node, gully, reference: BRANCHA (2: GULLY			
BRANCHA (2							
Depth: m							


Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Inspection - 10/05/2025 - BRANCH B(1X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
18	1	10/05/25	10:42	Not Specified	Not Specified	Not Specified	BRANCH B(1X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
Not Specified		Not Specified		Not Specified	Not Specified	Not Specified	Not Specified

Town or Village:	Inspection Direction: Upstream	Upstream Node: BRANCH B(1
Road:	Inspected Length: 8.80 m	Upstream Pipe Depth:
Location:	Total Length: 8.80 m	Downstream Node: S17
Surface Type:	Joint Length:	Downstream Pipe Depth:
Use: Surface water	Pipe Shape: Circular	
Type of Pipe:	Dia/Height: 100 mm	
Flow Control:	Material: Polyvinyl chloride	
Year Constructed: Not Specified	Lining Type: No Lining	
Inspection Purpose:	Lining Material: No Lining	
Comments:		
Recommendations:		

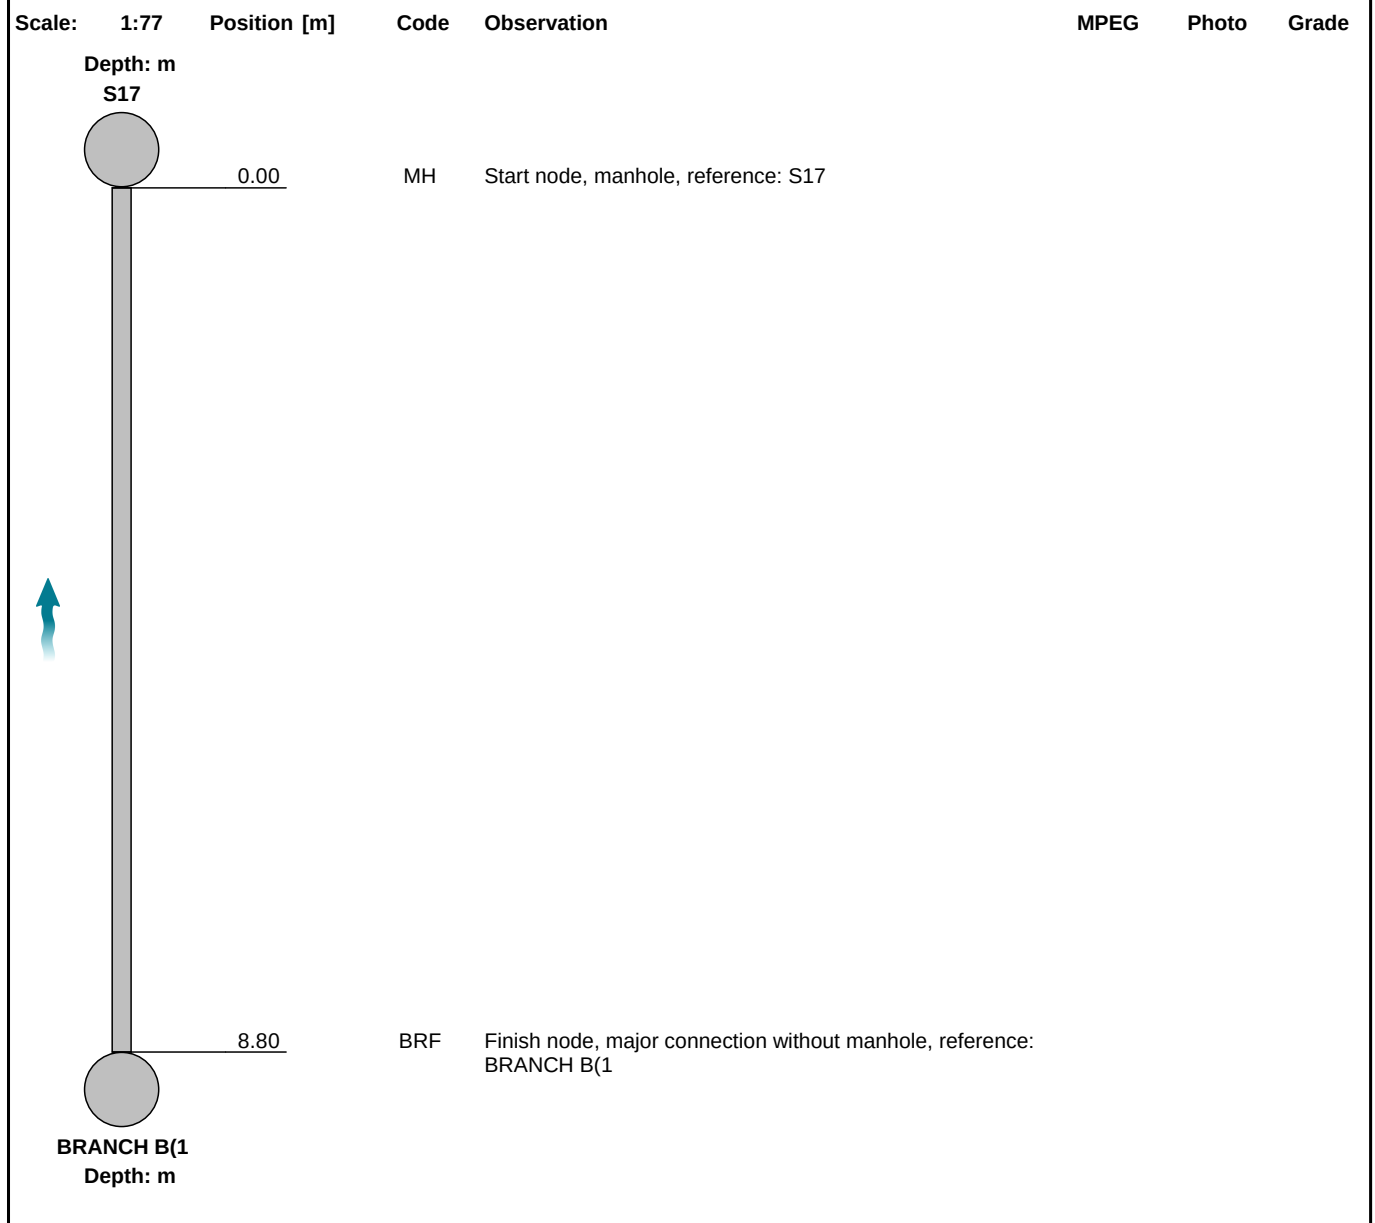

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0




Section Inspection - 10/05/2025 - BRANCH CX

Item No. 19	Insp. No. 1	Date 10/05/25	Time 10:43	Client's Job Ref Not Specified	Weather Not Specified	Pre Cleaned Not Specified	PLR BRANCH CX
Operator Not Specified		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Not Specified	Alternative ID Not Specified

Town or Village:		Inspection Direction: Upstream		Upstream Node: BRANCH C	
Road:		Inspected Length: 9.36 m		Upstream Pipe Depth:	
Location:		Total Length: 9.36 m		Downstream Node: S17	
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use: Surface water			Pipe Shape: Circular		
Type of Pipe:			Dia/Height: 150 mm		
Flow Control:			Material: Polyvinyl chloride		
Year Constructed: Not Specified			Lining Type: No Lining		
Inspection Purpose:			Lining Material: No Lining		

Comments:
Recommendations:

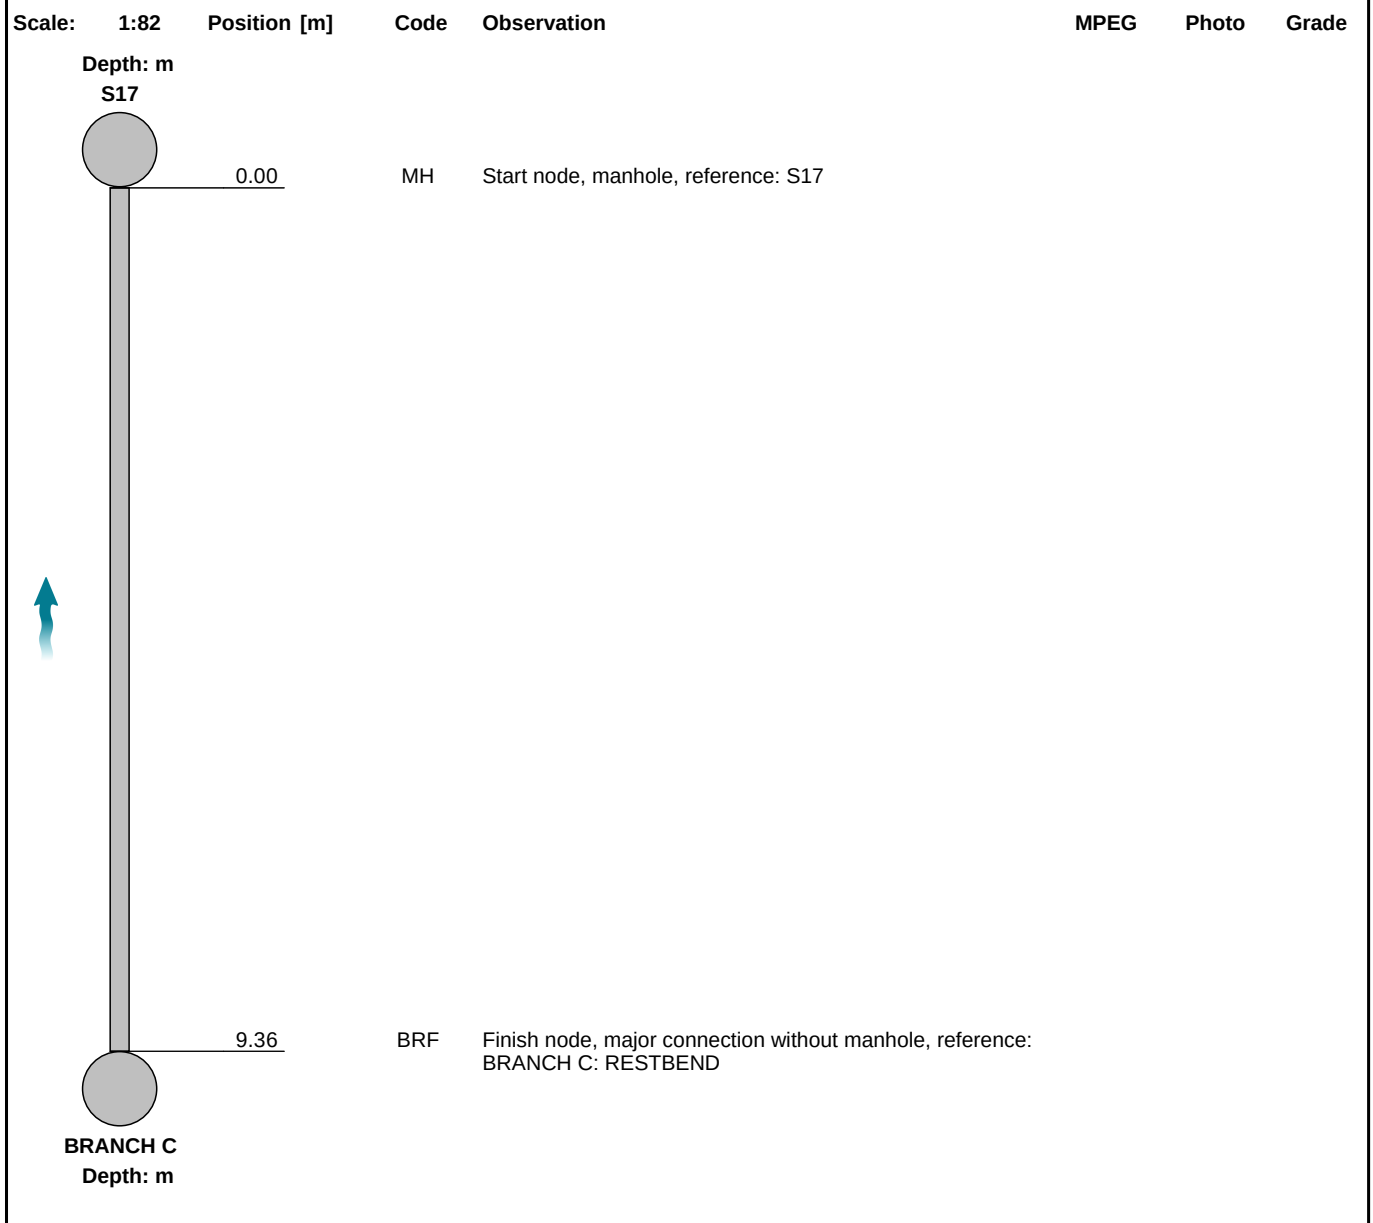

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0




Section Inspection - 10/05/2025 - S17X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
20	1	10/05/25	10:45	Not Specified	Not Specified	Not Specified	S17X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
Not Specified		Not Specified		Not Specified	Not Specified	Not Specified	Not Specified

Town or Village:		Inspection Direction: Downstream		Upstream Node: S17	
Road:		Inspected Length: 19.50 m		Upstream Pipe Depth:	
Location:		Total Length: 19.50 m		Downstream Node: S18	
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use: Surface water			Pipe Shape: Circular		
Type of Pipe:			Dia/Height: 150 mm		
Flow Control:			Material: Polyvinyl chloride		
Year Constructed: Not Specified			Lining Type: No Lining		
Inspection Purpose:			Lining Material: No Lining		

Comments:

Recommendations:

Scale:	1:169	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: m S17  0.00 MH Start node, manhole, reference: S17							

Construction Features

Miscellaneous Features

Structural Defects

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Inspection - 10/05/2025 - S18X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
21	1	10/05/25	11:14	Not Specified	Not Specified	Not Specified	S18X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
Not Specified		Not Specified		Not Specified	Not Specified	Not Specified	Not Specified

Town or Village:	Inspection Direction: Downstream	Upstream Node: S18
Road:	Inspected Length: 13.86 m	Upstream Pipe Depth:
Location:	Total Length: 13.86 m	Downstream Node: S19
Surface Type:	Joint Length:	Downstream Pipe Depth:
Use: Surface water	Pipe Shape: Circular	
Type of Pipe:	Dia/Height: 150 mm	
Flow Control:	Material: Polyvinyl chloride	
Year Constructed: Not Specified	Lining Type: No Lining	
Inspection Purpose:	Lining Material: No Lining	

Comments:
Recommendations:

Scale: 1:120	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: m S18						
	0.00	MH	Start node, manhole, reference: S18			
	11.84	CN	Connection other than junction at 1 o'clock, 150mm dia			
	13.86	MHF	Finish node, manhole, reference: S19			
S19 Depth: m						

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Inspection - 10/05/2025 - BRANCH A(2X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
22	1	10/05/25	11:16	Not Specified	Not Specified	Not Specified	BRANCH A(2X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
Not Specified		Not Specified		Not Specified	Not Specified	Not Specified	Not Specified

Town or Village:		Inspection Direction: Upstream		Upstream Node: BRANCH A(2	
Road:		Inspected Length: 6.07 m		Upstream Pipe Depth:	
Location:		Total Length: 6.07 m		Downstream Node: S19	
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use: Surface water			Pipe Shape: Circular		
Type of Pipe:			Dia/Height: 100 mm		
Flow Control:			Material: Polyvinyl chloride		
Year Constructed: Not Specified			Lining Type: No Lining		
Inspection Purpose:			Lining Material: No Lining		

Comments:

Recommendations:

Scale: 1:53 Position [m] Code Observation MPEG Photo Grade

Depth: m
S19



0.00

MH

Start node, manhole, reference: S19

2.59

D

Deformed sewer or drain, 5%: DINT IN PIPE/SQUASHED

1 / 2

6.07

BRF

Finish node, major connection without manhole, reference: BRANCH A(2

BRANCH A(2
Depth: m

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
1	0.0	0.0	0.0	1.0	1	1.0	0.2	1.0	2.0




Section Inspection - 10/05/2025 - BRANCH A(3X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
23	1	10/05/25	11:18	Not Specified	Not Specified	Not Specified	BRANCH A(3X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
Not Specified		Not Specified		Not Specified	Not Specified	Not Specified	Not Specified

Town or Village:		Inspection Direction: Upstream		Upstream Node: BRANCH A(3	
Road:		Inspected Length: 2.27 m		Upstream Pipe Depth:	
Location:		Total Length: 2.27 m		Downstream Node: S21	
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use: Surface water		Pipe Shape: Circular			
Type of Pipe:		Dia/Height: 100 mm			
Flow Control:		Material: Polyvinyl chloride			
Year Constructed: Not Specified		Lining Type: No Lining			
Inspection Purpose:		Lining Material: No Lining			

Comments:
Recommendations:

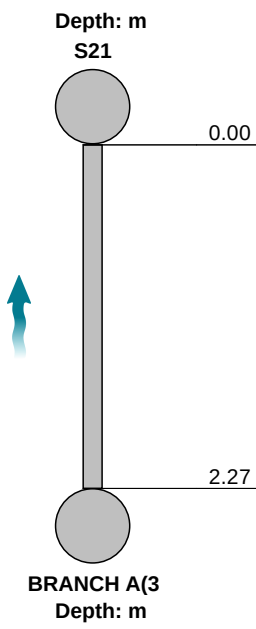Scale:	1:50	Position [m]	Code	Observation	MPEG	Photo	Grade
							
Depth: m							
S21		0.00	MH	Start node, manhole, reference: S21			
		2.27	GYF	Finish node, gully, reference: BRANCH A(3: GULLY			
BRANCH A(3							
Depth: m							

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Inspection - 10/05/2025 - S21X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
24	1	10/05/25	11:19	Not Specified	Not Specified	Not Specified	S21X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
Not Specified		Not Specified		Not Specified	Not Specified	Not Specified	Not Specified

Town or Village:		Inspection Direction:	Downstream	Upstream Node:	S21
Road:		Inspected Length:	16.19 m	Upstream Pipe Depth:	
Location:		Total Length:	16.19 m	Downstream Node:	S22
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use:	Surface water			Pipe Shape:	Circular
Type of Pipe:				Dia/Height:	150 mm
Flow Control:				Material:	Polyvinyl chloride
Year Constructed:	Not Specified			Lining Type:	No Lining
Inspection Purpose:				Lining Material:	No Lining

Comments:
Recommendations:

Scale:	1:141	Position [m]	Code	Observation	MPEG	Photo	Grade
Depth: m							
S21							
		0.00	MH	Start node, manhole, reference: S21			
		16.19	MHF	Finish node, manhole, reference: S22			
S22 Depth: m							

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Inspection - 10/05/2025 - BRANCH A(4X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
25	1	10/05/25	11:21	Not Specified	Not Specified	Not Specified	BRANCH A(4X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
Not Specified		Not Specified		Not Specified	Not Specified	Not Specified	Not Specified

Town or Village:		Inspection Direction: Upstream		Upstream Node: BRANCH A(4	
Road:		Inspected Length: 4.13 m		Upstream Pipe Depth:	
Location:		Total Length: 4.13 m		Downstream Node: S22	
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use: Surface water			Pipe Shape: Circular		
Type of Pipe:			Dia/Height: 100 mm		
Flow Control:			Material: Polyvinyl chloride		
Year Constructed: Not Specified			Lining Type: No Lining		
Inspection Purpose:			Lining Material: No Lining		

Comments:

Recommendations:

Scale: 1:50 Position [m] Code Observation MPEG Photo Grade

Depth: m
S22



0.00

MH

Start node, manhole, reference: S22

4.13

GYF

Finish node, gully, reference: BRANCH A(4: GULLY

BRANCH A(4
Depth: m

Construction Features

Miscellaneous Features

Structural Defects

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Inspection - 10/05/2025 - BRANCH B(2X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
26	1	10/05/25	11:22	Not Specified	Not Specified	Not Specified	BRANCH B(2X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
Not Specified		Not Specified		Not Specified	Not Specified	Not Specified	Not Specified

Town or Village:		Inspection Direction: Upstream		Upstream Node: BRANCH B(2	
Road:		Inspected Length: 14.96 m		Upstream Pipe Depth:	
Location:		Total Length: 14.96 m		Downstream Node: S22	
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use: Surface water			Pipe Shape: Circular		
Type of Pipe:			Dia/Height: 150 mm		
Flow Control:			Material: Polyvinyl chloride		
Year Constructed: Not Specified			Lining Type: No Lining		
Inspection Purpose:			Lining Material: No Lining		

Comments:

Recommendations:

Scale: 1:130 Position [m] Code Observation MPEG Photo Grade

Depth: m
S22



0.00

MH

Start node, manhole, reference: S22



14.96

GYF

Finish node, gully, reference: BRANCH B(2: GULLY

BRANCH B(2
Depth: m

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0




Section Inspection - 10/05/2025 - S22X

Item No.	Insp. No.	Date	Time	Client's Job Ref	Weather	Pre Cleaned	PLR
27	1	10/05/25	11:24	Not Specified	Not Specified	Not Specified	S22X
Operator		Vehicle		Camera	Preset Length	Legal Status	Alternative ID
Not Specified		Not Specified		Not Specified	Not Specified	Not Specified	Not Specified

Town or Village:		Inspection Direction: Upstream		Upstream Node: S22	
Road:		Inspected Length: 2.45 m		Upstream Pipe Depth:	
Location:		Total Length: 2.45 m		Downstream Node: S23	
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use: Surface water			Pipe Shape: Circular		
Type of Pipe:			Dia/Height: 150 mm		
Flow Control:			Material: Polyvinyl chloride		
Year Constructed: Not Specified			Lining Type: No Lining		
Inspection Purpose:			Lining Material: No Lining		

Comments:
Recommendations:

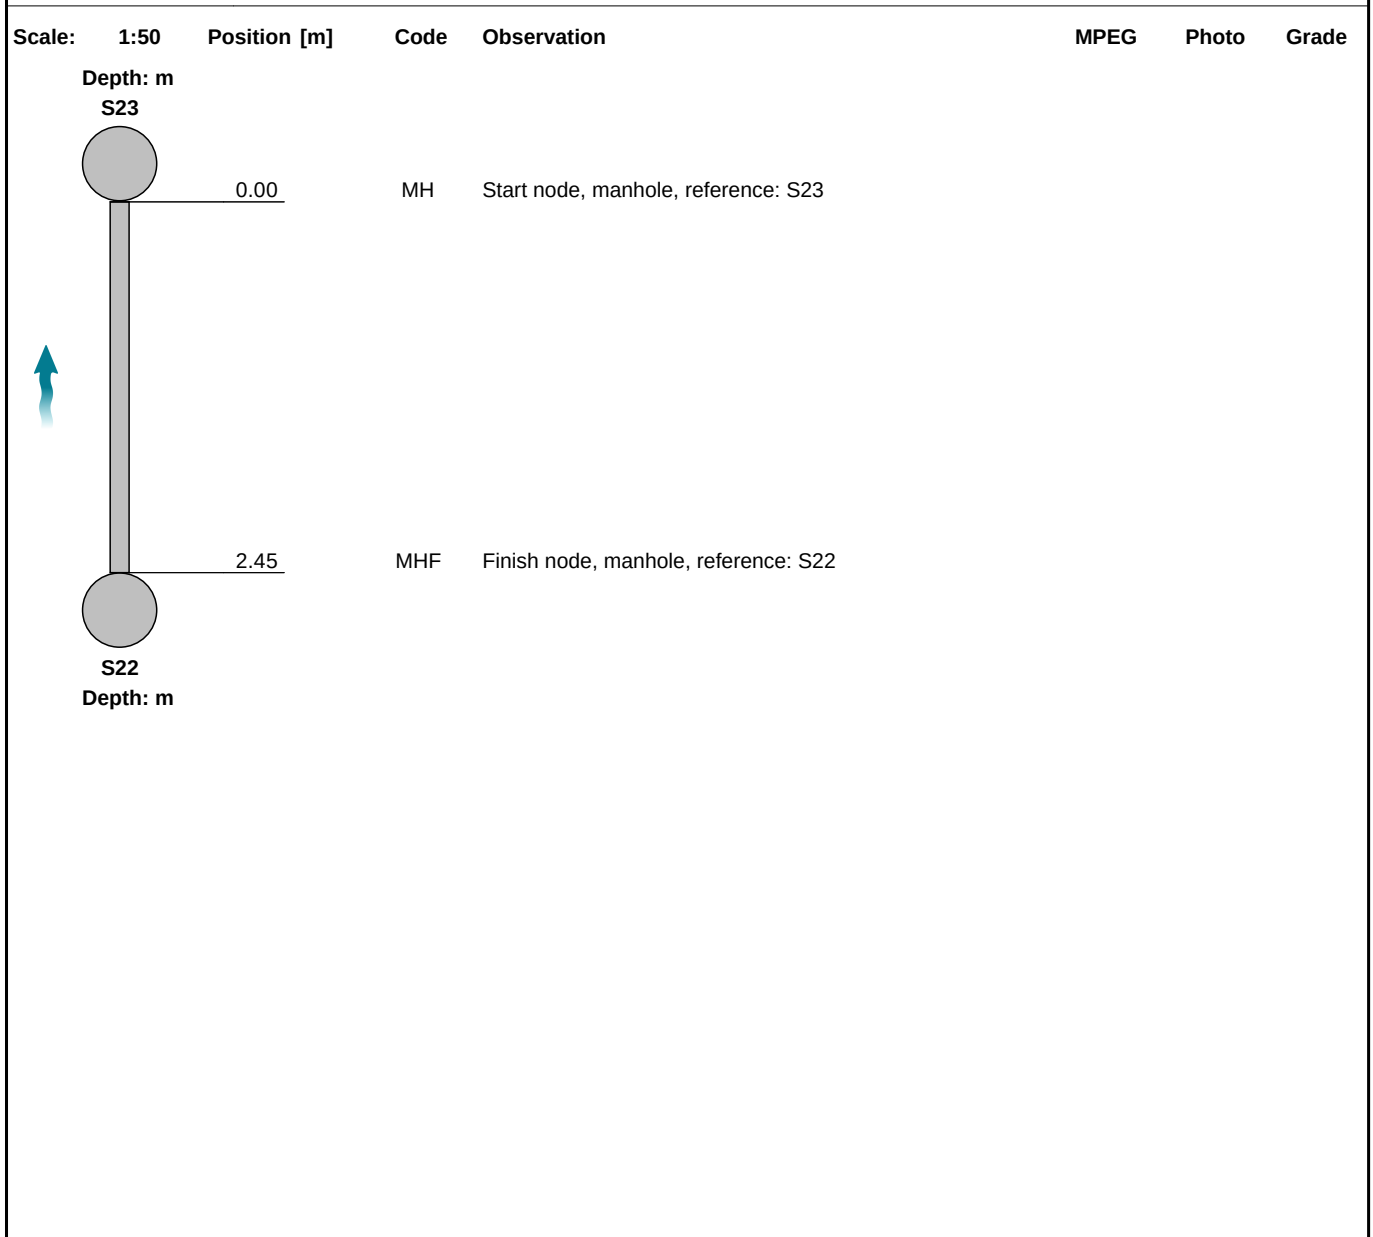

Construction Features					Miscellaneous Features				
Structural Defects					Service & Operational Observations				
STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0



Section Inspection - 13/05/2025 - BRANCH A(5X

Item No. 28	Insp. No. 1	Date 13/05/25	Time 11:02	Client's Job Ref Not Specified	Weather Not Specified	Pre Cleaned Not Specified	PLR BRANCH A(5X
Operator Not Specified		Vehicle Not Specified		Camera Not Specified	Preset Length Not Specified	Legal Status Not Specified	Alternative ID Not Specified

Town or Village:		Inspection Direction: Upstream		Upstream Node: BRANCH A(5	
Road:		Inspected Length: 3.07 m		Upstream Pipe Depth:	
Location:		Total Length: 3.07 m		Downstream Node: S11	
Surface Type:		Joint Length:		Downstream Pipe Depth:	
Use: Surface water			Pipe Shape: Circular		
Type of Pipe:			Dia/Height: 100 mm		
Flow Control:			Material: Polyvinyl chloride		
Year Constructed: Not Specified			Lining Type: No Lining		
Inspection Purpose:			Lining Material: No Lining		

Comments:

Recommendations:

Scale: 1:50 Position [m] Code Observation MPEG Photo Grade

Depth: m
S11



0.00

MH

Start node, manhole, reference: S11

3.07

BRF

Finish node, major connection without manhole, reference: BRANCH A(5

BRANCH A(5
Depth: m

Construction Features

Structural Defects

Miscellaneous Features

Service & Operational Observations

STR No. Def	STR Peak	STR Mean	STR Total	STR Grade	SER No. Def	SER Peak	SER Mean	SER Total	SER Grade
0	0.0	0.0	0.0	1.0	0	0.0	0.0	0.0	1.0
