

4th Floor Canada House

Internal Works: Method Statement (January 2024)

Please also refer to existing and proposed drawings.

A) and B) Main Meeting Room and Breakout Room

- Removal of modern raised floor including the following approach:
 - i. Strip up the existing modern carpet tiles.
 - ii. Removal of modern key clamp balustrading and pedestals on raised floor entrances (Fig 1).
 - iii. Carefully remove of all existing modern raised floor which has been installed and built up against the existing doors, skirting and walls (Figs 1 and 2).
 - iv. Re-screed the modern sub-floor (where required).
 - v. Re-lay existing modern carpet tiles.
- Installation of 4x new surface mounted socket outlets to provide power supply in Breakout Room.
- Insertion of modern 5 metre full height stud and board wall (Fig 7).



Figs 1, 2 and 3: Modern raised floor within Breakout Room and Sting Room which covers the existing doors, skirting and radiators. Figure 4: Example of raised floor method of construction (from other section of the building).

D) Sting Room

- Removal of modern 5 metre full height stud and board wall and repainting of column and surrounding area (Figs 5 and 6).
- Relocation of a 5 metre full height stud and board wall to enlarge the size of the Sting Room, built and cut around existing features (columns, skirting and beams) with no direct works/fixings (Fig 7).
- Removal of existing door well and infill space with raised floor abutting up to skirting and door (to match existing and align with the remainder of the Sting Room).



Figs 5 and 6: Existing modern 5 metre full height stud and board wall to be removed and relocated to enlarge the Sting Room. This would be built against existing features with no direct fixings.

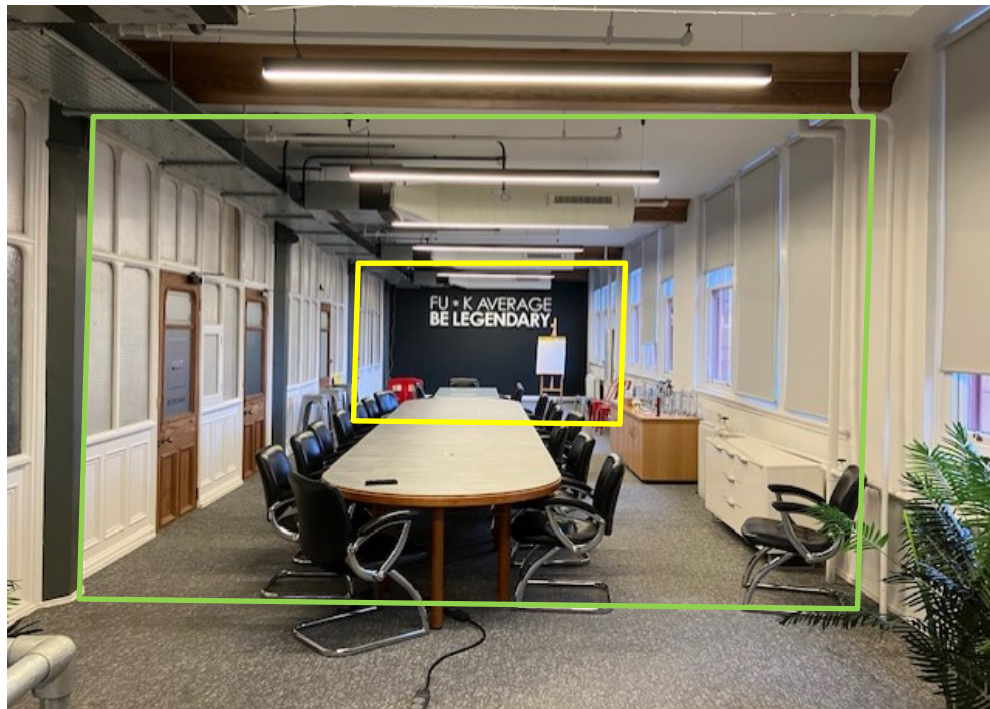


Fig 7: Position of re-positioned modern stud wall (outlined in yellow) and new wall (outlined in green), utilising the same method and form of construction.
