



The University of Manchester Network Transformation Project (WLAN)



Dover Street Installation Pack

Prepared by

 **Projective**
Consulting Ltd.

Contents

Document Version	3
1 Overview	4
1.1 AP Name Key.....	4
1.2 WLAN AP Overview	5
1.3 Installation Guidance Notes (Please Read)	6
2 AP Locations.....	7
2.1 Dover Street Level -10 - Basement Floor	7
3 AP Locations.....	10
3.1 Dover Street Level 00 - Ground Floor	10
4 AP Locations.....	12
4.1 Dover Street Level 10 - First Floor.....	12
5 AP Locations.....	15
5.1 Dover Street Level 20 - Second Floor	15

Document Version

<i>Date</i>	<i>Name</i>	<i>Reason</i>	<i>Date</i>
Draft 0.1	Benjamin Bedford	Report Template Created	28/06/2019
Issue 0.1	Shelley Horan	Report Created	07/07/2023
Issue 0.2	Shelley Horan	Amendments as per Paul Hopper	14/07/2023
Issue 0.3	Paul Hopper	Amendments as per LBC	22/08/2023

Confidentiality Notice

The contents of this document are confidential and proprietary to Roc Technologies Limited (Roc). This document is submitted on the condition that the recipient does not disclose the information contained herein to any third party without the written consent of Roc. By receiving the Roc submission of this document, the recipient further agrees not to disclose the contents hereof internally other than to those of its agents, principals, representatives, consultants or employees who need to know these contents for the purposes of the recipient's evaluation of the document.

The recipient agrees to inform such persons of the confidential nature of the contents hereof and to obtain their agreement to preserve the confidentiality hereof to the same extent as the recipient. The recipient further agrees to treat the confidential information contained herein with at least the same level of care as it takes with respect to its own confidential information, but in no event with less than reasonable care.

1 Overview

1.1 AP Name Key

This document presents the final position of all APs within this location following a detailed survey.

AP naming convention:

New or refreshed APs will be named using the following format

FXX-T-M(A)

Where:

- F = Floor Number
- XX = AP Number
- T = AP Type
 - H = AP-535
 - L = AP-515
 - B = AP-303
- M = Mount Type
 - C = Ceiling or other horizontal mounting e.g. cable tray
 - W= Wall
 - O = Oberon Bracket
- (A) = Action - AP locations
 - R = Refresh
 - M = Move
 - N = New

So, for example, a ceiling mount AP-535, which is the first AP on floor 4 and is to be moved from an existing wall mount location, would be named:

401-H-C(M)

Other AP labels

(D) = Decommission AP location

There may be a requirement to fully decommission an AP position within the site. These AP locations have been marked with a (D). This AP position is no longer required.

(K) = Keep AP location and leave AP (AP does not need refreshing\replacing)

These APs are already of a minimum standard and do not need any action.

Cabinet and comms rooms locations that were identified during the survey are marked on the floorplan with red hatching.

1.2 WLAN AP Overview

Below highlights the total AP(s) following refresh and installation activity (Total APs) across each floor.

The New AP Hardware section highlights the number of APs required per model that you will require*.

Level	(M)	(N)	(D)	Total	New AP Hardware		
					Aruba 515	Aruba 535	Aruba 303
Dover Street Level - 10 - Basement Floor	0	4	1	5	4	0	0
Dover Street Level 00 - Ground Floor	1	1	1	3	1	0	0
Dover Street Level 10 - First Floor	0	3	6	9	3	0	0
Dover Street Level 20 - Second Floor	0	1	1	3	1	0	0
Dover Street Level 30 - Third Floor	0	0	0	0	0	0	0
Total	1	9	9	20	9	0	0

The total new AP Hardware may not match the total numbers under each heading (R,K,D,M,N). Do not worry, the combined total 'New AP Hardware' will match the combined total of R,M,N as this represents the new APs to be installed.

Table Key:

R= APs that require replacement in their current position

K = APs that are to be left. No work is required to these APs

D = APs that require decommissioning. The AP location is no longer required

M = APs that need to be moved from existing location to a new location

N = Brand new AP location

1.3 Installation Guidance Notes (Please Read)


- 1) **Please** install APs whether refreshed, moved or new, as per the floor diagrams within this pack. To support the location of AP point, photos will be presented in this pack after each floor diagram. Please note: where access was not granted, photos are unavailable to aid the installation).
- 2) **Where AP locations are marked as (D) 'decommission'** please ensure you remove this AP.
- 3) **The plotted recommended AP locations** on each floor diagram **are the desired install location**. Should the direct location not be available due to restrictions, please advise the project team immediately.
- 4) **The APs should** be installed/mounted as per the naming convention on page 4.
- 5) **Each data point at the AP** is to be **labelled** with the patching details as to the terminated cabling to the Comms room patch panel and **recorded on the floor plan**.
- 6) The additional **AP stickers** that contain the Serial number, Mac address and barcode etc are **to be attached to the floor plan and with a clear line pointing to the AP location installed to**. This enables us to identify where each actual AP is once you have installed it.
- 7) **If the AP is marked to be moved**, please where possible re-use any existing cabling should it be deemed acceptable to re-use (refer to EPM PM19). There will be occasions where a new cable(s) will need to be run.
- 8) Please ensure you complete this document fully **to enable sign off of the site**.
- 9) Please refer to EPM PM19 for cabling policy and procedures.
- 10) **There may be AP locations that require installing outside of EPM PM19 procedures**. The photos that are provided for the install will correctly identify the location that has been approved for install.

Questions should be referred to the project team if not sure.

NOTE: When carrying out a **MOVE AP** task, the original AP location will be within a 3-meter radius. Any queries in relation to a MOVE AP, please contact the project team.

2 AP Locations

2.1 Dover Street Level -10 - Basement Floor

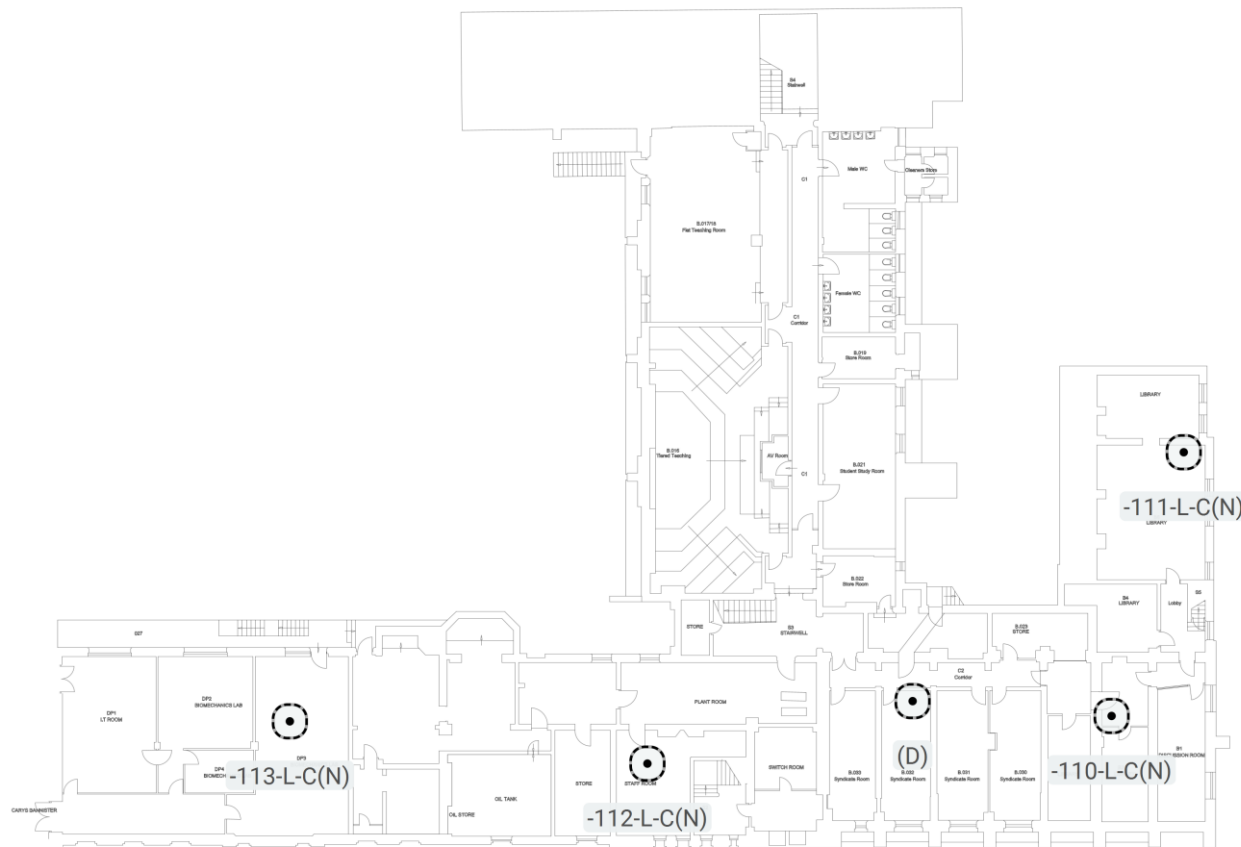



AP Name	Mounting	Location	Antenna Type
-110-L-C(N)		Dover Street Level -10 - Basement Floor	Internal




AP Name	Mounting	Location	Antenna Type
-111-L-C(N)	No access provided by UOM. Space does not look habitable.	Dover Street Level -10 - Basement Floor	Internal



AP Name	Mounting	Location	Antenna Type
-112-L-C(N)	Minor relocate from original planned location. Mount to existing tray in plant room.	Dover Street Level -10 - Basement Floor	Internal
[PHOTO UNAVAILABLE]			
AP Name	Mounting	Location	Antenna Type
-113-L-C(N)	No access provided by UoM.	Dover Street Level -10 - Basement Floor	Internal

3 AP Locations

3.1 Dover Street Level 00 - Ground Floor

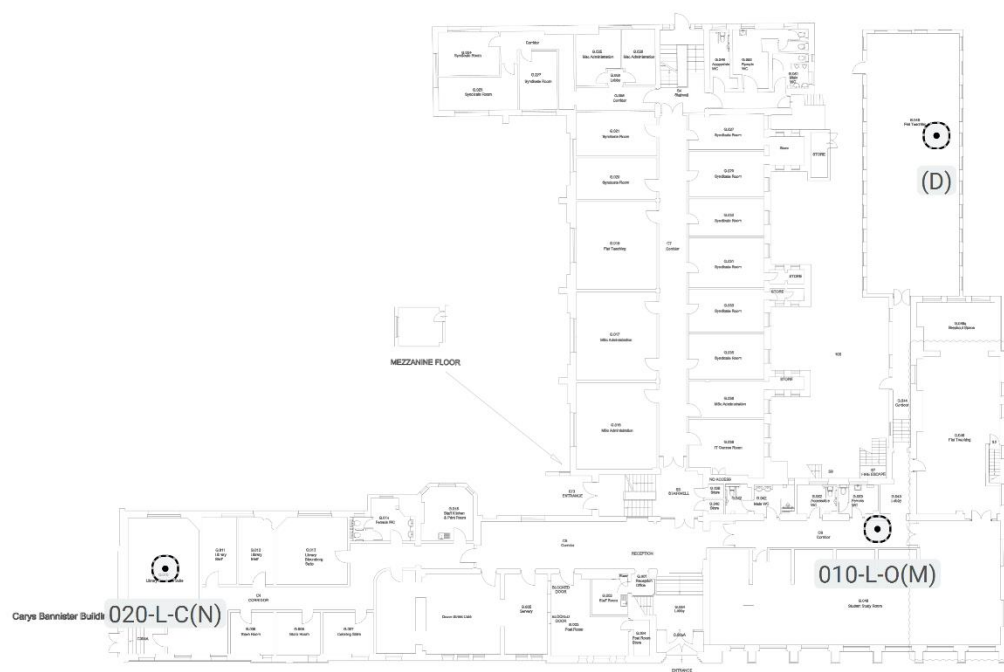




AP Name	Mounting	Location	Antenna Type
010-L-O(M)	Move existing AP lower so that it can be serviced if device fails/needs replacing.	Dover Street Level 00 - Ground Floor	Internal



AP Name	Mounting	Location	Antenna Type
020-L-C(N)		Dover Street Level 00 - Ground Floor	Internal

4 AP Locations

4.1 Dover Street Level 10 - First Floor

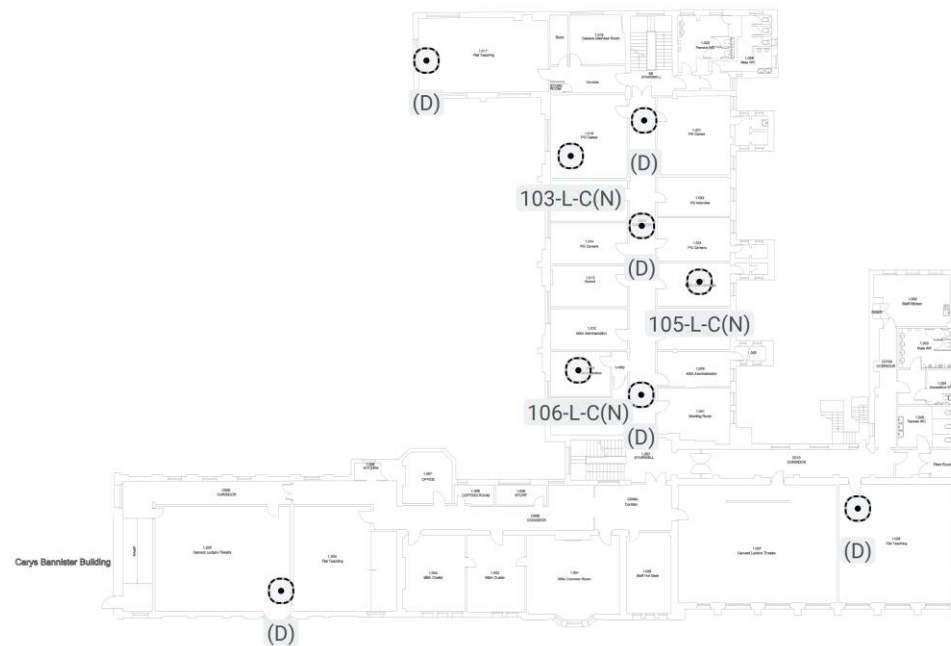




AP Name	Mounting	Location	Antenna Type
103-L-C(N)		Dover Street Level 10 - First Floor	Internal



AP Name	Mounting	Location	Antenna Type
105-L-O(N)	Ap to be wall mounted near existing containment, with possible use of existing data port.	Dover Street Level 10 - First Floor	Internal

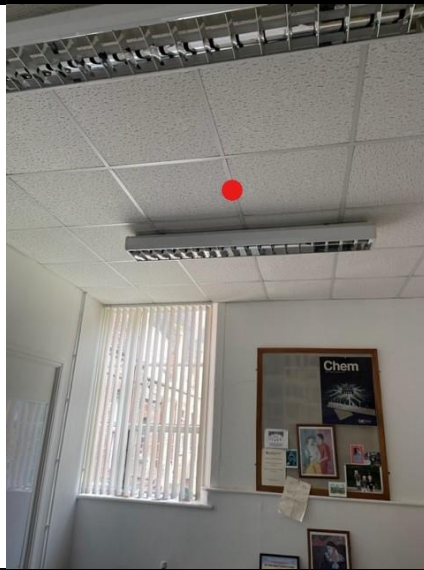


AP Name	Mounting	Location	Antenna Type
106-L-C(N)		Dover Street Level 10 - First Floor	Internal

5 AP Locations

5.1 Dover Street Level 20 - Second Floor



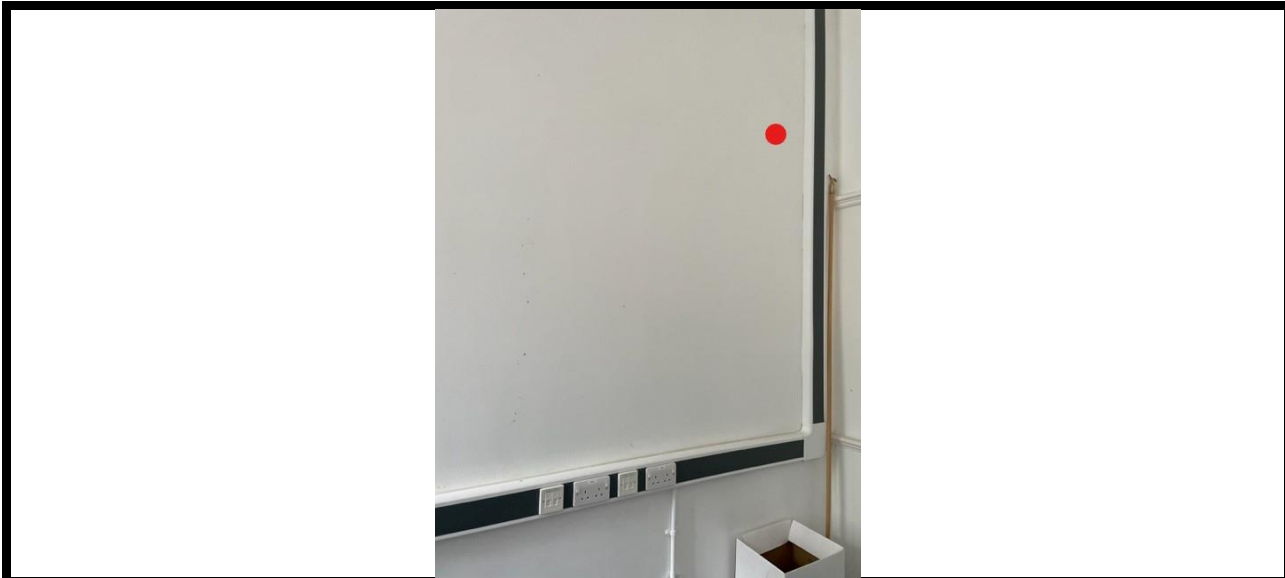

AP Name	Mounting	Location	Antenna Type
205-L-O(N)	AP to be wall mounted next to existing containment and possible use of existing data port.	Dover Street Level 20 - Second Floor	Internal
