




GEOSHIELD Verification Report



OVERVIEW PHOTOGRAPHS



Overview of verified area







GEOSHIELD Verification Report



OVERVIEW PHOTOGRAPHS

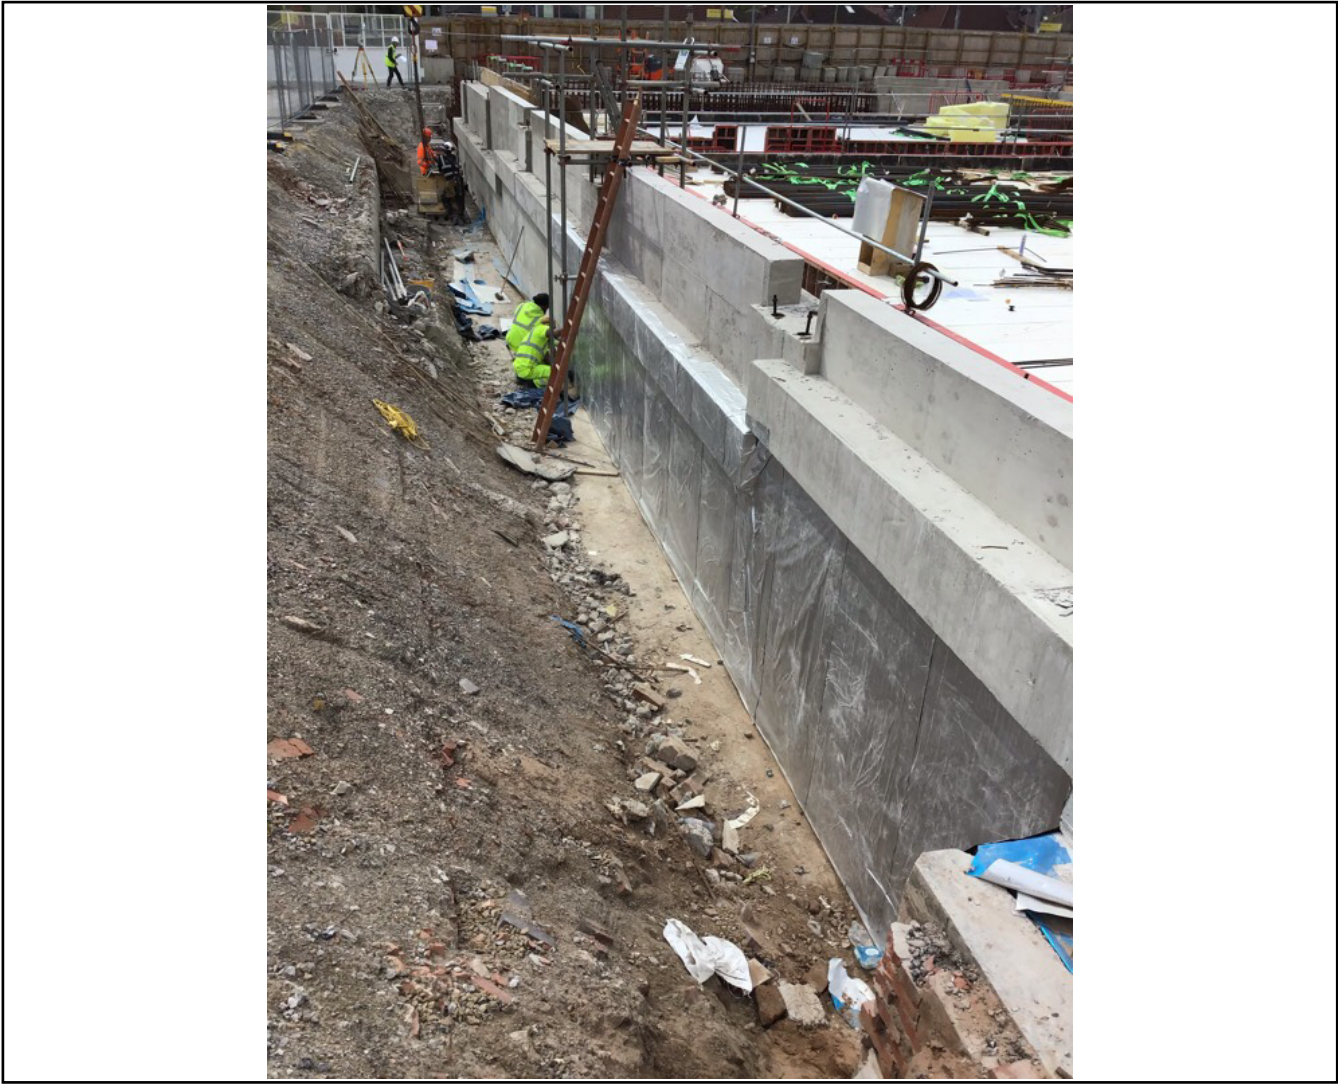

Overview of verified area






GEOSHIELD Verification Report



OVERVIEW PHOTOGRAPHS



Overview of verified area





GEOSHIELD Verification Report



VERIFICATION ITEM ONE

LOCATION/GRID LINE: Perimeter Termination

NOTES: GR SAM Application

Visqueen Gas Resistant Self Adhesive Membrane has been used terminate the design to the perimeter of the the slab. The Visqueen Standard Gas Barrier installed has been lapped up the side of the concrete slab and sections of Visqueen GR SAM have been



lapped 300mm down to create a continuous barrier as can be seen in the right photo.

Air lancing was not undertaken due to no access however a thorough pick and probe

GEOSHIELD Verification Report

VERIFICATION ITEM ONE



test was carried out. Some small areas of damage were found which were remediated on site. All material installed to manufacturers specification and design, to an excellent overall standard.
