

070452-CUR-00-XX-DR-GE-002-V01

Gorton Library


Foundation Pit Cross Sectional Sketches

HP01

Comments:

Not to scale.

- Hand pit terminated at 0.60m bgl on concrete.
- Groundwater not encountered.
- Concrete foundation encountered at 0.60m bgl.
- Concrete foundation extends more than 1.20m away from building (measured from face of wall, not face of column).
- Base/thickness of concrete foundation not identified due to restrictions preventing extension of trial pit.
- Further detailed information in log HP01.

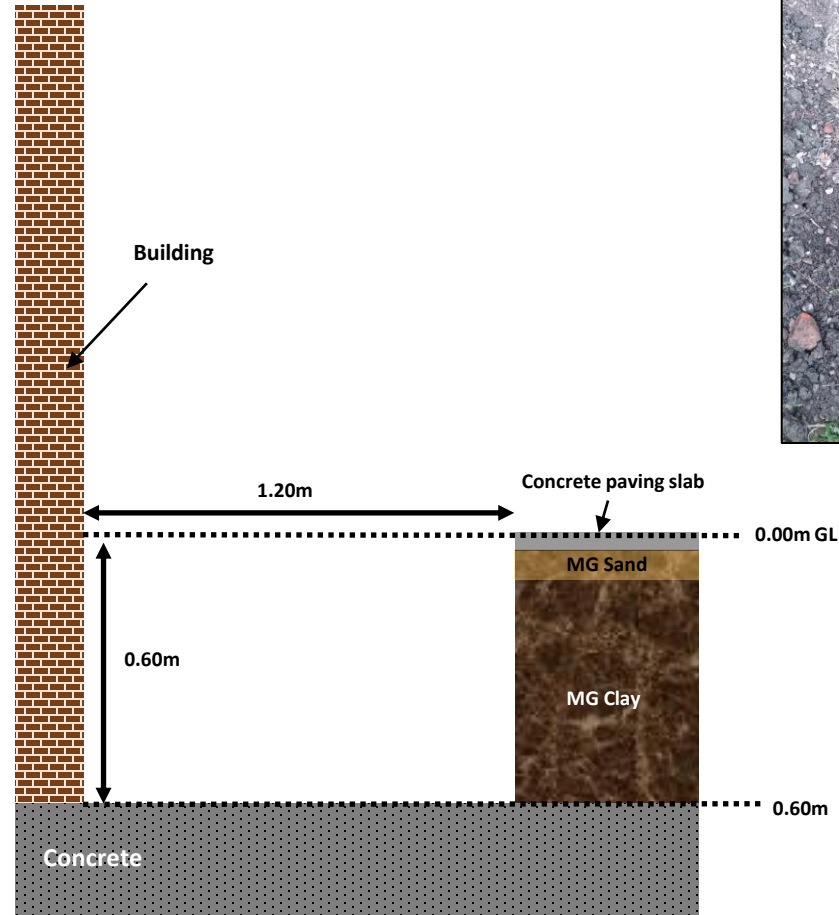

070452-CUR-00-XX-DR-GE-002-V01

Gorton Library


Foundation Pit Cross Sectional Sketches

HP02

Comments:

Not to scale.

- Hand pit terminated at 1.05m bgl in natural clay.
- Groundwater not encountered.
- Concrete foundation extends 0.15m away from building wall.
- Concrete foundation encountered at 0.60m bgl and the base of concrete slab identified at 0.80m bgl with a thickness of 0.20m.
- Further detailed information in log HP02.

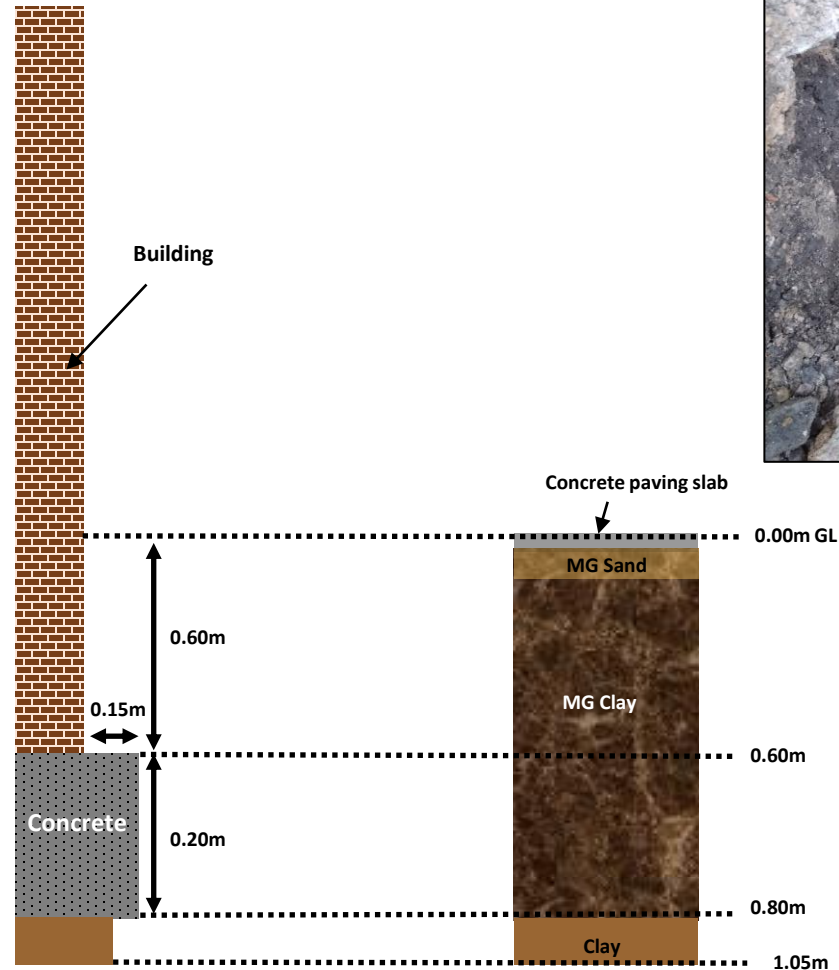

070452-CUR-00-XX-DR-GE-002-V01

Gorton Library


Foundation Pit Cross Sectional Sketches

HP03

Comments:

Not to scale.

- Hand pit terminated at 0.77m bgl in Made Ground due to water in the base of hand pit.
- Groundwater was encountered at 0.60m bgl.
- Concrete foundation projects 0.69m from building wall.
- Concrete foundation encountered at 0.60m bgl and the base of concrete foundation identified at 0.77m bgl with a thickness of 0.17m bgl.
- Further detailed information in log HP03.

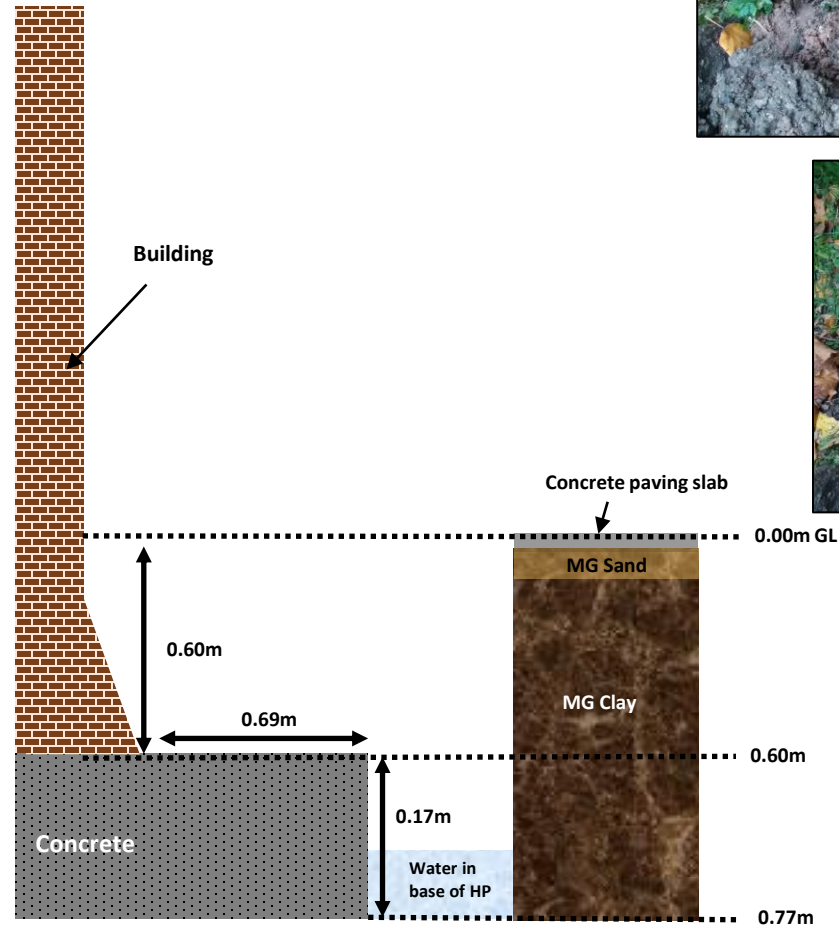

070452-CUR-00-XX-DR-GE-002-V01

Gorton Library

Foundation Pit Cross Sectional Sketches

HP04

Comments:

Not to scale.

- Hand pit terminated at 1.00m bgl in natural clay.
- Groundwater not encountered.
- Concrete foundation encountered at ground level, extending to 0.20m bgl, formed on Made Ground.
- Further detailed information in log HP04.

