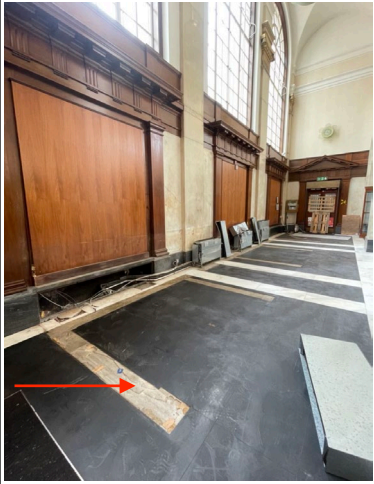


PROJECT NO:	5287		ISSUE DATE:	31 AUG 22'
PROJECT TITLE	LUCKY CAT, MANCHESTER			
AREAS:	BASEMENT, GROUND FLOOR, MEZZANINE & FACADE			
REQUEST FOR RESTORATION SCHEDULE				
	REVISION: A			
				STATUS
	NOT CRITICAL			
	CRITICAL (Elements with an impact on the heritage statement)			
	CRITICAL (Elements with no impact on heritage statement)			
Item	Restoration Required	Photo	Location	Date Reqd
1	Floor marble to be repaired/ re-installed where there is a missing tile or cracked marble		LHS Entrance	28/7/22

2	Timber wall panels to be made good or repaired as close to original as possible, remove all tapes, markings and scratches		General	28/7/22
3	Existing marble walls to be strip clean and repaired where chipped, scratched and/ or cracked		General	28/7/22

4	Existing marble walls to be strip clean and repaired where chipped, scratched and/ or cracked		LHS Doorway	28/7/22
5	Doormat to be replaced; All material on door panels and door gears to be inspected and made good where necessary		LHS Doorway	28/7/22

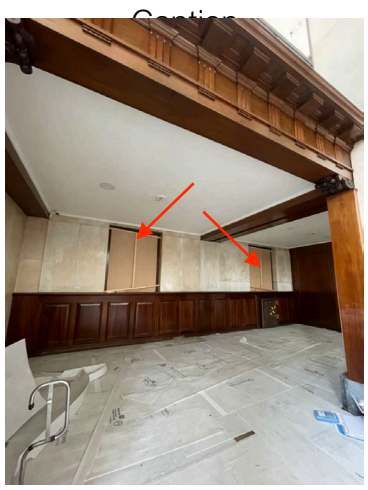
6	Jamie Italian's branding to be carefully removed on RHS entrance door; replace clear glass panel if necessary while maintaining all door gear and heritage element on panel		RHS Doorway	28/7/22
---	--	--	-------------	---------

Marble floor to be cleaned and make good as close to original as possible; remove any unused floor mounted floor boxes and close holes on floor where possible



Main Hall

28/7/22

8	Unknown pipe; MC to inspect and check whether it can be removed to allow more room for new booth seat and close hole on floor after		Room next to RHS entrance under Mezzanine	28/7/22
9	Remove timber panels in front of windows; MC to make good window frame and sill behind		Room next to RHS entrance under Mezzanine	28/7/22

10	Unable to inspect heritage timber flooring below; MC to inspect and make good flooring to match as close as original as possible and ensure it is free of stains, scratches and repair if necessary		Room next to RHS entrance under Mezzanine	28/7/22
11	MC to check feasibility to remove blackboard; clean & make good adjacent glass and timber feature panel to match original as much as possible; Remove timber panels in front of windows; MC to make good window frame and sill behind		Room next to RHS entrance under Mezzanine	28/7/22

12	MC to clean, make good and repair heritage materials; install new tile to match existing where necessary	Caption  The photograph shows a narrow archway leading into a kitchen. On either side of the archway are tall, dark wood pillars. The floor is made of dark, square tiles. Three red arrows point to the base of the pillars and the floor area, indicating the work to be done. A white electrical outlet is visible on the right pillar.	Archway into kitchen	28/7/22
13	MC to remove timber panel in front of windows and make good windows and sill behind.	 The photograph shows a room with wood-paneled walls and a patterned tile floor. A large window is on the left, and a door is on the right. A red arrow points to the top of the window frame, indicating the area to be worked on. A small, dark object is visible on the wall above the door.	PDR 3	28/7/22

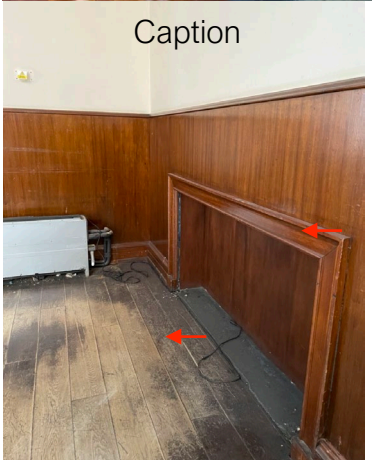
14	MC to carefully remove panel (behind heritage door) between PDRs without damaging heritage timber wall panelling		PDR 3	28/7/22
15	MC to remove all tapes and markings, clean and make good, as close to original as possible heritage fireplace, timber floor finishes and timber wall panels		PDR 3	28/7/22

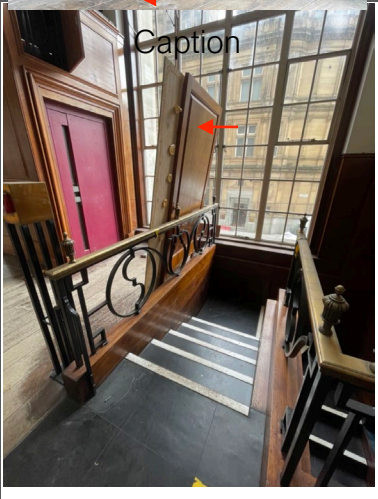
16	MC to remove all tapes and markings, clean and make good, as close to original as possible heritage fireplace, timber floor finishes and timber wall panels		PDR 2	28/7/22
----	---	--	-------	---------

17	MC to clean and make good all risers, treads, step nosings, railings and marble walls as close to original as possible. All cracked and/ or chipped marble to be repaired	Caption 	LHS Stairwell to Mezzanine	28/7/22
----	--	--	----------------------------	---------

18	MC to clean and make good heritage timber flooring and wall panelling as much as possible to match original	 The top photograph shows a long, narrow room with wooden flooring and wall panelling. Red arrows point to specific areas on the floor and wall. The bottom photograph shows a corner of the room with wooden wall panelling and a window. Red arrows point to specific areas on the wall and floor.	LHS Mezzanine	28/7/22
----	--	--	------------------	---------

19	MC to inspect whether exposed wire can be removed and close and make good any floor holes after		LHS Mezzanine	28/7/22
20	MC to clean and make good all timber panels as close to original as possible		Doorway to BOH corridors	28/7/22

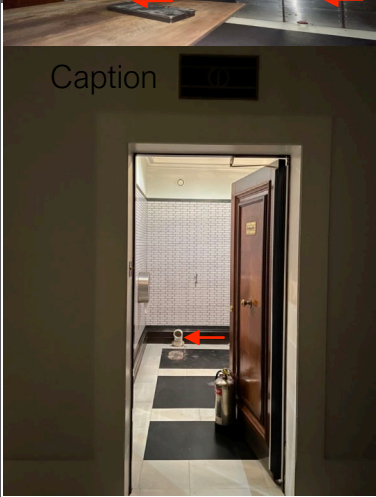
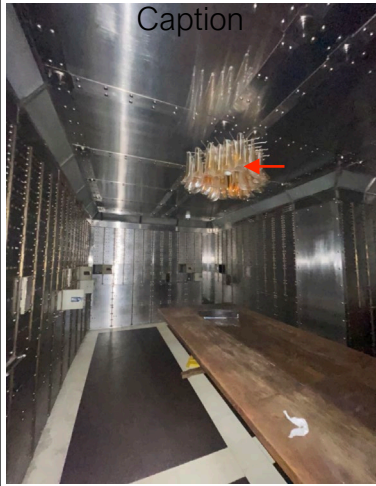
21	MC to clean and make good all timber panels, floor finish, fire place, close hole on panel, remove black board and finish as close to original as possible	Caption  Caption  	Central Mezzanine	28/7/22
----	---	---	----------------------	---------

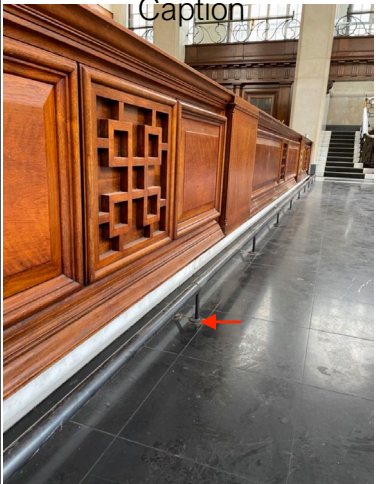
22	MC to clean and make good all timber panels, fix lift door panel and inspect if the lift can be operable		RHS Mezzanine	28/7/22
----	--	--	------------------	---------

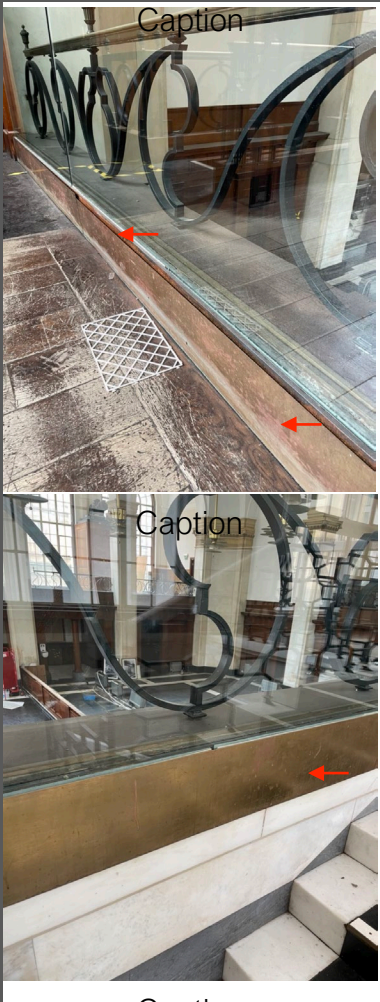
23	MC to clean, repair and make good all timber panels, floor finish, treads, tread nosings, risers, radiator (and tiling around) and railing as close to original as possible		RHS Stairwell to Mezzanine	28/7/22
----	--	---	-------------------------------	---------

24	MC to clean and make good all risers, treads, step nosings, railings and marble walls as close to original as possible. All cracked and/ or chipped marble to be repaired	 Caption Caption	LHS Stairwell to Basement	28/7/22
----	---	--	---------------------------	---------

25	MC to clean and make good internal finishes on ceiling, floor and wall in vault room; MC to inspect if light strip detail above deposit boxes are functioning, re-lamp per lighting consultant's specifications		tion Basement Vault Room	28/7/22
----	--	---	--	---------

26	Missing loo in WC #1	 Caption	Basement WCs	28/7/22
27	Pendant to be removed, retain existing wiring & fixing and connect to PL-02	 Caption	Basement Vault Room	28/7/22

28	Foot rail in front of ground floor bar panels to be removed and install new foot rail in brass, MT-01	Caption 	Ground Floor Bar	28/7/22
----	---	---	------------------	---------

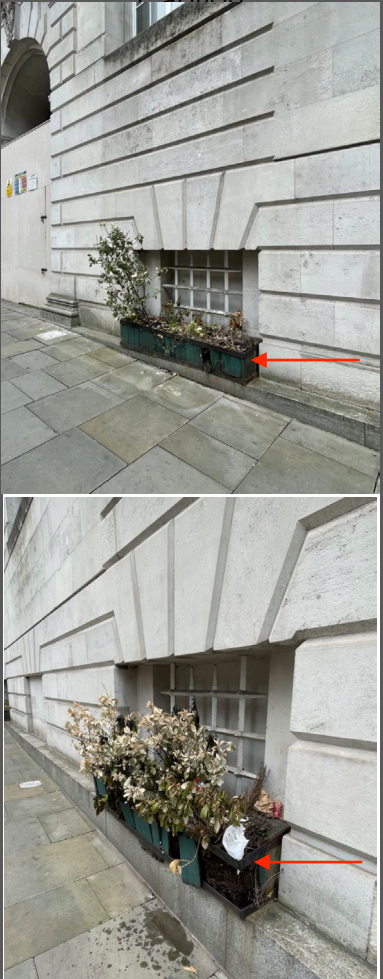
29	Existing brass skirtings are loose; MC to ensure all skirting to be secured, cleaned and made good	 Two photographs of the Mezzanine Balustrade. The top photo shows a close-up of the brass skirting on a wooden floor, with two red arrows pointing to loose areas. The bottom photo shows a wider view of the balustrade with a red arrow pointing to a loose section of the brass skirting.	Mezzanine Balustrade	28/7/22
----	--	--	-------------------------	---------

30	Drywalls to be repaired and re-painted in new paint colour		Mezzaline drywalls	28/7/22
31	Existing pendant to be removed; Retain all wiring, fixings and install new ceiling fitting		PDR 2	28/7/22

32	Existing pendant to be removed; Retain all wiring, fixings and install new ceiling fitting		PDR 3	28/7/22
----	--	--	-------	---------

33	All existing framed artwork to be removed, wall behind to be made good as close to original as possible		PDRs	28/7/22
----	--	---	------	---------

34	Remove existing flags and allow for new flags	Caption  Caption	On facade above both entrances facing King Street	28/7/22
----	---	--	---	---------

35	Remove existing flags and allow for new flags		On niches facing King Street	28/7/22
		Caption		
