

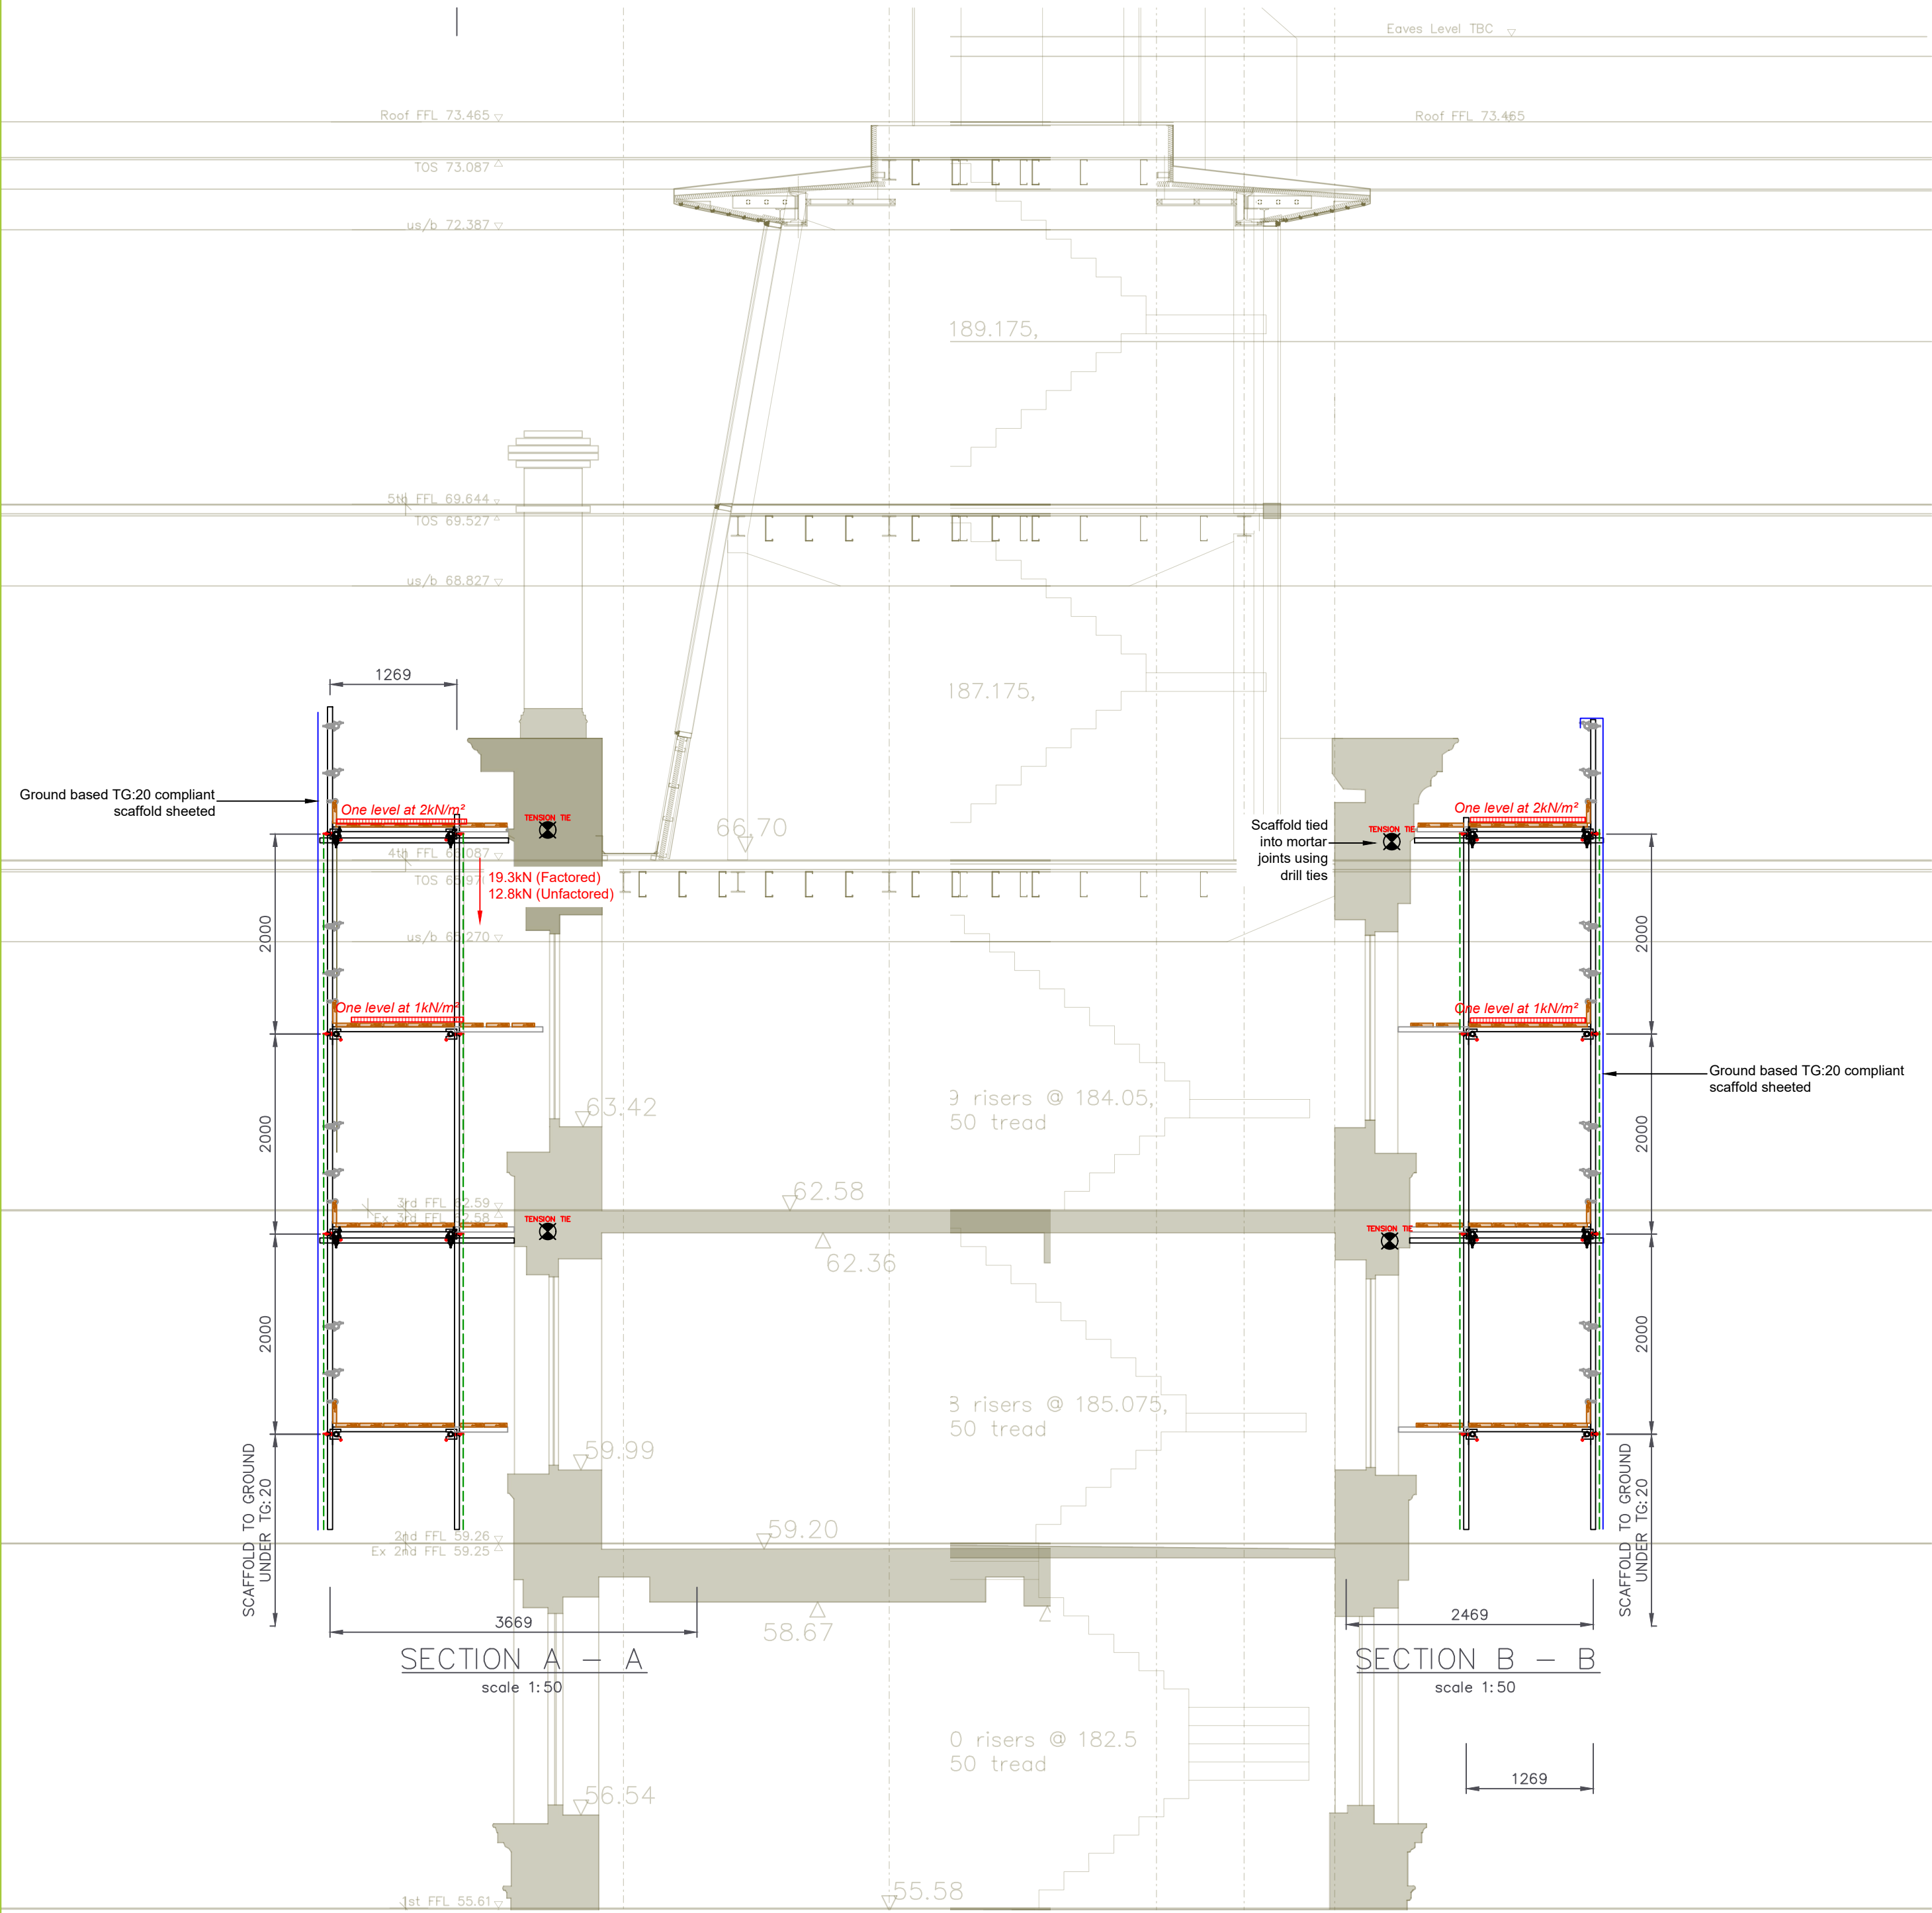


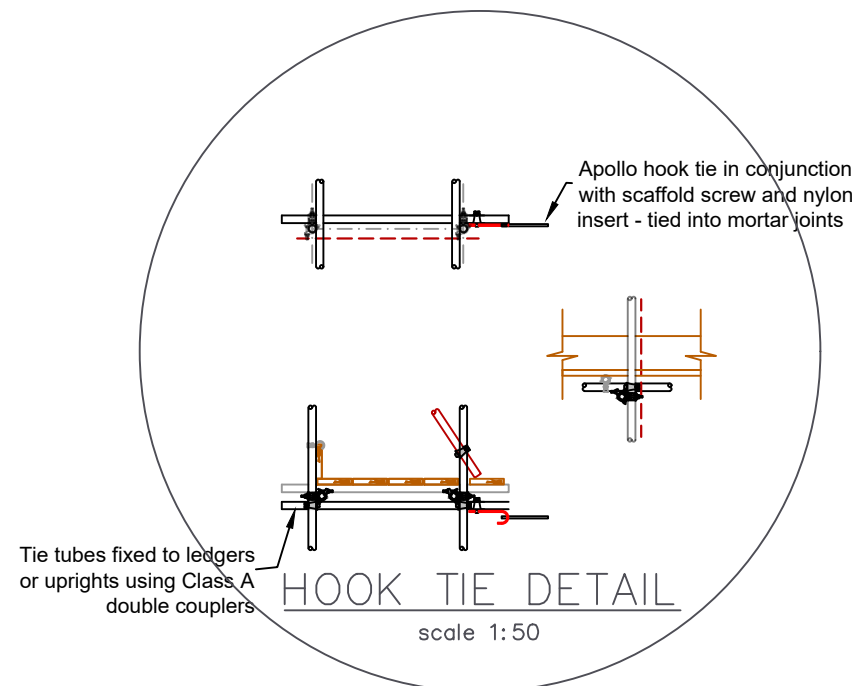

- ⚠ **RISK – ACCURACIES IN BUILDING LINE CAUSING SCAFFOLD TO BE DIMENSIONALLY INACCURATE**
Control Measure: Prior to erection the scaffold contractor and/or principal contractor should check the existing structure to ensure the scaffold can be based out and erected as detailed and inform Creator Ltd of any discrepancies.
- ⚠ **RISK – EXCESSIVE BAY SIZES INSTALLED DURING ERECTION**
Control Measure: The scaffold contractor must ensure that the maximum bay size installed are as indicated and should not be exceeded. It is the responsibility of the scaffold contractor to remedy any defects.
- ⚠ **RISK – OVERLOADING OF SCAFFOLD STRUCTURE**
Control Measure: The design service loads indicated should be closely site managed to ensure that only 2 number of working levels are present at one time. The load conditions of the scaffold should be clearly identified on the scaffag.
- ⚠ **RISK – OVERLOADING OF EXISTING STRUCTURE**
Control Measure: Principal contractor to employ a structural engineer to ensure the applied loads from the scaffold do not overload the existing structure. Creator Ltd to be contacted where structure is deemed unsafe to support scaffold structure.
- ⚠ **RISK – EXCESSIVE LIFT HEIGHTS CAUSING BUCKLING**
Control Measure: Maximum lift heights to be installed as detailed by the scaffold contractor and have a maximum tolerance of ±100mm
- ⚠ **RISK – OVERLOADING OF EXISTING STRATA**
Control Measure: Principal contractor to employ a structural engineer to ensure the applied loads from the scaffold do not overload the existing strata. Creator Ltd to be contacted where strata is deemed unsafe to support scaffold structure.

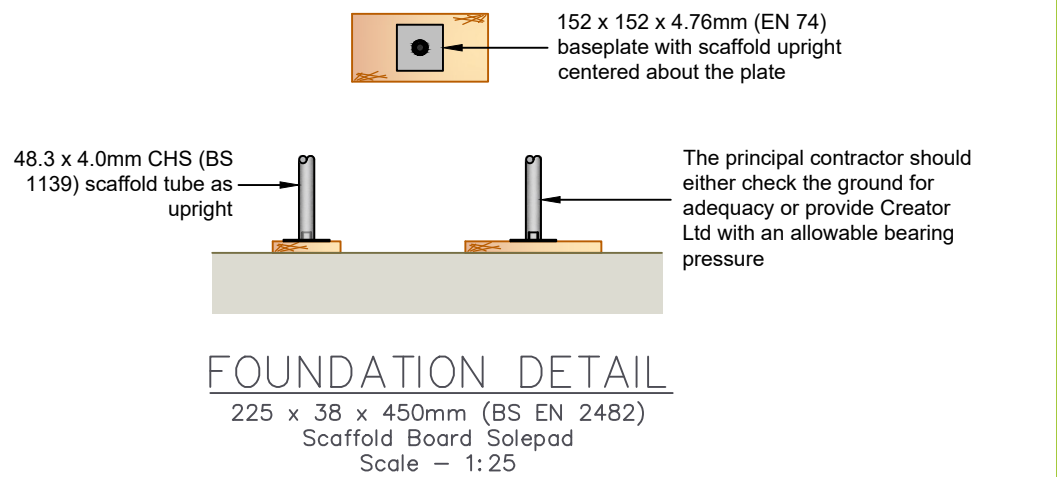

DOCUMENT REFERENCES
This design is to be read in conjunction with the following design drawings and/or documents:
CRE-IBN-082-001E_REPORT
APPENDIX A - CRE-IBN-082-001E_1,2,3,4.dwg

AMENDMENTS / REVISIONS					
REV	BY	DATE	CHECK	DATE	APP'D
E	AW	22.04.22	KRB	22.04.22	
D	APS	23.08.21	KRB	23.08.21	
C	SLS	17.08.21	KRB	17.08.21	
B	KRB	22.06.21			
A	CH	15.06.21	KRB	15.06.21	
-	EAS	02.06.21	MDB	03.06.21	KRB
REV	BY	DATE	CHECK	DATE	APP'D

ibn

FOR CONSTRUCTION

Project Number	Page Number	Scale	Rev
CRE-IBN-082-001E_recover	2	1 : 50,25	A2

ACCESS SCAFFOLD
CAVENDISH HOUSE
MANCHESTER
M1 5EE

SEE QUOTE

CREATOR
SCAFFOLD DESIGNS
& TEMPORARY WORKS CONSULTANTS LTD

Company Address:
Fullerton House, Fullerton Road,
Rotherham, S60 1DH
Contact Details:
Email: enquiries@creator-scaffolddesigns.co.uk
Tel: 0114 3610060
www.creator-scaffolddesigns.co.uk
