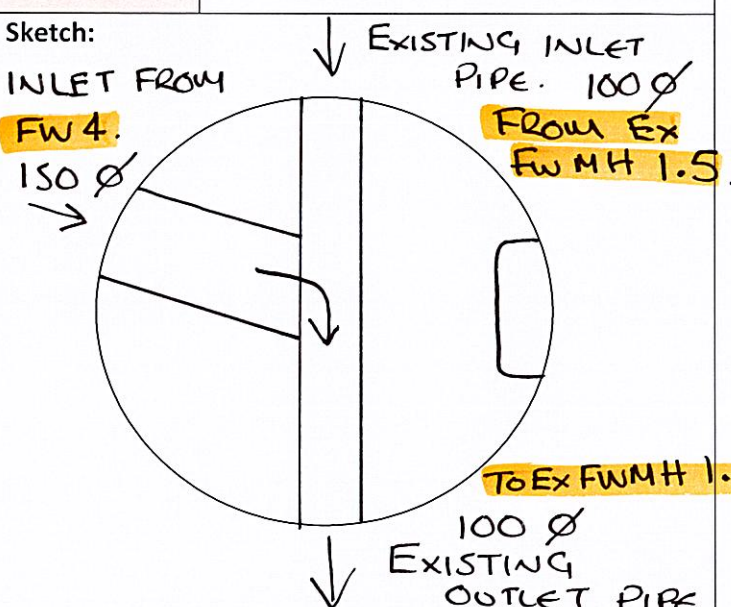


QA Form - Manholes

Installation of Manhole			Sheet No:
Project C376 WITHINGTON CDC			G.
Location:	F7	Drawing No:	22182-CCS-WCH006-XX-DR-S-93000
As built coordinates:	383777.955 392007.598	Date: 28/04/2025	
Cover Level:	32.840		
Manhole No:	F7	Type:	FOUL/SURFACE WATER/COMBINED
Invert:	~~31.204~~ 31.204. BA.	(circle as appropriate)	
Inverts and Diameter of pipes:	Upstream: Dia: 150mm Downstream: Dia: 100mm Inlet 1: 100mm Dia: Inlet 2: Dia: Inlet 3: Dia: Inlet 4: Dia: Inlet 5: Dia:	Sketch: 	
Chamber Details:	Dia. Size: 1050mm Overall depth: 1.616m Cover Depth: 100mm Biscuit Depth: 150mm Reducing Slab: 150mm	Position of step irons/fittings, orientation of cover/slab and branches (including backdrops) to be detailed.	
WORK TO BE INSPECTED	Accepted Yes/ No or N/a	Comments	MW Construction Eng/QA Signed as Checked:-
Setting out to drawing	YES	ON EXISTING LINE MOVED BY BAM AGREEMENT DUE TO SITE HOARDING	B.H. S
Trench excavation supported	YES	STEPPED BACK TO SUIT	B.H. S
Installation of concrete to channel	YES	PIPE CUT TO OPEN CHANNEL	B.H. S

QA Form - Manholes


Installation of drainage channel/first manhole ring	YES	AS DESIGN	
MWC Signature confirming invert/positioning check	B.H.G		Date 24/06/2025
Client Signature confirming invert/positioning check	Daniel Allen		Date 25/6/2025.

WORK TO BE INSPECTED	Accepted Yes/ No or N/A	Comments	MW Construction Eng/QA Signed as Checked:-
Installation of manhole rings to required levels	YES	Depths and No's of rings:	B.H.G
Installation of dropshafts/inlets above manhole invert	YES		B.H.G
Manhole Surround	YES	Details:	B.H.G
Backfilling to manhole to required level and layers as instructed in spec	YES		B.H.G
Biscuit Installation	YES	Type: PCC	B.H.G
Benching/Water proofing to Manhole	YES		B.H.G
Installation of Step Irons	YES	Type & Numbers:	B.H.G
Brickwork		No of courses:	B.H.G
Lid and Frame	YES	Cover Type: D400 100mm	B.H.G
Client Signature confirming Handover of Manhole:-			Date

QA Form - Manholes**MWC Signature confirming
Handover of Manhole:-**


B.H.S

Date 24/06/2025

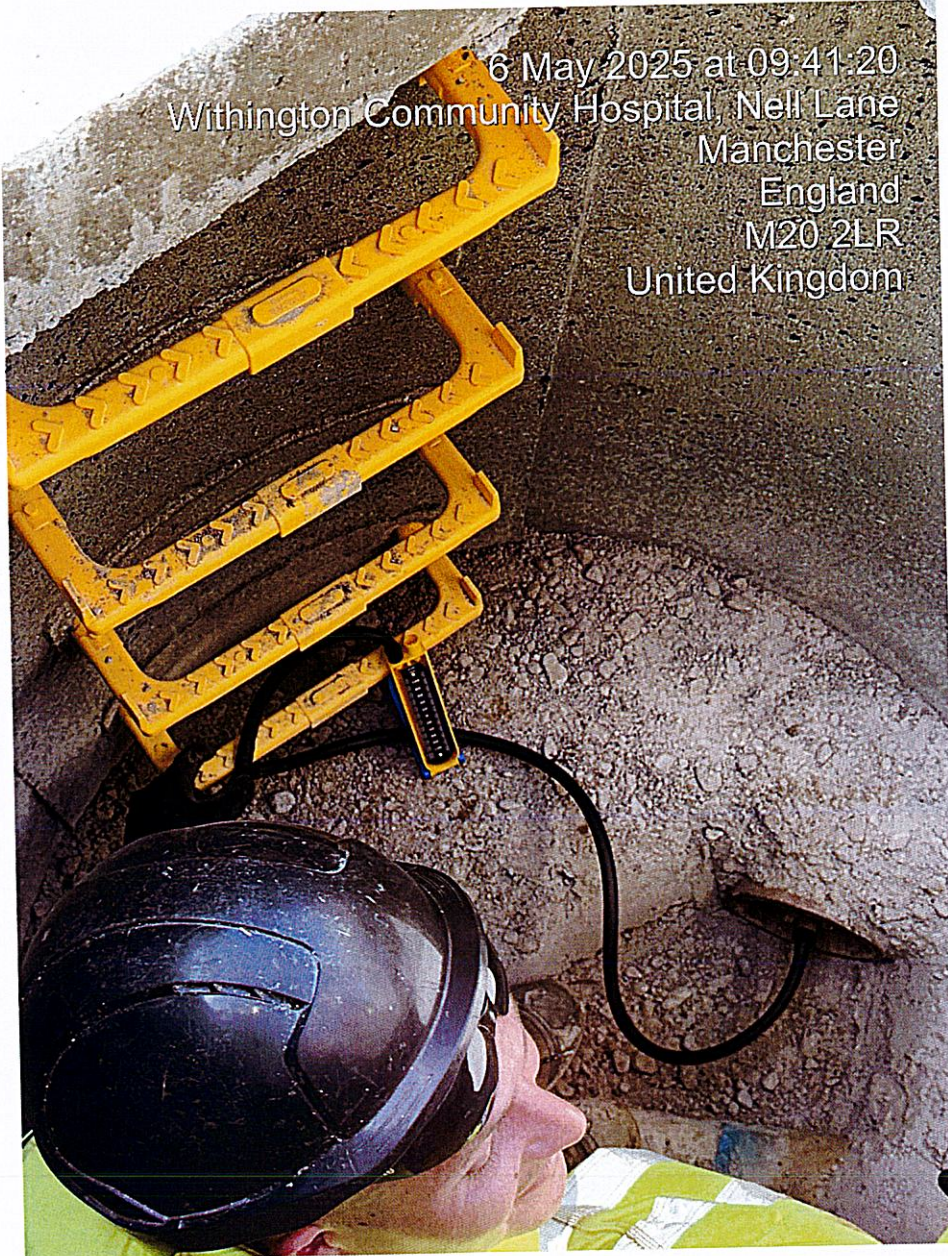







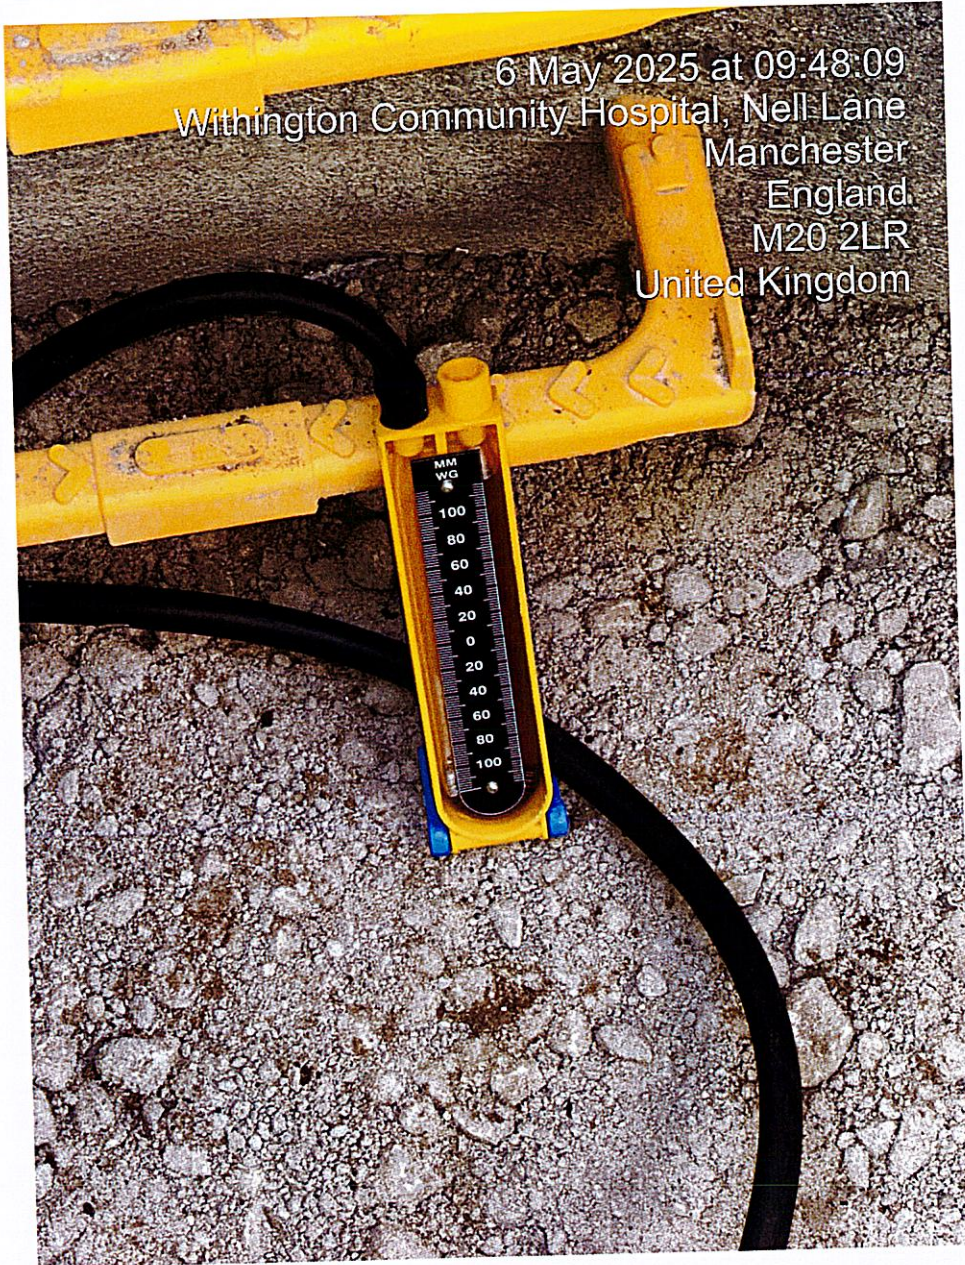





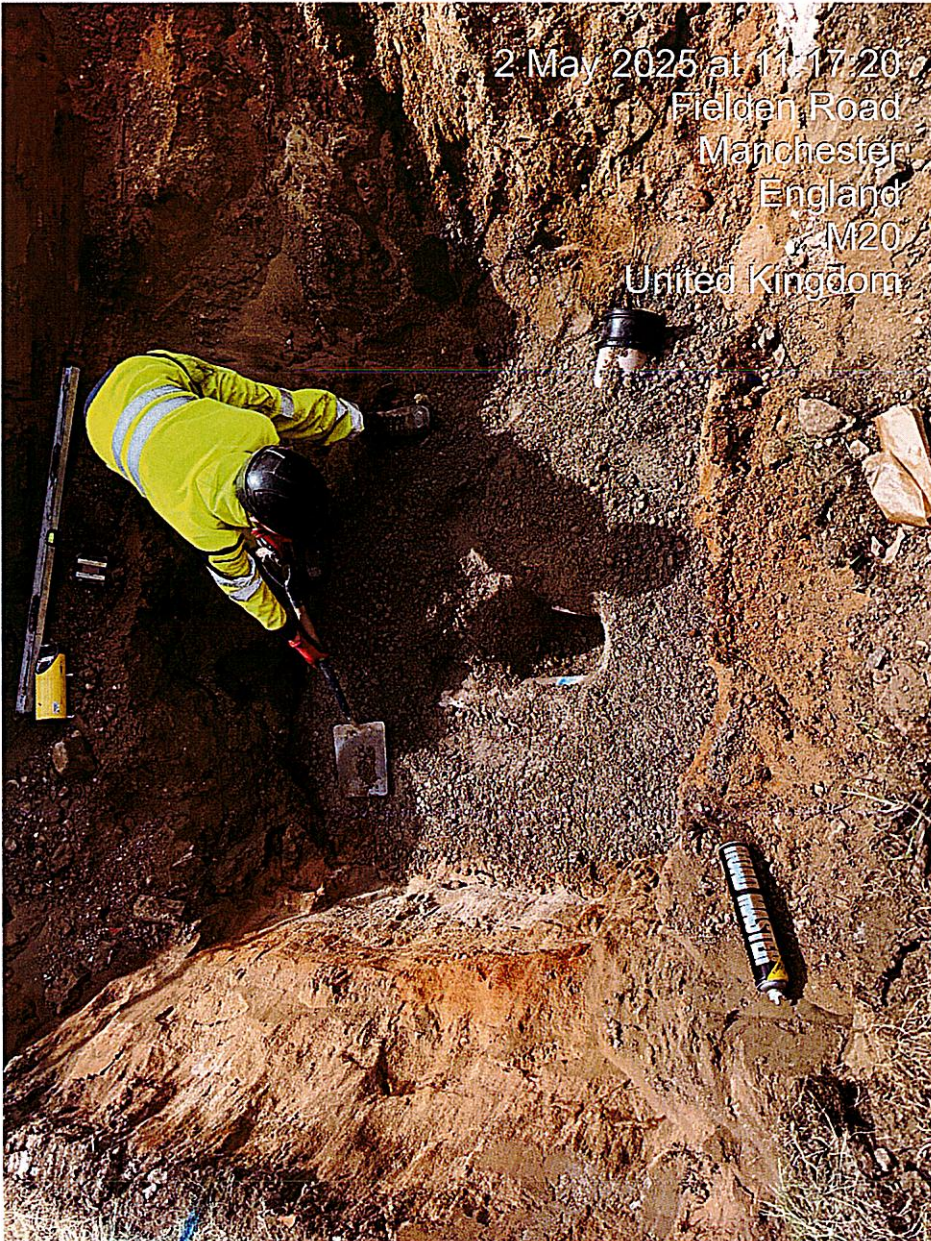

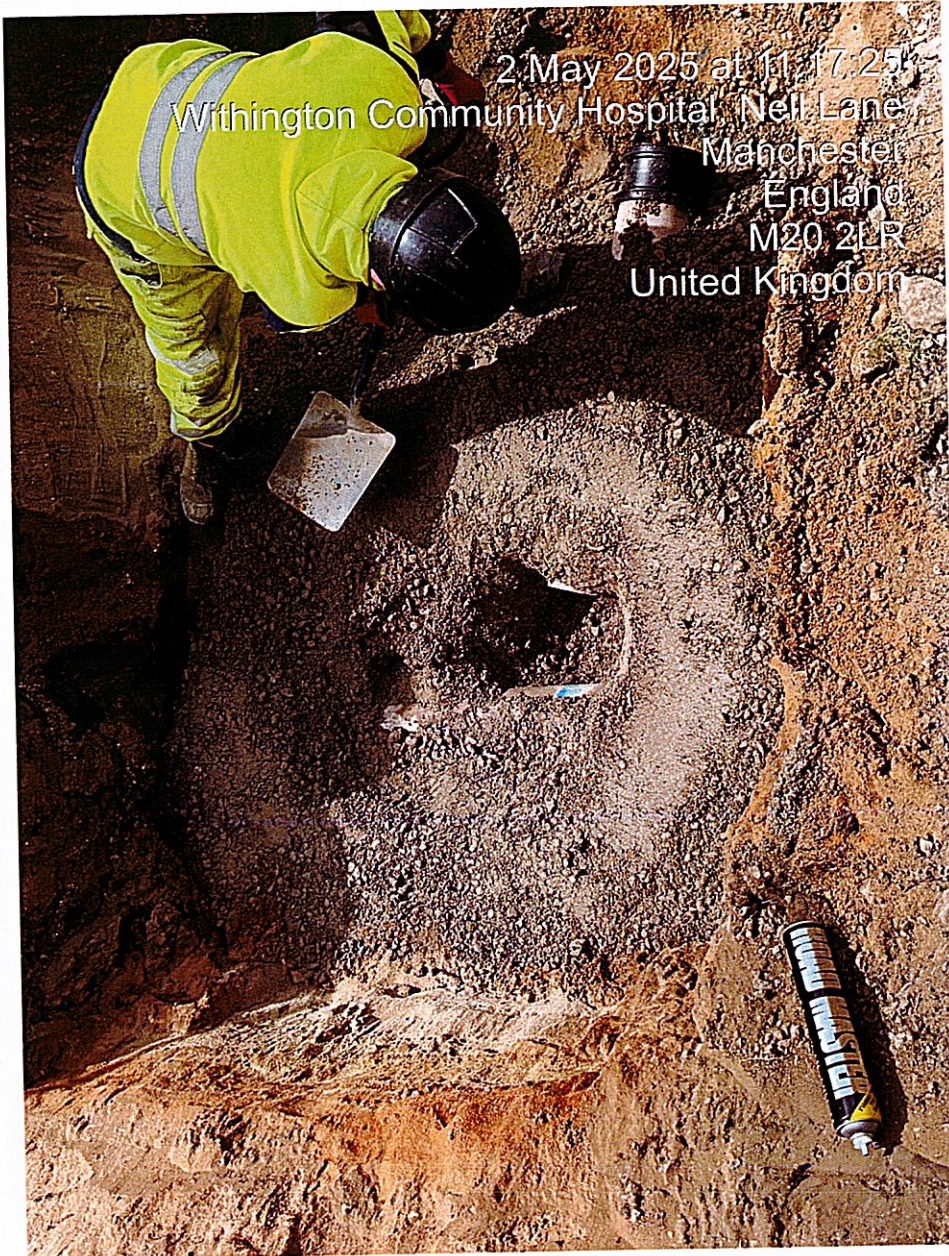



MURRAYWOOD
CONSTRUCTION LTD

QA Form - Manholes



Doc No:	QAF-061	Revision:	5	Issue Date:	10/11/17	Page:	12
---------	---------	-----------	---	-------------	----------	-------	----

