



Waterproofing Installation Report

Date: 18 February 2026

Project: 22 Honor Street, Manchester, M13 0WY

Client: NA Design and Builds

Project Overview

Photographic evidence has been provided showing the stages of installation and materials used. All materials were supplied by Delta and installed by a Delta-approved contractor.

Preparation & Tanking Works

- TG500 Lime and Salt Inhibitor Treatment
- Koster NB1 Grey Tanking Slurry – 2 coats applied to walls and floor


Type C Cavity Drain Membrane System Installed

- Delta MS500 (2.4m x 20m – 48m²) Wall Membrane
- Delta Corner Strip Tape (20m x 150mm) – Wall/Floor Junctions
- Brick-Seal Plugs
- Delta MS20 Floor Membrane
- Drainage Channel
- Corner Units with Jetting Ports
- 6 x Jetting Ports
- Delta HLA High Level Alarm

Guarantee

The waterproofing system installed by Select Basements Ltd is covered by a 10-year guarantee. Works have been completed alongside an insurance-backed guarantee for additional peace of mind.

Type C Wall & Floor Application Detail

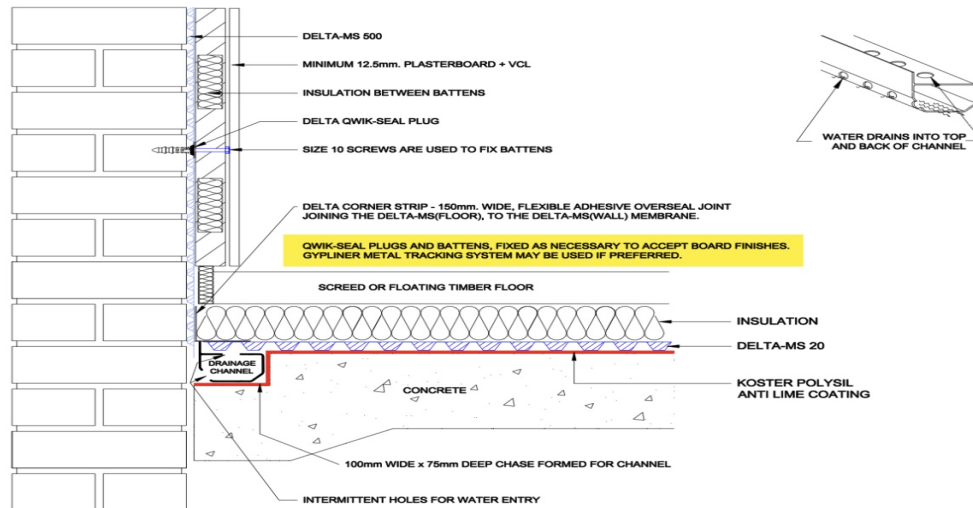

TYPE C, DRAINED PROTECTION, WALL AND FLOOR APPLICATION
