


|                              |                                                |                                                   |                                                         |                          |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|--------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP10A</b> |
| Contract Ref: <b>11264</b>   | Start: <b>17.05.18</b><br>End: <b>17.05.18</b> | Ground Level: <b>26.18</b>                        | National Grid Co-ordinate: <b>E:382686.0 N:397257.5</b> | Sheet: <b>3 of 4</b>     |

Trial Pit JTP10A Sketch of Profile

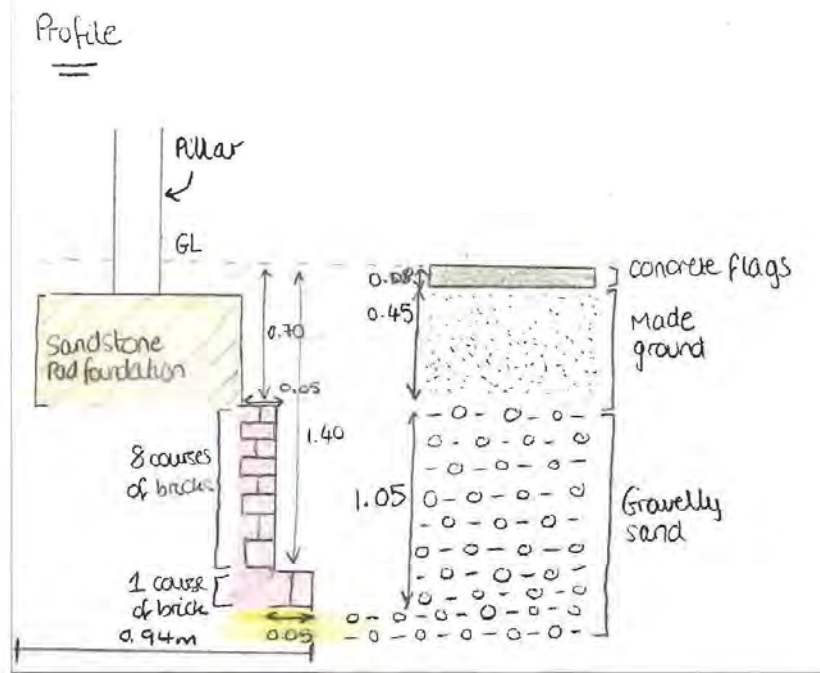

|                              |                                                |                                                   |                                                         |                          |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|--------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP10A</b> |
| Contract Ref: <b>11264</b>   | Start: <b>17.05.18</b><br>End: <b>17.05.18</b> | Ground Level: <b>26.18</b>                        | National Grid Co-ordinate: <b>E:382686.0 N:397257.5</b> | Sheet: <b>4 of 4</b>     |

Trial Pit JTP10A - Photo 1



Trial Pit JTP10A - Photo 2

|                              |                               |                        |             |  |
|------------------------------|-------------------------------|------------------------|-------------|--|
| Method Used: <b>Hand dug</b> | Plant Used: <b>Hand tools</b> | Logged By: <b>JTee</b> | Checked By: |  |
|------------------------------|-------------------------------|------------------------|-------------|--|



# TRIAL PIT LOG


|                              |                                                |                            |                                                         |  |                         |
|------------------------------|------------------------------------------------|----------------------------|---------------------------------------------------------|--|-------------------------|
| Contract: <b>Talbot Mill</b> |                                                |                            | Client: <b>Capital &amp; Centric (Adored) Ltd</b>       |  | Trial Pit: <b>JTP12</b> |
| Contract Ref: <b>11264</b>   | Start: <b>17.05.18</b><br>End: <b>17.05.18</b> | Ground Level: <b>26.14</b> | National Grid Co-ordinate: <b>E:382676.0 N:397266.5</b> |  | Sheet: <b>1 of 5</b>    |

| Samples and In-situ Tests            |        |         |         | Water | Backfill                                                                          | Description of Strata                                                                                                                 | Depth<br>(Thick<br>ness) | Material<br>Graphic<br>Legend                                                       |
|--------------------------------------|--------|---------|---------|-------|-----------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------|--------------------------|-------------------------------------------------------------------------------------|
| Depth                                | No     | Type    | Results |       |                                                                                   |                                                                                                                                       |                          |                                                                                     |
| 0.20-0.60                            | 1      | ES      | T, V, J |       |  | MADE GROUND: Yorkstone flags.                                                                                                         | 0.08                     |  |
|                                      |        |         |         |       |                                                                                   | MADE GROUND: Dark brown gravelly SAND. Gravel is angular to subrounded fine to coarse brick and sandstone with occasional half brick. | (0.62)                   |  |
| 0.80-1.20<br>0.80-1.20               | 2<br>3 | ES<br>D | T, V, J |       |                                                                                   | Light brown gravelly SAND. Gravel is subrounded to rounded fine to coarse mudstone and sandstone.<br>(GLACIOFLUVIAL DEPOSITS)         | (0.60)                   |  |
| Trial pit terminated at 1.30m depth. |        |         |         |       |                                                                                   | 1.30                                                                                                                                  |                          |                                                                                     |

|                              |                               |                                                                                                                                                                                                                                                                                                                                                                                                                           |             |  |  |
|------------------------------|-------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------|--|--|
| Plan (Not to Scale)          |                               | General Remarks                                                                                                                                                                                                                                                                                                                                                                                                           |             |  |  |
|                              |                               | <ol style="list-style-type: none"><li>1. Scanned with CAT and Genny prior to excavation.</li><li>2. Ease of trial pit excavation: difficult.</li><li>3. No groundwater encountered.</li><li>4. Trial pit remained dry and stable during excavation.</li><li>5. Trial pit terminated at 1.30m bgl.</li><li>6. On completion, trial pit backfilled with arisings and flagstone reinstated with post mix concrete.</li></ol> |             |  |  |
| All dimensions in metres     |                               | Scale: <b>1:21</b>                                                                                                                                                                                                                                                                                                                                                                                                        |             |  |  |
| Method Used: <b>Hand dug</b> | Plant Used: <b>Hand tools</b> | Logged By: <b>JTee</b>                                                                                                                                                                                                                                                                                                                                                                                                    | Checked By: |  |  |


GINT\_LIBRARY\_v8\_06.GLB LibVersion: v8\_06 - Core+Logs - 002 | Log TRIAL PIT LOG - A4P | 11264 TALBOT MILL.GPJ - v8\_06.  
RSK Environment Ltd, Fourways House, 57 Hilton Street, Piccadilly, Manchester, M1 2EJ. Tel: 0161 236 2757, Fax: 0161 236 7029, Web: www.rsk.co.uk. | 02/10/18 - 14:41 | JS12 |

|                              |                                                |                                                   |                                                         |                         |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|-------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP12</b> |
| Contract Ref: <b>11264</b>   | Start: <b>17.05.18</b><br>End: <b>17.05.18</b> | Ground Level: <b>26.14</b>                        | National Grid Co-ordinate: <b>E:382676.0 N:397266.5</b> | Sheet: <b>2 of 5</b>    |

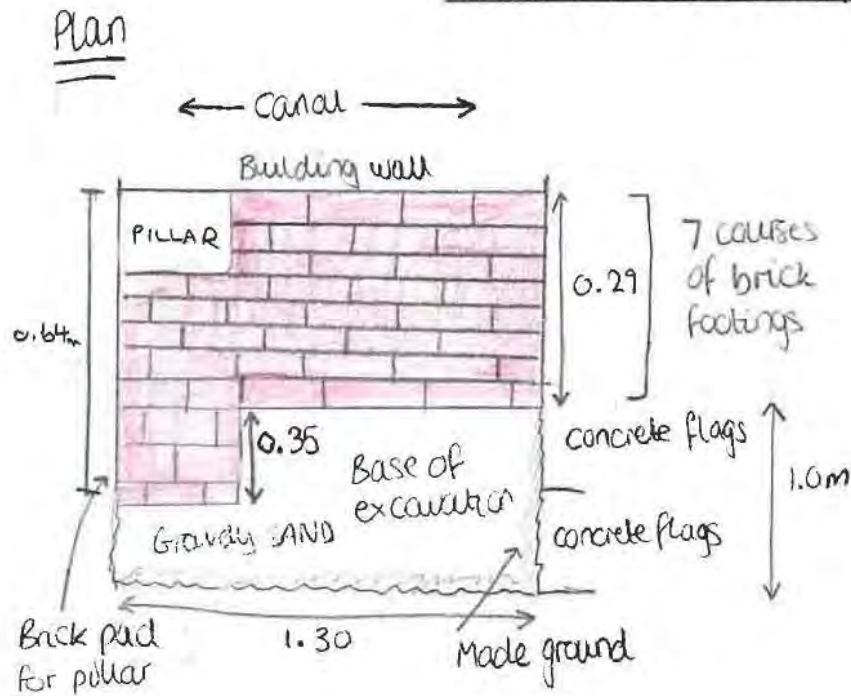

|                              |                               |                        |                         |            |
|------------------------------|-------------------------------|------------------------|-------------------------|------------|
| Method Used: <b>Hand dug</b> | Plant Used: <b>Hand tools</b> | Logged By: <b>JTee</b> | Checked By: <b>JTee</b> | <b>AGS</b> |
|------------------------------|-------------------------------|------------------------|-------------------------|------------|

|                              |                                                |                                                   |                                                         |                         |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|-------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP12</b> |
| Contract Ref: <b>11264</b>   | Start: <b>17.05.18</b><br>End: <b>17.05.18</b> | Ground Level: <b>26.14</b>                        | National Grid Co-ordinate: <b>E:382676.0 N:397266.5</b> | Sheet: <b>3 of 5</b>    |

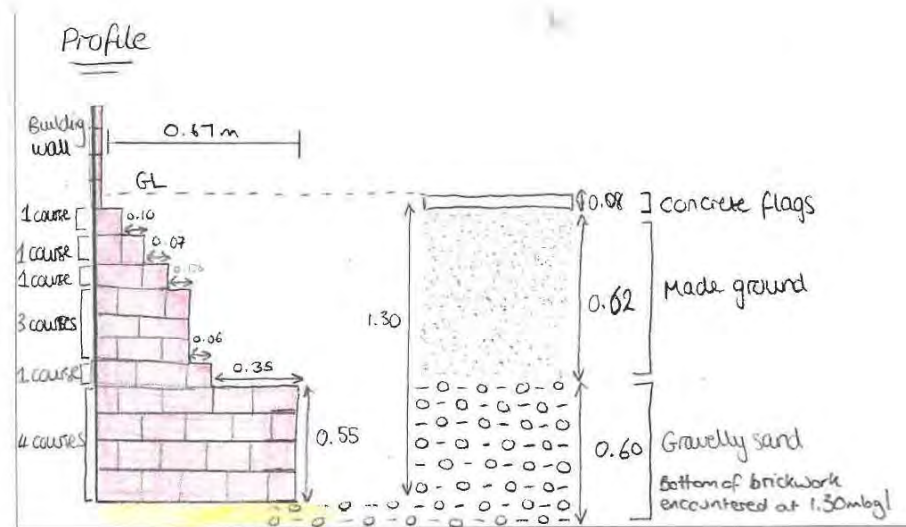

|                              |                               |                        |                         |            |
|------------------------------|-------------------------------|------------------------|-------------------------|------------|
| Method Used: <b>Hand dug</b> | Plant Used: <b>Hand tools</b> | Logged By: <b>JTee</b> | Checked By: <b>JTee</b> | <b>AGS</b> |
|------------------------------|-------------------------------|------------------------|-------------------------|------------|

|                              |                                                |                                                   |                                                         |                             |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|-----------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP12</b>     |
| Contract Ref: <b>11264</b>   | Start: <b>17.05.18</b><br>End: <b>17.05.18</b> | Ground Level: <b>26.14</b>                        | National Grid Co-ordinate: <b>E:382676.0 N:397266.5</b> | Sheet: <b>4</b> of <b>5</b> |

Trial Pit JTP12 - Photo 1



Trial Pit JTP12 - Photo 2

|                              |                               |                        |                       |                                                                                       |
|------------------------------|-------------------------------|------------------------|-----------------------|---------------------------------------------------------------------------------------|
| Method Used: <b>Hand dug</b> | Plant Used: <b>Hand tools</b> | Logged By: <b>JTee</b> | Checked By: <b>JS</b> |  |
|------------------------------|-------------------------------|------------------------|-----------------------|---------------------------------------------------------------------------------------|

|                              |                                                |                                                   |                                                         |                             |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|-----------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP12</b>     |
| Contract Ref: <b>11264</b>   | Start: <b>17.05.18</b><br>End: <b>17.05.18</b> | Ground Level: <b>26.14</b>                        | National Grid Co-ordinate: <b>E:382676.0 N:397266.5</b> | Sheet: <b>5</b> of <b>5</b> |

Trial Pit JTP12 - Photo 3




|                              |                               |                        |                                                                                                   |                                                                                       |
|------------------------------|-------------------------------|------------------------|---------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------|
| Method Used: <b>Hand dug</b> | Plant Used: <b>Hand tools</b> | Logged By: <b>JTee</b> | Checked By:  |  |
|------------------------------|-------------------------------|------------------------|---------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------|



# TRIAL PIT LOG


|                              |                                                |                            |                                                         |  |                             |
|------------------------------|------------------------------------------------|----------------------------|---------------------------------------------------------|--|-----------------------------|
| Contract: <b>Talbot Mill</b> |                                                |                            | Client: <b>Capital &amp; Centric (Adored) Ltd</b>       |  | Trial Pit: <b>JTP20</b>     |
| Contract Ref: <b>11264</b>   | Start: <b>16.05.18</b><br>End: <b>16.05.18</b> | Ground Level: <b>29.49</b> | National Grid Co-ordinate: <b>E:382732.5 N:397271.3</b> |  | Sheet: <b>1</b> of <b>3</b> |

| Samples and In-situ Tests |    |      |         | Water | Backfill | Description of Strata                                                                                                                                                                                                                       | Depth (Thickness) | Material Graphic Legend |
|---------------------------|----|------|---------|-------|----------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------|-------------------------|
| Depth                     | No | Type | Results |       |          |                                                                                                                                                                                                                                             |                   |                         |
| 0.20-0.40                 | 1  | ES   | T,V,J   |       |          | MADE GROUND: Cobble setts with bituminous tar surround.                                                                                                                                                                                     | 0.15              |                         |
| 0.20-0.40                 | 2  | D    |         |       |          | MADE GROUND: Greyish brown slightly silty gravelly medium to coarse SAND with a medium cobble content of sandstone and brick. Gravel is angular to subangular fine to coarse of sandstone, bituminous macadam, coal, slate, tile and brick. | (0.33)            |                         |
|                           |    |      |         |       |          | Trial pit terminated at 0.48m depth due to ceramic pipe.                                                                                                                                                                                    | 0.48              |                         |


|                                                                                     |                               |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                 |                                                                                                   |                                                                                       |  |
|-------------------------------------------------------------------------------------|-------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------|--|
| Plan (Not to Scale)                                                                 |                               | General Remarks                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                 |                                                                                                   |                                                                                       |  |
|  |                               | <ol style="list-style-type: none"><li>1. Scanned with CAT and Genny prior to excavation.</li><li>2. Ease of trial pit excavation: digging easy, but difficult to remove cobbles setts.</li><li>3. No groundwater encountered.</li><li>4. Ceramic pipe encountered at 0.45m.</li><li>5. Trial pit remained dry and stable during excavation.</li><li>6. Trial pit terminated at 0.48m bgl.</li><li>7. On completion, trial pit backfilled with arisings and cobbles reinstated with post mix concrete.</li></ol> |                                                                                                   |                                                                                       |  |
|                                                                                     |                               | All dimensions in metres                                                                                                                                                                                                                                                                                                                                                                                                                                                                                        |                                                                                                   | Scale: <b>1:21</b>                                                                    |  |
| Method Used: <b>Hand dug</b>                                                        | Plant Used: <b>Hand tools</b> | Logged By: <b>JTee</b>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                          | Checked By:  |  |  |

|                              |                                                |                                                   |                                                         |                         |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|-------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP20</b> |
| Contract Ref: <b>11264</b>   | Start: <b>16.05.18</b><br>End: <b>16.05.18</b> | Ground Level: <b>29.49</b>                        | National Grid Co-ordinate: <b>E:382732.5 N:397271.3</b> | Sheet: <b>2 of 3</b>    |

Trial Pit JTP20 - Sketch of Profiles




PROFILE

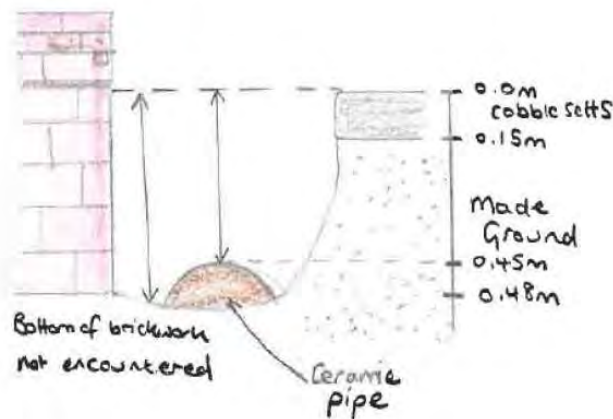

|                              |                               |                        |                                                                                                   |                                                                                       |
|------------------------------|-------------------------------|------------------------|---------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------|
| Method Used: <b>Hand dug</b> | Plant Used: <b>Hand tools</b> | Logged By: <b>JTee</b> | Checked By:  |  |
|------------------------------|-------------------------------|------------------------|---------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------|

|                              |                                                |                                                   |                                                         |                         |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|-------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP20</b> |
| Contract Ref: <b>11264</b>   | Start: <b>16.05.18</b><br>End: <b>16.05.18</b> | Ground Level: <b>29.49</b>                        | National Grid Co-ordinate: <b>E:382732.5 N:397271.3</b> | Sheet: <b>3 of 3</b>    |

Trial Pit JTP20 - Photo 1

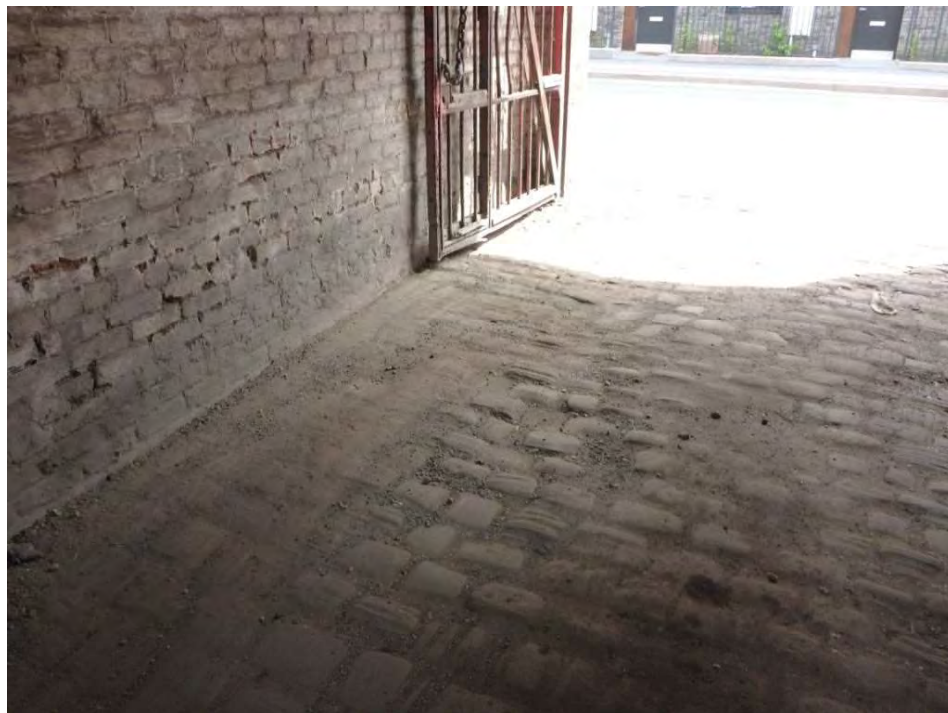

Trial Pit JTP20 - Photo 2


|                              |                               |                        |                                |            |
|------------------------------|-------------------------------|------------------------|--------------------------------|------------|
| Method Used: <b>Hand dug</b> | Plant Used: <b>Hand tools</b> | Logged By: <b>JTee</b> | Checked By: <b>[Signature]</b> | <b>AGS</b> |
|------------------------------|-------------------------------|------------------------|--------------------------------|------------|



# TRIAL PIT LOG

|                              |                                                |                            |                                                         |  |                             |
|------------------------------|------------------------------------------------|----------------------------|---------------------------------------------------------|--|-----------------------------|
| Contract: <b>Talbot Mill</b> |                                                |                            | Client: <b>Capital &amp; Centric (Adored) Ltd</b>       |  | Trial Pit: <b>JTP21</b>     |
| Contract Ref: <b>11264</b>   | Start: <b>16.05.18</b><br>End: <b>16.05.18</b> | Ground Level: <b>29.16</b> | National Grid Co-ordinate: <b>E:382726.8 N:397281.4</b> |  | Sheet: <b>1</b> of <b>4</b> |

| Samples and In-situ Tests |    |      |         | Water | Backfill | Description of Strata                                                                                                                                                                                                                                                                                | Depth (Thickness) | Material Graphic Legend |
|---------------------------|----|------|---------|-------|----------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------|-------------------------|
| Depth                     | No | Type | Results |       |          |                                                                                                                                                                                                                                                                                                      |                   |                         |
|                           |    |      |         |       |          | MADE GROUND: Cobbles setts with bituminous tar surround.                                                                                                                                                                                                                                             | 0.15              |                         |
|                           |    |      |         |       |          | MADE GROUND: Greyish brown with reddish brown slightly clayey gravelly medium to coarse SAND with a medium cobble content of sandstone and concrete. Gravel is angular to subangular fine to coarse of brick, sandstone, clinker slate and rare ceramic. . . . 0.35m - 0.40m, empty / dry clay pipe. | (1.45)            |                         |
|                           |    |      |         |       |          |                                                                                                                                                                                                                                                                                                      | 1.60              |                         |
|                           |    |      |         |       |          | Trial pit terminated at 1.60m depth due to maximum depth for a hand dug pit being reached.                                                                                                                                                                                                           |                   |                         |

|                                                                                     |                               |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                   |                                                                                                   |                                                                                       |  |
|-------------------------------------------------------------------------------------|-------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------|--|
| Plan (Not to Scale)                                                                 |                               | General Remarks                                                                                                                                                                                                                                                                                                                                                                                                                                                                                   |                                                                                                   |                                                                                       |  |
|  |                               | <ol style="list-style-type: none"><li>1. Scanned with CAT and Genny prior to excavation.</li><li>2. Ease of trial pit excavation: digging moderate, but difficult to remove cobble setts.</li><li>3. No groundwater encountered.</li><li>4. Trial pit remained dry and stable during excavation.</li><li>5. Trial pit terminated at maximum depth possible by hand digging.</li><li>6. On completion, trial pit backfilled with arisings and cobbles reinstated with post mix concrete.</li></ol> |                                                                                                   |                                                                                       |  |
|                                                                                     |                               | All dimensions in metres                                                                                                                                                                                                                                                                                                                                                                                                                                                                          |                                                                                                   | Scale: <b>1:21</b>                                                                    |  |
| Method Used: <b>Hand dug</b>                                                        | Plant Used: <b>Hand tools</b> | Logged By: <b>JTee</b>                                                                                                                                                                                                                                                                                                                                                                                                                                                                            | Checked By:  |  |  |

|                              |                                                |                                                   |                                                         |                         |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|-------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP21</b> |
| Contract Ref: <b>11264</b>   | Start: <b>16.05.18</b><br>End: <b>16.05.18</b> | Ground Level: <b>29.16</b>                        | National Grid Co-ordinate: <b>E:382726.8 N:397281.4</b> | Sheet: <b>2 of 4</b>    |

Trial Pit JTP21 - Sketch of Profile and Plan



|                              |                               |                        |                                |            |
|------------------------------|-------------------------------|------------------------|--------------------------------|------------|
| Method Used: <b>Hand dug</b> | Plant Used: <b>Hand tools</b> | Logged By: <b>JTee</b> | Checked By: <b>[Signature]</b> | <b>AGS</b> |
|------------------------------|-------------------------------|------------------------|--------------------------------|------------|

|                              |                                                |                                                   |                                                         |                         |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|-------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP21</b> |
| Contract Ref: <b>11264</b>   | Start: <b>16.05.18</b><br>End: <b>16.05.18</b> | Ground Level: <b>29.16</b>                        | National Grid Co-ordinate: <b>E:382726.8 N:397281.4</b> | Sheet: <b>3 of 4</b>    |

JTP21 - Photo 1



JTP21 - Photo 2

|                              |                               |                        |                       |            |
|------------------------------|-------------------------------|------------------------|-----------------------|------------|
| Method Used: <b>Hand dug</b> | Plant Used: <b>Hand tools</b> | Logged By: <b>JTee</b> | Checked By: <b>JS</b> | <b>AGS</b> |
|------------------------------|-------------------------------|------------------------|-----------------------|------------|

|                              |                                                |                                                   |                                                         |                         |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|-------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP21</b> |
| Contract Ref: <b>11264</b>   | Start: <b>16.05.18</b><br>End: <b>16.05.18</b> | Ground Level: <b>29.16</b>                        | National Grid Co-ordinate: <b>E:382726.8 N:397281.4</b> | Sheet: <b>4 of 4</b>    |

JTP21 - Photo 3




|                              |                               |                        |                       |  |
|------------------------------|-------------------------------|------------------------|-----------------------|--|
| Method Used: <b>Hand dug</b> | Plant Used: <b>Hand tools</b> | Logged By: <b>JTee</b> | Checked By: <b>JS</b> |  |
|------------------------------|-------------------------------|------------------------|-----------------------|--|



# TRIAL PIT LOG



|                              |                                                |                            |                                                         |  |                             |
|------------------------------|------------------------------------------------|----------------------------|---------------------------------------------------------|--|-----------------------------|
| Contract: <b>Talbot Mill</b> |                                                |                            | Client: <b>Capital &amp; Centric (Adored) Ltd</b>       |  | Trial Pit: <b>JTP22</b>     |
| Contract Ref: <b>11264</b>   | Start: <b>16.05.18</b><br>End: <b>16.05.18</b> | Ground Level: <b>29.46</b> | National Grid Co-ordinate: <b>E:382706.0 N:397253.9</b> |  | Sheet: <b>1</b> of <b>3</b> |

| Samples and In-situ Tests |    |      |         | Water | Backfill | Description of Strata                                                                                                                                                | Depth<br>(Thickness) | Material<br>Graphic<br>Legend |
|---------------------------|----|------|---------|-------|----------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------|-------------------------------|
| Depth                     | No | Type | Results |       |          |                                                                                                                                                                      |                      |                               |
| 0.45<br>0.50              | 1  | ES   | T,V,J   |       |          | MADE GROUND: Concrete hardstanding.                                                                                                                                  | 0.08                 |                               |
|                           |    |      |         |       |          | MADE GROUND: Cobble setts with bituminous binding.                                                                                                                   |                      |                               |
|                           |    |      |         |       |          | MADE GROUND: Blackish brown gravelly ashy SAND. Gravel is angular to subangular fine to coarse brick and clinker.                                                    | 0.30<br>0.40         |                               |
|                           | 2  | ES   | T,V,J   |       |          | MADE GROUND: Brown gravelly clayey medium to coarse SAND. Gravel is angular to subrounded fine to coarse of mudstone and brick. Trial pit terminated at 0.50m depth. | 0.50                 |                               |

|                                                                                     |                               |                                                                                                                                                                                                                                                                                                                                                        |                                                                                                   |                                                                                       |  |
|-------------------------------------------------------------------------------------|-------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------|--|
| Plan (Not to Scale)                                                                 |                               | General Remarks                                                                                                                                                                                                                                                                                                                                        |                                                                                                   |                                                                                       |  |
|  |                               | <ol style="list-style-type: none"><li>1. Scanned with CAT and Genny prior to excavation.</li><li>2. Ease of trial pit excavation: difficult.</li><li>3. No groundwater encountered.</li><li>4. Trial pit remained dry and stable during excavation.</li><li>5. On completion, trial pit backfilled with arisings and finished with concrete.</li></ol> |                                                                                                   |                                                                                       |  |
|                                                                                     |                               | All dimensions in metres                                                                                                                                                                                                                                                                                                                               |                                                                                                   | Scale: <b>1:21</b>                                                                    |  |
| Method Used: <b>Hand dug</b>                                                        | Plant Used: <b>Hand tools</b> | Logged By: <b>JTee</b>                                                                                                                                                                                                                                                                                                                                 | Checked By:  |  |  |

|                              |                                                |                                                   |                                                         |                         |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|-------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP22</b> |
| Contract Ref: <b>11264</b>   | Start: <b>16.05.18</b><br>End: <b>16.05.18</b> | Ground Level: <b>29.46</b>                        | National Grid Co-ordinate: <b>E:382706.0 N:397253.9</b> | Sheet: <b>2 of 3</b>    |


Trial Pit JTP22 - Sketch of Faces A and B

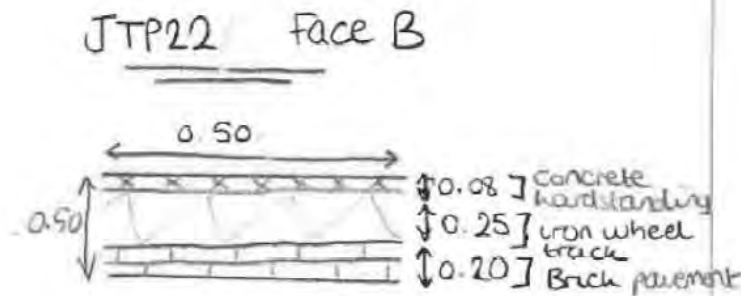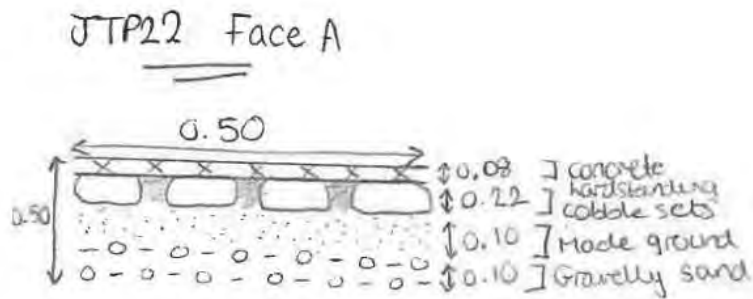

|                              |                               |                        |                                                                                                   |                                                                                       |
|------------------------------|-------------------------------|------------------------|---------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------|
| Method Used: <b>Hand dug</b> | Plant Used: <b>Hand tools</b> | Logged By: <b>JTee</b> | Checked By:  |  |
|------------------------------|-------------------------------|------------------------|---------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------|

|                              |                                                |                                                   |                                                         |                         |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|-------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP22</b> |
| Contract Ref: <b>11264</b>   | Start: <b>16.05.18</b><br>End: <b>16.05.18</b> | Ground Level: <b>29.46</b>                        | National Grid Co-ordinate: <b>E:382706.0 N:397253.9</b> | Sheet: <b>3 of 3</b>    |

JTP22 - Photo 1

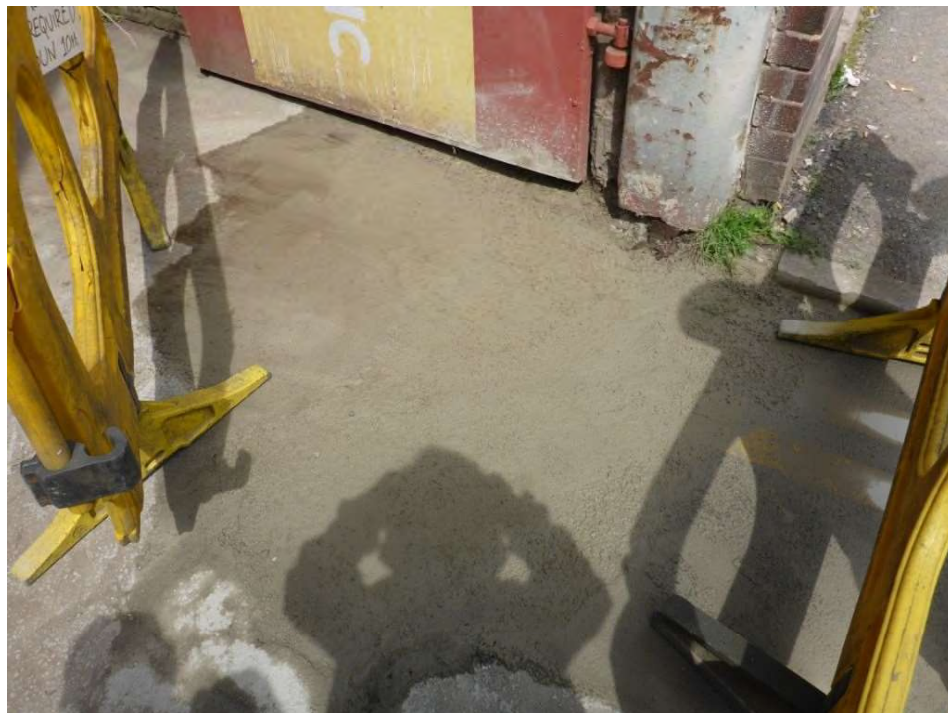

JTP22 - Photo 2


|                              |                               |                        |                         |  |
|------------------------------|-------------------------------|------------------------|-------------------------|--|
| Method Used: <b>Hand dug</b> | Plant Used: <b>Hand tools</b> | Logged By: <b>JTee</b> | Checked By: <b>JS12</b> |  |
|------------------------------|-------------------------------|------------------------|-------------------------|--|



# TRIAL PIT LOG


|                              |                                                |                                                   |                                                         |                          |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|--------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP22A</b> |
| Contract Ref: <b>11264</b>   | Start: <b>16.05.18</b><br>End: <b>16.05.18</b> | Ground Level: <b>29.53</b>                        | National Grid Co-ordinate: <b>E:382706.5 N:397254.8</b> | Sheet: <b>1 of 2</b>     |

| Samples and In-situ Tests |    |      |         | Water | Backfill | Description of Strata                                                                                                             | Depth (Thickness) | Material Graphic Legend |
|---------------------------|----|------|---------|-------|----------|-----------------------------------------------------------------------------------------------------------------------------------|-------------------|-------------------------|
| Depth                     | No | Type | Results |       |          |                                                                                                                                   |                   |                         |
|                           |    |      |         |       |          | MADE GROUND: Concrete hardstanding.                                                                                               | 0.08              |                         |
|                           |    |      |         |       |          | MADE GROUND: Sandstone pad foundation.                                                                                            | (0.35)            |                         |
|                           |    |      |         |       |          |                                                                                                                                   | 0.43              |                         |
|                           |    |      |         |       |          | MADE GROUND: Brick footing.                                                                                                       | 0.53              |                         |
|                           |    |      |         |       |          | Brown gravelly clayey medium to coarse SAND. Gravel is angular to subrounded fine to coarse of mudstone. (GLACIOFLUVIAL DEPOSITS) | (1.02)            |                         |
|                           |    |      |         |       |          |                                                                                                                                   | 1.55              |                         |
|                           |    |      |         |       |          | Trial pit terminated at 1.55m depth.                                                                                              |                   |                         |


|                                                                                     |                                      |                                                                                                                                                                                                                                                                                                                                                        |                                                                                                   |                                                                                       |
|-------------------------------------------------------------------------------------|--------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------|
| Plan (Not to Scale)                                                                 |                                      | General Remarks                                                                                                                                                                                                                                                                                                                                        |                                                                                                   |                                                                                       |
|  |                                      | <ol style="list-style-type: none"><li>1. Scanned with CAT and Genny prior to excavation.</li><li>2. Ease of trial pit excavation: difficult.</li><li>3. No groundwater encountered.</li><li>4. Trial pit remained dry and stable during excavation.</li><li>5. On completion, trial pit backfilled with arisings and finished with concrete.</li></ol> |                                                                                                   |                                                                                       |
|                                                                                     |                                      | All dimensions in metres                                                                                                                                                                                                                                                                                                                               |                                                                                                   | Scale: <b>1:21</b>                                                                    |
| Method Used: <b>Hand and machine dug</b>                                            | Plant Used: <b>Tracked excavator</b> | Logged By: <b>JTee</b>                                                                                                                                                                                                                                                                                                                                 | Checked By:  |  |

|                              |                                                |                                                   |                                                         |                          |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|--------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP22A</b> |
| Contract Ref: <b>11264</b>   | Start: <b>16.05.18</b><br>End: <b>16.05.18</b> | Ground Level: <b>29.53</b>                        | National Grid Co-ordinate: <b>E:382706.5 N:397254.8</b> | Sheet: <b>2 of 2</b>     |


Trial Pit JTP22A - Sketch of Faces A and B and Profile

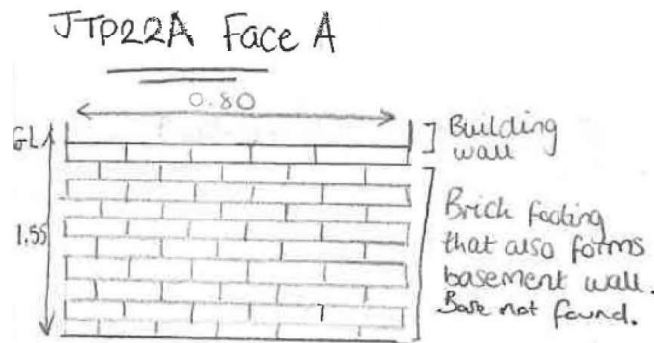

JTP22A Face B



Profile

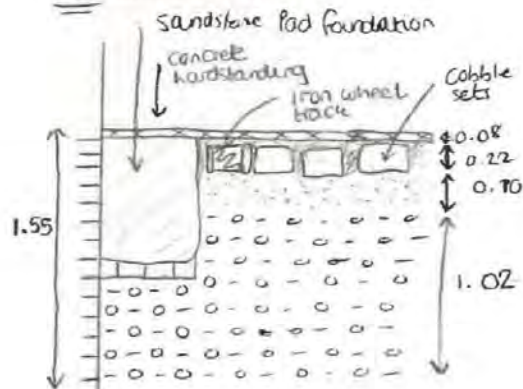



# TRIAL PIT LOG

|                              |                                                |                                                   |                                                         |                         |  |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|-------------------------|--|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP23</b> |  |
| Contract Ref: <b>11264</b>   | Start: <b>16.05.18</b><br>End: <b>16.05.18</b> | Ground Level: <b>26.27</b>                        | National Grid Co-ordinate: <b>E:382694.1 N:397273.7</b> | Sheet: <b>1 of 3</b>    |  |


| Samples and In-situ Tests |    |      |         | Water | Backfill | Description of Strata                                                                                                                                 | Depth (Thickness) | Material Graphic Legend |
|---------------------------|----|------|---------|-------|----------|-------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------|-------------------------|
| Depth                     | No | Type | Results |       |          |                                                                                                                                                       |                   |                         |
| 0.25-0.35                 | 1  | ES   |         |       |          | MADE GROUND: Cobbles setts with bituminous binding.                                                                                                   | 0.20              |                         |
|                           |    |      |         |       |          | MADE GROUND: Brown gravelly SAND. Gravel is angular to subrounded fine to coarse brick, clinker and sandstone.                                        | 0.35              |                         |
| 0.40-0.60                 | 2  | ES   |         |       |          | Light brown gravelly clayey medium to coarse SAND. Gravel is subrounded to rounded fine to coarse of mudstone and sandstone. (GLACIOFLUVIAL DEPOSITS) | (0.50)            |                         |
| 0.40-0.60                 | 3  | D    |         |       |          |                                                                                                                                                       |                   |                         |
|                           |    |      |         |       |          | Trial pit terminated at 0.85m depth.                                                                                                                  | 0.85              |                         |

|                                          |                                      |                                                                                                                                                                                                                                                                                                                                                                                                                                                |             |                    |  |
|------------------------------------------|--------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------|--------------------|--|
| Plan (Not to Scale)                      |                                      | General Remarks                                                                                                                                                                                                                                                                                                                                                                                                                                |             |                    |  |
|                                          |                                      | <ol style="list-style-type: none"><li>1. Scanned with CAT and Genny prior to excavation.</li><li>2. Ease of trial pit excavation: hand digging difficult, made use of excavator.</li><li>3. No groundwater encountered.</li><li>4. Trial pit remained dry and stable during excavation, slight spalling of gravelly sand.</li><li>5. On completion, trial pit backfilled with arisings and cobbles reinstated with postmix concrete.</li></ol> |             |                    |  |
|                                          |                                      | All dimensions in metres                                                                                                                                                                                                                                                                                                                                                                                                                       |             | Scale: <b>1:21</b> |  |
| Method Used: <b>Hand and machine dug</b> | Plant Used: <b>Tracked excavator</b> | Logged By: <b>JTee</b>                                                                                                                                                                                                                                                                                                                                                                                                                         | Checked By: |                    |  |


|                              |                                                |                                                   |                                                         |                         |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|-------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP23</b> |
| Contract Ref: <b>11264</b>   | Start: <b>16.05.18</b><br>End: <b>16.05.18</b> | Ground Level: <b>26.27</b>                        | National Grid Co-ordinate: <b>E:382694.1 N:397273.7</b> | Sheet: <b>2 of 3</b>    |

Trial Pit JTP23 - Sketch of Profile and Face A

Profile

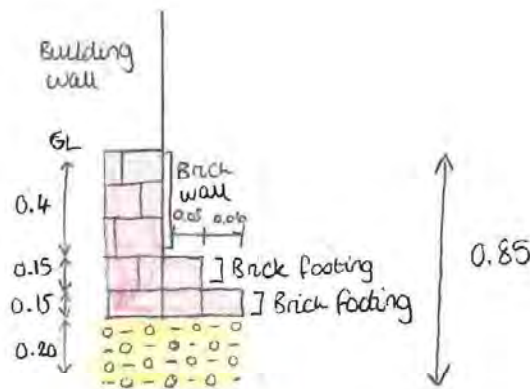

Face A



|                              |                                                |                                                   |                                                         |                         |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|-------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP23</b> |
| Contract Ref: <b>11264</b>   | Start: <b>16.05.18</b><br>End: <b>16.05.18</b> | Ground Level: <b>26.27</b>                        | National Grid Co-ordinate: <b>E:382694.1 N:397273.7</b> | Sheet: <b>3 of 3</b>    |

Trial Pit JTP23 - Photo 1




|                                          |                                      |                        |                         |            |
|------------------------------------------|--------------------------------------|------------------------|-------------------------|------------|
| Method Used: <b>Hand and machine dug</b> | Plant Used: <b>Tracked excavator</b> | Logged By: <b>JTee</b> | Checked By: <b>JTee</b> | <b>AGS</b> |
|------------------------------------------|--------------------------------------|------------------------|-------------------------|------------|



# TRIAL PIT LOG

|                              |                                                |                            |                                                         |  |                         |
|------------------------------|------------------------------------------------|----------------------------|---------------------------------------------------------|--|-------------------------|
| Contract: <b>Talbot Mill</b> |                                                |                            | Client: <b>Capital &amp; Centric (Adored) Ltd</b>       |  | Trial Pit: <b>JTP24</b> |
| Contract Ref: <b>11264</b>   | Start: <b>16.05.18</b><br>End: <b>16.05.18</b> | Ground Level: <b>26.34</b> | National Grid Co-ordinate: <b>E:382688.6 N:397284.1</b> |  | Sheet: <b>1 of 3</b>    |


| Samples and In-situ Tests |        |         |         | Water | Backfill                                                                          | Description of Strata                                                                                                                    | Depth (Thick<br>ness) | Material<br>Graphic<br>Legend                                                       |
|---------------------------|--------|---------|---------|-------|-----------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------|-----------------------|-------------------------------------------------------------------------------------|
| Depth                     | No     | Type    | Results |       |                                                                                   |                                                                                                                                          |                       |                                                                                     |
| 0.30-0.60                 | 1      | ES      | T,V,J   |       |  | MADE GROUND: Cobble setts with bituminous binding.                                                                                       | 0.20                  |  |
|                           |        |         |         |       |                                                                                   | MADE GROUND: Blackish brown gravelly SAND. Gravel is angular to rounded fine to coarse brick and clinker.                                | (0.50)                |                                                                                     |
| 0.80-1.00<br>0.80-1.00    | 2<br>3 | ES<br>D | T,V,J   |       |                                                                                   | Light brown gravelly medium to coarse SAND. Gravel is angular to rounded fine to coarse mudstone and sandstone. (GLACIOFLUVIAL DEPOSITS) | (0.40)                |  |
|                           |        |         |         |       |                                                                                   | Reddish brown silty medium to coarse grained SAND. (Recovered as weathered sandstone)<br>Trial pit terminated at 1.15m depth.            | 1.10<br>1.15          |                                                                                     |

|                              |                               |                                                                                                                                                                                                                                                                                                                                                                                                                                 |             |  |  |
|------------------------------|-------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------|--|--|
| Plan (Not to Scale)          |                               | General Remarks                                                                                                                                                                                                                                                                                                                                                                                                                 |             |  |  |
|                              |                               | <ol style="list-style-type: none"><li>1. Scanned with CAT and Genny prior to excavation.</li><li>2. Ease of trial pit excavation: moderate.</li><li>3. No groundwater encountered.</li><li>4. Trial pit remained dry and stable during excavation.</li><li>5. Trial pit terminated at base of foundations.</li><li>6. On completion, trial pit backfilled with arisings and cobbles reinstated with postmix concrete.</li></ol> |             |  |  |
| All dimensions in metres     |                               | Scale: <b>1:21</b>                                                                                                                                                                                                                                                                                                                                                                                                              |             |  |  |
| Method Used: <b>Hand dug</b> | Plant Used: <b>Hand tools</b> | Logged By: <b>JTee</b>                                                                                                                                                                                                                                                                                                                                                                                                          | Checked By: |  |  |

GINT\_LIBRARY\_v8\_06.GLB LibVersion: v8\_06 - Core+Logs - 002 | Log TRIAL PIT LOG - A4P | 11264 TALBOT MILL.GPJ - v8\_06.  
RSK Environment Ltd, Fourways House, 57 Hilton Street, Piccadilly, Manchester, M1 2EJ. Tel: 0161 236 2757, Fax: 0161 236 7029, Web: www.rsk.co.uk. | 02/10/18 - 14:42 | JS12 |

|                              |                                                |                                                   |                                                         |                         |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|-------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP24</b> |
| Contract Ref: <b>11264</b>   | Start: <b>16.05.18</b><br>End: <b>16.05.18</b> | Ground Level: <b>26.34</b>                        | National Grid Co-ordinate: <b>E:382688.6 N:397284.1</b> | Sheet: <b>2 of 3</b>    |

Trial Pit JTP24 - Sketch of Faces

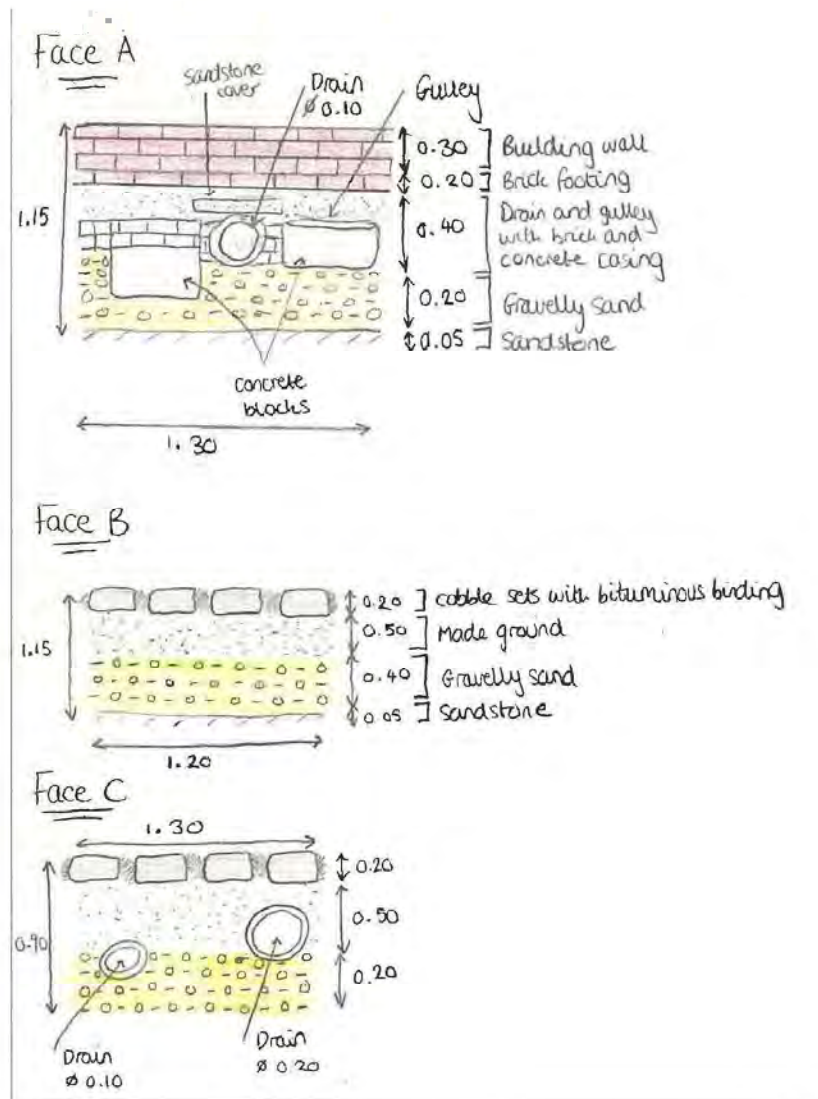

|                              |                               |                        |                       |            |
|------------------------------|-------------------------------|------------------------|-----------------------|------------|
| Method Used: <b>Hand dug</b> | Plant Used: <b>Hand tools</b> | Logged By: <b>JTee</b> | Checked By: <b>HT</b> | <b>AGS</b> |
|------------------------------|-------------------------------|------------------------|-----------------------|------------|

|                              |                                                |                                                   |                                                         |                         |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|-------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP24</b> |
| Contract Ref: <b>11264</b>   | Start: <b>16.05.18</b><br>End: <b>16.05.18</b> | Ground Level: <b>26.34</b>                        | National Grid Co-ordinate: <b>E:382688.6 N:397284.1</b> | Sheet: <b>3 of 3</b>    |

Trial Pit JTP24 - Photo Face A



Trial Pit JTP24 - Photo Face C

|                              |                               |                        |                         |            |
|------------------------------|-------------------------------|------------------------|-------------------------|------------|
| Method Used: <b>Hand dug</b> | Plant Used: <b>Hand tools</b> | Logged By: <b>JTee</b> | Checked By: <b>JTee</b> | <b>AGS</b> |
|------------------------------|-------------------------------|------------------------|-------------------------|------------|



# TRIAL PIT LOG


|                              |                                                |                                                   |                                                         |                         |  |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|-------------------------|--|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP25</b> |  |
| Contract Ref: <b>11264</b>   | Start: <b>16.05.18</b><br>End: <b>16.05.18</b> | Ground Level: <b>26.49</b>                        | National Grid Co-ordinate: <b>E:382702.8 N:397281.4</b> | Sheet: <b>1 of 4</b>    |  |

| Samples and In-situ Tests |        |         |         | Water | Backfill | Description of Strata                                                                                                                       | Depth (Thickness) | Material Graphic Legend |
|---------------------------|--------|---------|---------|-------|----------|---------------------------------------------------------------------------------------------------------------------------------------------|-------------------|-------------------------|
| Depth                     | No     | Type    | Results |       |          |                                                                                                                                             |                   |                         |
| 0.15-0.25                 | 1      | ES      | T,V,J   |       |          | MADE GROUND: Concrete hardstanding.                                                                                                         | 0.10              |                         |
|                           |        |         |         |       |          | MADE GROUND: Blackish brown gravelly SAND. Gravel is angular to subangular fine to coarse brick and clinker.                                | 0.30              |                         |
|                           |        |         |         |       |          | MADE GROUND: Brick courses.                                                                                                                 | 0.50              |                         |
| 0.40-0.50<br>0.40-0.50    | 2<br>3 | ES<br>D | T,V,J   |       |          | Light brown gravelly medium to coarse SAND. Gravel is subrounded to rounded fine to coarse mudstone and sandstone. (GLACIOFLUVIAL DEPOSITS) | (0.50)            |                         |
|                           |        |         |         |       |          | Reddish brown silty medium to coarse grained SAND. (Recovered as weathered sandstone)                                                       | 1.00              |                         |
|                           |        |         |         |       |          | Trial pit terminated at 1.05m depth.                                                                                                        | 1.05              |                         |

|                              |                               |                                                                                                                                                                                                                                                                                                                                                                                                    |             |                    |  |
|------------------------------|-------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------|--------------------|--|
| Plan (Not to Scale)          |                               | General Remarks                                                                                                                                                                                                                                                                                                                                                                                    |             |                    |  |
|                              |                               | <ol style="list-style-type: none"> <li>Scanned with CAT and Genny prior to excavation.</li> <li>Ease of trial pit excavation: moderate.</li> <li>No groundwater encountered.</li> <li>Trial pit remained dry and stable during excavation.</li> <li>Trial pit terminated at base of foundations.</li> <li>On completion, trial pit backfilled with arisings and finished with concrete.</li> </ol> |             |                    |  |
|                              |                               | All dimensions in metres                                                                                                                                                                                                                                                                                                                                                                           |             | Scale: <b>1:21</b> |  |
| Method Used: <b>Hand dug</b> | Plant Used: <b>Hand auger</b> | Logged By: <b>JTee</b>                                                                                                                                                                                                                                                                                                                                                                             | Checked By: |                    |  |

|                              |                                                |                                                   |                                                         |                         |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|-------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP25</b> |
| Contract Ref: <b>11264</b>   | Start: <b>16.05.18</b><br>End: <b>16.05.18</b> | Ground Level: <b>26.49</b>                        | National Grid Co-ordinate: <b>E:382702.8 N:397281.4</b> | Sheet: <b>2 of 4</b>    |

Trial Pit JTP25 - Sketches of Faces A & B and Profile

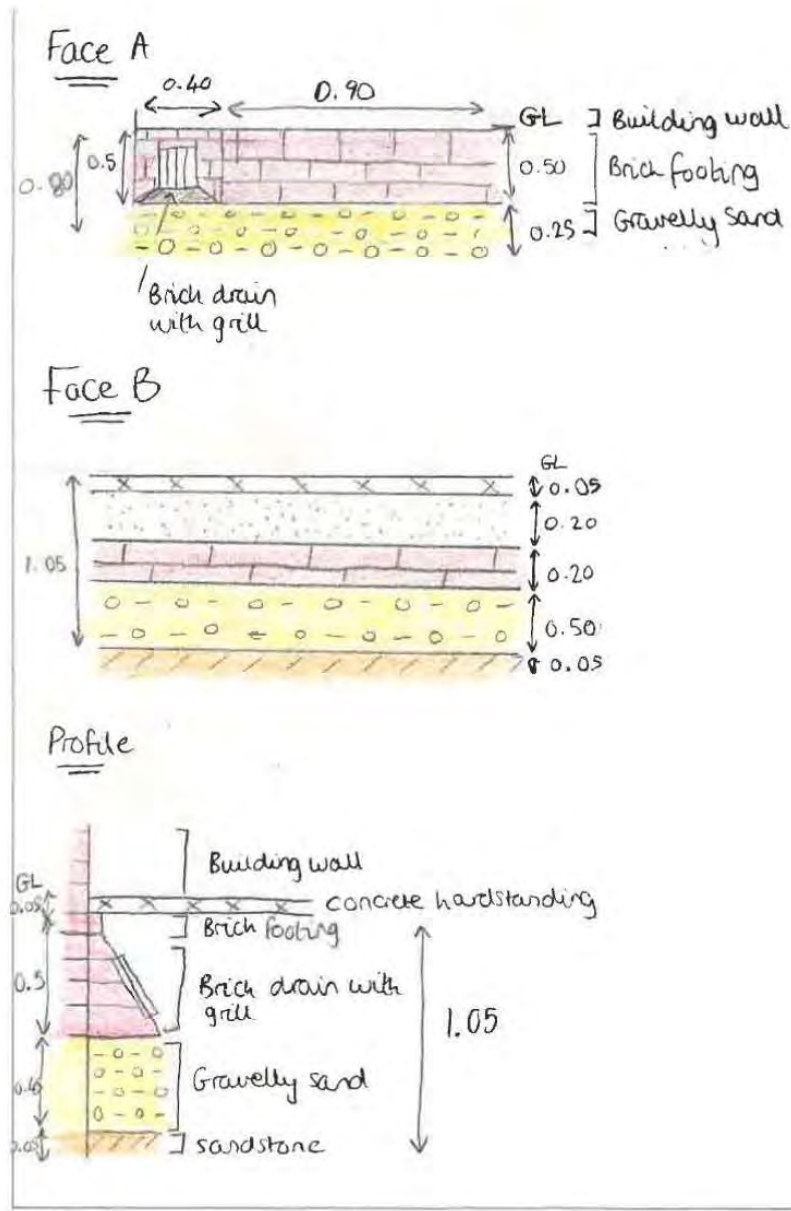

|                              |                                                |                                                   |                                                         |                         |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|-------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP25</b> |
| Contract Ref: <b>11264</b>   | Start: <b>16.05.18</b><br>End: <b>16.05.18</b> | Ground Level: <b>26.49</b>                        | National Grid Co-ordinate: <b>E:382702.8 N:397281.4</b> | Sheet: <b>3 of 4</b>    |

Trial Pit JTP25 - Photo Face A



Trial Pit JTP25 Photo Face B

|                              |                               |                        |                         |  |
|------------------------------|-------------------------------|------------------------|-------------------------|--|
| Method Used: <b>Hand dug</b> | Plant Used: <b>Hand auger</b> | Logged By: <b>JTee</b> | Checked By: <b>JS12</b> |  |
|------------------------------|-------------------------------|------------------------|-------------------------|--|

|                              |                                                |                                                   |                                                         |                             |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|-----------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP25</b>     |
| Contract Ref: <b>11264</b>   | Start: <b>16.05.18</b><br>End: <b>16.05.18</b> | Ground Level: <b>26.49</b>                        | National Grid Co-ordinate: <b>E:382702.8 N:397281.4</b> | Sheet: <b>4</b> of <b>4</b> |

Trial Pit JTP25 Photo Base



|                              |                               |                        |                                                                                                   |                                                                                       |
|------------------------------|-------------------------------|------------------------|---------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------|
| Method Used: <b>Hand dug</b> | Plant Used: <b>Hand auger</b> | Logged By: <b>JTee</b> | Checked By:  |  |
|------------------------------|-------------------------------|------------------------|---------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------|




| Samples and In-situ Tests            |    |      |         | Water                                                                               | Backfill                                                                           | Description of Strata                                                                                                                                    | Depth<br>(Thickness) | Material<br>Graphic<br>Legend                                                       |
|--------------------------------------|----|------|---------|-------------------------------------------------------------------------------------|------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------|-------------------------------------------------------------------------------------|
| Depth                                | No | Type | Results |                                                                                     |                                                                                    |                                                                                                                                                          |                      |                                                                                     |
| 0.00-0.10                            | 1  | ES   | T,V,J   |  |  | MADE GROUND: Greyish brown gravelly SAND. Gravel is subangular to subrounded fine to coarse limestone and brick with occasional glass, metal and timber. | 0.20                 |  |
|                                      |    |      |         |                                                                                     |                                                                                    | MADE GROUND: Concrete flags.                                                                                                                             | 0.30                 |                                                                                     |
| 0.35-0.40                            | 2  | ES   | T,V,J   |                                                                                     |                                                                                    | MADE GROUND: Blackish grey slightly gravelly ashy SAND. Gravel is angular to subangular brick, clinker and sandstone.                                    | 0.45                 |  |
| 0.40-1.90                            | 6  | ES   | T,V,J   |                                                                                     |                                                                                    | MADE GROUND: Brick course.                                                                                                                               | 0.55                 |                                                                                     |
| 0.60-0.70                            | 3  | ES   | T,V,J   |                                                                                     |                                                                                    | MADE GROUND: Blackish grey slightly gravelly SAND. Gravel is angular to subangular brick, clinker and sandstone.                                         | 0.75                 |  |
| 0.80-1.50                            | 4  | ES   | T,V,J   |                                                                                     |                                                                                    | Reddish brown silty medium to coarse grained SAND. (Recovered as weathered sandstone)                                                                    | (1.75)               |                                                                                     |
| 0.80-1.50                            | 5  | B    |         |                                                                                     |                                                                                    |                                                                                                                                                          |                      | 2.50                                                                                |
| Trial pit terminated at 2.50m depth. |    |      |         |                                                                                     |                                                                                    |                                                                                                                                                          |                      |                                                                                     |

|                                                              |                                      |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                |             |                    |  |
|--------------------------------------------------------------|--------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------|--------------------|--|
| Plan (Not to Scale) <div style="text-align: center;"> </div> |                                      | <h2 style="text-align: center;">General Remarks</h2> <ol style="list-style-type: none"> <li>1. Scanned with CAT and Genny prior to excavation.</li> <li>2. Ease of trial pit excavation: moderate.</li> <li>3. Groundwater strike at 2.10m.</li> <li>4. Trial pit remained stable during excavation.</li> <li>5. Trial pit terminated due to difficult digging (scraping)</li> <li>6. On completion, trial pit backfilled with arisings and finished with concrete.</li> </ol> |             |                    |  |
|                                                              |                                      | All dimensions in metres                                                                                                                                                                                                                                                                                                                                                                                                                                                       |             | Scale: <b>1:21</b> |  |
| Method Used: <b>Machine dug</b>                              | Plant Used: <b>Tracked excavator</b> | Logged By: <b>JTee</b>                                                                                                                                                                                                                                                                                                                                                                                                                                                         | Checked By: |                    |  |

PRINT LIBRARY\_v8\_06.GLB LibVersion: v8\_06\_018 PrjVersion: v8\_06 - Core+Logs - 002 | Log TRIAL PIT LOG - A4P | 11264 TALBOT MILL.GPJ - v8\_06.  
 57 Hilton Street, Piccadilly, Manchester, M1 2EJ. Tel: 0161 236 2757, Fax: 0161 236 7029, Web: www.rsk.co.uk. 02/10/18 - 14:42 | JS12 |

|                              |                                                |                                                   |                                                         |                                |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|--------------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP30 Face A</b> |
| Contract Ref: <b>11264</b>   | Start: <b>15.05.18</b><br>End: <b>15.05.18</b> | Ground Level: <b>26.36</b>                        | National Grid Co-ordinate: <b>E:382660.7 N:397301.9</b> | Sheet: <b>2 of 3</b>           |

Trial Pit JTP30 - Sketch Face A

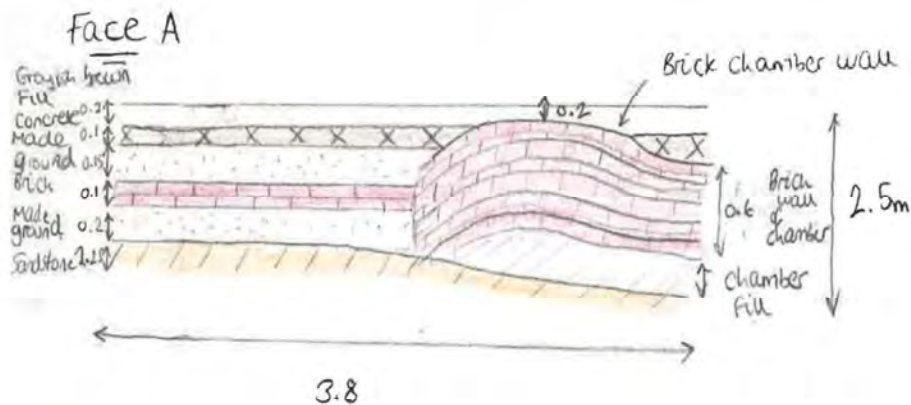

|                                 |                                      |                        |                                |            |
|---------------------------------|--------------------------------------|------------------------|--------------------------------|------------|
| Method Used: <b>Machine dug</b> | Plant Used: <b>Tracked excavator</b> | Logged By: <b>JTee</b> | Checked By: <b>[Signature]</b> | <b>AGS</b> |
|---------------------------------|--------------------------------------|------------------------|--------------------------------|------------|

|                              |                                                |                                                   |                                                         |                                |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|--------------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP30 Face A</b> |
| Contract Ref: <b>11264</b>   | Start: <b>15.05.18</b><br>End: <b>15.05.18</b> | Ground Level: <b>26.36</b>                        | National Grid Co-ordinate: <b>E:382660.7 N:397301.9</b> | Sheet: <b>3 of 3</b>           |

Trial Pit JTP30 - Photo



|                                 |                                      |                        |                                                                                                   |                                                                                       |
|---------------------------------|--------------------------------------|------------------------|---------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------|
| Method Used: <b>Machine dug</b> | Plant Used: <b>Tracked excavator</b> | Logged By: <b>JTee</b> | Checked By:  |  |
|---------------------------------|--------------------------------------|------------------------|---------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------|



# TRIAL PIT LOG

|                              |                                                |                            |                                                         |  |                                |
|------------------------------|------------------------------------------------|----------------------------|---------------------------------------------------------|--|--------------------------------|
| Contract: <b>Talbot Mill</b> |                                                |                            | Client: <b>Capital &amp; Centric (Adored) Ltd</b>       |  | Trial Pit: <b>JTP30 Face B</b> |
| Contract Ref: <b>11264</b>   | Start: <b>16.05.18</b><br>End: <b>16.05.18</b> | Ground Level: <b>26.36</b> | National Grid Co-ordinate: <b>E:382660.7 N:397301.9</b> |  | Sheet: <b>1 of 3</b>           |


| Samples and In-situ Tests |    |      |         | Water | Backfill | Description of Strata                                                                                                                                         | Depth (Thickness) | Material Graphic Legend |
|---------------------------|----|------|---------|-------|----------|---------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------|-------------------------|
| Depth                     | No | Type | Results |       |          |                                                                                                                                                               |                   |                         |
|                           |    |      |         |       |          | MADE GROUND: Greyish brown gravelly SAND. Gravel if angular to subrounded fine to coarse limestone, brick and slate. With occasional glass, metal and timber. | (0.35)<br>0.35    |                         |
|                           |    |      |         |       |          | MADE GROUND: Brick wall of chamber infilled with blackish brown sandy angular to subangular fine to coarse GRAVEL of ash and clinker.                         | (1.60)<br>1.95    |                         |
|                           |    |      |         |       |          | Reddish brown silty medium to coarse grained SAND. (Recovered as weathered sandstone)                                                                         | (0.55)<br>2.50    |                         |
|                           |    |      |         |       |          | Trial pit terminated at 2.50m depth.                                                                                                                          |                   |                         |

|                                 |                                      |                                                                                                                                                                                                                                                                                                                                       |             |                    |  |
|---------------------------------|--------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------|--------------------|--|
| Plan (Not to Scale)             |                                      | General Remarks                                                                                                                                                                                                                                                                                                                       |             |                    |  |
|                                 |                                      | <ol style="list-style-type: none"> <li>Scanned with CAT and Genny prior to excavation.</li> <li>Ease of trial pit excavation: moderate.</li> <li>Groundwater strike at 2.10m.</li> <li>Trial pit remained stable during excavation.</li> <li>On completion, trial pit backfilled with arisings and finished with concrete.</li> </ol> |             |                    |  |
|                                 |                                      | All dimensions in metres                                                                                                                                                                                                                                                                                                              |             | Scale: <b>1:21</b> |  |
| Method Used: <b>Machine dug</b> | Plant Used: <b>Tracked excavator</b> | Logged By: <b>JTee</b>                                                                                                                                                                                                                                                                                                                | Checked By: |                    |  |

GINT\_LIBRARY\_v8\_06.GLB LibVersion: v8\_06 - Core+Logs - 002 | Log TRIAL PIT LOG - A4P | 11264 TALBOT MILL.GPJ - v8\_06.  
 RSK Environment Ltd, Fourways House, 57 Hilton Street, Piccadilly, Manchester, M1 2EJ. Tel: 0161 236 2757, Fax: 0161 236 7029, Web: www.rsk.co.uk. | 02/10/18 - 14:42 | JS12 |

|                              |                                                |                                                   |                                                         |                                |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|--------------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP30 Face B</b> |
| Contract Ref: <b>11264</b>   | Start: <b>16.05.18</b><br>End: <b>16.05.18</b> | Ground Level: <b>26.36</b>                        | National Grid Co-ordinate: <b>E:382660.7 N:397301.9</b> | Sheet: <b>2 of 3</b>           |

Trial Pit JTP30 - Sketch Face B

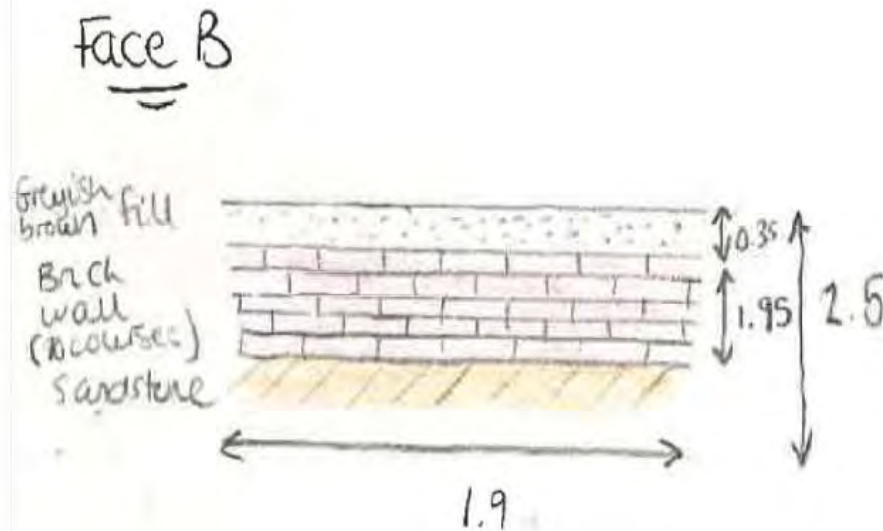

|                              |                                                |                                                   |                                                         |                                |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|--------------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP30 Face B</b> |
| Contract Ref: <b>11264</b>   | Start: <b>16.05.18</b><br>End: <b>16.05.18</b> | Ground Level: <b>26.36</b>                        | National Grid Co-ordinate: <b>E:382660.7 N:397301.9</b> | Sheet: <b>3 of 3</b>           |

Trial Pit JTP30 - Photo 1



Trial Pit JTP JTP30 Face B Photo 2


|                                 |                                      |                        |                         |            |
|---------------------------------|--------------------------------------|------------------------|-------------------------|------------|
| Method Used: <b>Machine dug</b> | Plant Used: <b>Tracked excavator</b> | Logged By: <b>JTee</b> | Checked By: <b>JTee</b> | <b>AGS</b> |
|---------------------------------|--------------------------------------|------------------------|-------------------------|------------|



# TRIAL PIT LOG


|                              |                                                |                                                   |                                                         |                                |  |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|--------------------------------|--|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP30 Face C</b> |  |
| Contract Ref: <b>11264</b>   | Start: <b>16.05.18</b><br>End: <b>16.05.18</b> | Ground Level: <b>26.36</b>                        | National Grid Co-ordinate: <b>E:382660.7 N:397301.9</b> | Sheet: <b>1 of 4</b>           |  |

| Samples and In-situ Tests |    |      |         | Water | Backfill | Description of Strata                                                                                                                                         | Depth<br>(Thickness) | Material<br>Graphic<br>Legend |
|---------------------------|----|------|---------|-------|----------|---------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------|-------------------------------|
| Depth                     | No | Type | Results |       |          |                                                                                                                                                               |                      |                               |
|                           |    |      |         |       |          | MADE GROUND: Greyish brown gravelly SAND. Gravel is angular to subrounded fine to coarse limestone, brick and slate. With occasional glass, metal and timber. | 0.20                 |                               |
|                           |    |      |         |       |          | MADE GROUND: Concrete flags.                                                                                                                                  | 0.30                 |                               |
|                           |    |      |         |       |          | MADE GROUND: Blackish grey slightly gravelly ashy SAND. Gravel is angular to subangular fine to coarse brick, clinker and sandstone.                          | 0.50                 |                               |
|                           |    |      |         |       |          | MADE GROUND: Brick wall.                                                                                                                                      | (0.30)<br>0.80       |                               |
|                           |    |      |         |       |          | Reddish brown silty medium to coarse grained SAND. (Recovered as weathered sandstone)                                                                         | (1.70)               |                               |
|                           |    |      |         |       |          |                                                                                                                                                               | 2.50                 |                               |
|                           |    |      |         |       |          | Trial pit terminated at 2.50m depth.                                                                                                                          |                      |                               |

|                                                                                     |                                      |                                                                                                                                                                                                                                                                                                                                                                                                                    |                                                                                                   |                                                                                       |  |
|-------------------------------------------------------------------------------------|--------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------|--|
| Plan (Not to Scale)                                                                 |                                      | General Remarks                                                                                                                                                                                                                                                                                                                                                                                                    |                                                                                                   |                                                                                       |  |
|  |                                      | <ol style="list-style-type: none"><li>1. Scanned with CAT and Genny prior to excavation.</li><li>2. Ease of trial pit excavation: moderate.</li><li>3. Groundwater strike at 2.10m.</li><li>4. Trial pit remained stable during excavation.</li><li>5. Trial pit terminated due to difficult digging (scraping)</li><li>6. On completion, trial pit backfilled with arisings and finished with concrete.</li></ol> |                                                                                                   |                                                                                       |  |
| All dimensions in metres                                                            |                                      | Scale: <b>1:21</b>                                                                                                                                                                                                                                                                                                                                                                                                 |                                                                                                   |                                                                                       |  |
| Method Used: <b>Machine dug</b>                                                     | Plant Used: <b>Tracked excavator</b> | Logged By: <b>JTee</b>                                                                                                                                                                                                                                                                                                                                                                                             | Checked By:  |  |  |

|                              |                                                |                                                   |                                                         |                                |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|--------------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP30 Face C</b> |
| Contract Ref: <b>11264</b>   | Start: <b>16.05.18</b><br>End: <b>16.05.18</b> | Ground Level: <b>26.36</b>                        | National Grid Co-ordinate: <b>E:382660.7 N:397301.9</b> | Sheet: <b>2 of 4</b>           |

Trial Pit JTP30 - Sketch -Face C

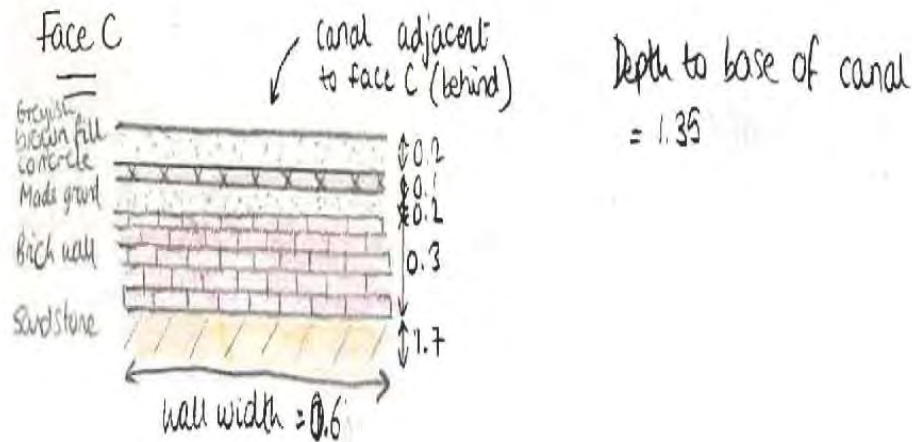

|                                 |                                      |                        |                         |            |
|---------------------------------|--------------------------------------|------------------------|-------------------------|------------|
| Method Used: <b>Machine dug</b> | Plant Used: <b>Tracked excavator</b> | Logged By: <b>JTee</b> | Checked By: <b>JTee</b> | <b>AGS</b> |
|---------------------------------|--------------------------------------|------------------------|-------------------------|------------|

|                              |                                                |                                                   |                                                         |                                |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|--------------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP30 Face C</b> |
| Contract Ref: <b>11264</b>   | Start: <b>16.05.18</b><br>End: <b>16.05.18</b> | Ground Level: <b>26.36</b>                        | National Grid Co-ordinate: <b>E:382660.7 N:397301.9</b> | Sheet: <b>3</b> of <b>4</b>    |

Trial Pit JTP30 Face C - Photo 1



Trial Pit JTP30 Face C - Photo 2

|                                 |                                      |                        |                                |            |
|---------------------------------|--------------------------------------|------------------------|--------------------------------|------------|
| Method Used: <b>Machine dug</b> | Plant Used: <b>Tracked excavator</b> | Logged By: <b>JTee</b> | Checked By: <b>[Signature]</b> | <b>AGS</b> |
|---------------------------------|--------------------------------------|------------------------|--------------------------------|------------|

|                              |                                                |                                                   |                                                         |                                |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|--------------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP30 Face C</b> |
| Contract Ref: <b>11264</b>   | Start: <b>16.05.18</b><br>End: <b>16.05.18</b> | Ground Level: <b>26.36</b>                        | National Grid Co-ordinate: <b>E:382660.7 N:397301.9</b> | Sheet: <b>4 of 4</b>           |

Trial Pit JTP30 Face C - Photo 3




|                                 |                                      |                        |                         |            |
|---------------------------------|--------------------------------------|------------------------|-------------------------|------------|
| Method Used: <b>Machine dug</b> | Plant Used: <b>Tracked excavator</b> | Logged By: <b>JTee</b> | Checked By: <b>JTee</b> | <b>AGS</b> |
|---------------------------------|--------------------------------------|------------------------|-------------------------|------------|



# TRIAL PIT LOG


|                              |                                                |                                                   |                                                         |                                |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|--------------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP31 Face A</b> |
| Contract Ref: <b>11264</b>   | Start: <b>14.05.18</b><br>End: <b>14.05.18</b> | Ground Level: <b>26.88</b>                        | National Grid Co-ordinate: <b>E:382691.1 N:397311.6</b> | Sheet: <b>1 of 3</b>           |

| Samples and In-situ Tests                                      |             |             |             | Water                                                                              | Backfill                                                                                                                                                                                                                 | Description of Strata | Depth<br>(Thick<br>ness)                                                             | Material<br>Graphic<br>Legend |
|----------------------------------------------------------------|-------------|-------------|-------------|------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------|--------------------------------------------------------------------------------------|-------------------------------|
| Depth                                                          | No          | Type        | Results     |                                                                                    |                                                                                                                                                                                                                          |                       |                                                                                      |                               |
| 0.60-0.80<br>0.60-0.80                                         | 1<br>2      | D<br>ES     | T,V,J       |  | MADE GROUND: Greyish brown slightly clayey gravelly medium to coarse SAND with a medium cobble content. Gravel is subrounded to subangular fine to coarse of brick, sandstone and concrete with rare metal and rootlets. | (0.25)<br>0.25        |   |                               |
|                                                                |             |             |             |                                                                                    | MADE GROUND: Six courses of 73m red brick.                                                                                                                                                                               | (0.40)<br>0.65        |                                                                                      |                               |
| 0.80-1.10                                                      | 3           | ES          | T,V,J       |                                                                                    | MADE GROUND: Brown and greyish red silty gravelly SAND with a medium cobble content of sandstone (250mm to 170mm). Gravel is subrounded to subangular fine to coarse of brick, sandstone, glass and quartzite.           | 0.80                  |   |                               |
|                                                                |             |             |             |                                                                                    | Yellowish greyish brown slightly silty slightly gravelly coarse SAND with a low to medium cobble content of sandstone. Gravel is subrounded to rounded fine to coarse sandstone. (GLACIOFLUVIAL DEPOSITS)                | (0.60)<br>1.40        |                                                                                      |                               |
| 1.50-1.80<br>1.50-1.80<br>1.50-1.80                            | 2<br>3<br>4 | D<br>B<br>B | D<br>B<br>B |                                                                                    | Orangish red slightly silty gravelly coarse SAND with a low cobble content. Gravel is subangular to subrounded of weak coarse sandstone. (Weathered sandstone).                                                          | (0.50)<br>1.90        |  |                               |
|                                                                |             |             |             |                                                                                    |                                                                                                                                                                                                                          |                       |                                                                                      |                               |
|                                                                |             |             |             |                                                                                    |                                                                                                                                                                                                                          |                       |                                                                                      |                               |
| Trial pit terminated at 1.90m depth due to difficulty digging. |             |             |             |                                                                                    |                                                                                                                                                                                                                          |                       |                                                                                      |                               |

|                                 |                                      |                                                                                                                                                                                                                                                                                                                                                                       |             |  |
|---------------------------------|--------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------|--|
| Plan (Not to Scale)             |                                      | General Remarks                                                                                                                                                                                                                                                                                                                                                       |             |  |
|                                 |                                      | <ol style="list-style-type: none"> <li>Scanned with CAT and Genny prior to excavation.</li> <li>Ease of trial pit excavation: moderate.</li> <li>No groundwater encountered.</li> <li>Trial pit sides unstable during excavation.</li> <li>Brick wall very fragile.</li> <li>On completion, trial pit backfilled with arisings and finished with concrete.</li> </ol> |             |  |
| All dimensions in metres        |                                      | Scale: <b>1:21</b>                                                                                                                                                                                                                                                                                                                                                    |             |  |
| Method Used: <b>Machine dug</b> | Plant Used: <b>Tracked excavator</b> | Logged By: <b>EHobbs</b>                                                                                                                                                                                                                                                                                                                                              | Checked By: |  |

|                              |                                                |                                                   |                                                         |                                |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|--------------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP31 Face A</b> |
| Contract Ref: <b>11264</b>   | Start: <b>14.05.18</b><br>End: <b>14.05.18</b> | Ground Level: <b>26.88</b>                        | National Grid Co-ordinate: <b>E:382691.1 N:397311.6</b> | Sheet: <b>2 of 3</b>           |

Trial Pit JTP31 Face A - Sketch of plan and profile

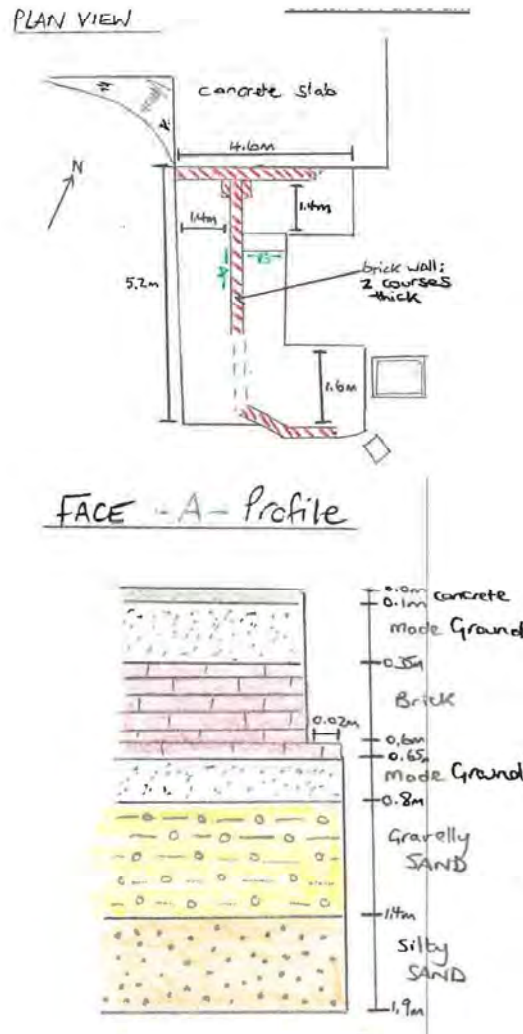

|                                 |                                      |                          |                       |            |
|---------------------------------|--------------------------------------|--------------------------|-----------------------|------------|
| Method Used: <b>Machine dug</b> | Plant Used: <b>Tracked excavator</b> | Logged By: <b>EHobbs</b> | Checked By: <b>EH</b> | <b>AGS</b> |
|---------------------------------|--------------------------------------|--------------------------|-----------------------|------------|

|                              |                                                |                                                   |                                                         |                                |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|--------------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP31 Face A</b> |
| Contract Ref: <b>11264</b>   | Start: <b>14.05.18</b><br>End: <b>14.05.18</b> | Ground Level: <b>26.88</b>                        | National Grid Co-ordinate: <b>E:382691.1 N:397311.6</b> | Sheet: <b>3 of 3</b>           |

Trial Pit JP31 Face A Photo 1



Trial Pit JP31 Face A Photo 2

|                                 |                                      |                          |                                                                                                   |                                                                                       |
|---------------------------------|--------------------------------------|--------------------------|---------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------|
| Method Used: <b>Machine dug</b> | Plant Used: <b>Tracked excavator</b> | Logged By: <b>EHobbs</b> | Checked By:  |  |
|---------------------------------|--------------------------------------|--------------------------|---------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------|



# TRIAL PIT LOG

|                              |                                                |                                                   |                                                         |                                |  |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|--------------------------------|--|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP31 Face B</b> |  |
| Contract Ref: <b>11264</b>   | Start: <b>14.05.18</b><br>End: <b>14.05.18</b> | Ground Level: <b>26.88</b>                        | National Grid Co-ordinate: <b>E:382691.1 N:397311.6</b> | Sheet: <b>1 of 3</b>           |  |


| Samples and In-situ Tests |    |      |         | Water | Backfill | Description of Strata                                                                                                                                                                                                                                                 | Depth (Thickness)      | Material Graphic Legend |
|---------------------------|----|------|---------|-------|----------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------|-------------------------|
| Depth                     | No | Type | Results |       |          |                                                                                                                                                                                                                                                                       |                        |                         |
| 0.40-0.60                 | 1  | ES   | T,V,J   |       |          | MADE GROUND: Un-reinforced concrete.                                                                                                                                                                                                                                  | 0.05                   |                         |
|                           |    |      |         |       |          | MADE GROUND: Greyish brown slightly clayey gravelly medium to coarse SAND with a low to medium cobble content of brick and concrete. Gravel is subrounded to subangular fine to coarse with frequent angular brick, sandstone and concrete with rare metal and glass. | (0.25)<br>0.30<br>0.35 |                         |
|                           |    |      |         |       |          | MADE GROUND: Yorkstone paving slab.                                                                                                                                                                                                                                   |                        |                         |
|                           |    |      |         |       |          | MADE GROUND: Brown and greyish red silty gravelly SAND with a medium cobble content of sandstone. Gravel is subrounded to subangular fine to coarse of brick, sandstone and glass with occasional rare paper and metal pipe.<br>... 0.50m, corroded metal pipe.       | (0.50)<br>0.85         |                         |
|                           |    |      |         |       |          | Yellowish greyish brown slightly silty slightly gravelly coarse SAND with a low to medium cobble content of sandstone. Gravel is subrounded to rounded fine to coarse of sandstone and quartzite.<br>(GLACIOFLUVIAL DEPOSITS)<br>Trial pit terminated at 0.95m depth. | 0.95                   |                         |

|                                 |                                      |                                                                                                                                                                                                                                                                                                                                                                                        |             |                    |  |
|---------------------------------|--------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------|--------------------|--|
| Plan (Not to Scale)             |                                      | General Remarks                                                                                                                                                                                                                                                                                                                                                                        |             |                    |  |
|                                 |                                      | <ol style="list-style-type: none"><li>1. Scanned with CAT and Genny prior to excavation.</li><li>2. Ease of trial pit excavation: moderate.</li><li>3. No groundwater encountered.</li><li>4. Trial pit remained stable during excavation.</li><li>5. Corroded metal pipe at 0.50m.</li><li>6. On completion, trial pit backfilled with arisings and finished with concrete.</li></ol> |             |                    |  |
|                                 |                                      | All dimensions in metres                                                                                                                                                                                                                                                                                                                                                               |             | Scale: <b>1:21</b> |  |
| Method Used: <b>Machine dug</b> | Plant Used: <b>Tracked excavator</b> | Logged By: <b>EHobbs</b>                                                                                                                                                                                                                                                                                                                                                               | Checked By: |                    |  |


|                              |                                                |                                                   |                                                         |                                |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|--------------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP31 Face B</b> |
| Contract Ref: <b>11264</b>   | Start: <b>14.05.18</b><br>End: <b>14.05.18</b> | Ground Level: <b>26.88</b>                        | National Grid Co-ordinate: <b>E:382691.1 N:397311.6</b> | Sheet: <b>2 of 3</b>           |

Trial Pit JTP31 Face B - Sketch of plan and profile

PLAN VIEW

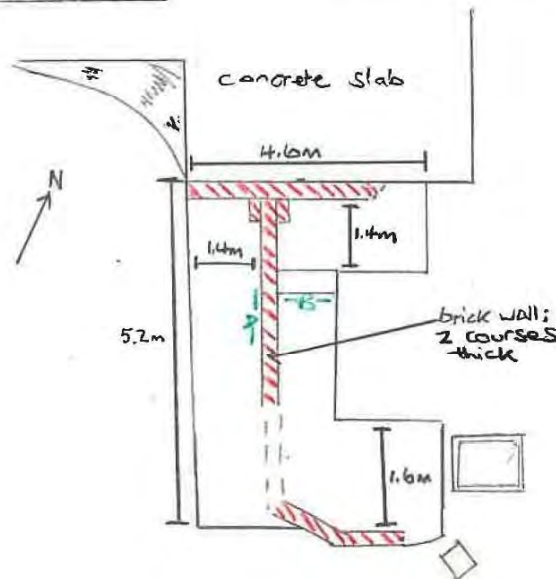

Face - B - Profile

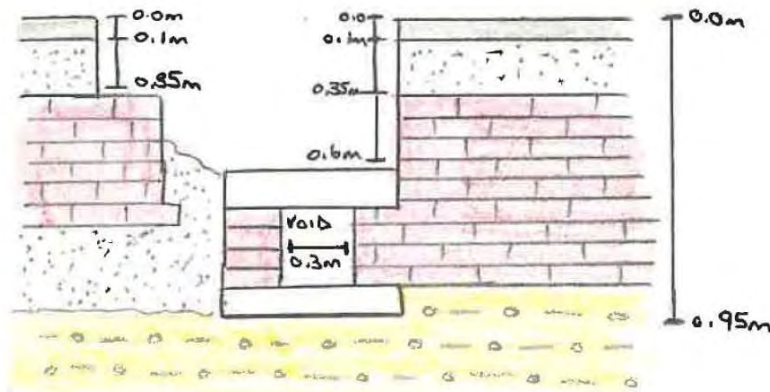

|                              |                                                |                                                   |                                                         |                                |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|--------------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP31 Face B</b> |
| Contract Ref: <b>11264</b>   | Start: <b>14.05.18</b><br>End: <b>14.05.18</b> | Ground Level: <b>26.88</b>                        | National Grid Co-ordinate: <b>E:382691.1 N:397311.6</b> | Sheet: <b>3 of 3</b>           |

Trial Pit JP31 Face B Photo 1




|                                 |                                      |                          |                                                                                                   |                                                                                       |
|---------------------------------|--------------------------------------|--------------------------|---------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------|
| Method Used: <b>Machine dug</b> | Plant Used: <b>Tracked excavator</b> | Logged By: <b>EHobbs</b> | Checked By:  |  |
|---------------------------------|--------------------------------------|--------------------------|---------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------|



# TRIAL PIT LOG


|                              |                                                |                                                   |                                                         |                          |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|--------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP31A</b> |
| Contract Ref: <b>11264</b>   | Start: <b>14.05.18</b><br>End: <b>14.05.18</b> | Ground Level: <b>27.21</b>                        | National Grid Co-ordinate: <b>E:382701.8 N:397308.6</b> | Sheet: <b>1 of 3</b>     |

| Samples and In-situ Tests |    |      |         | Water | Backfill | Description of Strata                                                                                                                                                                                                         | Depth (Thickness) | Material Graphic Legend |
|---------------------------|----|------|---------|-------|----------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------|-------------------------|
| Depth                     | No | Type | Results |       |          |                                                                                                                                                                                                                               |                   |                         |
| 0.50-0.80                 | 1  | ES   | T,V,J   |       |          | MADE GROUND: Un-reinforced concrete.                                                                                                                                                                                          | 0.15              |                         |
|                           |    |      |         |       |          | MADE GROUND: Reddish brown very gravelly SAND with abundant bricks (whole and fragmented) and occasional sandstone, metal pieces and glass. (Brick Fill)                                                                      | (2.45)            |                         |
|                           |    |      |         |       |          |                                                                                                                                                                                                                               | 2.60              |                         |
| 3.00-3.20                 | 2  | ES   | T,V,J   |       |          | MADE GROUND: Greyish brown and black slightly silty gravelly medium to coarse SAND with a high cobble content of sandstone blocks and flagstones. Gravel is brick and sandstone. (Sandstone blocks are 350mm x 200mm x 400mm) | (0.80)            |                         |
| 3.40-3.50                 | 3  | ES   | T,V,J   |       |          | Orangish purplish red gravelly coarse SAND. Gravel is fine to coarse weak coarse sandstone. (Weathered sandstone recovered as SAND).<br>Trial pit terminated at 3.50m depth due to collapsing sides.                          | 3.40<br>3.50      |                         |

|                                                                                                                   |                                      |                                                                                                                                                                                                                                                                                                                   |                                                                                                              |
|-------------------------------------------------------------------------------------------------------------------|--------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------|
| <b>Plan (Not to Scale)</b><br> |                                      | <b>General Remarks</b><br>1. Scanned with CAT and Genny prior to excavation.<br>2. Ease of trial pit excavation: difficult.<br>3. Slight groundwater seepage at 3.50m.<br>4. Trial pit sides very unstable during excavation.<br>5. On completion, trial pit backfilled with arisings and finished with concrete. |                                                                                                              |
| All dimensions in metres                                                                                          |                                      | Scale: <b>1:21</b>                                                                                                                                                                                                                                                                                                |                                                                                                              |
| Method Used: <b>Machine dug</b>                                                                                   | Plant Used: <b>Tracked excavator</b> | Logged By: <b>EHobbs</b>                                                                                                                                                                                                                                                                                          | Checked By:  <b>AGS</b> |

|                              |                                                |                                                   |                                                         |                          |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|--------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP31A</b> |
| Contract Ref: <b>11264</b>   | Start: <b>14.05.18</b><br>End: <b>14.05.18</b> | Ground Level: <b>27.21</b>                        | National Grid Co-ordinate: <b>E:382701.8 N:397308.6</b> | Sheet: <b>2 of 3</b>     |

Trial Pit JP31A - Sketch of plan and profiles

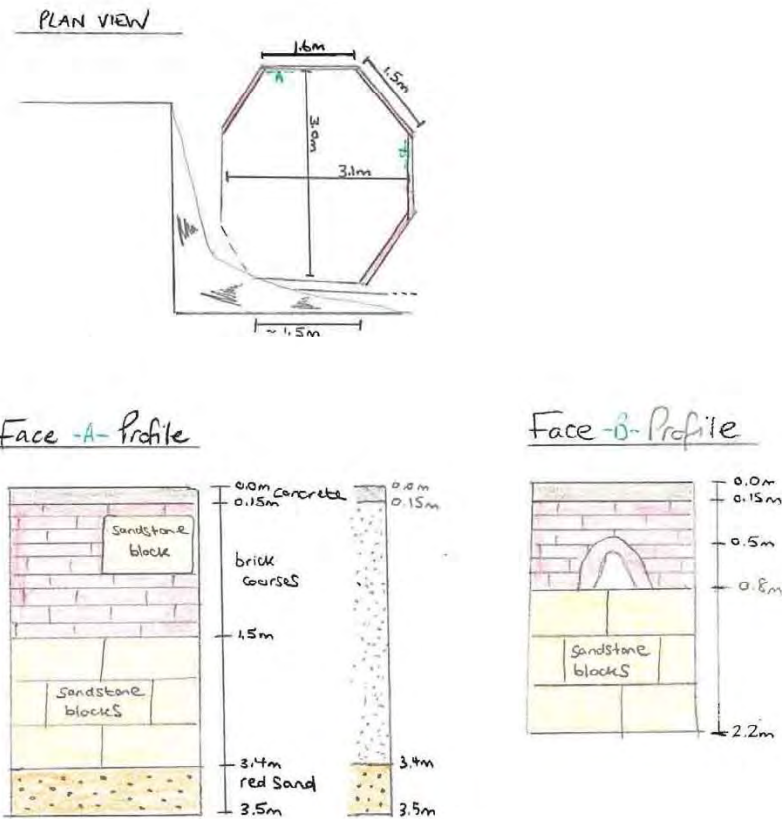

|                              |                                                |                                                   |                                                         |                          |
|------------------------------|------------------------------------------------|---------------------------------------------------|---------------------------------------------------------|--------------------------|
| Contract: <b>Talbot Mill</b> |                                                | Client: <b>Capital &amp; Centric (Adored) Ltd</b> |                                                         | Trial Pit: <b>JTP31A</b> |
| Contract Ref: <b>11264</b>   | Start: <b>14.05.18</b><br>End: <b>14.05.18</b> | Ground Level: <b>27.21</b>                        | National Grid Co-ordinate: <b>E:382701.8 N:397308.6</b> | Sheet: <b>3 of 3</b>     |

Trial Pit JP31A Photo 1



Trial Pit JP31A Photo 2

|                                 |                                      |                          |                       |            |
|---------------------------------|--------------------------------------|--------------------------|-----------------------|------------|
| Method Used: <b>Machine dug</b> | Plant Used: <b>Tracked excavator</b> | Logged By: <b>EHobbs</b> | Checked By: <b>EH</b> | <b>AGS</b> |
|---------------------------------|--------------------------------------|--------------------------|-----------------------|------------|



# TRIAL PIT LOG

|                              |                                                |                            |                                                         |  |                              |
|------------------------------|------------------------------------------------|----------------------------|---------------------------------------------------------|--|------------------------------|
| Contract: <b>Talbot Mill</b> |                                                |                            | Client: <b>Capital &amp; Centric (Adored) Ltd</b>       |  | Trial Pit: <b>JTP10A rev</b> |
| Contract Ref: <b>11264</b>   | Start: <b>28.11.18</b><br>End: <b>29.11.18</b> | Ground Level: <b>26.18</b> | National Grid Co-ordinate: <b>E:382686.0 N:397257.5</b> |  | Sheet: <b>1 of 4</b>         |

| Samples and In-situ Tests |    |      |         | Water | Backfill | Description of Strata                                                                                                                                                   | Depth (Thickness) | Material Graphic Legend |
|---------------------------|----|------|---------|-------|----------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------|-------------------------|
| Depth                     | No | Type | Results |       |          |                                                                                                                                                                         |                   |                         |
|                           |    |      |         |       |          | MADE GROUND: Yorkstone flags.                                                                                                                                           | 0.08              |                         |
|                           |    |      |         |       |          | MADE GROUND: Greyish brown gravelly ashy SAND. Gravel is angular to subrounded fine to coarse of brick and sandstone.                                                   | (0.45)            |                         |
|                           |    |      |         |       |          | Light brown gravelly SAND. Gravel is subrounded to rounded fine to coarse mudstone and sandstone. With occasional pockets of sandy silty clay. (GLACIOFLUVIAL DEPOSITS) | (0.32)            |                         |
|                           |    |      |         |       |          | Firm slightly gravelly sandy CLAY. Gravel is subangular to subrounded fine to coarse of mixed lithologies. (GLACIOFLUVIAL DEPOSITS)                                     | (0.70)            |                         |
|                           |    |      |         |       |          | Weak red sandstone recovered as silty SAND. (WEATHERED SANDSTONE)                                                                                                       | 1.55              |                         |
|                           |    |      |         |       |          | Trial pit terminated at 1.63m depth.                                                                                                                                    | 1.63              |                         |

## General Remarks

1. Scanned with CAT and Genny prior to excavation.
2. Ease of trial pit excavation: difficult.
3. No groundwater encountered.
4. Trial pit remained dry and stable during excavation.
5. Trial pit terminated at 1.63m bgl.
6. On completion, trial pit backfilled with arisings and flagstones replaced.

All dimensions in metres

Scale:

**1:11**

|                              |                               |                          |                       |  |
|------------------------------|-------------------------------|--------------------------|-----------------------|--|
| Method Used: <b>Hand dug</b> | Plant Used: <b>Hand tools</b> | Logged By: <b>EHobbs</b> | Checked By: <b>KF</b> |  |
|------------------------------|-------------------------------|--------------------------|-----------------------|--|
