
ID	Task Name	Duration	Start	Finish
0	**Fraser House, Charlotte St, Manchester**	**275 days**	**Mon 04/07/22**	**Fri 21/07/23**
1	**Site set up**	**35 days**	**Mon 04/07/22**	**Fri 19/08/22**
2	Site set up	5 days	Mon 04/07/22	Fri 08/07/22
3	Delivery of fencing	2 days	Thu 07/07/22	Fri 08/07/22
4	Delivery of Cabins/toilet	2 days	Thu 07/07/22	Fri 08/07/22
5	Scaffold Erection to Portland and Charlotte St	25 days	Mon 11/07/22	Fri 12/08/22
6	Erection of advertisment hoarding	5 days	Mon 15/08/22	Fri 19/08/22
7	**Works to Portland St**	**145 days**	**Wed 24/08/22**	**Tue 14/03/23**
8	Joint survey with KPS architects	5 days	Wed 24/08/22	Tue 30/08/22
9	Template stone and produce working drawing	10 days	Wed 31/08/22	Tue 13/09/22
10	Order new stone	20 days	Wed 14/09/22	Tue 11/10/22
11	Manufacture of new masonry	20 days	Wed 12/10/22	Tue 08/11/22
12	Rebed copings	10 days	Wed 14/09/22	Tue 27/09/22
13	Rebuild brick piers	10 days	Wed 28/09/22	Tue 11/10/22
14	Cut out existing masonry	15 days	Wed 12/10/22	Tue 01/11/22
15	Refix new Masonry	25 days	Wed 02/11/22	Tue 06/12/22
16	Lead works	15 days	Wed 07/12/22	Tue 27/12/22
17	Structural works	15 days	Wed 28/12/22	Tue 17/01/23
18	Repointing works	20 days	Wed 18/01/23	Tue 14/02/23
19	Decoration works	20 days	Wed 15/02/23	Tue 14/03/23
20	**Masonry works to Charlotte St**	**122 days**	**Wed 18/01/23**	**Thu 06/07/23**
21	Joint survey with KPS architects	10 days	Wed 18/01/23	Tue 31/01/23
22	Template stone and produce working drawing	25 days	Wed 01/02/23	Tue 07/03/23
23	Order new stone	15 days	Wed 08/03/23	Tue 28/03/23
24	Manufacture of new masonry	50 days	Wed 29/03/23	Tue 06/06/23
25	Rebed copings	10 days	Wed 01/03/23	Tue 14/03/23
26	Rebuild brick piers	10 days	Wed 15/03/23	Tue 28/03/23
27	Cut out existing masonry	20 days	Wed 29/03/23	Tue 25/04/23
28	Refix new Masonry	20 days	Wed 26/04/23	Tue 23/05/23
29	Lead works	15 days	Wed 24/05/23	Tue 13/06/23
30	Repointing works	20 days	Wed 24/05/23	Tue 20/06/23
31	Decoration works	12 days	Wed 21/06/23	Thu 06/07/23
32	**Clear site**	**11 days**	**Fri 07/07/23**	**Fri 21/07/23**
33	Dismantle Scaffold to Portland and Charlotte St	11 days	Fri 07/07/23	Fri 21/07/23
34	Remove cabins,toilet and fencing, clear site and snag the works	4 days	Tue 18/07/23	Fri 21/07/23

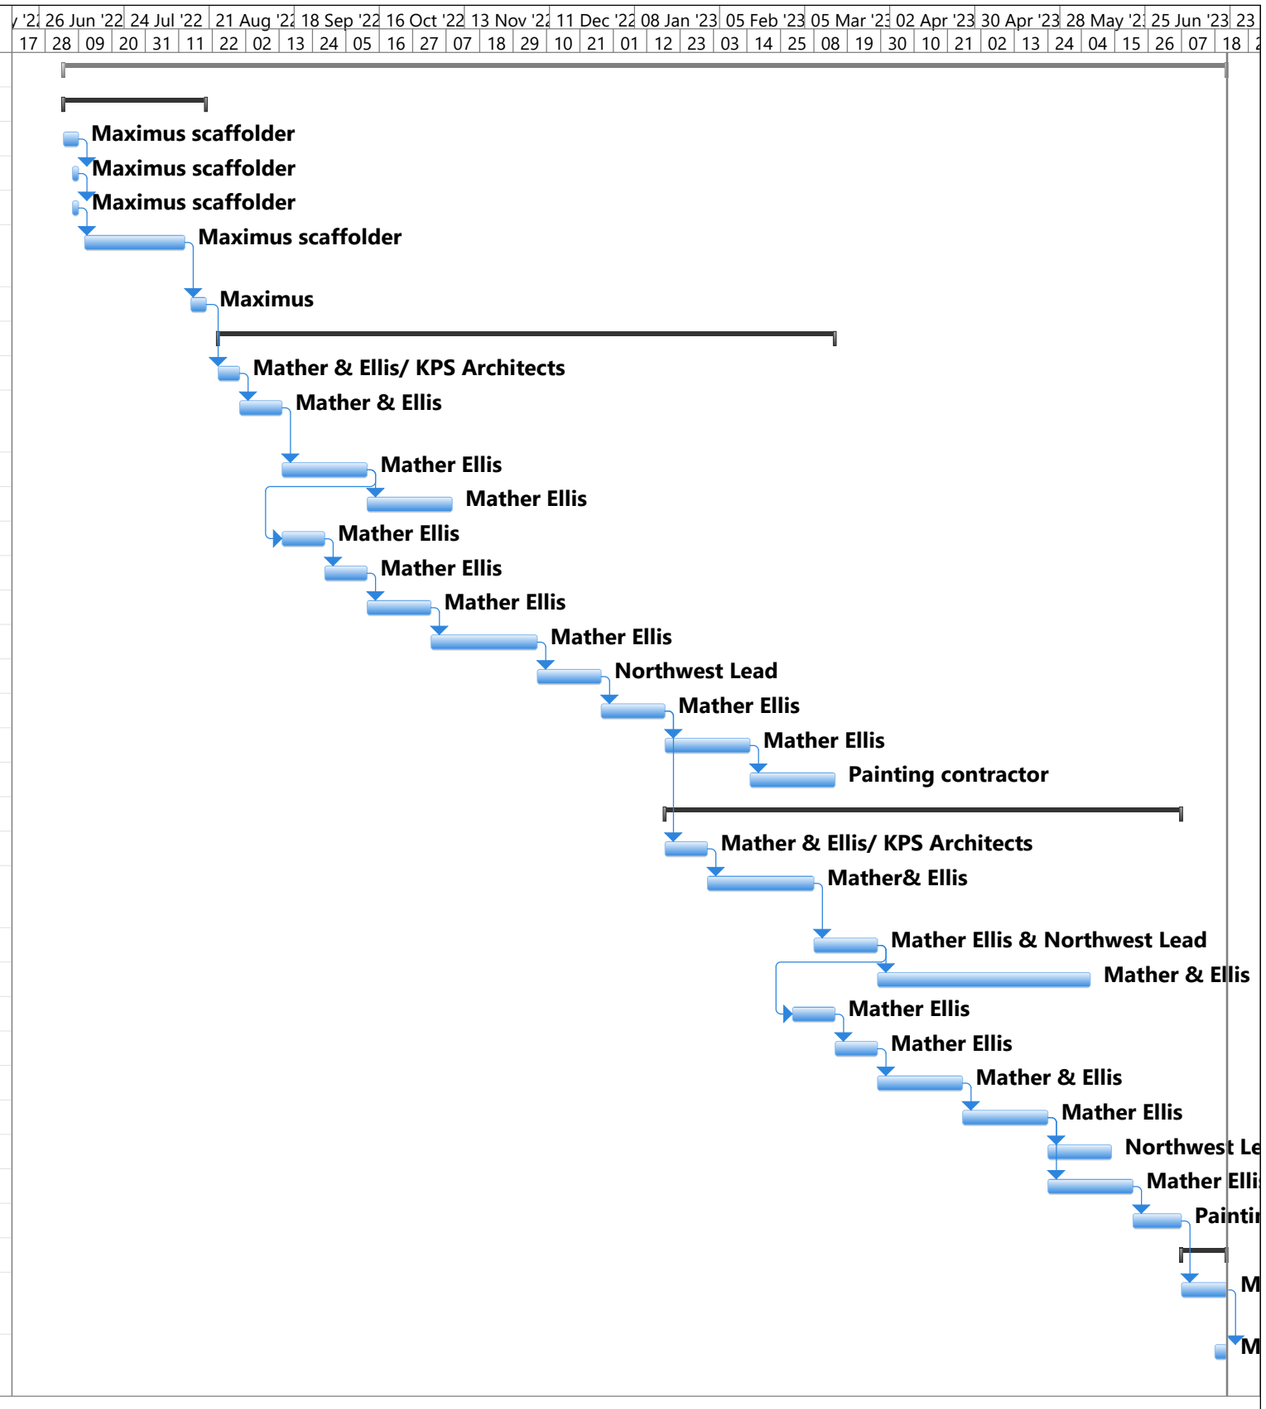

Project: Fraser House, Charlotte
Date: Fri 29/04/22

Task	Project Summary	Manual Task	Start-only	Deadline			
Split	Inactive Task	Duration-only	Finish-only	Progress			
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress			
Summary	Inactive Summary	Manual Summary	External Milestone				
