SAMPLE TRACKER

Project: OGS
Job Number: 63050
Client: Allied London
Architect: 3DR
LPA: Manchester
LPA Contact:
Revision: P10

	Sample Rejected
	Submitted for Approval
	Confirmation Required that named supplier is to be used
	Approved / Named Supplier Confirmed

Ref.	Description	Product/Material	Colour/Finish	NBS Ref.	Sub-Contractor or Supplier	Photo	DT Approval	Client Approval	LPA Approval	Comments
Façade										
FCD -001	FLH-131 (M40) - Corium brick tiles: Stretcher	Taylor Maxwell Weinerberger Corium	93800 with Stone Grey EA2030 mortar	FLH-131 (M40) - Corium brick tiles: Stretcher	Keyclad					
FCD-002	FLH-131 (M40) - Corium brick tiles: Stacked	Taylor Maxwell Weinerberger Corium	Sample Brick 6200 and Corium Historic KL charcoal mortar EA288	FLH-131 (M40) - Corium brick tiles: Stacked	Keyclad					
FCD-003	EWS-421 (H72) - Pressed aluminium parapet flashing	SoTech Optima	Black PPC	EWS-421 (H72) - Pressed aluminium parapet flashing	Keyclad					

SAMPLE TRACKER

FCD-004	EWS-121 (H11) - Automatic opening vent	Kawneer	Black PPC	EWS-121 (H11) - Automatic opening vent	Quest	 				
FCD-005	EWS-121 (H11) - Curtain walling system	Kawneer	Black PPC	EWS-121 (H11) -Curtain walling system	Quest					
FCD-006	Louvered extract and supply to WCs			Louvered extract and supply to WCs	Vaughan					

SAMPLE TRACKER

FCD-007	EWS-421 (H72) - Aluminium cladding to beams	SoTech Optima	Black PPC	EWS-421 (H72) - Aluminium cladding to beams – RAL 9011	Keyclad					
FCD-008	DRS-231 (L10) - Sliding glazed doors	Kawneer	Black PPC	DRS-231 (L10) - Sliding glazed doors- Ral 9011	Quest	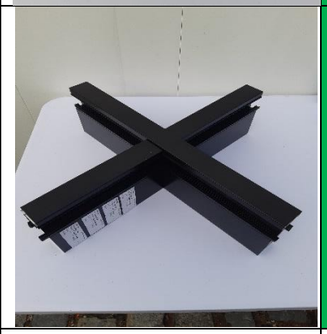				Frame will be as Curtain wall profiler sample
FCD-009	BAL-103 (L32) – Glass balustrade with handrail – Terrace			BAL-103 (L32) – Glass balustrade with handrail	TBC					
FCD-010	EWS-521 (H92) – Aluminium Rainscreen panel	SoTech Optima	Black PPC	EWS-521 (H92) – Aluminium Rainscreen panel-RAL 9011	Keyclad	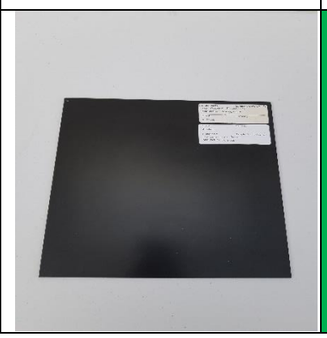				

SAMPLE TRACKER

FCD-011	Louvres	ALU+	Black PPC	Louvres- RAL 9011	Quest					
FCD-012	Anvil Mesh EM03 expanded mesh screen	Anvil Mesh	Black anodising		Keyclad					
FCD-013	BAL-101 (L32) – Frameless glass balustrade – Roof			BAL-101 (L32) – Frameless glass balustrade	TBC					
FCD-014	DRS-221 (H11) – Automatic glazed door	Kawneer	Black PPC	DRS-221 (H11) – Automatic glazed door	Quest					Frame will be as Curtain wall profiler sample
FCD-015	DRS-401 (L25) – External Metal doors	Kawneer	Black PPC	DRS-401 (L25) – External Metal doors	Quest					Frame will be as Curtain wall profiler sample

SAMPLE TRACKER

FCD-016	DRS-421 (L13) – Metal Louvred doors		Black PPC	DRS-421 (L13) – Metal Louvred doors	TBC					Frame will be as Curtain wall profiler sample
FCD-017	DRS-240 (L25) – Glazed Framed doors	Kawneer	Black PPC	DRS-240 (L25) – Glazed Framed doors	Quest					Frame will be as Curtain wall profiler sample
FCD-018 - A	GLP-211 (L42) – Back coated opaque glass / spandrel panel	Euroview Glass	Black PPC framing	GLP-211 (L42) – Back coated opaque glass / spandrel panel – Grey	Quest					
FCD-019	GLP-302 (L42) - Louvred panels	ALU+	Black PPC	GLP-302 (L42) - Louvred panels	Quest	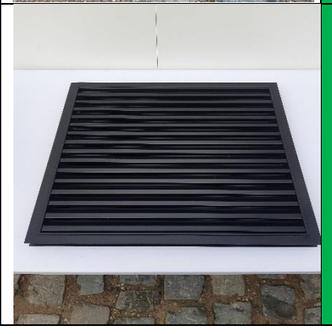				

SAMPLE TRACKER

FCD-020	Clear Glass Spandrel	Euroview Glass	Black PPC framing							
Externals/Landscaping										
EXT-001	(NBS TBC) – Bollards by other			(NBS TBC) – Bollards by other	TBC by client					
Roof										
RF-001	Paving Slabs to Roof, Terrace and Externals			Paving Slabs to Roof, Terrace and Externals	TBC					
Internal Finishes										
INT-001	LIN-102 (M40) Ceramic Wall Tiling			LIN-102 (M40) Ceramic Wall Tiling	TBC					
INT-002	PAN-200 Series (K32) Cubicles, IPS, vanity Units			PAN-200 Series (K32) Cubicles, IPS, vanity Units	TBC					
INT-003	PTS-100 Series (M60) Paint Finishes			PTS-100 Series (M60) Paint Finishes	TBC					

SAMPLE TRACKER

INT-004	SCR-100 (M10) Polished Concrete			SCR-100 (M10) Polished Concrete	TBC					
MEP										
MEP-001	Luminaires				Vaughan					
MEP-002	Sanitaryware				Vaughan					
MEP-003	Sockets and Switches				Vaughan					
MEP-005	Dry riser inlet - To M&E Engineer Spec			Dry riser inlet - To M&E Engineer Spec	Vaughan					
Stairs										
ST-001		STR-100 series (L30) Metal Stairs			STR-100 series (L30) Metal Stairs	Marshalls				External Stair Galvanised – MCC require black painting to underside of stairs and landings. Internal Stair Black RAL 9011
ST-001		Nosing to stairs				Marshalls				North Stair Grey RAL 7047 South Stair Black RAL 9011
Lifts										
LI-001	Push Button									
LI-002	Car Indicator									
LI-003	Wrap Round reveal									
LI-005	Wall Finishes									

BOWMER KIRKLAND

SAMPLE TRACKER

LI-006	Floor Finishes									



FCD-001	Brick - stretcher bond	FCD-011	Louvres
FCD-002	Brick - stack bond	FCD-012	Expanded mesh screen
FCD-003	Pressed aluminium parapet flashing	FCD-013	Glass balustrade without handrail
FCD-004	AOV	FCD-014	Automatic glazed door
FCD-005	Curtain walling system	FCD-015	External metal door - solid
FCD-006	Louvre (WC extract & supply)	FCD-016	External metal door - louvred
FCD-007	Aluminium beam cladding	FCD-017	Glazed framed doors
FCD-008	Sliding glazed doors	FCD-018	Back painted opaque glass
FCD-009	Glass balustrade with handrail	FCD-020	Clear glazed units
FCD-010	Aluminium rainscreen panel		

ENVELOPE MATERIAL SAMPLE KEY

OGS - ZONE 6
MANCHESTER NOVEMBER 2020

Drawing No. 190146-3DR-Z6-XX-PP-08102
Rev No. A
Scale. NTS@A2

3D REID



Notes

Do not scale from this drawing.

All dimensions are to be checked prior to construction and any discrepancies are to be identified to the Architect.

Copyright reserved.

KEY

01. Existing curtain wall refurbished - new film to spandrel panels to match existing
02. Existing windows refurbished - damaged units replaced to match existing
03. Existing brickwork
04. Existing low level cladding
05. Existing glazed curtain wall - clear
06. Existing windows replaced with new to match
07. Existing glass louvres
08. Window opening to match existing adjacent window
09. Glass louvres to match existing
10. Metal louvres - dark grey
11. Glazed capped curtain wall and entrance door - clear with dark grey frame
12. Glazed capped curtain wall - clear
13. Glazed retractable roof - clear
14. Glazed capless curtain wall - clear
15. Glazed capless curtain wall - opaque
16. Frameless glazed balustrade - top section clear, bottom section opaque
17. Louvre screen - light grey
18. Aluminium rainscreen panel - light grey

21. Brick tiles - stretcher bond, dark grey blue
22. Brick tiles - stacked bond, grey
23. Capped glazed curtain wall - clear
24. Glass balustrade with handrail - clear
25. Aluminium rainscreen panel - black grey
26. Louvred screen - light grey
27. Metal expanded mesh screen - dark grey
28. Frameless glass balustrade - clear
29. Glazed framed doors - clear
30. Metal doors - dark grey
31. Metal louvred doors - dark grey
32. External metal stair - black
33. Back coated opaque glass / spandrel panel - light grey
34. Metal louvred panels - dark grey

41. Bricks - stretcher bond, blue grey
42. Blackened metal glazing
43. Textured Metal cladding - black
44. Capped glazed curtain wall - clear
45. Capped curtain wall - opaque
46. Louvre screen - light grey with planting over
47. Metal Canopy - dark grey

51. Prefabricated container unit with clear glazing on the front
52. Glazed capped curtain wall - clear
53. Metal rainscreen - mid grey
54. Proprietary metal balustrade - black grey
55. Metal gate - black grey
56. External metal stair - black grey

61. Existing brickwork
62. Existing brickwork behind the previous extension
63. Existing windows - clear glazing
64. Existing grey cladding and louvres
65.Existing decorative banner
66. Metal mesh cladding
67. Signage subject to separate applications

E	09/07/20	Updated for Planning	HM
D	02/04/20	Issued for review	GL
C	28/02/20	Material key added	GL
B	20/02/20	Updated for planning draft	CLH
A	04/11/19	First issue	GL

Revisions

Status
INFORMATION

Client
Manchester Quays Ltd

Project
OGS
St John's
Manchester

Title
Proposed North Elevation
All Zones

Scale	Size	Date	Drawn	Checked
1 : 100	A1	20/02/20	CH	NS

3DReid
www.3DReid.com
Architecture Interiors Masterplanning

Drawing No. 180146-3DR-Z0-SE-DR-D133

Rev. E



FCD-001	Brick - stretcher bond
FCD-002	Brick - stack bond
FCD-003	Pressed aluminium parapet flashing
FCD-004	AOV
FCD-005	Curtain walling system
FCD-006	Louvre (WC extract & supply)
FCD-007	Aluminium beam cladding
FCD-008	Sliding glazed doors
FCD-009	Glass balustrade with handrail
FCD-010	Aluminium rainscreen panel
FCD-011	Louvres
FCD-012	Expanded mesh screen
FCD-013	Glass balustrade without handrail
FCD-014	Automatic glazed door
FCD-015	External metal door - solid
FCD-016	External metal door - louvred
FCD-017	Glazed framed doors
FCD-018	Back painted opaque glass
FCD-020	Clear glazed units

ENVELOPE MATERIAL SAMPLE KEY

OGS - ZONE 6
MANCHESTER NOVEMBER 2020

Drawing No. 190146-3DR-Z6-XX-PP-08101
Rev No. A
Scale. NTS@A2

3D REID
