
Methodology for the formation of new doorway openings to corner of Corporation / Hanover street. To Hanover building.

Issued By: Peter Cresswell

Position: Project Manager

Date: 21/02/2021

All sandstone & granite will be identified against a picture and ID tagged. Any recovered stone not used to re dress openings will be stored on site.

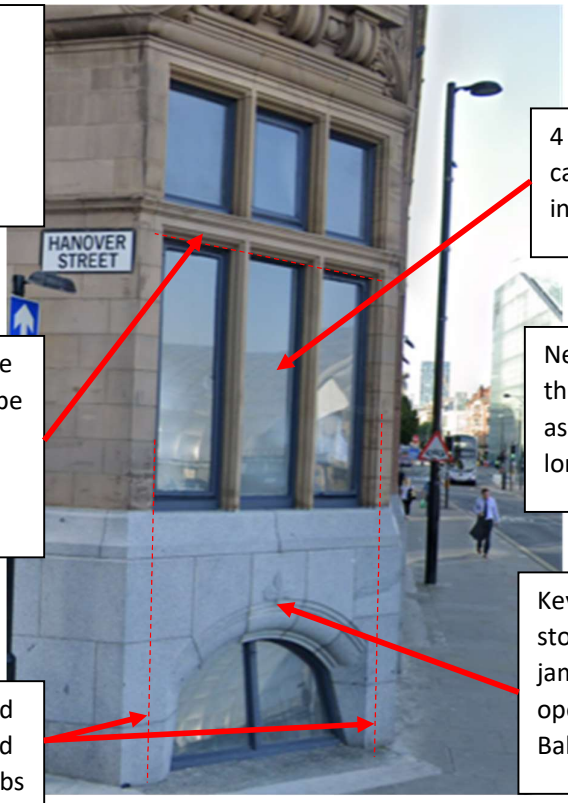

4 No. Existing windows are to be carefully removed and stored on site in a location identified by the client.

All stone below this transom will be removed to allow the doorway to be formed. Additional permanent support may be needed. This is to be ascertained as work proceeds.

New lifting points will be added to the granite stones where necessary as the original lift points can no longer be used.

Key stone to be saved. All other stone will be used to re dress the jambs of this opening and the opening on the opposite corner of Balloon Street.

Granite arch to be cut along dashed line to form opening using diamond cutting techniques. The stone jambs will be protected with Plywood as soon as practically possible.

Any recovered stone will be attached to a pallet using banding and NOT pallet wrap. Each piece of recovered stone will be ID tagged to show location and a master document will be issued to the client in the O&M manual at Practical Completion.
