Line	Name	Duration	Start Date	Finish Date
1	Agree facade samples and specification required with Project Architect	6w	27/07/2020	07/09/2020
2	Project Architect issues proposed facade sample drawings	1w	07/09/2020	11/09/2020
3	Procurement of facade specialist design contractors	8w	07/08/2020	02/10/2020
4	Project Architect develops interface / drip details with facade specialist design contractor	2w	05/10/2020	16/10/2020
5	Facade specialist design contractor manufacture desk top samples	4w	05/10/2020	30/10/2020
6	Physical desk top samples are reviewed and agreed with Project Architect	1w	02/11/2020	06/11/2020
7	Present desk top facade samples to MCC and full size mock up drawing / interface details/ material specifications	1w	09/11/2020	13/11/2020
8	Facade specilaist contractor designs full size mock up sample panel inc approvals/shop drawings	6w	05/10/2020	13/11/2020
9	Facade specialist design contractors manufacture sample Panel / inc support structure	5w	09/11/2020	11/12/2020
10	Erect Full size facade sample panel on site	2w	07/12/2020	18/12/2020
11	Project Architect inspects and approves Mock Up	1w	04/01/2021	08/01/2021
12	Inspect Full size Mock up with MCC for final approvals	1w	11/01/2021	15/01/2021
13	Draft Facade Quality Control Plan	3w	30/11/2020	18/12/2020
14	Issue Facade Quality Control Plan to MCC for approval	1w	04/01/2021	08/01/2021

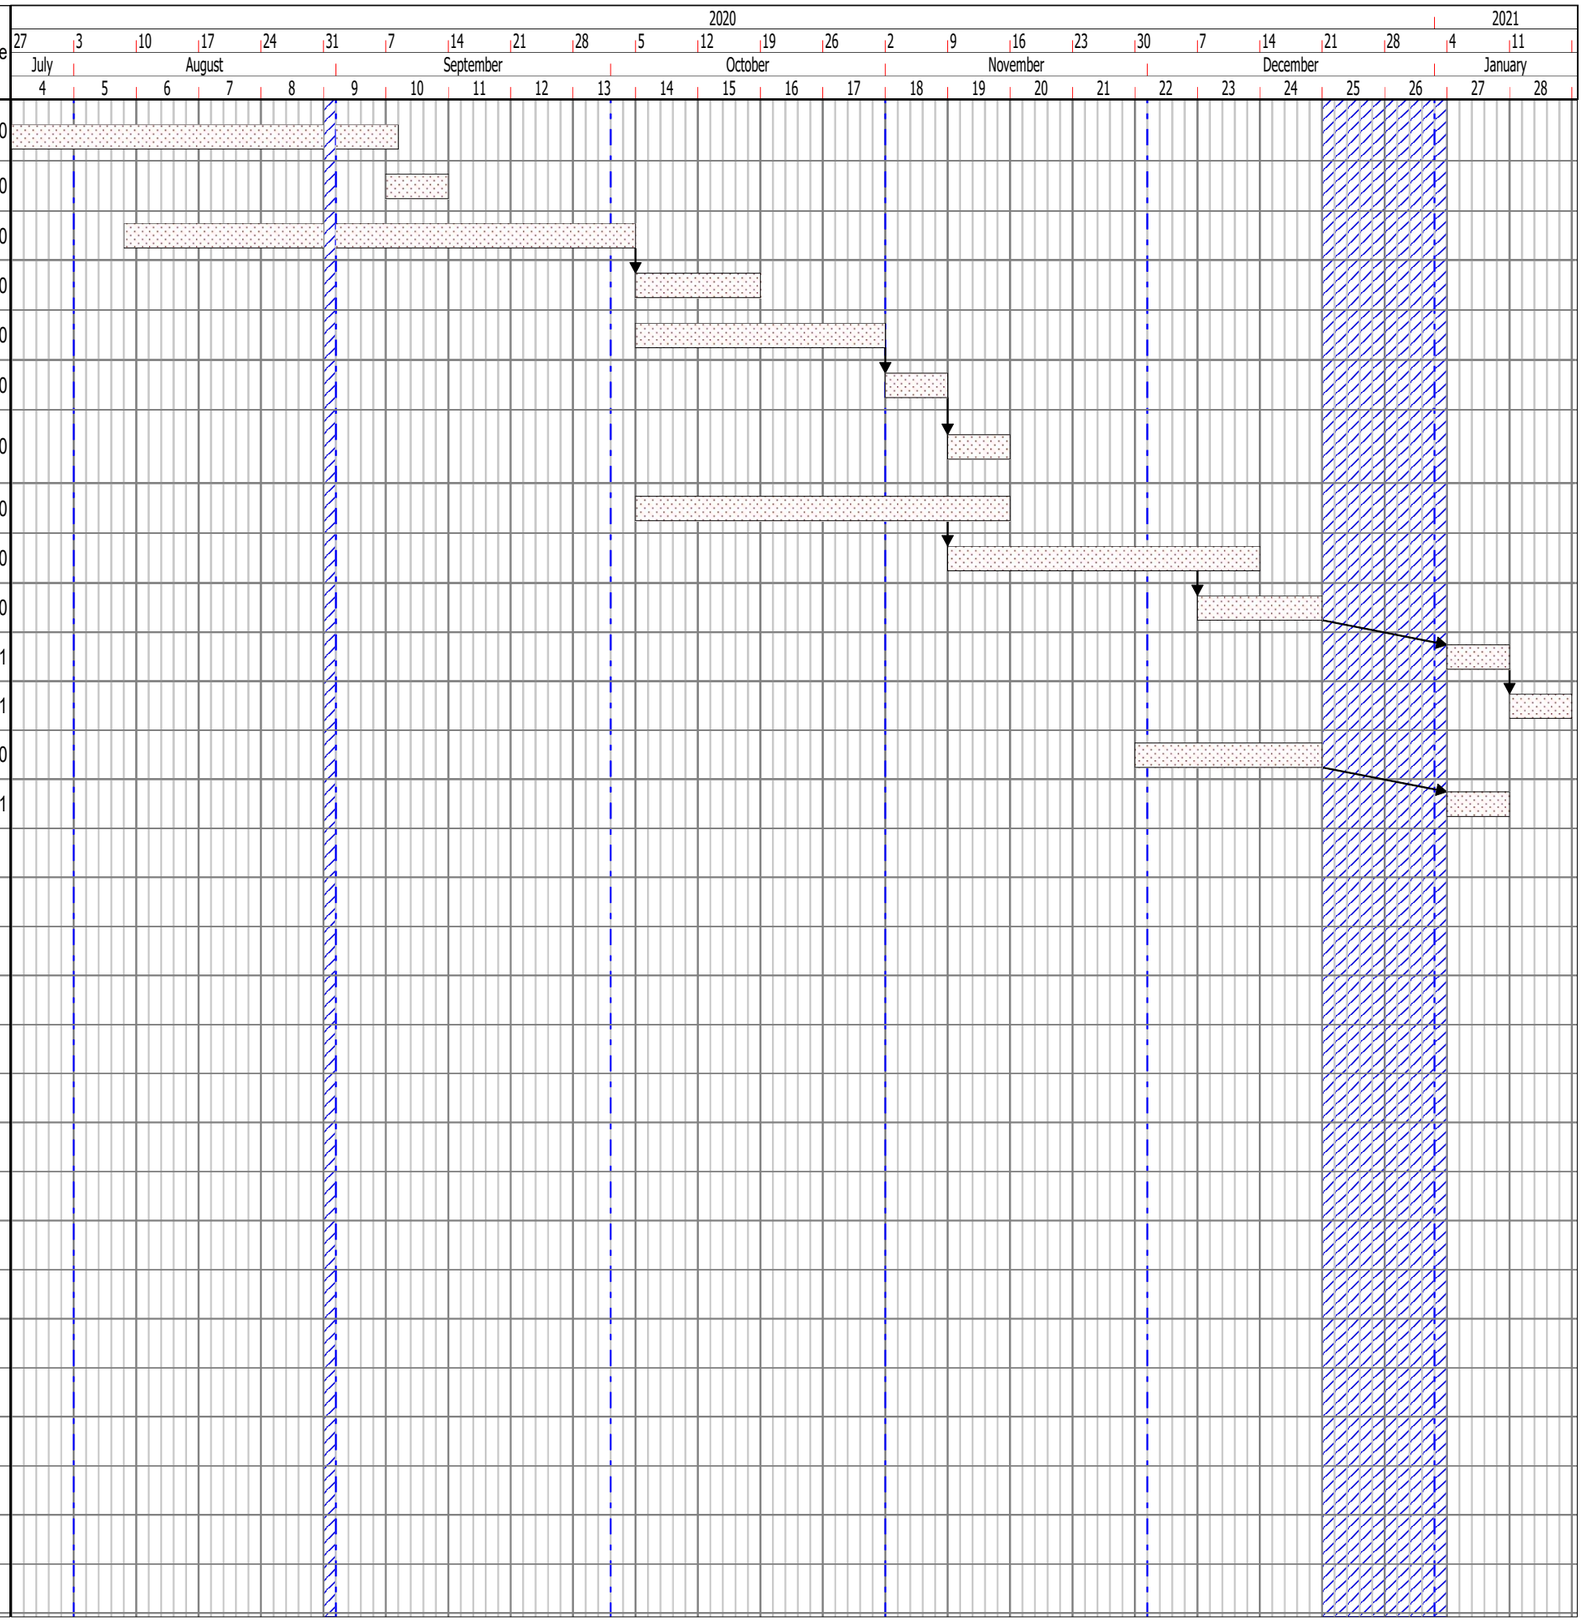

Planned by Asta Easyplan
