SITE SURVEY WAYFINDING

trueform

SD02	Sign reference	Minilith	Sign type
TT6593	TT Number	TfGM	Client
2200mm to crane	Lifting distance	Yorkstone flags	Reinstatement material
Metrolink Cables	Overhead obstructions?		Obstruction height
No	Decluttering required?	11/01/2019	Survey date
Standard chapter 8 (Footway parking)	Traffic management type	N/A	Traffic count
Standard barriers and access ramp for stairs	Pedestrian management	JT/CK	Surveyed By
Yes	Installation photos taken?	Yes	Obstruction photos taken?
Yes	TM Photos	Yes	Pedestrian management photos taken?

Installation notes

Access to site for the foundation installation is gained through Metrolink tram only road Corportation Street.
Access to site for the sign installation is via parking on the Northside of the Arndale Centre at the junction with Corporation Street and Withy Grove.. Standard chapter 8 traffic management vehicle parked on footway so no effect on traffic flow. Heavy duty utility access points close to installation point.
Standard pedestrian safety barriers around work area.
Very busy area with high number of pedestrians due to vicinity to Arndale centre and Exchange Square metrolink stop.
Liaison with Metrolink neccessary for work permit required, access and working near overhead cables
Liason with Arndale centre operators due to vicinity (will.smith@manchesterarndale.com)
New site reinstatement material is 900 x 600 Yorkstone flags and 400 x 400 hazard warning tactile paving charcoal

Site plan (not to scale)

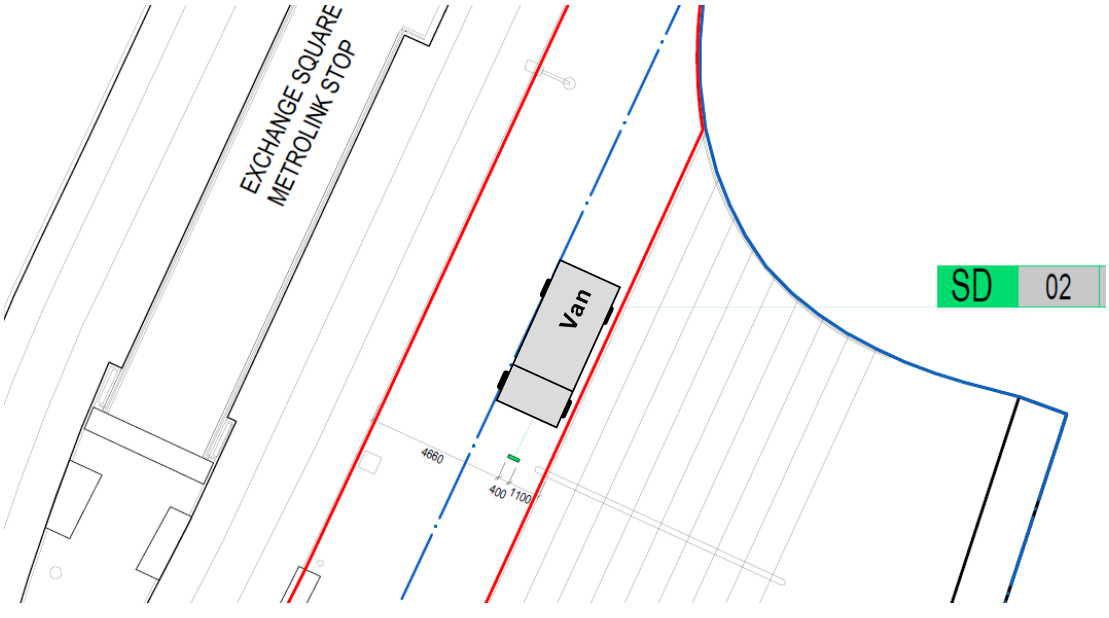

© Crown copyright and database rights 2017 OS 0100022610
