25/07/24	CASEY – BENMORE RD, BLACKLEY – 24CHE350	PLOTS 9-10

BETTS GEO
CONSULTING ENGINEERS

House Types: 2B4P Type 1 & 3
Construction Type: Pile and Ground Beam
Protection Anticipated: CS2

Floor Type	1. Precast beam and Insulation block with minimal service penetrations and passively ventilated sub floor void.
Installation Quality	2. Good level of workmanship in line with good practice to CQA.
Testing Regime 1	3. Independent validation of all plots by Betts Geo Environmental Ltd.
Membrane type	4. ITP Powerbase Multigas 500 https://itpltd.com/wp-content/uploads/Powerbase-Multigas-500-Data-Sheet-R5-4-1.pdf
Extent of Coverage	5. All
Underside of membrane	6. Onto beam and insulation block
Slab/membrane condition	7. Precast beam and insulation block with minimal service penetrations via sealed top hats. Membrane in V good condition.
Laps and joints	8. Very good – welded seams.
Damp-proof course	9. Yes.
ervice entries and seals	10. Good seals: Top-hats/taped
Cavity inspection (150mm void)	11. On plots 9-10 prior to membrane installation
Telescopic Air Vents	12. 16 x telescopic air vents installed. 0.9m to 1.8m centres

Plot has PASSED inspection.
(Any proposed remedial works will be noted in the 'Remarks' column on this form).

An additional inspection visit IS NOT required for this plot.
Qualified Engineer: Marc Fawcett

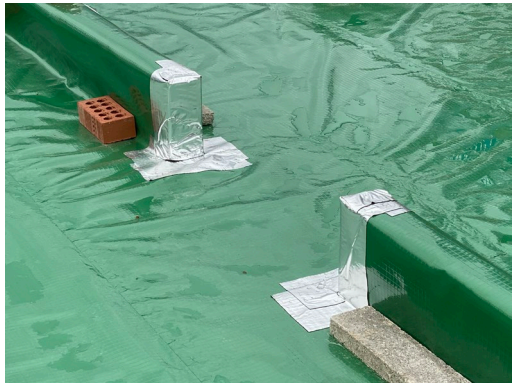

25/07/24	CASEY – BENMORE RD, BLACKLEY – 24CHE350	PLOTS 9-10

Sub Floor Void and Ventilation Details
