
Novus PPM 2021

WHITWORTH ART FINIALS

Details

Building	WHITWORTH ART FINIALS
Team	Adam Hayes, Ash Peake
Start Date	January 14, 2022
Completion Date	January 14, 2022
Comments	Finial 1: Ball seciton of final removed and some of the lower coping stone. The pillar is stable but has cracks all the way round Recommend removing 3 no coping stones and the two main top coping stones and re bedding. New finials and coping stones would need to be cast and made bespoke. This location can be accessed via tower scaffold Finial 2: Has several cracks around it, to both ball and base but is currently stable. Moss was removed from the cracks. Recommend monitoring and planned replacement in the future.
Management Approval	-

Defect Photos

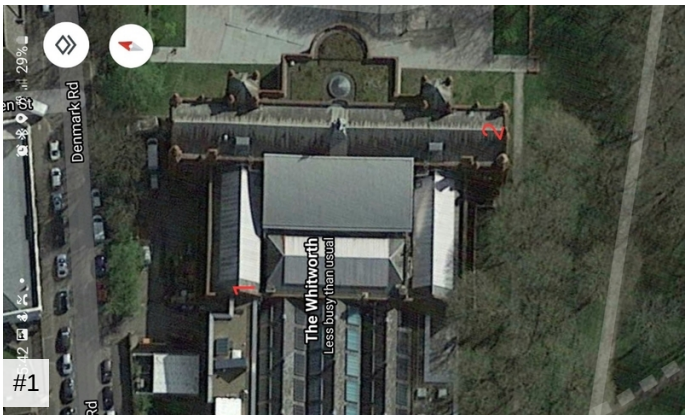

#1

Before Photos


Finial 1


Finial 1


Finial 1


Finial 1


Finial 1


Finial 1


Finial 1


Finial 2


Finial 2


Finial 2


Finial 2

After Photos


Finial 1


Finial 1


Finial 1


Finial 1



Finial 1



Finial 2



Finial 2



Finial 2
