Sunlight House - MCR

17/Jun/2024 | 09:41

Tester	Neil Dolan	Email	neil@inventivehomes.co.uk
Company	NCD Ltd t/as Anchor Pull Testing	Telephone	07787178750

Sunlight House Anchors

Category	Substrate	Fixing Type	Size	Manufacturer	Part Number	Component	Type
Fixing / Anchor / Construction Eyebolt	Various layers - see drawing	Mechanical	M12	Unknown			Proof Test

Task Results:

3 Tests	3 Passed	0 Failed


Mechanical 1 (Equipment: MAN6952 25kN, Calibration Expiry: 30/Jan/2025)

Time	Total Time	Target	Torque Achieved	Displacement	Reference	Result
30 secs	1m 56s	16kN	16.4 kN	0 mm	WOLES6EJ706IKU	Passed

Latitude: 53.478759765625

Longitude: -2.25003642673836

Test date: 01/01/0001 00:00:00

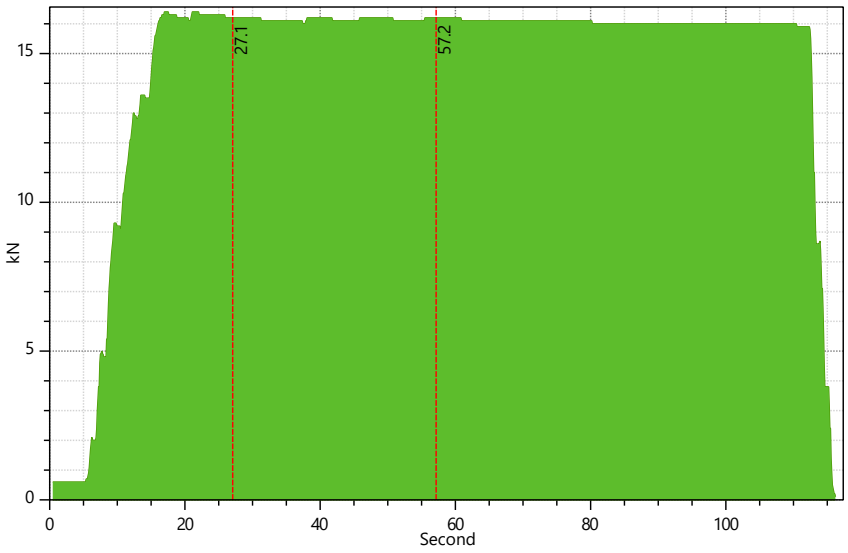

Load Over Time

Mechanical 1

Test Images:




Mechanical 2 (Equipment: MAN6952 25kN, Calibration Expiry: 30/Jan/2025)

Time	Total Time	Target	Torque Achieved	Displacement	Reference	Result
30 secs	1m 26s	16kN	16.8 kN	0 mm	ELB7KTQMAXGARS	Passed

Latitude: 53.4787292480469

Longitude: -2.25004378397926

Test date: 01/01/0001 00:00:00

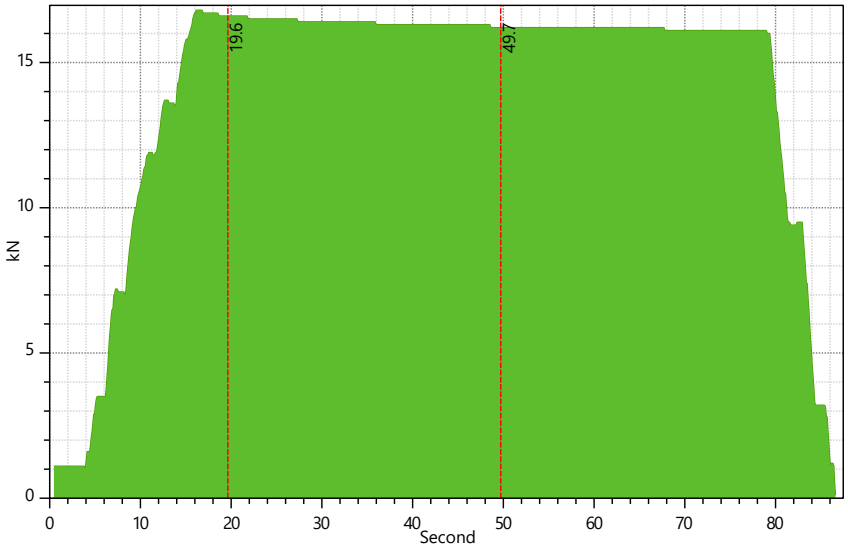

Load Over Time

Mechanical 2

Test Images:



Mechanical 3 (Equipment: MAN6952 25kN, Calibration Expiry: 30/Jan/2025)


Time	Total Time	Target	Torque Achieved	Displacement	Reference	Result
30 secs	1m 1s	16kN	16.8 kN	0 mm	OXWZCDNVY97BFA	Passed

Lowest fixing of 3

Latitude: 53.4788513183594

Longitude: -2.24995357473684

Test date: 01/01/0001 00:00:00

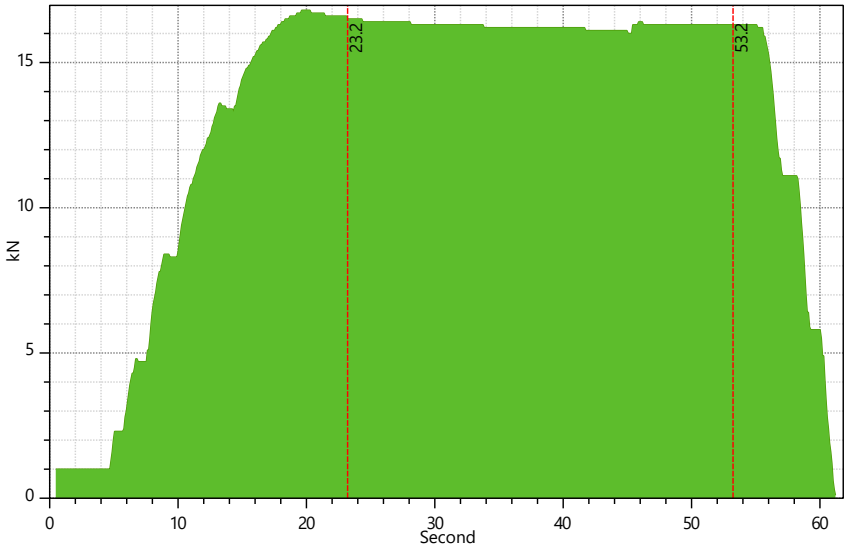

Load Over Time

Mechanical 3

Test Images:



Powered by Hydrajaws
