Project: Signage installation

Retail shop (KK Sports)

Location

Gorton Tesco's



Date of works: not decided yet

Description of activity

Signage installation

Site (Facia Outside the Shopping Centre)
Involves:
Description of sign mounting and materials
Composite grey cladding mounted on the frame level on the back then
Acrylic 3d illuminated letters with chrome returns standing off mounted on composite cladding
Background as designed.





Composite :



Led description:
3 DIFFUSION LENS LED MODULE
Made in Korea
Provided by Samsung
Brightness / illumination of the sign is maximum 150cd/msq and can be lowered using the dimmer switch.



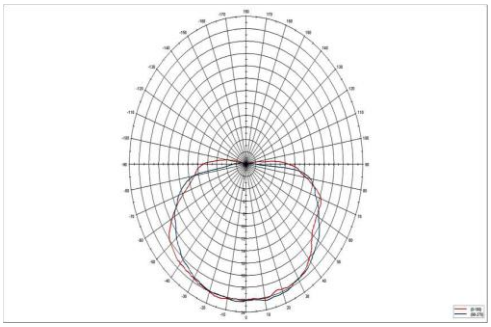





Requirement:
Access on-site required
220v ip67 rated electric supply to the sign.

Installation Hours

Installing new Shop exterior fit outs:

Supervision and personnel

- Mr Faheem Khan (07588883183) Head Team Lead
- Mr Moin Khan

Training

All operatives are adequately trained to carry out required tasks.

Legislation

- Health and Safety Work Act 1974
- The Management of Health and Safety at Work Regulations 2006
- Workplace (Health, Safety and Welfare) Regulations 1992
- The Control of Asbestos Regulations 2012
- Provision and Use of Work Equipment Regulations (PUWER) 1998
- Control of Substances Hazardous to Health Regulations 2002
- The Work at Height Regulations 2005
- The Personal Protective Equipment at Work Regulations 2002
- The Manual Handling Operations Regulations 1992
- The Construction (Design and Management) Regulations 2015
- Electricity at Work Regulations 1989
- The Pressure Systems Safety Regulations 2000
- Pressure Equipment Regulations 1999 (SI 1999/2001)

Working at height

When working at height, site operatives must ensure that the working area is cleared on a period basis to
ensure that there is continually a clear and safe working area to prevent slips trips and falls.
Manual handling

PPE requirements

- Hard hats
- Safety boots
- Hi-vis vest
- Safety gloves
- Safety glasses

Welfare

Welfare arrangements are supplied by the client or principal contractor.
These should be in line with Schedule 2 of the Construction Design & Management Regulations 2015
(CDM). All sites are to have a minimum amount of welfare facilities available for workers, which include the
Following:

- Toilets
- Washing facilities
- Drinking water
- Changing rooms and lockers
- Heating
- Rest facilities

First aid

Refer to the onsite safety notice board for all first aid information.

A first aid box with enough equipment to cope with the number of workers on site should be provided for by the client or principal contractor.

The client or principal contractor should nominate an appointed person to take care of first-aid arrangements.

The number of appointed first aiders shall be dependent on the number of employees.

Emergency procedures

The client or principal contractor will ensure that the existing site emergency procedures are followed and
that relevant information is given to operatives at time of induction or when changes are made to procedures.
