BURO HAPPOLD

Co-Op Live Arena

Verification Report – Part A (Groundworks)

BRA-BHE-XX-XX-RP-CG-0008

0042841

31 January 2024

Revision P07

Final


Copyright © 1976 - 2024 Buro Happold. All rights reserved

Revision	Description	Issued by	Date	Checked
P01	For information DRAFT	FG	March 2022	HM
P02	For information DRAFT	FG	April 2023	HM
P03	For information DRAFT (addressing comments)	FG	May 2023	HM
P04	For information DRAFT (inclusion of appendices)	JY	November 2023	GP
P05	For information DRAFT (inclusion of appendices)	JY	December 2023	GP
P06	Final	JY	December 2023	HM
P07	Final	JY	January 2024	HM

https://burohappold.sharepoint.com/sites/0042841projectbradford/05_Discipline Specific/09_Ground Engineering/F9 Ground Eng- Site Inv/03 Reports/Verification/BRA-BHE-XX-XX-RP-CG-0008 P07.docx

Report Disclaimer

This Report was prepared by Buro Happold Limited ("BH") for the sole benefit, use and information of BAM Construction Ltd for information. BH assumes no liability or responsibility for any reliance placed on this Report by any third party for any actions taken by any third party in reliance of the information contained herein. BH's responsibility regarding the contents of the Report shall be limited to the purpose for which the Report was produced and shall be subject to the express contract terms with BAM Construction Ltd . The Report shall not be construed as investment or financial advice. The findings of this Report are based on the available information as set out in this Report.

author	**Francesca Gould / James Young**
date	**31st January 2024**
approved	**Hugh Mallett**
Signature	

Copyright © 1976 - 2024 Buro Happold. All rights reserved

date **31st January 2024**

Copyright © 1976 - 2024 Buro Happold. All rights reserved

Contents

1 Introduction 5

2 Site context 7

3 Conceptual site model 12

4 Planned remediation actions 16

5 Verification Plan 18

6 Verification of groundworks 21

7 Conclusions 33

References 35

Appendix A Provectus Completion Report

Appendix B Provectus Landfill Permits

Appendix C Careys Waste Transfer Tickets (attenuation tank excavation)

Appendix D Groundwater and River Monitoring Records

Appendix E Trade Effluent Consent

Appendix F Concrete Class Certification

Appendix G Provectus Environmental Monitoring (RAMS)

Appendix H Borehole Decommissioning

Appendix I Ground Gas Membrane Sign Off Certification

Appendix J Membrane Testing Solutions Completion Report

Appendix K Buro Happold Periodic Inspection Records

Copyright © 1976 - 2024 Buro Happold. All rights reserved

1 Introduction

1.1 Report scope and objectives

This Verification Report (Part A – Groundworks) was prepared by Buro Happold on behalf of BAM Construction Ltd. It provides the evidence of successful implementation of the approved Remediation Strategy [1] relevant to the Co-op Live Arena. Its objectives are: (i) to describe the verification activities that have been carried out during the groundworks; (ii) present supporting information on the remedial measures undertaken to mitigate the risks identified in the previous investigations and; (iii) to describe the presence and remediation of any unforeseen contamination excavated during the groundworks. The report has been prepared in accordance with the Environment Agency Land Contamination Risk Management [2] and has taken into account the substantial programme of investigation and remediation carried out across the Site for the development. It also reflects the nature of the development (including excavation earthworks of areas yet to be completed by soft landscaping) all in the context of the approved Remediation Strategy [1]. In due course, a Part B – Landscaping verification report will be prepared upon completion of all imported topsoil within the soft landscaped areas and above ground planters.

1.2 Relevant planning conditions

The report has been prepared to address the requirements of Manchester City Council with respect to land affected by contamination set out planning condition 7b Planning Permission Ref. 126431/FO/2020 approved on the 23rd October 2020. Part of Condition 7 was discharged under application Ref. CDN/20/0767. In order to discharge Condition 7 in full, part (b) needs to be complied with. This requires a Completion/Verification Report to be submitted and approved in writing by the City Council as local planning authority, prior to the first use of the development. This report addresses this requirement. The conditions relevant to this Verification Report are presented below for ease of reference:

> *"**7) (a)** Notwithstanding the Geoenvironmental and Geotechnical Desk Study and gas calibration certificates stamped as received by the City Council, as Local Planning Authority, on the 30th March 2020 and 11th September 2020 respectively, prior to the commencement of development hereby approved, the following details shall be submitted for approval in writing by the City Council, as Local Planning Authority:*
>
> *- Submission of a remediation strategy.*
>
> *The development shall then be carried out in accordance with the approved remediation strategy.*
>
> ***(b)** A Completion/Verification Report shall be submitted to and approved in writing by the City Council as local planning authority, prior to the first use of the development.*
>
> *In the event that ground contamination, groundwater contamination and/or ground gas, not previously identified, are found to be present on the site at any time before the development is occupied, then associated works shall cease and/or the development shall not be occupied until, a report outlining what measures, if any, are required to remediate the land (the Revised Remediation Strategy) is submitted to and approved in writing by the City Council as local planning authority and the development shall be carried out in accordance with the Revised Remediation Strategy, which shall take precedence over any Remediation Strategy or earlier Revised Remediation Strategy.*
>
> *Reason - To ensure that the presence of or the potential for any contaminated land and/or groundwater is detected and appropriate remedial action is taken in the interests of public safety, pursuant to policies DM1 and EN18 of the Manchester Core Strategy (2012).*

Copyright © 1976 - 2024 Buro Happold. All rights reserved

Planning Condition 9 addressed verification of the mine works and was formally discharged by the local authority on 28th May 2021, refer to Decision Notice CDN/21/0281.

In order to enable the discharge of Condition 7 (b) this Verification Report demonstrates how the risks from contamination have been mitigated by the implementation of the approved Remediation Strategy [1].

1.3 Responsibilities of parties involved

The parties with responsibility for various elements of the verification activities are summarised below.

Name	Role	Description of activities	Contact information
BAM Construction Ltd	Principal Contractor	Contractor for the development construction	Metro, 2nd Floor, 33 Trafford Road, Exchange Quay 2, Salford, M5 3NN 0161 877 9274
Turner and Townsend	Cost Consultant / Project Managers	Overall responsibility for all activities related to the redevelopment	6th Floor. 55 Springs, Manchester, M2 2BY 0161 237 7750
Buro Happold Engineering Ltd	Consultant	Preparation of the Verification Report	230 Lower Bristol Road, Bath, BA2 3DQ 0122 532 0600
Provectus Remediation Ltd	Sub-contractor	Bulk earthworks contractor	Regent House, Bath Avenue, Wolverhampton, WV1 4EG 0190 281 0084.
Cementation Skanska Ltd	Sub-contractor	Grouting and piling works	Maple Cross House, Denham Way, Maple Cross, Hertfordshire, WD3 9SW
Careys Civil Engineering Ltd	Sub-contractor	Substructure contractor	Carey House, Great Central Way, Wembley, Middlesex, HA9 0HR
GCP Applied Technologies (UK) Ltd	Specialist	Supplier of ground gas and waterproofing systems (Product: Preprufe)	487-488 Ipswich Rd, Slough, SL1 4EP
Membrane Testing Solutions (MTS)	Specialist	Independent verifier of ground gas membrane and waterproofing	Parsonage House, Parsonage Street, Halstead, Essex, CO9 2JR

Copyright © 1976 - 2024 Buro Happold. All rights reserved

2 Site context

2.1 General

This Chapter presents a brief summary of the site context and conditions, consideration of which enabled the definition of the remediation scheme. This summary has been prepared from source information prepared by Buro Happold [3], [4] and [5]. It is recommended that appropriate reference is made to these reports for more detail.

2.2 Site setting

The site is located to the north east of Manchester City Centre, within the Etihad Campus. It occupies approximately 4.5 hectares, centred on National Grid Reference SJ 86841, 98878. It is currently used as an over-spill surface level car park for those attending events associated with the Etihad Stadium. The perimeter of the site is populated with informal, dense shrubbery and trees and secured with tall mesh fence. Ashton Canal is located along the southern boundary and the River Medlock is located within a culvert to the north west. There are no existing buildings on the site.

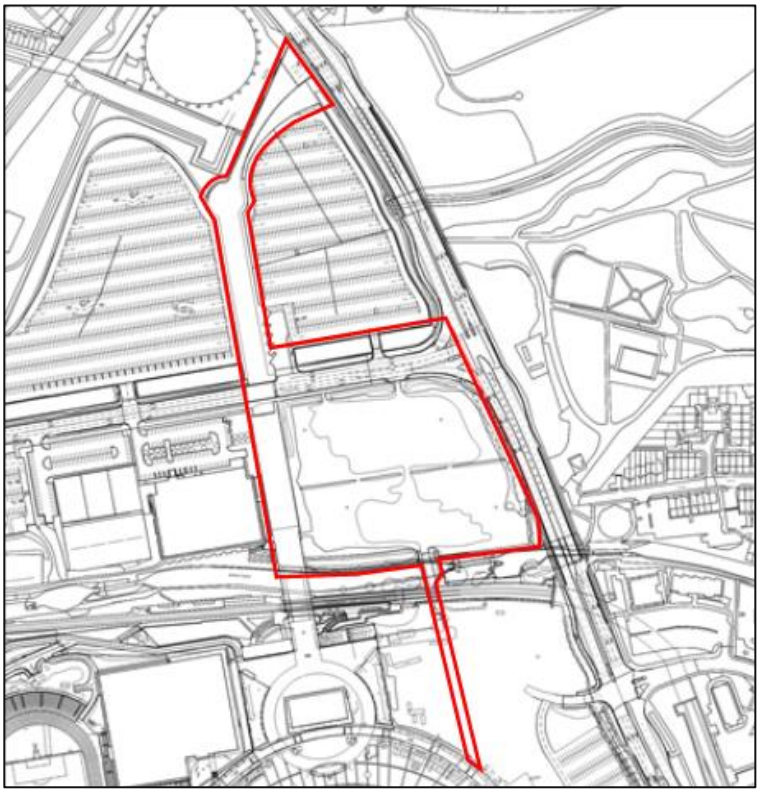


Figure 2-1 Red line boundary

2.3 History

Until the mid-1800s, the site and surrounding area was occupied by agricultural land with the River Medlock meandering through the north-west corner of the site. The Ashton canal and lock formed the southern boundary and Mill Lane the east. Victoria Gardens were located to the north and in part occupied the north of the site. By 1848, the River Medlock

Copyright © 1976 - 2024 Buro Happold. All rights reserved

had been straightened and diverted further north, away from the site. Industrial works began to occupy the land south of the Canal during the early 1890s and residential development occupied the eastern part of the site.

During the early 1900s the River Medlock was culverted, Forge Lane was constructed running north/south centrally through the site and other residential roads connected onto Forge Lane from the east. The largest change at this time was the development of Bradford Road Gas Works, which included tanks, gas holders, tramways and large buildings (some within the site boundary). By the early 1930s, there was further development to these gas works on site and further development to the industrial works to the south, beyond the Canal. There were no further significant changes to the site and its surroundings until late 1970s when the majority of these works were cleared, including buildings associated with Bradford Road Gas Works. Between the late 1980s and late 1990s there were changes to the land use east of Forge Lane within the site boundary and by 1995 Mill Lane developed into Alan Turing Way. By 2002, construction of the Etihad Stadium (formally Manchester Stadium) to the south was underway and road layouts in the surrounding area developed. A temporary BMX track occupied the site in 2009 and by 2010 the site was cleared.

2.4 Geology, hydrogeology and hydrology

2.4.1 Geology

The published 1:50,000 and 1:10,000 geological maps [6], [7], [8] together with historical and recent ground investigation information indicate the geology to be the Pennine Upper Coal Measures of the Upper Carboniferous, overlain by Quaternary deposits. The map shows the site to be underlain by the following:

- Made Ground
- Alluvium and River Terrace Deposits (north-western area) – Soft grey clay and unconsolidated orange-brown clayey sands and gravels.
- Glacial Till – Firm becoming very stiff reddish-brown clay and silty clay with gravels and pebbles.
- Pennine Upper and Middle Coal Measures – Mudstones, siltstones and sandstones with beds of coal, fireclay and ironstone within the upper parts.

Due to the nature of the site history and the current site uses, and as shown on the mapping, the natural strata are overlain by variable thicknesses of Made Ground, which is locally extensive (up to 17mbgl). Incorporated within this Made Ground are many large below ground obstructions (reinforced concrete blocks) as well as hard strata (which when machine excavated during the site investigation was too hard to penetrate), for more detail refer to Constraints Plan (drawing No. BRA-BHE-XX-XX-DR-GE-0101). Much of the ground surface across the site is gravel and grass cover.

Coal seams are known to sub-crop across the site and there are two mine shafts located beneath the area proposed for development, details of these can be found within the Coal Mining Risk Assessment [5]. To summarise, known coal seams include the Bradford Four Foot, Bradford Three Quarter and Charlotte Mine (Thin B and C). A further seam sub-crops to the north east, up dip of the site, and is present beneath the site at depth due to the dip orientation of the seam (all seams generally dip south-west). The maps indicate that the strata dips between 20° (inclined strata measured underground) and 25° (inclined strata) SW. Cross sections have been produced to detail the ground profile, these have been modified slightly since the production of the interpretative report [4] and have been included within the Drawings section at the back of this report (drawing No. BRA-BHE-XX-XX-DR-GE-0201 to 0203).

Copyright © 1976 - 2024 Buro Happold. All rights reserved

Table 2-1 Encountered geological strata across the site from the ground investigation information

Name	Description	Top of Strata *(average)*		Thickness *(average)* (m)
		m bgl	m OD	
Made Ground	Soft to firm brown black sandy gravelly CLAY. Locally sandy clayey GRAVEL and occasionally fine to coarse SAND. Constituents include ash, coal, clinker, brick, sandstone, limestone, pottery, concrete, rootlets, wood, plastic, rebar.	0 *(0)*	60.8 – 56.9 *(59.1)*	1.3 – 17.2 *(8.1)*
Alluvium	Soft to firm orangish brown slightly gravelly sand CLAY	7.4 – 12.6 *(9.8)*	52.8 – 44.8 *(49.0)*	0.3 – 2.0 *(1.3)*
River Terrace Gravels	Medium dense to very dense orangish brown slightly gravelly to gravelly clayey fine to coarse SAND	9.0 – 13.9 *(10.8)*	51.4 – 43.5 *(48.4)*	0.6 – 3.0 *(1.7)*
Glacial Till	Soft to very stiff brown gravelly CLAY	1.3 – 14.5 *(7.8)*	59.2 – 42.9 *(51.6)*	0.9 – 12.0 *(5.6)*
Coal Measures (interbedded layers of predominantly mudstone, with sandstone, siltstone and coal)	Very weak to weak grey MUDSTONE with locally thin to thickly laminations of light grey siltstone and/or fine grained sandstone Discontinuities are extremely closely to closely spaced planar smooth or undulating rough clean locally polished or clay smeared. SEATEARTH generally found below coal seams and consists of extremely weak grey MUDSTONE with gravel-sized fragments of black organic matter/fossilised plant remains and gravel-sized ironstone nodules. Very weak to moderately weak light grey fine to medium grained SANDSTONE with localised thin laminations of mudstone and/or siltstone. Discontinuities are extremely closely to medium spaced undulating rough clean. Very weak to weak grey SILTSTONE with localised thin to thick laminations of mudstone and/or sandstone. Discontinuities are very closely to medium spaced planar smooth or undulating rough clean or stained. Very weak black COAL.	11.5 – 18.0 *(13.8)*	48.5 – 39.9 *(45.0)*	Base not proven

2.4.2 Hydrogeology

The superficial deposits have been classified as a Secondary (undifferentiated) Aquifer. In general, these layers have previously been designated as both minor and non-aquifer in different locations due to the variable characteristics of the rock type. In this instance reflective of the variable nature of the Glacial Till. The Coal Measures are classified as Secondary (A) Aquifer, defined as permeable layers capable of supporting water supplies at a local rather than strategic scale and in some cases forming an important source of base flow to rivers. There are five active groundwater abstraction located within 1km of the site. However, the site is not within a groundwater source protection zone. The abstractions are relating to the following:

- Borehole at Norton Street, Miles Platting, Manchester (611m north)
- Two boreholes at Openshaw, West Ashton, Manchester (971m south-east).

Copyright © 1976 - 2024 Buro Happold. All rights reserved

2.4.3 Hydrology

Ashton Canal is located along the southern boundary of the site (8m south). The canal climbs for 10.8km through 18 locks toward Ashton-under-Lyne. Lock No.9 is located adjacent to the site resulting in approximately 3.5m ground level change. According to the topographical survey the east side of Lock No. 9 (SE of the site) is at approximately +60.4mOD and west of the lock (SW of the site) the ground drops to +56.7mOD. a steep embankment up to the site is present on the west side with the site at approximately +59.0mOD.

The River Medlock is located approximately 40m to the north of the site and flows south and west toward the River Irwell in Manchester city centre. The course of the River Medlock meandered through the north-western part of the site during the late 1840s. By the early 1890s it had been diverted away from the main site area and straightened. By 1905, the River was contained within a 500m-long culvert below the former Bradford Road Gas Works, north of the main site area, see Figure 2-2 for the approximate position.

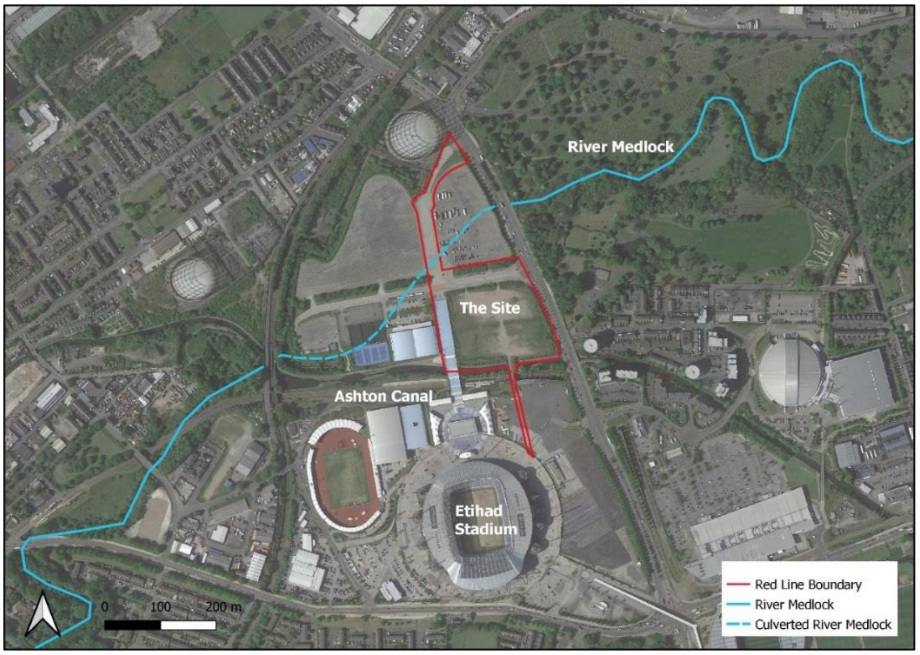


Figure 2-2 Location of River Medlock with approximate alignment of culvert

2.5 Summary of ground investigations

The most recent phase of ground investigation was carried out by Provectus Remediation Ltd in February 2020 [9]. Provectus are the remediation contractor and completed trial pitting across the site in order to determine the waste characteristics of the material down to final excavation level of approximately +55.0mOD. The findings of this investigation together with the Buro Happold Remediation Strategy informed their Remediation Strategy Implementation Plan [10].

A previous phase of investigation was designed by Buro Happold and undertaken by Structural Soils between September and October 2019 with post fieldwork ground gas and groundwater monitoring completed by December 2019. An earlier ground investigation had been carried out by May Gurney in 2010 and other intrusive works (grouting and some remediation) undertaken by BWB in 2011. All this information has been summarised and where appropriate included within the assessment summarised within the Buro Happold Interpretative Report [4].

Copyright © 1976 - 2024 Buro Happold. All rights reserved

Following the ground investigation work in 2019 by Structural Soils, grouting was proposed across the Site in order to facilitate construction of the Arena. Buro Happold prepared engaged with the Environment Agency and prepared a Grouting Works: Groundwater Risk Assessment [11] which set out the requirements for undertaking grouting activities below the water table across the Site. Cementation Skanska Ltd prepared a Grouting Philosophy that incorporated the requirements of the Buro Happold Groundwater Risk Assessment. Further information regarding this work is presented in Section 6.4. A completion report and method statements were issued to City Council on 7th April 2021 (CDN/21/0281) in order to address and discharge Condition 9 (b) and approved on the 28th May 2021.

Copyright © 1976 - 2024 Buro Happold. All rights reserved

3 Conceptual site model

3.1 Residual contamination

The various ground investigations referred to above recorded evidence of contamination and obstructions in the form of, reinforced concrete blocks and boulders as well as ash, slag, hydrocarbon odours, oil on groundwater and evolution of gases. Perched groundwater was encountered in the Made Ground. The assessment of the Made Ground and underlying natural strata was facilitated by sub-division of the Site into different zones based on previous remediation work and historical uses. These zones are shown in Figure 3-1 and summarised as follows:

- Zone 1 Ground Level – 2.0mBGL (site-wide)
- Zone 2 Over 2.0m BGL West (formerly Bradford Gas Works)
- Zone 3 Over 2.0m BGL East (formerly residential use)
- Zone 4 Natural strata (site-wide)

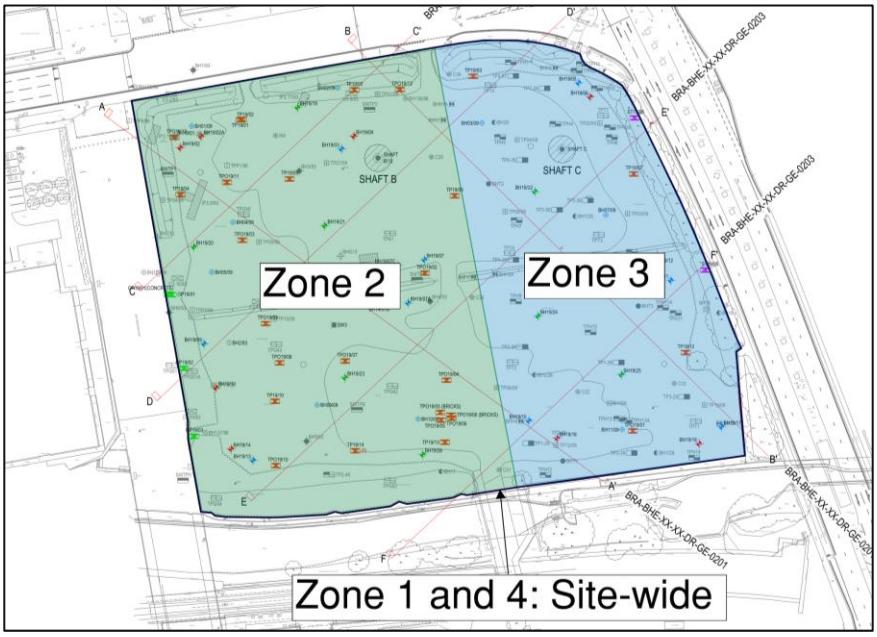


Figure 3-1 Assessment zone plan

Zone 1 - A total of 48 samples were analysed within this zone (shallow Made Ground across entire site, <2.0m bgl). All samples recorded concentrations of all inorganic and organic determinands below the relevant commercial criteria. All samples were screened for asbestos, four different samples and three separate locations identified asbestos. Three of the samples included concentrations below the hazardous threshold. One sample, TP19/01 at 2.0m bgl included a concentration of 3.62%, above the hazardous threshold (0.1%).

Zone 2 – A total of 36 samples were analysed within this zone (west of the site >2.0m bgl). All samples recorded concentrations of all inorganic and organic determinands below the relevant commercial criteria. All samples were screened for asbestos, four samples at three separate locations identified asbestos. Two samples recorded concentrations below the limit of quantification and the other two samples were marginally above the limit for quantification but well below the hazardous threshold (0.1%).

Copyright © 1976 - 2024 Buro Happold. All rights reserved

Zone 3 – A total of 17 samples were analysed within this zone (east of the site >2.0m bgl). All samples recorded concentrations of all inorganic and organic determinands below the relevant commercial thresholds. All samples were screened for asbestos, no asbestos containing material was detected.

Zone 4 – A total of 7 samples were analysed within this zone, the natural strata beneath the Made Ground. All samples recorded concentrations of all inorganic and organic determinands below the relevant commercial criteria.

The potential risks to health were assessed as Moderate to Moderate/Low for construction workers, future site users, and occupiers/users of neighbouring land, based on the potential for direct contact with, ingestion and/or dust inhalation of Made Ground.

3.1.1 Phytotoxicity

All soil samples were compared to relevant phytotoxic thresholds for copper, nickel and zinc. Elevated concentrations of zinc and copper were recorded however the calculated US95 was well below the threshold. The risk to flora has been assessed as Very Low on the basis that a suitable thickness of clean imported material will be used for horticultural purposes.

3.1.2 Below ground infrastructure

The data within the shallow Made Ground was assessed against particular organic determinands, which when elevated, have the potential to permeate plastic pipes and taint water supply. The assessment indicates that polyethylene (PE), poly-vinyl chloride (PVC) and copper pipes may not be appropriate for potable water supply within the Made Ground due to the elevated concentrations of TPHs and total SVOCs. Where Made Ground remains in-situ and the pipes are laid within that Made Ground, barrier pipe materials are likely to be required unless otherwise agreed with the utility company. The risk to below ground infrastructure has been assessed as Low based on the use of clean fill for all below ground service trenches.

3.1.3 Groundwater

Perched groundwater was recorded within the Made Ground. A total of 12 samples were taken from the perched water table and assessed against Water Supply Regulations, Environmental Quality Standards and World Health Organisations Drinking Water Standards. The analytical test results show elevated concentrations of some heavy metals and heavy end TPHs within the perched water table.

A total of four samples were taken from the groundwater within the Coal Measures (Secondary A Aquifer). The analytical test results show elevated concentrations of some heavy metals and heavy end TPHs. The Secondary A Aquifer within the coal measures has not been considered as a sensitive receptor with respect to the assessment of risk at this location but does have the potential to be a pathway. It is not considered a sensitive receptor as its quality of the aquifer has already been degraded due to the mining history, the nature of the Coal Measures aquifer and the absence of local abstractions. The risk assessment from the interpretative report [4] assesses the risk to the culverted River Medlock via migration through permeable strata (i.e. through the Coal Measures Secondary A Aquifer) as Low.

Grout works were carried out across the Site with the intention to fill voids associated with the mining legacy, this work was carried out by Cementation Skanska and a Completion Report prepared thereafter [12]. Accordingly, a Groundwater Risk Assessment in association with the grout works was prepared by Buro Happold [11], this should be read in conjunction with the Remediation Strategy [1].

Copyright © 1976 - 2024 Buro Happold. All rights reserved

3.1.4 Ground gas

Ground gas monitoring was undertaken on a total of 11 locations on six different monitoring occasions following the site investigation. The monitoring data is generally consistent with the nature and extent of the source (Made Ground). The Made Ground is typically about 9m thick (varies from 1.3m to 17.2m) [thicker in the north and west of the site]. This residual Made Ground typically contained organic material including hydrocarbons, coal and rare visual sightings of oily sheen on the perched water in the monitoring installations. The maximum concentrations of methane were recorded at 8.2%, 10.1% and 10.9%, all other recorded concentrations within these installations were also elevated above the guideline threshold (1%). The maximum concentrations of carbon dioxide (in installations with elevated concentrations) were typically in the range of 1 to 8.9% with concentrations above 2.5% recorded in 4 of the 11 installations on at least one occasion. Three installations recorded concentrations of carbon dioxide elevated above 5%.

The calculated Q_{hg} for CO_2 and CH_4 (concentrations x flow rate) fall within the values for Characteristic Situation 1. However, in accordance with CIRIA C665 [13] it is recommended the Characteristic Situation is increased to Characteristic Situation 2 due to the multiple elevated concentrations of CH_4 and $C0_2$ above the typical maximum value for CS1 (1% and 5%, respectively) and the depleted oxygen concentrations (<16%). Under the worst case scenario gas flow rates only need to increase to 0.7l/hr with the methane concentration recorded for a classification of CS2 to be assigned. Such a variation in flow though not recorded is feasible and therefore it is considered appropriate for the site to be considered CS2.

3.2 Provectus waste characterisation

Following the ground investigation in 2019, Provectus carried out a trial pitting exercise to further determine the waste characteristics across the site [9]. A total of 48 trial pits were excavated down to the final excavation level of +55.0mOD, shown below in Figure 3-2.

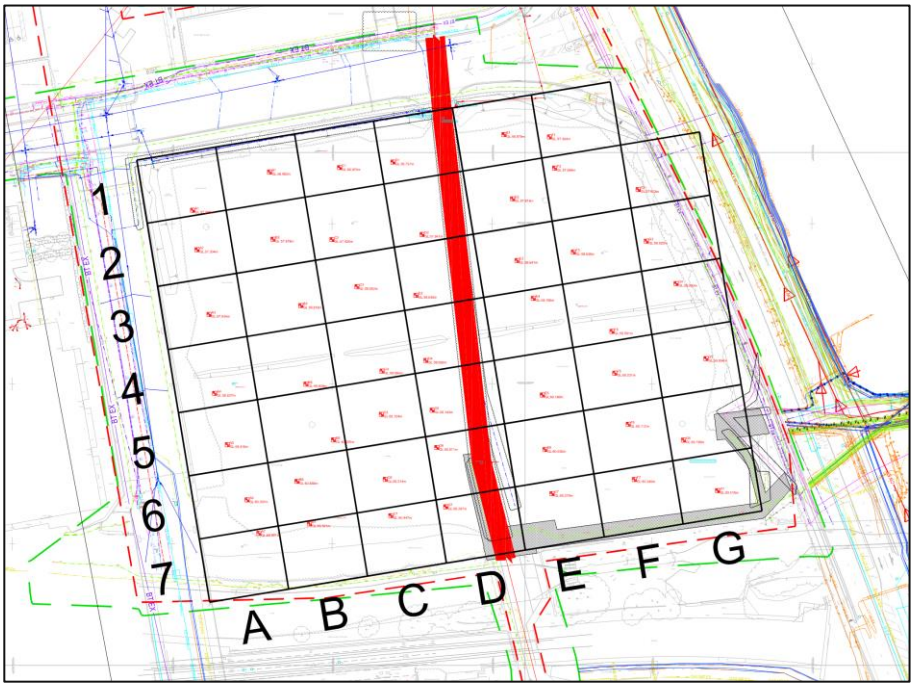


Figure 3-2 Trial pit locations from Provectus site investigation

Copyright © 1976 - 2024 Buro Happold. All rights reserved

This further investigation found the most likely hazardous substance across the site was associated with the coal tar derived hydrocarbons due to historical site use as Bradford Road Gas Works and associated coal carbonisation. The following summary has been derived from the report:

- Non-Hazardous Waste found within 117 sample locations (55%), equivalent of 58,500m3
- Non-Hazardous soil with LOI >10% found within 66 sample locations (31%), equivalent of 33,000m3
- Hazardous Waste found within 25 sample locations (12%), equivalent of 12,500m3
- Hazardous Waste with LOI >10% found within 4 sample locations (2%), equivalent of 2,000m3

3.3 Summary of pollutant linkages

The pollutant linkages (assuming no mitigation measures) listed below are relevant to; the short term (during enabling works, earthworks and construction), or to the long term (during operation as an arena and public open space).

Short term – during enabling works, earthworks and construction

1. Construction workers potentially exposed to on-site contaminants within the soils and groundwater. The assessed risk is **Moderate**.
2. Construction workers potentially exposed to hazardous ground gases within confined spaces. The assessed risk is **Moderate / Low**.
3. Occupiers / users of neighbouring land potentially exposed to dusts. The assessed risk is **Moderate / Low**.
4. There is a **Moderate** risk with regards to potential UXO at the site and combustion of the coal measures during piling works.
5. The River Medlock (in culvert) potentially exposed to migrating on site contaminants within the soils and groundwater. The assessed risk is Low.
6. Ashton Canal potentially exposed to contaminated surface water run-off. The assessed risk is Low.

Long-term – during operation

7. Future site users and occupiers / users of neighbouring land potentially exposed to hazardous ground gases within confined spaces. The assessed risks are **Moderate** and **Moderate / Low** respectively.
1. Future site users potentially exposed to contamination in soils within soft landscaped areas. The assessed risk is **Moderate / Low.**
2. Built environment (below ground infrastructure including foundations) potentially in direct contact with hazardous/ aggressive ground conditions. The assessed risk is Low.
8. Site flora potentially exposed to phytotoxic contamination via root up-take from soils in landscaped areas. The assessed risk is Low.

Copyright © 1976 - 2024 Buro Happold. All rights reserved

4 Planned remediation actions

4.1 Remedial objectives

The remedial objectives for the site addressed all of the significant pollutant linkages (see Section 3.3). The onjectives were defined in three categories; (i) contamination related, (ii) engineering related and (iii) management/ amenity related. These objectives can be found in detail within the Remediation Strategy [1] but have been set out in turn below for ease of reference, with a summary of the Remediation Strategy set out in Table 4-1.

4.1.1 Contamination Related Objectives

The contaminated related objectives are:

1. To ensure workers engaged in enabling works and construction of the proposed development are not exposed to concentrations of contamination in the solid, liquid or gaseous/vapour phase at concentrations that could give rise to acute risks;
2. To ensure occupiers / users of neighbouring land are not exposed to concentrations of contamination in dusts at concentration that could give rise to acute risks;
3. To ensure future site users and visitors are not exposed to concentrations of contamination that could give rise to acute or chronic risks;
4. To ensure the quality of surface waters (Ashton Canal and River Medlock) are not significantly impacted by any potentially mobile inorganic or organic contaminants in both the short and long terms;
5. To ensure soils in areas of soft landscaping meet appropriate physical and chemical criteria to enable health / growth of on-site plants; and
6. To ensure that the redeveloped site cannot be determined as 'Contaminated Land'.

4.1.2 Engineering Related Objectives

The engineering related objectives are:

1. To ensure the landform reduces rainwater infiltration and manages run off etc. in the long term and that run-off is also controlled during construction,
2. To ensure that the retaining structures on the site retain their integrity into the longer term,
3. To ensure that buildings and above ground infrastructure is protected against possible ingress and accumulation of hazardous gases and vapours;
4. To ensure that any below ground infrastructure and services are designed taking the residual contamination profile into account.

4.1.3 Management and Amenity Related Objectives

The management and amenity related objectives are:

1. To deliver the proposed development to time and budget;
2. To enable discharge of the relevant planning condition(s);
3. To minimise environmental impacts and ensure that 'nuisance' effects to occupiers / users of neighbouring land are mitigated to acceptably low; and
4. To ensure the remedial works undertaken are cost effective.

Copyright © 1976 - 2024 Buro Happold. All rights reserved

Table 4-1 Summary of remediation strategy

Receptor	Source	Pathways	Mitigation
Construction Workers	1) Contaminants within the Made Ground 2) Unexploded ordnance	Direct contact / inhalation of contaminated dusts	Awareness raising. Provision and use of standard PPE. Good standard H&S and hygiene. Good construction practice as set out in the CEMP [14] and Remediation Strategy Implementation Plan [10]. UXO briefing
	1) Hazardous ground gas 2) Contaminants in the Made Ground (ACMs)	Asphyxiation / inhalation of gas, vapour and / or dusts	Awareness raising. Provision and use standard PPE. Good standard H&S and hygiene. Availability of specialist PPE (i.e. vapour masks). Good construction practice as set out in the CEMP [14] and Remediation Strategy Implementation Plan [10]
Occupiers and users of neighbouring land	1) Hazardous ground gas 2) Contaminants in the Made Ground (ACMs)	Asphyxiation / inhalation of gas, vapour and / or dusts	Good construction practice as set out in the CEMP [14] and Remediation Strategy Implementation Plan [10] . Implementation of suitable ventilation surrounding the site (i.e. soft landscaped areas).
Future site users	Imported soils	Direct contact	Clean suitable topsoils imported to comply with relevant British Standard [15] and criteria set out within the Remediation Strategy [1].
	Hazardous ground gas	Asphyxiation / inhalation of gas	Ground gas protection measures (incorporated in the waterproof concrete basement construction) that accord with the relevant British Standard [16].
Controlled Waters (Ashton Canal and River Medlock)	Contaminants in the groundwater and Made Ground.	Migration via permeable strata and / or implemented pathways (e.g. surface water run off, piling etc.)	Restricting areas of open excavation at any one time to reduce potential for infiltration. Removal of source material (any gross contamination encountered as part of the excavation reducing potential of future leaching of contamination from impacted soils to shallow groundwater. Prevention of uncontrolled run-off during earthworks, including an appropriate cut-off / barrier in the vicinity of the canal, bund as necessary. Good construction practice as set out in the CEMP [14].
Built environment	Contaminants within Made ground	Direct contact	Appropriate design of below ground concrete and water supply pipework in accordance with the relevant BRE guidance [17], the Water UK guidance [18], and requirements of the water utility provider [19].
Ecology	Contaminants within the Made Ground	Direct contact	Isolation of flora within planters, away from the Made Ground. In areas of soft landscaping, an appropriate thickness of clean imported subsoil/topsoil to act as a cap to the underlying Made Ground, criteria set out within the Remediation Strategy [1].

Copyright © 1976 - 2024 Buro Happold. All rights reserved

5 Verification Plan

5.1 General

The overall objective of the planned verification was to demonstrate that the remedial works were carried out in accordance with the agreed Strategy [1] and that the works have not given rise to any unacceptable impacts upon people or the environment. The verification activities will provide evidence that:

- Planning/permit/licence conditions have been met; and
- Environmental management goals have been met.

The planned verification activities are described below.

5.2 Construction workforce – health, safety and hygiene regime

The Principal Contractor's (BAM Construction Ltd) health and safety plan will be reviewed and its implementation recorded by site staff (Contractor and Project Manager) and periodic inspection by Buro Happold. It is anticipated that the visits will be undertaken at approximate 2 week intervals during the main earthworks. There is also a provision for immediate attendance by Buro Happold if unforeseen hazards associated with land affected by contamination that could give rise to particular risks to health and safety of the workforce are encountered (e.g. unusual vapours, gross visual contamination etc.).

5.3 Earthworks

5.3.1 Excavated soils

Substantial volumes of Made Ground arising will be derived from the levelling of the site. There is limited opportunity for the re-use of such materials on site and it is anticipated that the majority of the arisings will be subject to off-site treatment and / or disposal at an appropriate facility. This will be managed by the remediation contractor, Provectus.

In the event that any Made Ground spoil is re-used on site, records of suitability will be obtained and reported. Sampling of such soils will be carried out at a frequency of 1 sample per 250m^3. Physical testing will be carried out to demonstrate geotechnical suitability as required. Chemical analysis will be carried out by an appropriate specialist laboratory (with MCERTS/UKAS accreditation for relevant determinants). The chemical analytical suite will be designed to reflect the contaminants of concern, site observations and as described in the Remediation Strategy [1]. The criteria are adapted within the Remediation Strategy Implementation Plan [10] by Provectus, commensurate with the works they were completing, re-use of material below the cover system and "marker layer" (i.e. the shallower target concentrations do not apply).

Records of off-site spoil disposal will also be obtained and reported. Those records will include; volume, description, classification, destination etc.]. Copies of the waste tickets will be retained by the Contractor in accordance with the Duty of Care Regulations. Selected records will be presented in the Verification Report. Copies of any additional chemical testing that may have been carried out/ required by the receiving landfill will be retained by the Principal Contractor and will be presented in the Verification Report.

Copyright © 1976 - 2024 Buro Happold. All rights reserved

5.3.2 Imported soils

The physical and chemical suitability of imported materials for temporary use (e.g. pile mat, or similar) will be determined by the provision of data from the supplier. If that data is inadequate (with respect to frequency or suspect quality) it will be supplemented by analysis at a frequency of approximately 1 sample per 250m^3.

5.4 Groundwater

The following measures will be implemented as standard good practice during enabling works and earthworks to ensure any potential risks to controlled waters are mitigated:

i. Restricting the area of open excavation at any one time to reduce the potential for infiltration. Any dewatering of such excavation;
ii. Removal of source material (any gross contamination encountered as part of the excavation / removal of below ground obstructions) reducing the potential for future leaching of contamination from impacted soils to shallow groundwater;
iii. Prevention of uncontrolled run off during earthworks, including the provision of an appropriate cut-off/ barrier in the vicinity of the Canal bund as necessary. Appropriately managed dewatering during excavations to mitigate risks to receptors.

A groundwater risk assessment has been produced [11] to cover the grouting works associated with the known coal mining legacy at the Site. The contractor responsible for the grouting works (Cementation Skanska Ltd) were responsible for compiling the associated Completion Report [12]. The Principal Contractor is responsible for the monitoring of groundwater wells, River Medlock and Ashton Canal. All records are to be retained by the Contractor and a selection will be presented in this Verification Report.

5.5 Below ground infrastructure

The appropriateness of the design of below ground concrete will be demonstrated by the supplier's certification records of which will be held by the contractor. The Verification Report will confirm compliance and present appropriate evidence (e.g. example certification). Similarly, the appropriateness of the water supply pipework will be demonstrated by the supplier's certification records of which will be held by the client. The Verification Report will confirm compliance and present appropriate evidence (e.g. example certification if appropriate, or conformation that pipe material is suitable for its application / location).

5.6 Unexpected contamination

Upon encountering any unforeseen contamination, appropriate investigation / remedial action will be instigated and recorded by the remediation contractor (Provectus). Depending upon the scale and nature of that contamination, appropriate consultation / liaison may also be held with Buro Happold, local authority and/or the Environment Agency (as set out within the Remediation Strategy [1]). A record of all such instances will be taken by the Contractor, reviewed by Buro Happold and included in the Verification Report.

5.7 Environmental monitoring

To ensure the successful function of the works monitoring of noise and dust are being carried out at the site. Monitoring details will be recorded for process control purposes, and to check that mitigation measures are working effectively. The data will be recorded and presented in the Verification report.

Copyright © 1976 - 2024 Buro Happold. All rights reserved

5.8 Ground Gas Protection

The site has been classified as Characteristic Situation 2 (CS2) and the building type has been broken into two parts, Type C across the majority of the development with Type D in areas of service yard and vehicle access (owing to ventilation requirements). The building will need to achieve a minimum gas protection score of 2.5 points from at least two different protection elements, in accordance with BS 8485:2015+A1:2019 [16].

5.9 Independent Inspection

Buro Happold will be responsible for the provision of a watching brief comprising three main elements;

i. **Periodic site inspection**

   Currently, allowance has been made for an average of half a day at two week intervals for the initial period of earthworks plus office support. It is likely that initially, visits will be more frequent, but that once we are all confident that appropriate monitoring / record keeping is being undertaken, the frequency can be relaxed. A comparable pattern of visits will be implemented for the final phase of landscaping.

   A site visit pro forma will be prepared and completed on each visit to record observations. (Appendix A). This will be accompanied by supporting photographs. These pro forma & photographs will form a part of the evidence to be presented in the Report (and will support the Contractor's own records which will also be used in the Verification Report).

   When no below ground works are underway, no site visits are anticipated.

ii. **Ad hoc responses** to requests for advice (e.g. if unexpected contamination is encountered)

iii. **liaison with the local authority** if unexpected contamination is encountered.

Copyright © 1976 - 2024 Buro Happold. All rights reserved

6 Verification of groundworks

6.1 Introduction

Buro Happold were appointed by Bam Construction Ltd to undertake periodic inspection and recording of the works relevant to land affected by contamination, the primary responsibility for collection of the verification data was held by the remediation contractor (Provectus). Their record of the work is presented within a completion report [20], included here in Appendix A

The following text describes the data obtained relevant to the groundworks providing the necessary lines of evidence set out in the above plan. Much of this information is presented in a series of appendices to this report which are cross referenced in the appropriate section of the text. The text is presented for each of the aspects identified in the Plan and in the same order.

6.2 Health and safety

During the earthworks good standard practice and standard health, safety and hygiene was adopted in accordance with the Site Health and Safety Plan [21]. This good practice ensured that the potential risks to construction workers and occupiers of neighbouring sites, associated with the potential for hazardous materials in the Made Ground released into air as dust was appropriately mitigated.

During the periodic site inspections carried out by Buro Happold it was evident that good standard practice, health and safety and hygiene was consistently implemented. For example, appropriate PPE was always worn by personnel, there was always good control of site traffic and plant and there was no evidence of environmental nuisance (or hazard) associated with dust generation from construction activities (see Appendix K).

6.3 Earthworks


6.3.1 Site investigation

In 2019 and prior to completing the bulk earthworks, Provectus, the remediation contractor, completed a site investigation to determine the waste characteristics across the Site [9] (summarised in Section 3.2 of this report). The Provectus report informed their Materials Management Plan (MMP) which was submitted to CL:AIRE Department of Waste Code of Practice (DoW CoP) on 24th March 2021. The Buro Happold Remediation Strategy [1] informed the Provectus Remediation Strategy Implementation Plan [10] covering the bulk earthworks.

6.3.2 Excavation and disposal of soils

The excavation across the site to bring the site down to a formation level of +55mAOD resulted in spoil arisings total volume around 100,000m3. The large majority of the spoil comprised Made Ground materials removed from site as either Hazardous, Non-Hazardous or Recyclable. Soils were excavated to formation on a grid square by grid square basis, defined within the Waste Classification Report [9]. All hardstanding obstructions were broken out using a hydraulic breaker, stockpiled and sent off site for recycling. An online waste tracker was used by Provectus to record and store all the waste transfer notes and volumes (and is retained by them). A copy was also provided to, and is retained by, Buro Happold. An illustrative excerpt is presented below (Figure 6-1) and a summary of the total volumes of exported from site is summarised in Table 6-1 below.

Copyright © 1976 - 2024 Buro Happold. All rights reserved

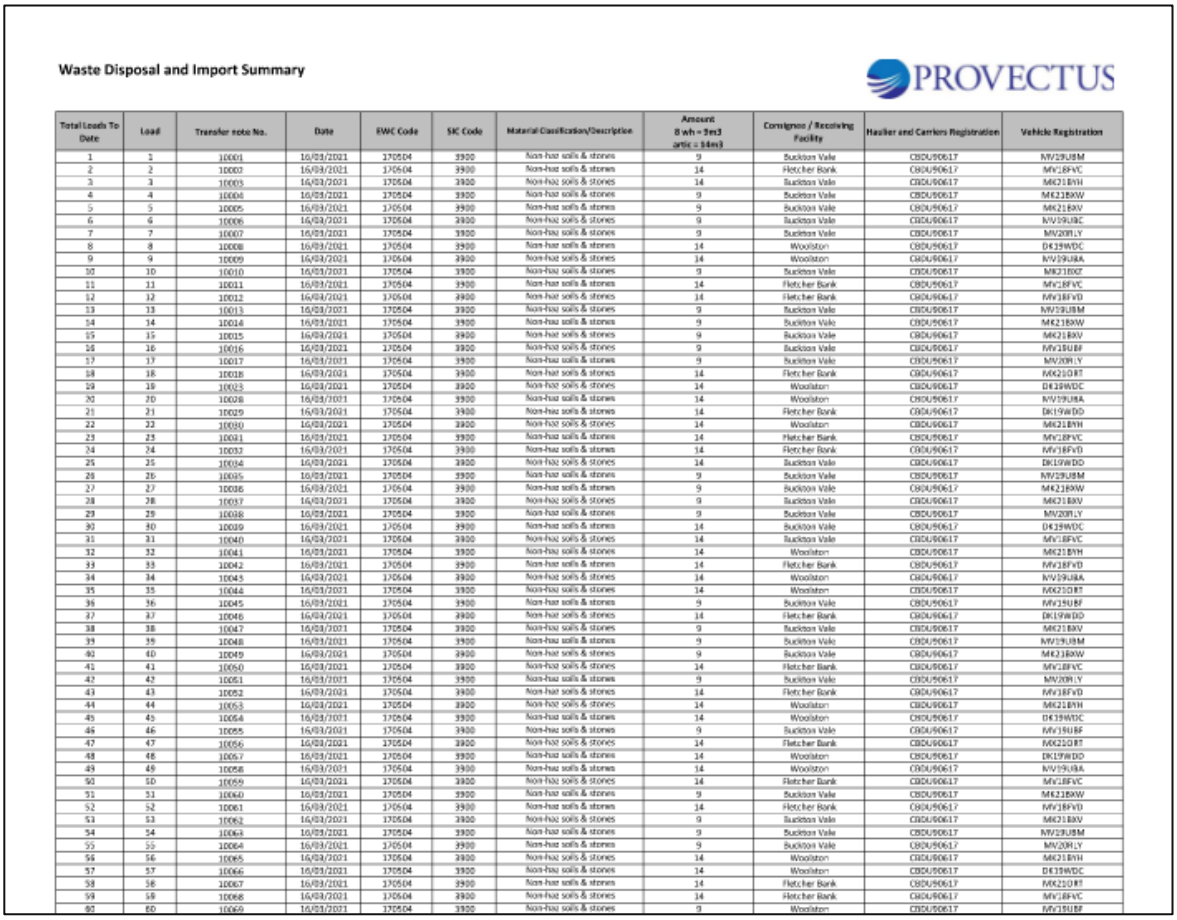

Waste Disposal and Import Summary

PROVECTUS

Total Loads To Date	Load	Transfer note No.	Date	EWC Code	SIC Code	Material Classification/Description	Amount 8 wh = 5m3 artic = 14m3	Consignee / Receiving Facility	Haulier and Carriers Registration	Vehicle Registration
1	1	10001	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU/90617	MV19UBM
2	2	10002	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU/90617	MV18FVC
3	3	10003	16/03/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU/90617	MK21BYH
4	4	10004	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU/90617	MK21BKW
5	5	10005	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU/90617	MK21BKV
6	6	10006	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU/90617	MV19UBC
7	7	10007	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU/90617	MV20RLY
8	8	10008	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU/90617	DK19WDC
9	9	10009	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU/90617	MV19UBA
10	10	10010	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU/90617	MK21BKF
11	11	10011	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU/90617	MV18FVC
12	12	10012	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU/90617	MV18FVD
13	13	10013	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU/90617	MV19UBM
14	14	10014	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU/90617	MK21BKW
15	15	10015	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU/90617	MK21BKV
16	16	10016	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU/90617	MV19UBF
17	17	10017	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU/90617	MV20RLY
18	18	10018	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU/90617	MX21DRT
19	19	10025	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU/90617	DK19WDC
20	20	10028	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU/90617	MV19UBA
21	21	10029	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU/90617	DK19WDD
22	22	10030	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU/90617	MK21BYH
23	23	10031	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU/90617	MV18FVC
24	24	10032	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU/90617	MV18FVD
25	25	10034	16/03/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU/90617	DK19WDD
26	26	10035	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU/90617	MV19UBM
27	27	10036	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU/90617	MK21BKW
28	28	10037	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU/90617	MK21BKV
29	29	10038	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU/90617	MV20RLY
30	30	10039	16/03/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU/90617	DK19WDC
31	31	10040	16/03/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU/90617	MV18FVC
32	32	10041	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU/90617	MK21BYH
33	33	10042	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU/90617	MV18FVD
34	34	10043	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU/90617	MV19UBA
35	35	10044	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU/90617	MX21DRT
36	36	10045	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU/90617	MV19UBF
37	37	10046	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU/90617	DK19WDD
38	38	10047	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU/90617	MK21BKV
39	39	10048	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU/90617	MV19UBM
40	40	10049	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU/90617	MK21BKW
41	41	10050	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU/90617	MV18FVC
42	42	10051	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU/90617	MV20RLY
43	43	10052	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU/90617	MV18FVD
44	44	10053	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU/90617	MK21BYH
45	45	10054	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU/90617	DK19WDC
46	46	10055	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU/90617	MV19UBF
47	47	10056	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU/90617	MX21DRT
48	48	10057	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU/90617	DK19WDD
49	49	10058	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU/90617	MV19UBA
50	50	10059	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU/90617	MV18FVC
51	51	10060	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU/90617	MK21BKW
52	52	10061	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU/90617	MV18FVD
53	53	10062	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU/90617	MK21BKV
54	54	10063	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU/90617	MV19UBM
55	55	10064	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU/90617	MV20RLY
56	56	10065	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU/90617	MK21BYH
57	57	10066	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU/90617	DK19WDC
58	58	10067	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU/90617	MX21DRT
59	59	10068	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU/90617	MV18FVC
60	60	10069	16/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU/90617	MV19UBF

Figure 6-1 Excert of the waste tracker information provided by Provectus

The bulk excavation took place between March 2021 and November 2021, presented in full within the Provectus Report, Appendix B, Drawing 11789c-8 (Appendix A).

A total of 576m^3 materials were consigned as 'recyclable materials', these were removed from site and transported to:

- **W. Maher & Sons Limited**. Ashton Old Road Recycling Depot, Ashton Old Road, Manchester M11 2XX [Permit No. EPR/GB3930AM]

Where material was consigned as 'Non-hazardous soil arisings', these were removed from site and transported to the following destinations:

- **Churchill Enviro Ltd**. Buckton Vale Quarry – Western Rock Trap, Carrbrook, Stalybridge, Greater Manchester, SK15 3RD [Permit No. EPR/GB3004XN & EPR/CB3301TX]
- **Fletcher Bank Quarry Landfill Site**. Marshalls Mono Ltd, Fletcher Bank, Ramsbottom, Bury, Lancashire, BL0 0DD [Permit No. DP3638ST]
- **Churchill Enviro Ltd**. Woolsten Deposit Ground, Off Thelwall Lane, Thelwall, Waarrington, Cheshire {Permit No. EAWML/50470]

Copyright © 1976 - 2024 Buro Happold. All rights reserved

Where materials were determined as 'Hazardous soil arisings', these were removed from site and transported to either a soil waste facility or appropriate landfill:

- **Waste Recycling Group (Central) Limited**. Edwin Richards Quarry – Soil Treatment Care, Portway Road, Rowley Regis, Warley, West Midlands, B65 9BT [Permit No. EPR/HP3632RP/V002]
- **3C Waste Limited**. Maw Green Landfill Site, Maw Green Road, Coppenhall, Crewe, Cheshire, CW1 5NG [Permit No. EPR/BS7722ID]

Environment Permits for each end destination were provided to Buro Happold (by Provectus) for review and are presented within Appendix B.

Management of pile arisings was undertaken by Provectus from December 2021 to February 2022. Provectus received material from the on-Site piling works, samples of which were then subject to testing prior to consignment and appropriate off-site disposal. Total exported materials as summarised in Table 6-1 below.

Table 6-1 Summary of exported waste volumes

Material Type	Volume (m3)	End Destination
Non-Hazardous soils	116,721	Fletcher Bank Quarry Landfill Buckton Vale Quarry Woolston Deposit Ground
Hazardous soils (hydrocarbons)	7,455	Maw Green Landfill Site
Hazardous soils (asbestos)	433	Edwin Richards Quarry
Recycled materials (concrete / hard materials / asphalt)	576	Ashton Old Road Recycling Depot

Careys completed an excavation for the harvesting / attenuation tank in March 2023, located within the east of the Site. The excavation took place at ground level and was taken down to formation level. No Made Ground materials were encountered within these excavations. The material comprised Glacial Till (clay), sand and carbonaceous mudstone. A total of 500m3 of natural material was removed with relevant waste transfer tickets presented in Appendix C.

6.3.3 Re-use of materials on site

Provectus produced a Materials Management Plan allowing re-use of geotechnically and chemically suitable material in the temporary batters re-engineered to support the tiered pile mats as well as the use of site won aggregates in the pile mats and working platform. A total of 1,296m3 was recovered from the high level piling mat and engineered ramp systems, segregated, sampled and successfully reused onsite within the low level pile mats. Soil samples were obtained for grading and chemical analysis (one sample per 250m^3), the results are presented within the Provectus Completion Report, Appendix J (refer to Appendix A of this report).

6.3.4 Imported material

Provectus were instructed by BAM to form pile platforms (high level and low level) using site won and imported aggregates in accordance with the pile platform design. The high level piling mat was installed adjacent to the eastern, western and southern boundaries along with a number of ramps. Once piling works at this high level were complete, the high-level piling mat was excavated to the low level pile mat formation levels.

Copyright © 1976 - 2024 Buro Happold. All rights reserved

A summary of the importation of material is presented below in Table 6-2. The full import log is presented within Appendix D of the Provectus Completion Report (Appendix A). All imported material was stockpiled separately from the excavated waste materials and signed appropriately.

Table 6-2 Summary of material import from March 2021 to December 2021

Imported material	Requirement	Loads No.	Quantity (m^3)
Quarried MOT Type 1	Pile mat	789	19,617
Quarried 6F5	Pile mat	628	15,388
Quarried 10mm	Surface Water Works	3	57
Quarried 20mm	Surface Water Works	31	670
Quarried 75mm	Haul Roads for BAM	176	1,584

6.4 Groundwater

Groundwater monitoring was carried out prior to and during the programme of grouting, in line with the recommendations of the approved Groundwater Risk Assessment [11]. Visual inspection of the River Medlock culvert entrances was also carried out. These activities were completed by the Principal Contractor, BAM Construction Ltd and records of these activities are presented within Appendix D. Provectus were responsible for decommissioning the boreholes when appropriate (during the excavation works), see Section 6.8 below.

Perched groundwater was identified during the initial ground investigation by Structural Soils in 2019. Provectus also identified perched groundwater within the Made Ground, around +51mAOD. This groundwater was managed via surface water drainage, treatment and discharge under an appropriate consent (see Photograph 1).

Bunds were formed on site to control any surface water run-off in the direction of Ashton Canal (see Photograph 2). During the earthwork programme, BAM engineers continued to monitor the groundwater levels (where possible) and the River Medlock to ensure no contamination from the site was migrating to this sensitive off-site receptor. Records of this monitoring are held by the Principal Contractor and have been reviewed by Buro Happold with examples presented here in Appendix D.

Copyright © 1976 - 2024 Buro Happold. All rights reserved



Photograph 1 Provectus surface water drainage, treatment and discharge point



Photograph 2 Bund along the boundary of the site adjacent to Ashton Canal.

Provectus also carried out their own monitoring of the canal to ensure no surface water run-off was taking place during the main excavation works. Provectus marked up their canal monitoring points, these are shown in Figure 6-2 with the observation records presented in Appendix G of the Provectus Completion Report (Appendix A of this report).



Figure 6-2 Canal monitoring points

BAM obtained a consent to the discharge of trade effluent (Water Industry Act 1991) through United Utilities on 15th January 2021. A record of this consent is presented within Appendix E. As part of the earthworks activities, surface water run-off and shallow perched water within the Made ground being excavated was encountered. A surface water collection system was installed by Provectus to prevent surface water run-off leaving site. The collection system comprised channels containing pea gravel and a perforated drainage pipe which fell to the northeast corner of the site where it was directed to a collection sump and subsequently pumped to the onsite water treatment system prior to consented discharge to foul sewer. Photographic evidence of this treatment system can be found within the Provectus Completion Report, Appendix P (see Appendix A of this report).

Copyright © 1976 - 2024 Buro Happold. All rights reserved

6.5 Below ground infrastructure

The appropriateness of the design of the below ground concrete has been demonstrated by the supplier's certification records shown in Appendix F

6.6 Unexpected contamination

During the bulk earthworks, Provectus ensured all excavations were monitored under an environmental watching brief to ensure any unexpected contamination was identified.

Soils impacted with visible fragments of asbestos cement sheeting were identified in the north-east section if the Site. These materials were quarantined prior to off-site disposal as Hazardous Waste to a Provectus Hazardous Waste Facility at Edwin Richards Quarry, Rowley Regis.

In addition to the Hazardous Waste material previously identified by Provectus in the pre works site investigation [9], an additional 35m3 of Made Ground, suspected to be historic gasworks material, was identified during the earthworks. This material was segregated and sampled prior to disposal off site as Hazardous Waste.

6.7 Unexploded Ordnance (UXO)

Provectus maintained a watching brief for UXO during the bulk earthworks (completed by a specialist contractor). A pre works briefing was also given to all Site staff prior to commencing works. No suspected UXOs were encountered during the works.

6.8 Environmental monitoring

An environmental monitoring method statement and risk assessment was provided by Provectus to Buro Happold for review (see Appendix G). The following summarises the monitoring that took place at the Site:

- Noise (to British Standard BS:4142)
- Dust (quantifiable Frisbee Dust Sampling)
- Dust (visible)
- Odour (quantitative)
- Asbestos monitoring via sub-contractor
- Air Quality Monitoring (gas and vapour via photo-ionisation detector (PID))
- Weather assessment
- Visual inspection of potential site run-off to the canal
- Visual inspection of the Water Treatment Plant and daily flow meter reading
- Borehole decommissioning across the site

There were a total of four boundary monitoring points (BMP 1-4) and four environmental monitoring points (EMP 1-4), see Figure 6-3 below. Odour monitoring was carried out three times a day whilst noise and dust required one round of monitoring per day. Dust monitoring was carried out using Frisbee Deposition Gauges which were sampled monthly. During the main excavation works, additional odour and PID monitoring was conducted on an ad hoc basis and records kept, these are presented in the Provectus Completion Report, Appendix G (see Appendix A of this report). Each BMP was monitored once a day (15 minutes per location) during operational hours but only whilst soil treatment activities were taking place. The results show dust deposition per day and were averaged for each month. All recordings were below the nuisance threshold of 200mg/m2 day.

Copyright © 1976 - 2024 Buro Happold. All rights reserved

A visual assessment of the canal took place once a day. The water treatment plant was monitored once a day. Provectus were responsible for the decommissioning of the boreholes across the Site, in line with the GWRA [11] and EA guidance [22]. A record of the decommissioned wells is presented in Appendix H.

Throughout the works a total of 32 visits were undertaken by Fourstage Environmental Ltd to monitor asbestos fibre emissions. Background concentrations did not exceed 0.01 fibres/cm3 (10% of the HSE control limit for asbestos working). All records are presented within Appendix H of the Provectus Completion Report (see Appendix A of this report).

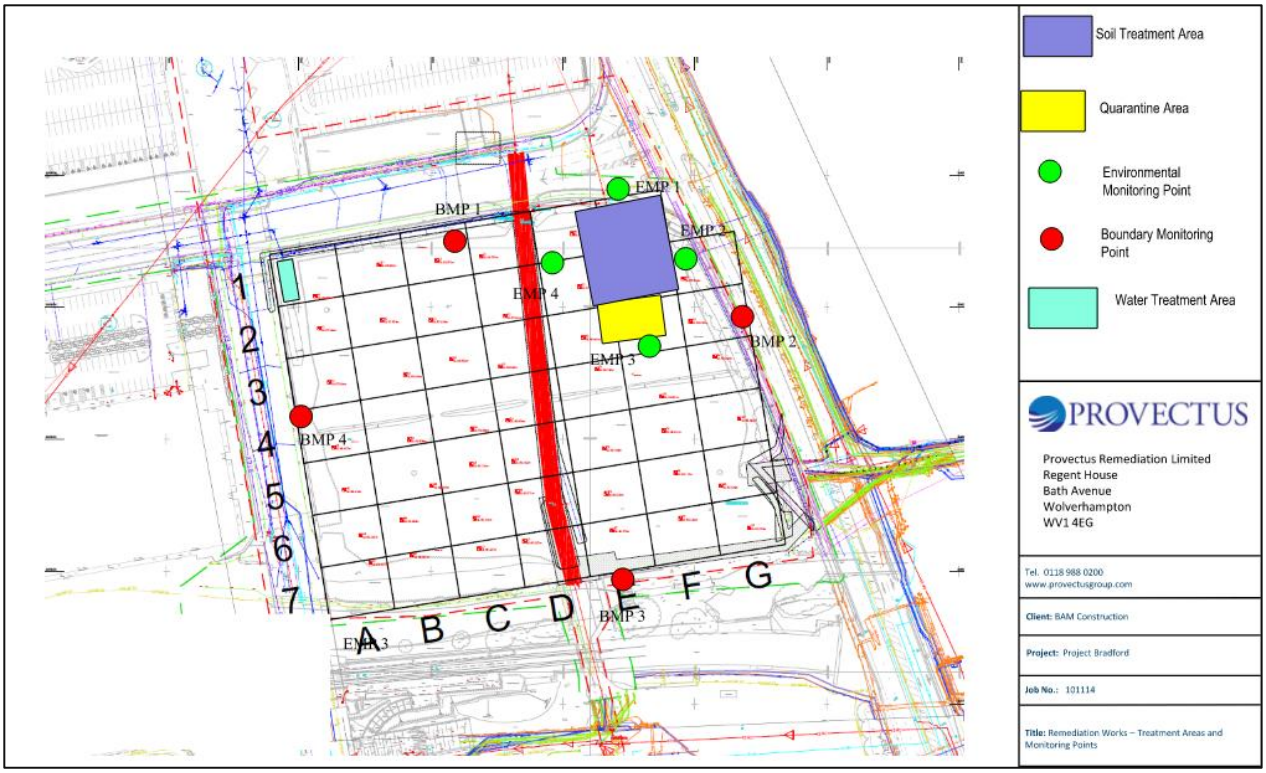


Figure 6-3 Environmental monitoring points provided by Provectus

6.9 Ground gas

GCP Applied Technologies were the supplier of the Preprufe 300R Plus gas resistant membrane (this product achieves 2 points in accordance with BS8485 [16]) with a Type B protection providing Grade 3 waterproofing as the structural barrier (2.5 points). Bituthene 8000 is certified as a gas-resistant membrane (2 points) for post-applied applications.

GCP Applied Technologies undertook eight site visits to review placement of the gas-resistant and waterproofing membrane. A summary of these visits and the remedial actions noted are as follows:

15th July 2021 by Chris Murray (GCP) accompanied by Jordan Harvey (Careys). Area reviewed: Core No. 1 GL, EN/DN – No1 / N04+. *[BRA-CCE-ZZ-ZZ-RP-Y-16111]*

Copyright © 1976 - 2024 Buro Happold. All rights reserved

- GCP Notes: Re-visit to Bituthene Liquid Membrane (BLM) application around exposed pile heads as there were isolated gaps or voids within the applied BLM (these are localised areas, not across the general BLM application).

16th July 2021 by Chris Murray (GCP) accompanied by Tom Ansell (Careys). Area reviewed: Eastern capping beam GL, AN – E01, Pile No's. 326-312, Pour No. 1. *[BRA-CCE-ZZ-ZZ-RP-Y-16112]*

- GCP Notes: as above.

23rd & 26th July 202 by Chris Murray (GCP) accompanied by Colm Farrell (Careys). Area reviewed: Eastern capping beam GL, E01 – E03+, Pile No's. 311 – 280, Pour No. 2. *[BRA-CCE-ZZ-ZZ-RP-Y-16113]*.

- GCP Notes: Localised areas of BLM application to exposed pile heads requires remedial work to repair mechanical damage and or scuffs etc. Site teams are to remove as required and overlay with correctly mixed BLM as applicable.

5th August 2021 by Chris Murray (GCP) accompanied by Colm Farrell (Careys). Area reviewed: Eastern capping beam GL, E02+ – E03+, Pile No's. 287 – 299, Pour No. 3. *[BRA-CCE-ZZ-ZZ-RP-Y-16114]*.

- GCP Notes: No remedial actions, just advise site teams to do final visual checks prior to concrete placement and to ensure any cuts, holes or other damage through Preprufe Plus carrier layer are repaired appropriately.

19th August 2021 by Chris Murray (GCP) accompanied by Colm Farrell (Careys). Area reviewed: Eastern capping beam GL, E05+ – E06, Pile No's. 265 – 272, Pour No. 4/5. *[BRA-CCE-ZZ-ZZ-RP-Y-16115]*.

- GCP Note: Remedial actions previously discussed on the 16th August to both the horizontal concrete blinding layer and localised exposed pile head locations were previously completed by the site teams prior to the GCP membrane system installation.

31st August 2021 by Lee Clow (GCP) accompanied by Colm Farrell (Careys). Area reviewed: Core 6.

- GCP Notes: BLM incorrectly applied to internal face of Preprufe membrane. BLM in this location prevents the bond of the membrane to the poured in-situ concrete, thereby creating a potential path for water should ingress occur. Preprufe patches installed incorrectly. Where Preprufe membrane has been installed to cover fixings, patches have been installed upside down. Patches installed with HDPE facing uppermost and not the acrylic coating. These areas require remedial work by reinstallation, ensuring membrane face is the correct way around (i.e. acrylic coated adhesive facing to receive concrete).

3th September 2021 by Lee Clow (GCP) accompanied by Colm Farrell (Careys). Area reviewed: Core 6 & GL E07 Movement Joint. *[BRA-CCE-ZZ-ZZ-RP-Y-16117]*

- GCP Notes: BLM incorrectly applied to internal face of Preprufe membrane. BLM in this location prevents the bond of the membrane to the poured in-situ concrete, thereby creating a potential path for water should ingress occur, patch of Preprufe or Preprufe LT Tape to be applied to the area to ensure bond with concrete.

The actions highlighted by GCP during their site visits were actioned by Careys with photographs showing the remediation detail and a certificate signing off each area. A selection of these certificates is presented in Appendix I.

To date MTS have undertaken eleven visits to the site (including an additional visit for photographic validation purposes) to independently verify the installation of the membrane, with the most recent visit taking place in December 2023. On each occasion a sign-off certificate was produced, including photographic records (see Appendix I for a selection of certificates).

Membrane Testing Solutions (MTS) were instructed by BAM to verify the installation of the Preprufe ground gas and waterproofing membrane. MTS are an appropriately qualified independent verifier. A copy of completion report was

Copyright © 1976 - 2024 Buro Happold. All rights reserved

provided by MTS in December 2023 (Appendix J) upon completion of installation. A summary of the report's findings is presented in Section 7.2.7.

24th January 2022, Barrie Ackroyd and Dan Squire. Areas checked included the slab area to gridlines W07-W08 and EW.

MTS Note: Visual inspection confirmed very good standard of installation of the membrane. Membrane was lined across main floor and tape jointed in line with GPC material specifications and industry best practices. Membrane jointed into perimeter liner wall membrane and all stainless-steel starter bars sealed with Bituthene LM E trowel applied membrane. Seam pick probe was employed for integrity testing, no defects reported. Waterbar's weld jointed using hot knife and stuck down to the 300R membrane using Bitustik BT 240 double sided jointing tape. No defects, area passed inspection.

3rd February 2022, Dan Squire. Areas checked included North west slab (pour 2); main floor gridlines W06-W08 / NW – N01; Core 5 (base installation) gridlines E07-BS / N12-BE.

MTS Note: Visual inspection confirmed very good standard of installation of the membrane. Preprufe 300R plus membrane lined across pour slab areas, joined to previously installed membrane up the liner wall to the capping beam. Membrane has permanent back binding, used to join membrane together and pressure rolled. Some areas included additional strip of Preprufe Tape LT on top of joints. Mix of Bituthene LM and Bituthene liquid membrane applied to seal all penetrations. Patch repairs to membrane along vertical face of liner wall and on floor where minor damages were caused by steel. Cleaning of membrane prior to pour. Restricted access meant some areas were not inspected. Area passed inspection.

24th February 2022, Dan Squire. Area inspected: Core 5 (wrap installation) gridlines E07-BS / N12-BE

MTS Note: Visual inspection of tanking wrap installation. Membrane lined across core base and extended up vertical face of core walls. Overlaps installed to correct measurement and all tanking thoroughly rolled and adhered. Site undertaking their own inspections, where air was trapped under tanking, slit made and Bituthene LM applied with additional piece of Bituthene 8000/S. Tanking approximately 20% complete when inspection took place, all works being carried out to good standard. Area passed inspection.

24th February 2022, Dan Squire. Area inspected: Core 7 base. Main floor installation gridlines S11-S15 / SW3.

MTS Note: Visual inspection of membrane, installed to good standard. Membrane lined across core base and extended up temporary shuttering (stayed in place 5 days after pour to allow membrane to adhere to concrete). Membrane has permanent back binding, used to join membrane together and pressure rolled. Some areas included strip of Preprufe Tape LT on top of joints. Mix of Bituthene LM and Bituthene liquid membrane applied to seal all penetrations. Patch repairs to membrane along vertical face of liner wall and on floor where minor damages were caused by steel. Area passed inspection.

24th February 2022, Dan Squire. Area inspected: South west slab – Pour 9. Main floor installation gridlines S1-S3 / NW - N01

MTS Note: Visual inspection of membrane, installed to good standard. Membrane lined across pour slab and joined to the membrane previously installed up liner wall to capping beam. Membrane has permanent back binding, used to join membrane together and pressure rolled. Some areas included strip of Preprufe Tape LT on top of joints. Mix of Bituthene LM and Bituthene liquid membrane applied to seal all penetrations. Patch repairs to membrane along vertical face of liner wall. Cleaning of membrane prior to pour. Area passed inspection.

5th April 2022, Keith Barsby. Area inspected: Sprinkler room pool 2 gridlines S15.8/S17.5 – FS/GS. Buttress walls gridlines E06 – E07

MTS Note: Visual inspection of membrane, installed to good standard. Sprinkler room: Membrane installed across concrete base and turned up 90° against piles. Piles sealed to membrane using Bituthene LM. Fixings through membrane and walls sealed using patches of Preprufe 300R Plus membrane with

Copyright © 1976 - 2024 Buro Happold. All rights reserved

Preprufe LT tape. Buttress walls: Membrane installed vertically against piles, sealed using Bituthene LM (unable to inspect due to height). No defects reported. Water ingress noted below membrane within Sprinkler Room in lower floor area after installation, this was pumped out during the inspections. Area passed inspection.

30th June 2022, Keith Barsby. Area inspected: Sprinkler tank area gridlines S15.8/S17.5 south liner walls gridlines S13/S15 – liner walls east gridlines E04/E06.

MTS Note: Visual inspection of membrane, installed to good standard. Membrane installed vertically against piles, sealed using Bituthene LM (unable to inspect due to height). Reinforcement mesh for walls installed against Preprufe 300R Plus membrane. Fixings sealed using patches of Preprufe 300R Plus membrane, Preprufe LT tape and Bituthene LM. Area passed inspection.

23rd August 2022, Dan Squire. Area inspected: Core 1 tanking to pre cast walls. Gridlines N01-N04 / NW2-NW3

MTS Note: Visual inspection of membrane, installed to good standard. Preprufe 300R plus membrane previously lined across core base and extended up toe and joins to Bituthene 8000 tanking which was adhered to the pre cast walls up to the correct height as per the design. Approx. 12m of tanking installed at time of inspection to west and south facing core walls. No recorded defects.

25th January 2023, Dan Squire. Area inspected: South-west Slab east of core 6.

MTS Note: Visual inspection of the membrane, the membrane had been installed to a good standard. Preprufe 300R membrane has been lined across footprint of the slab. Joining onto the membrane located under the slab previously poured. The membrane has a permanent back binding which is used to join the membrane together and is pressure rolled. Additional Lap tap is then installed over the membrane joints. No recorded defects however the area was incomplete.

7th August 2023, Dan Squire. Area inspected: Bowl slab area to gridlines E01-E04 and N10-AE

MTS Note: Visual inspection of membrane, majority of the Preprufe 300R Plus membrane had been covered with steel reinforcing bars meaning the majority of the membrane seams were unable to be inspected below the steel reinforcement. However, there was an area where the membrane installation was ongoing and being completed with lap tape over non-compliant membrane seams. The membrane seams in this area proved to be well sealed and fully bonded in the carried-out a thorough visual inspection of the membrane, the membrane had been installed to a good standard. The raft slab edge was incomplete and some areas of the Waterbar were not bonded to the Preprufe 300R membrane, there were also holes drilled through the membrane which will require remedial works. Some defects identified including several seam de-bonds areas which were marked with blue paint. Steel stanchion depressions were also identified which are to be boxed out and repaired at a later date. At the time of the inspection the membrane works were ongoing and incomplete.

12th September 2023, Dan Squire. Area inspected: Bowl area to Gridlines E01-E04 and N10-AE

MTS Note: Visual inspection of membrane and seam pick testing to the above area. during site visit there were a number of seam de-bond defects and punctures which were marked with blue paint. Unfortunately the repairs were unable to be performed at that time, therefore it was agreed MTS Ltd would accept photographic validation of the completed repairs. MTS Ltd received a completion and close out report from BAM on the 6.9.2023 which provided evidence that the repairs have been performed using Cordeck LM material and upon a detailed visual examination all repairs had been completed and on this basis close out the original pass work in progress certificate issued on the 7.8.2023. On this basis a pass in full has been achieved.

29th September 2023, Dan Squire. Area inspected: Perimeter tanking and waterproofing detail.

MTS Note: Visual inspection of waterproofing and membrane, installed to good standard. Bituthene 8000 has been installed by P J Carey's. Sealed to the required height of the walls and joined to the Preprufe

Copyright © 1976 - 2024 Buro Happold. All rights reserved

membrane previously installed under the concrete walls. An additional layer of S2 primer is installed to the walls prior to the Bituthene 8000 installation. Bituthene LM black sealant is used between the joints of the 8000 tanking and existing Preprufe membrane. Holes were being drilled through the 8000 tanking to allow for dowels to be installed. These dowels will be sealed using Bituthene LM black sealant at a later date and re-inspected. The area passed inspection.

18th October 2023, Dan Squire. Area inspected: East perimeter tanking and waterproof detail.

MTS Note: Visual inspection of waterproofing and membrane, installed to good standard. Waterseal have installed the movement joint to the east perimeter walls. Integritank waterproofing spray was then applied to the walls. Sealing the movement joint and overlapping with the Bituthene 8000 tanking to allow for dowels to be installed. These dowls are still to be sealed using bituthene LM Black sealant at a later date and re-inspected, and therefore is discounted from this cert. Some repairs were made to the Bituthene 8000 using additional layers of the Bituthene and jointing tape overlapping to reduce the risk of the Bituthene delaminating at the edges. The area was noted to be incomplete.

4th December 2023, Dan Squire. Area inspected: South-east and west perimeter tanking and waterproofing detail. Main floor membrane installation.

MTS Note: Visual inspection of waterproofing and membrane, installed to good standard. Waterseal have installed the movement joint to the south-east perimeter walls and south west upper slab. Integritank waterproofing spray is installed onto the pre primed slab and walls. Sealing the movement joint and overlapping with the Bituthene 8000 which had previously been installed by P J Carey's. Waterseal have installed the movement joint to the south-east perimeter walls and south west upper slab. Integritank waterproofing spray is installed onto the pre primed slab and walls. Sealing the movement joint and overlapping with the Bituthene 8000 which had previously been installed by P J Carey's. The Integritank spray is sealed to the required height of the walls. Some repairs have been made to the Bituthene 8000 using additional layers of the Bituthene and joining tape overlapping the joints to reduce the risk of the Bituthene peeling away at the edges. Preprufe 300R membrane has been lined across footprint of main arena floor by PJ Carey's. Joining onto the membrane previously laid under the slab previously poured. The membrane has a permanent back binding which is used to join the membrane together and is pressure rolled. Additional Lap tap is then installed over the membrane joints. At the time of inspection the membrane works were ongoing and incomplete. The stanchions were yet to be sealed using the Bituthene LM black sealant and the movement joint needed additional LM Black to re seal as this was installed last year. All other works in this area were being installed to a good standard. A large section for the main floor membrane has re bar installed ready for the concrete meaning a restricted inspection in this area which seemed well cleaned off and free from any damages that we could see. The area was noted to have passed inspection.

6.10 Buro Happold inspection

Periodic Site inspections: Staff from Buro Happold periodically attended site to inspect and record the works. In total 22 visits have been undertaken over the period March 2021 to February 2022. A copy of the Site visit records and selected photographs are presented in Appendix K. During these Site inspections a good standard of health, safety and hygiene was consistently observed. Similarly, traffic and plant management was well managed. Suitable haul roads were constructed to minimise production of dust and monitoring points installed around the Site, checked daily. Activities were being appropriately recorded and have been produced for this report.

Ad hoc responses: During this period there were no urgent calls for ad hoc inspection or advice with respect to unforeseen contamination.

Copyright © 1976 - 2024 Buro Happold. All rights reserved

Liaison with the local authority: Because of the absence of any unexpected gross contamination, no liaison between the local authority and BuroHappold with respect to ground contamination / remediation was required or carried out.

Copyright © 1976 - 2024 Buro Happold. All rights reserved

7 Conclusions

7.1 Achievement of remedial objectives

The Remediation Strategy [1] has been successfully delivered by the works with the achieved contamination related objectives set out below. The specific aims to the Strategy were:

- To ensure potentially significant risks to people or the environment are mitigated in both the short and long term;
- To meet specific planning conditions put in place by the local planning authority;
- To avoid regulatory intervention
- To ensure both client and stakeholder expectations are satisfied;
- To minimise long term liabilities.

7.2 Compliance with Remediation Strategy

7.2.1 Health and safety

Throughout the earthworks good standard practice, health and safety and hygiene was consistently implemented, this was witnessed by Buro Happold during periodic site inspections.

7.2.2 Earthworks and contamination

All excavated soil arisings from the bulk earthworks were removed from site as either Hazardous, Non-Hazardous or Recyclable, and transported to appropriately licensed receiving facilities. Relevant evidence is provided by a detailed waste tracker which includes details of the waste tickets together with monthly summaries of volumes of material exported or imported from site. A small volume of material was suitable for re-use on site within the lower level pile mats. This was managed under a Materials Management Plan and relevant sampling and testing undertaken to determine suitability.

There was a requirement to import materials to site (quarried aggregate) for the construction of the pile mats. The material was subject to review prior to import to ensure compliance with the material specification. All imported material was stockpiled separately from the excavated waste materials and signed appropriately.

7.2.3 Groundwater

Groundwater monitoring was undertaken prior to and during the grouting activities at the site. Visual inspection of the River Medlock culvert entrances was also carried out. These inspections were undertaken by the Principal Contractor (BAM) and records were made available for review. No noticeable contamination was recorded. Upon completion of the grouting activities, Provectus decommissioned all boreholes in line with EA guidance.

Perched water was recorded on site, Provectus installed a water treatment system in the northeast of the site together with drainage channels to allow the water to collect, be treated and then disposed of via foul sewer (under the relevant discharge consent).

7.2.4 Infrastructure

The appropriateness of the design of the below ground concrete has been demonstrated by the supplier's certification.

Copyright © 1976 - 2024 Buro Happold. All rights reserved

7.2.5 Unexpected contamination

Soils impacted with visible fragments of asbestos cement sheeting were identified in the north-east section if the Site. These materials were quarantined prior to off-site disposal as Hazardous Waste to a Provectus Hazardous Waste Facility at Edwin Richards Quarry, Rowley Regis.

7.2.6 Environmental monitoring

Odour, PID, dust, asbestos, and noise monitoring were carried out during the bulk earthworks from set positions around the site. A visual assessment of the canal took place once a day. The water treatment plant was monitored once a day. All results were below the relevant thresholds and no contamination was observed within the nearby sensitive controlled waters. Bunds were formed on site to control any surface water run-off in the direction of Ashton Canal. During the earthwork programme, BAM engineers continued to monitor the River Medlock to ensure no contamination from the site was migrating to this sensitive off-site receptor.

7.2.7 Ground gas installation

Membrane Testing Solutions (MTS) were employed by BAM Construction Ltd to undertake independent verification of the ground gas membrane placement across the Site. Individual sign off certificates have been made available for review and on all occasions no defects were recorded, the works were reported to be completed to a good standard and all inspected areas passed. A selection of sign off certificates are provided in Appendix I. The final completion report from MTS was made available in December 2023 (see Appendix J). The report concluded that ground gas mitigation measures prescribed for this Site have been inspected, tested, and validated in accordance with GCP design, materials specifications, and industry best practice. Whilst MTS have not validated every m^2 of membrane installed, they confirm that sufficient evidence has been captured for all detailing and design elements to ensure confidence of the installation process.

Accordingly, MTS concluded the 'CS2 Low Risk' ground gas mitigation measures installed to this project have been sufficiently managed to maintain maximum confidence to the proficiency of the installed gas mitigation system. Therefore, MTS concluded that the materials installed are appropriate, have been "validated in accordance with CIRIA C735 [23]" and their accepted Verification Plan. MTS have therefore recommended that this report be submitted to the LPA to support sign-off of the associated planning condition(s).

7.3 Status of the site at completion of works

This report (Verification Report - Part A) forms part of a two-part Verification Report. A subsequent report (Part B) shall be prepared and submitted on completion of the soft landscaped areas and above ground planters. Based on the above it is concluded that the provisions of the local authority Planning Condition 7 have been met reflecting the successful implementation of a remediation strategy with respect to Part A activities (Ground Works). This report presents the evidence demonstrating the effective implementation of the agreed remedial measures in accordance with Planning Condition 7. Accordingly, this report should be submitted to the local authority for their consideration with respect to the discharge of this condition. To discharge Condition 7 fully a Verification Report Part B (Landscaping) will need to be completed in due course, on completion of the landscaping and completion of any remaining below ground infrastructure across the Site.

7.3.1 Long term monitoring

Because of the successful implementation of the Remediation Strategy, and the absence of any discovery of unforeseen / unexpected contamination and associated residual risks, no long term monitoring of the site is required.

Copyright © 1976 - 2024 Buro Happold. All rights reserved

References

[1] Buro Happold Engineering Ltd, "BRA-BHE-XX-XX-RP-CG-0006 P02 Remediation Strategy," 2020.

[2] Environment Agency, Land Contamination Risk Management (LCRM), 2020.

[3] Buro Happold Engineering Ltd, "BRA-BHE-XX-XX-RP-CG-0001 P01 Geoenvironmental and Geotechnical Desk Study," 2019.

[4] Buro Happold Engineering Ltd, "BRA-BHE-XX-XX-RP-CG-0004 P04 Geoenvironmental and Geotechnical Interpretative Report," 2020.

[5] Buro Happold Engineering Ltd, "BRA-BHE-XX-XX-RP-CG-0005 P03 Coal Mining Risk Assessment," 2020.

[6] British Geological Survey, "Manchester. England and Wales Sheet 85. Bedrock. 1: 50 000.," 2010.

[7] B. G. Survey, "Manchester. England and Wales Sheet 85. Bedrock and Superficial Deposits. 1: 50 000.," 2011.

[8] British Geological Survey, "1: 10 000 Geology Series. Sheet SJ89NE (Gorton)," 2004.

[9] Provectus Remediation Ltd, "10114/R002 Project Bradford Waste Classification Report," 2020.

[10] Provectus Remediation Ltd, "101114/003/RSIP/001 Remediation Strategy Implementation Plan," 2021.

[11] Buro Happold Engineering Ltd, "BRA-BHE-XX-XX-DN-CG-0001 P02 Grouting Works: Groundwater Risk Assessment," 2020.

[12] Cementation Skanska, "BRA-CSL-ZZ-ZZ-RP-X-00900 Old COal WOrkings 0 Project COmpletion Report," 2021.

[13] CIRIA, "C665 Assessing risks posed by hazardous ground gases to buildings," 2007.

[14] BAM Construction Ltd, "HNW0337 Co-op Live: Construction Environmental Management Plan (CEMP)," 2021.

[15] British Standard Institute , "BS 3882:2015 Specification for topsoil," 2015.

[16] British Standard Institute, "BS 8485:2015+A1:2019 Code of practice for the design of protective measures for methane and carbon dioxide ground gases for new buildings," 2019.

[17] British Research Establishement Report, "Special Digest 1: Concrete in agressive ground (third edition)," 2005.

[18] Water UK, "Contaminated Land Assessment Guidance," 2014.

[19] United Utilities, "Supplementary guidance for the selection of water pipes in land potentially affected by contamination".

Copyright © 1976 - 2024 Buro Happold. All rights reserved

[20] Provectus Remediation Ltd, "101114/VR/001 Enabling Works Validation Report (DRAFT)," 2022.

[21] Turner and Townsend, "Pre-Construction Information Report," 2020.

[22] Environment Agency, "Good practice for decommissoning redundant boreholes and wells," 2012.

Copyright © 1976 - 2024 Buro Happold. All rights reserved

Appendix A Provectus Completion Report

Copyright © 1976 - 2024 Buro Happold. All rights reserved

ENABLING WORKS VALIDATION REPORT

101114/VR/002

BAM Construction Ltd



Enabling Works Completion Report

Co-op Live! Manchester

December 2022

PROVECTUS

Project Quality Assurance

Information Sheet

Report Type	:	Enabling Works Validation Report
Site Location	:	Co-op Live! Manchester
Report Number	:	[101114/VR/002]
Report Status	:	Final
Report Date	:	16th December 2022
Prepared for	:	BAM Construction Ltd
Prepared by	:	Provectus Remediation Limited
		Genesis Centre, Garrett Field
		Birchwood
		Warrington
		WA3 7BH

Compiled by : Tom Harrington

Project Manager



Reviewed by : Alex Clifford



Project Director

Authorised by : Steve Langford



pp

Managing Director

TABLE OF CONTENTS

1 INTRODUCTION 6

1.1 Background 6
1.2 Project Objectives 6
1.3 Site Location 7
1.4 Project Timescales 7
1.5 Scope of Works 7
1.6 Ground Conditions 8
1.7 Site Set up 8

2 SUMMARY OF WORKS 9

2.1 Pre-Works Site Investigation and Waste Classification 9
2.2 Excavation of soils 9
2.3 Asbestos Protection Measures 10
2.4 Discovery Strategy and Unexpected Contamination 10
2.5 Import of Materials 11
2.6 Pile Mat Installation 11
2.7 Plate Load Testing 11
2.8 UXO 12
2.9 Perched Water and Surface Water Management 12
2.10 Mobile Treatment Licence 12
2.10.1 Soil Screening 13

3 ENVIRONMENTAL MANAGEMENT AND CONTROL 14

3.1 Environmental and Health and Safety Management Overview 14
3.2 Environmental Control and Monitoring 14
3.2.1 Dust 14
3.2.2 Asbestos Air Emissions 15
3.2.3 Volatile Organic Compounds 16
3.2.4 Noise 16
3.2.5 Wheel Washing 16
3.2.6 Further Pollution Prevention and Control Measures 17
3.3 Traffic Management 17
3.4 Odour Control 17

4 WASTE MANAGEMENT AND MATERIAL TRACKING 18

4.1 Material Tracking 19

4.2 MATERIALS MANAGEMENT PLAN 19
4.3 RE-USE 19
5 OTHER REMEDIATION REQUIREMENTS 21
6 COMPLETION AND HANDOVER 22
6.1 PHASED HANDOVER OF SITE AREAS 22
6.2 MATERIALS MANAGEMENT PLAN VALIDATION 22
6.3 VALIDATION SUMMARY AND CONCLUSION 22

APPENDICES

APPENDIX A Report Conditions
APPENDIX B Drawings
APPENDIX C Planning and Programme of Works
APPENDIX D Waste Disposal and Import Summary
APPENDIX E Waste Consignment Notes
APPENDIX F Stockpile Surveys
APPENDIX G Environmental Monitoring Forms
APPENDIX H Asbestos Air Monitoring Results
APPENDIX I Plate Bearing Test Results and Location Plan
APPENDIX J Sample Tracker and Geochemical/Dust Laboratory Test Results
APPENDIX K Material and Stockpile Tracker
APPENDIX L Mobile Treatment Licence and Discharge Consent
APPENDIX M Material Management Plan
APPENDIX N Borehole Decommissioning Logs
APPENDIX O Temporary Works Design
APPENDIX P Photographs
Appendix Q Imported Stone Grading Certificates

1 INTRODUCTION

1.1 Background

BAM Construction Ltd (the Client), herein referred to as BAM, commissioned Provectus Remediation Ltd (PRL) to undertake the enabling earthworks phase for the construction of the Co-op Live arena. This Validation Report relates to the earthworks phase of Co-op Live and is to be read in conjunction with the PRL Remediation Strategy and Implementation Plan: **Error! Reference source not found.** (RSIP).

This document is intended to demonstrate that the remediation works undertaken are in accordance with the Remediation Strategy and Remediation Method Statement.

The following data sources were used in the preparation of this report:

- Stockpile, formation and finished Level Surveys
- Waste consignment/transfer note and Waste Tracker
- Imported material records
- Stockpile and Materials Tracker
- Soil Laboratory Test Results
- Geotechnical Plate Test and Grading Results
- Environmental Monitoring Forms
- Asbestos Air Monitoring Results
- Photographs

1.2 Project Objectives

BAM engaged PRL as a Sub-Contractor to remove impacted made ground in order to reduce the contaminant loading of the site and to provide an enabling works platform for piling and construction.

The PRL main project objectives were:

- To safely deliver the earthworks phase of the project in line with the parameters of the RMS/ RSIP and the BAM working platform / pile mat designs.

- To reduce site levels to circa 55m AOD meaning circa 100,000m^3 of material needed to be excavated for off-site disposal.

- To form pile platforms (high level and low level) using site won and imported aggregates in accordance with the pile platform design.

1.3 Site Location

The Co-op Live site is situated off Sport City Way, Manchester. The Ashton Canal and footpath form the southern boundary, Alan Turing Way the eastern, Joe Mercer Way the western and Sport City Way the northern. The National grid reference for the approximate site centre is 386841, 398878.

A Location Plan and Subject Site boundary is presented in Appendix B ref. SK101114/01 Site Location Plan.

The site is approximately 25,000m^2 in area. On occupation the site was generally flat with a shallow downward gradient from south to north providing a fall of approximately 4m across the extent of the site.

Historically, following agricultural use, the western portion of the site was occupied by the Bradford Road Gas Works while the eastern portion was residential. The River Medlock which formerly passed through the northwest of site is now diverted through a culvert beyond the northern site boundary.

At the time of PRL mobilisation in March 2021, the site was occupied by Skanksa Piling, a sub-contractor of BAM undertaking grouting of historic mine workings.

1.4 Project Timescales

The programme of works is included with Appendix C, site works commenced on the 15th March 2021 with handover of the final pile mat area completed on 3rd December 2021. Due to rephasing of works by other contractors on site, the release of work areas to PRL was delayed resulting in a programme extension of 14 weeks.

Additional pile arisings management was undertaken by PRL from December to January 2021 whereby PRL are receiving material from the onsite piling works, testing soils prior to disposal, and maintaining the waste consignment of the material during offsite disposal.

1.5 Scope of Works

- Undertake supplementary site investigation prior to enabling works commencing on a sample grid to confirm the waste classification for surplus soils;

- Excavation of made ground and surplus materials to formation and management of arisings for disposal, including segregation of different waste streams i.e. Hazardous and non hazardous

- Surface water management and on site treatment prior to discharge to foul sewer under a Discharge Consent

- Implementation of environmental controls and environmental monitoring (including asbestos monitoring);
- Placement of Primary Aggregate 6F5/Type 1 Piling Mats as enabling works
- Testing of site won soils and stone for reuse on site as per the RMS/RSIP
- Management of pile arisings for testing and offsite disposal
- Validation testing and reporting

1.6 Ground Conditions

The site investigations identified potential obstructions in the form of reinforced concrete blocks and boulders. Contamination was identified as ash, slag and hydrocarbon impact to soils and water.

The chemical data identified elevated metals (including arsenic, beryllium, lead, and mercury), petroleum hydrocarbons, polycyclic aromatic hydrocarbons, and volatile organic compounds and asbestos.

Perched groundwater was identified in the Made Ground with groundwater at 51m AOD. This was managed via surface water drainage, treatment, and discharge under appropriate consent.

In addition to the general Made Ground at site previous remedial works have been undertaken leaving a circa 600mm thick layer of crushed aggregate across approximately half the site prior to major bulk earthworks commencing.

1.7 Site Set up

As Principal contractor, BAM mobilised welfare provisions comprising site offices, canteen, drying rooms and toilets in a site welfare compound south of the main site boundary across Forge Lane Bridge. A secure boundary was maintained at all times and comprised of hoarding to help mitigate fugitive emissions and to prevent unauthorised access. The maintenance of the boundary and site security during the works is the responsibility of BAM.

PRL mobilised a number of plant machinery to undertake the excavation and earthworks element of the work. This comprised of:

- 20T-50T 360 excavators
- 30T Articulated Dumper Trucks
- D6 Dozer
- 13T Smooth Drum Vibratory Roller
- 2-Way Screener
- Dust suppression equipment – including mobile atomisers
- Water Treatment System

PRL established a site office to manage waste disposal tickets on the gate.

2 SUMMARY OF WORKS

2.1 Pre-Works Site Investigation and Waste Classification

A pre-works testing and waste characterisation exercise was undertaken in January 2020. This comprised dividing the site using a grid system and advancing trial pits in each square (48 no. in total) to the formation level of the proposed earthworks. Each location was sampled per metre below ground level with a total of 212 samples being analysed at a frequency of one sample per 500m^3 of soil to be excavated and disposed of.

This investigation and associated report (Provectus Waste Classification Report Ref: 101114/R002/02 dated 12 March 2020.) enabled waste classification of the subject soils prior to bulk excavation thereby allowing for proper planning, identification of suitable disposal facilities and haulage requirements prior to commencement on site. In addition to the above QA sampling was undertaken from stockpiles of excavated materials/quarantined area. During the excavation and disposal works additional QA samples were recovered to confirm the waste assessment.

2.2 Excavation of soils

Site levels were excavated and reduced to the formation levels designed by BAM in their design drawing "Low Level Pile Mat Design Rev 08, Drawing Number 11789c8", dated 13th August 2021 (Appendix B).

In order to achieve this, a phased excavation, segregation, and export programme was followed along with the import of required aggregates to install the pile mats.

The work sequence broadly followed the phasing, as set out in the PRL Phasing Plan "101114 Project Bradford Bulk Excavation Phasing Plan Rev 3", dated 19th (Appendix C).

Soils were excavated by 360° Heavy Duty Excavators (HDEs) to formation on a grid square by grid square basis, the grid squares are as defined in the PRL Waste Classification Report, 101114/R002/02 dated 12th March 2020.

Any hard standing obstructions were broken out using a hydraulic breaker attachment, stockpiled and sent offsite for recycling.

A high-level piling mat was installed adjacent to the eastern, western, and southern boundaries with a number of ramps constructed, in order to allow piling works to continue. Once the piling works from the high level were complete, the high-level piling mats were excavated to the low-level pile mat formation levels.

Where required, excavations were battered at a suitable gradient as per the Temporary Works Design (Appendix O). Having been pre-classified during the Waste Classification Site Investigation, the excavated soils were transported by 30 tonne Articulated Dump Trucks (ADTs) to the central

stockpiling hard standing area of site, where they were segregated and stockpiled according to waste classification.

The stockpiles were managed and segregated by an onsite engineer with the use of dedicated stockpile signage, driver briefings and tracked using a Stockpile Tracker (See Appendix K), in compliance with the Material Management Plan (MMP). Soils were then loaded onto road going wagons for off-site disposal from this central stockpiling location.

The bulk excavation was undertaken between March and November 2021 and is presented in full in the PRL survey Formation Drawing (Appendix B).

During bulk excavation, there were a number of "soft spots" where further excavation was required in order to strengthen the formation level prior to pile mat construction. All soft spots, which were excavated and disposed of offsite, are presented in the "Soft Spot Drawing" (Appendix B).

2.3 Asbestos Protection Measures

Asbestos controls, mitigation and monitoring complied with the requirements of the PRL Asbestos Management Plan (AMP), the Control of Asbestos Regulations 2012 (CAR) and in accordance with best practice including CIRIA Report C733 Asbestos in Soils and Made Ground and JIWG CAR Soil Guidance 2016.

All asbestos related works were supervised on site by a suitable qualified PRL Engineer with asbestos air monitoring being undertaken regularly during works. All asbestos air monitoring results are presented in Appendix H and are summarised in Section 4.2.2 of this report.

No elevated concentrations of asbestos fibres were recorded during the works.

2.4 Discovery Strategy and Unexpected Contamination

Excavations were monitored under an environmental watching brief to ensure any unexpected contamination was identified and transferred a quarantine area, for further assessment prior to disposal, in accordance with the approved RSIP.

Soils impacted with visible fragments of asbestos cement sheeting were identified in the north-east section of site, in PRL Grid Section G2. These materials were quarantined prior to offsite disposal to a Provectus Hazardous Waste Treatment Facility at Edwin Richards Quarry, Rowley Regis.

In addition to the hazardous material previously identified in the pre works site investigations approximately 35m3 of made ground, suspected to be historical gasworks material, was segregated and sampled prior to disposal off site as hazardous. This approach was adopted to ensure that any unforeseen potentially hazardous material was identified and assessed prior to appropriate offsite disposal.

2.5 Import of Materials

There was a requirement to import construction materials including quarried aggregate for construction of the pile mats and surface water collection points onsite. Prior to import, all geotechnical certificates representative of the material, were issued to PRL to review against the material specification set within the BAM Pile Mat Design.

A summary of the importation of material onsite up to the end of the programmed works on 3rd December, is presented in Table 2. The full Import Log is presented in Appendix D, geotechnical results presented in Appendix J and import tickets presented in Appendix E.

Imported Material	Requirement	Loads No.	Quantity (m3)
Quarried MOT Type 1	Pile Mat	789	19,617
Quarried 6F5	Pile Mat	628	15,388
Quarried 10mm	Surface Water Works	3	57
Quarried 20mm	Surface Water Works	31	670
Quarried 75mm	Haul Roads for BAM	176	1584

Table 2 – Summary of Material Import from March 16th to 3rd December 2021

All imported material was stockpiled separately from the excavated waste material and signed appropriately. The aggregate used for the pile mat construction was imported as return loads for the non hazardous soils to minimise the number of wagon movements.

2.6 Pile Mat Installation

Following the bulk excavation to formation level, the base of the pile mat was surveyed by BAM and PRL engineers to ensure compliance to the Pile Mat Design. The complete asbuilt “Formation Level Drawing”, is presented in Appendix B.

Formation was proof rolled by a 13-tonne roller and the pile mats installed in layers using a combination of 6F5 and MOT quarried primary aggregate, in full accordance with the BAM design.

On completion of each completed pile mat area, the top of pile mat was surveyed with BAM and PRL to ensure compliance to the pile mat design. The complete asbuilt “Top of Pile Mat Drawing” is presented in Appendix B.

2.7 Plate Load Testing

PRL arranged for a competent third-party sub-contractor to undertake plate bearing tests on the top of the pile mats as per BAM instruction. These results and test locations are detailed in Appendix I.

2.8 UXO

In accordance with the UXO risk assessment an Unexploded Ordinance (UXO) watching brief was maintained on site during the excavation bulk works by a specialist sub-contractor. A pre works briefing was given to all site staff prior to commencing works. No evidence of UXO was identified onsite during the bulk earthworks. No suspected UXO's were identified during the works.

2.9 Perched Water and Surface Water Management

As identified in the BHE site investigations, the ground water table rests at circa 51m AOD, therefore groundwater was not expected nor was it encountered during the remediation works.

As part of the earthworks, surface water run-off and shallow perched water within the Made Ground being excavated was encountered. A surface water collection system was installed to prevent surface water run-off leaving site and to maintain a site free of standing water and suitable for earthworks:

The collection system comprised of channels containing pea gravel and perforated drainage pipe which fell to the northeast corner of site where they were directed to a collection sump and subsequently pumped to the onsite water treatment system prior to consented discharge to foul sewer.

Any surface water was to be treated to meet the requirements of the Discharge Consent and PRL Mobile Treatment Licence (See Appendix L).

The water treatment system comprised of the following components:

- Silt removal unit with oil/water separator – to remove larger suspended solids and free-phase hydrocarbons if present
- Sand filter – to remove finer suspended solids
- Granular activated carbon filter – to treat any dissolved phase hydrocarbon contamination
- Pumps as required

Photos of the groundwater treatment system are presented in Appendix P.

2.10 Mobile Treatment Licence

PRL successfully applied for consent to deploy their Mobile Treatment Licence (MTL) for the treatment of contaminated soils and water. A copy of the application and letter of consent are included in Appendix L.

Pollution control measures and a schedule of environmental monitoring established in the MTL deployment documentation, were adhered to throughout the PRL works.

Works were regularly inspection by a COTC WAMITAB Professional during screening and surface water processing works to ensure compliance with the MTL.

2.10.1 Soil Screening

Excavated materials were screened (including soils with hydrocarbon impact) to remove oversize concrete and brick prior to offsite disposal. The aim of the soil processing was to remove the oversize fraction for further processing to recycled aggregate and allow disposal of the balance of made ground.

A total of 576m3 of recycled aggregate was screened and disposed of offsite to Ashton Old Road Recycling Facility, See Section 4.

3 ENVIRONMENTAL MANAGEMENT AND CONTROL

3.1 Environmental and Health and Safety Management Overview

PRL ensured that their contract works were compliant with the RMS/RSIP and AMP at all times.

PRL engineer supervision included the following:

- Maintaining records of site activities throughout the project
- Supervision of remedial excavation as part of the Discovery Strategy
- Ensuring adherence with the AMP and Mobile Treatment Licence
- Management of waste consignment

3.2 Environmental Control and Monitoring

3.2.1 Dust

PRL established dust deposit gauges at 4 No. Boundary Monitoring Points (BMP) on the site boundary, to monitor dust production on a monthly basis during contracted remediation works (See “in Appendix B). Daily inspections of dust generation were undertaken and recorded in the Daily Environmental Monitoring Forms (Appendix G).

Dust suppression was undertaken to mitigate the potential for dust generation throughout the works. The location of the fixed monitoring points was reviewed as the works progressed to ensure representative samples were recovered.

Based on the Environment Agency M17 guidance a value of 200mg/m^2/day is to be used as a trigger level.

It should be noted that during the period of reporting there has been a lot of activity in close proximity to the site boundary with multiple piling operations and associated attendant plant. Further to this, concreting and associated excavation activities have also been carried out along the site boundary.

A number of mobile atomiser units were positioned at suitable locations throughout site works, including on-site haul routes, excavation areas and stockpiles. In addition, BAM provided supplementary dust control measures including water tankers with trickle bars.

Elevated dust concentrations were recorded on a number of occasions during the site works across all boundary monitoring points, these are summarised in Table 1.

Dates of Measurement	Results mg/m2/day	Comment
14.05.2021 - 11.06.21	BMP1 – 950, BMP2 – 1500, BMP3 – 1200, BMP4 - 570	High activity in close proximity to site boundary with multiple piling operations and heavy plant in operation. Consistently dry with little to no precipitation
11.06.21 – 12.07.21	BMP1 – 800, BMP2 –3800, BMP3 – 620, BMP4 - 360	High activity in close proximity to site boundary with multiple piling operations and heavy plant in operation. Consistently dry with little to no precipitation
12.07.21-13.08.21	BMP2 –230, BMP3 – 520, BMP4 - 640	Heavy plant in operation around site boundaries. Consistently dry with little to no precipitation
13.07.21-13.08.21	BMP1 –520, BMP2 –200, BMP3 –350	Heavy plant in operation around site boundaries. Consistently dry with little to no precipitation
13.08.21-17.09.21	BMP1-530, BMP2- 200, BMP3- 300	Heavy plant in operation around site boundaries. Consistently dry with little to no precipitation
17.09.21-16.10.21	BMP2 – 490, BMP4-70	Heavy plant in operation around site boundaries. BMP2 and BMP4
16.10.21-12.11.21	BMP4-230	Marginal exceedance during heavy plant operations around BMP4

Table 1 – Exceedances' of Quantifiable Dust

Following exceedances and throughout exceptionally dry periods, further mitigation measures were introduced to manage the dust on site. This included additional mobile atomisers and mobile water bowsers to manage and mitigate the impact of nuisance dust.

It is to be noted that the dust did not migrate in large quantities beyond the Boundary Monitoring Points (BMP) and remained mainly on site around the areas of where site traffic is most prevalent.

3.2.2 Asbestos Air Emissions

Airborne asbestos reassurance monitoring was undertaken weekly by Fourstage Environmental Ltd during the bulk excavation works to monitor the background respirable fibre concentrations and to implement any control measures necessary to reduce the risks to workers onsite if necessary.

Throughout the works a total of 32 visits were undertaken between March and November. Background concentrations did not exceed 0.01 fibres/cm^3, which is 10% of the HSE control limit for asbestos working.

All asbestos air monitoring records are presented in Appendix H.

3.2.3 Volatile Organic Compounds

During the excavation and disposal works PID monitoring was undertaken at all boundary monitoring points on a daily basis, to ensure volatile contaminants were below 8 hr time weighted average levels described in EH40 publication. The monitoring used a reference compound of benzene as this has the most stringent criteria of the hydrocarbons present in soil. The benzene limit for the works was 1ppm.

PID monitoring confirmed that Volatile Organic Compound (VOC) concentrations did not exceed the trigger level of 1ppm throughout the works on site.

Additional PID monitoring was undertaken when strong hydrocarbon odours were detected from pile arising stockpiles; with no exceedances over the 1ppm limit recorded.

All VOC monitoring records are presented in the Daily Environmental Monitoring Forms, found in Appendix G.

3.2.4 Noise

Noise monitoring was undertaken at all boundary monitoring points on a daily basis, with the average and peak being recorded during site works to give a true and accurate representation of site activities being conducted, for 15-minute intervals. The trigger level for the noise monitoring is 85 dBa.

This trigger was exceeded once on 16.04.2021 at BMP4 whilst sheet piling works were taking place adjacent to this monitoring point. Task specific PPE (Ear Defenders) were worn at all times by the Piling contractors to reduce risks of hearing damage.

All mobile plant was equipped with appropriate noise insulation and working hours were limited to those specified in the planning consent.

PRL did not receive any noise complaints during the works.

All noise monitoring records are presented in the Daily Environmental Monitoring Forms, found in Appendix G.

3.2.5 Wheel Washing

Throughout the material transfer off site, haulage wagons were trafficked on hardstanding/tarmac areas to reduce the spread of debris offsite. In addition during periods of wet weather a combination of jet-wash bowsers and road sweepers were utilised to reduce off site migration of soils on the highway.

This was implemented successfully, with no complaints recorded of mud on the roads.

3.2.6 Further Pollution Prevention and Control Measures

Throughout the bulk excavation works, all fuel bowsers were double bunded with spill kits installed under all parked machinery and fuelling points to mitigate any potential hydrocarbon impact to shallow soils and surface water.

3.3 Traffic Management

With regular wagons entering and exiting the site on a daily basis, the access and egress points were carefully managed between the BAM and PRL Traffic Marshalls to maintain high levels of health and safety to site personnel and the general public.

Onsite traffic was managed by PRL banksmen at all times, to control plant movements and ensure wagons were loaded safely. Daily site meetings were held by BAM and all sub-contractors to discuss pedestrian segregation and plant/vehicle haul routes.

3.4 Odour Control

Hydrocarbon odours were detected from pile arising stockpiles generated by the piling works and when excavating contaminated soils from the made ground. Reassurance PID monitoring was carried out on these occurrences and on no occasion did PID readings exceed trigger levels of 1ppm.

Evidence of this additional PID monitoring is detailed in the Daily Monitoring records found in Appendix G.

4 WASTE MANAGEMENT AND MATERIAL TRACKING

All materials surplus to requirements were characterised as waste and consigned for disposal at suitably licensed facilities. A waste classification exercise was completed prior to commencement of the main works. The classification of waste was completed in accordance with the below:

- 'The Landfill (England and Wales) Regulations 2002 with 2004 & 2005 Amendments'
- 'Hazardous Waste (England and Wales) Regulations'
- 'Framework for the Classification of Hazardous Waste'
- 'EA Technical Guidance Note WM3. Hazardous Waste: Interpretation of the definition and classification of Hazardous waste' (v1.1 26 June 2018)
- 'The List of Waste Regulations 2005'
- 'European Classification, Labelling and Packaging of Chemicals Regulations 2009' and 'Adaptations to Technical Progress (ATPs)'
- 'Revised European Waste Catalogue'

Materials were classified, excavated, segregated, and stockpiled in a central stockpile area determined by their waste classification:

- 170504 - Non Hazardous soil and stones
- 170503 - Hazardous containing asbestos >0.1% fibres and or visible asbestos fragments (ACM)
- 170503 - Hazardous containing elevated hydrocarbon concentrations
- 170107 - Non Hazardous concrete and bricks
- 170302 - Asphalt

Details of the waste classification exercise and QA sampling can be found in Section 2.1

Details of the sampling and results are shown in the Sample Tracker Form (Appendix J), Stockpile Record Form (Appendix K), Material Tracker (Appendix K) and soil sample results (Appendix J).

All waste transfer tickets are listed in the Waste Disposal and Import Summary Log, presented in Appendix E and presented in Table 3.

Type of Material Disposal	Volume	Disposal Site
Non-hazardous soils	116,721m3	Fletcher Bank Quarry Landfill Buckton Vale Quarry Woolston Deposit Ground
Hazardous soils (Hydrocarbons)	7,455m3	Maw Green
Hazardous soils (Asbestos)	433m3	ERQ
Concrete/Hard Materials/Asphalt	576m3	Ashton
Total	125,215m3	

Table 3 - Disposal Summary

4.1 Material Tracking

Effective stockpile management was provided to achieve waste type segregation and traceability of the waste from grid square to off-site disposal facility.

All excavated material was tracked from each grid square, stockpile location to offsite disposal, via the Material Tracker. The Material Tracker and Stockpile Tracker is presented in Appendix K with weekly surveys presented in Appendix F.

4.2 Materials Management Plan

Provectus produced a CL;aire DoW Materials Management Plan (MMP) for the site which allows the re-use of geotechnically and chemically suitable soils in the temporary batters re-engineered to support the tiered pile mats as well as the use of site won aggregates in the pile mats and working platform.

The Materials Management Plan (MMP) is presented in Appendix M.

4.3 Re-Use

Material was re-used where it is suitable in accordance with the MMP/RMS. This reduced requirements for imported material thereby reducing vehicular movements to and from site and the associated emissions as well as meeting the requirements of the waste hierarchy and saving costs. This was demonstrated by chemical and grading testing on a one sample per 250m^3 basis.

This re-use accounts for the placement of site won aggregate in the pile mat for the first phase of piling to them be subsequently re-used again in the next phase of pile mat installation.

Soil samples were taken of 6F5/Type 1 for grading and chemical analysis against the pile mat specification and reuse criteria respectively.

A summary of the reuse samples are presented in Table 4 with the full geochemical laboratory test results presented in Appendix J.

Samples	Material Type	Sample Date	Quantity (m3)	Pass Reuse Criteria and Grading requirements
SP2 – SP2	6F5	22.04.21	80	Yes
SP4 – HLM/A2	6F5	22.06.21	200	Yes
SP5 - HLM/A3, A4, A5, A6, A7	6F5 and Type 1	05.07.21	615	Yes
SP6 – HLM/G2, G7, E7, F7	6F5	15.07.21	289	Yes
SP8 - LLMF2/01, LLMF2/02, SOUTHRAMP/01, SOUTHRAMP/02	6F5 and Type 1	12.11.21	112	Yes
Total			1296	

Table 4 – Summary of Reuse Material

A total of 1,296m3 was recovered from the high-level piling mat and engineered ramp systems, segregated, sampled, and successfully reused onsite within the low-level pile mats.

5 OTHER REMEDIATION REQUIREMENTS

Prior to major bulk excavation works, 8 No. boreholes were monitored and decommissioned.

Details of the decommissioning is presented in Table 4, with the full decommissioning Logs presented in Appendix N.

Borehole	Actual (m)		m3	Comment
	Depth			
	Borehole 1	Borehole 2	Borehole Volume	
BH19/02A	49.5	17.55	Lost	Lost
BH19/03	29.71	N/A	Lost	Lost
	20.85			Decommissioned
BH19/05	50	Only 1 pipe	0.041	31.03.21
BH19/07C	23.1			Decommissioned
Diameter	35mm	Only 1 pipe	0.031	30.03.21
BH19/09	42.6	14.1		Decommissioned
Diameter	35mm	35mm	0.074	29.03.21
BH19/11	24.7	14.5		Decommissioned
Diameter	35mm	50mm	0.06	31.03.21
BH19/13	8.75	26.2		Decommissioned
Diameter	35mm	35mm	0.043	29.03.21
BH19/15	41.8	12.5		Decommissioned
Diameter	35mm	50mm	0.078	07.04.21
BH19/17	15.1	25.1		Decommissioned
Diameter	35mm	35mm	0.013	07.04.21
BH19/14	28.3			Decommissioned
Diameter	35mm	Only 1 pipe	0.044	07.04.21
Total			**0.384**	

6 COMPLETION AND HANDOVER

6.1 Phased Handover of Site Areas

The Inspection Test Plan (ITP) formed the basis of each area handover to BAM following completion of the Pile Mats.

Each area handover form contained the following information, which was issued to BAM prior to approval and acceptance of the areas:

- Formation level on a grid-by-grid basis; - Appendix B
- Geotechnical grading certificates of imported stone is presented in Appendix Q with reused stone geotechnical certificates presented in Appendix J and confirmation of placement/compaction methodology
- Top of pile mat level – Appendix B

All area handover forms were signed by PRL and BAM representatives prior to piling works commencing.

6.2 Materials Management Plan Validation

The works were undertaken compliantly, in line with the PRL MMP and the approved Remediation Strategy including all appropriate chemical/geotechnical testing of materials during the reuse of site won material.

The appendices for the MMP are presented in Appendix M of this report.

6.3 Validation Summary and Conclusion

PRL have consigned all excavated soils compliantly, in accordance with the RSIP and provided BAM with piling mats in line with the BAM piling mat designs.

APPENDIX A Report Conditions


This report is produced solely for the use of BAM Construction Limited and no liability is accepted for any reliance placed on it by any other party unless specifically agreed in writing otherwise.

Some of the opinions are based on unconfirmed data and information and are presented as the best that can be obtained without extensive research. Provectus accepts no responsibility for data provided by others.

Provectus does not assume any liability for misrepresentation of information or for items not visible, accessible, or present on the subject site at the time of the site reconnaissance.

All recommendations made are subject to any relevant statutory regulations in force concerning design methods and safe construction practice.

APPENDIX B Drawings

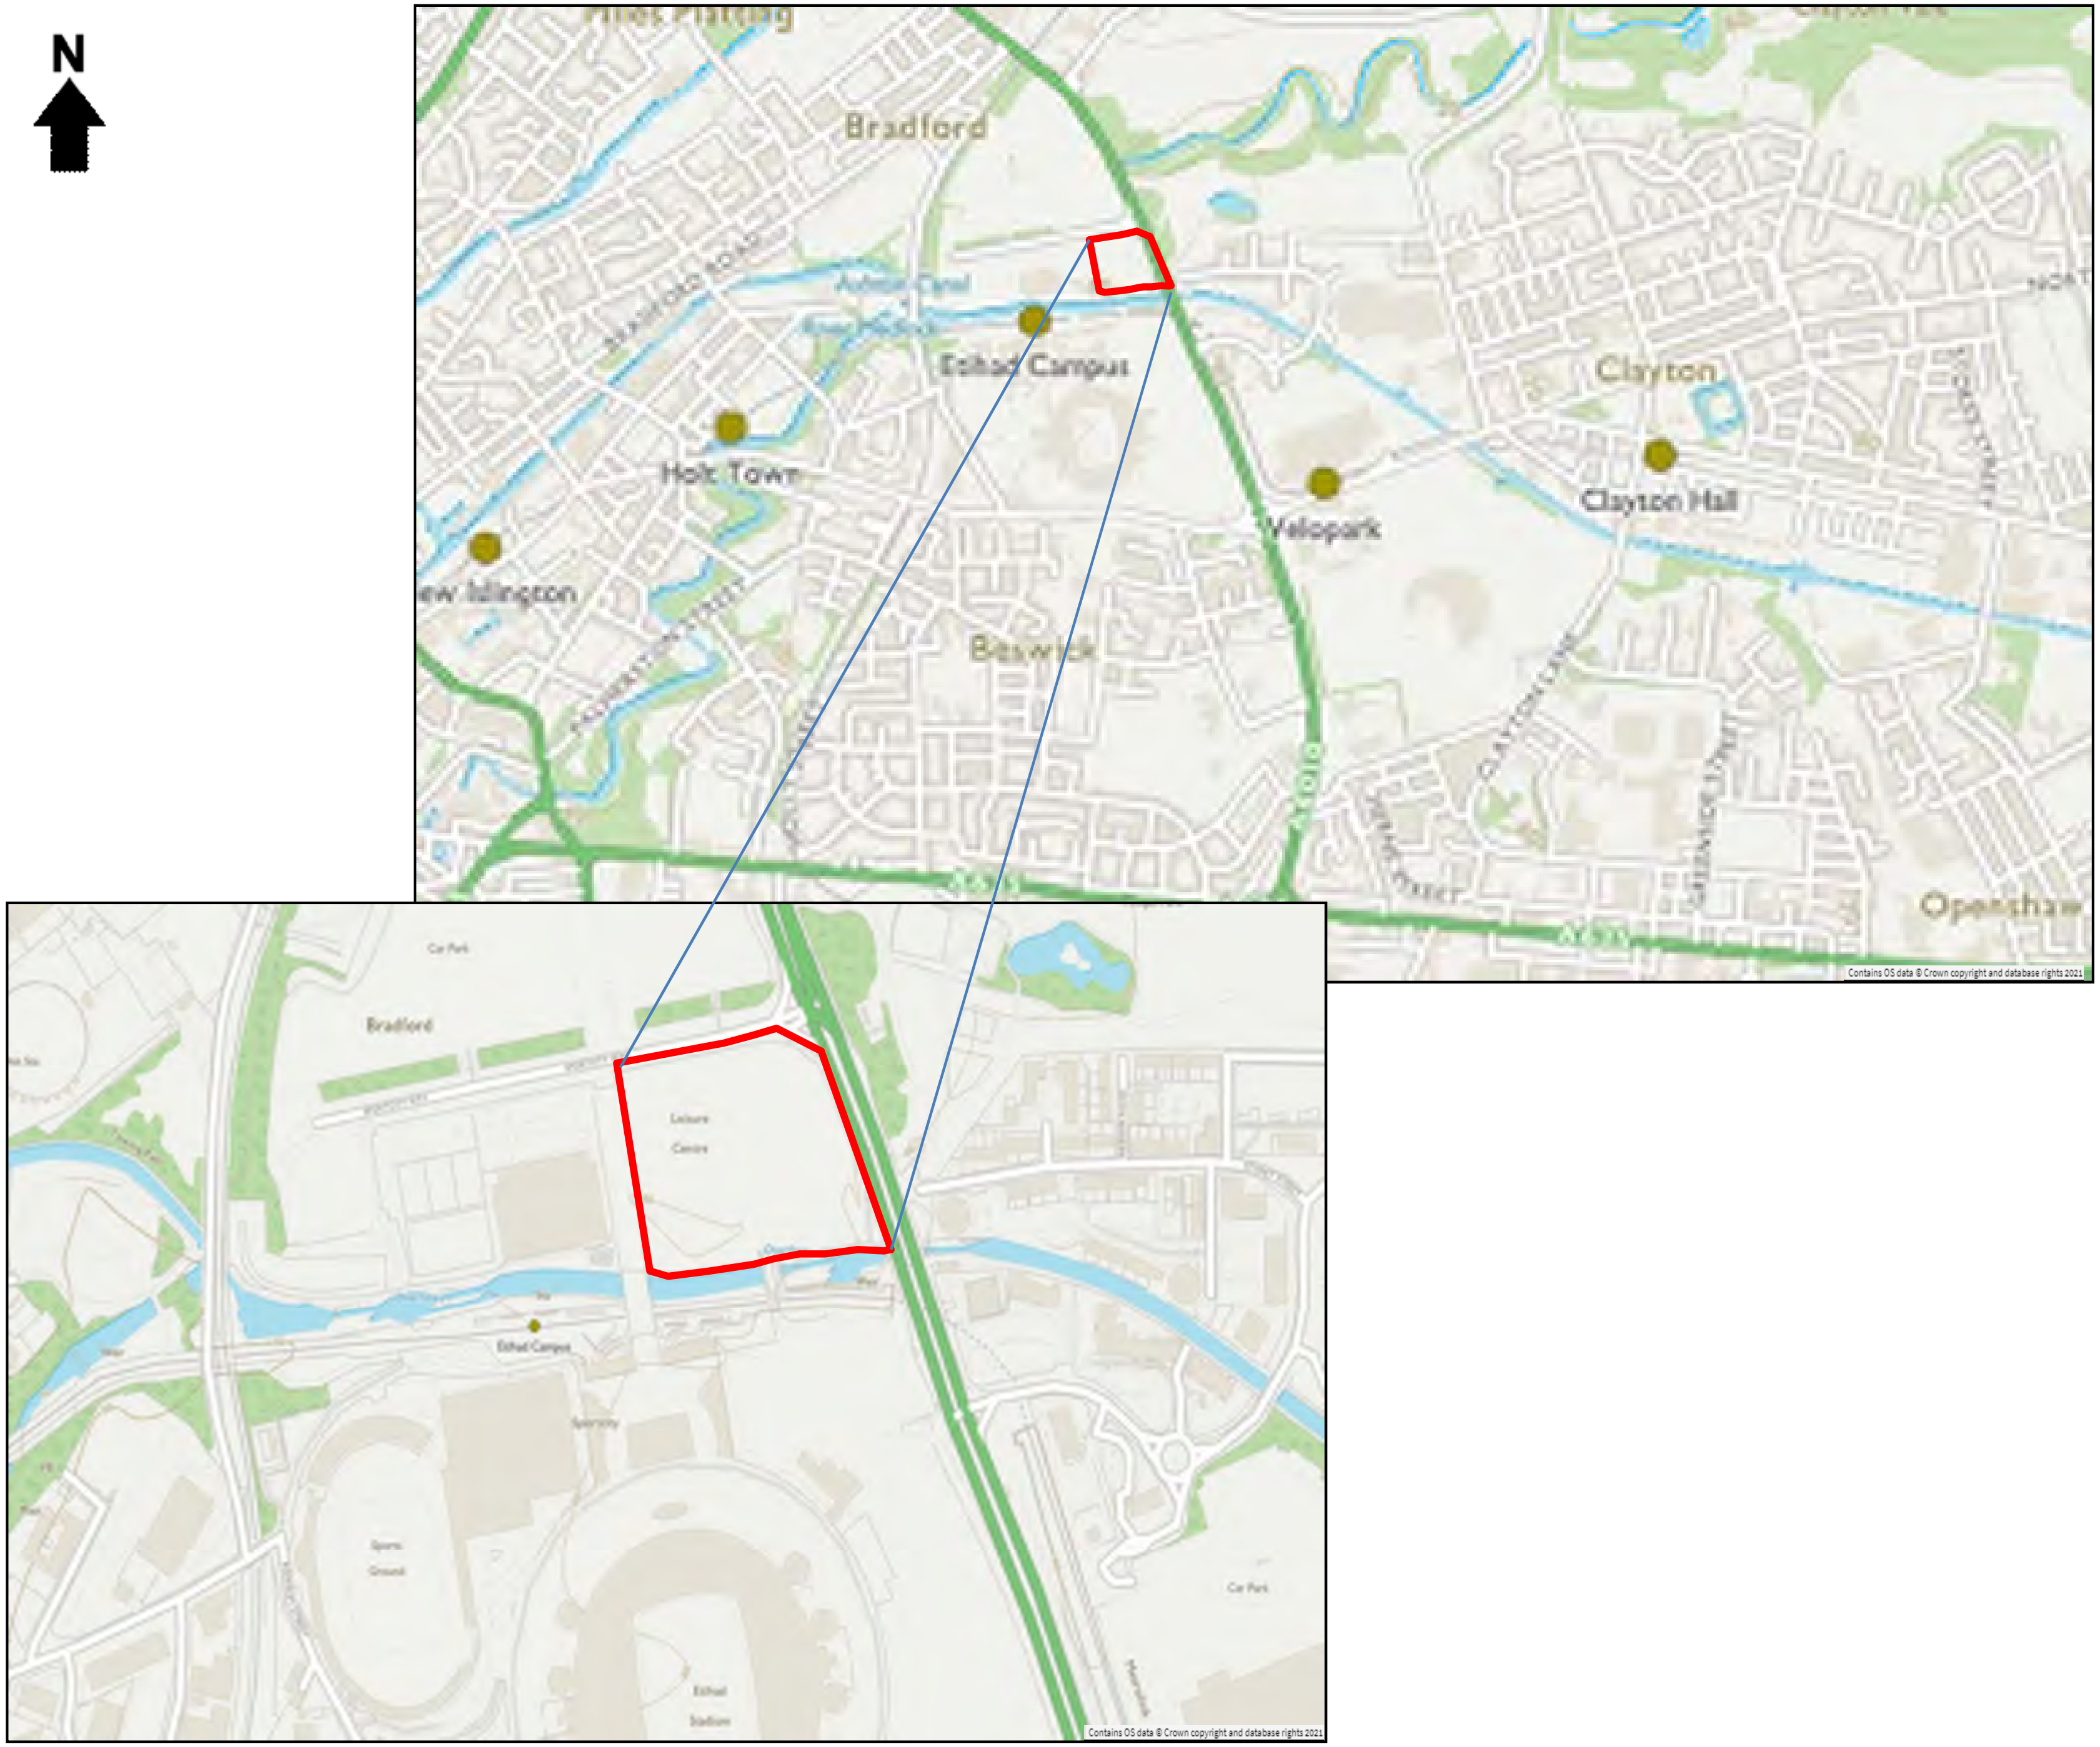

Site Boundary

PROVECTUS

Provectus Remediation Ltd
9 Kingsdale Business Centre
Regina Road
Chelmsford
Essex
CM1 1PE

Tel. 01245 505 600
www.provectusgroup.com

Client: BAM

Project: 101114 Project Bradford


Job No.: **101114**

Title: Site Location Plan

Scale: NTS

Date Drawn: 05/01/2021 **Drawn By**: SLR

Sketch No.: SK101114/ 01

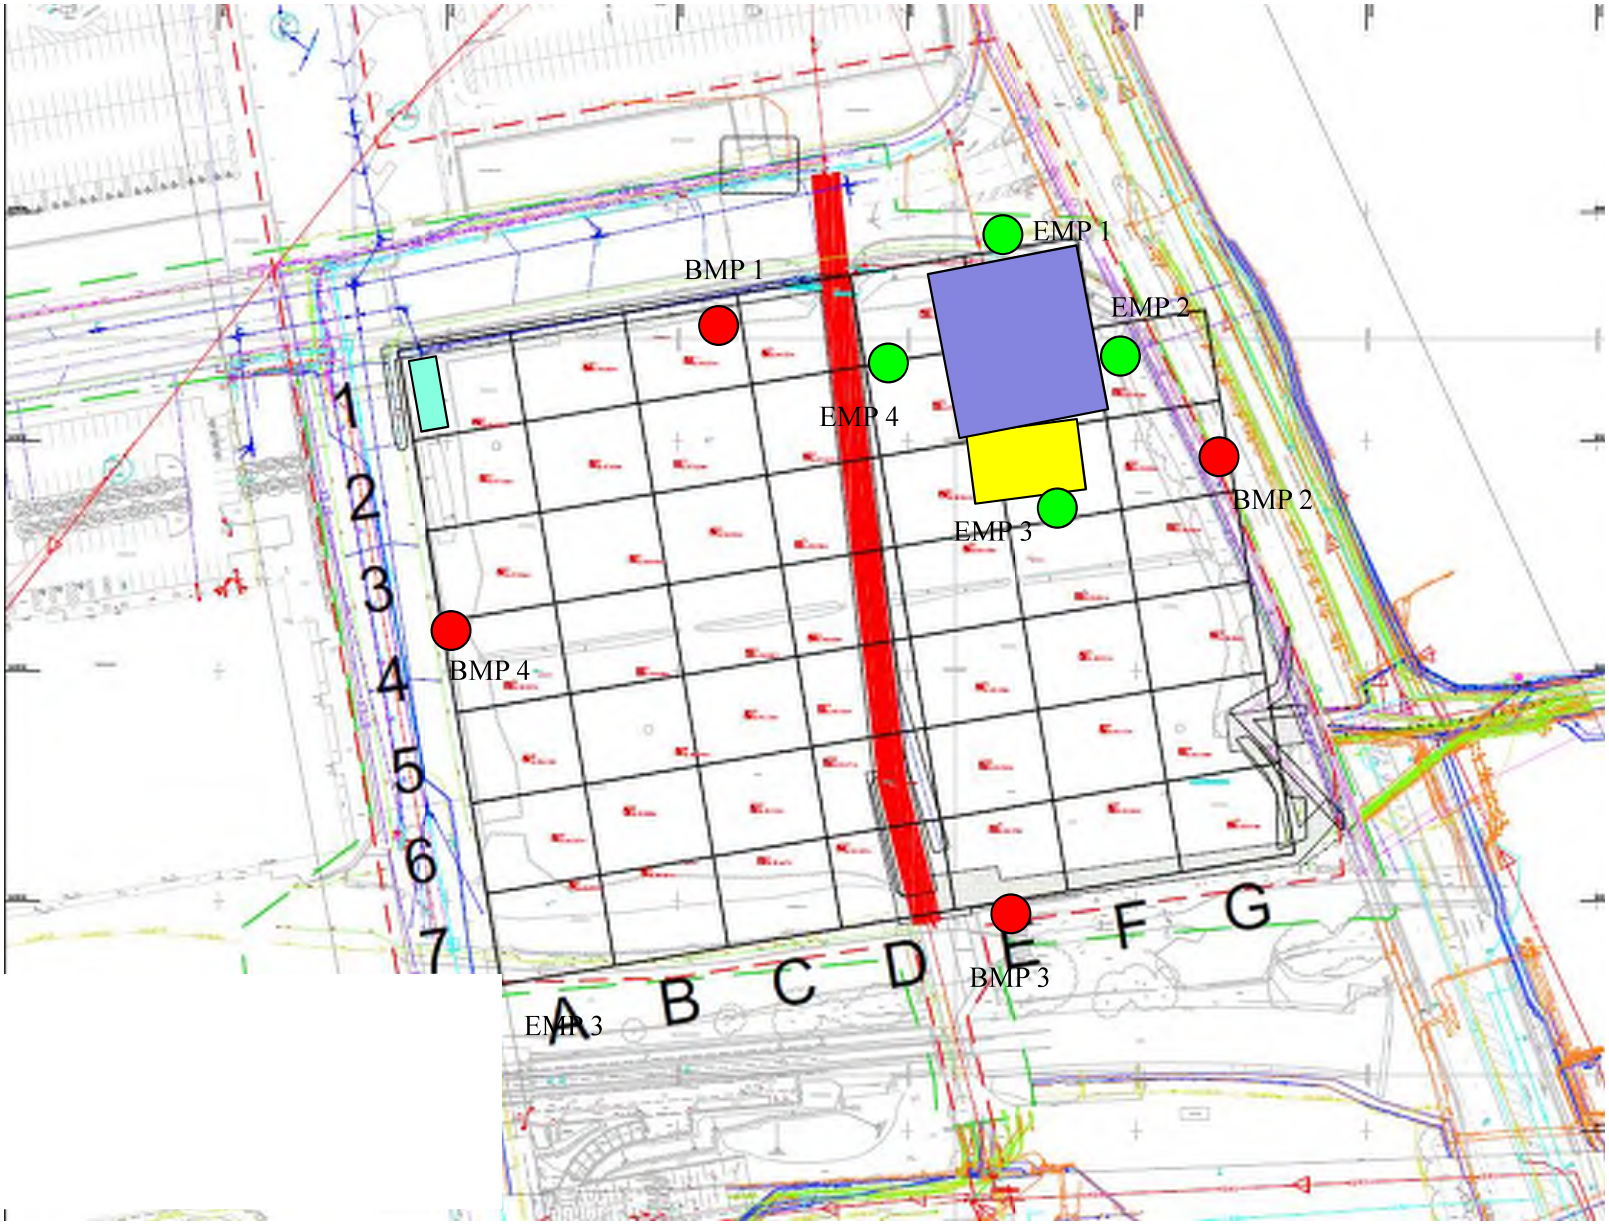

Soil Treatment Area

Quarantine Area

Environmental Monitoring Point

Boundary Monitoring Point

Water Treatment Area

PROVECTUS

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Tel. 0118 988 0200
www.provectusgroup.com

Client: BAM Construction

Project: Project Bradford


Job No.: 101114

Title: Remediation Works – Treatment Areas and Monitoring Points

Scale: NTS

Date Drawn: July 2020

Drawing No.: Figure 4 101114STA -1

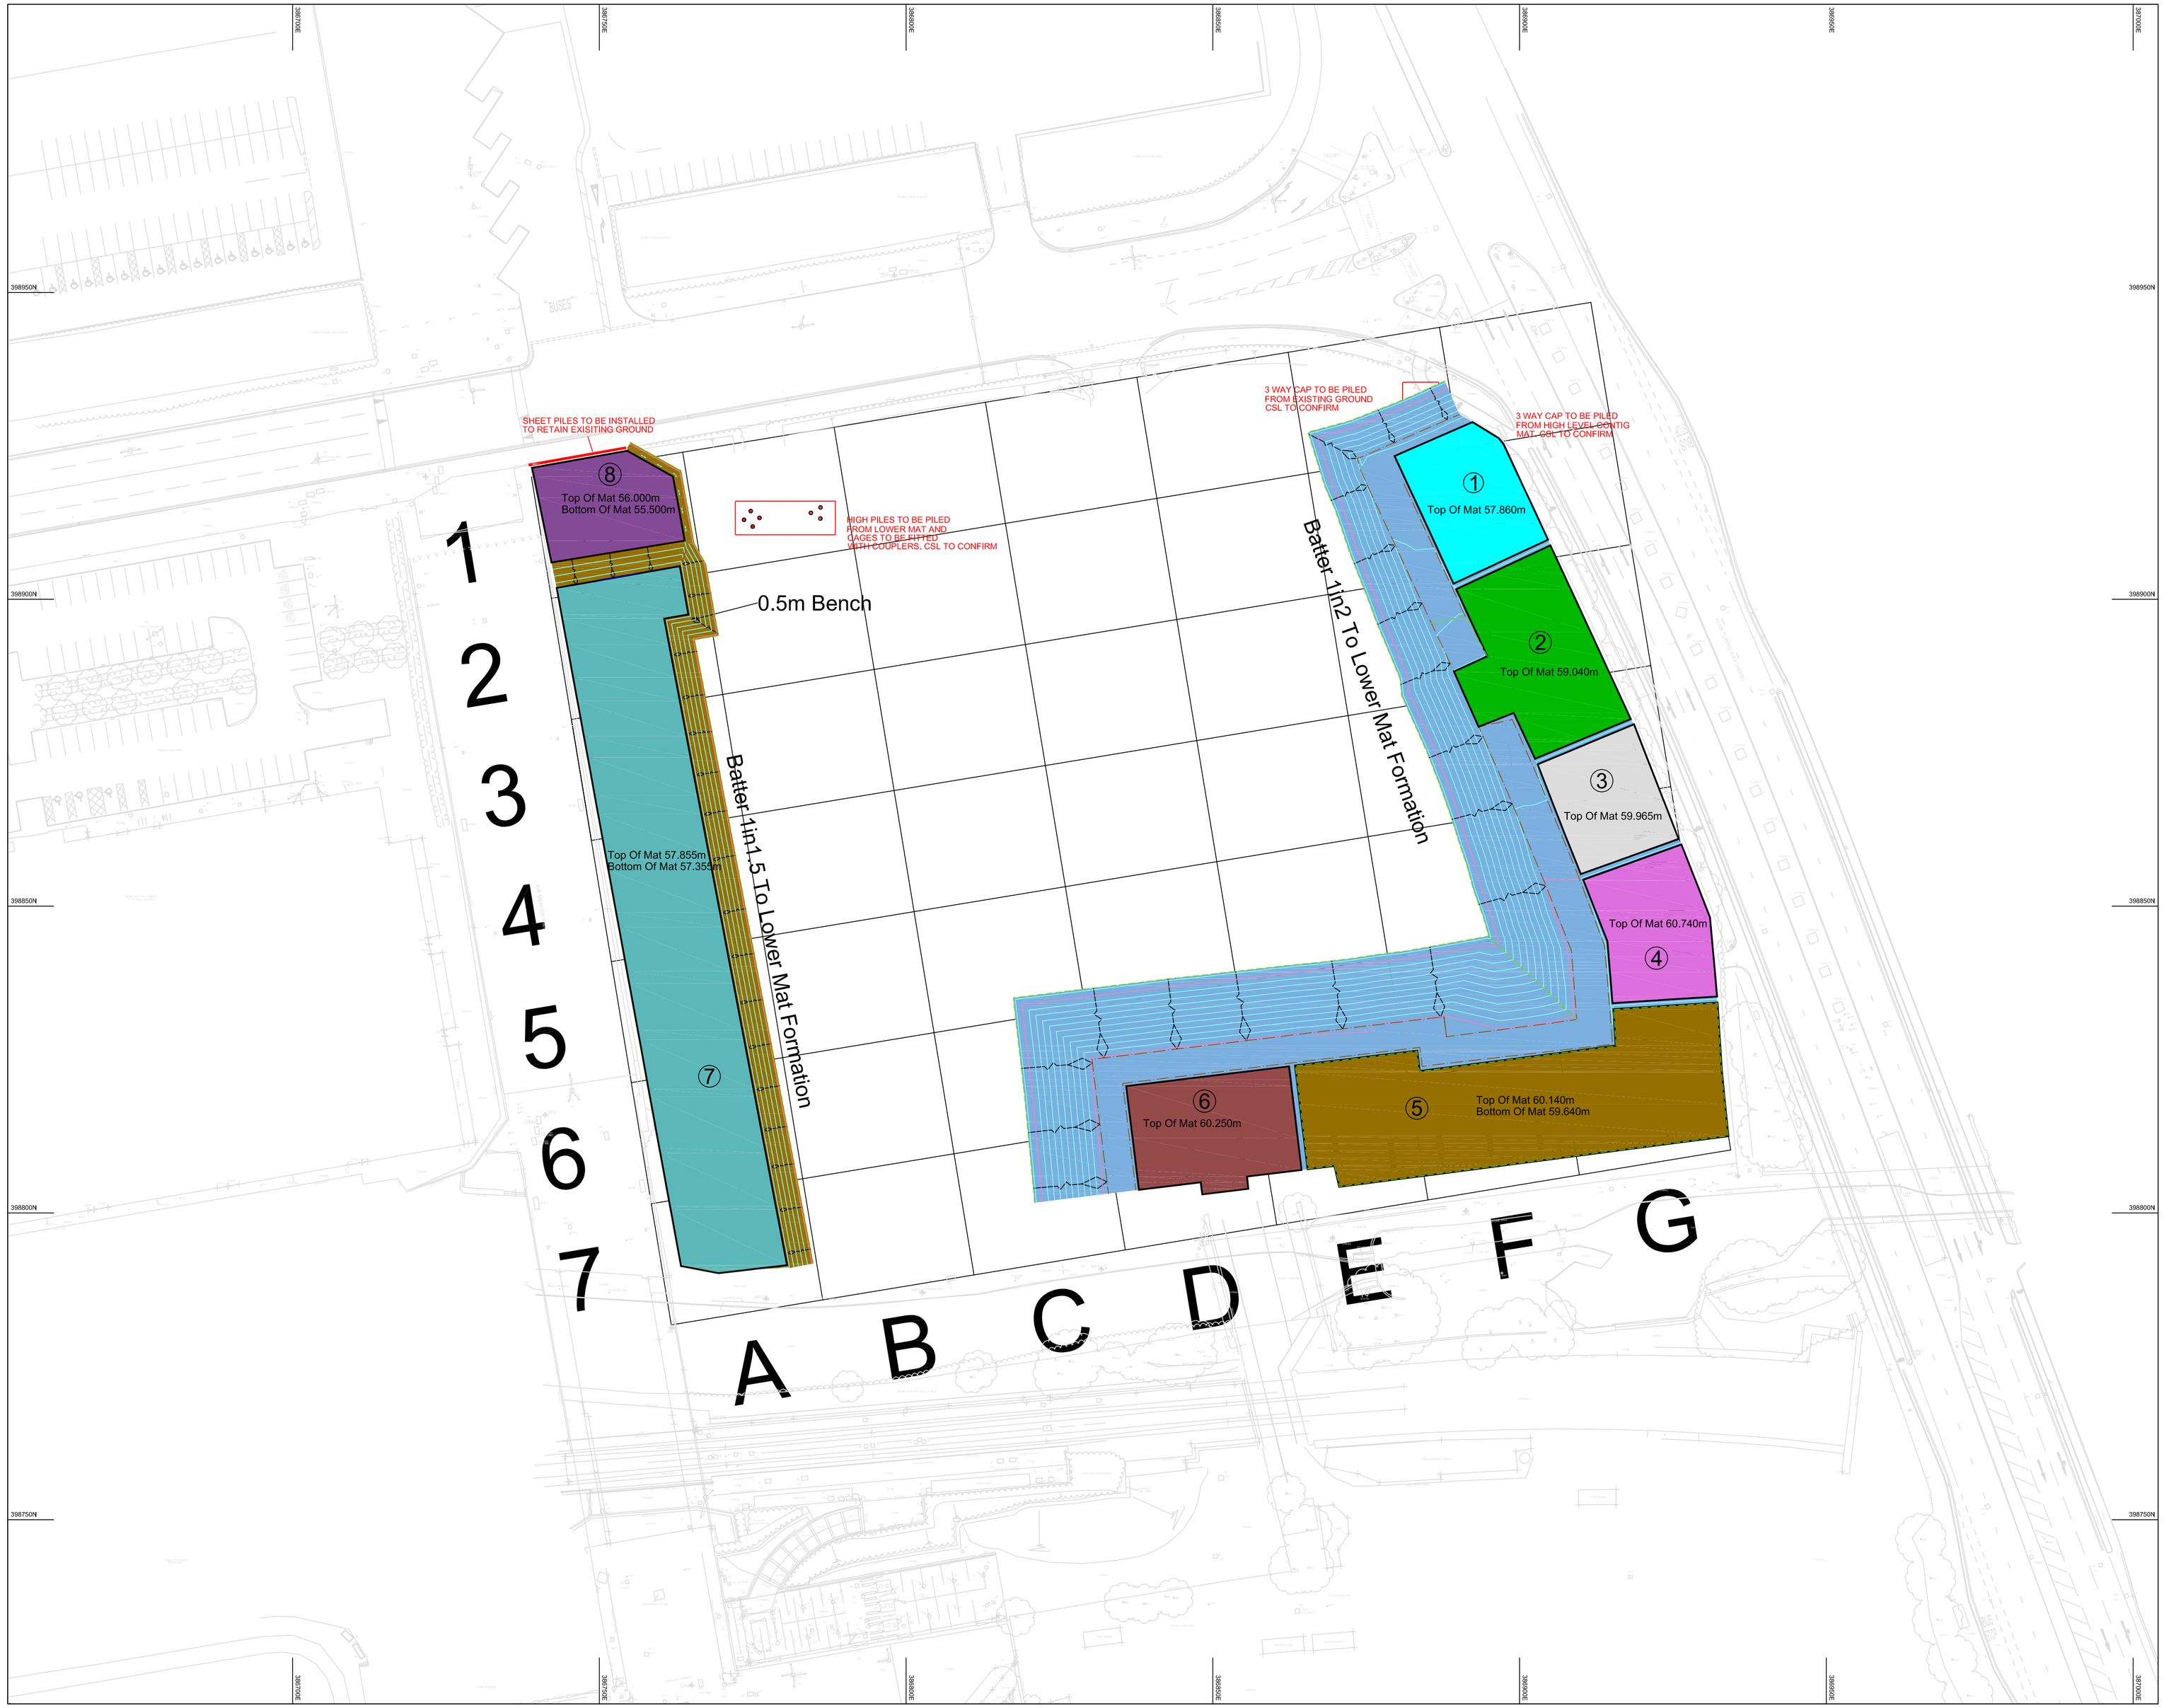

stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 · F 01284 584844 · E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordInates : SITE GRID

1
2
3
4
5
6
7
8

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

High Level Mat
(SITE GRID 20m x 25m)

SCALE


1:500 @ A1

DATE

23/04/2021

DRAWING No.

11559a-5

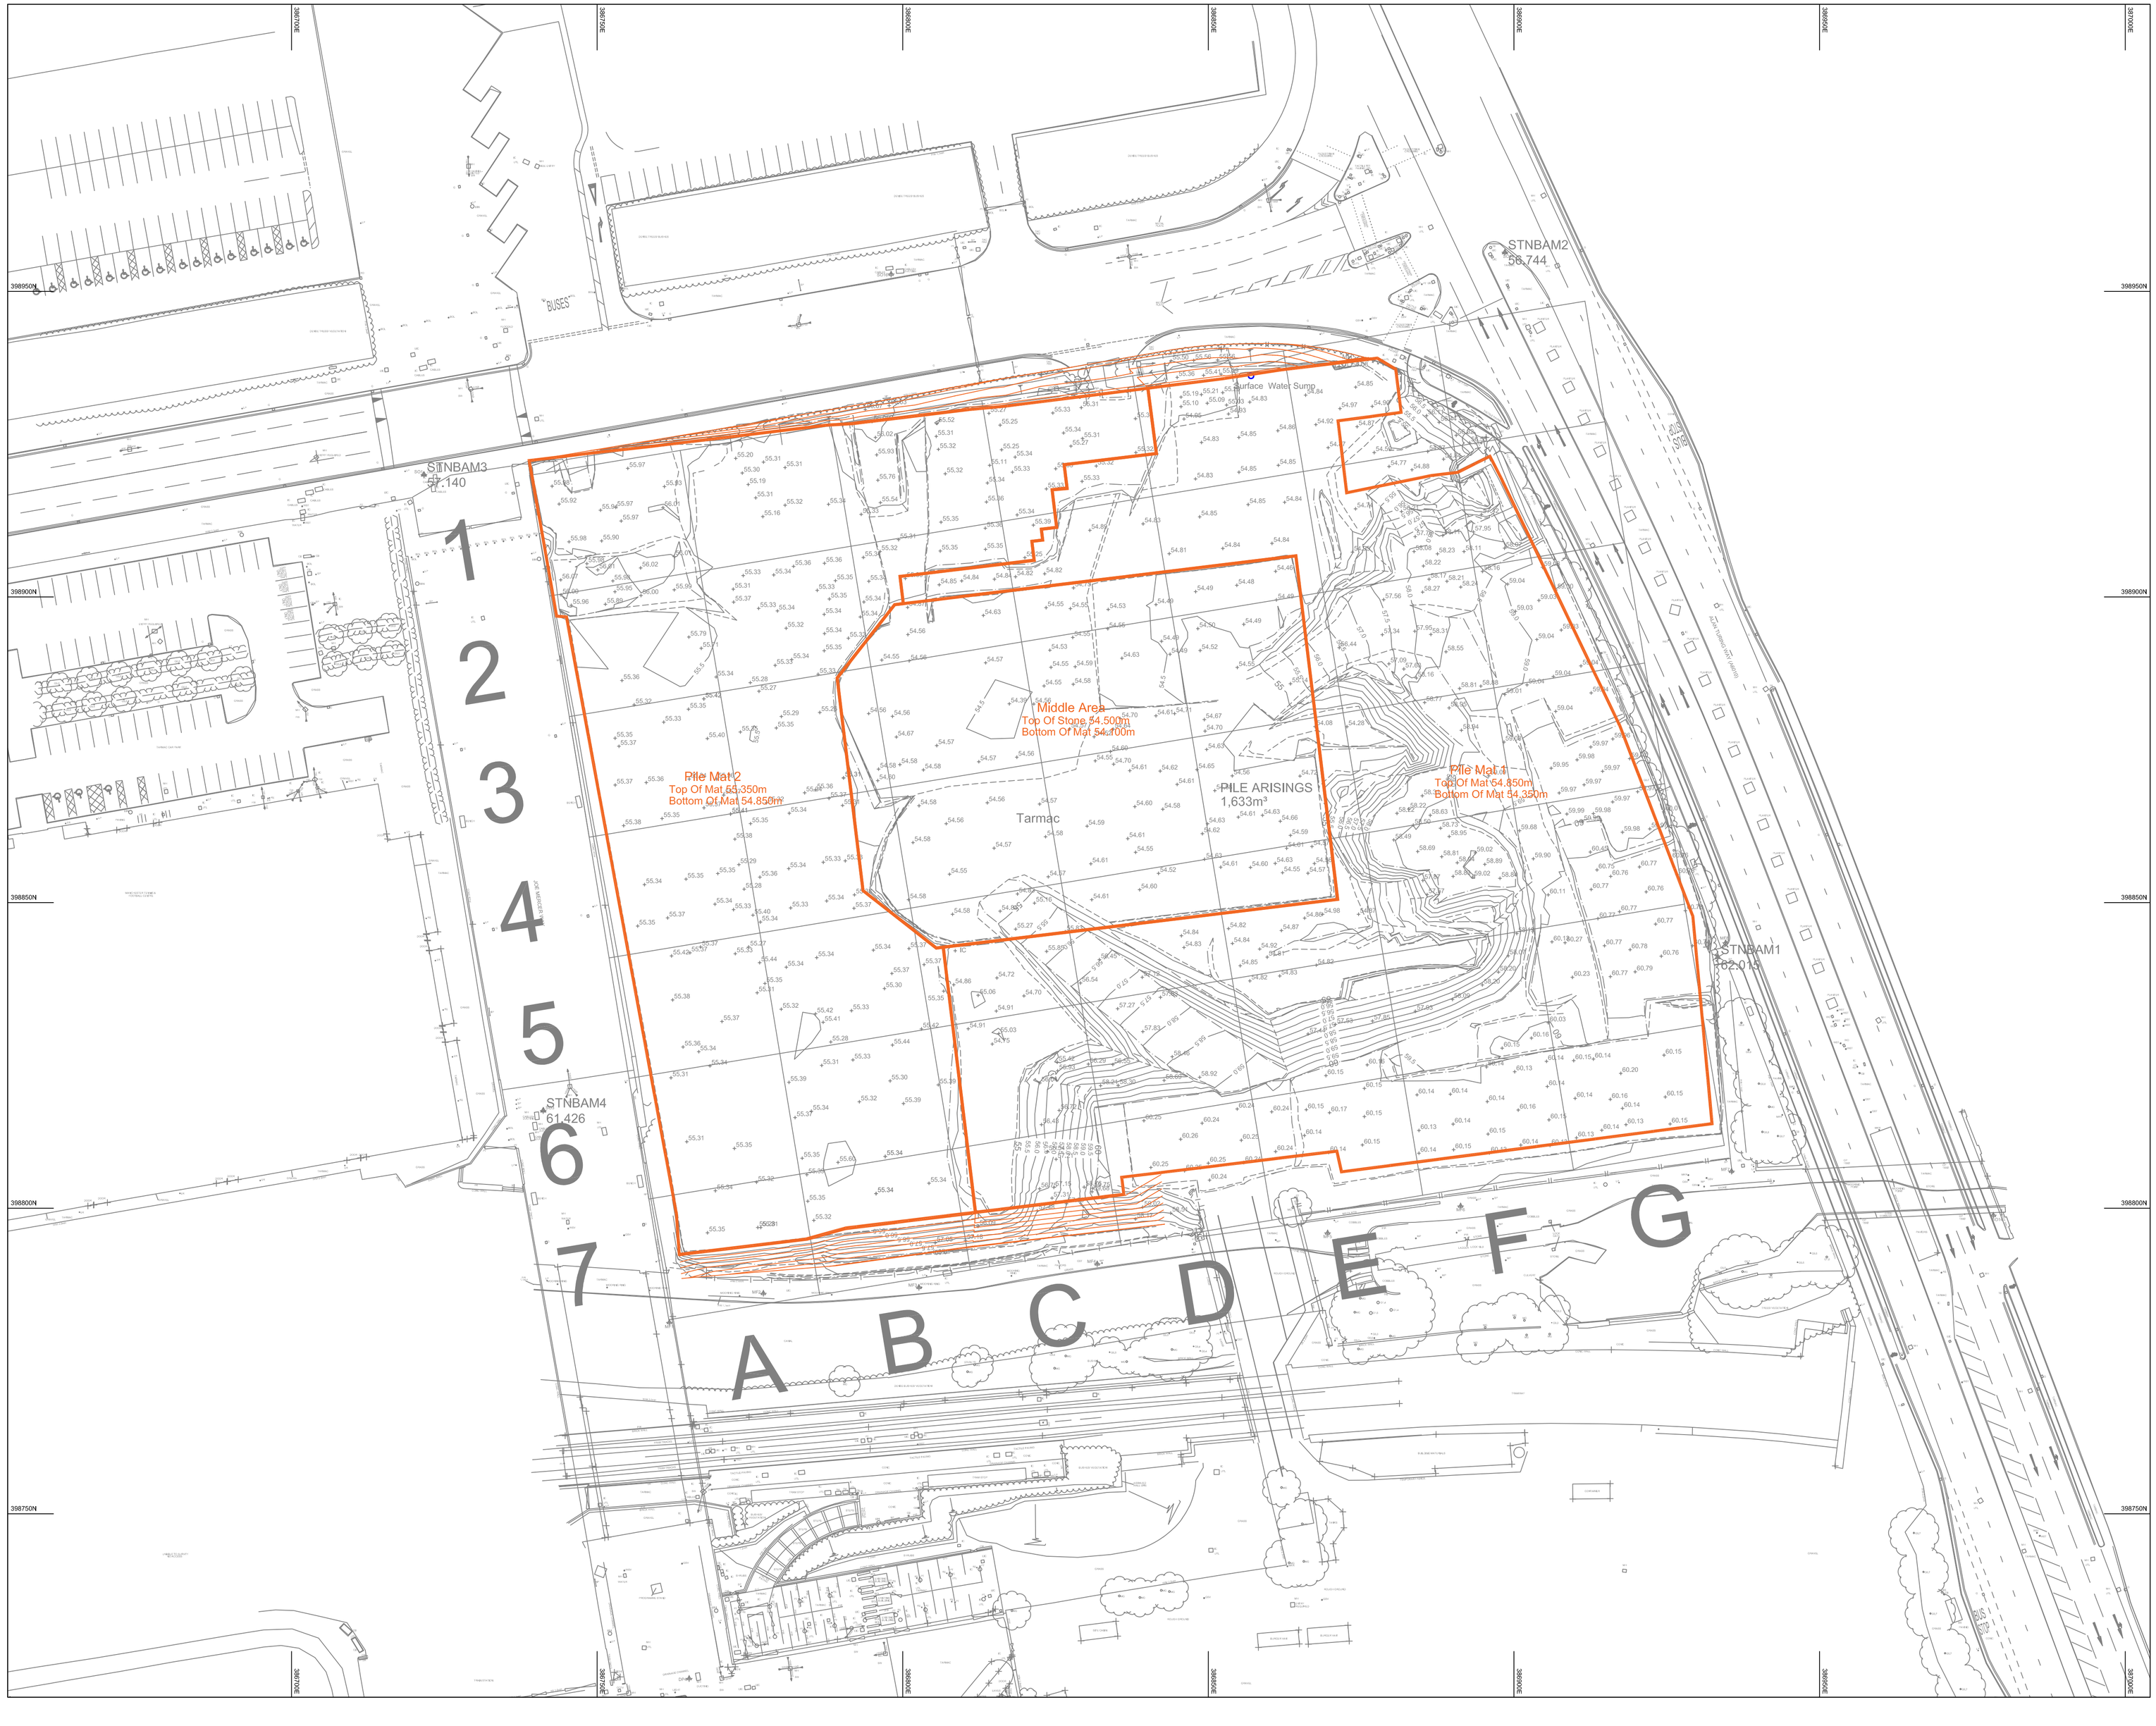

stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 > F 01284 584844 > E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordinates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.420

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

Site Survey 13-08-2021
Low Level Rev.8 Design

SCALE	DATE
1:500 @ A1	13/08/2021

DRAWING No.

11789c-8



stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 F 01284 584844 E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordInates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.063	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114


PROJECT

As Built Formation Survey
Low Level Area

SCALE	DRAWING DATE
1:500 @ A1	16/12/2021

DRAWING No.

12037a-1

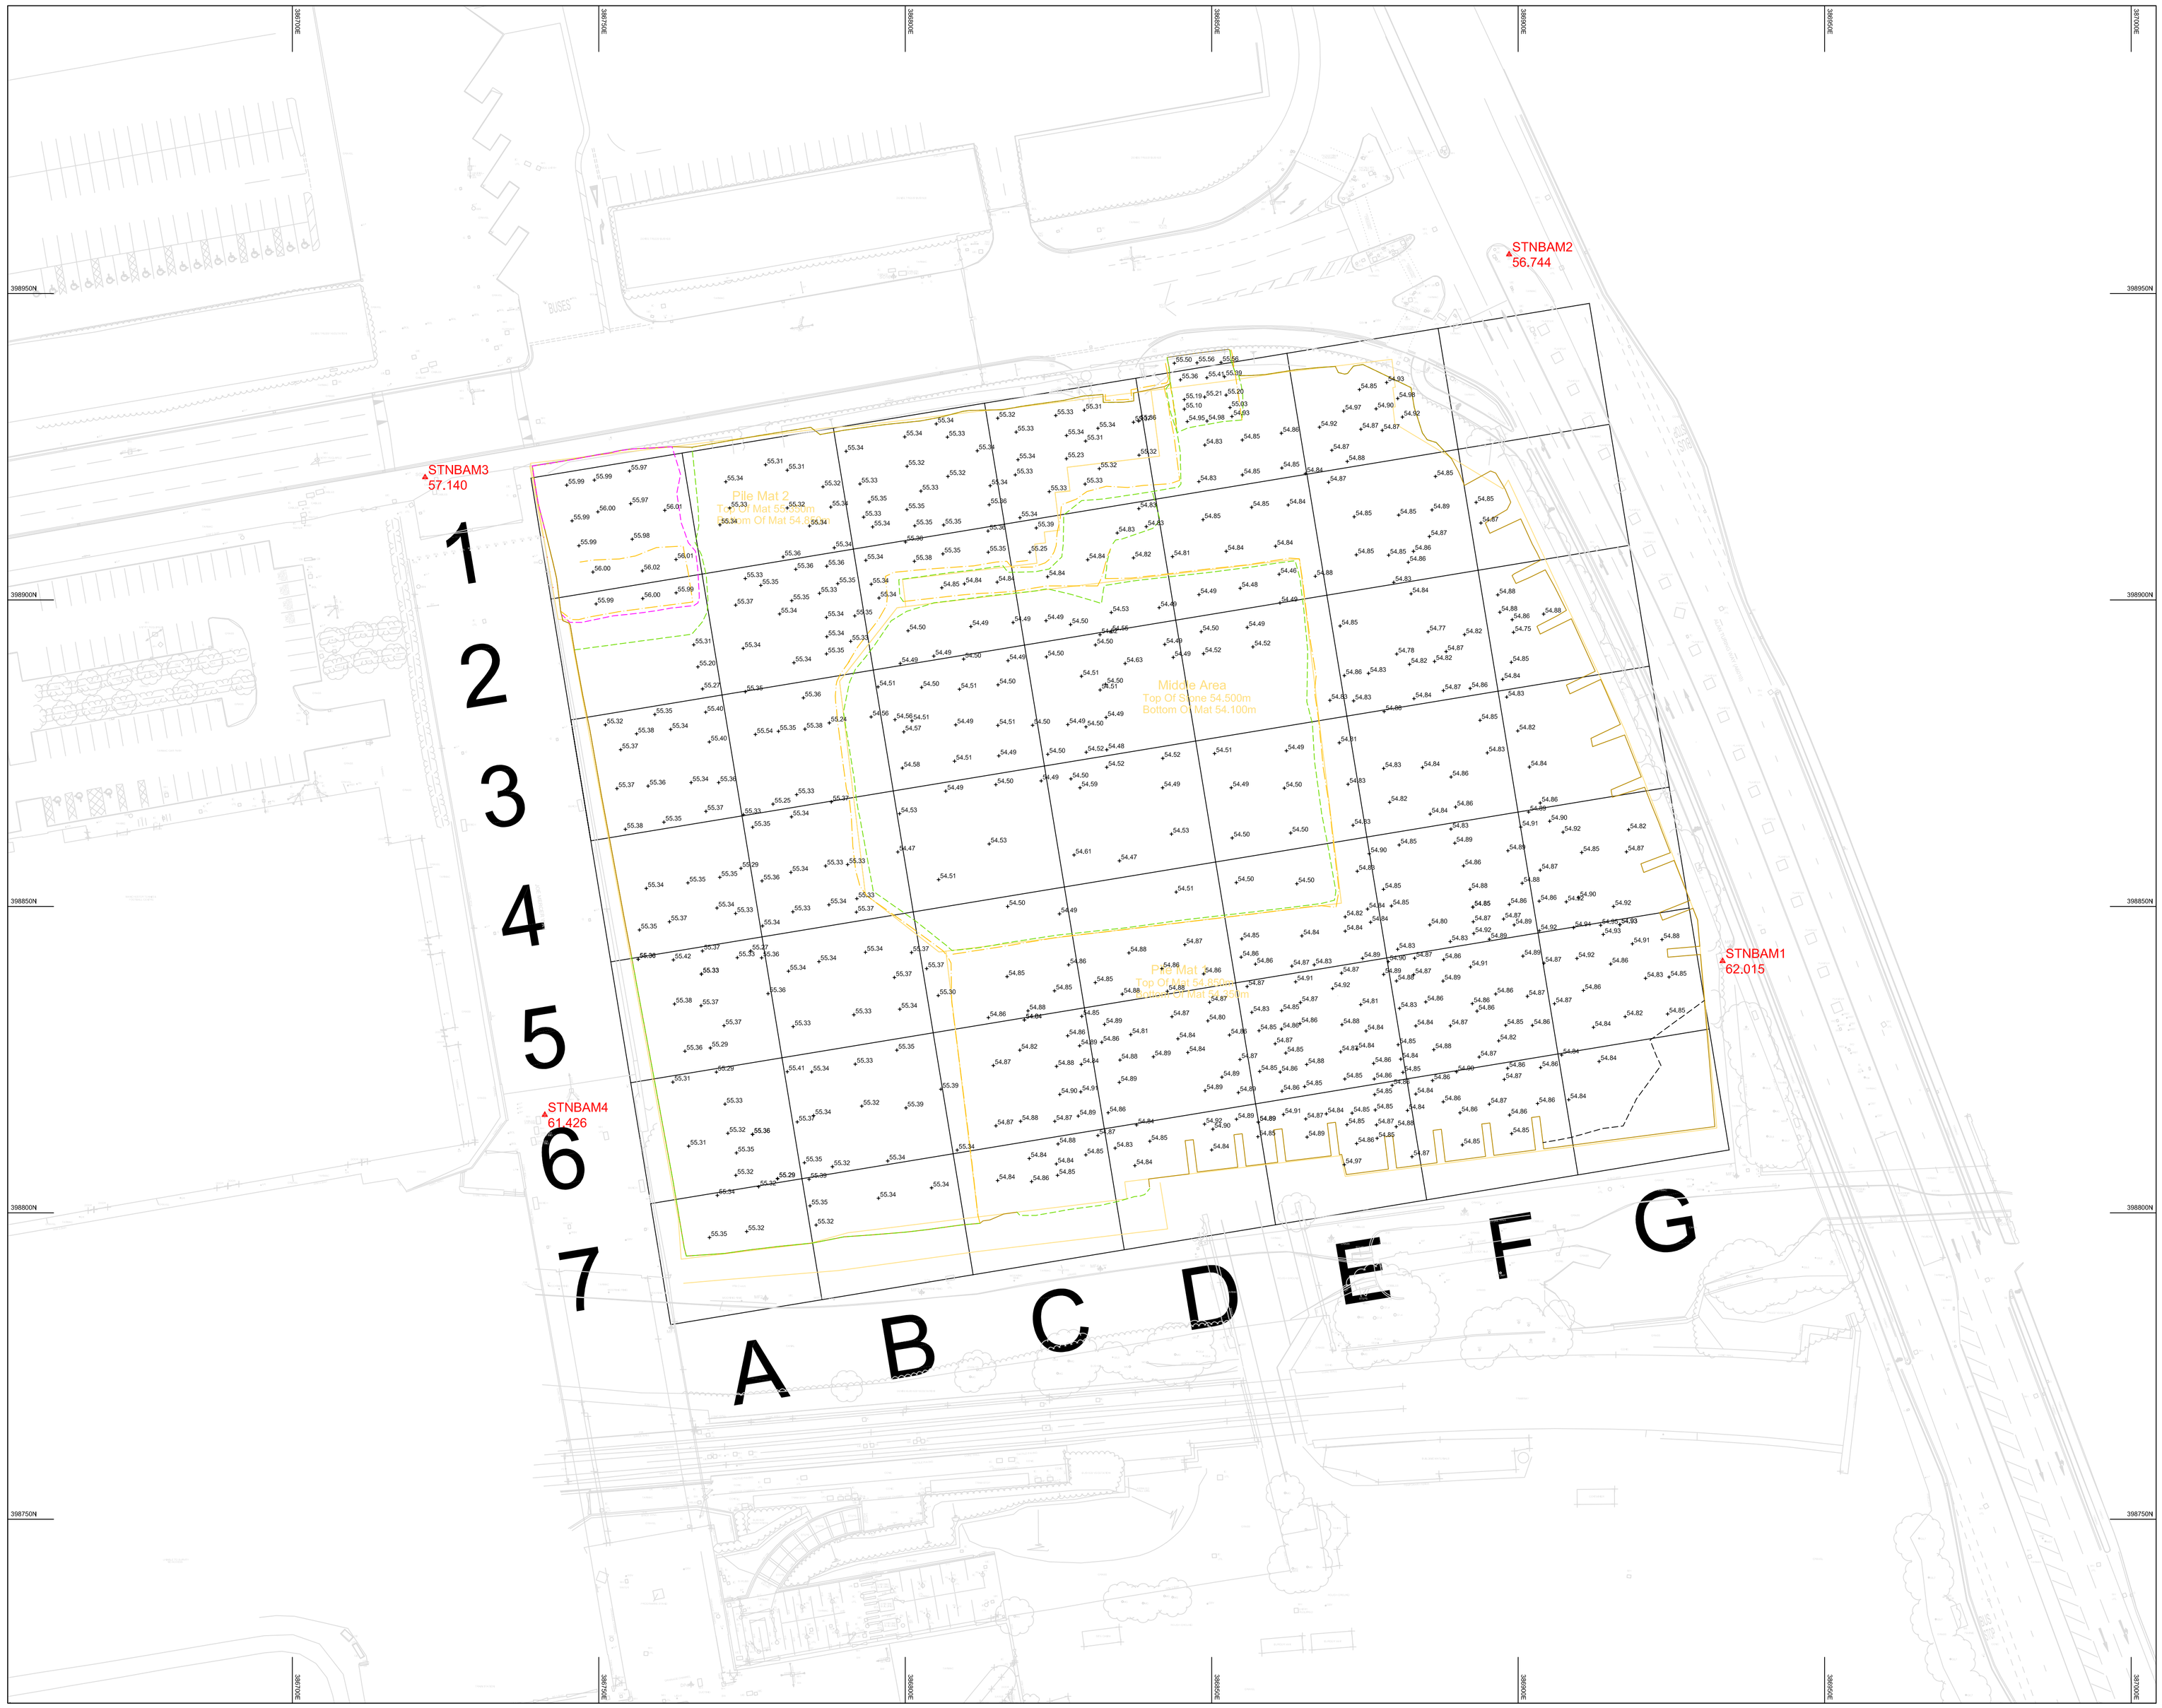

stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 - F 01284 584844 - E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordinates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

As Built Top Of Mat Survey
Low Level Area

SCALE


1:500 @ A1

DRAWING DATE

14/12/2021

DRAWING No.

12037b-0

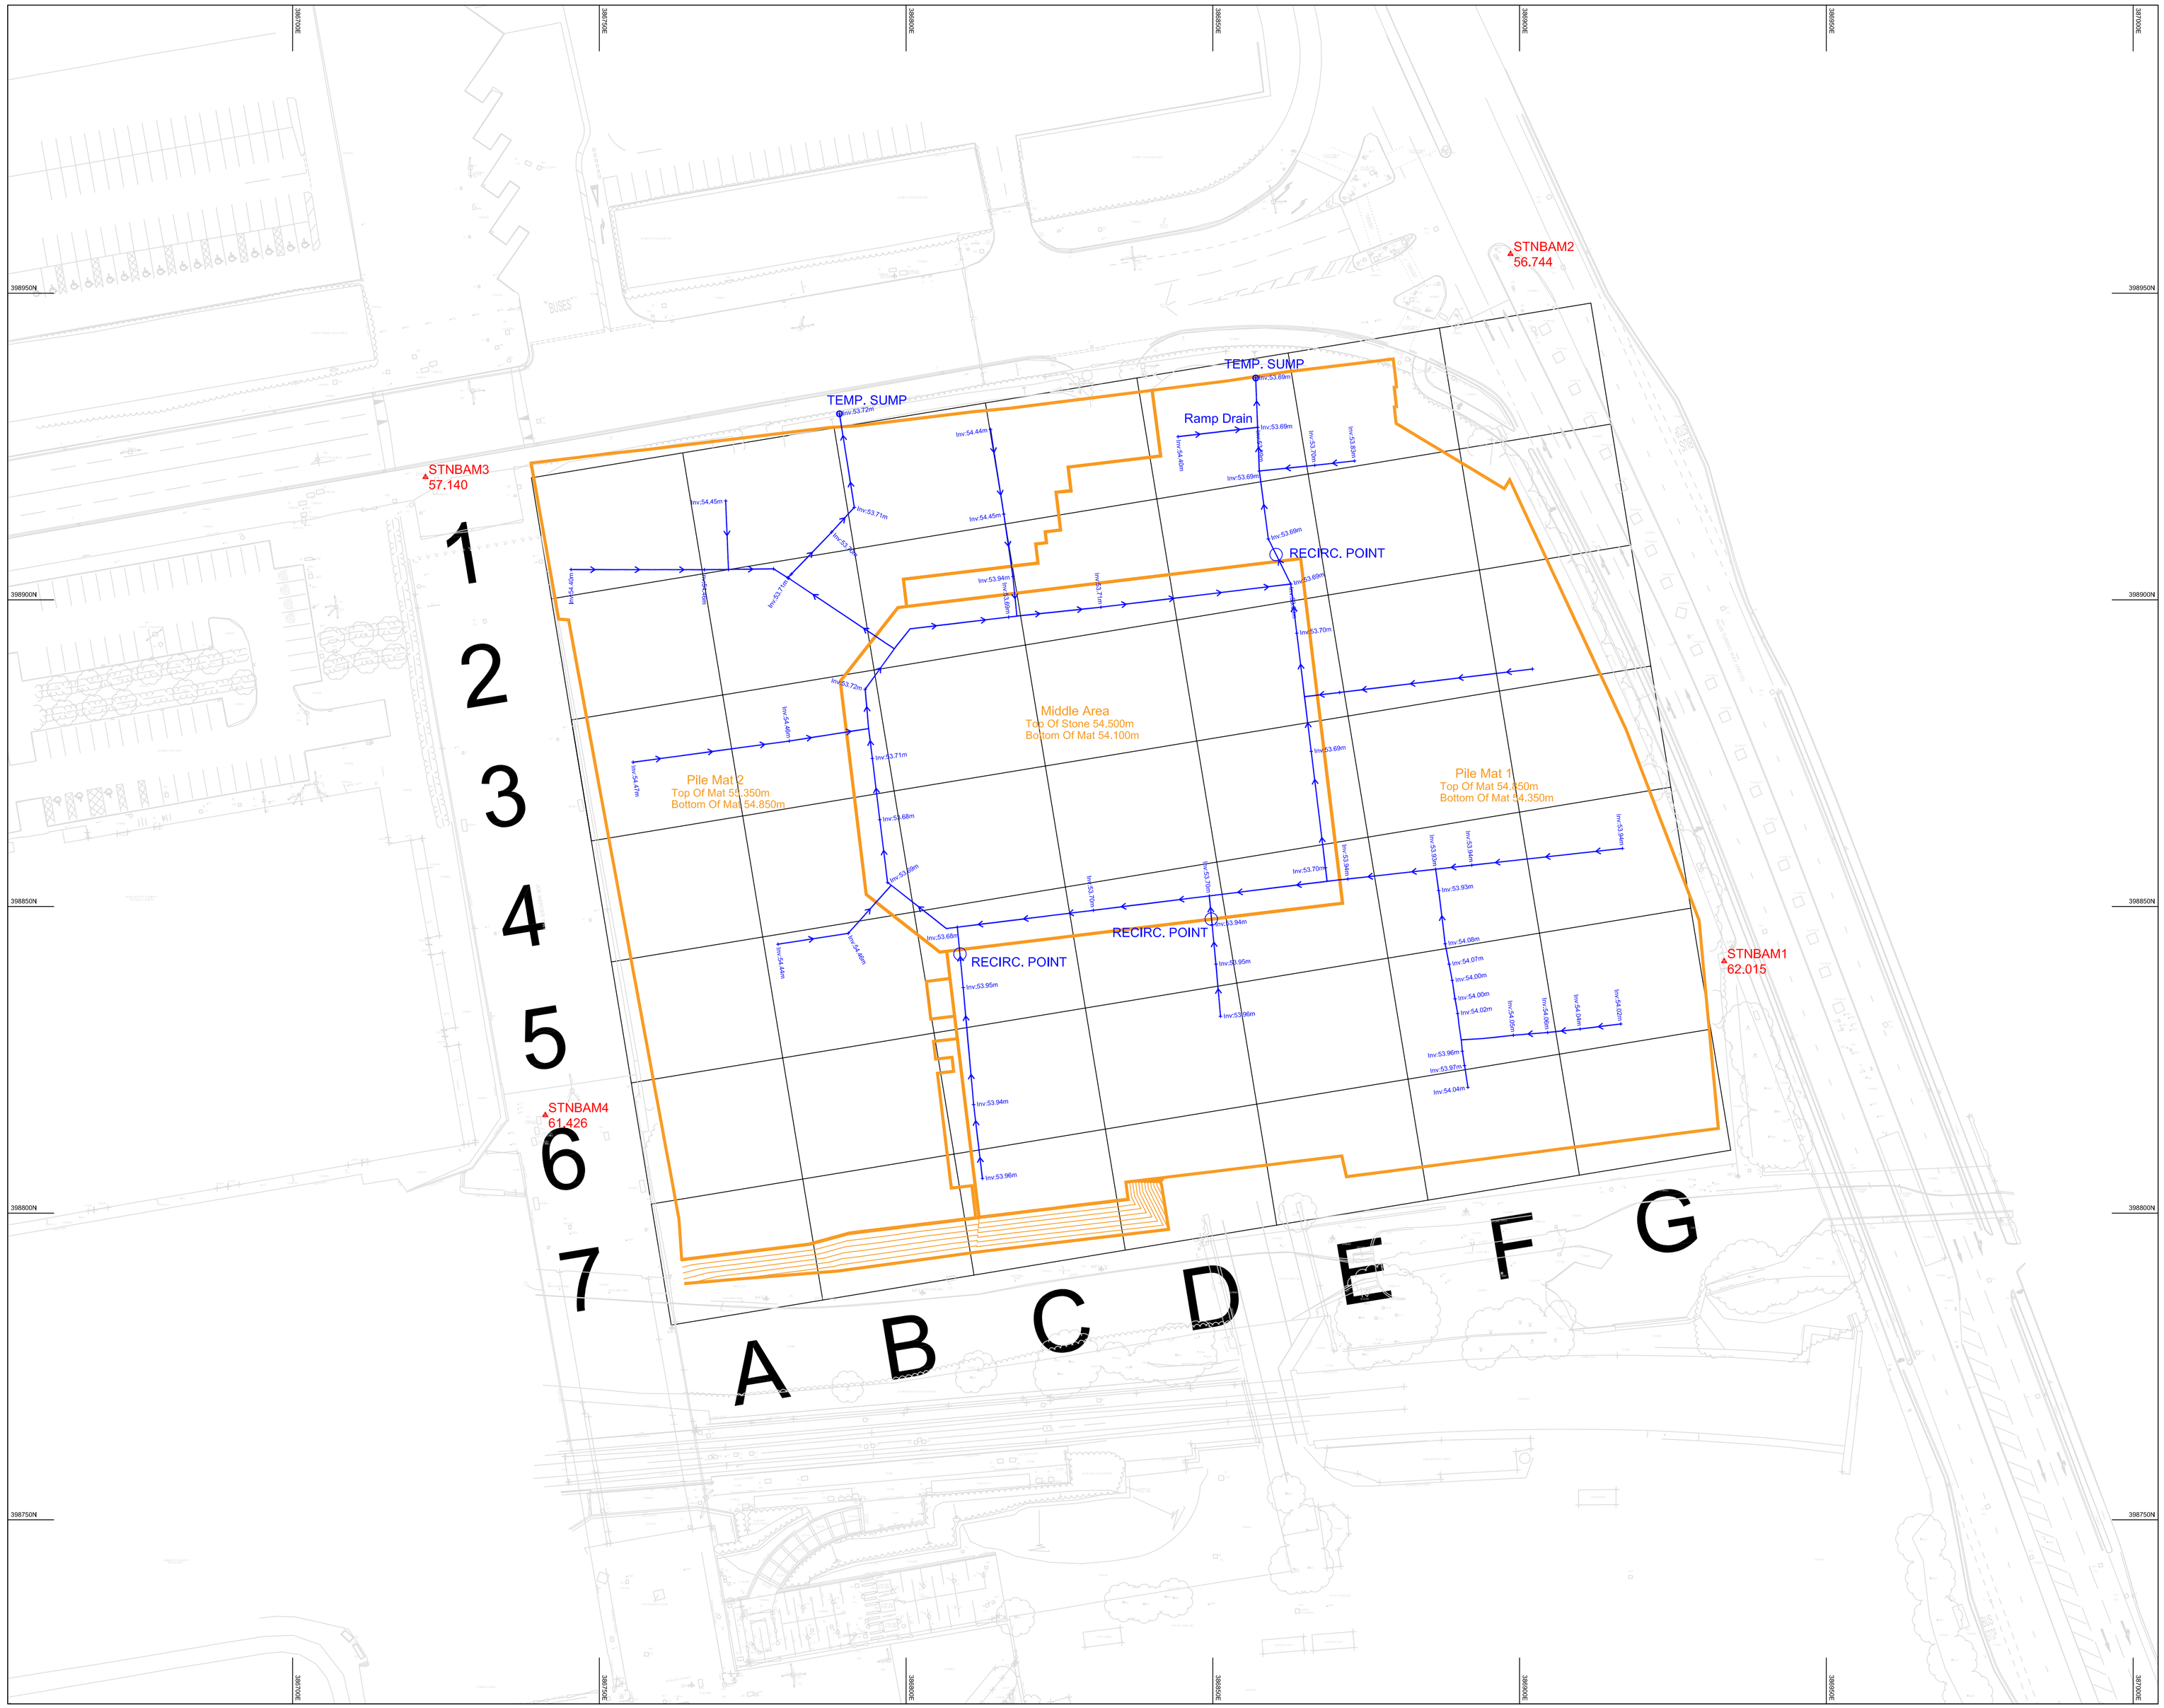

stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire, DE6 5HS
T 01283 584800 F 01284 584844 E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordinates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

As Built Land Drainage
Low Level Areas

SCALE


1:500 @ A1

DRAWING DATE

14/12/2021

DRAWING No.

12037c-0

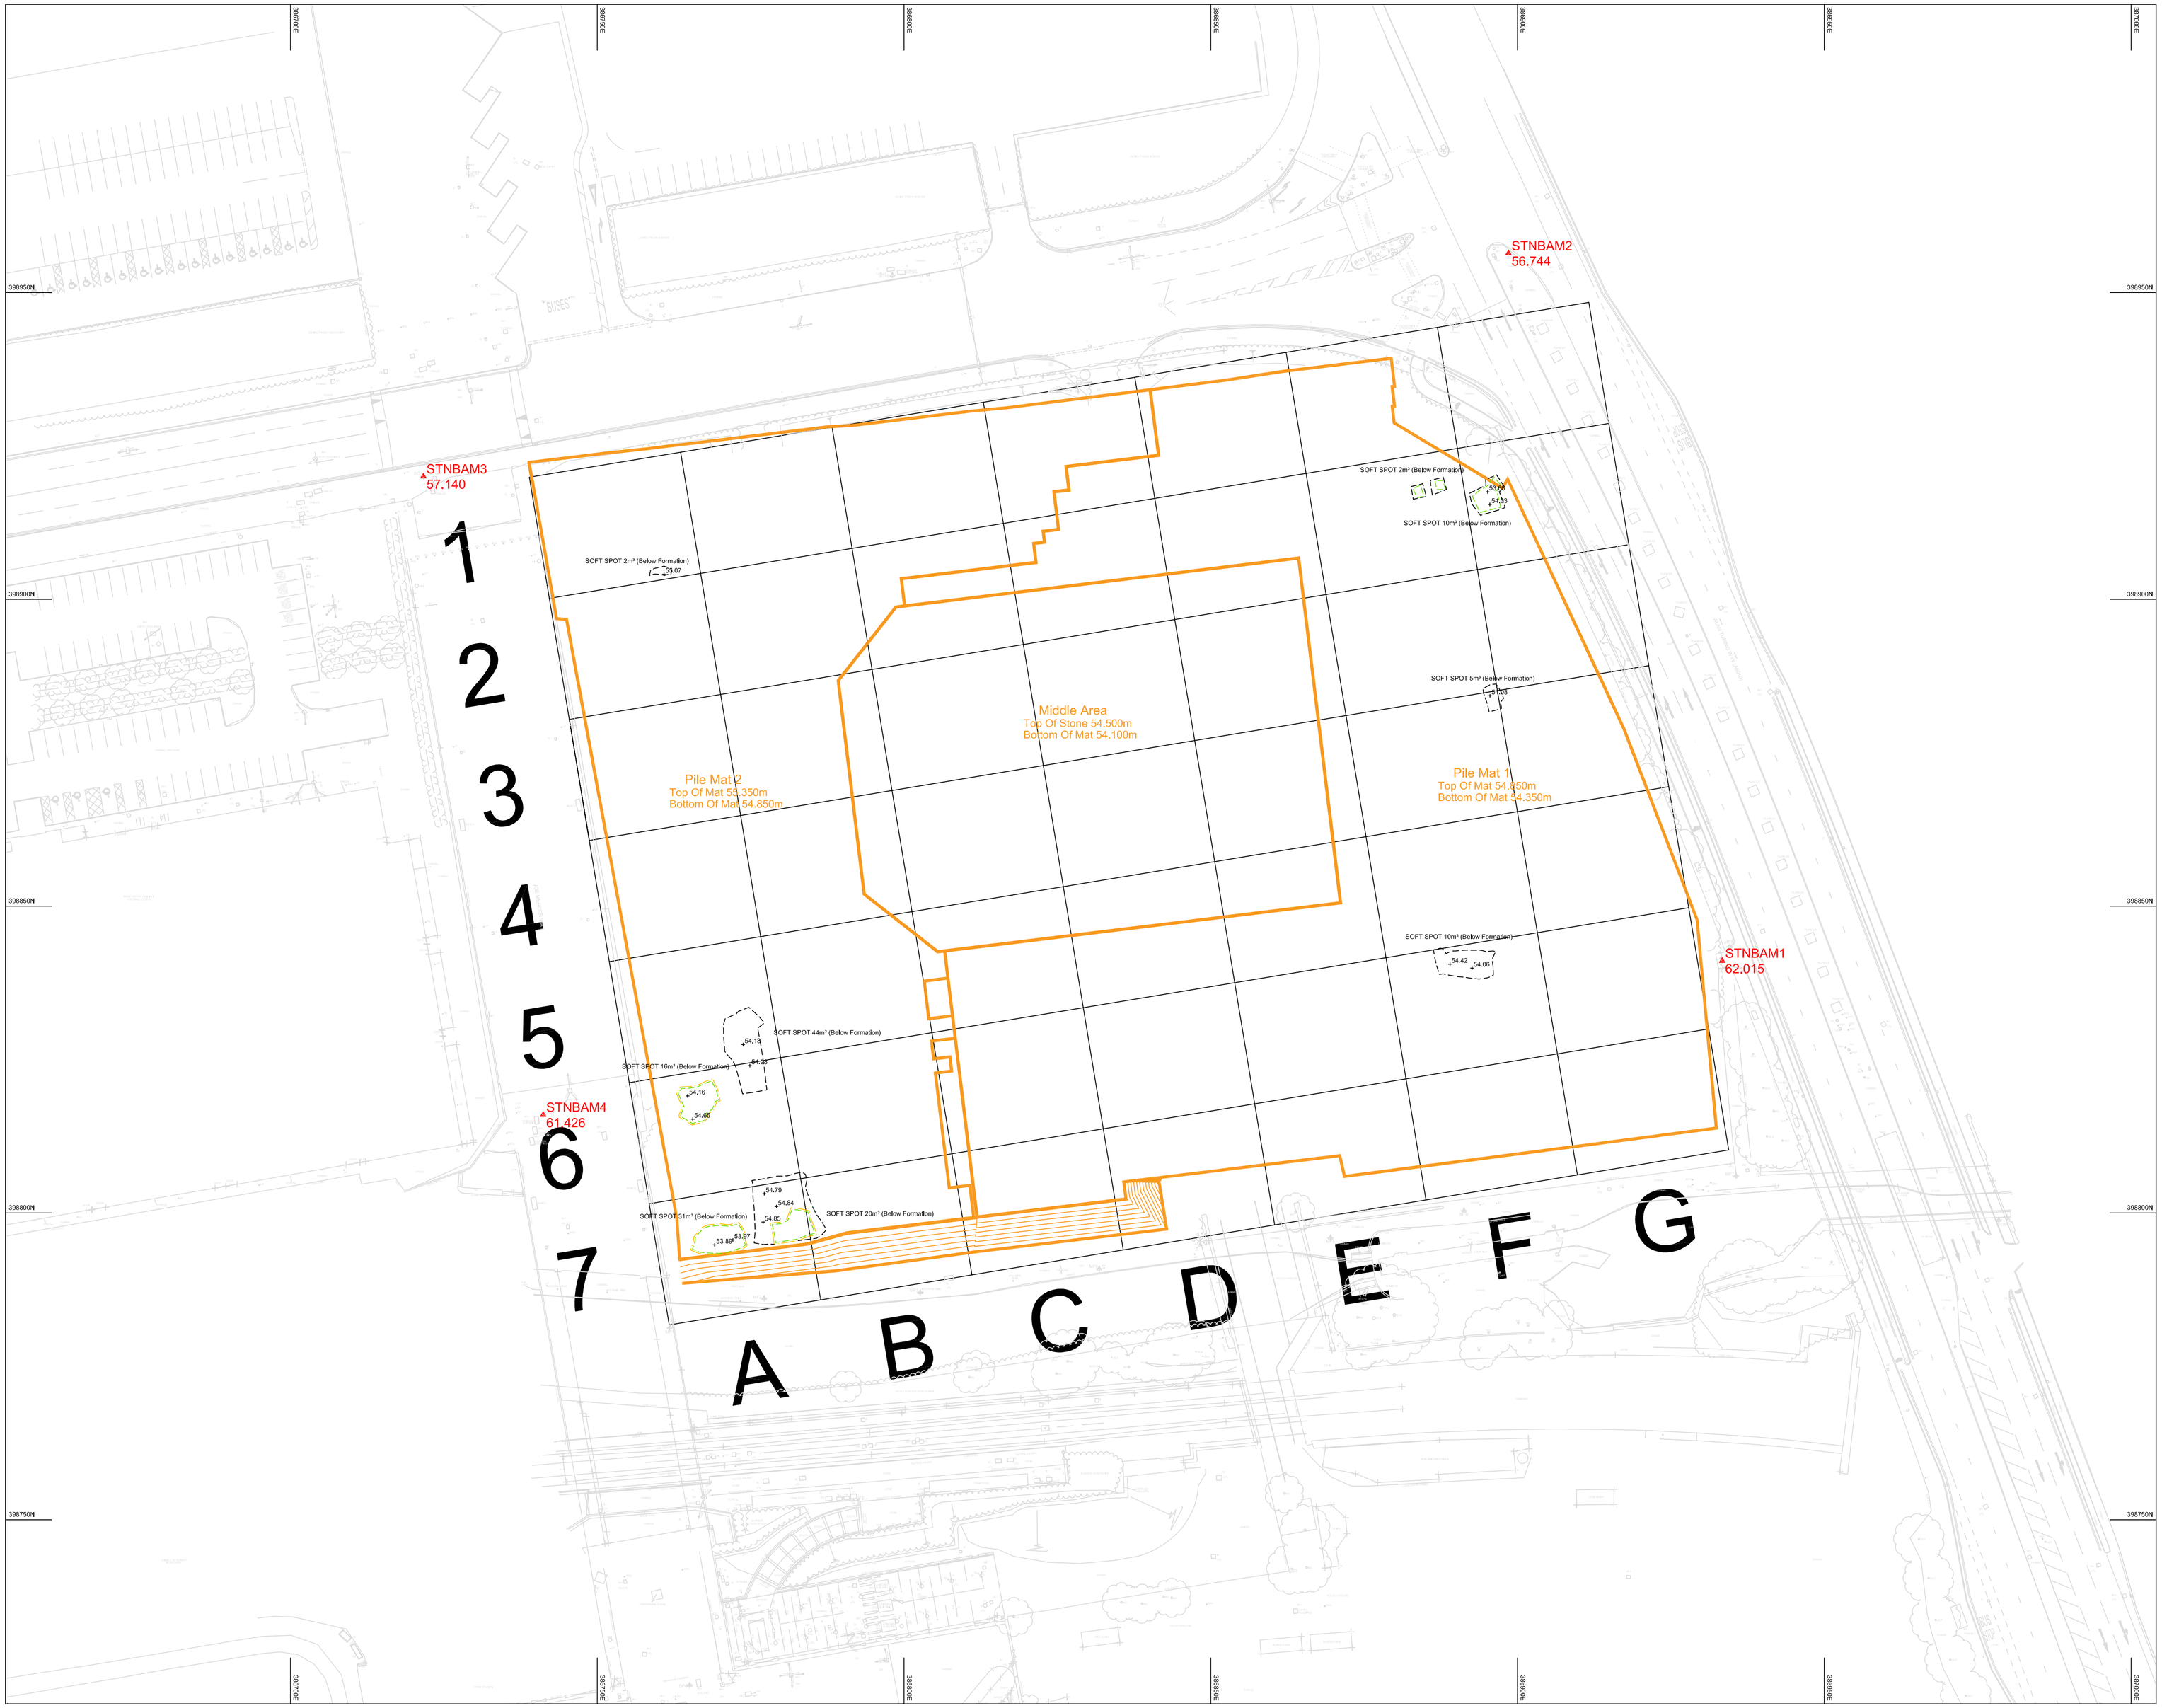

stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 F 01284 584844 E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordInates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

As Built Soft Spot Locations
Low Level Areas

SCALE

1:500 @ A1

DRAWING DATE


14/12/2021

DRAWING No.

12037e-0


APPENDIX C Planning and Programme of Works

ID	Task Name	Duration	Start	Finish
1	**Pre Commencement Works**	**30 days**	**Mon 10/08/20**	**Fri 18/09/20**
2	H&S Document Prep (AMP, CPHSP, EMP)	15 days	Mon 10/08/20	Fri 28/08/20
3	EA MTL Deployment & Review	30 days	Mon 10/08/20	Fri 18/09/20
4	Material Management Plan Declaration	1 day	Mon 14/09/20	Mon 14/09/20
5	**Site Works**	**5 days**	**Mon 21/09/20**	**Fri 25/09/20**
6	Mobilisation	2 days	Mon 21/09/20	Tue 22/09/20
7	Vegetation Strip/Tree Clearance	5 days	Mon 21/09/20	Fri 25/09/20
8	**Bulk Excavation**	**110 days**	**Mon 21/09/20**	**Mon 22/02/21**
9	Excavation from North West proceeding south - Refer to Excavation Phasing	110 days	Mon 21/09/20	Mon 22/02/21
10	Install Access Road 1	3 days	Mon 28/09/20	Wed 30/09/20
11	Install Access Road 2	3 days	Thu 08/10/20	Mon 12/10/20
12	**Pile Mat formation**	**120 days**	**Thu 24/09/20**	**Thu 11/03/21**
13	Import stone	116 days	Fri 25/09/20	Mon 08/03/21
14	Land Drain Installation	110 days	Thu 24/09/20	Thu 25/02/21
15	Section Placement of Piling Mat	117 days	Tue 29/09/20	Thu 11/03/21
16	**Offsite disposal**	**120 days?**	**Mon 21/09/20**	**Mon 08/03/21**
17	Refer to materials generation breakdown - C. 1000m3 day	118 days?	Wed 23/09/20	Mon 08/03/21
18		1 day?	Mon 21/09/20	Mon 21/09/20
19	**Support Works**	**185 days**	**Mon 14/09/20**	**Mon 31/05/21**
20	Install Water Treatment System	5 days	Mon 21/09/20	Fri 25/09/20
21	Operate Water Treatment System	180 days	Mon 21/09/20	Mon 31/05/21
22	Road Crossing for Water Discharge	3 days	Mon 14/09/20	Wed 16/09/20
23	Tarmac Central Bowl 50%	5 days	Mon 09/11/20	Fri 13/11/20
24	Tarmac Central Bowl 50%	5 days	Mon 04/01/21	Fri 08/01/21
25	**Attendances**	**124 days**	**Mon 21/09/20**	**Fri 12/03/21**
26	UXO Watching Brief	124 days	Mon 21/09/20	Fri 12/03/21
27	Environmental monitoring	124 days	Mon 21/09/20	Fri 12/03/21
28	CBR Testing on formation	2 days	Mon 19/10/20	Tue 20/10/20

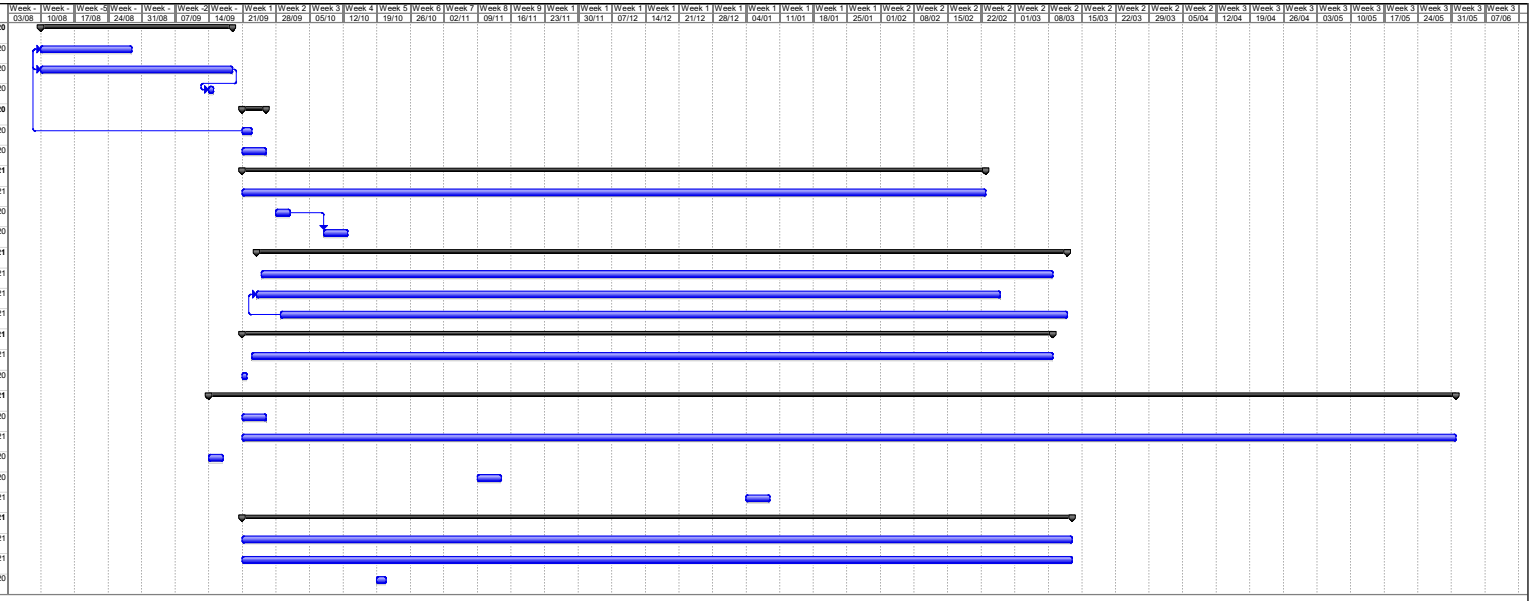

Project: Provectus Project Bradford Bu
Date: Sun 19/04/20

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline

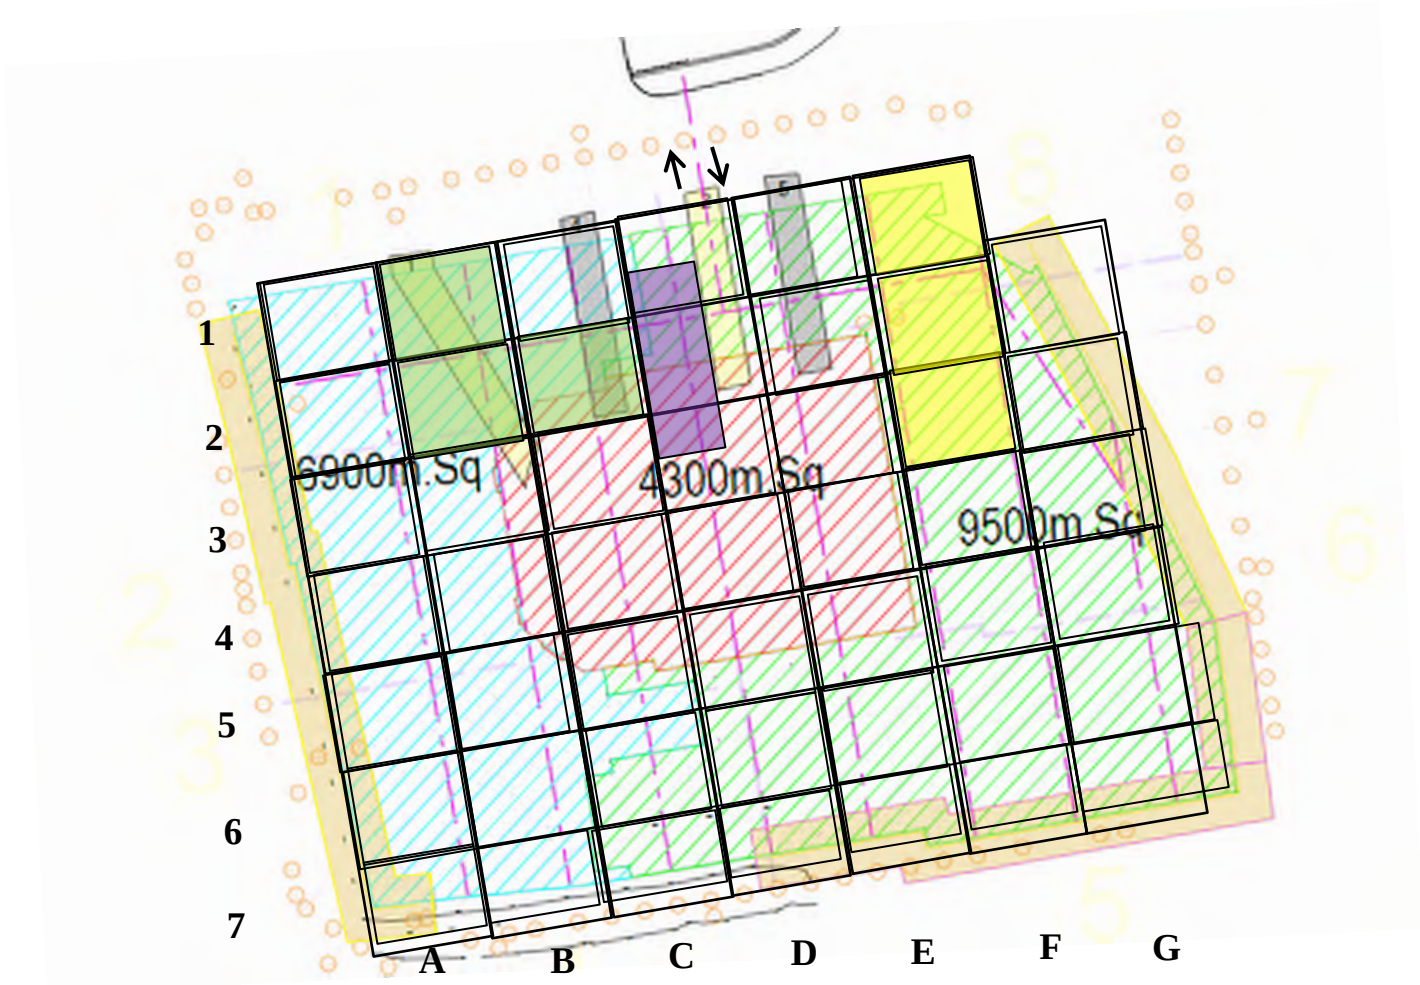

Reduced Level Excavation

Placement of Piling Mat

High Level Piling Mat

Soil Stockpile/Loading

Materials Processing Area

Works Complete

PROVECTUS

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Tel. 0118 988 0200
www.provectusgroup.com

Client: OVG

Project: Project Bradford


Job No.: 101114

Title: Remediation and Bulk Excavation works Week Site Grid 20m x 25m

Scale: NTS

Date Drawn: April 2020

Drawing No.: 101114 Week 1

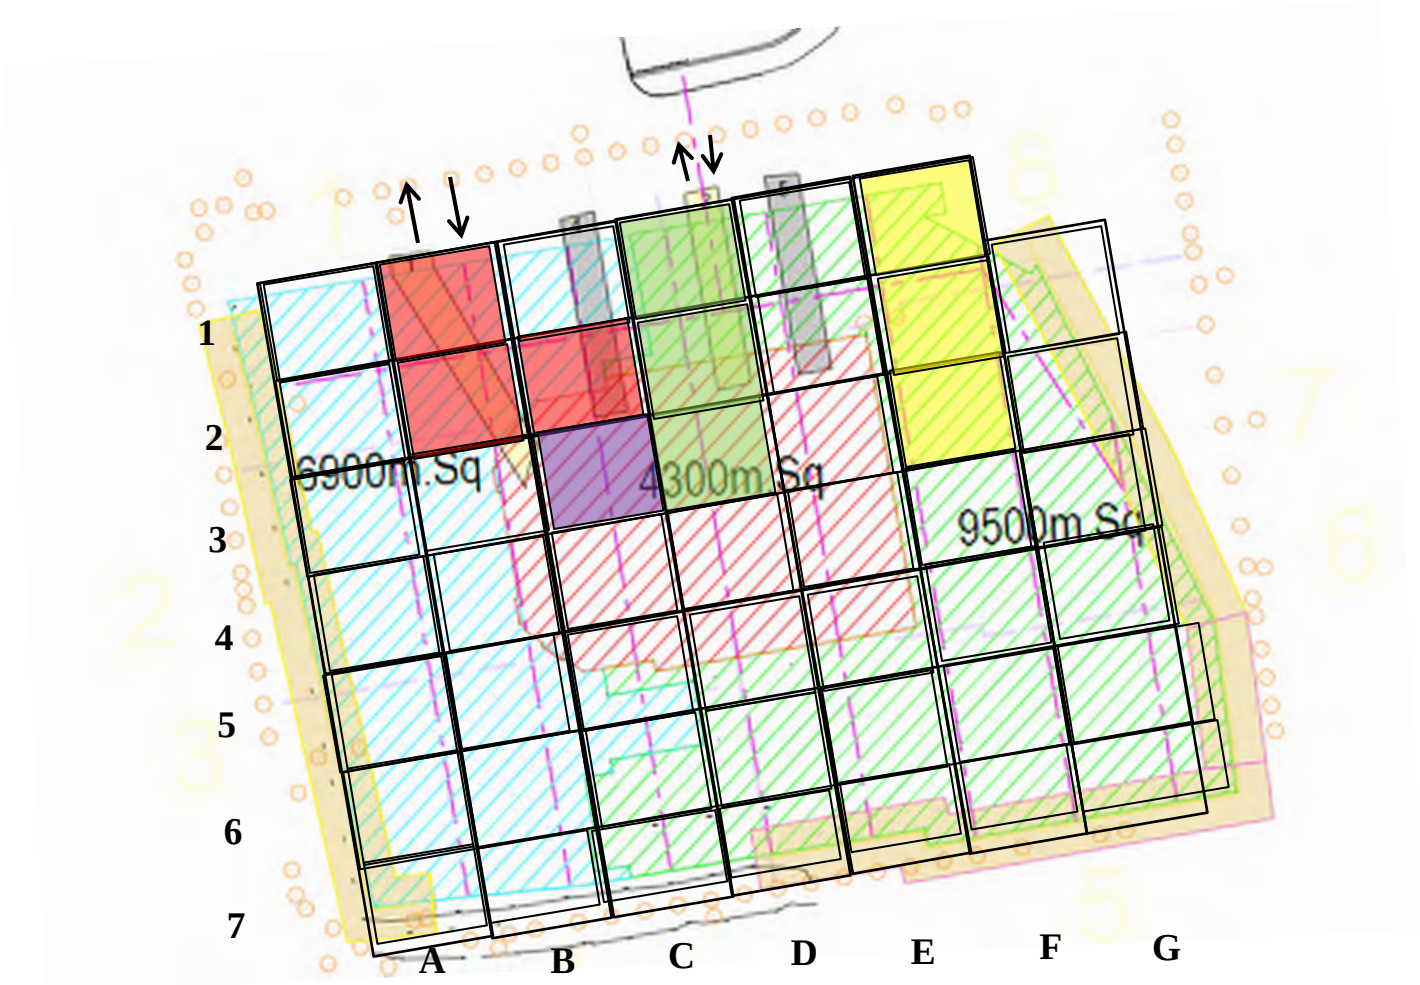

Reduced Level Excavation

Placement of Piling Mat

High Level Piling Mat

Soil Stockpile/Loading

Materials Processing Area

Works Complete

PROVECTUS

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Tel. 0118 988 0200
www.provectusgroup.com

Client: OVG

Project: Project Bradford


Job No.: 101114

Title: Remediation and Bulk Excavation works Week Site Grid 20m x 25m

Scale: NTS

Date Drawn: April 2020

Drawing No.: 101114 Week 2

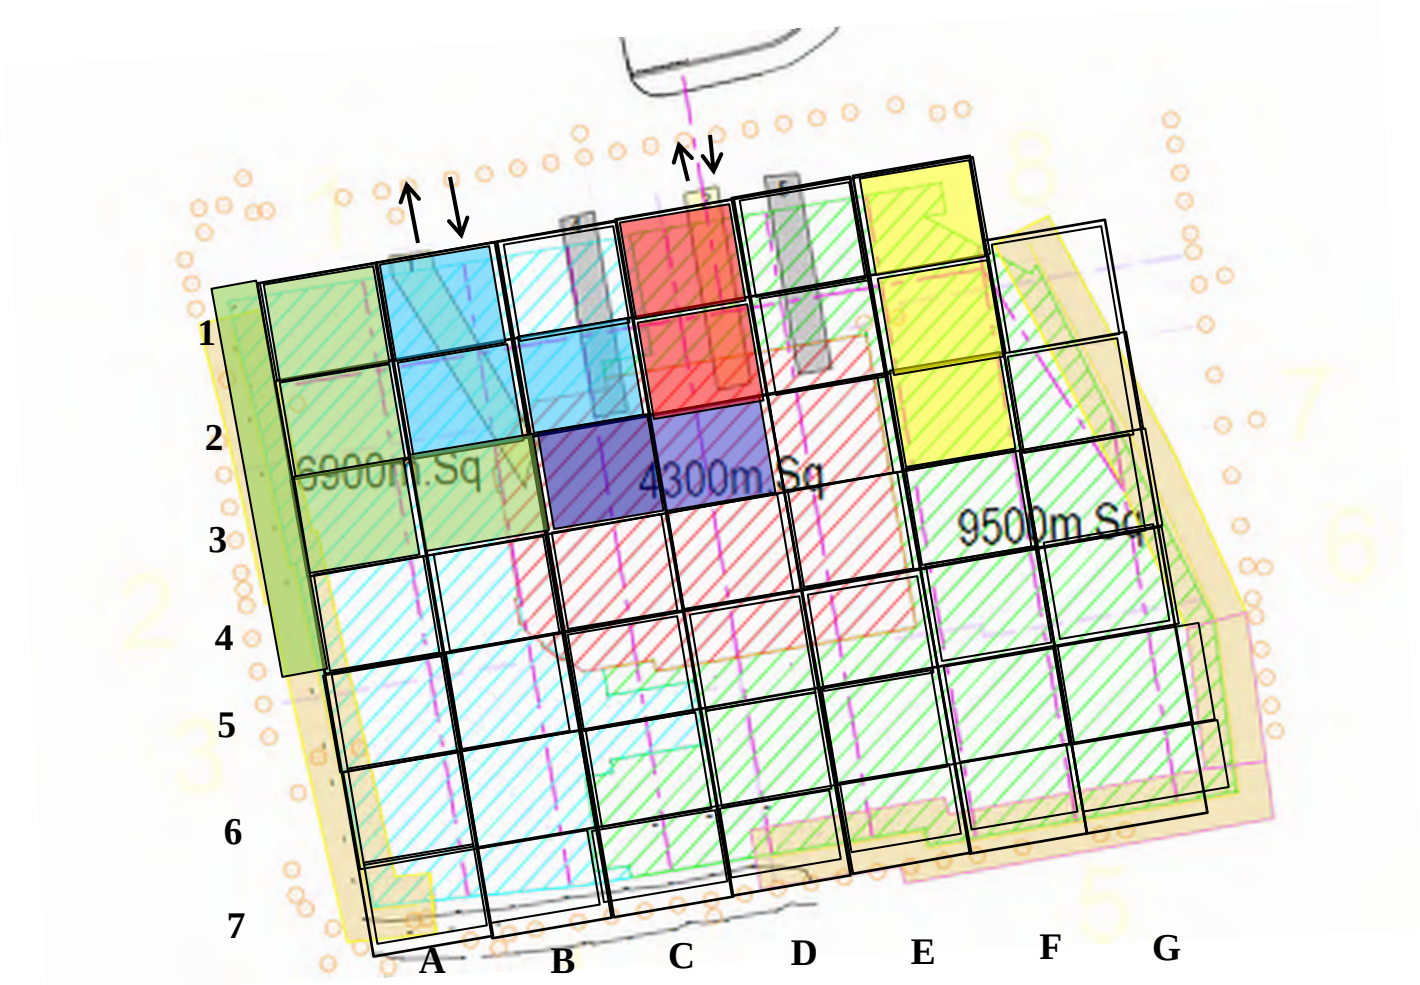

Reduced Level Excavation

Placement of Piling Mat

High Level Piling Mat

Soil Stockpile/Loading

Materials Processing Area

Works Complete

PROVECTUS

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Tel. 0118 988 0200
www.provectusgroup.com

Client: OVG

Project: Project Bradford


Job No.: 101114

Title: Remediation and Bulk Excavation works Week Site Grid 20m x 25m

Scale: NTS

Date Drawn: April 2020

Drawing No.: 101114 Week 3

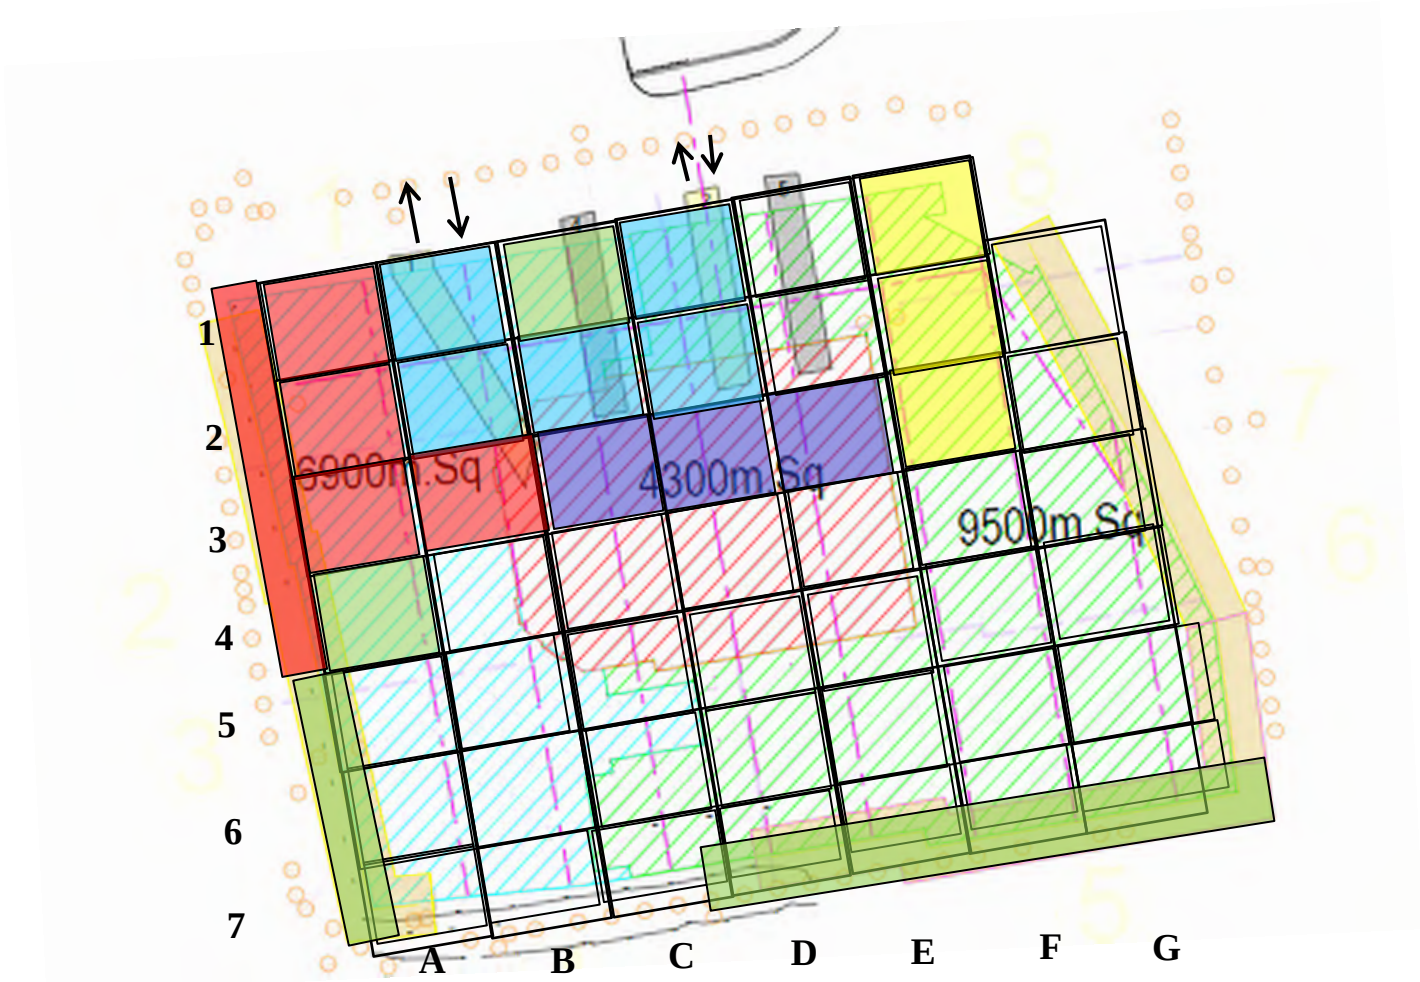

Reduced Level Excavation

Placement of Piling Mat

High Level Piling Mat

Soil Stockpile/Loading

Materials Processing Area

Works Complete

PROVECTUS

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Tel. 0118 988 0200
www.provectusgroup.com

Client: OVG

Project: Project Bradford


Job No.: 101114

Title: Remediation and Bulk Excavation works Week Site Grid 20m x 25m

Scale: NTS

Date Drawn: April 2020

Drawing No.: 101114 Week 4

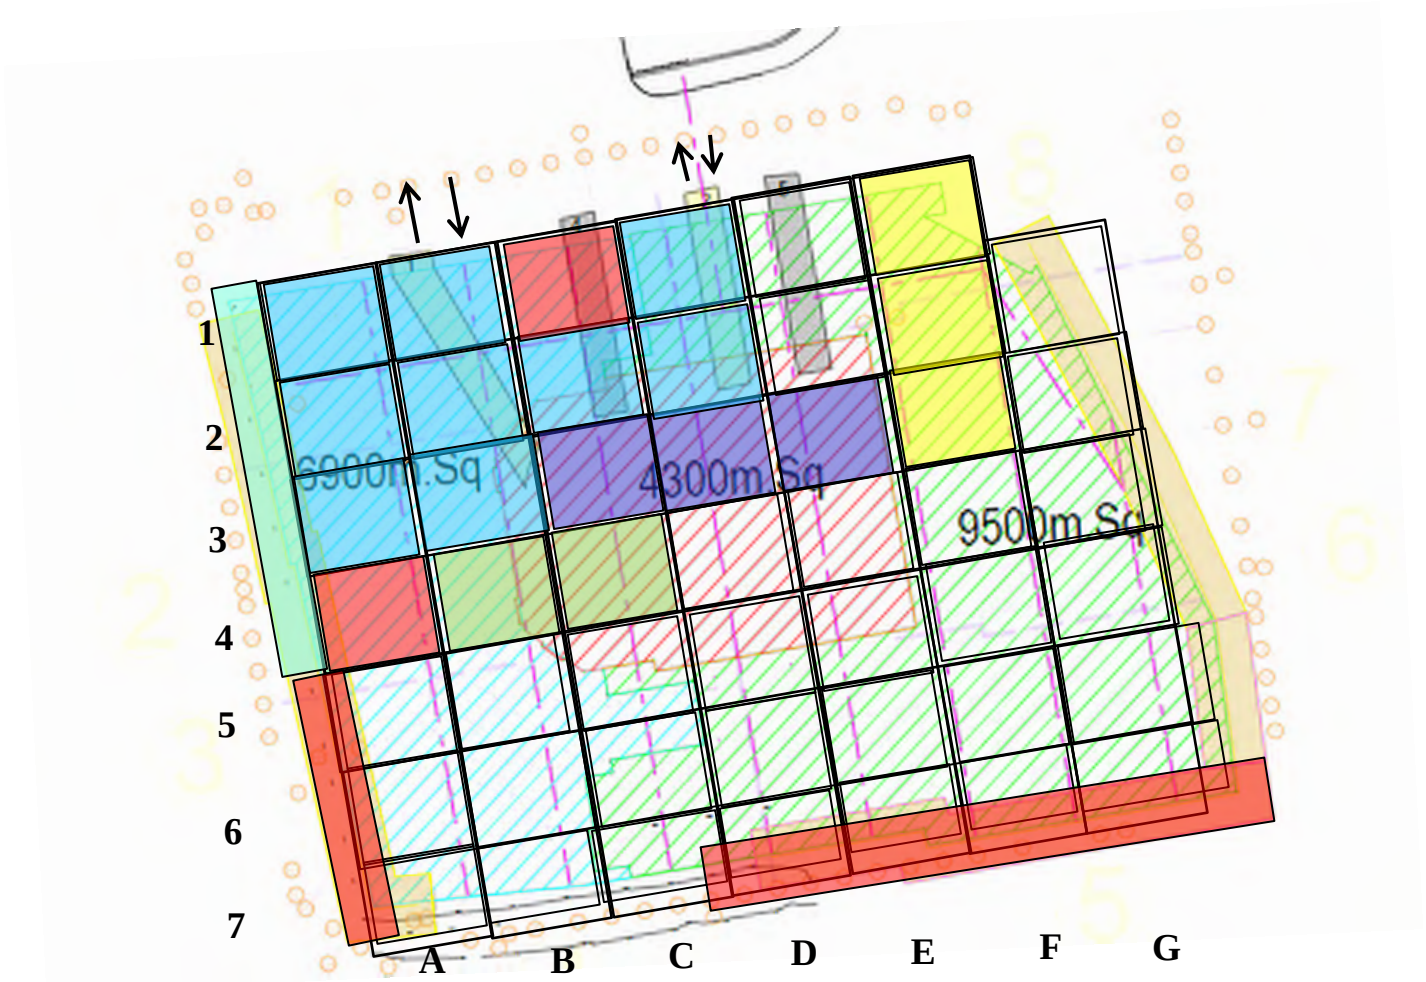

Reduced Level Excavation

Placement of Piling Mat

High Level Piling Mat

Soil Stockpile/Loading

Materials Processing Area

Works Complete

PROVECTUS

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Tel. 0118 988 0200
www.provectusgroup.com

Client: OVG

Project: Project Bradford


Job No.: 101114

Title: Remediation and Bulk Excavation works Week Site Grid 20m x 25m

Scale: NTS

Date Drawn: April 2020

Drawing No.: 101114 Weeks 5

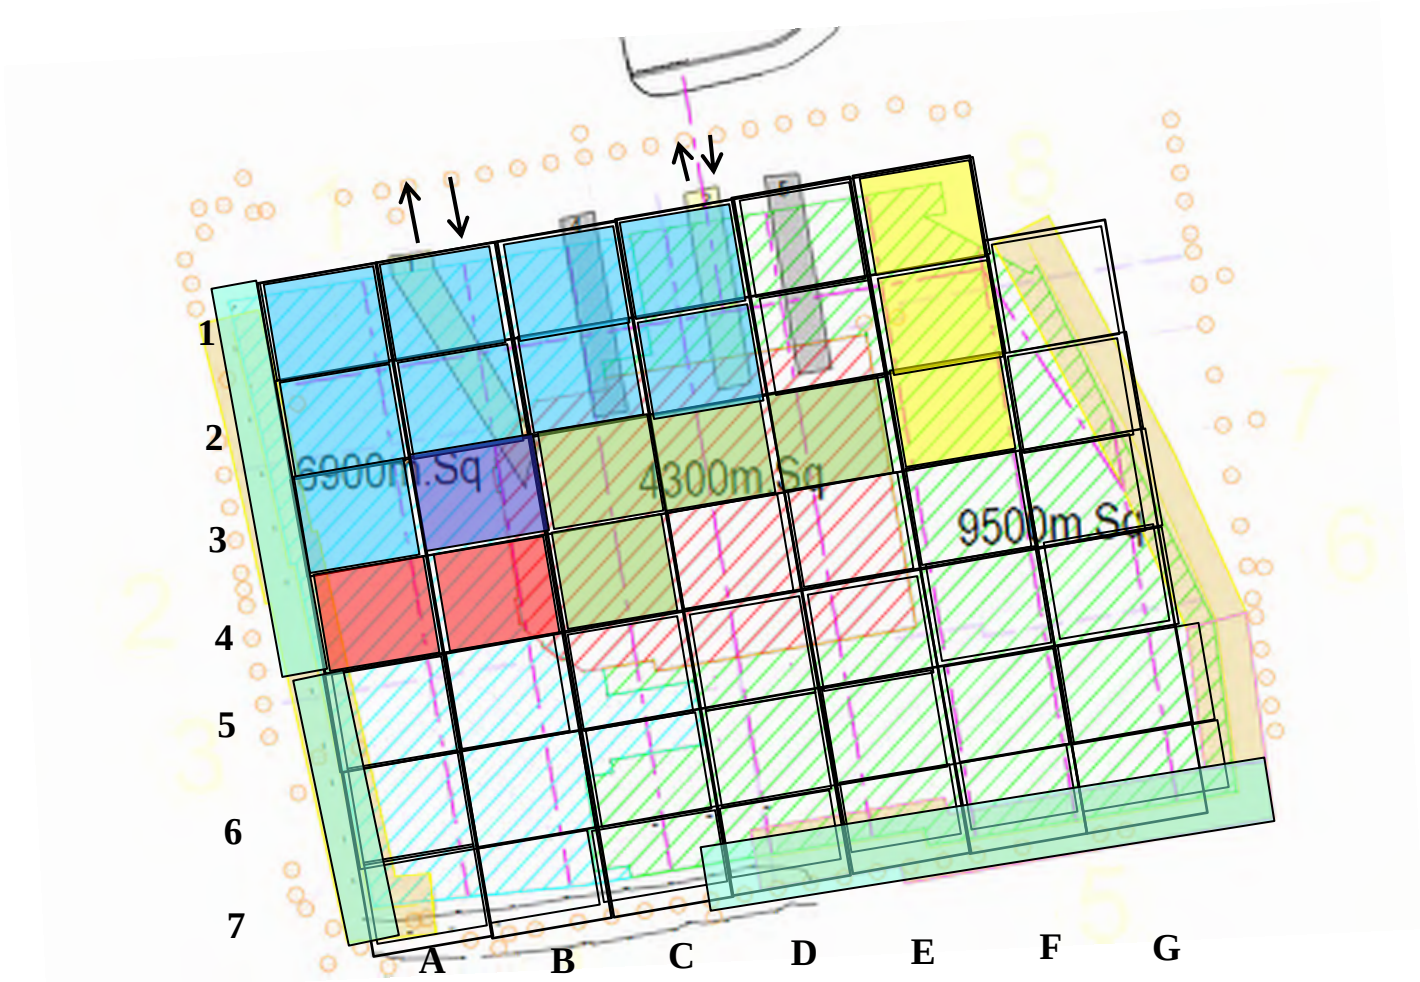

Reduced Level Excavation

Placement of Piling Mat

High Level Piling Mat

Soil Stockpile/Loading

Materials Processing Area

Works Complete

PROVECTUS

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Tel. 0118 988 0200
www.provectusgroup.com

Client: OVG

Project: Project Bradford


Job No.: 101114

Title: Remediation and Bulk Excavation works Week Site Grid 20m x 25m

Scale: NTS

Date Drawn: April 2020

Drawing No.: 101114 Weeks 6

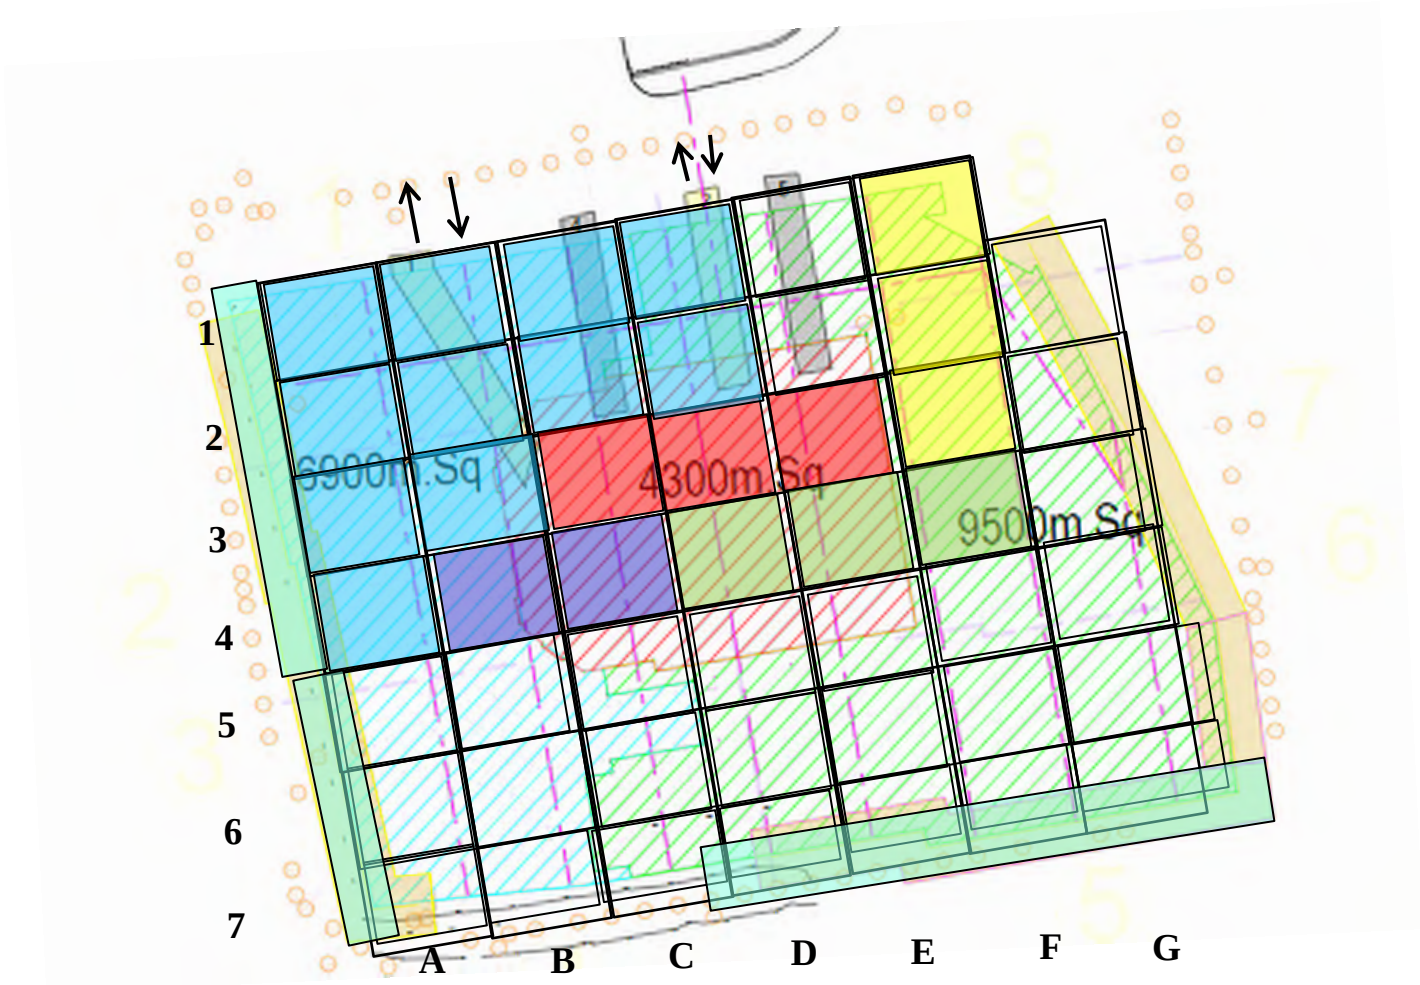

Reduced Level Excavation

Placement of Piling Mat

High Level Piling Mat

Soil Stockpile/Loading

Materials Processing Area

Works Complete

PROVECTUS

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Tel. 0118 988 0200
www.provectusgroup.com

Client: OVG

Project: Project Bradford


Job No.: 101114

Title: Remediation and Bulk Excavation works Week Site Grid 20m x 25m

Scale: NTS

Date Drawn: April 2020

Drawing No.: 101114 Weeks 7

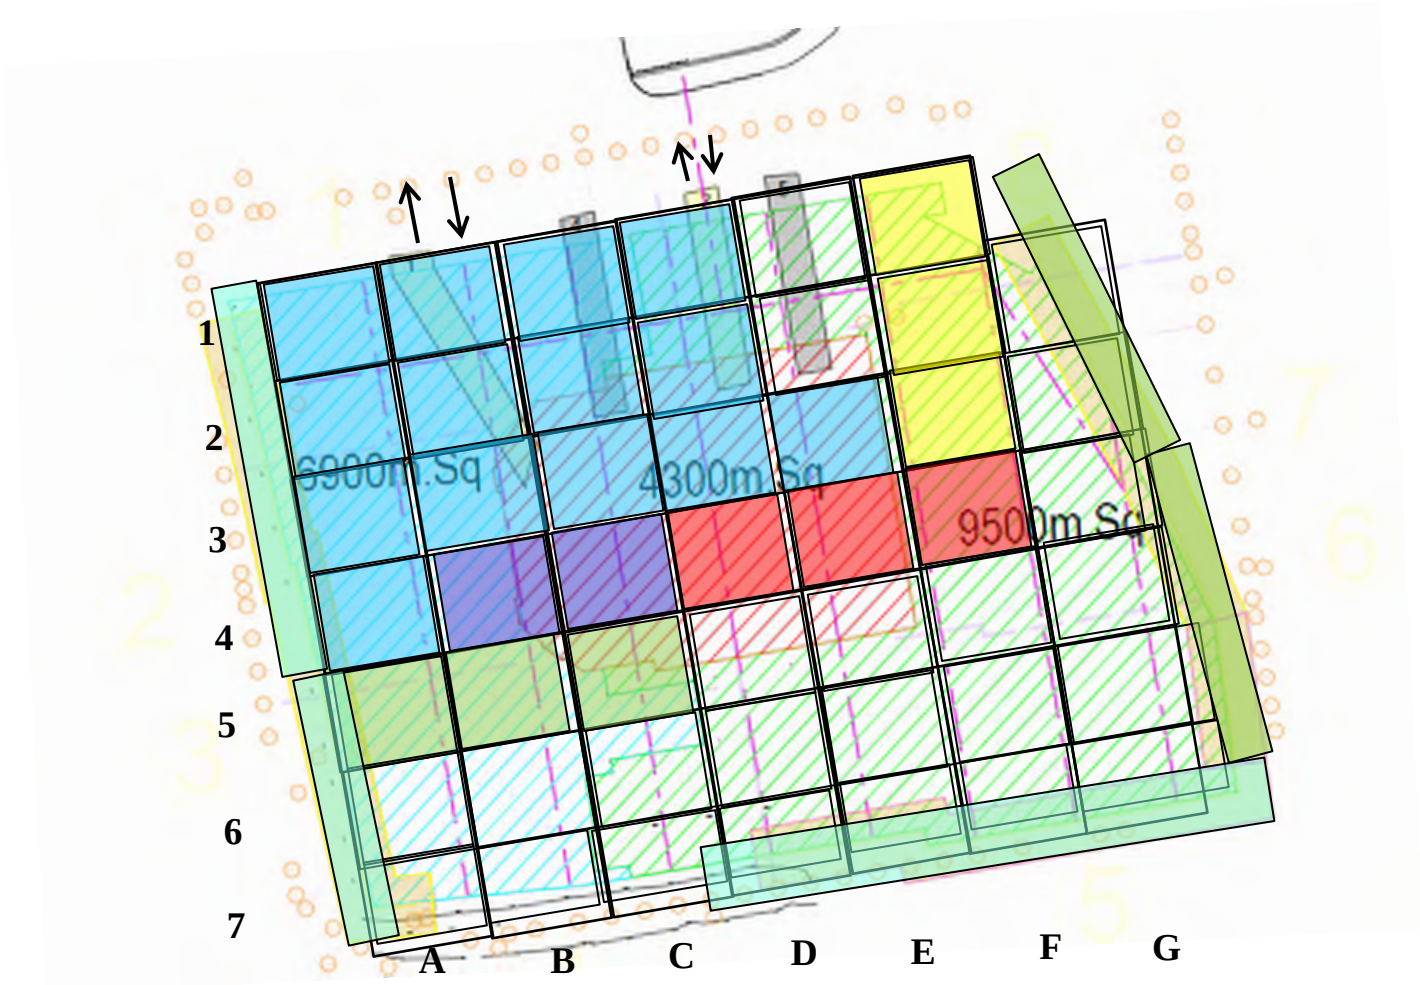

Reduced Level Excavation

Placement of Piling Mat

High Level Piling Mat

Soil Stockpile/Loading

Materials Processing Area

Works Complete

PROVECTUS

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Tel. 0118 988 0200
www.provectusgroup.com

Client: OVG

Project: Project Bradford


Job No.: 101114

Title: Remediation and Bulk Excavation works Week Site Grid 20m x 25m

Scale: NTS

Date Drawn: April 2020

Drawing No.: 101114 Weeks 8

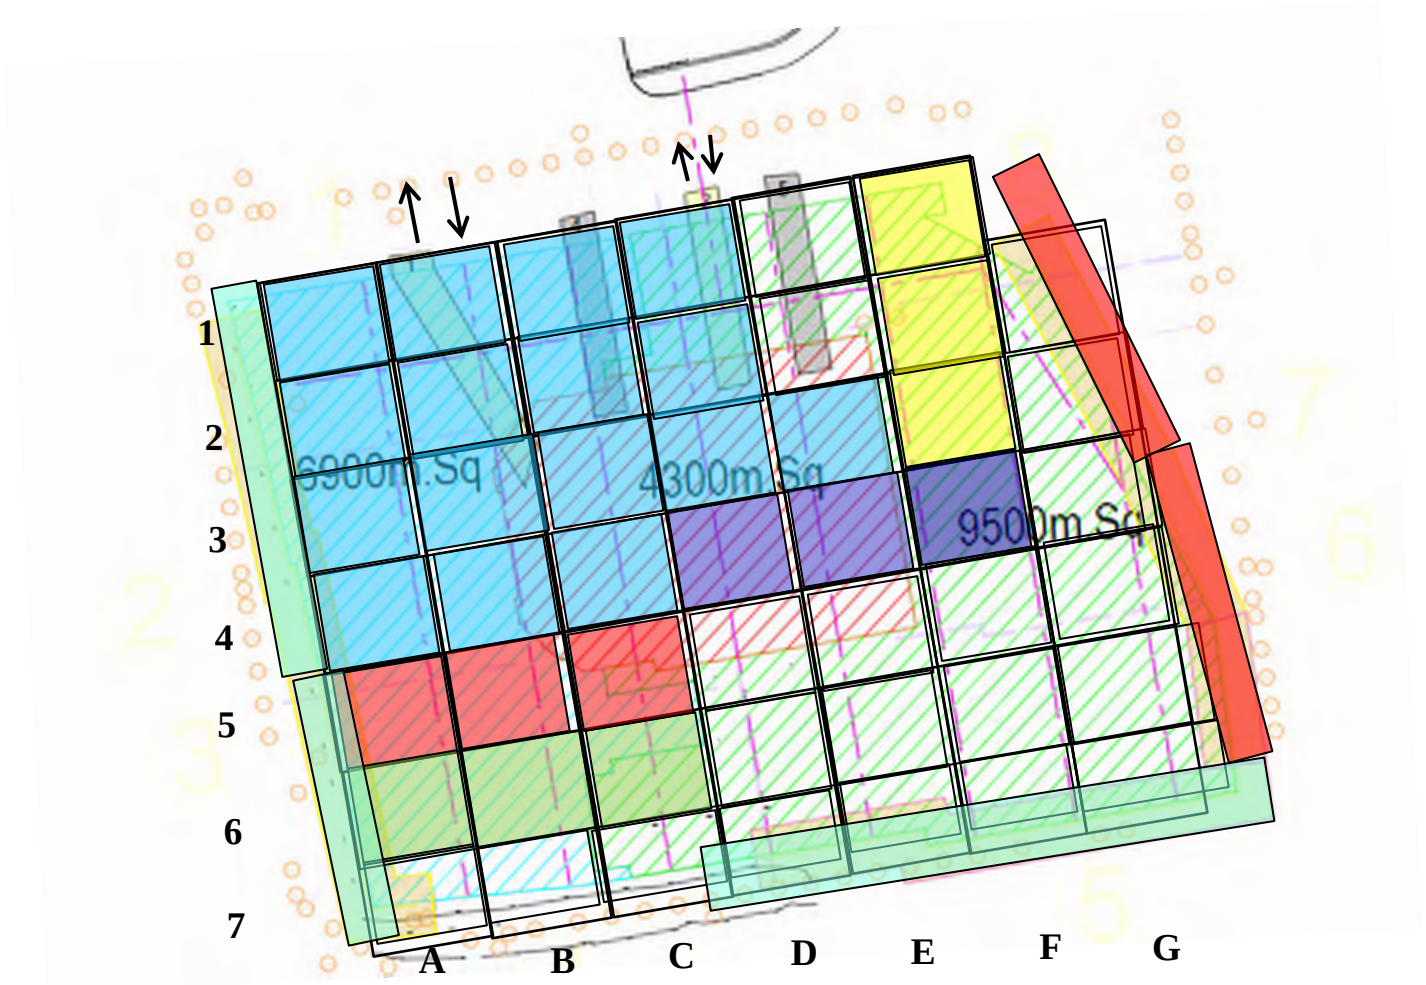

Reduced Level Excavation

Placement of Piling Mat

High Level Piling Mat

Soil Stockpile/Loading

Materials Processing Area

Works Complete

PROVECTUS

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Tel. 0118 988 0200
www.provectusgroup.com

Client: OVG

Project: Project Bradford


Job No.: 101114

Title: Remediation and Bulk Excavation works Week Site Grid 20m x 25m

Scale: NTS

Date Drawn: April 2020

Drawing No.: 101114 Weeks 9

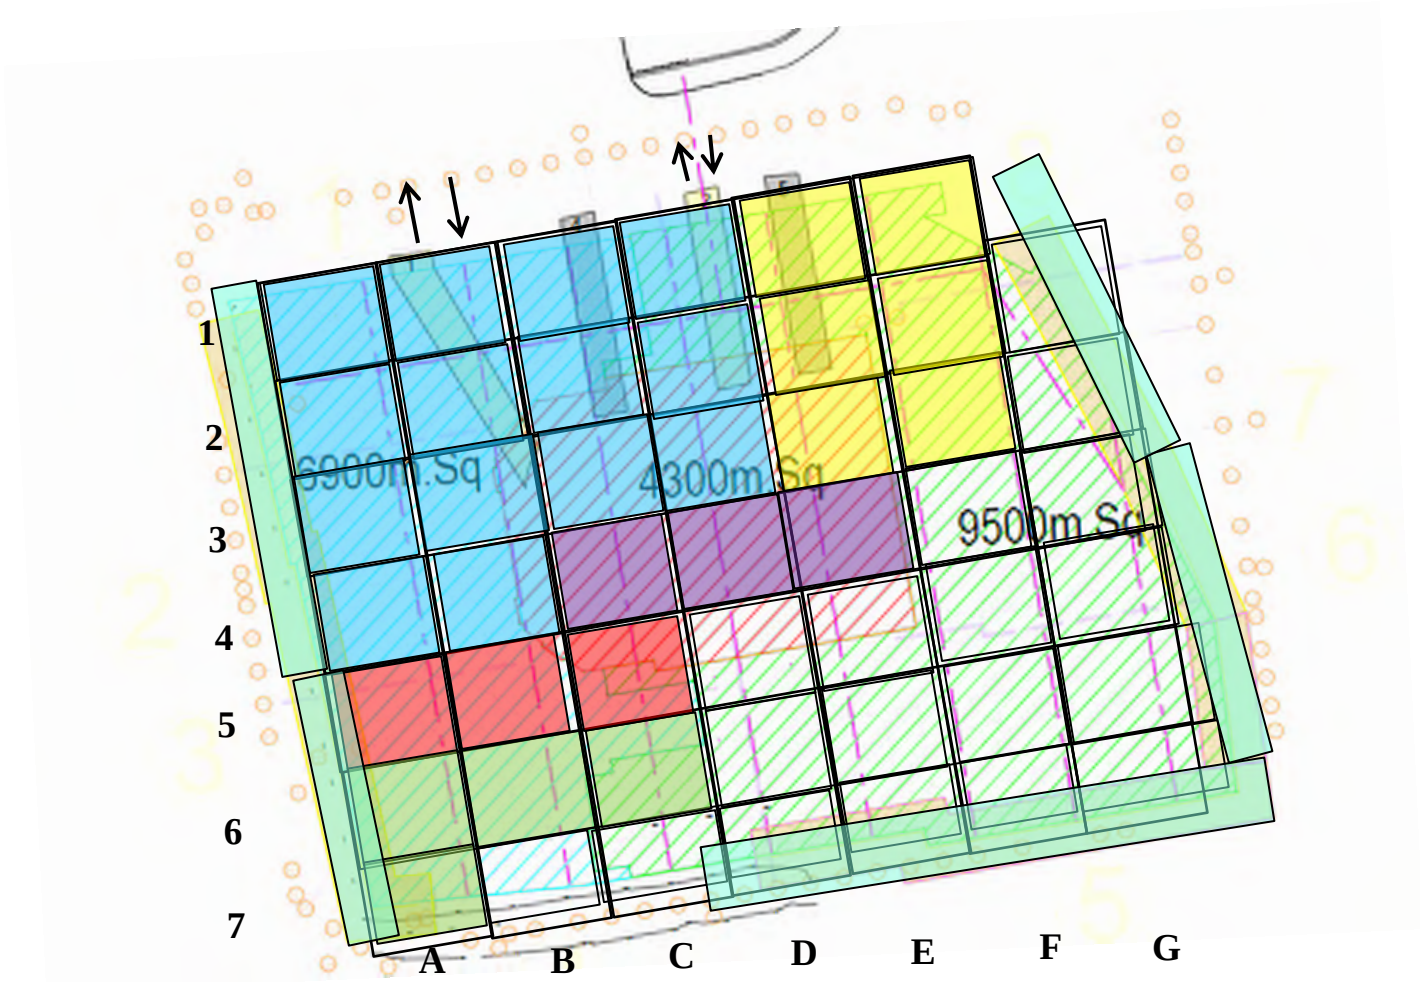

Reduced Level Excavation

Placement of Piling Mat

High Level Piling Mat

Soil Stockpile/Loading

Materials Processing Area

Works Complete

PROVECTUS

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Tel. 0118 988 0200
www.provectusgroup.com

Client: OVG

Project: Project Bradford


Job No.: 101114

Title: Remediation and Bulk Excavation works Week Site Grid 20m x 25m

Scale: NTS

Date Drawn: April 2020

Drawing No.: 101114 Week 10

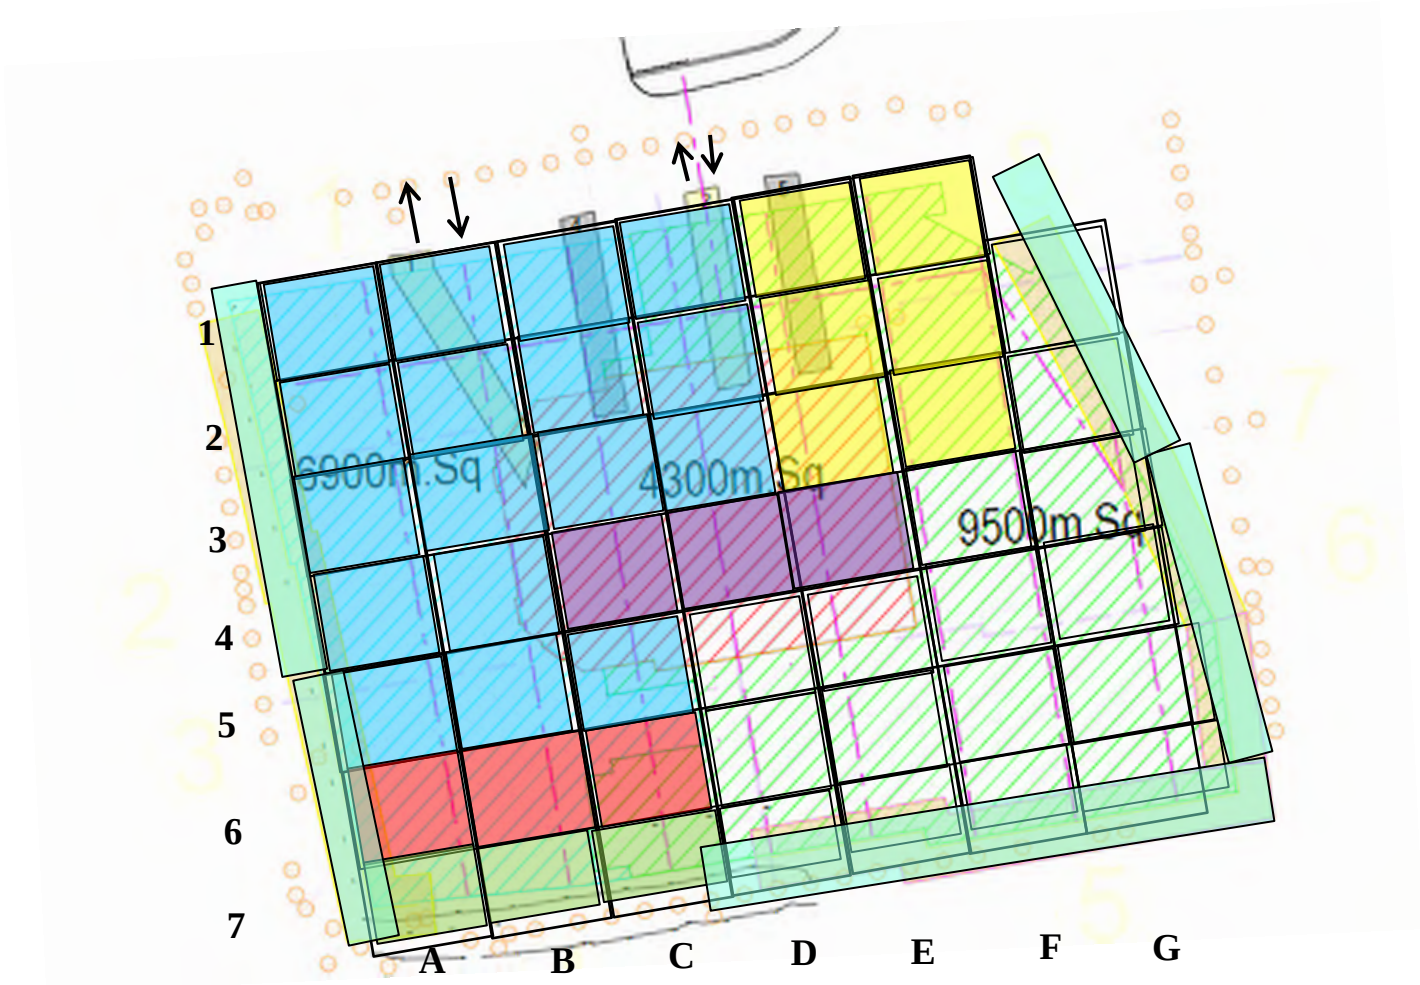

Reduced Level Excavation

Placement of Piling Mat

High Level Piling Mat

Soil Stockpile/Loading

Materials Processing Area

Works Complete

PROVECTUS

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Tel. 0118 988 0200
www.provectusgroup.com

Client: OVG

Project: Project Bradford


Job No.: 101114

Title: Remediation and Bulk Excavation works Week Site Grid 20m x 25m

Scale: NTS

Date Drawn: April 2020

Drawing No.: 101114 Week 11

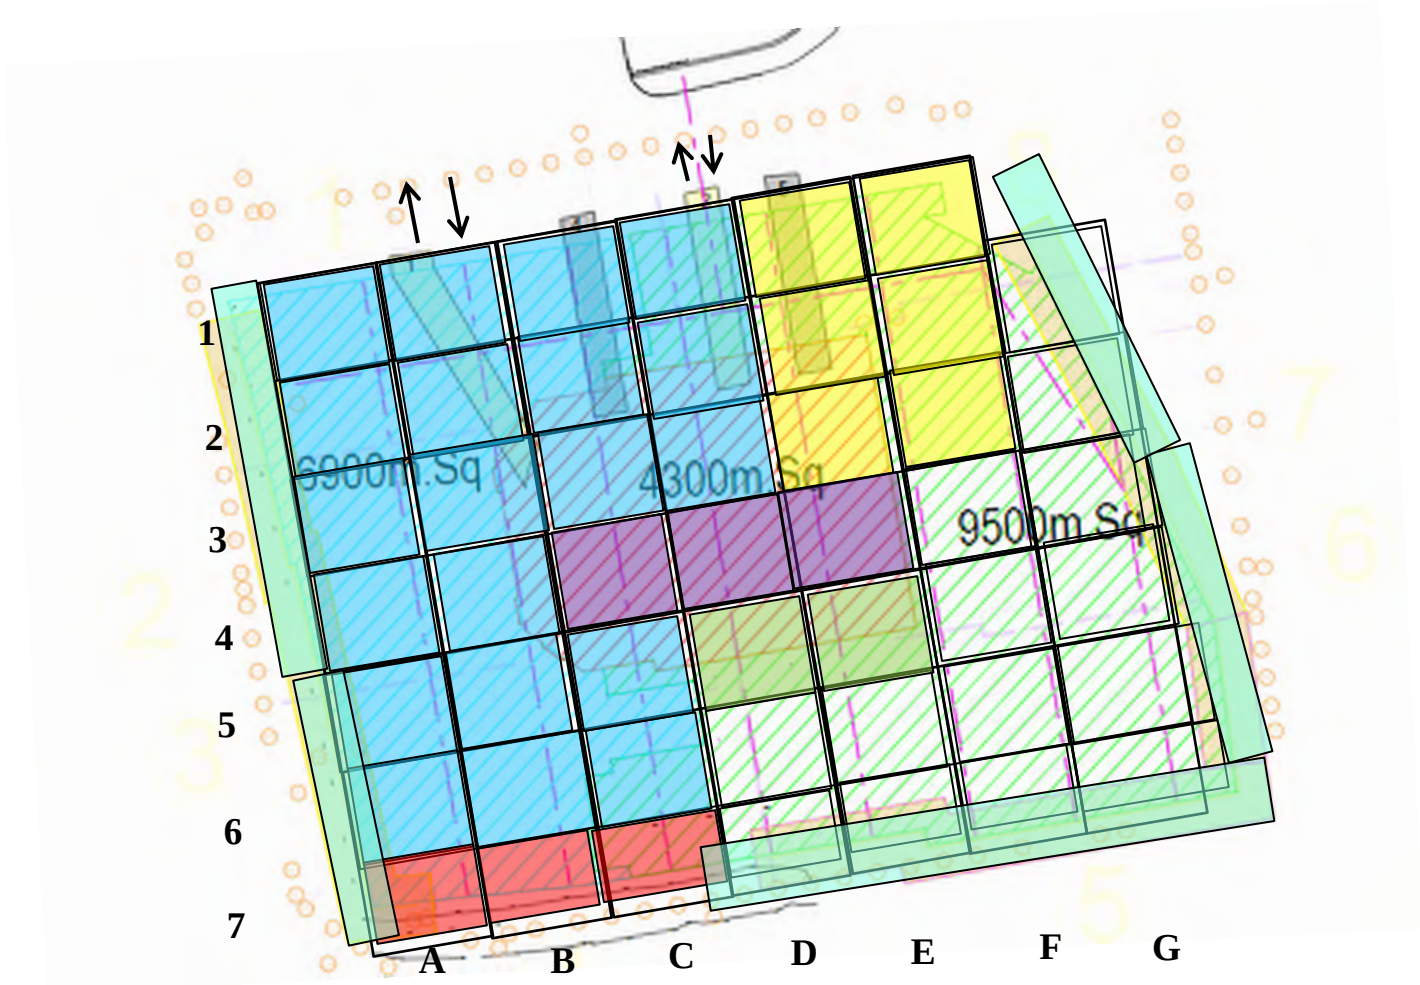

Reduced Level Excavation

Placement of Piling Mat

High Level Piling Mat

Soil Stockpile/Loading

Materials Processing Area

Works Complete

PROVECTUS

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Tel. 0118 988 0200
www.provectusgroup.com

Client: OVG

Project: Project Bradford


Job No.: 101114

Title: Remediation and Bulk Excavation works Week Site Grid 20m x 25m

Scale: NTS

Date Drawn: April 2020

Drawing No.: 101114 Week 12

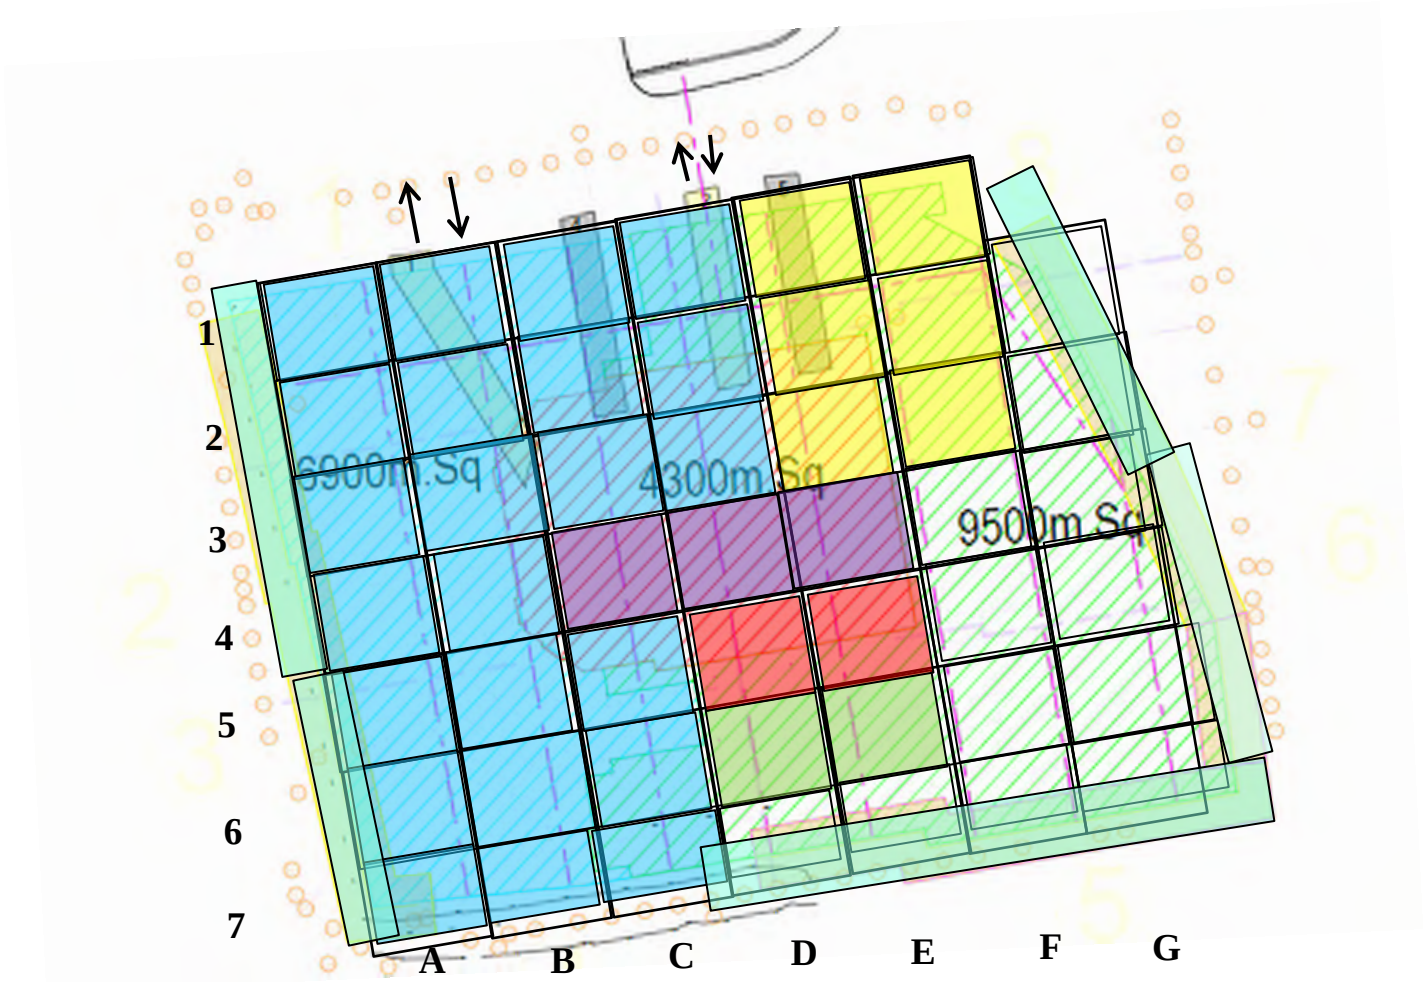

Reduced Level Excavation

Placement of Piling Mat

High Level Piling Mat

Soil Stockpile/Loading

Materials Processing Area

Works Complete

PROVECTUS

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Tel. 0118 988 0200
www.provectusgroup.com

Client: OVG

Project: Project Bradford


Job No.: 101114

Title: Remediation and Bulk Excavation works Week Site Grid 20m x 25m

Scale: NTS

Date Drawn: April 2020

Drawing No.: 101114 Week 13

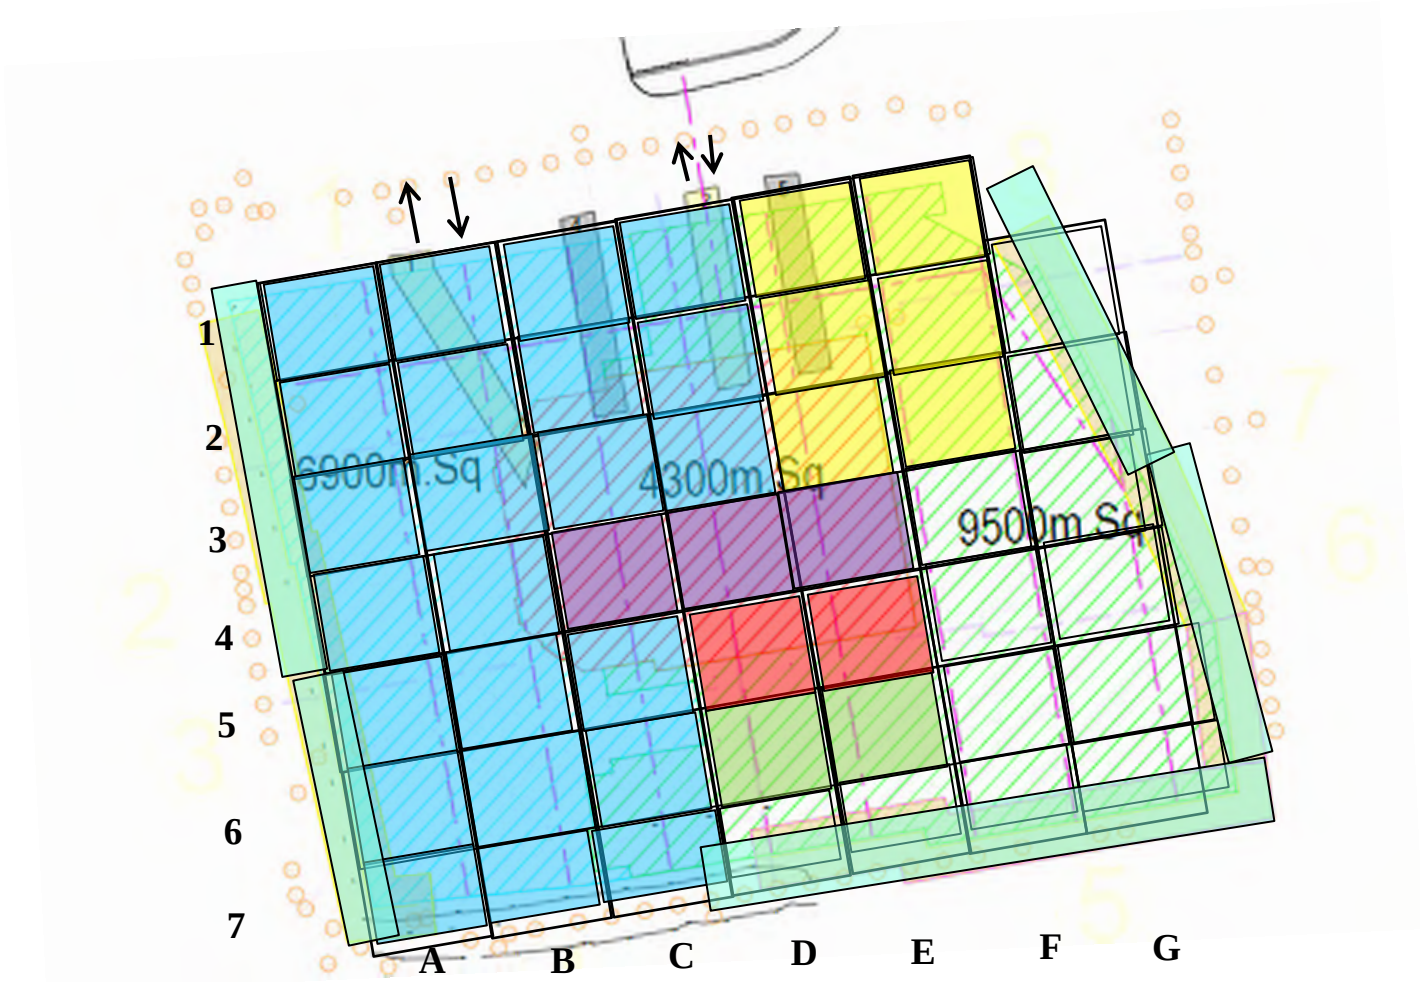

Reduced Level Excavation

Placement of Piling Mat

High Level Piling Mat

Soil Stockpile/Loading

Materials Processing Area

Works Complete

PROVECTUS

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Tel. 0118 988 0200
www.provectusgroup.com

Client: OVG

Project: Project Bradford


Job No.: 101114

Title: Remediation and Bulk Excavation works Week Site Grid 20m x 25m

Scale: NTS

Date Drawn: April 2020

Drawing No.: 101114 Week 14

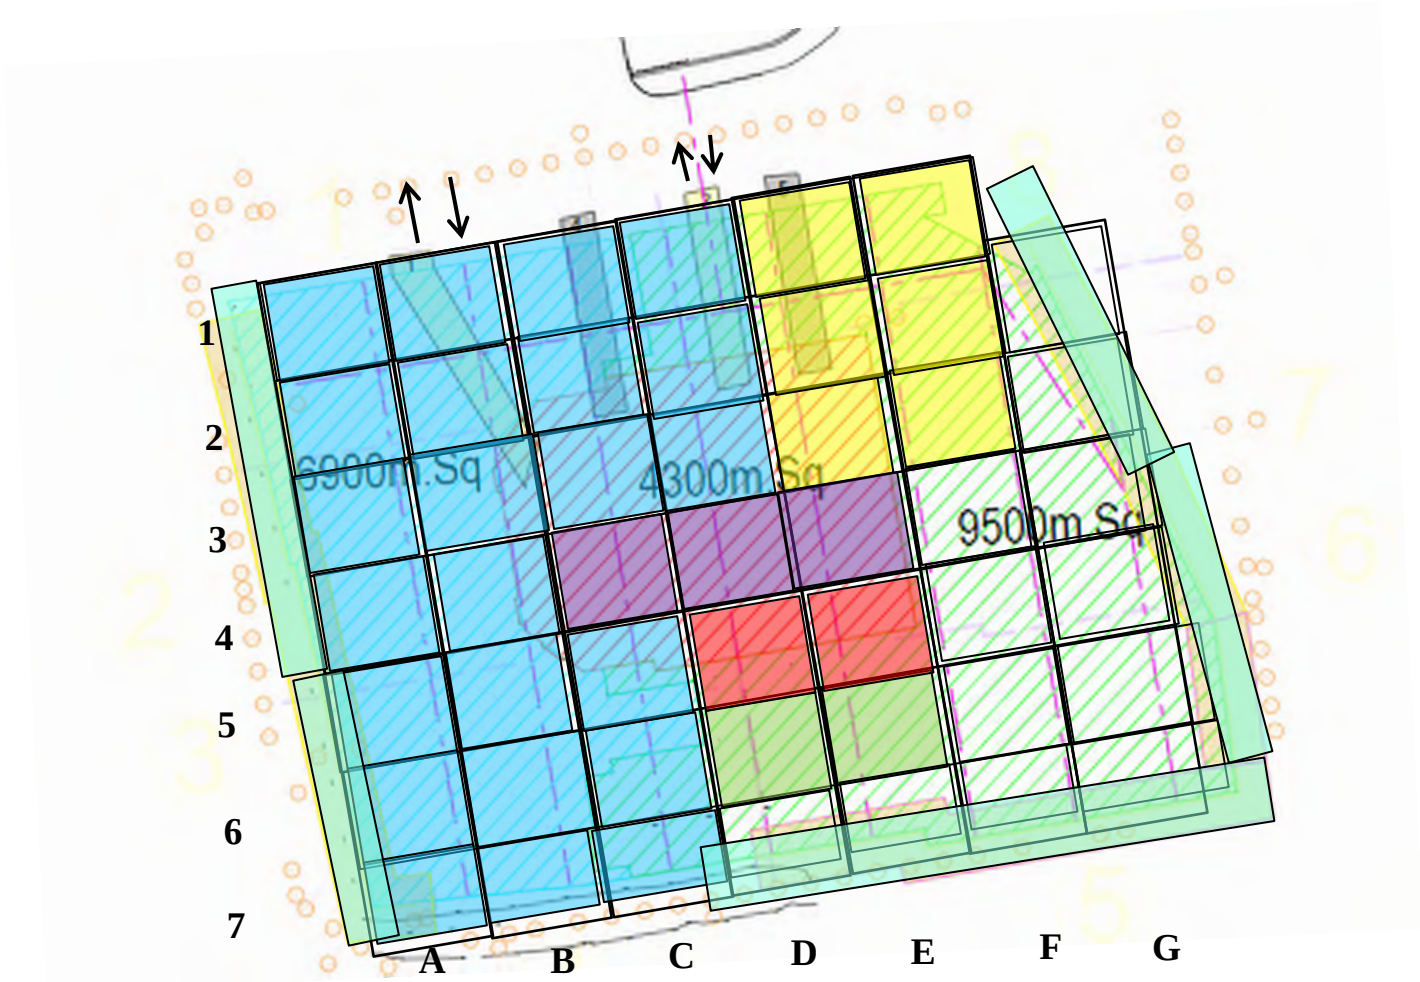

Reduced Level Excavation

Placement of Piling Mat

High Level Piling Mat

Soil Stockpile/Loading

Materials Processing Area

Works Complete

PROVECTUS

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Tel. 0118 988 0200
www.provectusgroup.com

Client: OVG

Project: Project Bradford


Job No.: 101114

Title: Remediation and Bulk Excavation works Week Site Grid 20m x 25m

Scale: NTS

Date Drawn: April 2020

Drawing No.: 101114 Week 15

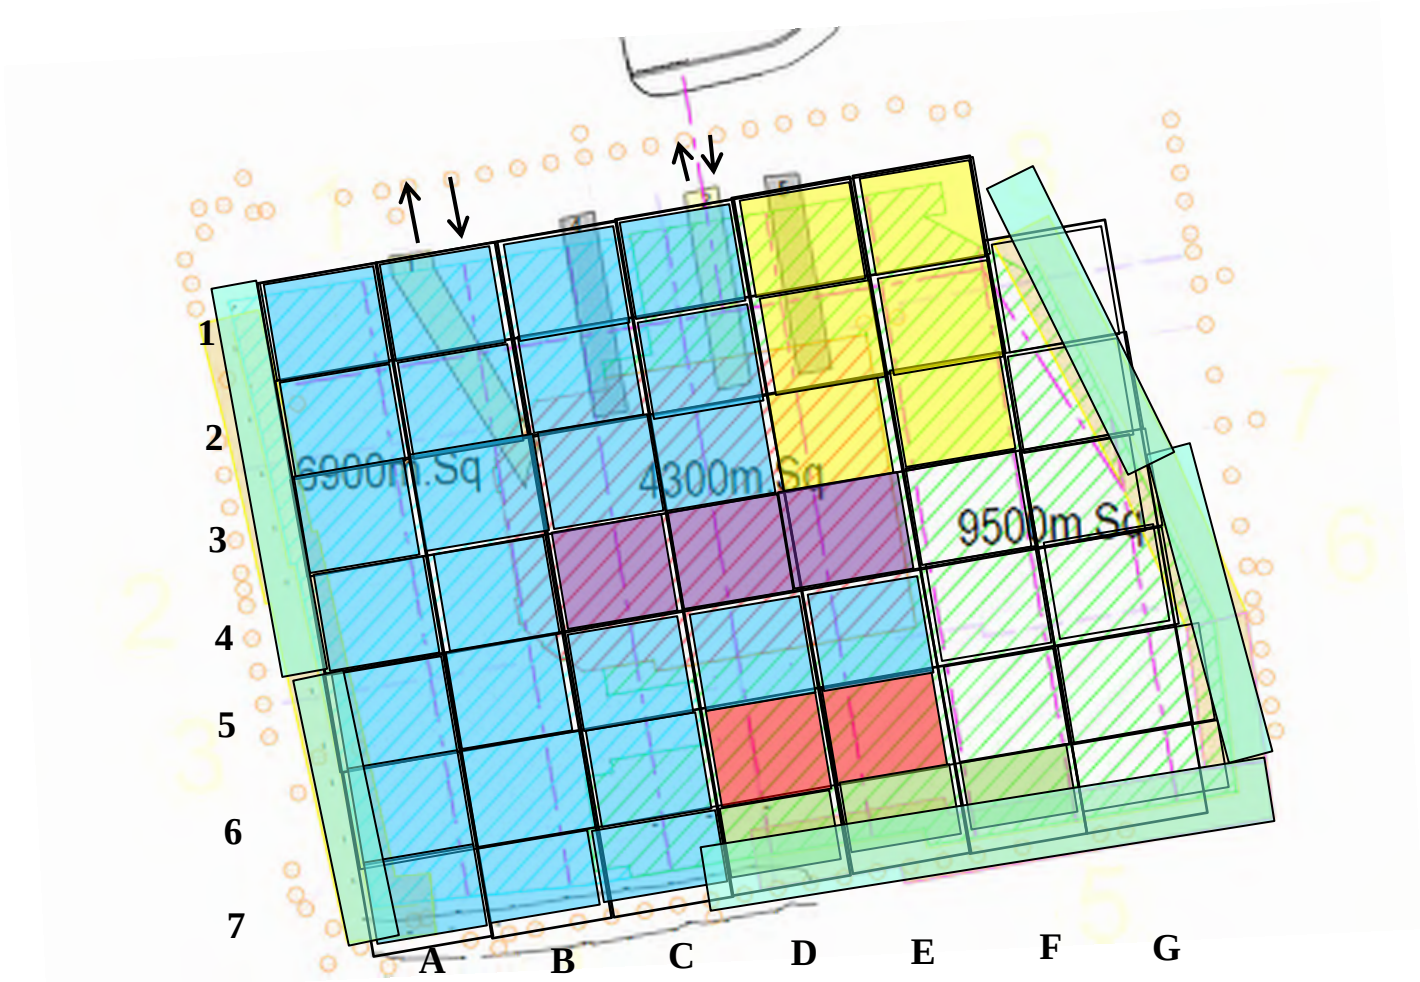

Reduced Level Excavation

Placement of Piling Mat

High Level Piling Mat

Soil Stockpile/Loading

Materials Processing Area

Works Complete

PROVECTUS

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Tel. 0118 988 0200
www.provectusgroup.com

Client: OVG

Project: Project Bradford


Job No.: 101114

Title: Remediation and Bulk Excavation works Week Site Grid 20m x 25m

Scale: NTS

Date Drawn: April 2020

Drawing No.: 101114 Week 16

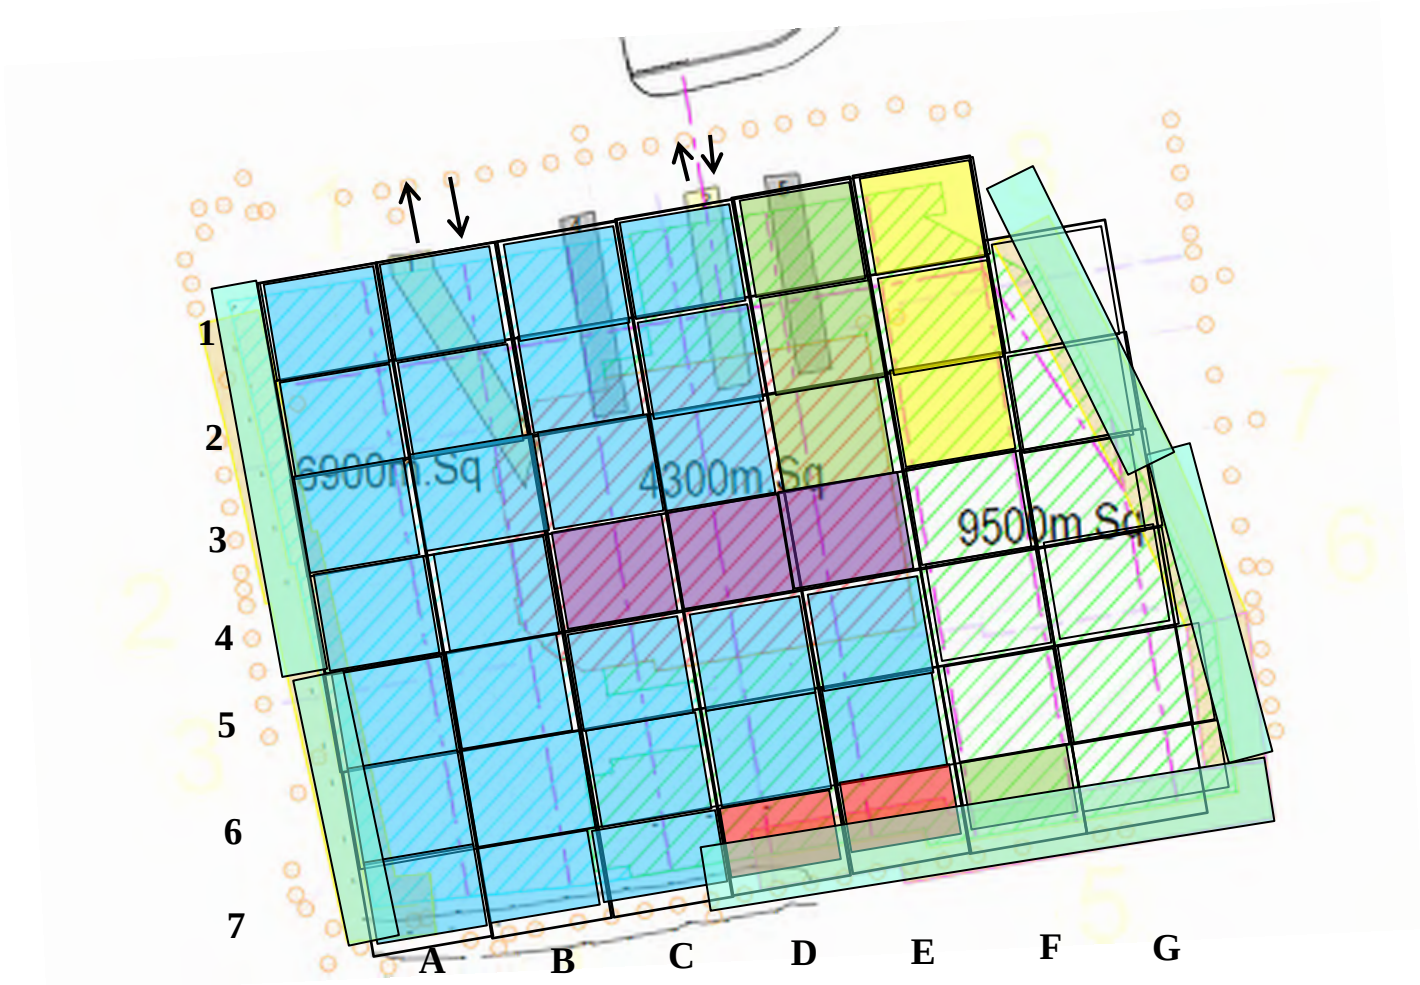

Reduced Level Excavation

Placement of Piling Mat

High Level Piling Mat

Soil Stockpile/Loading

Materials Processing Area

Works Complete

PROVECTUS

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Tel. 0118 988 0200
www.provectusgroup.com

Client: OVG

Project: Project Bradford


Job No.: 101114

Title: Remediation and Bulk Excavation works Week Site Grid 20m x 25m

Scale: NTS

Date Drawn: April 2020

Drawing No.: 101114 Week 17

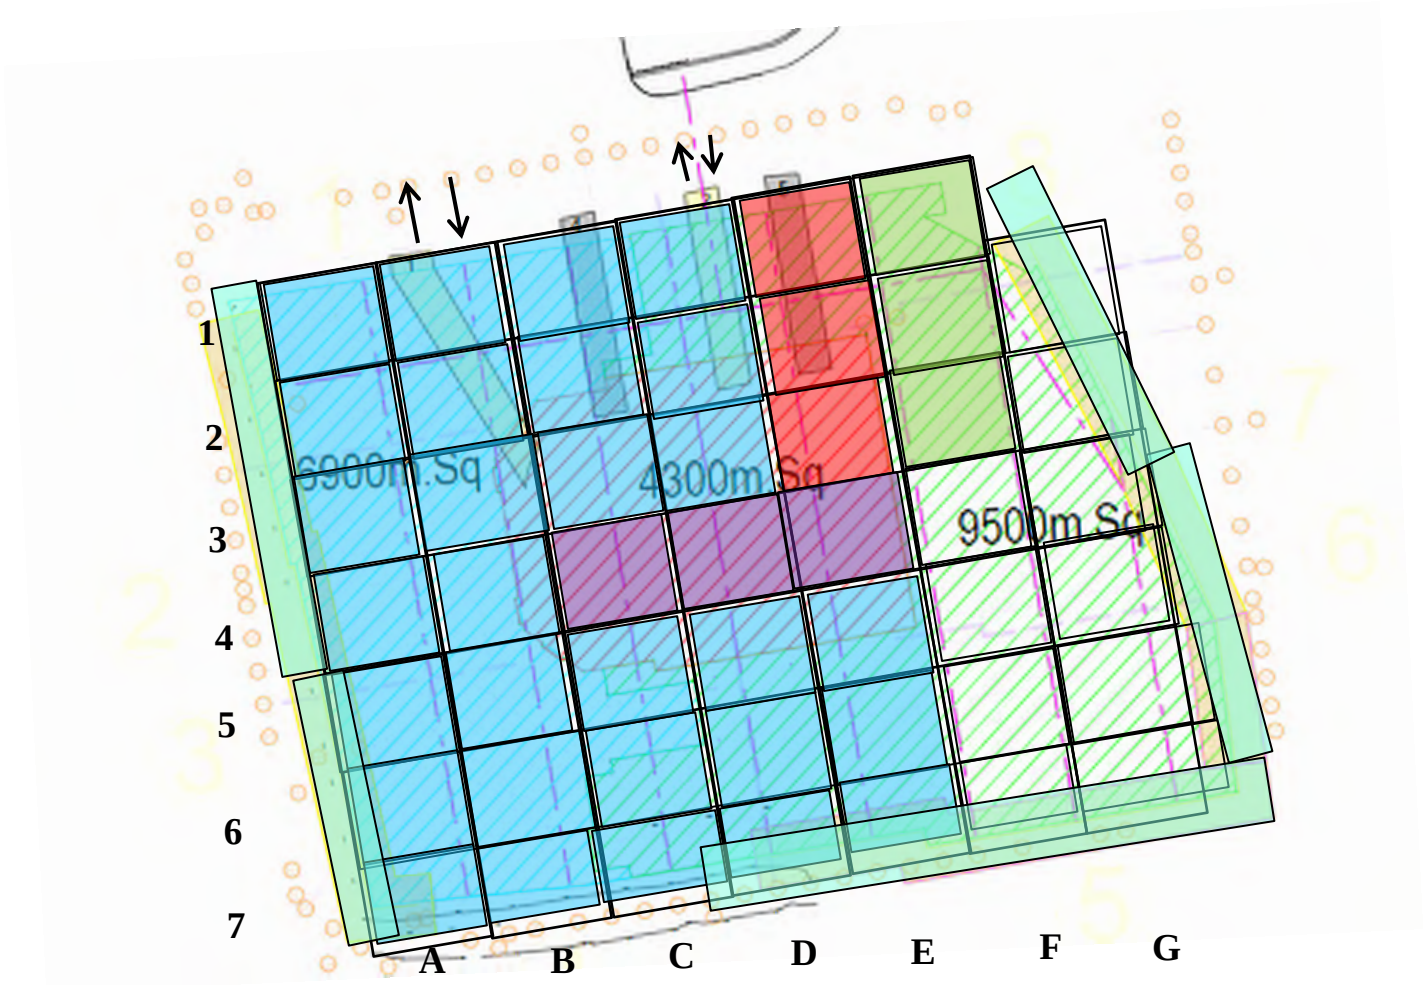

Reduced Level Excavation

Placement of Piling Mat

High Level Piling Mat

Soil Stockpile/Loading

Materials Processing Area

Works Complete

PROVECTUS

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Tel. 0118 988 0200
www.provectusgroup.com

Client: OVG

Project: Project Bradford


Job No.: 101114

Title: Remediation and Bulk Excavation works Week Site Grid 20m x 25m

Scale: NTS

Date Drawn: April 2020

Drawing No.: 101114 Week 18

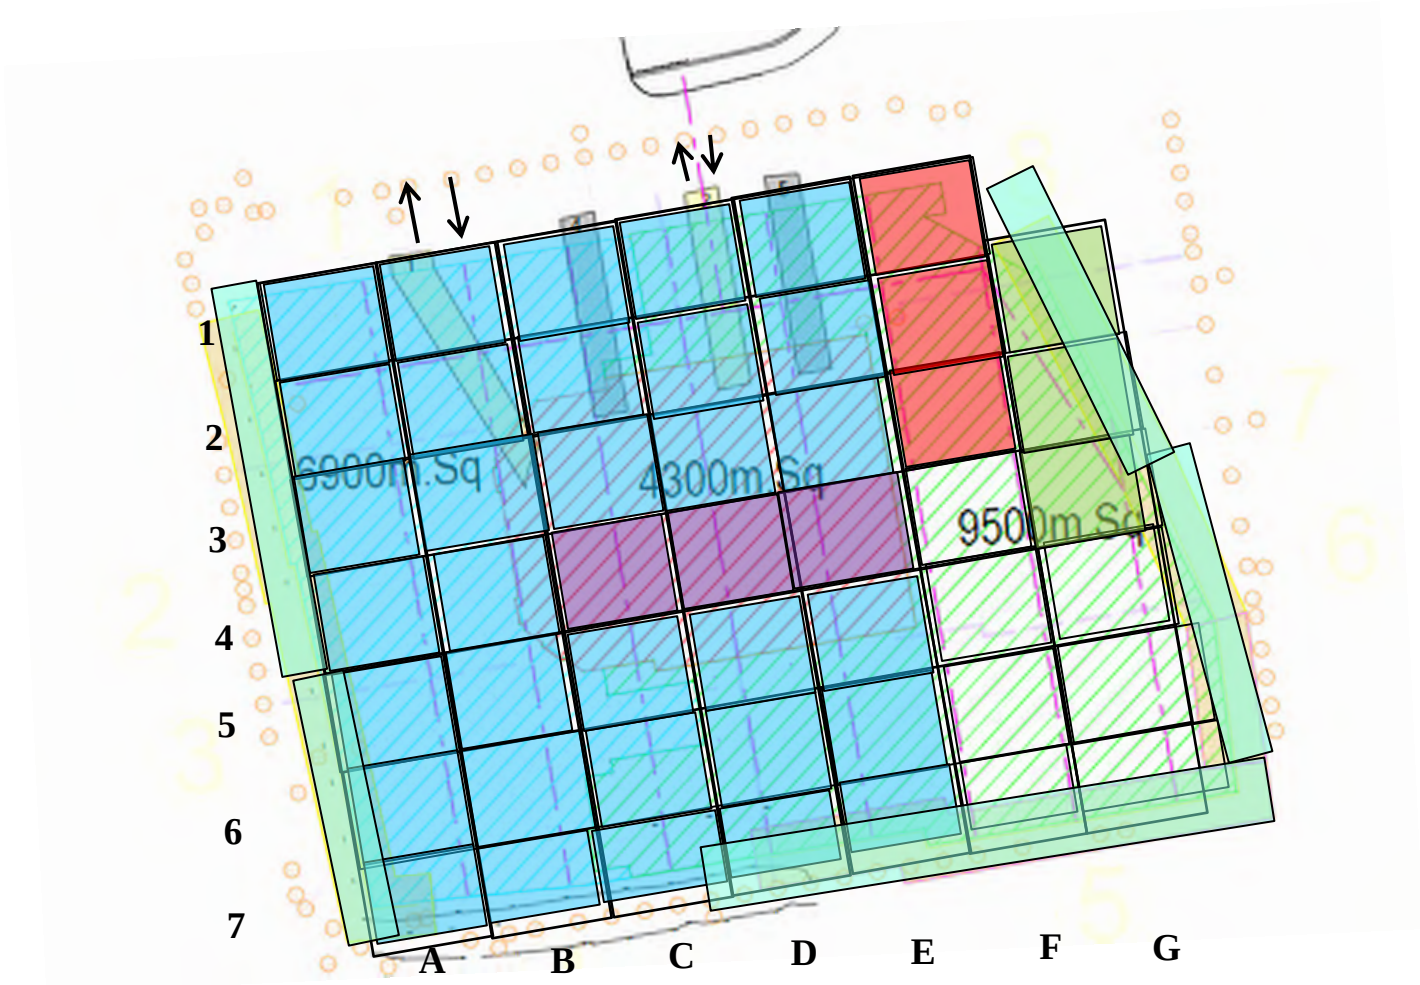

Reduced Level Excavation

Placement of Piling Mat

High Level Piling Mat

Soil Stockpile/Loading

Materials Processing Area

Works Complete

PROVECTUS

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Tel. 0118 988 0200
www.provectusgroup.com

Client: OVG

Project: Project Bradford


Job No.: 101114

Title: Remediation and Bulk Excavation works Week Site Grid 20m x 25m

Scale: NTS

Date Drawn: April 2020

Drawing No.: 101114 Week 19

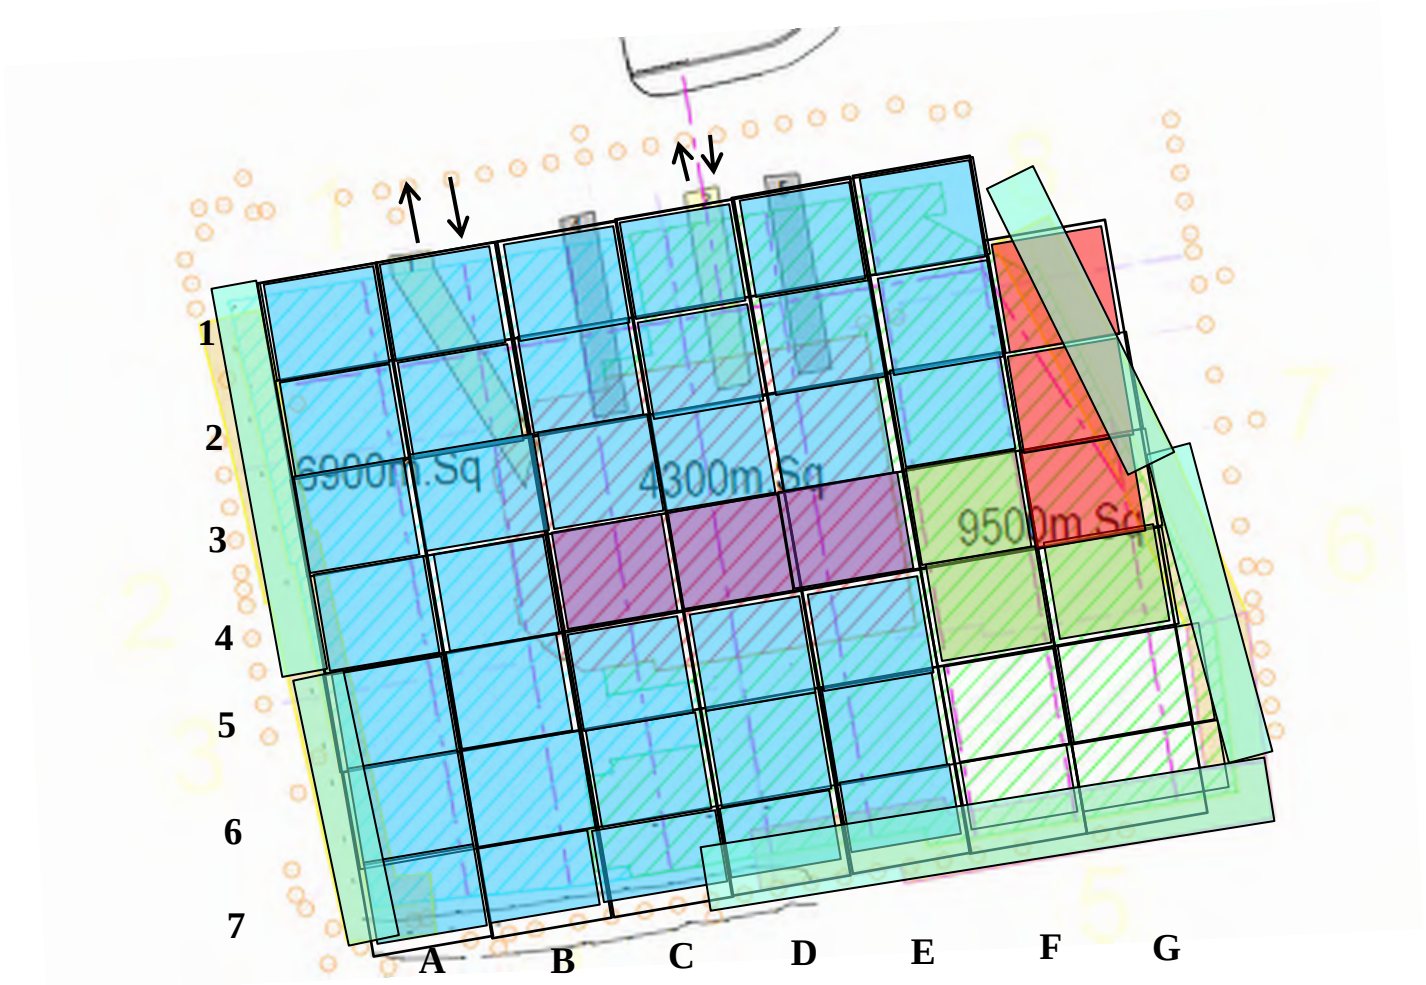

Reduced Level Excavation

Placement of Piling Mat

High Level Piling Mat

Soil Stockpile/Loading

Materials Processing Area

Works Complete

PROVECTUS

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Tel. 0118 988 0200
www.provectusgroup.com

Client: OVG

Project: Project Bradford


Job No.: 101114

Title: Remediation and Bulk Excavation works Week Site Grid 20m x 25m

Scale: NTS

Date Drawn: April 2020

Drawing No.: 101114 Week 20

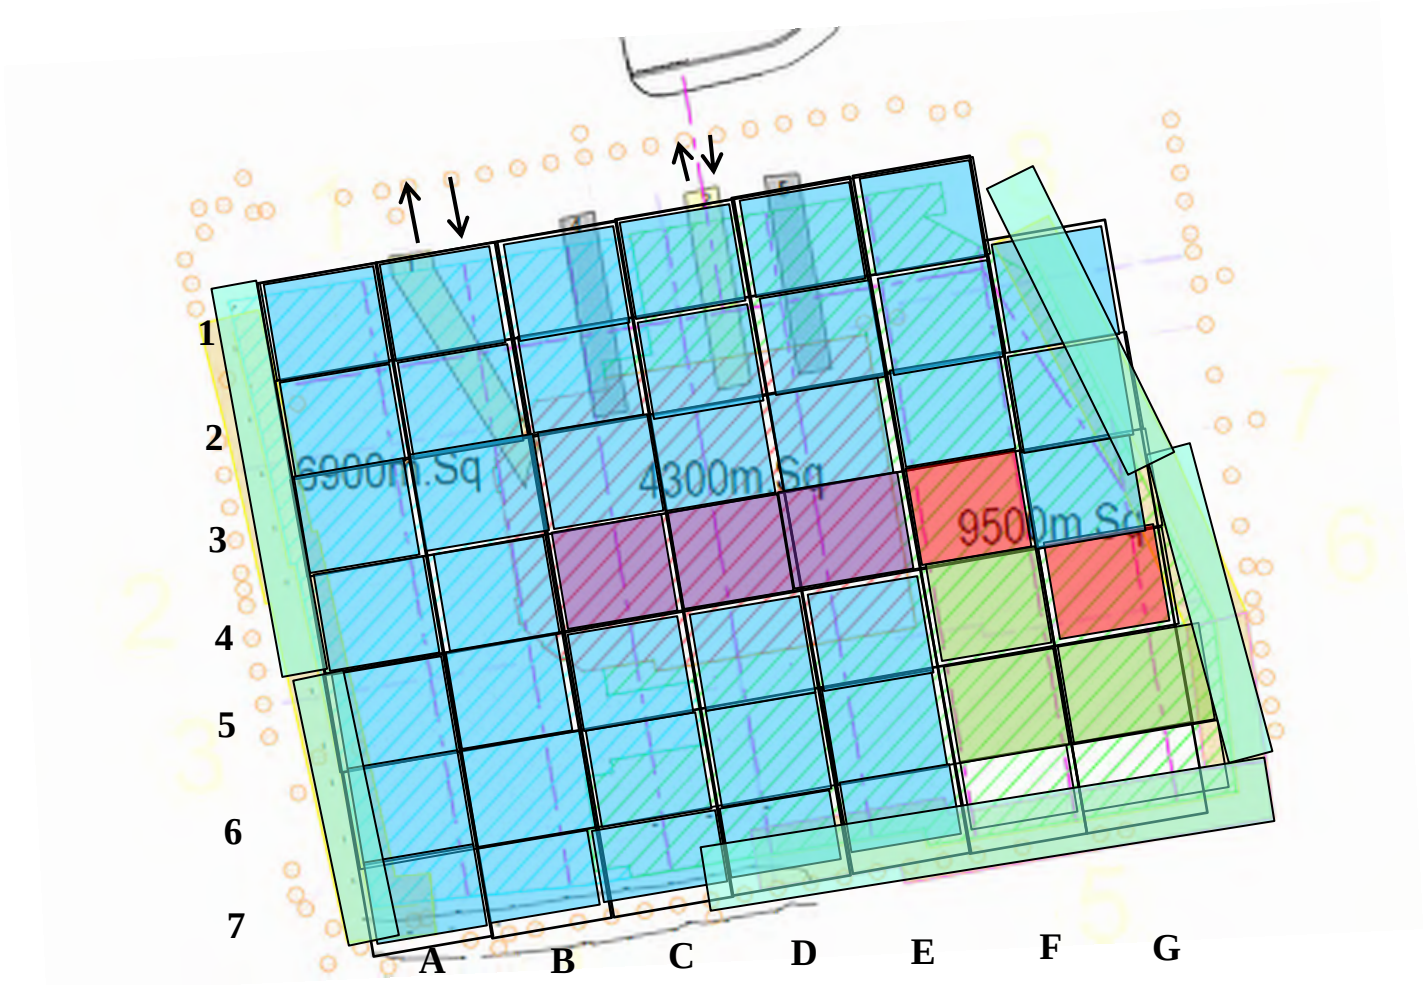

Reduced Level Excavation

Placement of Piling Mat

High Level Piling Mat

Soil Stockpile/Loading

Materials Processing Area

Works Complete

PROVECTUS

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Tel. 0118 988 0200
www.provectusgroup.com

Client: OVG

Project: Project Bradford


Job No.: 101114

Title: Remediation and Bulk Excavation works Week Site Grid 20m x 25m

Scale: NTS

Date Drawn: April 2020

Drawing No.: 101114 Week 21

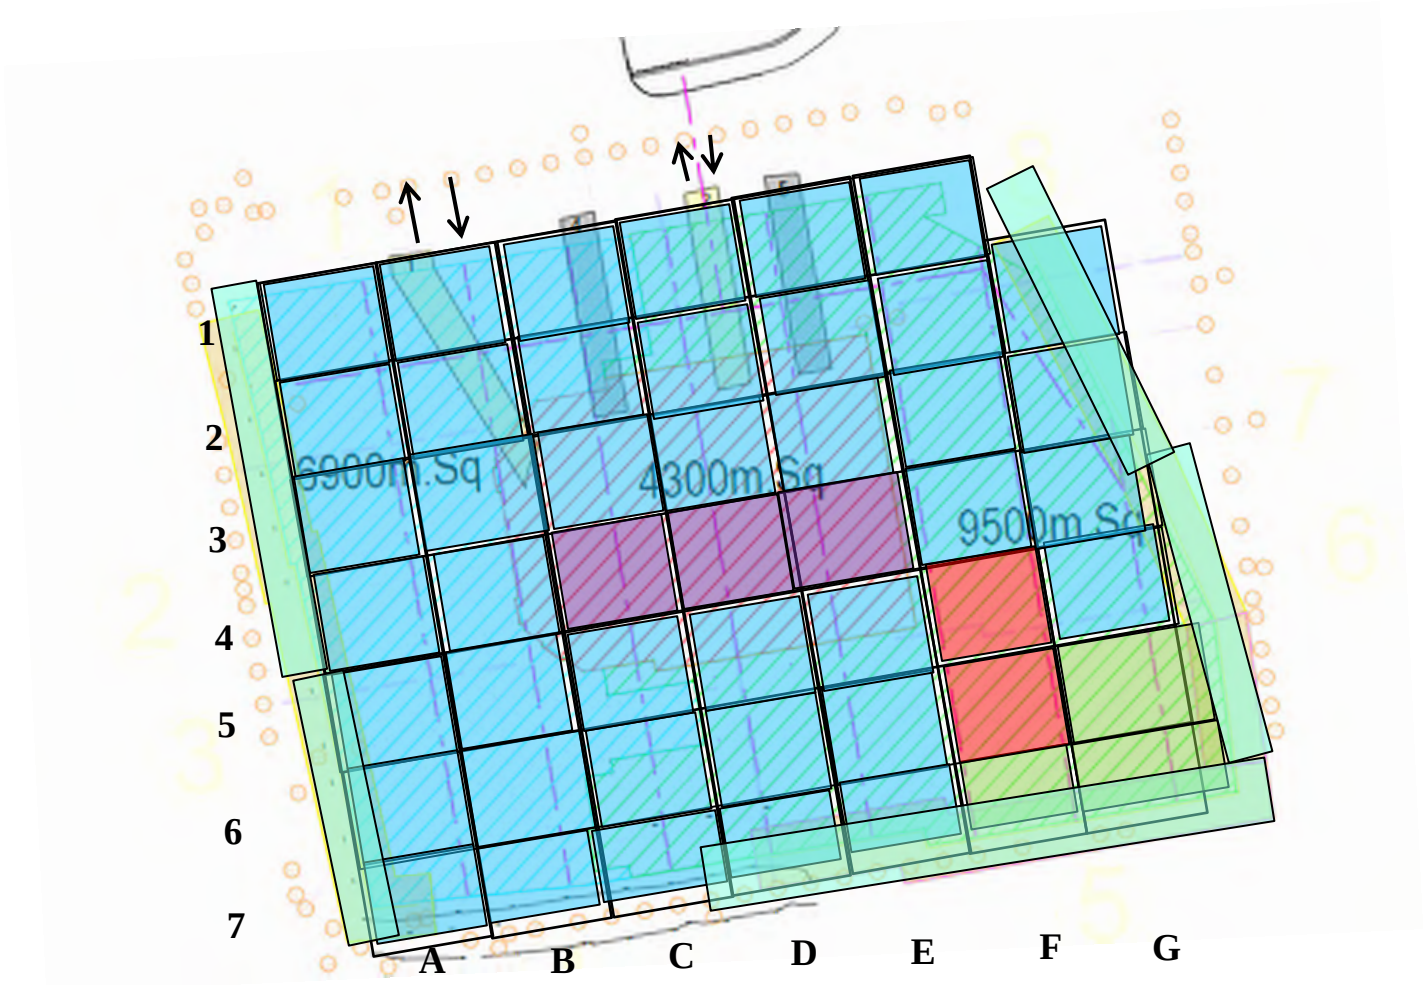

Reduced Level Excavation

Placement of Piling Mat

High Level Piling Mat

Soil Stockpile/Loading

Materials Processing Area

Works Complete

PROVECTUS

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Tel. 0118 988 0200
www.provectusgroup.com

Client: OVG

Project: Project Bradford


Job No.: 101114

Title: Remediation and Bulk Excavation works Week Site Grid 20m x 25m

Scale: NTS

Date Drawn: April 2020

Drawing No.: 101114 Week 22

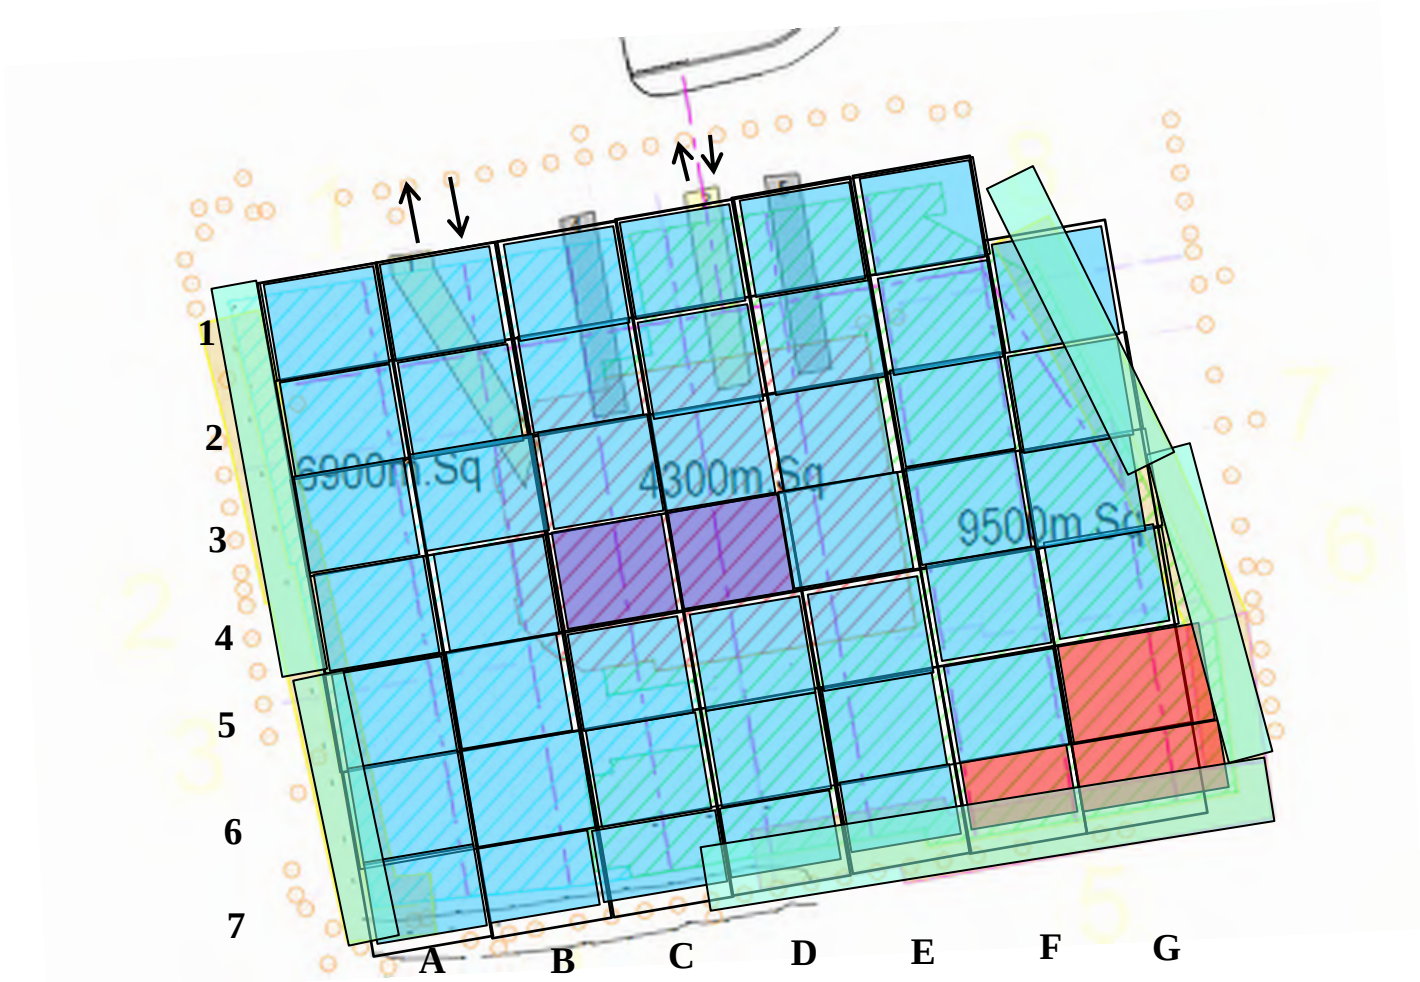

Reduced Level Excavation

Placement of Piling Mat

High Level Piling Mat

Soil Stockpile/Loading

Materials Processing Area

Works Complete

PROVECTUS

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Tel. 0118 988 0200
www.provectusgroup.com

Client: OVG

Project: Project Bradford


Job No.: 101114

Title: Remediation and Bulk Excavation works Week Site Grid 20m x 25m

Scale: NTS

Date Drawn: April 2020

Drawing No.: 101114 Week 23

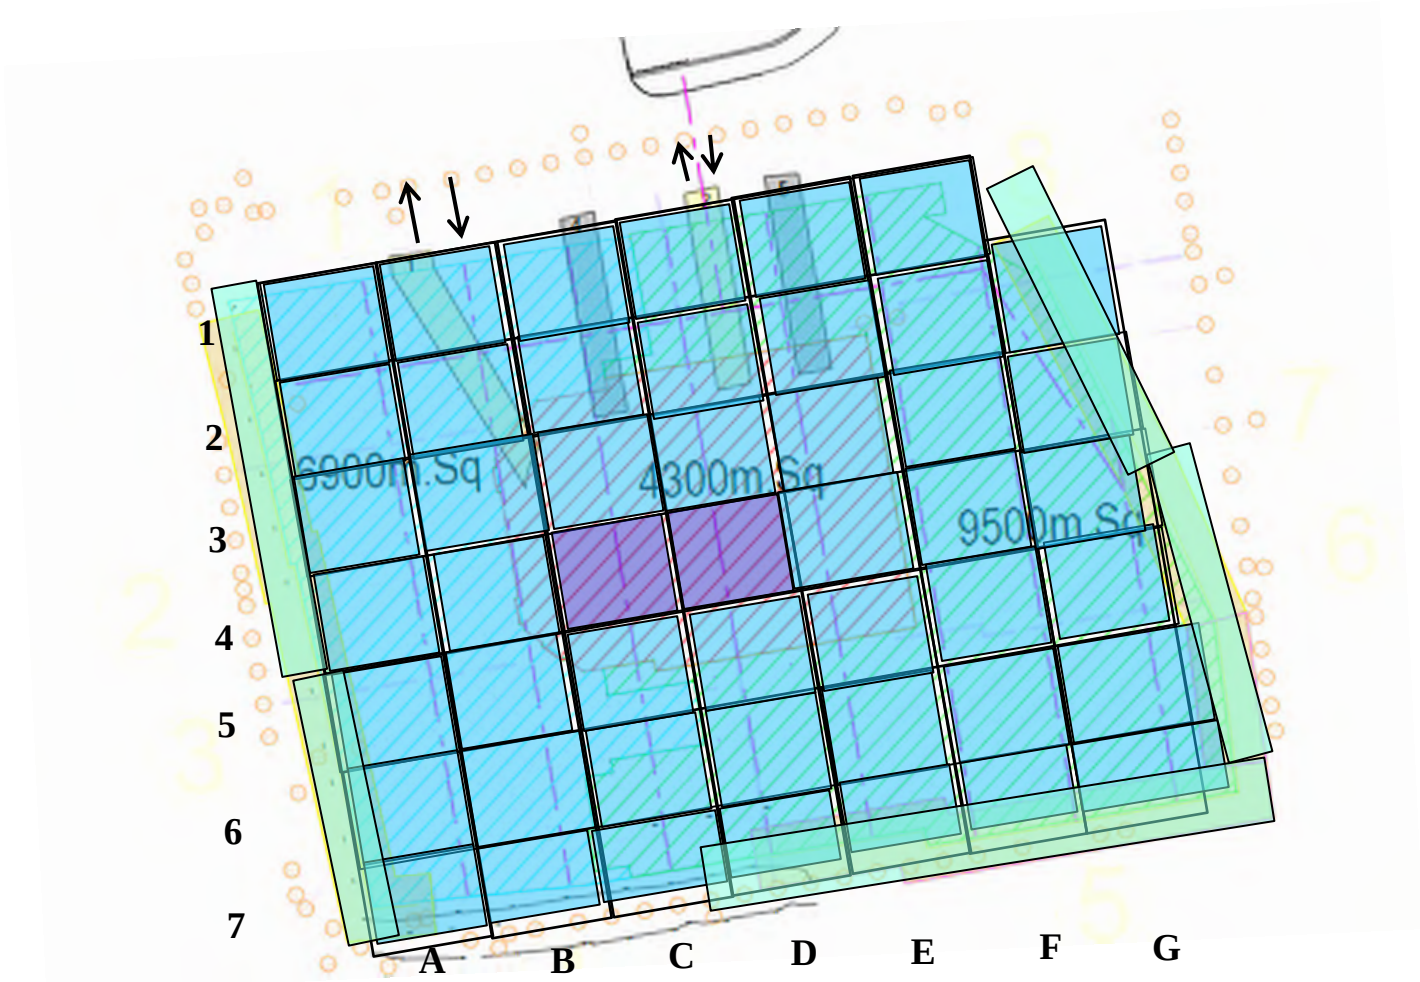

Reduced Level Excavation

Placement of Piling Mat

High Level Piling Mat

Soil Stockpile/Loading

Materials Processing Area

Works Complete

PROVECTUS

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Tel. 0118 988 0200
www.provectusgroup.com

Client: OVG

Project: Project Bradford


Job No.: 101114

Title: Remediation and Bulk Excavation works Week Site Grid 20m x 25m

Scale: NTS

Date Drawn: April 2020

Drawing No.: 101114 Week 24

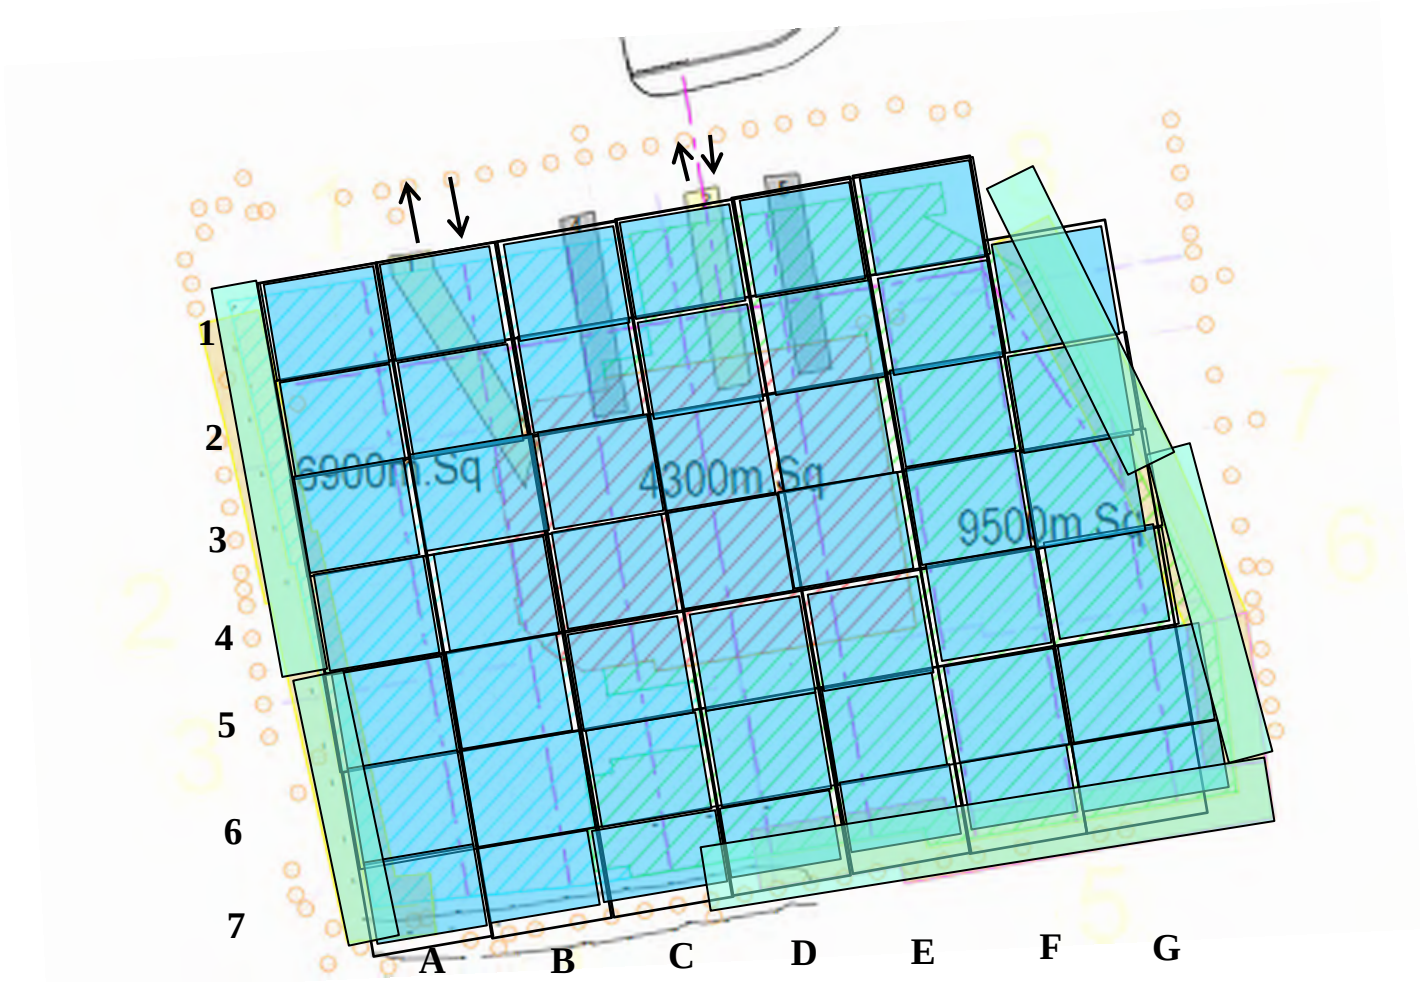

Reduced Level Excavation

Placement of Piling Mat

High Level Piling Mat

Soil Stockpile/Loading

Materials Processing Area

Works Complete

PROVECTUS

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Tel. 0118 988 0200
www.provectusgroup.com

Client: OVG

Project: Project Bradford

Job No.: 101114

Title: Remediation and Bulk Excavation works Week Site Grid 20m x 25m

Scale: NTS

Date Drawn: April 2020

Drawing No.: 101114 Week 25

Week	Exc Area	Exc Volume m3	Disposal m3	Stockpile Volume	6F2/Type 1 Import Volume m3	Daily Wagon Movements	Wagon Movements per hour	Comments
1	B1 B2 C2	3780.8	3000	780.8	675	81.7	9	
2	D1 D2 D3	4714.95	4000	1495.75	450	98.9	11	
3	A1 A2 A3 B3 West High Level Mat (HLM)	5453.175	5000	1948.925	1400	142.2	16	Utilise 2 x site entrances
4	A4 C1 West HLM and South HLM	4697.475	5000	1646.4	725	127.2	14	
5	B4 C4	4675.85	5500	822.25	450	132.2	15	
6	C3 E3 D3	6030.325	5500	1352.575	675	137.2	15	
7	D4 E4 F4	6977.65	5500	2830.225	0	122.2	14	
8	A5 B5 C5 East HLM	7057.125	5500	4387.35	675	137.2	15	
9	A6 B6	5024.775	5500	3912.125	500	133.3	15	
10	A7 C6 Stockpile/materials Processing	5250.875	5500	3663	0	122.2	14	
11	B7 C7	5388.15	5500	3551.15	675	137.2	15	
12	D5 E5	5341.825	5500	3392.975	675	137.2	15	
13	D6 E6	5032.425	5000	3425.4	450	121.1	13	
14				3425.4				
15				3425.4				
16	D7 E7	5234.3	5000	3659.7	450	121.1	13	Pile Arising Generation
17	E1 E2 F7	5373.275	5000	4032.975	450	121.1	13	Pile Arising Generation
18	F1 F2 F3	4775.3	5000	3808.275	675	126.1	14	Pile Arising Generation
19	G2 G3 G4	5649.525	5000	4457.8	675	126.1	14	Pile Arising Generation
20	G5 F5	4957.625	5000	4415.425	450	121.1	13	Pile Arising Generation
21	F6	3901.755	5000	3317.18	675	126.1	14	Pile Arising Generation
22	G6 F7 G7	5354.15	5000	3671.33	450	121.1	13	Pile Arising Generation
23	Stockpile/Arisings		2500	1171.33	675	70.6	8	Pile Arising Generation
24	Stockpile/Arisings		1000	171.33	0	22.2	2	Pile Arising Generation
25	Stockpile/Arisings		150	21.33	0	3.3	0	Pile Arising Generation

APPENDIX D Waste Disposal and Import Summary

Waste Disposal and Import Summary

PROVECTUS

Total Loads To Date	Load	Transfer note No.	Date	EWC Code	SIC Code	Material Classification/Description	Amount 8 wh = 9m3 artic = 14m3	Consignee / Receiving Facility	Haulier and Carriers Registration	Vehicle Registration
1	1	10001	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBM
2	2	10002	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
3	3	10003	16/03/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
4	4	10004	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXW
5	5	10005	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXV
6	6	10006	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBC
7	7	10007	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RLY
8	8	10008	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
9	9	10009	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
10	10	10010	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXZ
11	11	10011	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
12	12	10012	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
13	13	10013	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBM
14	14	10014	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXW
15	15	10015	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXV
16	16	10016	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBF
17	17	10017	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RLY
18	18	10018	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
19	19	10023	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
20	20	10028	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
21	21	10029	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
22	22	10030	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
23	23	10031	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
24	24	10032	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
25	25	10034	16/03/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	DK19WDD
26	26	10035	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBM
27	27	10036	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXW
28	28	10037	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXV
29	29	10038	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RLY
30	30	10039	16/03/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	DK19WDC
31	31	10040	16/03/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV18FVC
32	32	10041	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
33	33	10042	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
34	34	10043	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
35	35	10044	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX21ORT
36	36	10045	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBF
37	37	10046	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
38	38	10047	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXV
39	39	10048	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBM
40	40	10049	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXW
41	41	10050	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
42	42	10051	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RLY
43	43	10052	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
44	44	10053	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
45	45	10054	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
46	46	10055	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBF
47	47	10056	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
48	48	10057	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
49	49	10058	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
50	50	10059	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
51	51	10060	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXW
52	52	10061	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
53	53	10062	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXV
54	54	10063	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBM
55	55	10064	16/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RLY
56	56	10065	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
57	57	10066	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
58	58	10067	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
59	59	10068	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
60	60	10069	16/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
61	61	10070	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
62	62	10071	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
63	63	10072	16/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
64	64	10073	16/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXU
65	65	10074	16/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXV
66	66	10075	16/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBM
67	67	10076	16/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
68	68	10077	16/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
69	1	10078	17/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBM
70	2	10079	17/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
71	3	10080	17/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXV
72	4	10081	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
73	5	10082	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
74	6	10083	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
75	7	10084	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
76	8	10085	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
77	9	10086	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
78	10	10087	17/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBK
79	11	10088	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
80	12	10089	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYM
81	13	10090	17/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBK
82	14	10091	17/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
83	15	10092	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
84	16	10093	17/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
85	17	10094	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
86	18	10095	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
87	19	10096	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
88	20	10097	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
89	21	10098	17/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
90	22	10099	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
91	23	10100	17/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBM
92	24	10101	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
93	25	10102	17/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXV
94	26	10103	17/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
95	27	10104	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
96	28	10105	17/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
97	29	10106	17/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBK
98	30	10107	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
99	31	10108	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
100	32	10109	17/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
101	33	10110	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
102	34	10111	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
103	35	10112	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
104	36	10113	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
105	37	10114	17/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
106	38	10115	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
107	39	10116	17/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
108	40	10117	17/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBM
109	41	10118	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
110	42	10119	17/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
111	43	10120	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
112	44	10121	17/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBK
113	45	10122	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
114	46	10123	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
115	47	10124	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
116	48	10125	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
117	49	10126	17/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
118	50	10127	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
119	51	10128	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE

120	52	10129	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
121	53	10130	17/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
122	54	10131	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
123	55	10132	17/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBM
124	56	10133	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
125	57	10134	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
126	58	10135	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
127	59	10136	17/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBK
128	60	10137	17/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
129	61	10138	17/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
130	62	10139	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
131	63	10140	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
132	64	10141	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
133	65	10142	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
134	66	10143	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
135	67	10144	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
136	68	10145	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
137	69	10146	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
138	70	10147	17/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
139	71	10148	17/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
140	72	10149	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
141	73	10150	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
142	74	10151	17/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBM
143	75	10152	17/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBK
144	76	10153	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
145	77	10154	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
146	78	10155	17/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
147	79	10156	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
148	80	10157	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
149	81	10158	17/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
150	82	10159	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
151	83	10160	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
152	84	10161	17/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
153	85	10162	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
154	86	10163	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
155	87	10164	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
156	88	10165	17/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
157	89	10166	17/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
158	90	10167	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
159	91	10168	17/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBM
160	92	10169	17/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBK
161	93	10170	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
162	94	10171	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
163	95	10172	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
164	96	10173	17/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
165	97	10174	17/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
166	98	10175	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
167	99	10176	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
168	100	10177	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
169	101	10178	17/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
170	102	10179	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
171	103	10180	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
172	104	10181	17/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
173	105	10182	17/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
174	106	10183	17/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBM
175	1	10184	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
176	2	10185	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
177	3	10186	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
178	4	10188	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
179	5	10189	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
180	6	10190	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
181	7	10191	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
182	8	10192	18/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBK
183	9	10193	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
184	10	10194	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
185	11	10195	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
186	12	10196	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
187	13	10197	18/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
188	14	10198	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
189	15	10199	18/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBK
190	16	10200	18/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
191	17	10201	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
192	18	10202	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
193	19	10203	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
194	20	10204	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
195	21	10205	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
196	22	10206	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
197	23	10207	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
198	24	10208	18/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
199	25	10209	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
200	26	10210	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
201	27	10211	18/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBK
202	28	10212	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
203	29	10213	18/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
204	30	10214	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX16CVV
205	31	10215	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
206	32	10216	18/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
207	33	10217	18/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
208	34	10218	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
209	35	10219	18/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
210	36	10220	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
211	37	10221	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
212	38	10222	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
213	39	10223	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
214	40	10224	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
215	41	10225	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
216	42	10226	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
217	43	10227	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
218	44	10228	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
219	45	10229	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
220	46	10230	18/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBK
221	47	10231	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX16CVV
222	48	10232	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
223	49	10233	18/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
224	50	10234	18/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
225	51	10235	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
226	52	10236	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
227	53	10237	18/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
228	54	10238	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
229	55	10239	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
230	56	10240	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
231	57	10241	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
232	58	10242	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
233	59	10243	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
234	60	10244	18/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBK
235	61	10245	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
236	62	10246	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
237	63	10247	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX16CVV
238	64	10248	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
239	65	10249	18/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
240	66	10250	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
241	67	10251	18/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
242	68	10252	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
243	69	10253	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
244	70	10254	18/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
245	71	10255	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
246	72	10256	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD

247	73	10257	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
248	74	10258	18/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBK
249	75	10259	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
250	76	10260	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
251	77	10261	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
252	78	10262	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
253	79	10263	18/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
254	80	10264	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
255	81	10265	18/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
256	82	10266	18/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
257	83	10267	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX16CVV
258	84	10268	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
259	85	10269	18/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
260	86	10270	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
261	87	10271	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
262	88	10272	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
263	89	10273	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
264	90	10274	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
265	91	10275	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
266	92	10276	18/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBK
267	93	10277	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
268	94	10278	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
269	95	10279	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
270	96	10280	18/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBM
271	97	10281	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
272	98	10282	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
273	99	10283	18/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
274	100	10284	18/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
275	101	10285	18/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
276	102	10286	18/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
277	103	10287	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX16CVV
278	104	10288	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
279	105	10289	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
280	106	10290	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
281	107	10291	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
282	108	10292	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
283	109	10293	18/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBK
284	110	10294	18/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
285	1	10295	19/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
286	2	10296	19/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
287	3	10297	19/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBD
288	4	10298	19/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
289	5	10299	19/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
290	6	10300	19/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
291	7	10301	19/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXD
292	8	10302	19/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBK
293	9	10303	19/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXZ
294	10	10304	19/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
295	11	10305	19/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
296	12	10306	19/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
297	13	10307	19/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
298	14	10308	19/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
299	15	10309	19/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
300	16	10310	19/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBF
301	17	10311	19/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
302	18	10312	19/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
303	19	10313	19/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
304	20	10314	19/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
305	21	10315	19/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
306	22	10316	19/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
307	23	10317	19/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
308	24	10318	19/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
309	25	10319	19/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
310	26	10320	19/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
311	27	10321	19/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
312	28	10322	19/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
313	29	10323	19/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBM
314	30	10324	19/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MX21BXW
315	31	10325	19/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
316	32	10326	19/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
317	33	10327	19/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
318	34	10328	19/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
319	35	10329	19/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
320	36	10330	19/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
321	37	10331	19/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
322	38	10332	19/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
323	39	10333	19/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
324	40	10334	19/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
325	41	10335	19/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
326	42	10336	19/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV18UBC
327	43	10337	19/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
328	44	10338	19/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
329	45	10339	19/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
330	46	10340	19/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
331	47	10341	19/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
332	48	10342	19/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
333	49	10343	19/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXM
334	50	10344	19/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXU
335	51	10345	19/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
336	52	10346	19/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
337	1	10347	22/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
338	2	10348	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19YBK
339	3	10349	22/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBD
340	4	10350	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
341	5	10351	22/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
342	6	10352	22/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
343	7	10353	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
344	8	10354	22/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKN
345	9	10355	22/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
346	10	10356	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
347	11	10357	22/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
348	12	10358	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
349	13	10359	22/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
350	14	10360	22/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
351	15	10361	22/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
352	16	10362	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
353	17	10363	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
354	18	10364	22/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBL
355	19	10365	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
356	20	10366	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
357	21	10367	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
358	22	10368	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
359	23	10369	22/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
360	24	10370	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBK
361	25	10371	22/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
362	26	10372	22/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
363	27	10373	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
364	28	10374	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
365	29	10375	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
366	30	10376	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
367	31	10377	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
368	32	10378	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
369	33	10379	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
370	34	10380	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
371	35	10381	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
372	36	10382	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
373	37	10383	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBL

374	38	10384	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
375	39	10385	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
376	40	10386	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
377	41	10387	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
378	42	10388	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
379	43	10389	22/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
380	44	10390	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
381	45	10391	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
382	46	10392	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBK
383	47	10393	22/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
384	48	10394	22/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
385	49	10395	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
386	50	10396	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
387	51	10397	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
388	52	10398	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
389	53	10399	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
390	54	10400	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
391	55	10401	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
392	56	10402	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
393	57	10403	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
394	58	10404	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
395	59	10405	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBL
396	60	10406	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
397	61	10407	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
398	62	10408	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
399	63	10409	22/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
400	64	10410	22/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBA
401	65	10411	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
402	66	10412	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBK
403	67	10413	22/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
404	68	10414	22/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
405	69	10415	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
406	70	10416	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
407	71	10417	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
408	72	10418	22/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXM
409	73	10419	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
410	74	10420	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
411	75	10421	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
412	76	10422	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
413	77	10423	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
414	78	10424	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBL
415	79	10425	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
416	80	10426	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
417	81	10427	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
418	82	10428	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
419	83	10429	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
420	84	10430	22/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
421	85	10431	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
422	86	10432	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
423	87	10433	22/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBK
424	88	10434	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
425	89	10435	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
426	90	10436	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
427	91	10437	22/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
428	92	10438	22/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXM
429	93	10439	22/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
430	94	10440	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
431	95	10441	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBL
432	96	10442	22/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
433	97	10443	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
434	98	10444	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
435	99	10445	22/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
436	100	10446	22/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
437	101	10447	22/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
438	102	10448	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
439	103	10449	22/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBK
440	104	10450	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
441	105	10451	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
442	106	10452	22/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
443	107	10453	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
444	108	10454	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
445	109	10455	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
446	110	10456	22/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
447	111	10457	22/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBL
448	112	10458	22/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
449	113	10459	22/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
450	114	10460	22/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BYL
451	115	10461	22/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
452	116	10462	22/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
453	117	10463	22/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
454	118	10464	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
455	119	10465	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
456	120	10466	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
457	121	10467	22/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBK
458	122	10468	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
459	123	10469	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
460	124	10470	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
461	125	10471	22/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
462	126	10472	22/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
463	127	10473	22/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXM
464	128	10474	22/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
465	1	PROVEC50001	23/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
466	2	10475	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
467	3	10476	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBK
468	4	PROVEC50002	23/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYH
469	5	PROVEC50003	23/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYJ
470	6	10477	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
471	7	10478	23/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXU
472	8	10479	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
473	9	10480	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
474	10	10481	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
475	11	PROVEC50004	23/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBB
476	12	10482	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
477	13	10483	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
478	14	10484	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
479	15	10485	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBL
480	16	PROVEC50005	23/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
481	17	10486	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
482	18	PROVEC50006	23/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
483	19	10487	23/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MC16CVV
484	20	10488	23/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
485	21	10489	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
486	22	10490	23/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
487	23	10491	23/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
488	24	10492	23/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
489	25	10493	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
490	26	10494	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
491	27	10495	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBK
492	28	10496	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
493	29	10497	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
494	30	10498	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
495	31	10499	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
496	32	10500	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBL
497	33	10501	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
498	34	10502	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
499	35	10503	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
500	36	10504	23/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD

501	37	10505	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK20RKF
502	38	10506	23/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXU
503	39	10507	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
504	40	10508	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
505	41	10509	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBK
506	42	10510	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
507	43	10511	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
508	44	10512	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
509	45	10513	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
510	46	10514	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
511	47	10515	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
512	48	10516	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
513	49	10517	23/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
514	50	10518	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBL
515	51	10519	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
516	52	10520	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
517	53	10521	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
518	54	10522	23/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXU
519	55	PROVEC50012	23/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
520	56	PROVEC50013	23/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYH
521	57	PROVEC50014	23/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYJ
522	58	PROVEC50015	23/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBB
523	59	PROVEC50016	23/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
524	60	PROVEC50017	23/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
525	61	10523	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
526	62	10524	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBK
527	63	10525	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
528	64	10526	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
529	65	10527	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
530	66	10528	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
531	67	10529	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
532	68	10530	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
533	69	10531	23/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
534	70	10532	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBL
535	71	10533	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
536	72	10534	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
537	73	10535	23/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXU
538	74	10536	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
539	75	10537	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
540	76	10538	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBK
541	77	10539	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
542	78	10540	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
543	79	10541	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
544	80	10542	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
545	81	10543	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
546	82	10544	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
547	83	10545	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19 UBL
548	84	10546	23/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
549	85	10547	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
550	86	10548	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
551	87	10549	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
552	88	10550	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
553	89	10551	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBK
554	90	10552	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
555	91	10553	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
556	92	PROVEC50018	23/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
557	93	PROVEC50019	23/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYH
558	94	PROVEC50020	23/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYJ
559	95	PROVEC50021	23/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBE
560	96	PROVEC50022	23/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
561	97	PROVEC50023	23/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
562	98	10554	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
563	99	10555	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
564	100	10556	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
565	101	10557	23/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
566	102	10558	23/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
567	103	10559	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBL
568	104	10560	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXU
569	105	10561	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
570	106	10562	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXO
571	107	10563	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
572	108	10564	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
573	109	10565	23/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBE
574	110	10566	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
575	111	10567	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
576	112	10568	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBK
577	113	10569	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
578	114	10570	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
579	115	10571	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBM
580	116	10572	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
581	117	10573	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
582	118	10574	23/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
583	1	PROVEC50024	24/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
584	2	PROVEC50025	24/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYJ
585	3	PROVEC50026	24/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYH
586	4	10575	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
587	5	10576	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBK
588	6	10577	24/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBD
589	7	10578	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXZ
590	8	10579	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
591	9	PROVEC50027	24/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	DK19WDA
592	10	PROVEC50028	24/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
593	11	PROVEC50029	24/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBB
594	12	10580	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
595	13	10581	24/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXW
596	14	10582	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
597	15	10583	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
598	16	10584	24/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXV
599	17	PROVEC50030	24/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
600	18	10585	24/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXV
601	19	10586	24/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX16CVV
602	20	10587	24/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
603	21	10588	24/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
604	22	PROVEC50031	24/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	DK19WDD
605	23	10589	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
606	24	10590	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
607	25	10591	24/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
608	26	10592	24/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
609	27	10593	24/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBL
610	28	10594	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
611	29	10595	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
612	30	10596	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
613	31	10597	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
614	32	10598	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
615	33	10599	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
616	34	10600	24/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXU
617	35	10601	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
618	36	10602	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBK
619	37	10603	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
620	38	10604	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
621	39	10605	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
622	40	10606	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
623	41	10607	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
624	42	10608	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
625	43	10609	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
626	44	10610	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
627	45	10611	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC

628	46	10612	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
629	47	10613	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
630	48	PROVEC50032	24/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
631	49	PROVEC50033	24/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYH
632	50	10614	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBK
633	51	10615	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
634	52	10616	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
635	53	10617	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
636	54	PROVEC50034	24/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK19BYJ
637	55	10618	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
638	56	PROVEC50035	24/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	DK19WDA
639	57	10619	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK19BXP
640	58	10620	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK19BXN
641	59	10621	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
642	60	10622	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
643	61	10623	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
644	62	10624	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MB20RLY
645	63	10625	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
646	64	PROVEC50036	24/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
647	65	PROVEC50037	24/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBB
648	66	10626	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
649	67	PROVEC50038	24/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
650	68	PROVEC50039	24/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	DK19WDD
651	69	10627	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBK
652	70	10628	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
653	71	10629	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
654	72	10630	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
655	73	10631	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
656	74	10632	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
657	75	10633	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
658	76	10634	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
659	77	10635	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
660	78	10636	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
661	79	10637	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
662	80	10638	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
663	81	10639	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
664	82	10640	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBK
665	83	10641	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
666	84	10642	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
667	85	10643	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
668	86	10644	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
669	87	10645	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
670	88	PROVEC50040	24/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
671	89	10646	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
672	90	10647	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXO
673	91	10648	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
674	92	PROVEC50041	24/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYH
675	93	PROVEC50042	24/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYJ
676	94	PROVEC50043	24/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
677	95	10649	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
678	96	PROVEC50044	24/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	DK19WDA
679	97	PROVEC50045	24/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBB
680	98	PROVEC50046	24/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
681	99	PROVEC50047	24/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	DK19WDD
682	100	10650	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
683	101	10651	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
684	102	10652	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBK
685	103	10653	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
686	104	10654	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
687	105	10655	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
688	106	10656	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
689	107	10657	24/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
690	108	10658	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
691	109	10659	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
692	110	10660	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
693	111	10661	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
694	112	10662	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
695	113	10663	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
696	114	10664	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBK
697	115	10665	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
698	116	10666	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
699	117	10667	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
700	118	10668	24/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
701	119	10669	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
702	120	10670	24/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
703	121	10671	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
704	122	10672	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
705	123	10673	24/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
706	124	10674	24/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
707	1	PROVEC50048	25/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
708	2	PROVEC50051	25/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
709	3	PROVEC50052	25/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBB
710	4	PROVEC50053	25/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
711	5	10675	25/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
712	6	10676	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBK
713	7	10677	25/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
714	8	10678	25/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
715	9	10679	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
716	10	10680	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
717	11	10681	25/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
718	12	PROVEC50054	25/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD
719	13	PROVEC50055	25/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	GN18OSG
720	14	10682	25/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
721	15	10683	25/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
722	16	10684	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBM
723	17	10685	25/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
724	18	10686	25/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX16CVV
725	19	10687	25/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
726	20	10688	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RLY
727	21	10689	25/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
728	22	10690	25/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
729	23	10691	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
730	24	10692	25/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
731	25	10693	25/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
732	26	10694	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXP
733	27	10695	25/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
734	28	10696	25/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
735	29	10697	25/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
736	30	10698	25/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
737	31	10699	25/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
738	32	10700	25/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
739	33	10701	25/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
740	34	10702	25/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
741	35	10703	25/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
742	36	10704	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBK
743	37	10705	25/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
744	38	10706	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
745	39	10707	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
746	40	10708	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBM
747	41	PROVEC50056	25/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
748	42	PROVEC50057	25/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
749	43	PROVEC50058	25/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBB
750	44	PROVEC50059	25/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD
751	45	PROVEC50060	25/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU90617	MK21BYL
752	46	PROVEC50061	25/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU119097	GN18OSG
753	47	10709	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RLY
754	48	10710	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF

755	49	10711	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXP
756	50	10712	25/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
757	51	10713	25/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
758	52	10714	25/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
759	53	10715	25/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
760	54	10716	25/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
761	55	10717	25/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX16CVV
762	56	10718	25/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
763	57	10719	25/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
764	58	10720	25/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
765	59	10721	25/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
766	60	10722	25/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
767	61	10723	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBK
768	62	10724	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
769	63	10725	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
770	64	10726	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBM
771	65	10727	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RLY
772	66	10728	25/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
773	67	10729	25/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
774	68	10730	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
775	69	10731	25/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
776	70	10732	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXP
777	71	10733	25/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
778	72	10734	25/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
779	73	10735	25/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
780	74	10736	25/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
781	75	10737	25/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX16CVV
782	76	10738	25/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
783	77	10739	25/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
784	78	10740	25/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
785	79	10741	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBK
786	80	10742	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBM
787	81	10743	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
788	82	10744	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
789	83	10745	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RLY
790	84	PROVEC50062	25/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
791	85	PROVEC50063	25/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
792	86	PROVEC50064	25/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBB
793	87	10746	25/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
794	88	10747	25/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
795	89	PROVEC50065	25/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD
796	90	PROVEC50066	25/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
797	91	10748	25/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
798	92	PROVEC50067	25/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	GN18OSG
799	93	10749	25/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
800	94	10750	25/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
801	95	10751	25/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
802	96	10752	25/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
803	97	10753	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
804	98	10754	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXP
805	99	10755	25/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
806	100	10756	25/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
807	101	10757	25/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
808	102	10758	25/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
809	103	10759	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBM
810	104	10760	25/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
811	105	10761	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBK
812	106	10762	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
813	107	10763	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
814	108	10764	25/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
815	109	10765	25/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
816	110	10766	25/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
817	111	10767	25/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
818	112	10768	25/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RLY
819	113	10769	25/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
820	114	10770	25/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
821	115	10771	25/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
822	116	10772	25/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
823	117	10773	25/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
824	118	10774	25/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
825	119	10775	25/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
826	120	10776	25/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
827	121	10777	25/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
828	122	10778	25/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
829	123	10779	25/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
830	124	10780	25/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXM
831	125	10781	25/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
832	126	10782	25/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBL
833	127	10783	25/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
834	128	10784	25/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXV
835	129	10785	25/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
836	130	10786	25/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
837	131	10787	25/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
838	132	10788	25/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBM
839	133	10789	25/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
840	134	10790	25/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
841	135	PROVEC50068	25/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	YD16ERZ
842	136	PROVEC50069	25/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	PN19HVC
843	137	10791	25/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBK
844	138	10792	25/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
845	139	10793	25/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
846	140	10794	25/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
847	141	10795	25/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
848	1	PROVEC50070	26/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
849	2	PROVEC50071	26/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
850	3	PROVEC50072	26/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD
851	4	PROVEC50073	26/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU90617	GN18OSG0
852	5	PROVEC50074	26/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYH
853	6	PROVEC50075	26/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYJ
854	7	10796	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MC16CVV
855	8	10797	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
856	9	10798	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
857	10	10799	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
858	11	10800	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
859	12	10801	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBK
860	13	10802	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXO
861	14	10803	26/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
862	15	10804	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
863	16	10805	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
864	17	10806	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXW
865	18	10807	26/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
866	19	10808	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
867	20	10809	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
868	21	10812	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
869	22	10813	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RLY
870	23	10814	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
871	24	10815	26/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
872	25	10816	26/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
873	26	10817	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXP
874	27	10818	26/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
875	28	10819	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
876	29	10820	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
877	30	10821	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
878	31	10822	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
879	32	10823	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
880	33	10824	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
881	34	10825	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC

882	35	10826	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
883	36	10827	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
884	37	10828	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
885	38	10829	26/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
886	39	10830	26/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
887	40	10831	26/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBK
888	41	10832	26/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
889	42	10833	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
890	43	10834	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
891	44	10835	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX16CVV
892	45	10836	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
893	46	10837	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXO
894	47	10838	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXW
895	48	10839	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
896	49	10840	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RLY
897	50	10841	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
898	51	10842	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
899	52	PROVEC50076	26/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
900	53	10843	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXP
901	54	10845	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
902	55	10846	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
903	56	PROVEC50077	26/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
904	57	10847	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
905	58	10848	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
906	59	PROVEC50078	26/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	YD16ERZ
907	60	PROVEC50079	26/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	GN18OSG
908	61	PROVEC50080	26/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD
909	62	PROVEC50081	26/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYJ
910	63	PROVEC50082	26/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYK
911	64	10849	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
912	65	10850	26/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
913	66	10851	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
914	67	10852	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
915	68	10853	26/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
916	69	10854	26/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
917	70	10855	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
918	71	10856	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
919	72	10857	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBK
920	73	10858	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MCX16CVV
921	74	10859	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
922	75	10860	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
923	76	10861	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXO
924	77	10862	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
925	78	10863	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
926	79	10864	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
927	80	10865	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXP
928	81	10866	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXW
929	82	10867	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RLY
930	83	10868	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
931	84	10869	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
932	85	10870	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
933	86	10871	26/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
934	87	10872	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
935	88	10873	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
936	89	10874	26/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
937	90	10875	26/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
938	91	10876	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
939	92	10877	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
940	93	10878	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
941	94	PROVEC50083	26/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	YD16ERZ
942	95	10879	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX16CVV
943	96	10880	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBK
944	97	10881	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
945	98	PROVEC50084	26/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
946	99	PROVEC50085	26/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
947	100	10882	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
948	101	PROVEC50086	26/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD
949	102	PROVEC50087	26/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	GN18OSG
950	103	PROVEC50088	26/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYH
951	104	PROVEC50089	26/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD
952	105	10883	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
953	106	10884	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
954	107	10885	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
955	108	10886	26/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
956	109	10887	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
957	110	10888	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
958	111	10889	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXO
959	112	10890	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXW
960	113	10891	26/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
961	114	10892	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
962	115	10893	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXP
963	116	10894	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
964	117	10895	26/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
965	118	10896	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
966	119	10897	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
967	120	10898	26/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
968	121	10899	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
969	122	10900	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
970	123	10901	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
971	124	10902	26/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBK
972	125	10903	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
973	126	10904	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
974	127	10905	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX16CVV
975	128	10906	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
976	129	10907	26/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
977	130	PROVEC50090	26/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	PN19HVC
978	131	10908	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
979	132	10909	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
980	133	10910	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
981	134	10911	26/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
982	135	10912	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
983	136	10913	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
984	137	10914	26/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
985	138	10915	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
986	139	10916	26/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
987	140	10917	26/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXO
988	141	10918	26/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
989	142	10919	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
990	143	10920	26/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
991	144	10921	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
992	145	10922	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
993	146	10923	26/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
994	147	10924	26/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
995	148	PROVEC50091	26/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	YD16ERZ
996	149	PROVEC50092	26/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYH
997	150	10925	26/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
998	151	PROVEC50093	26/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	GN18OSG
999	152	10926	26/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBL
1000	153	10927	26/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXV
1001	154	10928	26/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MX16CVV
1002	155	PROVEC50094	26/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYJ
1003	156	10929	26/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
1004	157	10930	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
1005	158	10931	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
1006	159	10932	26/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
1007	160	10933	26/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXM
1008	161	10934	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA

1009	162	10935	26/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
1010	163	10936	26/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBK
1011	1	PROVEC50095	29/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
1012	2	PROVEC50096	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD
1013	3	10937	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1014	4	10938	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
1015	5	10939	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
1016	6	10940	29/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
1017	7	10941	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
1018	8	10942	29/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RLY
1019	9	10943	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
1020	10	10944	29/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
1021	11	10945	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
1022	12	10946	29/03/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	DK19WDA
1023	13	10947	29/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
1024	14	10948	29/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBM
1025	15	10949	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
1026	16	10950	29/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKJ
1027	17	10951	29/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBK
1028	18	10952	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
1029	19	10953	29/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
1030	20	10954	29/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
1031	21	10955	29/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
1032	22	10956	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
1033	23	10957	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
1034	24	10958	29/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1035	25	PROVEC50097	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
1036	26	PROVEC50098	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
1037	27	10959	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX19CVV
1038	28	10960	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1039	29	10961	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
1040	30	10962	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
1041	31	10963	29/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
1042	32	10964	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
1043	33	10965	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
1044	34	10966	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
1045	35	10967	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
1046	36	10968	29/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
1047	37	10969	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
1048	38	10970	29/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
1049	39	10971	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
1050	40	10972	29/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
1051	41	10973	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
1052	42	10974	29/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1053	43	10975	29/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
1054	44	10976	29/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBM
1055	45	10977	29/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RLY
1056	46	10978	29/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
1057	47	10979	29/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBK
1058	48	10980	29/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKJ
1059	49	PROVEC50099	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYH
1060	50	PROVEC50100	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	GN18OSG
1061	51	10981	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
1062	52	10982	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
1063	53	10983	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX16CVV
1064	54	10984	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
1065	55	10985	29/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
1066	56	10986	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
1067	57	10987	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
1068	58	10988	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
1069	59	10989	29/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
1070	60	10990	29/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
1071	61	10991	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
1072	62	PROVEC50101	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYJ
1073	63	PROVEC50102	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	YD16ERZ
1074	64	PROVEC50103	29/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
1075	65	PROVEC50104	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD
1076	66	PROVEC50105	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
1077	67	PROVEC50106	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
1078	68	10992	29/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
1079	69	10993	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
1080	70	10994	29/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1081	71	10995	29/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
1082	72	10996	29/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBM
1083	73	10997	29/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RLY
1084	74	PROVEC50107	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFR
1085	75	10998	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
1086	76	10999	29/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
1087	77	11000	29/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBK
1088	78	PROVEC50108	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN70EFJ
1089	79	PROVEC50109	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN70DZE
1090	80	PROVEC50110	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN70EFC
1091	81	PROVEC50111	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFS
1092	82	11001	29/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
1093	83	11002	29/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKJ
1094	84	11003	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
1095	85	11004	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
1096	86	11005	29/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
1097	87	11006	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
1098	88	11007	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
1099	89	11008	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
1100	90	11009	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21 BYJ
1101	91	11010	29/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
1102	92	11011	29/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
1103	93	11012	29/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
1104	94	PROVEC50012	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFG
1105	95	PROVEC50013	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN70EFF
1106	96	11013	29/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1107	97	11014	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
1108	98	11015	29/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
1109	99	11016	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
1110	100	11017	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
1111	101	11018	29/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBM
1112	102	11019	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
1113	103	11020	29/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RLY
1114	104	PROVEC50114	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	YD16ERZ
1115	105	PROVEC50115	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFF
1116	106	PROVEC50116	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFE
1117	107	11021	29/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBK
1118	108	11022	29/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
1119	109	11023	29/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKJ
1120	110	11024	29/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
1121	111	11025	29/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
1122	112	11026	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1123	113	11027	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
1124	114	11028	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
1125	115	11029	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
1126	116	11030	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
1127	117	11031	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
1128	118	11032	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BXO
1129	119	11033	29/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
1130	120	11034	29/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
1131	121	11035	29/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1132	122	PROVEC50117	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	PN19YYH
1133	123	PROVEC50118	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN70EFD
1134	124	PROVEC50119	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	GN18OSG
1135	125	PROVEC50120	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYJ

1136	126	PROVEC50121	29/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
1137	127	PROVEC50122	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD
1138	128	PROVEC50123	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN70EFB
1139	129	PROVEC50124	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
1140	130	PROVEC50125	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
1141	131	11036	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
1142	132	11037	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
1143	133	11038	29/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
1144	134	11039	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
1145	135	11040	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
1146	136	11041	29/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
1147	137	11042	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1148	138	11043	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
1149	139	11044	29/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
1150	140	11045	29/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
1151	141	11046	29/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
1152	142	11047	29/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBK
1153	143	11048	29/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
1154	144	11049	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
1155	145	11050	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
1156	146	11051	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
1157	147	11052	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
1158	148	11053	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX21ORT
1159	149	11054	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
1160	150	11055	29/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
1161	151	11056	29/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXO
1162	152	11057	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
1163	153	11058	29/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
1164	154	11059	29/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
1165	155	11060	29/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
1166	156	11061	29/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
1167	157	PROVEC50127	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	YD16ERZ
1168	158	11062	29/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
1169	159	11063	29/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
1170	160	11064	29/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBM
1171	161	11065	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
1172	162	11066	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
1173	163	11067	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
1174	164	11068	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
1175	165	11069	29/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
1176	166	11070	29/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
1177	167	PROVEC50128	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYH
1178	168	PROVEC50129	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	GN18OSG
1179	169	PROVEC50130	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYJ
1180	170	11071	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
1181	171	11072	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
1182	172	11073	29/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
1183	173	11074	29/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBK
1184	174	11075	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
1185	175	11076	29/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
1186	176	11077	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
1187	177	11078	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
1188	178	11079	29/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
1189	179	11080	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
1190	180	11081	29/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
1191	181	11082	29/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
1192	182	PROVEC50131	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
1193	183	PROVEC50132	29/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
1194	1	11083	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1195	2	11084	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
1196	3	11085	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
1197	4	11086	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
1198	5	11087	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBK
1199	6	11088	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
1200	7	11089	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
1201	8	PROVEC50133	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD
1202	9	11090	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
1203	10	PROVEC50134	30/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
1204	11	PROVEC50135	30/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MX21ORT
1205	12	PROVEC50136	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	YD16ERZ
1206	13	11091	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
1207	14	11092	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
1208	15	11093	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
1209	16	11094	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX16CVV
1210	17	11095	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
1211	18	11096	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
1212	19	11097	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
1213	20	11098	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1214	21	11099	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
1215	22	11100	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
1216	23	11101	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
1217	24	11102	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
1218	25	11103	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
1219	26	11104	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
1220	27	11105	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
1221	28	11106	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1222	29	11107	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBK
1223	30	11108	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
1224	31	11109	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
1225	32	11110	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
1226	33	11111	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
1227	34	11112	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
1228	35	11113	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	RV69ZVB
1229	36	11114	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
1230	37	11115	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
1231	38	11116	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
1232	39	11117	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
1233	40	11118	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
1234	41	11119	30/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
1235	42	11120	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
1236	43	11121	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
1237	44	11122	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
1238	45	11123	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
1239	46	11124	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
1240	47	11125	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
1241	48	11126	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
1242	49	11127	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
1243	50	PROVEC50137	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFS
1244	51	PROVEC50138	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFF
1245	52	PROVEC50139	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN70DZE
1246	53	PROVEC50140	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN70EFF
1247	54	PROVEC50141	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFR
1248	55	PROVEC50142	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN70EFB
1249	56	PROVEC50143	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFG
1250	57	PROVEC50144	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	GN18OSG
1251	58	PROVEC50145	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYJ
1252	59	PROVEC50146	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
1253	60	PROVEC50147	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
1254	61	PROVEC50148	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD
1255	62	PROVEC50149	30/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
1256	63	PROVEC50150	30/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MX21ORT
1257	64	PROVEC50151	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	YD16ERZ
1258	65	11128	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX16CVV
1259	66	11129	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
1260	67	11130	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBK
1261	68	11131	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
1262	69	11132	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE

1263	70	11133	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
1264	71	11134	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
1265	72	11135	30/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKJ
1266	73	11136	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
1267	74	11137	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
1268	75	11138	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
1269	76	11139	30/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXU
1270	77	11140	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
1271	78	11141	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
1272	79	11142	30/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBM
1273	80	11143	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
1274	81	11144	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
1275	82	11145	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
1276	83	11146	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
1277	84	11147	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
1278	85	11148	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
1279	86	11149	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
1280	87	11150	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
1281	88	11151	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1282	89	11152	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1283	90	11153	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
1284	91	11154	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
1285	92	11155	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
1286	93	11156	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
1287	94	11157	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
1288	95	11158	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
1289	96	11159	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
1290	97	11160	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
1291	98	11161	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
1292	99	11162	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
1293	100	11163	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
1294	101	11164	30/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
1295	102	11165	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBK
1296	103	11166	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
1297	104	11167	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
1298	105	11168	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
1299	106	11169	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
1300	107	11170	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
1301	108	11171	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
1302	109	11172	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1303	110	11173	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
1304	111	11174	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1305	112	11175	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
1306	113	11176	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
1307	114	11177	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
1308	115	11178	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
1309	116	11179	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
1310	117	11180	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
1311	118	11181	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
1312	119	11182	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
1313	120	11183	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
1314	121	11184	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
1315	122	11185	30/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
1316	123	11186	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
1317	124	11187	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
1318	125	11188	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
1319	126	11189	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
1320	127	11190	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
1321	128	11191	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
1322	129	11192	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
1323	130	11193	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
1324	131	11194	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1325	132	11195	30/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
1326	133	11196	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1327	134	11197	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
1328	135	PROVEC50152	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
1329	136	PROVEC50153	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN70EFD
1330	137	PROVEC50154	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	GN18OSG
1331	138	PROVEC50155	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYJ
1332	139	PROVEC50156	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
1333	140	PROVEC50157	30/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
1334	141	PROVEC50158	30/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MX21ORT
1335	142	PROVEC50159	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	YD16ERZ
1336	143	PROVEC50160	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFJ
1337	144	11198	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
1338	145	11199	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
1339	146	11200	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBK
1340	147	PROVEC50161	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU90617	GN18OSG
1341	148	PROVEC50162	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	PN19YYJ
1342	149	PROVEC50163	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
1343	150	PROVEC50164	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
1344	151	PROVEC50165	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFS
1345	152	PROVEC50166	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	YD16ERZ
1346	153	PROVEC50167	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU90617	PN20EFF
1347	154	PROVEC50168	30/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFR
1348	155	PROVEC70000	30/03/2021	170503	3900	Asbestos+TPH	14	ERQ	CBDU90617	MK21BYL
1349	156	PROVEC70001	30/03/2021	170503	3900	Asbestos+TPH	14	ERQ	CBDU90617	MX21ORT
1350	157	11201	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
1351	158	11202	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
1352	159	11203	30/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
1353	160	11204	30/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXU
1354	161	11205	30/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
1355	162	11206	30/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXO
1356	163	11207	30/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
1357	164	11208	30/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
1358	165	11209	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
1359	166	11210	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
1360	167	11211	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
1361	168	11212	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
1362	169	11213	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
1363	170	11214	30/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
1364	171	11215	30/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
1365	172	11216	30/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
1366	173	11217	30/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
1367	174	11218	30/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
1368	175	11219	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
1369	176	11220	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
1370	177	11221	30/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
1371	178	11222	30/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
1372	179	11223	30/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBK
1373	1	PROVEC50171	31/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD
1374	2	PROVEC50172	31/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYJ
1375	3	11224	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
1376	4	11225	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
1377	5	11226	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1378	6	11227	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
1379	7	11228	31/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXP
1380	8	11229	31/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
1381	9	11230	31/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
1382	10	11231	31/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
1383	11	11232	31/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKN
1384	12	11233	31/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
1385	13	11234	31/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXO
1386	14	PROVEC50173	31/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN70EFF
1387	15	11235	31/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBL
1388	16	11236	31/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1389	17	11237	31/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD

1390	18	11238	31/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
1391	19	11239	31/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
1392	20	11240	31/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
1393	21	11241	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
1394	22	11242	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
1395	23	11243	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
1396	24	PROVEC70002	31/03/2021	170503	3900	Asbestos+TPH	14	ERQ	CBDU90617	PX67JYN
1397	25	PROVEC70003	31/03/2021	170503	3900	Asbestos+TPH	14	ERQ	CBDU90617	PX15UNK
1398	26	11244	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
1399	27	11245	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
1400	28	11246	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
1401	29	11247	31/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
1402	30	11248	31/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
1403	31	11249	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
1404	32	11250	31/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1405	33	PROVEC50174	31/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN70EFB
1406	34	11251	31/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
1407	35	11252	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1408	36	11253	31/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBK
1409	37	11254	31/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
1410	38	11255	31/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXP
1411	39	PROVEC50175	31/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN70EFJ
1412	40	11256	31/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKN
1413	41	11257	31/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXO
1414	42	11258	31/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1415	43	11259	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
1416	44	11260	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
1417	45	PROVEC50176	31/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	GN18OSG
1418	46	11261	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
1419	47	11262	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
1420	48	11263	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
1421	49	PROVEC50177	31/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	YD16ERZ
1422	50	11264	31/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
1423	51	11265	31/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
1424	52	11266	31/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
1425	53	PROVEC50178	31/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
1426	54	11267	31/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
1427	55	PROVEC50179	31/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
1428	56	11269	31/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1429	57	PROVEC50180	31/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD
1430	58	11269	31/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
1431	59	11270	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1432	60	11271	31/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
1433	61	11272	31/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXU
1434	62	11273	31/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBK
1435	63	11274	31/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
1436	64	11275	31/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXP
1437	65	11276	31/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKN
1438	66	11277	31/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXO
1439	67	PROVEC70004	31/03/2021	170503	3900	Asbestos+TPH	14	ERQ	CBDU90617	MK21BYL
1440	68	PROVEC70005	31/03/2021	170503	3900	Asbestos+TPH	14	ERQ	CBDU90617	MX21ORT
1441	69	11278	31/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
1442	70	11279	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
1443	71	PROVEC50181	31/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYJ
1444	72	11280	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
1445	73	11281	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
1446	74	11282	31/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
1447	75	11283	31/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
1448	76	11284	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19FVC
1449	77	11285	31/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
1450	78	11286	31/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
1451	79	11287	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
1452	80	11288	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
1453	81	11289	31/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
1454	82	11290	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1455	83	11291	31/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
1456	84	PROVEC50182	31/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	GN18OSG
1457	85	11292	31/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBK
1458	86	11293	31/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
1459	87	11294	31/03/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BXP
1460	88	11295	31/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKN
1461	89	11296	31/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXO
1462	90	PROVEC50183	31/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	YD16ERZ
1463	91	PROVEC50184	31/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	WX16MLV
1464	92	PROVEC50185	31/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
1465	93	11297	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
1466	94	11298	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
1467	95	11299	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
1468	96	11300	31/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
1469	97	11301	31/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
1470	98	11302	31/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
1471	99	11303	31/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1472	100	11304	31/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
1473	101	PROVEC50186	31/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD
1474	102	PROVEC50187	31/03/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYJ
1475	103	11305	31/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
1476	104	11306	31/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
1477	105	11307	31/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
1478	106	11308	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
1479	107	11309	31/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
1480	108	11310	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1481	109	11311	31/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBK
1482	110	11312	31/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
1483	111	11313	31/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXP
1484	112	11314	31/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
1485	113	11315	31/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKN
1486	114	11316	31/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
1487	115	11317	31/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXO
1488	116	PROVEC70006	31/03/2021	170503	3900	Asbestos+TPH	14	ERQ	CBDU134035	PX15UNK
1489	117	PROVEC70007	31/03/2021	170503	3900	Asbestos+TPH	14	ERQ	CBDU134035	PX67JYN
1490	118	11318	31/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1491	119	11319	31/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
1492	120	11320	31/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
1493	121	11321	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
1494	122	11322	31/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
1495	123	11323	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
1496	124	11324	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
1497	125	11325	31/03/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
1498	126	11326	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
1499	127	11327	31/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
1500	128	11328	31/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
1501	129	PROVEC50188	31/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	GN18OSG
1502	130	11329	31/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
1503	131	11330	31/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
1504	132	11331	31/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
1505	133	PROVEC50189	31/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
1506	134	PROVEC50190	31/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
1507	135	11332	31/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
1508	136	PROVEC50191	31/03/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	YD16ERZ
1509	137	11333	31/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
1510	138	11334	31/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBK
1511	139	PROVEC70008	31/03/2021	170503	3900	Asbestos+TPH	14	ERQ	CBDU90617	MK21BYJ
1512	140	11335	31/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXV
1513	141	11336	31/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
1514	142	11337	31/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
1515	143	11338	31/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
1516	144	11339	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD

1517	145	11340	31/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
1518	146	11341	31/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
1519	147	11342	31/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
1520	148	11343	31/03/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
1521	149	11344	31/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
1522	150	11345	31/03/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXO
1523	151	11346	31/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXM
1524	152	11347	31/03/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
1525	1	PROVEC50192	01/04/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
1526	2	PROVEC50193	01/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYK
1527	3	11348	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
1528	4	11349	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
1529	5	11350	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1530	6	11351	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
1531	7	11352	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
1532	8	11353	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
1533	9	11354	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
1534	10	11355	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBL
1535	11	11356	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
1536	12	11357	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
1537	13	11358	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
1538	14	11359	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
1539	15	11360	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1540	16	11361	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV20RKN
1541	17	11362	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
1542	18	PROVEC70009	01/04/2021	170503	3900	Asbestos+TPH	14	ERQ	CBDU134035	PX15UNK
1543	19	PROVEC70010	01/04/2021	170503	3900	Asbestos+TPH	14	ERQ	CBDU134035	PX67JYN
1544	20	PROVEC70011	01/04/2021	170503	3900	Asbestos+TPH	14	ERQ	CBDU90617	MX21ORT
1545	21	11363	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
1546	22	PROVEC50194	01/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD
1547	23	11364	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
1548	24	11365	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
1549	25	11366	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBL
1550	26	11367	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1551	27	11368	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
1552	28	11369	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
1553	29	11370	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
1554	30	11371	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1555	31	11372	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBD
1556	32	11373	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
1557	33	PROVEC50195	01/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFG
1558	34	11374	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
1559	35	11375	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
1560	36	PROVEC50196	01/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFF
1561	37	PROVEC50197	01/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFR
1562	38	PROVEC50198	01/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN70EFF
1563	39	PROVEC50199	01/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN70EFB
1564	40	11376	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
1565	41	PROVEC50200	01/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN70EFD
1566	42	11377	01/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
1567	43	11378	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
1568	44	11379	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
1569	45	11380	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
1570	46	PROVEC50201	01/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFS
1571	47	PROVEC50202	01/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	GN18OSG
1572	48	11381	01/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
1573	49	PROVEC50203	01/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	YD16ERZ
1574	50	PROVEC50204	01/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
1575	51	11382	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBL
1576	52	11383	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
1577	53	PROVEC50205	01/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
1578	54	PROVEC50206	01/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYK
1579	55	PROVEC50207	01/04/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
1580	56	11384	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
1581	57	11385	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1582	58	11386	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
1583	59	11387	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
1584	60	11388	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1585	61	11389	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
1586	62	11390	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
1587	63	PROVEC50208	01/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD
1588	64	PROVEC70012	01/04/2021	170503	3900	Asbestos+TPH	14	ERQ	CBDU90617	MK21BYJ
1589	65	11391	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
1590	66	11392	01/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
1591	67	11393	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
1592	68	11394	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
1593	69	11395	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
1594	70	11396	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBL
1595	71	11397	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
1596	72	11398	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
1597	73	11399	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1598	74	11400	01/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
1599	75	11401	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1600	76	11402	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
1601	77	11403	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1602	78	11404	01/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
1603	79	11405	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
1604	80	11406	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
1605	81	11407	01/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
1606	82	11408	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
1607	83	11409	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
1608	84	11410	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
1609	85	PROVEC50209	01/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
1610	86	PROVEC50210	01/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	YD16ERZ
1611	87	PROVEC50211	01/04/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
1612	88	11411	01/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBL
1613	89	11412	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
1614	90	11413	01/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
1615	91	11414	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
1616	92	PROVEC50212	01/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	GN18OSG
1617	93	11415	01/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
1618	94	PROVEC50213	01/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYK
1619	95	11416	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1620	96	11417	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
1621	97	11418	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1622	98	PROVEC50214	01/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
1623	99	11419	01/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
1624	100	11420	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
1625	101	11421	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
1626	102	PROVEC50215	01/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD
1627	103	11422	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
1628	104	11423	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
1629	105	11424	01/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
1630	106	11425	01/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBL
1631	107	11426	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
1632	108	11427	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
1633	109	11428	01/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
1634	110	11429	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
1635	111	11430	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
1636	112	11431	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
1637	113	11432	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1638	114	11433	01/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
1639	115	11434	01/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
1640	116	11435	01/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
1641	117	11436	01/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
1642	118	11437	01/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
1643	119	11438	01/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXV

1644	120	11439	01/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
1645	121	11440	01/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
1646	122	11441	01/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBL
1647	123	11442	01/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
1648	124	11443	01/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
1649	125	11444	01/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
1650	126	11445	01/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
1651	127	11446	01/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
1652	128	11447	01/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
1653	129	11448	01/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
1654	130	PROVEC50216	01/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	MX16MLY
1655	131	11449	01/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
1656	132	PROVEC50217	01/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	GN18OSG
1657	133	11450	01/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXO
1658	134	11451	01/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
1659	135	11452	01/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
1660	136	11453	01/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
1661	137	11454	01/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
1662	138	11455	01/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
1663	1	PROVEC50218	06/04/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
1664	2	11456	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
1665	3	PROVEC50219	06/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD
1666	4	11457	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1667	5	11458	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBL
1668	6	PROVEC50220	06/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFG
1669	7	11459	06/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
1670	8	11460	06/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
1671	9	PROVEC50221	06/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	YD16ERZ
1672	10	11461	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
1673	11	11462	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
1674	12	11463	06/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
1675	13	11464	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
1676	14	11465	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
1677	15	11466	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
1678	16	11467	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
1679	17	11468	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
1680	18	11469	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
1681	19	PROVEC50222	06/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYJ
1682	20	PROVEC50223	06/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYH
1683	21	PROVEC70013	06/04/2021	170503	3900	Asbestos+TPH	14	ERQ	CBDU90617	MK21BYJ
1684	22	PROVEC70014	06/04/2021	170503	3900	Asbestos+TPH	14	ERQ	CBDU90617	MX21ORT
1685	23	PROVEC70015	06/04/2021	170503	3900	Asbestos+TPH	14	ERQ	CBDU134035	PX67JYN
1686	24	11470	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
1687	25	11471	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
1688	26	PROVEC70016	06/04/2021	170503	3900	Asbestos+TPH	14	ERQ	CBDU134035	PX15UNK
1689	27	11472	06/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
1690	28	PROVEC50224	06/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFF
1691	29	11473	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
1692	30	11474	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBL
1693	31	11475	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
1694	32	11476	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1695	33	11477	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
1696	34	11478	06/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
1697	35	11479	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
1698	36	11480	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
1699	37	11481	06/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
1700	38	11482	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
1701	39	11483	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
1702	40	11484	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
1703	41	11485	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
1704	42	11486	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
1705	43	11487	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
1706	44	PROVEC50225	06/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
1707	45	11488	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
1708	46	11489	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBL
1709	47	PROVEC50226	06/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	GN18OSG
1710	48	PROVEC50227	06/04/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
1711	49	11490	06/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
1712	50	11491	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
1713	51	PROVEC50228	06/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD
1714	52	PROVEC50229	06/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	YD16ERZ
1715	53	11492	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1716	54	11493	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
1717	55	11494	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
1718	56	PROVEC50230	06/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYJ
1719	57	11495	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
1720	58	11496	06/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
1721	59	PROVEC50231	06/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYH
1722	60	11497	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
1723	61	11498	06/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
1724	62	11499	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
1725	63	11500	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
1726	64	11501	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
1727	65	PROVEC50232	06/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFS
1728	66	11502	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
1729	67	PROVEC50233	06/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFJ
1730	68	PROVEC50234	06/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN70DZE
1731	69	PROVEC50235	06/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN70EFC
1732	70	11503	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
1733	71	PROVEC50236	06/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU90617	PN70EFB
1734	72	PROVEC50237	06/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU90617	PN70EFF
1735	73	11504	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBL
1736	74	11505	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
1737	75	11506	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
1738	76	11507	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1739	77	11508	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
1740	78	11509	06/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
1741	79	11510	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
1742	80	11511	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
1743	81	11512	06/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
1744	82	11513	06/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
1745	83	11514	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
1746	84	11515	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
1747	85	11516	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
1748	86	11517	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
1749	87	PROVEC50238	06/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
1750	88	11518	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
1751	89	PROVEC50239	06/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN70EFD
1752	90	PROVEC70017	06/04/2021	170503	3900	Asbestos+TPH	14	ERQ	CBDU134035	PX67JYN
1753	91	PROVEC50240	06/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	GN18OSG
1754	92	PROVEC50241	06/04/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
1755	93	PROVEC50242	06/04/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYJ
1756	94	PROVEC50243	06/04/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MX21ORT
1757	95	PROVEC50244	06/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD
1758	96	11519	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBL
1759	97	11520	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
1760	98	PROVEC70018	06/04/2021	170503	3900	Asbestos+TPH	9	ERQ	CBDU90617	MK21BYL
1761	99	11521	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
1762	100	11522	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1763	101	11523	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
1764	102	PROVEC50245	06/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	YD16ERZ
1765	103	PROVEC50246	06/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYJ
1766	104	PROVEC50247	06/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYH
1767	105	11524	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
1768	106	11525	06/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1769	107	11526	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
1770	108	11527	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA

1771	109	11528	06/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
1772	110	11529	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
1773	111	11530	06/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
1774	112	11531	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
1775	113	11532	06/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
1776	114	11533	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
1777	115	11534	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
1778	116	11535	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBL
1779	117	11536	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
1780	118	11537	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
1781	119	11538	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1782	120	11539	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
1783	121	11540	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
1784	122	11541	06/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1785	123	11542	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
1786	98	PROVEC70019	06/04/2021	170503	3900	Asbestos+TPH	9	ERQ	CBDU134035	PX15UNK
1787	125	11543	06/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
1788	126	11544	06/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
1789	127	11545	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
1790	128	11546	06/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
1791	129	11547	06/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX21ORT
1792	130	PROVEC70020	06/04/2021	170503	3900	Asbestos+TPH	14	ERQ	CBDU90617	MK21BYJ
1793	131	11548	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
1794	132	11549	06/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
1795	133	11550	06/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
1796	134	11551	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
1797	135	PROVEC50248	06/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
1798	136	11552	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
1799	137	11553	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBL
1800	138	PROVEC50249	06/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	WYD16ERZ
1801	139	11554	06/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
1802	140	11555	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
1803	141	11556	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
1804	142	11557	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
1805	143	11558	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXV
1806	144	11559	06/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
1807	1	11560	07/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
1808	2	11561	07/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1809	3	11562	07/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKJ
1810	4	11563	07/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
1811	5	11564	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
1812	6	11565	07/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBK
1813	7	11566	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
1814	8	11567	07/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
1815	9	11568	07/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
1816	10	11569	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
1817	11	11570	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1818	12	11571	07/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
1819	13	11572	07/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBL
1820	14	11573	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
1821	15	11574	07/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXV
1822	16	11575	07/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
1823	17	11576	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
1824	18	PROVEC50250	07/04/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MX21ORT
1825	19	11577	07/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RLY
1826	20	11578	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
1827	21	PROVEC50251	07/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD
1828	22	11579	07/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
1829	23	11580	07/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
1830	24	11581	07/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
1831	25	11582	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
1832	26	PROVEC50252	07/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYJ
1833	27	PROVEC70021	07/04/2021	170503	3900	Asbestos+TPH	14	ERQ	CBDU134035	PX67JYN
1834	28	11583	07/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
1835	29	11584	07/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
1836	30	11585	07/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
1837	31	11586	07/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXM
1838	32	11587	07/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
1839	33	PROVEC70022	07/04/2021	170503	3900	Asbestos+TPH	14	ERQ	CBDU134035	PX15UNK
1840	34	PROVEC50253	07/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYH
1841	35	11588	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
1842	36	11589	07/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1843	37	11590	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
1844	38	11591	07/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
1845	39	11592	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1846	40	11593	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
1847	41	11594	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
1848	42	11595	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
1849	43	11596	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
1850	44	11597	07/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV10UBE
1851	45	11598	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
1852	46	PROVEC50254	07/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFS
1853	47	11599	07/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
1854	48	PROVEC50255	07/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN70EFJ
1855	49	PROVEC50256	07/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFG
1856	50	PROVEC50257	07/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN70EFB
1857	51	11600	07/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
1858	52	PROVEC50258	07/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU90617	PN70EF
1859	53	11601	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
1860	54	11602	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1861	55	11603	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
1862	56	11604	07/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1863	57	11605	07/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
1864	58	11606	07/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
1865	59	11607	07/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
1866	60	PROVEC50259	07/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	YD16ERZ
1867	61	11608	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
1868	62	11609	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
1869	63	PROVEC50261	07/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
1870	64	11610	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
1871	65	11611	07/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
1872	66	11612	07/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
1873	67	PROVEC50260	07/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN70EFD
1874	68	11613	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
1875	69	PROVEC50262	07/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD
1876	70	11614	07/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
1877	71	11615	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1878	72	PROVEC50263	07/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFR
1879	73	11616	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
1880	74	PROVEC50264	07/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYH
1881	75	11617	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
1882	76	11618	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BXO
1883	77	PROVEC50265	07/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFF
1884	78	11619	07/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1885	79	PROVEC50266	07/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN70EFF
1886	80	PROVEC50267	07/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN70DZE
1887	81	11620	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
1888	82	11621	07/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
1889	83	11622	07/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
1890	84	11623	07/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
1891	85	PROVEC70024	07/04/2021	170503	3900	Asbestos+TPH	14	ERQ	CBDU90617	MK21BYL
1892	86	PROVEC70023	07/04/2021	170503	3900	Asbestos+TPH	14	ERQ	CBDU90617	MK21BYJ
1893	87	PROVEC50268	07/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFE
1894	88	11624	07/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
1895	89	11625	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
1896	90	11626	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
1897	91	PROVEC70025	07/04/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU134035	PX15UNK

1898	92	11627	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
1899	93	11628	07/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
1900	94	11629	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
1901	95	11630	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
1902	96	PROVEC269	07/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
1903	97	11631	07/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1904	98	11632	07/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXO
1905	99	11633	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
1906	100	11634	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
1907	101	11635	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
1908	102	PROVEC50270	07/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	YD16ERZ
1909	103	11636	07/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
1910	104	11637	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
1911	105	11638	07/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
1912	106	PROVEC50271	07/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD
1913	107	PROVEC70026	07/04/2021	170503	3900	Asbestos+TPH	14	ERQ	CBDU134035	PX67JYN
1914	108	11639	07/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
1915	109	11640	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
1916	110	11641	07/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
1917	111	11642	07/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBL
1918	112	11643	07/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
1919	113	PROVEC50272	07/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYH
1920	114	11644	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
1921	115	11645	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
1922	116	11646	07/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
1923	117	11647	07/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXO
1924	118	11648	07/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
1925	119	11649	07/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
1926	120	11650	07/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
1927	121	11651	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
1928	122	11652	07/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
1929	123	PROVEC50273	07/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYJ
1930	124	11653	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
1931	125	11654	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
1932	126	11655	07/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
1933	127	11656	07/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
1934	128	11657	07/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
1935	129	11658	07/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
1936	130	11659	07/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX21ORT
1937	131	11660	07/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
1938	132	11661	07/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBL
1939	133	11662	07/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
1940	134	11663	07/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
1941	135	11664	07/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
1942	136	11665	07/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
1943	137	11666	07/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
1944	138	11667	07/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXO
1945	139	11668	07/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
1946	140	11669	07/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBH
1947	141	11670	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
1948	142	11671	07/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
1949	143	11672	07/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBM
1950	144	11673	07/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
1951	145	PROVEC50274	07/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	YD16ERZ
1952	146	PROVEC50275	07/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
1953	147	11674	07/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
1954	148	11675	07/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
1955	149	11676	07/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
1956	150	11677	07/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
1957	151	11678	07/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBD
1958	152	PROVEC50276	07/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYH
1959	1	PROVEC50277	08/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	TP03MUD
1960	2	11679	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
1961	3	PROVEC50278	08/04/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
1962	4	11680	08/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKJ
1963	5	11681	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
1964	6	11682	08/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBK
1965	7	11683	08/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXU
1966	8	11684	08/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXV
1967	9	11685	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
1968	10	11687	08/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
1969	11	11686	08/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
1970	12	11688	08/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RLY
1971	13	11689	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
1972	14	11690	08/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RFK
1973	15	11691	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
1974	16	11692	08/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXZ
1975	17	11693	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
1976	18	11694	08/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
1977	19	11695	08/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
1978	20	11696	08/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
1979	21	11697	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
1980	22	11698	08/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
1981	23	11699	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
1982	24	11700	08/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
1983	25	11701	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
1984	26	11702	08/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
1985	27	11703	08/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBL
1986	28	11704	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
1987	29	PROVEC279	08/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYJ
1988	30	PROVEC280	08/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYK
1989	31	11705	08/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
1990	32	11706	08/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
1991	33	PROVEC50281	08/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
1992	34	PROVEC70027	08/04/2021	170503	3900	Asbestos+TPH	14	ERQ	CBDU134035	PX15UNK
1993	35	PROVEC70028	08/04/2021	170503	3900	Asbestos+TPH	14	ERQ	CBDU134035	PX67JYN
1994	36	11707	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
1995	37	11708	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
1996	38	11709	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX19UBA
1997	39	11710	08/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBK
1998	40	11711	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
1999	41	11712	08/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
2000	42	11713	08/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
2001	43	11714	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2002	44	11715	08/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2003	45	11716	08/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2004	46	11717	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
2005	47	11718	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
2006	48	11719	08/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBD
2007	49	11720	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2008	50	11721	08/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
2009	51	11722	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
2010	52	PROVEC50282	08/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFS
2011	53	11723	08/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
2012	54	11724	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2013	55	PROVEC50283	08/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFG
2014	56	PROVEC50284	08/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN70EFF
2015	57	PROVEC50285	08/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN70EFB
2016	58	11725	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2017	59	PROVEC50286	08/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN70EFC
2018	60	11726	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2019	61	11727	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2020	62	11728	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2021	63	11729	08/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBK
2022	64	11730	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
2023	65	11731	08/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
2024	66	11732	08/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF

2025	67	11733	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
2026	68	11734	08/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2027	69	11735	08/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2028	70	11736	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2029	71	11737	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
2030	72	11738	08/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
2031	73	PROVEC50287	08/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	YD16ERZ
2032	74	PROVEC50288	08/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN70DZE
2033	75	11739	08/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBD
2034	76	PROVEC50289	08/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFE
2035	77	11740	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
2036	78	11741	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2037	79	11742	08/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
2038	80	PROVEC50290	08/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
2039	81	11743	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2040	82	PROVEC50291	08/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD
2041	83	PROVEC50292	08/04/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
2042	84	PROVEC50293	08/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFR
2043	85	11744	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2044	86	PROVEC50294	08/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN70EFD
2045	87	11745	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2046	88	11746	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2047	89	PROVEC50295	08/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU134035	PN20EFF
2048	90	11747	08/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBK
2049	91	PROVEC50296	08/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYJ
2050	92	PROVEC50297	08/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYK
2051	93	11748	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
2052	94	11749	08/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2053	95	11750	08/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2054	96	PROVEC50298	08/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
2055	97	11751	08/04/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV20RKF
2056	98	11752	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2057	99	11753	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
2058	100	11754	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
2059	101	11755	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2060	102	11756	08/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBD
2061	103	11757	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
2062	104	PROVEC70029	08/04/2021	170503	3900	Asbestos+TPH	14	ERQ	CBDU134035	PX15UNK
2063	105	11758	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2064	106	11759	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2065	107	11760	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2066	108	11761	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2067	109	11762	08/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
2068	110	11763	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
2069	111	11764	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
2070	112	11765	08/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2071	113	11766	08/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2072	114	11767	08/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
2073	115	11768	08/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBK
2074	116	11769	08/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
2075	117	11770	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
2076	118	11771	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
2077	119	11772	08/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
2078	120	11773	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2079	121	11774	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2080	122	11775	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2081	123	11776	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2082	124	PROVEC50229	08/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	YD16ERZ
2083	125	11777	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
2084	126	PROVEC50300	08/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU90617	JP03MUD
2085	127	11778	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2086	128	11779	08/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBD
2087	129	PROVEC50301	08/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
2088	130	11780	08/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
2089	131	11781	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
2090	132	11782	08/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2091	133	11783	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
2092	134	PROVEC50302	08/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYK
2093	135	PROVEC50303	08/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
2094	136	PROVEC50304	08/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYJ
2095	137	11784	08/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2096	138	11785	08/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
2097	139	11786	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
2098	140	11787	08/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXM
2099	141	11788	08/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBK
2100	142	11789	08/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
2101	143	11790	08/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
2102	144	11791	08/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
2103	145	11792	08/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
2104	146	11793	08/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
2105	147	11794	08/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
2106	148	11795	08/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
2107	149	11796	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2108	150	11797	08/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
2109	151	11798	08/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
2110	152	11799	08/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXV
2111	153	11800	08/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBD
2112	154	11801	08/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
2113	155	11802	08/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
2114	156	11803	08/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
2115	157	11804	08/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
2116	158	11805	08/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
2117	159	PROVEC50305	08/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	YD16ERZ
2118	1	11806	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
2119	2	11807	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
2120	3	11808	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2121	4	11809	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
2122	5	11810	09/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
2123	6	11811	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2124	7	11812	09/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
2125	8	11813	09/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
2126	9	11814	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2127	10	11815	09/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RLY
2128	11	11816	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2129	12	11817	09/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBL
2130	13	11818	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2131	14	11819	09/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBK
2132	15	11820	09/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXU
2133	16	11821	09/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXV
2134	17	11822	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
2135	18	11823	09/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBD
2136	19	11824	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
2137	20	11825	09/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
2138	21	PROVEC50306	09/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD
2139	22	11826	09/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
2140	23	11827	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2141	24	11828	09/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
2142	25	11829	09/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2143	26	11830	09/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
2144	27	PROVEC50307	09/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYH
2145	28	PROVEC50308	09/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYJ
2146	29	PROVEC50309	09/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
2147	30	PROVEC70030	09/04/2021	170503	3900	Asbestos+TPH	14	ERQ	CBDU134035	PX15UNK
2148	31	11831	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
2149	32	11832	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2150	33	11833	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2151	34	11834	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ

2152	35	11835	09/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
2153	36	11836	09/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
2154	37	11837	09/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBK
2155	38	11838	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
2156	39	11839	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2157	40	11840	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2158	41	11841	09/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
2159	42	11842	09/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBD
2160	43	11843	09/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
2161	44	11844	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
2162	45	11845	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
2163	46	11846	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2164	47	PROVEC50310	09/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	YD16ERZ
2165	48	11847	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
2166	49	11848	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2167	50	11849	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
2168	51	11850	09/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2169	52	11851	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2170	53	PROVEC50311	09/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD
2171	54	PROVEC50312	09/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYK
2172	55	11852	09/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
2173	56	11853	09/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBK
2174	57	11854	09/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
2175	58	PROVEC50313	09/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYJ
2176	59	11855	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2177	60	PROVEC50314	09/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
2178	61	11856	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2179	62	11857	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
2180	63	PROVEC50315	09/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYH
2181	64	11858	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
2182	65	11859	09/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBD
2183	66	11860	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
2184	67	11861	09/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
2185	68	11862	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
2186	69	11863	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2187	70	11864	09/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2188	71	11865	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2189	72	11866	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
2190	73	11867	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2191	74	11868	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2192	75	11869	09/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
2193	76	11870	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
2194	77	11871	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2195	78	11872	09/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBK
2196	79	11873	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
2197	80	11874	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
2198	81	11875	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
2199	82	11876	09/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBD
2200	83	11877	09/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
2201	84	11878	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
2202	85	PROVEC50316	09/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	YD16ERZ
2203	86	11879	09/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
2204	87	PROVEC50317	09/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD
2205	88	11880	09/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
2206	89	11881	09/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2207	90	11882	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2208	91	PROVEC50318	09/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYK
2209	92	11883	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
2210	93	PROVEC50319	09/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYJ
2211	94	11884	09/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
2212	95	11885	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2213	96	11886	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
2214	97	PROVEC50320	09/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MCV
2215	98	11887	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
2216	99	11888	09/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
2217	100	11889	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2218	101	11890	09/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
2219	102	11891	09/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBK
2220	103	11892	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
2221	104	11893	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
2222	105	11894	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
2223	106	11895	09/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
2224	107	11896	09/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBD
2225	108	11897	09/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2226	109	11898	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2227	110	11899	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
2228	111	11900	09/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
2229	112	11901	09/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
2230	113	11902	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
2231	114	11903	09/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
2232	115	11904	09/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
2233	116	11905	09/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
2234	117	11906	09/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
2235	118	11907	09/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
2236	119	11908	09/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBK
2237	120	11909	09/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
2238	121	11910	09/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
2239	122	11911	09/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
2240	123	11912	09/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
2241	124	11913	09/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
2242	125	11914	09/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
2243	1	11915	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
2244	2	11916	12/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXO
2245	3	11917	12/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
2246	4	11918	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBM
2247	5	11919	12/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
2248	6	11920	12/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
2249	7	11921	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
2250	9	11922	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2251	10	11923	12/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
2252	11	11924	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2253	12	11925	12/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
2254	13	11926	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
2255	14	11927	12/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
2256	15	11928	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
2257	16	11929	12/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBL
2258	17	11930	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2259	18	11931	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
2260	19	11932	12/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
2261	20	11933	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
2262	21	11934	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
2263	22	11935	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2264	23	11936	12/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2265	24	PROVEC70031	12/04/2021	170503	3900	Asbestos+TPH	14	ERQ	CBDU90617	MK21BYL
2266	25	11937	12/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
2267	26	11938	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
2268	27	11939	12/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
2269	28	11940	12/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
2270	29	11941	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
2271	30	11942	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2272	31	11943	12/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXO
2273	32	11944	12/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
2274	33	11945	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
2275	34	11946	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
2276	35	11947	12/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
2277	36	11948	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2278	37	11949	12/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD

2279	38	11950	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2280	39	11951	12/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2281	40	11952	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2282	41	11953	12/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
2283	42	11954	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
2284	43	11955	12/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2285	44	11956	12/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBL
2286	45	11957	12/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
2287	46	11958	12/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
2288	47	11959	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
2289	48	11960	12/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
2290	49	11961	12/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
2291	50	11962	12/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
2292	51	11963	12/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
2293	52	11964	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
2294	53	11965	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2295	54	11966	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
2296	55	11967	12/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXO
2297	56	11968	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
2298	57	11969	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2299	58	11970	12/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
2300	59	11971	12/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
2301	60	11972	12/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
2302	61	11973	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
2303	62	11974	12/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
2304	63	11975	12/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2305	64	11976	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2306	65	11977	12/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
2307	66	11978	12/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
2308	67	11979	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
2309	68	11980	12/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
2310	69	11981	12/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
2311	70	11982	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2312	71	11983	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2313	72	11984	12/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZNA
2314	73	11985	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
2315	74	11986	12/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
2316	75	11987	12/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
2317	76	11988	12/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
2318	77	11989	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2319	78	11990	12/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
2320	79	11991	12/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2321	80	11992	12/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXO
2322	81	11993	12/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
2323	82	11994	12/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
2324	83	11995	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
2325	84	11996	12/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
2326	85	11997	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2327	86	11998	12/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2328	87	11999	12/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
2329	88	12000	12/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
2330	89	12001	12/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
2331	90	12002	12/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
2332	91	12003	12/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
2333	92	12004	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
2334	93	12005	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2335	94	12006	12/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
2336	95	12007	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
2337	96	12008	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
2338	97	12009	12/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVA
2339	98	12010	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2340	99	12011	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
2341	100	12012	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
2342	101	12013	12/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXO
2343	102	12014	12/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
2344	103	12015	12/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
2345	104	12016	12/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2346	105	12017	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2347	106	12018	12/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
2348	107	12019	12/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
2349	108	12020	12/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
2350	109	12021	12/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
2351	110	12022	12/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2352	111	12023	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
2353	112	12024	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2354	113	12025	12/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
2355	114	12026	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2356	115	12027	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2357	116	12028	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
2358	117	12029	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
2359	118	12030	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2360	119	12031	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
2361	120	12032	12/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
2362	121	12033	12/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXO
2363	122	12034	12/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
2364	123	12035	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
2365	124	12036	12/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
2366	125	12037	12/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
2367	126	12038	12/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBM
2368	127	12039	12/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
2369	128	12040	12/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
2370	129	12041	12/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
2371	130	12042	12/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
2372	131	12043	12/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
2373	132	12044	12/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
2374	133	12045	12/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
2375	134	12046	12/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
2376	135	12047	12/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
2377	136	12048	12/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2378	137	12049	12/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVA
2379	138	12050	12/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
2380	139	12051	12/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
2381	140	12052	12/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
2382	1	12053	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2383	2	12054	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
2384	3	12055	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2385	4	12056	13/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
2386	5	12057	13/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
2387	6	12058	13/04/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
2388	7	12059	13/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
2389	8	12060	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
2390	9	12061	13/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBL
2391	10	12062	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
2392	11	12063	13/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2393	12	12064	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
2394	13	12065	13/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2395	14	12066	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2396	15	12067	13/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
2397	16	12068	13/04/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
2398	17	12069	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
2399	18	12070	13/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
2400	19	12071	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2401	20	12072	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
2402	21	12073	13/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
2403	22	12074	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
2404	23	12075	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2405	24	12076	13/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM

2406	25	12077	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2407	26	12078	13/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
2408	27	12079	13/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
2409	28	12080	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
2410	29	12081	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
2411	30	12082	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2412	31	12083	13/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
2413	32	12084	13/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2414	33	12085	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
2415	34	12086	13/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2416	35	12087	13/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVA
2417	36	12088	13/04/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
2418	37	12089	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2419	38	12090	13/04/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
2420	39	12091	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2421	40	12092	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
2422	41	12093	13/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
2423	42	12094	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2424	43	12095	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
2425	44	12096	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2426	45	12097	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2427	46	12098	13/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
2428	47	12099	13/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
2429	48	12100	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
2430	49	12101	13/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
2431	50	12102	13/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2432	51	12103	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
2433	52	12104	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
2434	53	12105	13/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVA
2435	54	12106	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2436	55	12107	13/04/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
2437	56	12108	13/04/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
2438	57	12109	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
2439	58	12110	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2440	59	12111	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
2441	60	12112	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2442	61	12113	13/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
2443	62	12114	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
2444	63	12115	13/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
2445	64	12116	13/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2446	65	12117	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
2447	66	12118	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
2448	67	12119	13/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2449	68	12120	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2450	69	12121	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
2451	70	12122	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
2452	71	12123	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2453	72	12124	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
2454	73	12125	13/04/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
2455	75	12127	13/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
2456	76	12128	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
2457	77	12129	13/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
2458	78	12130	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2459	79	12131	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
2460	80	12132	13/04/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
2461	81	12133	13/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
2462	82	12134	13/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
2463	83	12135	13/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
2464	84	12136	13/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
2465	85	12137	13/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
2466	86	12138	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
2467	87	12139	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
2468	88	12140	13/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2469	89	12141	13/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
2470	90	12142	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2471	91	12143	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2472	92	12144	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
2473	93	12145	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2474	94	12146	13/04/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
2475	95	12147	13/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
2476	96	12148	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
2477	97	12149	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2478	98	12150	13/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
2479	99	12151	13/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2480	100	12152	13/04/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
2481	101	12153	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
2482	102	12154	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
2483	103	12155	13/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
2484	104	12156	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
2485	105	12157	13/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2486	106	12158	13/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
2487	107	12159	13/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
2488	108	12160	13/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBM
2489	109	12161	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2490	110	12162	13/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
2491	111	12163	13/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
2492	112	12164	13/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
2493	113	12165	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
2494	114	12166	13/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
2495	115	12167	13/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
2496	116	12168	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2497	117	12169	13/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
2498	118	12170	13/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
2499	119	12171	13/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
2500	120	12172	13/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
2501	121	12173	13/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVA
2502	122	12174	13/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
2503	123	12175	13/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
2504	124	12176	13/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
2505	125	12177	13/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
2506	1	12178	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
2507	2	12179	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2508	3	12180	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBK
2509	4	12181	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2510	5	12182	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2511	6	12183	14/04/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
2512	7	12184	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
2513	8	12185	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
2514	9	12186	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2515	10	12187	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2516	11	12188	14/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
2517	12	12189	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2518	13	12190	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
2519	14	12191	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
2520	15	12192	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
2521	16	12193	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
2522	17	12194	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2523	18	12195	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
2524	19	12196	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
2525	20	12197	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
2526	21	12198	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2527	22	12199	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
2528	23	12200	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2529	24	12201	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2530	25	12202	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
2531	26	12203	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2532	27	12204	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB

2533	28	12205	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2534	29	12206	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
2535	30	12207	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
2536	31	12208	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2537	32	12209	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
2538	33	30002	14/04/2021	170107	3900	Concrete/Hard Materials	9	Ashton Old Rd	CBDU90617	MV20RKJ
2539	34	12210	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
2540	35	12211	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
2541	36	12212	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2542	37	12213	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2543	38	12214	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
2544	39	12215	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
2545	40	12216	14/04/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
2546	41	12217	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2547	42	12218	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
2548	43	12219	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2549	44	12220	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2550	45	12221	14/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
2551	46	12222	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
2552	47	12223	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2553	48	12224	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
2554	49	12225	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2555	50	12226	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
2556	51	12227	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
2557	52	12228	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2558	53	12229	14/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
2559	54	30003	14/04/2021	170107	3900	Concrete/Hard Materials	9	Ashton Old Rd	CBDU90617	MV19UBL
2560	55	30004	14/04/2021	170107	3900	Concrete/Hard Materials	9	Ashton Old Rd	CBDU90617	MV20RKJ
2561	56	12230	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2562	57	12231	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2563	58	12232	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
2564	59	12233	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
2565	60	12234	14/04/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
2566	61	12235	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2567	62	12236	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
2568	63	12237	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2569	64	12238	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2570	65	12239	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
2571	66	12240	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2572	67	12241	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
2573	68	12242	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
2574	69	12243	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2575	70	12244	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2576	71	12245	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
2577	72	12246	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
2578	73	12247	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2579	74	30005	14/04/2021	170107	3900	Concrete/Hard Materials	9	Ashton Old Rd	CBDU90617	MV19UBL
2580	75	12248	14/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
2581	76	30006	14/04/2021	170107	3900	Concrete/Hard Materials	9	Ashton Old Rd	CBDU90617	MV20RKJ
2582	77	12249	14/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
2583	78	12250	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
2584	79	12251	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
2585	80	12252	14/04/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
2586	81	12253	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
2587	82	12254	14/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
2588	83	30007	14/04/2021	170107	3900	Concrete/Hard Materials	9	Ashton Old Rd	CBDU90617	MV20RKJ
2589	84	12255	14/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
2590	85	30008	14/04/2021	170107	3900	Concrete/Hard Materials	9	Ashton Old Rd	CBDU90617	MV19UBL
2591	86	12256	14/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
2592	87	12257	14/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
2593	88	12258	14/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
2594	89	12259	14/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
2595	90	12260	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2596	91	12261	14/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
2597	92	12262	14/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
2598	93	12263	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2599	94	12264	14/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
2600	95	12265	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
2601	96	12266	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2602	97	30009	14/04/2021	170107	3900	Concrete/Hard Materials	9	Ashton Old Rd	CBDU90617	MV20RKJ
2603	98	12267	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
2604	99	12268	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2605	100	12269	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
2606	101	12270	14/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
2607	102	12271	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
2608	103	12272	14/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
2609	104	12273	14/04/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
2610	105	12274	14/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
2611	106	12275	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2612	107	12276	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
2613	108	12277	14/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
2614	109	12278	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2615	110	12279	14/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
2616	111	12280	14/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
2617	112	12281	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
2618	113	12282	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2619	114	30010	14/04/2021	170107	3900	Concrete/Hard Materials	9	Ashton Old Rd	CBDU90617	MV19UBK
2620	115	12283	14/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
2621	116	30011	14/04/2021	170107	3900	Concrete/Hard Materials	9	Ashton Old Rd	CBDU90617	MV20RKJ
2622	117	12284	14/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
2623	118	12285	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2624	119	12286	14/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
2625	120	12287	14/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
2626	121	12288	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
2627	122	12289	14/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
2628	123	12290	14/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
2629	124	12291	14/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2630	125	12292	14/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
2631	126	12293	14/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
2632	127	12294	14/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
2633	128	12295	14/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
2634	129	12296	14/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
2635	130	12297	14/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
2636	131	12298	14/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
2637	132	12299	14/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
2638	133	12300	14/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
2639	134	12301	14/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
2640	135	12302	14/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBM
2641	136	12303	14/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
2642	1	12304	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
2643	2	12305	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2644	3	12306	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
2645	4	12307	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2646	5	12308	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
2647	6	12309	15/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
2648	7	12310	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2649	8	12311	15/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
2650	9	12312	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBK
2651	10	12313	15/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBL
2652	11	12314	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2653	12	12315	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
2654	13	12316	15/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
2655	14	12317	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2656	15	12318	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2657	16	12319	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
2658	17	12320	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
2659	18	12321	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXZ

2660	19	12322	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
2661	20	12323	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
2662	21	12324	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
2663	22	12325	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2664	23	12326	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
2665	24	12327	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
2666	25	12328	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2667	26	12329	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
2668	27	12330	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2669	28	12331	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
2670	29	12332	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2671	30	12333	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
2672	31	12334	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2673	32	12335	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2674	33	12336	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2675	34	12337	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2676	35	12338	15/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
2677	36	12339	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2678	37	12340	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
2679	38	12341	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
2680	39	12342	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
2681	40	12343	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2682	41	12344	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2683	42	12345	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
2684	43	12346	15/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
2685	44	12347	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXZ
2686	45	12348	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2687	46	12349	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2688	47	30012	15/04/2021	170407	3900	Mixed Metals	0	EMR	CBDU90617	MV19UBM
2689	48	12350	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2690	49	12351	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2691	50	12352	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2692	51	12353	15/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX21ORT
2693	52	12354	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2694	53	12355	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
2695	54	12356	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
2696	55	12357	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
2697	56	12358	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2698	57	12359	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2699	58	12360	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
2700	59	12361	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
2701	60	12362	15/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
2702	61	12363	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2703	62	12364	15/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
2704	63	12365	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	FMV18FVB
2705	64	12366	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2706	65	12367	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2707	66	12368	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2708	67	12369	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
2709	68	12370	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
2710	69	12371	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
2711	70	12372	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
2712	71	12373	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXZ
2713	72	12374	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
2714	73	12375	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2715	74	12376	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2716	75	12377	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
2717	76	12378	15/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
2718	77	12379	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2719	78	12380	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2720	79	12381	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2721	80	12382	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2722	81	12383	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
2723	82	12384	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
2724	83	12385	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
2725	84	12386	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
2726	85	12387	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2727	86	12388	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2728	87	12389	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2729	88	12390	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
2730	89	12391	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
2731	90	12392	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2732	91	12393	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2733	92	12394	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2734	93	12395	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
2735	94	12396	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2736	95	12397	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
2737	96	12398	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
2738	97	12399	15/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
2739	98	12400	15/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
2740	99	12401	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
2741	100	12402	15/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
2742	101	12403	15/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2743	102	12404	15/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXZ
2744	103	12405	15/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
2745	104	12406	15/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBM
2746	105	12407	15/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
2747	106	12408	15/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
2748	107	12409	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2749	108	12410	15/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
2750	109	12411	15/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
2751	110	12412	15/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
2752	111	12413	15/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
2753	112	12414	15/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
2754	113	12415	15/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
2755	1	12416	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2756	2	12417	16/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXU
2757	3	12418	16/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
2758	4	12419	16/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
2759	5	12420	16/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
2760	6	12421	16/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
2761	7	12422	16/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
2762	8	12423	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2763	9	12424	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2764	10	12425	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
2765	11	12426	16/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
2766	12	12427	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
2767	13	12428	16/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
2768	14	12429	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
2769	15	12430	16/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
2770	16	12431	16/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2771	17	12432	16/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
2772	18	12433	16/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBK
2773	19	PROVEC50321	16/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYH
2774	20	PROVEC50322	16/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYK
2775	21	PROVEC50324	16/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
2776	22	12434	16/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
2777	23	12435	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
2778	24	12436	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
2779	25	12437	16/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
2780	26	PROVEC50324	16/04/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
2781	27	12438	16/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
2782	28	12439	16/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
2783	29	12440	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2784	30	12441	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
2785	31	12442	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2786	32	12443	16/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX16CVV

2787	33	12444	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
2788	34	12445	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2789	35	12446	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
2790	36	12447	16/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2791	37	12448	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
2792	38	12449	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
2793	39	12450	16/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
2794	40	12451	16/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
2795	41	12452	16/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
2796	42	12453	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2797	43	12454	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
2798	44	12455	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2799	45	12456	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2800	46	12457	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2801	47	12458	16/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
2802	48	12459	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
2803	49	PROVEC50325	16/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYH
2804	50	12460	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
2805	51	12461	16/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
2806	52	12462	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
2807	53	12463	16/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
2808	54	PROVEC50326	16/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
2809	55	PROVEC50327	16/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYK
2810	56	12464	16/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
2811	57	12465	16/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
2812	58	12466	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2813	59	12467	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
2814	60	PROVEC50328	16/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	PN19HVC
2815	61	PROVEC50329	16/04/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
2816	62	12468	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2817	63	12469	16/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2818	64	12470	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
2819	65	12471	16/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
2820	66	12472	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
2821	67	12473	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
2822	68	12474	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2823	69	12475	16/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
2824	70	12476	16/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
2825	71	12477	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
2826	72	12478	16/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
2827	73	12479	16/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
2828	74	12480	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2829	75	12481	16/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
2830	76	12482	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2831	77	PROVEC50330	16/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYH
2832	78	12483	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
2833	79	12484	16/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
2834	80	PROVEC50331	16/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYK
2835	81	PROVEC50332	16/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
2836	82	PROVEC50333	16/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU90617	PN19HVC
2837	83	12485	16/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
2838	84	12486	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
2839	85	12487	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2840	86	12488	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
2841	87	12489	16/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
2842	88	12490	16/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
2843	89	12491	16/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
2844	90	12492	16/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
2845	91	12493	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2846	92	12494	16/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2847	93	12495	16/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
2848	94	12496	16/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
2849	95	12497	16/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
2850	96	12498	16/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
2851	97	12499	16/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
2852	98	12500	16/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
2853	99	12501	16/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
2854	100	12502	16/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
2855	101	12503	16/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
2856	102	12504	16/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBM
2857	103	12505	16/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
2858	104	PROVEC50334	16/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	PN21KCJ
2859	1	12506	19/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
2860	2	12507	19/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
2861	3	12508	19/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
2862	4	12509	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2863	5	12510	19/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
2864	6	12511	19/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
2865	7	12512	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2866	8	12513	19/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
2867	9	12514	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
2868	10	12515	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
2869	11	12516	19/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
2870	12	12517	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
2871	13	12518	19/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2872	14	12519	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2873	15	12520	19/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
2874	16	12521	19/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
2875	17	12522	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2876	18	12523	19/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2877	19	12524	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
2878	20	12525	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2879	21	12526	19/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
2880	22	12527	19/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
2881	23	12528	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
2882	24	PROVEC50335	19/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
2883	25	12529	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
2884	26	PROVEC50336	19/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
2885	27	12530	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2886	28	PROVEC50337	19/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
2887	29	12531	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
2888	30	12532	19/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
2889	31	12533	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
2890	32	12534	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBC
2891	33	PROVEC50338	19/04/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
2892	34	12535	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
2893	35	12536	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
2894	36	12537	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2895	37	12538	19/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
2896	38	12539	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2897	39	12540	19/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2898	40	12541	19/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2899	41	12542	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
2900	42	12543	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2901	43	12544	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2902	44	12545	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
2903	45	12546	19/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
2904	46	12547	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
2905	47	12548	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
2906	48	12549	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
2907	49	12550	19/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
2908	50	12551	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
2909	51	12552	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
2910	52	12553	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
2911	53	12554	19/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
2912	54	12555	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
2913	55	12556	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH

2914	56	12557	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
2915	57	12558	19/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
2916	58	12559	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2917	59	12560	19/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2918	60	12561	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2919	61	12562	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
2920	62	12563	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2921	63	12564	19/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
2922	64	PROVEC50339	19/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	PN21KCJ
2923	65	PROVEC50340	19/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
2924	66	12565	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
2925	67	PROVEC50341	19/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
2926	68	12566	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
2927	69	12567	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
2928	70	PROVEC50342	19/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
2929	71	PROVEC50343	19/04/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
2930	72	12568	19/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
2931	73	12569	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
2932	74	12570	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
2933	75	12571	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
2934	76	12572	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
2935	77	12573	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
2936	78	12574	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2937	79	12575	19/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2938	80	12576	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
2939	81	12577	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
2940	82	12578	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2941	83	12579	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
2942	84	12580	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
2943	85	12581	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
2944	86	12582	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
2945	87	12583	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
2946	88	12584	19/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
2947	89	12585	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
2948	90	12586	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
2949	91	12587	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
2950	92	12588	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
2951	93	12589	19/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
2952	94	12590	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2953	95	PROVEC50344	19/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
2954	96	12591	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
2955	97	12592	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
2956	98	12593	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
2957	99	PROVEC50345	19/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	PN21KCJ
2958	100	PROVEC50346	19/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
2959	101	PROVEC50347	19/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
2960	102	12594	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
2961	103	12595	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2962	104	12596	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
2963	105	PROVEC50348	19/04/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
2964	106	12597	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2965	107	12598	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
2966	108	12599	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18UBA
2967	109	12600	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
2968	110	12601	19/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
2969	111	12602	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
2970	112	12603	19/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
2971	113	12604	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
2972	114	12605	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
2973	115	12606	19/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	DE70OEC
2974	116	12607	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
2975	117	12608	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
2976	118	12609	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
2977	119	12610	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
2978	120	12611	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
2979	121	12612	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
2980	122	12613	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
2981	123	12614	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
2982	124	12615	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
2983	125	12616	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
2984	126	12617	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
2985	127	12618	19/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
2986	128	12619	19/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
2987	129	12620	19/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
2988	130	12621	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
2989	131	PROVEC50350	19/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
2990	132	12622	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
2991	133	12623	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
2992	134	12624	19/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
2993	135	PROVEC50351	19/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
2994	136	PROVEC50352	19/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	PN21KCJ
2995	1	PROVEC50353	20/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
2996	2	PROVEC50354	20/04/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
2997	3	12625	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
2998	4	12626	20/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
2999	5	12627	20/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
3000	6	12628	20/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
3001	7	12629	20/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
3002	8	12630	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
3003	9	12631	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3004	10	12632	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
3005	11	12633	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
3006	12	12634	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
3007	13	12635	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
3008	14	12636	20/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXZ
3009	15	12637	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
3010	16	12638	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
3011	17	12639	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
3012	18	12640	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
3013	19	12641	20/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	RV69ZVD
3014	20	12642	20/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBL
3015	21	12643	20/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	DE70OEC
3016	22	12644	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3017	23	12645	20/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
3018	24	12646	20/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
3019	25	12647	20/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
3020	26	12648	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3021	27	12649	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
3022	28	12650	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
3023	29	12651	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
3024	30	12652	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3025	31	12653	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
3026	32	12654	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
3027	33	12655	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
3028	34	12656	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
3029	35	12657	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3030	36	12658	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
3031	37	12659	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
3032	38	12660	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3033	39	12661	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
3034	40	12662	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3035	41	12663	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
3036	42	12664	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
3037	43	12665	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3038	44	12666	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
3039	45	12667	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
3040	46	12668	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD

3041	47	12669	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
3042	48	12670	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
3043	49	PROVEC50355	20/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	PN21KCJ
3044	50	PROVEC50356	20/04/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
3045	51	PROVEC50357	20/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	MK21EVW
3046	52	PROVEC50358	20/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
3047	53	12671	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
3048	54	12672	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
3049	55	12673	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
3050	56	12674	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3051	57	12675	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
3052	58	12676	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
3053	59	12677	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
3054	60	12678	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
3055	61	12679	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
3056	62	12680	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
3057	63	12681	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
3058	64	12682	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
3059	65	PROVEC50359	20/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
3060	66	12683	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
3061	67	12684	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
3062	68	12685	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
3063	69	12686	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
3064	70	12687	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
3065	71	12688	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
3066	72	12689	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
3067	73	12690	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
3068	74	12691	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
3069	75	12692	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
3070	76	12693	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
3071	77	12694	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
3072	78	PROVEC50360	20/04/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
3073	79	PROVEC50361	20/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
3074	80	PROVEC50362	20/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	PN21KCJ
3075	81	PROVEC50363	20/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
3076	82	12695	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
3077	83	12696	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
3078	84	12697	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
3079	85	12698	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
3080	86	12699	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3081	87	12700	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3082	88	12701	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
3083	89	12702	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
3084	90	12703	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
3085	91	12704	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
3086	92	12705	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
3087	93	12706	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
3088	94	PROVEC50364	20/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
3089	95	12707	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
3090	96	12708	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX21ORT
3091	97	12709	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
3092	98	12710	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
3093	99	12711	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
3094	100	12712	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
3095	101	12713	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
3096	102	12714	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
3097	103	12715	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
3098	104	12716	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
3099	105	12717	20/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
3100	106	12718	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
3101	107	12719	20/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
3102	108	PROVEC50365	20/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
3103	109	PROVEC50366	20/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	PN21KCJ
3104	1	PROVEC50367	21/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
3105	2	PROVEC50368	21/04/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
3106	3	12720	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX21ORT
3107	4	12721	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
3108	5	12722	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
3109	6	12723	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX16CVV
3110	7	12724	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
3111	8	12725	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
3112	9	12726	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
3113	10	12727	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
3114	11	12728	21/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
3115	12	12729	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
3116	13	12730	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
3117	14	12731	21/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
3118	15	12732	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
3119	16	12733	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
3120	17	12734	21/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
3121	18	12735	21/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	DE70OEC
3122	19	12736	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3123	20	12737	21/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
3124	21	12738	21/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBL
3125	22	12739	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3126	23	12740	21/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
3127	24	12741	21/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
3128	25	12742	21/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
3129	26	PROVEC50369	21/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
3130	27	12743	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
3131	28	12744	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
3132	29	12745	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
3133	30	12746	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
3134	31	12747	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
3135	32	12748	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
3136	33	12749	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
3137	34	12750	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
3138	35	12751	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
3139	36	12752	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3140	37	12753	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
3141	38	12754	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3142	39	12755	21/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
3143	40	12756	21/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
3144	41	12757	21/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
3145	42	12758	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
3146	43	12759	21/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
3147	44	12760	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
3148	45	12761	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
3149	46	12762	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
3150	47	12763	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
3151	48	12764	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
3152	49	12765	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
3153	50	12766	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3154	51	12767	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
3155	52	12768	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
3156	53	12769	21/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
3157	54	PROVEC50370	21/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	PN21KCJ
3158	55	12770	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3159	56	PROVEC50371	21/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
3160	57	PROVEC50372	21/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
3161	58	PROVEC50373	21/04/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
3162	59	12771	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
3163	60	PROVEC50374	21/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
3164	61	12772	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
3165	62	12773	21/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
3166	63	12774	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
3167	64	12775	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD

3168	65	12776	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
3169	66	12777	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
3170	67	12778	21/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
3171	68	12779	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
3172	69	12780	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
3173	70	12781	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
3174	71	12782	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
3175	72	12783	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
3176	73	12784	21/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
3177	74	12785	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3178	75	12786	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
3179	76	12787	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
3180	77	12788	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
3181	78	12789	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
3182	79	12790	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
3183	80	12791	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
3184	81	12792	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
3185	82	12793	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
3186	83	12794	21/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
3187	84	12795	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
3188	85	12796	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
3189	86	PROVEC50375	21/04/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
3190	87	12797	21/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
3191	88	PROVEC50376	21/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
3192	89	PROVEC50377	21/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
3193	90	PROVEC50378	21/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU46027	PN21KCJ
3194	91	PROVEC50379	21/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
3195	92	12798	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
3196	93	12799	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
3197	94	12800	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
3198	95	12801	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
3199	96	12802	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
3200	97	12803	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
3201	98	12804	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
3202	99	12805	21/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
3203	100	12806	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
3204	101	12807	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
3205	102	12808	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
3206	103	12809	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
3207	104	12810	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3208	105	12811	21/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
3209	106	12812	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
3210	107	12813	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
3211	108	12814	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
3212	109	12815	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
3213	110	12816	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
3214	111	12817	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
3215	112	12818	21/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
3216	113	12819	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
3217	114	12820	21/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
3218	115	12821	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
3219	116	12822	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
3220	117	12823	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
3221	118	12824	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
3222	119	PROVEC50380	21/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
3223	120	PROVEC50381	21/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
3224	121	12825	21/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
3225	122	12826	21/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
3226	1	12827	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX21ORT
3227	2	12828	22/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
3228	3	12829	22/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
3229	4	PROVEC50382	22/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
3230	5	PROVEC50383	22/04/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
3231	6	12830	22/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
3232	7	12831	22/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
3233	8	12832	22/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
3234	9	12833	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
3235	10	12834	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
3236	11	12835	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
3237	12	12836	22/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
3238	13	12837	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
3239	14	12838	22/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXU
3240	15	12839	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
3241	16	12840	22/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBL
3242	17	12841	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
3243	18	12842	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
3244	19	12843	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
3245	20	12844	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
3246	21	12845	22/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
3247	22	12846	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3248	23	12847	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
3249	24	12848	22/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
3250	25	12849	22/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
3251	26	12850	22/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
3252	27	12851	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3253	28	12852	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	SO64EEX
3254	29	12853	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3255	30	12854	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
3256	31	12855	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
3257	32	12856	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
3258	33	12857	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
3259	34	12858	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
3260	35	12859	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
3261	36	12860	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
3262	37	12861	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
3263	38	12862	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
3264	39	12863	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
3265	40	12864	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3266	41	12865	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3267	42	12866	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
3268	43	12867	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3269	44	12868	22/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
3270	45	12869	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
3271	46	12870	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
3272	47	12871	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
3273	48	12872	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
3274	49	12873	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
3275	50	12874	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
3276	51	12875	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
3277	52	12876	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
3278	53	12877	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
3279	54	PROVEC50384	22/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
3280	55	12878	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
3281	56	PROVEC50385	22/04/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
3282	57	PROVEC50386	22/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
3283	58	PROVEC50387	22/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
3284	59	12879	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3285	60	12880	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3286	61	12881	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3287	62	12882	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
3288	63	12883	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
3289	64	12884	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
3290	65	12885	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
3291	66	12886	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
3292	67	12887	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
3293	68	12888	22/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
3294	69	12889	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA

3295	70	12890	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
3296	71	12891	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
3297	72	12892	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
3298	73	12893	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
3299	74	12894	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3300	75	12895	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
3301	76	PROVEC50388	22/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
3302	77	12896	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
3303	78	12897	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
3304	79	12898	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
3305	80	PROVEC50389	22/04/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
3306	81	12899	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
3307	82	12900	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
3308	83	12901	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
3309	84	PROVEC50390	22/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
3310	85	12902	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
3311	86	12903	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
3312	87	12904	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
3313	88	12905	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
3314	89	12906	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
3315	90	PROVEC50391	22/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
3316	91	12907	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
3317	92	12908	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
3318	93	12909	22/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
3319	94	12910	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
3320	95	12911	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
3321	96	12912	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
3322	97	12913	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
3323	98	12914	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
3324	99	12915	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
3325	100	12916	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
3326	101	12917	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
3327	102	12918	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19FVC
3328	103	12919	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
3329	104	12920	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3330	105	12921	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3331	106	12922	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
3332	107	12923	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
3333	108	12924	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
3334	109	PROVEC50392	22/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
3335	110	12925	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
3336	111	12926	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
3337	112	12927	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
3338	113	PROVEC50393	22/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
3339	114	12928	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
3340	115	12929	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
3341	116	12930	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
3342	117	12931	22/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19FVC
3343	118	12932	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
3344	119	12933	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
3345	120	12934	22/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
3346	1	12935	23/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
3347	2	12936	23/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
3348	3	12937	23/04/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
3349	4	12938	23/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
3350	5	12939	23/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX16CVV
3351	6	12940	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
3352	7	12941	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
3353	8	12942	23/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
3354	9	12943	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3355	10	12944	23/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
3356	11	12945	23/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
3357	12	12946	23/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
3358	13	12947	23/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBL
3359	14	12948	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
3360	15	12949	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
3361	16	12950	23/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
3362	17	12951	23/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
3363	18	12952	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
3364	19	12953	23/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
3365	20	12954	23/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
3366	21	12955	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3367	22	12956	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
3368	23	12957	23/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
3369	24	PROVEC50394	23/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
3370	25	12958	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
3371	26	12959	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3372	27	12960	23/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	SO64EEX
3373	28	12961	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
3374	29	12962	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
3375	30	12963	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
3376	31	12964	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
3377	32	12965	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
3378	33	12966	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3379	34	12967	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3380	35	12968	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
3381	36	12969	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
3382	37	12970	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
3383	38	12971	23/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
3384	39	12972	23/04/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
3385	40	12973	23/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
3386	41	12974	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
3387	42	12975	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
3388	43	12976	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
3389	44	12977	23/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
3390	45	12978	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
3391	46	PROVEC50395	23/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
3392	47	12979	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
3393	48	12980	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3394	49	PROVEC50396	23/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
3395	50	12981	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3396	51	12982	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
3397	52	12983	23/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
3398	53	PROVEC50397	23/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
3399	54	12984	23/04/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
3400	55	12985	23/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
3401	56	12986	23/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
3402	57	12987	23/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
3403	58	12988	23/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
3404	59	12989	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
3405	60	12990	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
3406	61	12991	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
3407	62	12992	23/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
3408	63	12993	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3409	64	12994	23/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
3410	65	PROVEC50398	23/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
3411	66	12995	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
3412	67	12996	23/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
3413	68	12997	23/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
3414	69	12998	23/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
3415	70	12999	23/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
3416	71	13000	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
3417	72	13001	23/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
3418	73	PROVEC50399	23/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
3419	74	13002	23/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
3420	75	13003	23/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
3421	76	13004	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA

3422	77	13005	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
3423	78	PROVEC50400	23/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
3424	79	13006	23/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
3425	80	13007	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
3426	81	13008	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
3427	82	13009	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
3428	83	13010	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
3429	84	13011	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
3430	85	13012	23/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
3431	86	13013	23/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
3432	87	13014	23/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
3433	88	13015	23/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
3434	89	13016	23/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
3435	90	13017	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
3436	91	13018	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
3437	92	13019	23/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
3438	93	13020	23/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
3439	94	13021	23/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
3440	95	PROVEC50401	23/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
3441	1	13022	26/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXU
3442	2	13023	26/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
3443	3	13024	26/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
3444	4	13025	26/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXL
3445	5	13026	26/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
3446	6	13027	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
3447	7	13028	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX16CVV
3448	8	13029	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
3449	9	13030	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
3450	10	13031	26/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
3451	11	13032	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
3452	12	13033	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
3453	13	13034	26/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
3454	14	13035	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3455	15	13036	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
3456	16	13037	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
3457	17	13038	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3458	18	PROVEC50402	26/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
3459	19	13039	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
3460	20	PROVEC50403	26/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYH
3461	21	13040	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	SO64EEX
3462	22	13041	26/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
3463	23	13042	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
3464	24	PROVEC50404	26/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
3465	25	13043	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX16CVV
3466	26	13044	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
3467	27	13045	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
3468	28	13046	26/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
3469	29	13047	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
3470	30	13048	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
3471	31	13049	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
3472	32	13050	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
3473	33	13051	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3474	34	13052	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3475	35	13053	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	SO64EEX
3476	36	13054	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
3477	37	13055	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3478	38	13056	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX16CVV
3479	39	13057	26/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
3480	40	13058	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
3481	41	13059	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
3482	42	13060	26/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
3483	43	13061	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
3484	44	PROVEC50405	26/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
3485	45	13062	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
3486	46	PROVEC50406	26/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
3487	47	13063	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
3488	48	13064	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
3489	49	13065	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3490	50	PROVEC50407	26/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYH
3491	51	13066	26/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
3492	52	13067	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3493	53	13068	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	SO64EEX
3494	54	PROVEC50408	26/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
3495	55	13069	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3496	56	13070	26/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
3497	57	13071	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
3498	58	13072	26/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
3499	59	13073	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
3500	60	13074	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX16CVV
3501	61	13075	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
3502	62	13076	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
3503	63	13077	26/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
3504	64	13078	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
3505	65	13079	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
3506	66	13080	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
3507	67	13081	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
3508	68	13082	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	SO64EEX
3509	69	13083	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
3510	70	13084	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX16CVV
3511	71	13085	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
3512	72	13086	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
3513	73	13087	26/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
3514	74	13088	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3515	75	PROVEC50410	26/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
3516	76	PROVEC50409	26/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLY
3517	77	13089	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
3518	78	13090	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
3519	79	13091	26/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
3520	80	13092	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
3521	81	13093	26/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
3522	82	13094	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
3523	83	13095	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
3524	84	13096	26/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
3525	85	13097	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
3526	86	13098	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
3527	87	13099	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	SO64EEX
3528	88	PROVEC50411	26/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	PN19YYH
3529	89	13100	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX16CVV
3530	90	13101	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
3531	91	13102	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
3532	92	13103	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3533	93	PROVEC50412	26/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU119097	WX16MLV
3534	94	13104	26/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
3535	95	13105	26/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
3536	96	13106	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
3537	97	13107	26/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
3538	98	13108	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
3539	99	13109	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
3540	100	13110	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
3541	101	13111	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
3542	102	13112	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3543	103	13113	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3544	104	13114	26/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
3545	105	13115	26/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	SO64EEX
3546	106	13116	26/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
3547	107	13117	26/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
3548	108	13118	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT

3549	109	13119	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX16CVV
3550	110	13120	26/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
3551	111	13121	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
3552	112	13122	26/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXV
3553	113	13123	26/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
3554	114	13124	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
3555	115	13125	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX21ORT
3556	116	13126	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
3557	117	13127	26/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBM
3558	118	13128	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
3559	119	13129	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
3560	120	13130	26/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
3561	121	13131	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
3562	122	13132	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
3563	123	13133	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
3564	124	13134	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
3565	125	13135	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
3566	126	13136	26/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	SO64EEX
3567	1	13137	27/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXV
3568	2	13138	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
3569	3	13139	27/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBK
3570	4	13140	27/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXO
3571	5	13141	27/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
3572	6	13142	27/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV19UBD
3573	7	13143	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
3574	8	13144	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX16CVV
3575	9	13145	27/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXU
3576	10	13146	27/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
3577	11	13147	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
3578	12	13148	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
3579	13	13149	27/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXL
3580	14	13150	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
3581	15	13151	27/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
3582	16	13152	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3583	17	13153	27/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
3584	18	13154	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3585	19	13155	27/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
3586	20	13156	27/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBL
3587	21	13157	27/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
3588	22	13158	27/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
3589	23	13159	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3590	24	PROVEC50413	27/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
3591	25	13160	27/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
3592	26	13161	27/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
3593	27	13162	27/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
3594	28	13163	27/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
3595	29	13164	27/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
3596	30	13165	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
3597	31	13166	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX16CVV
3598	32	13167	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
3599	33	13168	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
3600	34	13169	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
3601	35	13170	27/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
3602	36	13171	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
3603	37	13172	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3604	38	13173	27/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
3605	39	13174	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3606	40	13175	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3607	41	13176	27/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
3608	42	13177	27/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
3609	43	13178	27/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
3610	44	13179	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
3611	45	13180	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX16CVV
3612	46	13181	27/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
3613	47	13182	27/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
3614	48	13183	27/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
3615	49	13184	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
3616	50	13185	27/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
3617	51	13186	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3618	52	13187	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3619	53	13188	27/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
3620	54	13189	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3621	55	13190	27/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
3622	56	13191	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
3623	57	13192	27/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
3624	58	PROVEC50414	27/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
3625	59	13193	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
3626	60	13194	27/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
3627	61	13195	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX16CVV
3628	62	13196	27/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
3629	63	13197	27/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
3630	64	13198	27/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
3631	65	13199	27/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
3632	66	13200	27/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
3633	67	13201	27/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
3634	68	13202	27/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
3635	69	13203	27/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
3636	70	13204	27/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
3637	71	13205	27/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
3638	72	13206	27/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
3639	73	13207	27/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX16CVV
3640	74	13208	27/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
3641	75	13209	27/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
3642	76	13210	27/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
3643	77	13211	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
3644	78	PROVEC50415	27/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
3645	79	13212	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
3646	80	13213	27/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
3647	81	13214	27/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
3648	82	13215	27/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
3649	83	13216	27/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
3650	84	13217	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
3651	85	13218	27/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
3652	86	13219	27/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
3653	87	13220	27/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
3654	88	13221	27/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXM
3655	89	13222	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
3656	90	13223	27/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX16CVV
3657	91	13224	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3658	92	13225	27/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
3659	93	13226	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
3660	94	13227	27/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
3661	95	13228	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
3662	96	13229	27/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
3663	97	13230	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3664	98	13231	27/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
3665	99	13232	27/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
3666	100	13233	27/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
3667	101	13234	27/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3668	102	13235	27/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXM
3669	103	13236	27/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
3670	104	13237	27/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
3671	105	13238	27/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
3672	106	13239	27/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX16CVV
3673	107	13240	27/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBL
3674	108	13241	27/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
3675	109	13242	27/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB

3676	110	13243	27/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
3677	111	13244	27/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
3678	112	13245	27/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
3679	113	13246	27/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
3680	114	13247	27/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
3681	115	13248	27/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
3682	116	13249	27/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
3683	117	13250	27/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
3684	118	13251	27/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
3685	1	13252	28/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXU
3686	2	13253	28/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
3687	3	13254	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
3688	4	13255	28/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
3689	5	13256	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
3690	6	13257	28/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXL
3691	7	13258	28/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
3692	8	13259	28/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
3693	9	13260	28/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
3694	10	13261	28/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX16CVV
3695	11	13262	28/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3696	12	13263	28/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
3697	13	13264	28/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXV
3698	14	13265	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
3699	15	13266	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
3700	16	13267	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
3701	17	PROVEC50416	28/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
3702	18	13268	28/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
3703	19	13269	28/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
3704	20	13270	28/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3705	21	13271	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
3706	22	13272	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
3707	23	13273	28/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3708	24	13274	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
3709	25	13275	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
3710	26	13276	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
3711	27	13277	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
3712	28	13278	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
3713	29	13279	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
3714	30	13280	28/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3715	31	13281	28/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX16CVV
3716	32	13282	28/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3717	33	13283	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
3718	34	13284	28/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
3719	35	13285	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
3720	36	13286	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
3721	37	13287	28/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3722	38	13288	28/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
3723	39	13289	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
3724	40	13290	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
3725	41	13291	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
3726	42	13292	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
3727	43	PROVEC50417	28/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
3728	44	13293	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
3729	45	13294	28/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3730	46	13295	28/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3731	47	13296	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
3732	48	13297	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
3733	49	13298	28/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
3734	50	13299	28/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX16CVV
3735	51	13300	28/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3736	52	13301	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
3737	53	13302	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
3738	54	13303	28/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
3739	55	13304	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
3740	56	13305	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
3741	57	13306	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
3742	58	13307	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
3743	59	13308	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
3744	60	13309	28/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3745	61	13310	28/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3746	62	13311	28/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
3747	63	13312	28/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
3748	64	13313	28/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX16CVV
3749	65	13314	28/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
3750	66	PROVEC50418	28/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
3751	67	13315	28/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3752	68	13316	28/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBD
3753	69	13317	28/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
3754	70	13318	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
3755	71	13319	28/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
3756	72	13320	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
3757	73	13321	28/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
3758	74	13322	28/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3759	75	13323	28/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3760	76	13324	28/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
3761	77	13325	28/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
3762	78	13326	28/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX16CVV
3763	79	13327	28/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
3764	80	13328	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
3765	81	13329	28/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
3766	82	13330	28/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
3767	83	13331	28/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
3768	84	13332	28/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3769	85	15019	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	DE70OEC
3770	86	13333	28/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
3771	87	13334	28/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
3772	88	13335	28/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXM
3773	89	13336	28/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
3774	90	13337	28/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX16CVV
3775	91	13338	28/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
3776	92	13339	28/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
3777	93	13340	28/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
3778	94	13341	28/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXV
3779	95	13342	28/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
3780	96	13343	28/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBM
3781	97	13344	28/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
3782	98	13345	28/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
3783	99	13346	28/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
3784	100	13347	28/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
3785	101	13348	28/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBA
3786	102	13349	28/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
3787	103	13350	28/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	DE70OEC
3788	104	13351	28/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
3789	1	13352	29/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
3790	2	13353	29/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXO
3791	3	13354	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX16CVV
3792	4	13355	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
3793	5	13356	29/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
3794	6	13357	29/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
3795	7	13358	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
3796	8	13359	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
3797	9	13360	29/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBD
3798	10	13361	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3799	11	13362	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3800	12	13363	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3801	13	13364	29/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
3802	14	13365	29/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP

3803	15	13366	29/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
3804	16	13367	29/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXU
3805	17	13368	29/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
3806	18	13369	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV20RLY
3807	19	13370	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX16CVV
3808	20	13371	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
3809	21	13372	29/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
3810	22	13373	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
3811	23	13374	29/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
3812	24	13375	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
3813	25	13376	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3814	26	13377	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3815	27	13378	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3816	28	13379	29/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
3817	29	13380	29/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV20RKK
3818	30	13381	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX16CVV
3819	31	13382	29/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
3820	32	13383	29/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
3821	33	13384	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
3822	34	13385	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
3823	35	13386	29/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
3824	36	13387	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3825	37	13388	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3826	38	13389	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3827	39	13390	29/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
3828	40	13391	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX16CVV
3829	41	13392	29/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
3830	42	13393	29/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
3831	43	13394	29/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
3832	44	13395	29/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
3833	45	13396	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
3834	46	13397	29/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
3835	47	13398	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3836	48	13399	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3837	49	13400	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3838	50	13401	29/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX16CVV
3839	51	13402	29/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
3840	52	13403	29/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
3841	53	13404	29/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
3842	54	13405	29/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
3843	55	13406	29/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
3844	56	13407	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
3845	57	13408	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
3846	58	13409	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3847	59	13410	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
3848	60	13411	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3849	61	13412	29/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX16CVV
3850	62	13413	29/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
3851	63	13414	29/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
3852	64	13415	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
3853	65	13416	29/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
3854	66	13417	29/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
3855	67	13418	29/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
3856	68	13419	29/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
3857	69	13420	29/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
3858	70	13421	29/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
3859	71	13422	29/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX16CVV
3860	72	13423	29/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
3861	73	13424	29/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBH
3862	74	13425	29/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
3863	75	13426	29/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBE
3864	76	13427	29/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
3865	77	13428	29/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
3866	1	13429	30/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
3867	2	13430	30/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
3868	3	13431	30/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
3869	4	13432	30/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
3870	5	13433	30/04/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
3871	6	13434	30/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXO
3872	7	13435	30/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
3873	8	13436	30/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	DE70OEC
3874	9	13437	30/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX16CVV
3875	10	13438	30/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
3876	11	13439	30/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBM
3877	12	PROVEC50422	30/04/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
3878	13	PROVEC50423	30/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
3879	14	13440	30/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXL
3880	15	13441	30/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
3881	16	13442	30/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
3882	17	13443	30/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3883	18	13444	30/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3884	19	13445	30/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
3885	20	13446	30/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
3886	21	13447	30/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
3887	22	13448	30/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	DE70OEC
3888	23	13449	30/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
3889	24	13450	30/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX16CVV
3890	25	13451	30/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
3891	26	13452	30/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
3892	27	13453	30/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
3893	28	13454	30/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3894	29	13455	30/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
3895	30	13456	30/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3896	31	13457	30/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
3897	32	13458	30/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBD
3898	33	13459	30/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
3899	34	13460	30/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
3900	35	13461	30/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX16CVV
3901	36	13462	30/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
3902	37	13463	30/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
3903	38	13464	30/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	DE70OEC
3904	39	13465	30/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
3905	40	PROVEC50424	30/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
3906	41	PROVEC50425	30/04/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
3907	42	13466	30/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3908	43	13467	30/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3909	44	13468	30/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
3910	45	13469	30/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBM
3911	46	13470	30/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
3912	47	13471	30/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
3913	48	13472	30/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
3914	49	13473	30/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
3915	50	13474	30/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBM
3916	51	13475	30/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
3917	52	13476	30/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX16CVV
3918	53	13477	30/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
3919	54	13478	30/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
3920	55	13479	30/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	DE70OEC
3921	56	13480	30/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
3922	57	13481	30/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBF
3923	58	13482	30/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3924	59	13483	30/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVA
3925	60	13484	30/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBC
3926	61	13485	30/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
3927	62	13486	30/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
3928	63	13487	30/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX16CVV
3929	64	PROVEC50426	30/04/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT

3930	65	13488	30/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
3931	66	13489	30/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
3932	67	PROVEC50427	30/04/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
3933	68	13490	30/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBE
3934	69	13491	30/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	DE70OEC
3935	70	13492	30/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
3936	71	13493	30/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
3937	72	13494	30/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
3938	73	13495	30/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
3939	74	30013	30/04/2021	170107	3900	Concrete/Hard Materials	9	Ashton Old Rd	CBDU90617	MV19UBC
3940	75	13496	30/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
3941	76	13497	30/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBH
3942	77	13498	30/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX16CVV
3943	79	13499	30/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3944	80	13500	30/04/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
3945	81	30014	30/04/2021	170107	3900	Concrete/Hard Materials	9	Ashton Old Rd	CBDU90617	MV19UBE
3946	82	30015	30/04/2021	170107	3900	Concrete/Hard Materials	9	Ashton Old Rd	CBDU90617	MV19UBC
3947	83	13501	30/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBM
3948	84	13502	30/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBF
3949	85	13503	30/04/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	DE70OEC
3950	86	13504	30/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
3951	87	13505	30/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV19UBC
3952	88	13506	30/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXM
3953	89	30016	30/04/2021	170107	3900	Concrete/Hard Materials	9	Ashton Old Rd	CBDU90617	MV19UBH
3954	90	13507	30/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVA
3955	91	13508	30/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
3956	92	13509	30/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX21ORT
3957	93	30017	30/04/2021	170107	3900	Concrete/Hard Materials	9	Ashton Old Rd	CBDU90617	MV20RKK
3958	94	13510	30/04/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
3959	95	13511	30/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX16CVV
3960	96	13512	30/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
3961	97	13513	30/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
3962	98	13514	30/04/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
3963	1	13515	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
3964	2	13516	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
3965	3	13517	04/05/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
3966	4	13518	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
3967	5	13519	04/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXO
3968	6	13520	04/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVW
3969	7	13521	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
3970	8	13523	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
3971	9	13524	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXZ
3972	10	13525	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
3973	11	13526	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
3974	12	PROVEC50428	04/05/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
3975	13	PROVEC50429	04/05/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
3976	14	13527	04/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
3977	15	13528	04/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3978	16	13529	04/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3979	17	13530	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
3980	18	13531	04/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
3981	19	13532	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
3982	20	13533	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
3983	21	13534	04/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
3984	22	13535	04/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
3985	23	13536	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
3986	24	13537	04/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
3987	25	13538	04/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
3988	26	13539	04/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
3989	27	13540	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
3990	28	13541	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
3991	29	13542	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
3992	30	13543	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
3993	31	13544	04/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
3994	32	13545	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
3995	33	13546	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
3996	34	13547	04/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
3997	35	PROVEC50430	04/05/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
3998	36	PROVEC50431	04/05/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
3999	37	13548	04/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
4000	38	13549	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20ERLY
4001	39	13550	04/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
4002	40	13551	04/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
4003	41	13552	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4004	42	13553	04/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
4005	43	13554	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4006	44	13555	04/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
4007	45	13556	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
4008	46	13557	04/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
4009	47	13558	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4010	48	13559	04/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
4011	49	13560	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
4012	50	13561	04/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
4013	51	13562	04/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
4014	52	13563	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4015	53	13564	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
4016	54	13565	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	RV69ZVA
4017	55	PROVEC50432	04/05/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
4018	56	13566	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
4019	57	13567	04/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
4020	58	13568	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4021	59	13569	04/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
4022	60	13570	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4023	61	PROVEC50433	04/05/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
4024	62	13571	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4025	63	13572	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
4026	64	13573	04/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
4027	65	13574	04/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
4028	66	13575	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4029	67	13576	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
4030	68	13577	04/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
4031	69	13578	04/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXU
4032	70	13579	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
4033	71	13580	04/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4034	72	13581	04/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
4035	73	13582	04/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXO
4036	74	13583	04/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
4037	75	13584	04/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXM
4038	76	13585	04/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
4039	77	13586	04/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
4040	78	13587	04/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
4041	79	13588	04/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
4042	80	13589	04/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
4043	81	13590	04/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVX
4044	82	13591	04/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
4045	83	13592	04/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
4046	84	13593	04/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVA
4047	85	13594	04/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
4048	86	13595	04/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
4049	87	13596	04/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVO
4050	1	13597	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4051	2	13598	05/05/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXW
4052	3	13599	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXZ
4053	4	13600	05/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
4054	5	13601	05/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVO
4055	6	13602	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
4056	7	13603	05/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXV

4057	8	13604	05/05/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
4058	9	13605	05/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
4059	10	PROVEC50420	05/05/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
4060	11	13606	05/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
4061	12	13607	05/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
4062	13	13608	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
4063	14	13609	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
4064	15	13610	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4065	16	PROVEC50421	05/05/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	DK19WDD
4066	17	13611	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4067	18	13612	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
4068	19	13613	05/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
4069	20	13614	05/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVZ
4070	21	13615	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4071	22	13616	05/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
4072	23	13617	05/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
4073	24	13618	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4074	25	13619	05/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
4075	26	13620	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
4076	27	13621	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4077	28	13622	05/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BCHF
4078	29	13623	05/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVV
4079	30	13624	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
4080	31	13625	05/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
4081	32	13626	05/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
4082	33	13627	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4083	34	13628	05/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
4084	35	13629	05/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
4085	36	13630	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4086	37	13631	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
4087	38	13632	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4088	39	PROVEC50434	05/05/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
4089	40	PROVEC50435	05/05/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	DK19WDD
4090	41	13633	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
4091	42	13634	05/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
4092	43	13635	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
4093	44	13636	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4094	45	PROVEC70032	05/05/2021	170503	3900	Asbestos+TPH	9	ERQ	CBDU90617	DE70OEC
4095	46	13637	05/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
4096	47	13638	05/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
4097	48	13639	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4098	49	13640	05/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
4099	50	13641	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4100	51	13642	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4101	52	13643	05/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
4102	53	13644	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
4103	54	13645	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
4104	55	13646	05/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
4105	56	13647	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
4106	57	13648	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4107	58	13649	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4108	59	13650	05/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
4109	60	13651	05/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
4110	61	13652	05/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
4111	62	13653	05/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
4112	63	13654	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
4113	64	13655	05/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
4114	65	13656	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
4115	66	PROVEC50436	05/05/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
4116	67	13657	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
4117	68	13658	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4118	69	PROVEC50437	05/05/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	DK19WDD
4119	70	13659	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
4120	71	13660	05/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
4121	72	13661	05/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
4122	73	13662	05/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
4123	74	13663	05/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
4124	75	13664	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4125	76	13665	05/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
4126	77	13666	05/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
4127	78	13667	05/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21ECHF
4128	79	13668	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4129	80	13669	05/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
4130	81	13670	05/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
4131	82	13671	05/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
4132	83	13672	05/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
4133	84	13673	05/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
4134	85	13674	05/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVX
4135	86	13675	05/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
4136	87	13676	05/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
4137	88	13677	05/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
4138	89	13678	05/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXL
4139	90	13679	05/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
4140	1	PROVEC50438	06/05/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
4141	2	13680	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
4142	3	13681	06/05/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXW
4143	4	13682	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
4144	5	13683	06/05/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
4145	6	13684	06/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
4146	7	13685	06/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
4147	8	13686	06/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
4148	9	13687	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
4149	10	13688	06/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVO
4150	11	PROVEC50439	06/05/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
4151	12	13689	06/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
4152	13	13690	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
4153	14	13691	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXZ
4154	15	13692	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
4155	16	13693	06/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
4156	17	13694	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
4157	18	13695	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4158	19	13696	06/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
4159	20	13697	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4160	21	13698	06/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVX
4161	22	13699	06/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
4162	23	13700	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	DE70OEC
4163	24	13701	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4164	25	13702	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4165	26	13703	06/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVZ
4166	27	13704	06/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
4167	28	13705	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
4168	29	13706	06/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
4169	30	13707	06/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
4170	31	13708	06/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
4171	32	13709	06/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
4172	33	13710	06/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
4173	34	13711	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
4174	35	13712	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
4175	36	13713	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
4176	37	13714	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
4177	38	13715	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4178	39	13716	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	DE70OEC
4179	40	13717	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4180	41	13718	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4181	42	13719	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
4182	43	13720	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4183	44	13721	06/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC

4184	45	13722	06/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
4185	46	13723	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV18FVC
4186	47	13724	06/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
4187	48	13725	06/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
4188	49	13726	06/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX21ORT
4189	50	13727	06/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
4190	51	13728	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
4191	52	13729	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
4192	53	13730	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
4193	54	13731	06/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
4194	55	13732	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4195	56	13733	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4196	57	13734	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	DE70OEC
4197	58	13735	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
4198	59	13736	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4199	60	13737	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4200	61	13738	06/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
4201	62	PROVEC50440	06/05/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
4202	63	PROVEC50441	06/05/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
4203	64	13739	06/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
4204	65	13740	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
4205	66	13741	06/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
4206	67	13742	06/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
4207	68	13743	06/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
4208	69	13744	06/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
4209	70	13745	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
4210	71	13746	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
4211	72	13747	06/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX21ORT
4212	73	13748	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
4213	74	13749	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
4214	75	13750	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4215	76	13751	06/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
4216	77	13752	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
4217	78	13753	06/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVV
4218	79	13754	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4219	80	13755	06/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
4220	81	13756	06/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	DE70OEC
4221	82	13757	06/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
4222	83	13758	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
4223	84	13759	06/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
4224	85	13760	06/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
4225	86	13761	06/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21CHF
4226	87	13762	06/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXV
4227	88	13763	06/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
4228	89	13764	06/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
4229	90	13765	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
4230	91	13766	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4231	92	13767	06/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXL
4232	93	13768	06/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
4233	94	PROVEC50442	06/05/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
4234	95	13769	06/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX21ORT
4235	96	13770	06/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
4236	97	13771	06/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
4237	98	13772	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4238	99	13773	06/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXM
4239	100	13774	06/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	DE70OEC
4240	101	13775	06/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
4241	102	PROVEC50443	06/05/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
4242	103	13776	06/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
4243	104	13777	06/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
4244	105	13778	06/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21CHF
4245	106	13779	06/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXV
4246	107	13780	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
4247	108	13781	06/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
4248	109	13782	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4249	110	13783	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
4250	111	13784	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4251	112	13785	06/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
4252	113	13786	06/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
4253	114	13787	06/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
4254	115	13788	06/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	DE70OEC
4255	116	13789	06/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
4256	117	13790	06/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXO
4257	118	13791	06/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVV
4258	119	13792	06/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
4259	120	13793	06/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
4260	121	13794	06/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21CHF
4261	122	13795	06/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXV
4262	123	13796	06/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
4263	124	13797	06/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
4264	125	13798	06/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
4265	126	13799	06/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
4266	127	13800	06/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
4267	128	13801	06/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
4268	129	13802	06/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXL
4269	130	13803	06/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
4270	131	13804	06/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	DE70OEC
4271	1	13805	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
4272	2	13806	07/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVX
4273	3	13807	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
4274	4	13808	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4275	5	13809	07/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
4276	6	PROVEC50444	07/05/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
4277	7	PROVEC50445	07/05/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD
4278	8	13810	07/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXL
4279	9	13811	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4280	10	13812	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4281	11	13813	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4282	12	13814	07/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
4283	13	13815	07/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
4284	14	13816	07/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	DE70OEC
4285	15	13817	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
4286	16	13818	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4287	17	13819	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
4288	18	13820	07/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
4289	19	13821	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4290	20	13822	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4291	21	PROVEC50446	07/05/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
4292	22	13823	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4293	23	13824	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
4294	24	13825	07/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
4295	25	13826	07/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
4296	26	13827	07/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
4297	27	13828	07/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
4298	28	13829	07/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
4299	29	13830	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	DE70OEC
4300	30	13831	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4301	31	13832	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
4302	32	13833	07/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
4303	33	13834	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4304	34	13835	07/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
4305	35	13836	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4306	36	13837	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4307	37	13838	07/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
4308	38	13839	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
4309	39	PROVEC50447	07/05/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
4310	40	PROVEC50448	07/05/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	JP03MUD

4311	41	13840	07/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
4312	42	13841	07/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
4313	43	13842	07/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
4314	44	13843	07/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	**CBDU90617**	MV19UBA
4315	45	13844	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	DE70OEC
4316	46	13846	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4317	47	13845	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
4318	48	PROVEC50449	07/05/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
4319	49	13847	07/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX21ORT
4320	50	13848	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4321	51	13849	07/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
4322	52	13850	07/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
4323	53	13851	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4324	54	13852	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
4325	55	13853	07/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
4326	56	13854	07/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
4327	57	13855	07/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
4328	58	13856	07/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
4329	59	13857	07/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
4330	60	13858	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4331	61	13859	07/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
4332	62	13860	07/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
4333	63	13861	07/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
4334	64	13862	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4335	65	13863	07/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
4336	66	13864	07/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX21ORT
4337	67	13865	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
4338	68	13866	07/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
4339	69	13867	07/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
4340	70	13868	07/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
4341	71	13869	07/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
4342	72	PROVEC50450	07/05/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
4343	73	13870	07/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
4344	74	13771	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	DE70OEC
4345	75	PROVEC50451	07/05/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
4346	76	13872	07/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
4347	77	13873	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
4348	78	13874	07/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
4349	79	13875	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4350	80	13876	07/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
4351	81	13877	07/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4352	82	13878	07/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX21ORT
4353	83	13879	07/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXL
4354	84	13880	07/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
4355	85	13881	07/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
4356	86	13882	07/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
4357	87	13883	07/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
4358	88	13884	07/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	DE70OEC
4359	89	13885	07/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
4360	90	13886	07/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
4361	91	13887	07/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
4362	92	13888	07/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
4363	93	13889	07/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
4364	94	13890	07/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVV
4365	95	13891	07/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXL
4366	96	13892	07/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
4367	1	PROVEC50452	10/05/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
4368	2	PROVEC50453	10/05/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
4369	3	13893	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
4370	4	13894	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
4371	5	13895	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
4372	6	13896	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
4373	7	13897	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
4374	8	13898	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
4375	9	13899	10/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
4376	10	13900	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
4377	11	13901	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
4378	12	13902	10/05/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
4379	13	13903	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	DE70OEC
4380	14	13904	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
4381	15	13905	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
4382	16	13906	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4383	17	13907	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
4384	18	13908	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
4385	19	13909	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
4386	20	13910	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4387	21	13911	10/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
4388	22	13912	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4389	23	13913	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
4390	24	13914	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
4391	25	13915	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
4392	26	13916	10/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
4393	27	13917	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
4394	28	13918	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
4395	29	13919	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
4396	30	13920	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
4397	31	13921	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	DE70OEC
4398	32	13922	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
4399	33	13923	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
4400	34	13924	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
4401	35	13925	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4402	36	13926	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
4403	37	13927	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4404	38	13928	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4405	39	13929	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FCV
4406	40	13930	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
4407	41	13931	10/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
4408	42	13932	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
4409	43	13933	10/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
4410	44	PROVEC50454	10/05/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
4411	45	PROVEC50455	10/05/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
4412	46	13934	10/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
4413	47	13935	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
4414	48	13936	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
4415	49	13937	10/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	DE70OEC
4416	50	13938	10/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
4417	51	13939	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
4418	52	13940	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
4419	53	13941	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4420	54	13942	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4421	55	13943	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4422	56	13944	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
4423	57	13945	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
4424	58	13946	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4425	59	13947	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
4426	60	13948	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
4427	61	13949	10/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
4428	62	13950	10/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
4429	63	13951	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
4430	64	13952	10/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
4431	65	13953	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
4432	66	13954	10/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	DE70OEC
4433	67	13955	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4434	68	13956	10/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
4435	69	13957	10/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
4436	70	13958	10/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
4437	71	13959	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ

4438	72	13960	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
4439	73	13961	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
4440	74	13962	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4441	75	13963	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
4442	76	13964	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
4443	77	PROVEC50456	10/05/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
4444	78	PROVEC50457	10/05/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU102036	MK21EVW
4445	79	13965	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4446	80	13966	10/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
4447	81	13967	10/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
4448	82	13968	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
4449	83	13969	10/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
4450	84	13970	10/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
4451	85	13971	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
4452	86	13972	10/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
4453	87	13973	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
4454	88	13974	10/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
4455	89	13975	10/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
4456	90	13976	10/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
4457	91	13977	10/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
4458	92	13978	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	DE70OEC
4459	93	13979	10/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVZ
4460	94	13980	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
4461	95	13981	10/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21CHF
4462	96	13982	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
4463	97	13983	10/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
4464	98	13984	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
4465	99	13985	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
4466	100	13986	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4467	101	13987	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
4468	102	13988	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
4469	103	13989	10/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
4470	104	13990	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
4471	105	13991	10/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV29RKF
4472	106	13992	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4473	107	13993	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
4474	108	13994	10/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
4475	109	13995	10/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	DE70OEC
4476	110	13996	10/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVV
4477	111	13997	10/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
4478	112	13998	10/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
4479	113	13999	10/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
4480	114	14000	10/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
4481	115	14001	10/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
4482	116	14002	10/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
4483	117	14003	10/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
4484	118	14004	10/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVX
4485	119	14005	10/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
4486	120	14006	10/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
4487	121	14007	10/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
4488	122	14008	10/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	DE70OEC
4489	123	14009	10/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
4490	124	14010	10/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
4491	125	14011	10/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
4492	126	14012	10/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVV
4493	127	14013	10/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
4494	1	14014	11/05/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXW
4495	2	14015	11/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXU
4496	3	14016	11/05/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
4497	4	14017	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
4498	5	14018	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
4499	6	14019	11/05/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21CHF
4500	7	14020	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
4501	8	14021	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4502	9	14022	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
4503	10	14023	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4504	11	14024	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
4505	12	14025	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
4506	13	14026	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4507	14	14027	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4508	15	PROVEC50458	11/05/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
4509	16	14028	11/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
4510	17	14029	11/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
4511	18	14030	11/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
4512	19	14031	11/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
4513	20	14032	11/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
4514	21	14033	11/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
4515	22	14034	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
4516	23	14035	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
4517	24	14036	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
4518	25	14037	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4519	26	14038	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
4520	27	14039	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4521	28	14040	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
4522	29	14041	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
4523	30	14042	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4524	31	14043	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4525	32	14044	11/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
4526	33	14045	11/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX21ORT
4527	34	14046	11/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
4528	35	14047	11/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
4529	36	14048	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV18FVE
4530	37	14049	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV18FVD
4531	38	14050	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
4532	39	14051	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4533	40	14052	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
4534	41	14053	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
4535	42	14054	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
4536	43	14055	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4537	44	14056	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4538	45	14057	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
4539	46	14058	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4540	47	14059	11/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
4541	48	14060	11/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
4542	49	14061	11/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
4543	50	PROVEC50459	11/05/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
4544	51	14062	11/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
4545	52	14063	11/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
4546	53	14064	11/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
4547	54	14065	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
4548	55	14066	11/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
4549	56	14067	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
4550	57	14068	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
4551	58	14069	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4552	59	14070	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4553	60	14071	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
4554	61	14072	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4555	62	14073	11/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
4556	63	14074	11/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
4557	64	14075	11/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
4558	65	14076	11/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
4559	66	14077	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
4560	67	14078	11/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
4561	68	14079	11/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
4562	69	14080	11/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVW
4563	70	14081	11/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
4564	71	14082	11/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21CHG

4565	72	14083	11/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVV
4566	73	14084	11/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
4567	74	14085	11/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
4568	75	14086	11/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
4569	76	14087	11/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
4570	77	14088	11/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
4571	78	14089	11/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
4572	79	14090	11/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
4573	80	14091	11/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
4574	81	14092	11/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
4575	82	14093	11/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
4576	83	14094	11/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
4577	84	14095	11/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVW
4578	85	14096	11/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
4579	86	14097	11/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
4580	87	14098	11/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21CHG
4581	88	14099	11/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVV
4582	89	14100	11/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
4583	90	14101	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
4584	91	14102	11/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
4585	92	14103	11/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
4586	93	14104	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
4587	94	14105	11/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
4588	95	14106	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4589	96	14107	11/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
4590	97	14108	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4591	98	14109	11/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
4592	99	14110	11/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
4593	100	14111	11/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVW
4594	101	14112	11/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
4595	102	14113	11/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
4596	103	14114	11/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXL
4597	104	14115	11/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXM
4598	105	14116	11/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
4599	106	14117	11/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
4600	107	14118	11/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21CHG
4601	108	14119	11/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVV
4602	109	14120	11/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
4603	110	14121	11/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX21ORT
4604	111	14122	11/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
4605	112	14123	11/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
4606	113	14124	11/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
4607	114	14125	11/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
4608	115	14126	11/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXO
4609	116	14127	11/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
4610	117	14128	11/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
4611	1	14129	12/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
4612	2	14130	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
4613	3	14131	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
4614	4	14132	12/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
4615	5	14133	12/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
4616	6	14134	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
4617	7	14135	12/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
4618	8	14136	12/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
4619	9	14137	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
4620	10	14138	12/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVX
4621	11	14139	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
4622	12	14140	12/05/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21CHF
4623	13	14141	12/05/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
4624	14	14142	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
4625	15	14143	12/05/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXW
4626	16	14144	12/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXL
4627	17	14145	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
4628	18	14146	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
4629	19	14147	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
4630	20	14148	12/05/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXU
4631	21	14149	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
4632	22	14150	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4633	23	14151	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4634	24	14152	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
4635	25	14153	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4636	26	14154	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4637	27	14155	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
4638	28	14156	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
4639	29	14157	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
4640	30	14158	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
4641	31	14159	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
4642	32	14160	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
4643	33	14161	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
4644	34	14162	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
4645	35	14163	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
4646	36	14164	12/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
4647	37	14165	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
4648	38	14166	12/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
4649	39	14167	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4650	40	14168	12/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
4651	41	14169	12/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
4652	42	14170	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4653	43	14171	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4654	44	14172	12/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
4655	45	14173	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4656	46	14174	12/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
4657	47	14175	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
4658	48	14176	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
4659	49	14177	12/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
4660	50	14178	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
4661	51	14179	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
4662	52	14180	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
4663	53	14181	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
4664	54	14182	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
4665	55	14183	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
4666	56	14184	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
4667	57	14185	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4668	58	14186	12/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
4669	59	14187	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4670	60	14188	12/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
4671	61	14189	12/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
4672	62	14190	12/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
4673	63	14191	12/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
4674	64	14192	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4675	65	14193	12/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
4676	66	14194	12/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
4677	67	14195	12/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
4678	68	14196	12/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
4679	69	14197	12/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
4680	70	14198	12/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
4681	71	14199	12/05/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVX
4682	72	14200	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
4683	73	14201	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
4684	74	14202	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
4685	75	14203	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
4686	76	14204	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4687	77	14205	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
4688	78	14206	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
4689	79	14207	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4690	80	14208	12/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
4691	81	14209	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF

4692	82	14210	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
4693	83	14211	12/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
4694	84	14212	12/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
4695	85	14213	12/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
4696	86	14214	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
4697	87	14215	12/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
4698	88	14216	12/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
4699	89	14217	12/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
4700	90	14218	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
4701	91	14219	12/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
4702	92	14220	12/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
4703	93	14221	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4704	94	14222	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
4705	95	14223	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
4706	96	14224	12/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
4707	97	14225	12/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
4708	98	14226	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
4709	99	14227	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4710	100	14228	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
4711	101	14229	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4712	102	14230	12/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX21ORT
4713	103	14231	12/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
4714	104	14232	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
4715	105	14233	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
4716	106	14234	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
4717	107	14235	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
4718	108	14236	12/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
4719	109	14237	12/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
4720	110	14238	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
4721	111	14239	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4722	112	14240	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
4723	113	14241	12/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4724	114	14242	12/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
4725	115	14243	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
4726	116	14244	12/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21CHG
4727	117	14245	12/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXM
4728	118	14246	12/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
4729	119	14247	12/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVW
4730	120	14248	12/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21CHF
4731	121	14249	12/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVV
4732	122	14250	12/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
4733	123	14251	12/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
4734	124	14252	12/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXL
4735	125	14253	12/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
4736	126	14254	12/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
4737	127	14255	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
4738	128	14256	12/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
4739	129	14257	12/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
4740	130	14258	12/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVX
4741	131	14259	12/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
4742	132	14260	12/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
4743	133	14261	12/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
4744	134	14262	12/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
4745	135	14263	12/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
4746	1	14264	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
4747	2	14265	13/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
4748	3	14266	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
4749	4	14267	13/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21CHF
4750	5	14268	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
4751	6	14269	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
4752	7	14270	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
4753	8	14271	13/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXL
4754	9	14272	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
4755	10	14273	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4756	11	14274	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4757	12	14275	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4758	13	14276	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4759	14	14277	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
4760	15	14278	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
4761	16	14279	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
4762	17	14280	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
4763	18	14281	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
4764	19	14282	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
4765	20	14283	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
4766	21	14284	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
4767	22	14285	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
4768	23	14286	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
4769	24	14287	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
4770	25	14288	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
4771	26	14289	13/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	DE70OEC
4772	27	14290	13/05/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXU
4773	28	14291	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4774	29	14292	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
4775	30	14293	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4776	31	14294	13/05/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
4777	32	14295	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4778	33	14296	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4779	34	14297	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
4780	35	14298	13/05/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXO
4781	36	14299	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
4782	37	14300	13/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
4783	38	14301	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
4784	39	14302	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
4785	40	14303	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
4786	41	14304	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
4787	42	14305	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
4788	43	14306	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
4789	44	14307	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
4790	45	14308	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
4791	46	14309	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
4792	47	14310	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
4793	48	14311	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
4794	49	14312	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
4795	50	14313	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4796	51	14314	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4797	52	14315	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4798	53	14316	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4799	54	14317	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
4800	55	14318	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
4801	56	14319	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
4802	57	14320	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
4803	58	14321	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
4804	59	14322	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
4805	60	14323	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
4806	61	14324	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
4807	62	14325	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
4808	63	14326	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
4809	64	14327	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
4810	65	14328	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
4811	66	14329	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
4812	67	14330	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4813	68	14331	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
4814	69	14332	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
4815	70	14333	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4816	71	14334	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
4817	72	14335	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
4818	73	14336	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA

4819	74	14337	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4820	75	14338	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
4821	76	14339	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
4822	77	14340	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
4823	78	14341	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
4824	79	14342	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
4825	80	14343	13/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVX
4826	81	14344	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
4827	82	14345	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
4828	83	14346	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
4829	84	14347	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
4830	85	14348	13/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVW
4831	86	14349	13/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
4832	87	14350	13/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVV
4833	88	14351	13/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
4834	89	14352	13/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21CHG
4835	90	14353	13/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
4836	91	14354	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
4837	92	14355	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
4838	93	14356	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
4839	94	14357	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
4840	95	14358	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
4841	96	14359	13/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
4842	97	14360	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
4843	98	14361	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
4844	99	14362	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
4845	100	14363	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
4846	101	14364	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
4847	102	14365	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
4848	103	14366	13/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVW
4849	104	14367	13/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
4850	105	14368	13/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVV
4851	106	14369	13/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
4852	107	14370	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
4853	108	14371	13/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
4854	109	14372	13/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21CHG
4855	110	14373	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
4856	111	14374	13/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
4857	112	14375	13/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
4858	113	14376	13/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	DK19WDD
4859	114	14377	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
4860	115	14378	13/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	DK19WDC
4861	116	14379	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
4862	117	14380	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
4863	118	14381	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
4864	119	14382	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
4865	120	14383	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
4866	121	14384	13/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
4867	122	14385	13/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
4868	123	14386	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
4869	124	14387	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
4870	125	14388	13/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVW
4871	126	14389	13/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
4872	127	14390	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
4873	128	14391	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69XVB
4874	129	14392	13/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVV
4875	130	14393	13/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXO
4876	131	14394	13/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
4877	132	14395	13/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVX
4878	133	14396	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
4879	134	14397	13/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
4880	135	14398	13/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
4881	136	14399	13/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
4882	137	14400	13/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV18FVD
4883	138	14401	13/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	DK19WDA
4884	139	14402	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
4885	140	14403	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
4886	141	14404	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
4887	142	14405	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
4888	143	14406	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
4889	144	14407	13/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
4890	1	14408	14/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
4891	2	14409	14/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
4892	3	14410	14/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
4893	4	14411	14/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
4894	5	14412	14/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXL
4895	6	14413	14/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21CHF
4896	7	14414	14/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
4897	8	14415	14/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVX
4898	9	14416	14/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
4899	10	14417	14/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVW
4900	11	14418	14/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
4901	12	14419	14/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVV
4902	13	14420	14/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
4903	14	14421	14/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXZ
4904	15	14422	14/05/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
4905	16	14423	14/05/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXO
4906	17	14424	14/05/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
4907	18	14425	14/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
4908	19	14426	14/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
4909	20	14427	14/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
4910	21	14428	14/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
4911	22	14429	14/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
4912	23	14430	14/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
4913	24	14431	14/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
4914	25	14432	14/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
4915	26	14433	14/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
4916	27	14434	14/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
4917	28	14435	14/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
4918	29	14436	14/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
4919	30	14437	14/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
4920	31	14438	14/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
4921	32	14439	14/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
4922	33	14440	14/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
4923	34	14441	14/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
4924	35	14442	14/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
4925	36	14443	14/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
4926	37	14444	14/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
4927	38	14445	14/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
4928	39	14446	14/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
4929	40	14447	14/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
4930	41	14448	14/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
4931	42	14449	14/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
4932	43	14450	14/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
4933	44	14451	14/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVF
4934	45	14452	14/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
4935	46	14453	14/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
4936	47	14454	14/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
4937	48	14455	14/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
4938	49	14456	14/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
4939	50	14457	14/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
4940	51	14458	14/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
4941	52	14459	14/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
4942	53	14460	14/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
4943	54	14461	14/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV18FVD
4944	55	14462	14/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
4945	56	14463	14/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH

4946	57	14464	14/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
4947	58	14465	14/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV18FVC
4948	59	14466	14/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
4949	60	14467	14/05/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXU
4950	61	14468	14/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
4951	62	14469	14/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
4952	63	14470	14/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
4953	64	14471	14/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
4954	65	14472	14/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
4955	66	14473	14/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
4956	67	14474	14/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
4957	68	14475	14/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
4958	69	14476	14/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
4959	70	14477	14/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
4960	71	14478	14/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
4961	72	14479	14/05/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
4962	73	14480	14/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
4963	74	14481	14/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXM
4964	75	14482	14/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXO
4965	76	14483	14/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX21ORT
4966	77	14484	14/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
4967	78	14485	14/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVX
4968	79	14486	14/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVZ
4969	80	14487	14/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
4970	81	14488	14/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
4971	82	14489	14/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXU
4972	83	14490	14/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
4973	1	14491	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
4974	2	14492	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
4975	3	14493	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
4976	4	14494	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXL
4977	5	14495	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVU
4978	6	14496	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21CHF
4979	7	14497	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
4980	8	14498	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
4981	9	14499	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
4982	10	14500	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
4983	11	14501	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
4984	12	14502	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVV
4985	13	14503	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
4986	14	14504	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
4987	15	14505	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
4988	16	14506	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
4989	17	14507	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
4990	18	14508	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
4991	19	14509	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
4992	20	14510	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
4993	21	14511	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
4994	22	14512	17/05/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
4995	23	14513	17/05/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXU
4996	24	14514	17/05/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
4997	25	14515	17/05/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXO
4998	26	14516	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
4999	27	14517	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
5000	28	14518	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
5001	29	14519	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
5002	30	14520	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
5003	31	14521	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
5004	32	14522	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
5005	33	14523	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
5006	34	14524	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
5007	35	14525	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
5008	36	14526	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5009	37	14527	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5010	38	14528	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5011	39	14529	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
5012	40	14530	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
5013	41	14531	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5014	42	14532	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
5015	43	14533	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
5016	44	14534	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5017	45	14535	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5018	46	14536	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
5019	47	14537	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
5020	48	14538	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5021	49	14539	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
5022	50	14540	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
5023	51	14541	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5024	52	14542	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
5025	53	14543	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
5026	54	14544	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
5027	55	14545	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
5028	56	14546	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
5029	57	14547	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5030	58	14548	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
5031	59	14549	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5032	60	14550	17/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
5033	61	14551	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5034	62	14552	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
5035	63	14553	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5036	64	14554	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
5037	65	14555	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5038	66	14556	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5039	67	14557	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
5040	68	14558	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
5041	69	14559	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
5042	70	14560	17/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
5043	71	14561	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
5044	72	14562	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5045	73	14563	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
5046	74	14564	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
5047	75	14565	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
5048	76	14566	17/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
5049	77	14567	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
5050	78	14568	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
5051	79	14569	17/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
5052	80	14570	17/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
5053	81	14571	17/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
5054	82	14572	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
5055	83	14573	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5056	84	14574	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5057	85	14575	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5058	86	14576	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
5059	87	14577	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
5060	88	14578	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
5061	89	14579	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
5062	90	14580	17/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
5063	91	14581	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5064	92	14582	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
5065	93	14583	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVO
5066	94	14584	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
5067	95	14585	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BYH
5068	96	14586	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
5069	97	14587	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
5070	98	14588	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5071	99	14589	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
5072	100	14590	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD

5073	101	14591	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
5074	102	14592	17/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
5075	103	14593	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
5076	104	14594	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5077	105	14595	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
5078	106	14596	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
5079	107	14597	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
5080	108	14598	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5081	109	14599	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5082	110	14600	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
5083	111	14601	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVO
5084	112	14602	17/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
5085	113	14603	17/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
5086	114	14604	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXU
5087	115	14605	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21CHF
5088	116	14606	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXM
5089	117	14607	17/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
5090	118	14608	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
5091	119	14609	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXL
5092	120	14610	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXZ
5093	121	14611	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
5094	122	14612	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21CHG
5095	123	14613	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5096	124	14614	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVX
5097	125	14615	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5098	126	14616	17/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
5099	127	14617	17/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
5100	128	14618	17/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5101	129	14619	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
5102	130	14620	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
5103	131	14621	17/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
5104	132	14622	17/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
5105	133	14623	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVO
5106	134	14624	17/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
5107	1	14625	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5108	2	14626	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5109	3	14627	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5110	4	14628	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5111	5	14629	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
5112	6	14630	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5113	7	14631	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
5114	8	14632	19/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
5115	9	14633	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5116	10	14634	19/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
5117	11	14635	19/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
5118	12	14636	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5119	13	14637	19/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
5120	14	14638	19/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
5121	15	14639	19/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
5122	16	14640	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5123	17	30018	19/05/2021	170107	3900	Concrete/Hard Materials	9	Ashton Old Rd	CBDU90617	MT21TVV
5124	18	30019	19/05/2021	170107	3900	Concrete/Hard Materials	9	Ashton Old Rd	CBDU90617	MV20RLY
5125	19	14641	19/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
5126	20	14642	19/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
5127	21	14643	19/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
5128	22	14644	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5129	23	14645	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5130	24	14646	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5131	25	14647	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5132	26	14648	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5133	27	14649	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5134	28	14650	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
5135	29	14651	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
5136	30	14652	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5137	31	14653	19/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
5138	32	14654	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5139	33	14655	19/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
5140	34	14656	19/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
5141	35	30020	19/05/2021	170107	3900	Concrete/Hard Materials	9	Ashton Old Rd	CBDU90617	MV20RKJ
5142	36	14657	19/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
5143	37	14658	19/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
5144	38	14659	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5145	39	14660	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5146	40	14661	19/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
5147	41	14662	19/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
5148	42	14663	19/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
5149	43	14664	19/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
5150	44	14665	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5151	45	14666	19/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
5152	46	14667	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
5153	47	14668	19/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
5154	48	14669	19/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
5155	49	14670	19/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
5156	50	14671	19/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
5157	51	14672	19/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
5158	52	14673	19/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
5159	53	14674	19/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
5160	54	14675	19/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
5161	55	14676	19/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
5162	56	14677	19/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
5163	57	14678	19/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
5164	58	14679	19/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
5165	59	14680	19/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
5166	60	14681	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5167	61	14682	19/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
5168	62	14683	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
5169	63	14684	19/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
5170	64	14685	19/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
5171	65	14686	19/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
5172	66	14687	19/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
5173	67	14688	19/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
5174	68	14689	19/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
5175	69	14690	19/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
5176	70	14691	19/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
5177	71	14692	19/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
5178	72	14693	19/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
5179	73	14694	19/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
5180	74	14695	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5181	75	14696	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5182	76	14697	19/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
5183	77	14698	19/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
5184	78	14699	19/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
5185	79	14700	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
5186	80	14701	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5187	81	14702	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5188	82	14703	19/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
5189	83	14704	19/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
5190	84	14705	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5191	85	14706	19/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
5192	86	14707	19/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
5193	87	14708	19/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
5194	88	14709	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5195	89	14710	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5196	90	14711	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5197	91	14712	19/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
5198	92	14713	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
5199	93	14714	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT

5200	94	14715	19/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
5201	95	14716	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5202	96	14717	19/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
5203	97	14718	19/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
5204	98	14719	19/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
5205	99	14720	19/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
5206	100	14721	19/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
5207	101	14722	19/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
5208	102	14723	19/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
5209	103	14724	19/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
5210	104	14725	19/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
5211	105	14726	19/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
5212	106	14727	19/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
5213	107	14728	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5214	108	14729	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5215	109	14730	19/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5216	110	994715	19/05/2021	170407	3900	Mixed Metals	0	EMR	CBDU188448	DK19WCG
5217	1	14731	20/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
5218	2	14732	20/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
5219	3	14733	20/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
5220	4	14734	20/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
5221	5	14735	20/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
5222	6	14736	20/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
5223	7	14737	20/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
5224	8	14738	20/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
5225	9	14739	20/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
5226	10	14740	20/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
5227	11	14741	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5228	12	14742	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5229	13	14743	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5230	14	14744	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
5231	15	14745	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
5232	16	14746	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
5233	17	14747	20/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
5234	18	14748	20/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
5235	19	14749	20/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
5236	20	14750	20/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
5237	21	14751	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5238	22	14752	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5239	23	14753	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5240	24	14754	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5241	25	14755	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
5242	26	14756	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5243	27	14757	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5244	28	14758	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
5245	29	14759	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
5246	30	14760	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5247	31	14761	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5248	32	14762	20/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
5249	33	14763	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5250	34	14764	20/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
5251	35	14765	20/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
5252	36	14766	20/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
5253	37	14767	20/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
5254	38	14768	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5255	39	14769	20/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
5256	40	14770	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5257	41	14771	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
5258	42	14772	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5259	43	14773	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5260	44	14774	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
5261	45	14775	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5262	46	14776	20/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
5263	47	14777	20/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
5264	48	14778	20/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
5265	49	14779	20/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
5266	50	14780	20/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
5267	51	14781	20/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
5268	52	14782	20/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
5269	53	14783	20/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
5270	54	14784	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5271	55	14785	20/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
5272	56	14786	20/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
5273	57	14787	20/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
5274	58	14788	20/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
5275	59	14789	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
5276	60	14790	20/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
5277	61	14791	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
5278	62	14792	20/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
5279	63	14793	20/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
5280	64	14794	20/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
5281	65	14795	20/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
5282	66	14796	20/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
5283	67	14797	20/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
5284	68	14798	20/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
5285	69	14799	20/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
5286	70	14800	20/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
5287	71	14801	20/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
5288	72	14802	20/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
5289	73	14803	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5290	74	14804	20/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
5291	75	14805	20/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
5292	76	14806	20/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
5293	77	14807	20/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
5294	78	14808	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5295	79	14809	20/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
5296	80	14810	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5297	81	14811	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5298	82	14812	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5299	83	14813	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5300	84	14814	20/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
5301	85	14815	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5302	86	14816	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
5303	87	14817	20/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21CHF
5304	88	14818	20/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
5305	89	14819	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
5306	90	14820	20/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
5307	91	14821	20/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
5308	92	14822	20/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
5309	93	14823	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5310	94	14824	20/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
5311	95	14825	20/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
5312	96	14826	20/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
5313	97	14827	20/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5314	98	14828	20/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
5315	99	14829	20/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
5316	100	14830	20/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
5317	101	14831	20/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
5318	1	14832	21/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
5319	2	14833	21/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
5320	3	14834	21/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
5321	4	14835	21/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
5322	5	14836	21/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
5323	6	14837	21/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
5324	7	14838	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5325	8	14839	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5326	9	14840	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB

5327	10	14841	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5328	11	14842	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
5329	12	14843	21/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
5330	13	14844	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
5331	14	14845	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5332	15	14846	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
5333	16	14847	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5334	17	14848	21/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
5335	18	14849	21/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
5336	19	14850	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5337	20	14851	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5338	21	14852	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5339	22	14853	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5340	23	14854	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5341	24	14855	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDD
5342	25	14856	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
5343	26	14857	21/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
5344	27	14858	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
5345	28	14859	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5346	29	14860	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5347	30	14861	21/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
5348	31	14862	21/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
5349	32	14863	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5350	33	14864	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5351	34	14865	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5352	35	14866	21/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
5353	36	14867	21/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
5354	37	14868	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
5355	38	14869	21/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
5356	39	14870	21/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDD
5357	40	14871	21/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
5358	41	14872	21/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
5359	42	14873	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5360	43	14874	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5361	44	14875	21/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
5362	45	14876	21/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
5363	46	14877	21/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
5364	47	14878	21/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
5365	48	14879	21/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
5366	49	14880	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
5367	50	14881	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5368	51	14882	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5369	52	14883	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5370	53	14884	21/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
5371	54	14885	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5372	55	14886	21/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVX
5373	56	14887	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
5374	57	14888	21/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
5375	58	14889	21/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
5376	59	14890	21/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
5377	60	14891	21/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
5378	61	14892	21/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
5379	62	14893	21/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
5380	63	14894	21/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
5381	64	14895	21/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
5382	65	14896	21/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXZ
5383	66	14897	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5384	67	14898	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5385	68	14899	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
5386	69	14900	21/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
5387	70	14901	21/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
5388	71	14902	21/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVX
5389	72	14903	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5390	73	14904	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5391	74	14905	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5392	75	14906	21/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21CHF
5393	76	14907	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5394	77	14908	21/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5395	78	14909	21/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVD
5396	79	14910	21/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
5397	80	14911	21/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXZ
5398	81	14912	21/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
5399	82	14913	21/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
5400	83	14914	21/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXU
5401	84	14915	21/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXL
5402	85	14916	21/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
5403	86	14917	21/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
5404	87	14918	21/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
5405	1	14919	24/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
5406	2	14920	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5407	3	14921	24/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
5408	4	14922	24/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
5409	5	14923	24/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
5410	6	14924	24/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
5411	7	14925	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5412	8	14926	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5413	9	14927	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
5414	10	14928	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5415	11	14929	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
5416	12	14930	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5417	13	14931	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5418	14	14932	24/05/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RLY
5419	15	14933	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5420	16	14934	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5421	17	14935	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5422	18	14936	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5423	19	14937	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
5424	20	14938	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
5425	21	14939	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5426	22	14940	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5427	23	14941	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5428	24	14942	24/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
5429	25	14943	24/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
5430	26	14944	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5431	27	14945	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5432	28	14946	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
5433	29	14947	24/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
5434	30	14948	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5435	31	14949	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5436	32	14950	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5437	33	14951	24/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
5438	34	14952	24/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
5439	35	14953	24/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
5440	36	14954	24/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
5441	37	14955	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5442	38	14956	24/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
5443	39	14957	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5444	40	14958	24/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
5445	41	14959	24/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
5446	42	14960	24/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
5447	43	14961	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
5448	44	14962	24/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
5449	45	14963	24/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
5450	46	14964	24/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
5451	47	14965	24/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
5452	48	14966	24/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
5453	49	14967	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT

5454	50	14968	24/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
5455	51	14969	24/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVE
5456	52	14970	24/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV18FVC
5457	53	14971	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
5458	54	14972	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5459	55	14973	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5460	56	14974	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5461	57	14975	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5462	58	14976	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
5463	59	14977	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5464	60	14978	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5465	61	14979	24/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5466	62	14980	24/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDC
5467	63	14981	24/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVV
5468	64	14982	24/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVW
5469	65	14983	24/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
5470	66	14984	24/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
5471	67	14985	24/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
5472	68	14986	24/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
5473	69	14987	24/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
5474	70	14988	24/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
5475	71	14989	24/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	DK19WDA
5476	1	14990	25/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5477	2	14991	25/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5478	3	14992	25/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5479	4	14993	25/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5480	5	14994	25/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
5481	6	14995	25/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5482	7	14996	25/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5483	8	14997	25/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
5484	9	14998	25/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
5485	10	14999	25/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV20RKJ
5486	11	15000	25/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
5487	12	15001	25/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21CHG
5488	13	15002	25/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXZ
5489	14	15003	25/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
5490	15	15004	25/05/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
5491	16	15005	25/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
5492	17	15006	25/05/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVO
5493	18	15007	25/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5494	19	15008	25/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5495	20	15009	25/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5496	21	15010	25/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDA
5497	22	15011	25/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	DK19WDC
5498	23	15012	25/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5499	24	15013	25/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5500	25	15014	25/05/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5501	26	15015	25/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
5502	27	15016	25/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
5503	28	15017	25/05/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
5504	1	15018	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5505	2	15020	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5506	3	15021	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5507	4	15022	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5508	5	15023	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5509	6	15024	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
5510	7	15025	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5511	8	15026	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
5512	9	15027	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5513	10	15028	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5514	11	15029	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5515	12	15030	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5516	13	15031	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5517	14	15032	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
5518	15	15033	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5519	16	15034	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
5520	17	15035	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5521	18	15036	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5522	19	15037	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5523	20	15038	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5524	21	15039	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5525	22	15040	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
5526	23	15041	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5527	24	15042	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
5528	25	15043	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5529	26	15044	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5530	27	15045	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5531	28	15046	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5532	29	15047	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5533	30	15048	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
5534	31	15049	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5535	32	15050	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5536	33	15051	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
5537	34	15052	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5538	35	15053	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5539	36	15054	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5540	37	15055	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5541	38	15056	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5542	39	15057	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5543	40	15058	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5544	41	15059	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
5545	42	15060	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5546	43	15061	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5547	44	15062	01/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5548	1	15063	02/06/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
5549	2	15064	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5550	3	15065	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5551	4	15066	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5552	5	15067	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5553	6	15068	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5554	7	15069	02/06/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKN
5555	8	15070	02/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
5556	9	15071	02/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
5557	10	15072	02/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
5558	11	15073	02/06/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
5559	12	15074	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5560	13	15075	02/06/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXV
5561	14	15076	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5562	15	15077	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5563	16	15078	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5564	17	15079	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5565	18	15080	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5566	19	15081	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5567	20	15082	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5568	21	15083	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5569	22	15084	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5570	23	15085	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5571	24	15086	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5572	25	15087	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5573	26	15088	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5574	27	15089	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5575	28	15090	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5576	29	15091	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5577	30	15092	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5578	31	15093	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5579	32	15094	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5580	33	15095	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH

5581	34	15096	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5582	35	15097	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5583	36	15098	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5584	37	15099	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5585	38	15100	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5586	39	15101	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5587	40	15102	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5588	41	15103	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5589	42	15104	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5590	43	15105	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5591	44	15106	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5592	45	15107	02/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5593	1	PROVEC50460	03/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYH
5594	2	PROVEC50461	03/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV18FVE
5595	3	PROVEC50462	03/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBB
5596	4	PROVEC50463	03/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
5597	5	PROVEC50464	03/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
5598	6	PROVEC50465	03/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYJ
5599	1	15108	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5600	2	15109	07/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
5601	3	15110	07/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
5602	4	15111	07/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
5603	5	15112	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5604	6	15113	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5605	7	15114	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5606	8	15115	07/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
5607	9	15116	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5608	10	15117	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
5609	11	15118	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5610	12	15119	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5611	13	15120	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5612	14	15121	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV61ZVA
5613	15	15122	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5614	16	15123	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
5615	17	15124	07/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
5616	18	15125	07/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
5617	19	15126	07/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
5618	20	15127	07/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
5619	21	15128	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5620	22	15129	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5621	23	15130	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5622	24	15131	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5623	25	15132	07/06/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXP
5624	26	15133	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5625	27	15134	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
5626	28	15135	07/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
5627	29	15136	07/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
5628	30	15137	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5629	31	15138	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5630	32	15139	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5631	33	15140	07/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
5632	34	15141	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5633	35	15142	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5634	36	15143	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5635	37	15144	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
5636	38	15145	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5637	39	15146	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5638	40	15147	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5639	41	15148	07/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
5640	42	15149	07/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
5641	43	15150	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5642	44	15151	07/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
5643	45	15152	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5644	46	15153	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
5645	47	15154	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5646	48	15155	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5647	49	15156	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5648	50	15157	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5649	51	15158	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5650	52	15159	07/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
5651	53	15160	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5652	54	15161	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5653	55	15162	07/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
5654	56	15163	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5655	57	15164	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5656	58	15165	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5657	59	15166	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5658	60	15167	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5659	61	15168	07/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5660	62	15169	07/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
5661	1	15170	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5662	2	15171	08/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
5663	3	15172	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5664	4	15173	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5665	5	15174	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5666	6	15175	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5667	7	15176	08/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
5668	8	15177	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5669	9	15178	08/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
5670	10	15179	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5671	11	15180	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5672	12	15181	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5673	13	15182	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5674	14	15183	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5675	15	15184	08/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
5676	16	15185	08/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
5677	17	15186	08/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
5678	18	15187	08/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
5679	19	15188	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5680	20	15189	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5681	21	15190	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5682	22	15191	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5683	23	15192	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5684	24	15193	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5685	25	15194	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5686	26	15195	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5687	27	15196	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5688	28	15197	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5689	29	15198	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5690	30	15199	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5691	31	15200	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5692	32	15201	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5693	33	15202	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5694	34	15203	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5695	35	15204	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5696	36	15205	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5697	37	15206	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5698	38	15207	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5699	39	15208	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5700	40	15209	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5701	41	15210	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5702	42	15211	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5703	43	15212	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5704	44	15213	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5705	45	15214	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5706	46	15215	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5707	47	15216	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB

5708	48	15217	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5709	49	15218	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5710	50	15219	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5711	51	15220	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5712	52	15221	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5713	53	15222	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5714	54	15223	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5715	55	15224	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5716	56	15225	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5717	57	15226	08/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5718	1	15227	09/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5719	2	15228	09/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5720	3	15229	09/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5721	4	15230	09/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
5722	5	15231	09/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV18FVD
5723	6	15232	09/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
5724	7	15233	09/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
5725	8	15234	09/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
5726	9	15235	09/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVC
5727	10	15236	09/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5728	11	15237	09/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
5729	12	15238	09/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV18FVD
5730	13	15239	09/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5731	14	15240	09/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5732	15	15241	09/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5733	16	15242	09/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5734	17	15243	09/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
5735	18	15244	09/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5736	19	15245	09/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5737	20	15246	09/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5738	21	15247	09/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5739	22	15248	09/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5740	23	15249	09/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
5741	24	15250	09/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5742	25	15251	09/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5743	26	15252	09/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5744	27	15253	09/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
5745	28	15254	09/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5746	29	15255	09/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
5747	30	15256	09/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5748	31	15257	09/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
5749	32	15258	09/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5750	33	15259	09/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5751	34	15260	09/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
5752	35	15261	09/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5753	36	15262	09/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5754	1	15263	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5755	2	15264	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5756	3	15265	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5757	4	15266	10/06/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXU
5758	5	15267	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5759	6	15268	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
5760	7	15269	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5761	8	15270	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5762	9	15271	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5763	10	15272	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5764	11	15273	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5765	12	15274	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
5766	13	15275	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5767	14	15276	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5768	15	15277	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5769	16	15278	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5770	17	15279	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5771	18	15280	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
5772	19	15281	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5773	20	15282	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5774	21	15283	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5775	22	15284	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5776	23	15285	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
5777	24	15286	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5778	25	15287	10/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
5779	26	15288	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5780	27	15289	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5781	28	15290	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5782	29	15291	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5783	30	15292	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
5784	31	15293	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5785	32	15294	10/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
5786	33	15295	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5787	34	15296	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5788	35	15297	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5789	36	15298	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5790	37	15299	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
5791	38	15300	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5792	39	15301	10/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
5793	40	15302	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5794	41	15303	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5795	42	15304	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18UBA
5796	43	15305	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5797	44	15306	10/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
5798	1	15307	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5799	2	15308	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5800	3	15309	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5801	4	15310	11/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
5802	5	15311	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5803	6	15312	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5804	7	15313	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5805	8	15314	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5806	9	PROVEC50466	11/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYH
5807	10	PROVEC50467	11/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYJ
5808	11	PROVEC50468	11/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
5809	12	15315	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5810	13	15316	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5811	14	15317	11/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
5812	15	15318	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5813	16	15319	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5814	17	15320	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5815	18	15321	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5816	19	PROVEC50469	11/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYH
5817	20	15322	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5818	21	PROVEC50470	11/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYJ
5819	22	PROVEC50471	11/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
5820	23	15323	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5821	24	15324	11/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
5822	25	15325	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5823	26	15326	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5824	27	15327	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5825	28	15328	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5826	29	15329	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5827	30	15330	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5828	31	15331	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5829	32	15332	11/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
5830	33	15333	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5831	34	15334	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5832	35	15335	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5833	36	PROVEC50472	11/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYH
5834	37	15336	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE

5835	38	PROVEC50473	11/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYJ
5836	39	PROVEC50474	11/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
5837	40	15337	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5838	41	15338	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5839	42	15339	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5840	43	15340	11/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
5841	44	15341	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5842	45	15342	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5843	46	15343	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5844	47	15344	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
5845	48	15345	11/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5846	1	PROVEC50475	14/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYH
5847	2	PROVEC50476	14/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
5848	3	PROVEC50477	14/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV18FVE
5849	4	PROVEC50478	14/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVC
5850	5	PROVEC50479	14/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
5851	6	15346	14/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
5852	7	PROVEC50480	14/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVA
5853	8	PROVEC50481	14/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
5854	9	PROVEC50482	14/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYJ
5855	10	PROVEC50483	14/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBB
5856	11	PROVEC50484	14/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV18FVD
5857	12	15347	14/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
5858	13	PROVEC50485	14/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVD
5859	14	PROVEC50486	14/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYH
5860	15	PROVEC50487	14/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
5861	16	PROVEC50488	14/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV18FVE
5862	17	PROVEC50489	14/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVC
5863	18	PROVEC50490	14/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
5864	19	PROVEC50491	14/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
5865	20	PROVEC50492	14/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYJ
5866	21	PROVEC50493	14/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBB
5867	22	PROVEC50494	14/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVA
5868	23	PROVEC50495	14/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV18FVD
5869	24	PROVEC50496	14/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVD
5870	25	PROVEC50497	14/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYH
5871	26	PROVEC50498	14/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
5872	27	PROVEC50499	14/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV18FVE
5873	28	15348	14/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5874	29	15349	14/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5875	30	15350	14/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5876	31	15351	14/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5877	32	15352	14/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5878	33	15353	14/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5879	34	15354	14/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5880	35	15355	14/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5881	36	15356	14/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
5882	37	15357	14/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5883	38	15358	14/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5884	39	15359	14/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5885	40	15360	14/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5886	41	15361	14/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5887	42	15362	14/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5888	43	15363	14/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5889	1	15364	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5890	2	15365	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5891	3	15366	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5892	4	15367	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5893	5	15368	15/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
5894	6	15369	15/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
5895	7	15370	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5896	8	15371	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5897	9	15372	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
5898	10	15373	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5899	11	15374	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5900	12	15375	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5901	13	15376	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5902	14	15377	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5903	15	15378	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5904	16	15379	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5905	17	15380	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5906	18	15381	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5907	19	15382	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
5908	20	15383	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5909	21	15384	15/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
5910	22	15385	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5911	23	15386	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19FVE
5912	24	15387	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5913	25	15388	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5914	26	15389	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5915	27	15390	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5916	28	15391	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5917	29	15392	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5918	30	15393	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
5919	31	15394	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5920	32	15395	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5921	33	15396	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5922	34	15397	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5923	35	15398	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5924	36	15399	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5925	37	15400	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5926	38	15401	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5927	39	15402	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5928	40	15403	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5929	41	15404	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
5930	42	15405	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5931	43	15406	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5932	44	15407	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5933	45	15408	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5934	46	15409	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5935	47	15410	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5936	48	15411	15/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
5937	49	15412	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5938	50	15413	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
5939	51	15414	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5940	52	15415	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5941	53	15416	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5942	54	15417	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5943	55	15418	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5944	56	15419	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5945	57	15420	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5946	58	15421	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5947	59	15422	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
5948	60	15423	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5949	61	15424	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5950	62	15425	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5951	63	15426	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5952	64	15427	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5953	65	15428	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5954	66	15429	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
5955	67	15430	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5956	68	15431	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5957	69	15432	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5958	70	15433	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
5959	71	15434	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5960	72	15435	15/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
5961	1	15436	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE

5962	2	15437	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5963	3	15438	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5964	4	15439	16/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
5965	5	15440	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5966	6	15441	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5967	7	15442	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5968	8	15443	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5969	9	15444	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5970	10	15445	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5971	11	15446	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
5972	12	15447	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5973	13	15448	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5974	14	15449	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5975	15	15450	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5976	16	15451	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5977	17	15452	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5978	18	15453	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5979	19	15454	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5980	20	15455	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5981	21	15456	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
5982	22	15457	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5983	23	15458	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5984	24	15459	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
5985	25	15460	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
5986	26	15461	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
5987	27	15462	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
5988	28	15463	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
5989	29	15464	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
5990	30	15465	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
5991	31	15466	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
5992	32	15467	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
5993	33	15468	16/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
5994	34	15469	16/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
5995	35	15470	16/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
5996	36	15471	16/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV18FVD
5997	37	15472	16/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
5998	38	15473	16/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
5999	1	15474	17/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
6000	2	PROVEC50501	17/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVA
6001	3	PROVEC50502	17/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV18FVC
6002	4	15475	17/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
6003	5	15476	17/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
6004	6	15477	17/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
6005	7	15478	17/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVC
6006	8	15479	17/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
6007	9	15480	17/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVA
6008	10	15481	17/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV18FVC
6009	11	15482	17/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
6010	12	15483	17/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
6011	13	15484	17/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
6012	14	15485	17/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVC
6013	15	15486	17/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
6014	16	15487	17/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVA
6015	17	15488	17/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVB
6016	1	15489	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6017	2	15490	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6018	3	15491	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6019	4	15492	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6020	5	15493	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6021	6	15494	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6022	7	15495	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
6023	8	15496	21/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
6024	9	15497	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6025	10	15498	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6026	11	15499	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6027	12	15500	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6028	13	15501	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6029	14	15502	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6030	15	15503	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6031	16	15504	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6032	17	15505	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
6033	18	15506	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6034	19	15507	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6035	20	15508	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6036	21	15509	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6037	22	15510	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6038	23	15511	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6039	24	15512	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6040	25	15513	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6041	26	15514	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6042	27	15515	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
6043	28	15516	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6044	29	15517	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6045	30	15518	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6046	31	15519	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6047	32	15520	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6048	33	15521	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6049	34	15522	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6050	35	15523	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6051	36	15524	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6052	37	15525	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6053	38	15526	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
6054	39	15527	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6055	40	15528	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6056	41	15529	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6057	42	15530	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6058	43	15531	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6059	44	15532	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6060	45	15533	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6061	46	15534	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6062	47	15535	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6063	48	15536	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6064	49	15537	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6065	50	15538	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
6066	51	15539	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6067	52	15540	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6068	53	15541	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6069	54	15542	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6070	55	15543	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6071	56	15544	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6072	57	15545	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6073	58	15546	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6074	59	15547	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6075	60	15548	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6076	61	15549	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
6077	62	15550	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6078	63	15551	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6079	64	15552	21/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6080	1	30022	23/06/2021	170107	3900	Concrete/Hard Materials	9	Ashton Old Rd	CBDU90617	MT21TVX
6081	2	30023	23/06/2021	170107	3900	Concrete/Hard Materials	9	Ashton Old Rd	CBDU90617	MT21TVZ
6082	3	30024	23/06/2021	170107	3900	Concrete/Hard Materials	4.5	Ashton Old Rd	CBDU90617	MT21TVX
6083	1	15553	24/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6084	2	15554	24/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6085	3	15555	24/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6086	4	15556	24/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6087	5	15557	24/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6088	6	15558	24/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL

6089	7	15559	24/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6090	8	15560	24/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6091	9	15561	24/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6092	10	15562	24/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6093	11	15563	24/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6094	12	15564	24/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6095	13	15565	24/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6096	14	15566	24/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6097	15	15567	24/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6098	16	15568	24/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6099	17	15569	24/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6100	18	15570	24/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6101	19	15571	24/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6102	1	15572	25/06/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
6103	2	15573	25/06/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
6104	3	15574	25/06/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKJ
6105	4	15575	25/06/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXU
6106	5	15576	25/06/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
6107	6	15577	25/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6108	7	15578	25/06/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
6109	8	15579	25/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
6110	9	15580	25/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
6111	10	15581	25/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6112	11	15582	25/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
6113	12	15583	25/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
6114	13	15584	25/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
6115	14	15585	25/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6116	15	15586	25/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6117	16	15587	25/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
6118	17	15588	25/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6119	18	15589	25/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
6120	19	15590	25/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
6121	20	15591	25/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
6122	21	15592	25/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
6123	22	15593	25/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
6124	23	15594	25/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6125	24	15595	25/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
6126	25	15596	25/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6127	26	15597	25/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6128	27	15598	25/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
6129	28	15599	25/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
6130	29	15600	25/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
6131	30	15601	25/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
6132	31	15602	25/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
6133	32	15603	25/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6134	33	15604	25/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6135	34	15605	25/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6136	35	15606	25/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
6137	36	15607	25/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
6138	37	15608	25/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
6139	38	15609	25/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
6140	39	15610	25/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
6141	40	15611	25/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
6142	41	15612	25/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
6143	42	15613	25/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6144	43	15614	25/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6145	44	15615	25/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
6146	45	15616	25/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVH
6147	46	15617	25/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6148	47	15618	25/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
6149	48	15619	25/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
6150	49	15620	25/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
6151	50	15621	25/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
6152	1	15622	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6153	2	15623	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6154	3	15624	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6155	4	15625	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
6156	5	15626	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6157	6	15627	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
6158	7	15628	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6159	8	15629	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6160	9	15630	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6161	10	15631	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6162	11	15632	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6163	12	15633	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
6164	13	15634	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
6165	14	15635	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
6166	15	15636	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
6167	16	15637	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
6168	17	15638	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
6169	18	15639	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6170	19	15640	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6171	20	15641	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BXU
6172	21	15642	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6173	22	15643	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6174	23	15644	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
6175	24	15645	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6176	25	15646	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6177	26	15647	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6178	27	15648	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
6179	28	15649	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
6180	29	15650	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
6181	30	15651	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
6182	31	15652	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6183	32	15653	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV20RKK
6184	33	15654	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
6185	34	15655	28/06/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
6186	35	15656	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6187	36	15657	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6188	37	15658	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
6189	38	15659	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
6190	39	15660	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6191	40	15661	28/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
6192	41	15662	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	RV60ZVC
6193	42	15663	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
6194	43	15664	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6195	44	15665	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
6196	45	15666	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6197	46	15667	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
6198	47	15668	28/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
6199	48	15669	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
6200	49	15670	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
6201	50	15671	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6202	51	15672	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
6203	52	15673	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
6204	53	15674	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6205	54	15675	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
6206	55	15676	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6207	56	15677	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
6208	57	15678	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6209	58	15679	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
6210	59	15680	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
6211	60	15681	28/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
6212	61	15682	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
6213	62	15683	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
6214	63	15684	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
6215	64	15685	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ

6216	65	15686	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6217	66	15687	28/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV18FVC
6218	67	15688	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
6219	68	15689	28/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
6220	69	15690	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
6221	70	15691	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6222	71	15692	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
6223	72	15693	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
6224	73	15694	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
6225	74	15695	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
6226	75	15696	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6227	76	15697	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6228	77	15698	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
6229	78	15699	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
6230	79	15700	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
6231	80	15701	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
6232	81	15702	28/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
6233	82	15703	28/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
6234	83	15704	28/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
6235	84	15705	28/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6236	1	15706	29/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6237	2	15707	29/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
6238	3	15708	29/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
6239	4	15709	29/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
6240	5	15710	29/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
6241	6	15711	29/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
6242	7	15712	29/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6243	8	15713	29/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6244	9	15714	29/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
6245	10	15715	29/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6246	11	15716	29/06/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6247	12	15717	29/06/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
6248	13	PROVEC50503	29/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV18FVC
6249	14	PROVEC50504	29/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
6250	15	PROVEC50505	29/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYH
6251	16	PROVEC50506	29/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVC
6252	17	PROVEC50507	29/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVD
6253	18	PROVEC50508	29/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV18FVD
6254	19	PROVEC50509	29/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVB
6255	20	PROVEC50510	29/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV18FVC
6256	21	PROVEC50511	29/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
6257	22	PROVEC50512	29/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYH
6258	23	PROVEC50513	29/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVC
6259	24	PROVEC50514	29/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVD
6260	25	PROVEC50515	29/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVB
6261	26	PROVEC50516	29/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV18FVD
6262	27	PROVEC50517	29/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
6263	28	PROVEC50518	29/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
6264	29	PROVEC50519	29/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYJ
6265	30	PROVEC50520	29/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV18FVC
6266	31	PROVEC50521	29/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
6267	32	PROVEC50522	29/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYH
6268	33	PROVEC50523	29/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVC
6269	34	PROVEC50524	29/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVD
6270	1	PROVEC50525	30/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYH
6271	2	PROVEC50526	30/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBB
6272	3	PROVEC50527	30/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVC
6273	4	PROVEC50528	30/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV18FVC
6274	5	PROVEC50529	30/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
6275	6	PROVEC50530	30/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
6276	7	PROVEC50531	30/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV18FVD
6277	8	15718	30/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
6278	9	15719	30/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVB
6279	10	PROVEC50532	30/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVD
6280	11	PROVEC50533	30/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYH
6281	12	PROVEC50534	30/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBB
6282	13	PROVEC50535	30/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVC
6283	14	PROVEC50536	30/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV18FVC
6284	15	15720	30/06/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
6285	16	PROVEC50537	30/06/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
6286	1	PROVEC50538	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBB
6287	2	PROVEC50539	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYH
6288	3	PROVEC50540	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVC
6289	4	PROVEC50541	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
6290	5	PROVEC50542	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVD
6291	6	PROVEC50543	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
6292	7	PROVEC50544	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV18FVC
6293	8	PROVEC50545	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV18FVD
6294	9	PROVEC50546	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVA
6295	10	15721	05/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVX
6296	11	15722	05/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21CHF
6297	12	15723	05/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21VXO
6298	13	15724	05/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
6299	14	PROVEC50547	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV18FVE
6300	15	15725	05/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
6301	16	15726	05/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKJ
6302	17	15727	05/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
6303	18	15728	05/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKK
6304	19	15729	05/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
6305	20	15730	05/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVO
6306	21	15731	05/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVX
6307	22	15732	05/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21CHF
6308	23	15733	05/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXO
6309	24	15734	05/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
6310	25	15735	05/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
6311	26	15736	05/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKK
6312	27	15737	05/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKJ
6313	28	15738	05/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
6314	29	15739	05/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
6315	30	15740	05/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVO
6316	31	PROVEC50548	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBB
6317	32	PROVEC50549	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
6318	33	PROVEC50550	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVC
6319	34	PROVEC50551	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
6320	35	PROVEC50552	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVD
6321	36	PROVEC50553	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
6322	37	PROVEC50554	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV18FVC
6323	38	PROVEC50555	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVA
6324	39	PROVEC50556	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV18FVD
6325	40	PROVEC50557	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV18FVE
6326	41	15741	05/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVX
6327	42	15742	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
6328	43	15743	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
6329	44	15744	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
6330	45	15745	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
6331	46	15746	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
6332	47	15747	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
6333	48	15748	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
6334	49	15749	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
6335	50	15750	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
6336	51	15751	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
6337	52	15752	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
6338	53	15753	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
6339	54	15754	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
6340	55	15755	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
6341	56	15756	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
6342	57	15757	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK

6343	58	15758	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
6344	59	PROVEC50558	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBB
6345	60	PROVEC50559	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYH
6346	61	PROVEC50560	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVC
6347	62	PROVEC50561	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV18FVC
6348	63	15759	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
6349	64	15760	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
6350	65	PROVEC50562	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
6351	66	15761	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
6352	67	15762	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
6353	68	PROVEC50563	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVD
6354	69	PROVEC50564	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVA
6355	70	PROVEC50565	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
6356	71	PROVEC50566	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV18FVE
6357	72	15763	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
6358	73	15764	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
6359	74	15765	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
6360	75	15766	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
6361	76	15767	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
6362	77	15768	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVP
6363	78	PROVEC50567	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV18FVD
6364	79	15769	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
6365	80	15770	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
6366	81	15771	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
6367	82	15772	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
6368	83	15773	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
6369	84	15774	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
6370	85	15775	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
6371	86	15776	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
6372	87	PROVEC50568	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBB
6373	88	15777	05/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
6374	89	PROVEC50569	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYH
6375	90	PROVEC50570	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVC
6376	91	PROVEC50571	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV18FVC
6377	92	PROVEC50572	05/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
6378	1	PROVEC50573	06/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV18FVD
6379	2	PROVEC50574	06/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVD
6380	3	PROVEC50575	06/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV18FVE
6381	4	15778	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
6382	5	15779	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
6383	6	15780	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
6384	7	15781	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
6385	8	15782	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
6386	9	15783	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
6387	10	15784	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
6388	11	PROVEC50576	06/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
6389	12	15785	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
6390	13	15786	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
6391	14	15787	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
6392	15	15788	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
6393	16	15789	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
6394	17	15790	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
6395	18	15791	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
6396	19	15792	06/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21CHF
6397	20	15793	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
6398	21	PROVEC50577	06/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
6399	22	15794	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6400	23	15795	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6401	24	15796	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6402	25	15797	06/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
6403	26	15798	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
6404	27	15799	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
6405	28	15800	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6406	29	15801	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
6407	30	15802	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6408	31	15803	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
6409	32	15804	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6410	33	15805	06/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
6411	34	15806	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
6412	35	15807	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
6413	36	15808	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
6414	37	15809	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
6415	38	15810	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6416	39	15811	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6417	40	15812	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6418	41	15813	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6419	42	15814	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
6420	43	15815	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
6421	44	15816	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
6422	45	15817	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6423	46	15818	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
6424	47	15819	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
6425	48	15820	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
6426	49	15821	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
6427	50	15822	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6428	51	15823	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
6429	52	15824	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
6430	53	15825	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6431	54	15826	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6432	55	15827	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
6433	56	15828	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6434	57	15829	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6435	58	15830	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6436	59	15831	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
6437	60	15832	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
6438	61	15833	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6439	62	15834	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
6440	63	15835	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
6441	64	15836	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
6442	65	15837	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6443	66	15838	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
6444	67	15839	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
6445	68	15840	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
6446	69	15841	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
6447	70	15842	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
6448	71	15843	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
6449	72	15844	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
6450	73	15845	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6451	74	15846	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
6452	75	15847	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
6453	76	15848	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6454	77	15849	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6455	78	15850	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
6456	79	15851	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6457	80	15852	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6458	81	15853	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6459	82	15854	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
6460	83	15855	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
6461	84	15856	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
6462	85	15857	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6463	86	15858	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
6464	87	15859	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
6465	88	15860	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6466	89	15861	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
6467	90	15862	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
6468	91	15863	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
6469	92	15864	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY

6470	93	15865	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
6471	94	15866	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
6472	95	15867	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
6473	96	15868	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6474	97	15869	06/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6475	98	15870	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
6476	99	15871	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
6477	100	15872	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
6478	101	15873	06/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
6479	1	15874	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
6480	2	15875	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
6481	3	15876	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
6482	4	15877	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
6483	5	15878	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
6484	6	15879	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
6485	7	15880	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
6486	8	15881	07/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6487	9	15882	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
6488	10	15883	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
6489	11	15884	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
6490	12	15885	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
6491	13	15886	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
6492	14	15887	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
6493	15	15888	07/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6494	16	15889	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
6495	17	15890	07/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
6496	18	15891	07/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6497	19	15892	07/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6498	20	15893	07/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6499	21	15894	07/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6500	22	15895	07/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6501	23	15896	07/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
6502	24	15897	07/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6503	25	15898	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
6504	26	15899	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
6505	27	15900	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
6506	28	15901	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
6507	29	15902	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
6508	30	15903	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
6509	31	15904	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
6510	32	15905	07/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6511	33	15906	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
6512	34	15907	07/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6513	35	15908	07/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
6514	36	15909	07/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6515	37	15910	07/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6516	38	15911	07/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6517	39	15912	07/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6518	40	15913	07/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6519	41	15914	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
6520	42	15915	07/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6521	43	15916	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
6522	44	15917	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
6523	45	15918	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
6524	46	15919	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
6525	47	15920	07/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVZ
6526	48	15921	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
6527	49	15922	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
6528	50	15923	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
6529	51	15924	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
6530	52	15925	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
6531	53	15926	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
6532	54	15927	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
6533	55	15928	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
6534	56	15929	07/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
6535	57	15930	07/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6536	58	15931	07/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKJ
6537	59	15932	07/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6538	60	15933	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
6539	61	15934	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
6540	62	15935	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
6541	63	15936	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
6542	64	15937	07/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6543	65	15938	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
6544	66	15939	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
6545	67	15940	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
6546	68	15941	07/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
6547	1	15942	08/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
6548	2	15943	08/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV18FVE
6549	3	15944	08/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6550	4	15945	08/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6551	5	15946	08/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6552	6	15947	08/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
6553	7	15948	08/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6554	8	15949	08/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6555	9	15950	08/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVZ
6556	10	15951	08/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
6557	11	15952	08/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6558	12	15953	08/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6559	13	15954	08/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6560	14	15955	08/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6561	15	15956	08/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6562	16	15957	08/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV18FVE
6563	17	15958	08/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
6564	18	15959	08/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
6565	19	15960	08/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6566	20	15961	08/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6567	21	15962	08/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6568	22	15963	08/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19FVC
6569	23	15964	08/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6570	24	15965	08/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
6571	25	15966	08/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6572	26	15967	08/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6573	27	15968	08/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV18FVE
6574	28	15969	08/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
6575	29	15970	08/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6576	30	15971	08/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6577	31	15972	08/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6578	32	15973	08/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
6579	33	15974	08/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6580	34	15975	08/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6581	35	15976	08/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6582	36	15977	08/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6583	1	15978	12/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6584	2	15979	12/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6585	3	15980	12/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6586	4	15981	12/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6587	5	15982	12/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6588	6	15983	12/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6589	7	15984	12/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6590	8	15985	12/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6591	9	15986	12/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6592	10	15987	12/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6593	11	15988	12/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6594	12	15989	12/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6595	13	15990	12/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6596	14	15991	12/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE

6597	15	15992	12/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6598	16	15993	12/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6599	17	15994	12/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6600	1	15995	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6601	2	15996	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6602	3	15997	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6603	4	15998	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6604	5	15999	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6605	6	16000	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6606	7	16001	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6607	8	16002	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6608	9	16003	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6609	10	16004	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6610	11	16005	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6611	12	16006	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6612	13	16007	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6613	14	16008	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6614	15	16009	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6615	16	16010	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6616	17	16011	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6617	18	16012	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6618	19	16013	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6619	20	16014	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6620	21	16015	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6621	22	16016	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6622	23	16017	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6623	24	16018	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6624	25	16019	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6625	26	16020	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6626	27	16021	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6627	28	16022	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6628	29	16023	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6629	30	16024	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6630	31	16025	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6631	32	16026	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6632	33	16027	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6633	34	16028	13/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6634	1	16029	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6635	2	16030	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6636	3	16031	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6637	4	16032	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6638	5	16033	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6639	6	16034	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6640	7	16035	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6641	8	16036	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6642	9	16037	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6643	10	16038	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6644	11	16039	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6645	12	16040	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6646	13	16041	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6647	14	16042	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6648	15	16043	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6649	16	16044	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6650	17	16045	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6651	18	16046	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6652	19	16047	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6653	20	16048	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6654	21	16049	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6655	22	16050	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6656	23	16051	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6657	24	16052	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6658	25	16053	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6659	26	16054	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6660	27	16055	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6661	28	16056	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6662	29	16057	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6663	30	16058	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6664	31	16059	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6665	32	16060	14/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6666	1	16061	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6667	2	16062	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6668	3	16063	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6669	4	16064	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6670	5	16065	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6671	6	16066	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6672	7	16067	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6673	8	16068	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6674	9	16069	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6675	10	16070	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6676	11	16071	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6677	12	16072	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6678	13	16073	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6679	14	16074	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6680	15	16075	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6681	16	30025	15/07/2021	170302	3900	Tarmac	9	Ashton Old Rd	CBDU90617	MT21TVW
6682	17	16076	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6683	18	16077	15/07/2021	170302	3900	Tarmac	9	Ashton Old Rd	CBDU90617	MT21TVW
6684	19	30027	15/07/2021	170302	3900	Tarmac	9	Ashton Old Rd	CBDU90617	MT21TVW
6685	20	16077	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6686	21	16078	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6687	22	16079	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6688	23	16080	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6689	24	16081	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6690	25	16082	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6691	26	16083	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6692	27	16084	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6693	28	30028	15/07/2021	170302	3900	Tarmac	9	Ashton Old Rd	CBDU90617	MT21TVW
6694	29	30029	15/07/2021	170302	3900	Tarmac	9	Ashton Old Rd	CBDU90617	MT21TVW
6695	30	16085	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6696	31	16086	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6697	32	16087	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6698	33	16088	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6699	34	16089	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6700	35	16090	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6701	36	16091	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6702	37	16092	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6703	38	16093	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6704	39	16094	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6705	40	16095	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6706	41	16096	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6707	42	16097	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6708	43	16098	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6709	44	16099	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6710	45	16100	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6711	46	16101	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6712	47	16102	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6713	48	16103	15/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
6714	49	16104	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6715	50	16105	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6716	51	16106	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6717	52	16107	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6718	53	16108	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6719	54	16109	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6720	55	16110	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6721	56	16111	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV20RKN
6722	57	16112	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BXW
6723	58	16113	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD

6724	59	16114	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6725	60	16115	15/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
6726	61	16116	15/07/2021	170504	3900	Non-haz soils & stones	10	Fletcher Bank	CBDU90617	MV20RKK
6727	62	16117	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6728	63	16118	15/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6729	64	16119	15/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
6730	65	16120	15/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
6731	66	16121	15/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXZ
6732	67	16122	15/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
6733	1	16123	16/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6734	2	16124	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
6735	3	16125	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
6736	4	16126	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
6737	5	16127	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
6738	6	16128	16/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6739	7	16129	16/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
6740	8	16130	16/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6741	9	16131	16/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6742	10	16132	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
6743	11	16133	16/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6744	12	16134	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
6745	13	16135	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
6746	14	16136	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
6747	15	16137	16/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6748	16	16138	16/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6749	17	16139	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
6750	18	16140	16/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6751	19	16141	16/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6752	20	16142	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
6753	21	16143	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
6754	22	16144	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
6755	23	16145	16/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6756	24	16146	16/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6757	25	16147	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
6758	26	16148	16/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6759	27	16149	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
6760	28	16150	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
6761	29	16151	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV18FVE
6762	30	16152	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
6763	31	16153	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
6764	32	16154	16/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6765	33	16155	16/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6766	34	16156	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
6767	35	16157	16/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6768	36	16158	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
6769	37	16159	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
6770	38	16160	16/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6771	39	16161	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21BXN
6772	40	16162	16/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6773	41	16163	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
6774	42	16164	16/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6775	43	16165	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
6776	44	16166	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
6777	45	16167	16/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6778	46	16168	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
6779	47	16169	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
6780	48	16170	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
6781	49	16171	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
6782	50	16172	16/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6783	51	16173	16/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6784	52	16174	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
6785	53	16175	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
6786	54	16176	16/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6787	55	16177	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
6788	56	16178	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
6789	57	16179	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
6790	58	16180	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
6791	59	16181	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
6792	60	16182	16/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
6793	61	16183	16/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6794	62	16184	16/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6795	1	16185	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6796	2	16186	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6797	3	16187	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6798	4	16188	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6799	5	16189	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6800	6	16190	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6801	7	16191	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6802	8	16192	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
6803	9	16193	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6804	10	16194	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6805	11	16195	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6806	12	16196	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6807	13	16197	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6808	14	16198	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
6809	15	16199	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
6810	16	16200	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6811	17	16201	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6812	18	16202	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6813	19	16203	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
6814	20	16204	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
6815	21	16205	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
6816	22	16206	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
6817	23	16207	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6818	24	16208	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
6819	25	16209	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
6820	26	16210	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6821	27	16211	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6822	28	16212	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
6823	29	16213	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6824	30	16214	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6825	31	16215	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6826	32	16216	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
6827	33	16217	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6828	34	16218	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
6829	35	16219	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6830	36	16220	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
6831	37	16221	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
6832	38	16222	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
6833	39	16223	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6834	40	16224	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
6835	41	16225	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6836	42	16226	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
6837	43	16227	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6838	44	16228	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
6839	45	16229	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6840	46	16230	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6841	47	16231	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6842	48	16232	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6843	49	16233	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
6844	50	16234	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
6845	51	16235	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6846	52	16236	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
6847	53	16237	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6848	54	16238	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
6849	55	16239	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
6850	56	16240	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ

6851	57	16241	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
6852	58	16242	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6853	59	16243	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
6854	60	16244	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6855	61	16245	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
6856	62	16246	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6857	63	16247	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6858	64	16248	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6859	65	16249	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
6860	66	16250	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6861	67	16251	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6862	68	16252	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6863	69	16253	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
6864	70	16254	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
6865	71	16255	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6866	72	16256	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6867	73	16257	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
6868	74	16258	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
6869	75	16259	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6870	76	16260	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6871	77	16261	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6872	78	16262	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
6873	79	16263	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6874	80	16264	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6875	81	16265	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6876	82	16266	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6877	83	16267	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
6878	84	16268	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
6879	85	16269	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6880	86	16270	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
6881	87	16271	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6882	88	16272	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
6883	89	16273	19/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
6884	90	16274	19/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6885	1	16275	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6886	2	16276	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6887	3	16277	20/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
6888	4	16278	20/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
6889	5	16279	20/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
6890	6	16280	20/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
6891	7	16281	20/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21CHF
6892	8	16282	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6893	9	16283	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6894	10	16284	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6895	11	16285	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6896	12	16286	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6897	13	16287	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6898	14	16288	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6899	15	16289	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6900	16	16290	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6901	17	16291	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6902	18	16292	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6903	19	16293	20/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
6904	20	16294	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6905	21	16295	20/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
6906	22	16296	20/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
6907	23	16297	20/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
6908	24	16298	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6909	25	16299	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	BK21BYH
6910	26	16300	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6911	27	16301	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6912	28	16302	20/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVD
6913	29	16303	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6914	30	16304	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6915	31	16305	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6916	32	16306	20/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
6917	33	16307	20/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
6918	34	16308	20/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
6919	35	16309	20/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
6920	36	16310	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6921	37	16311	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6922	38	16312	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6923	39	16313	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6924	40	16314	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6925	41	16315	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6926	42	16316	20/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
6927	43	16317	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6928	44	16318	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6929	45	16319	20/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
6930	46	16320	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6931	47	16321	20/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
6932	48	16322	20/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
6933	49	16323	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6934	50	16324	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6935	51	16325	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6936	52	16326	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6937	53	16327	20/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVD
6938	54	16328	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
6939	55	16329	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6940	56	16330	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6941	57	16331	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6942	58	16332	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6943	59	16333	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6944	60	16334	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6945	61	16335	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6946	62	16336	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6947	63	16337	20/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6948	1	16338	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6949	2	16339	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6950	3	16340	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6951	4	16341	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6952	5	16342	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6953	6	16343	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
6954	7	16344	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6955	8	16345	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6956	9	16346	21/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
6957	10	16347	21/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
6958	11	16348	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6959	12	16349	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6960	13	16350	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6961	14	16351	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6962	15	16352	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6963	16	16353	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6964	17	16354	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6965	18	16355	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6966	19	16356	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
6967	20	16357	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
6968	21	16358	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
6969	22	16359	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
6970	23	16360	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
6971	24	16361	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
6972	25	16362	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6973	26	16363	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
6974	27	16364	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
6975	28	16365	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
6976	29	16366	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6977	30	16367	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA

6978	31	PROVEC50578	21/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVA
6979	32	PROVEC50579	21/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
6980	33	PROVEC50580	21/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVC
6981	34	PROVEC50581	21/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVB
6982	35	PROVEC50582	21/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVD
6983	36	PROVEC50583	21/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV18FVE
6984	37	PROVEC50584	21/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYH
6985	38	PROVEC50585	21/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBB
6986	39	PROVEC50586	21/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYJ
6987	40	PROVEC50587	21/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
6988	41	PROVEC50588	21/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
6989	42	PROVEC50589	21/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVA
6990	43	PROVEC50590	21/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
6991	44	PROVEC50591	21/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVC
6992	45	PROVEC50592	21/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVD
6993	46	PROVEC50593	21/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYH
6994	47	PROVEC50594	21/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVB
6995	48	PROVEC50595	21/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBB
6996	49	PROVEC50596	21/07/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYJ
6997	50	16368	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
6998	51	16369	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
6999	52	16370	21/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7000	1	16371	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
7001	2	16372	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7002	3	16373	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7003	4	16374	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
7004	5	16375	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7005	6	16376	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7006	7	16377	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7007	8	16378	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
7008	9	16379	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7009	10	16380	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7010	11	16381	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7011	12	16382	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
7012	13	16383	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7013	14	16384	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7014	15	16385	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7015	16	16386	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
7016	17	16387	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7017	18	16388	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
7018	19	16389	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7019	20	16390	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7020	21	16391	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7021	22	16392	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
7022	23	16393	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7023	24	16394	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7024	25	16395	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7025	26	16396	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
7026	27	16397	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7027	28	16398	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7028	29	16399	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
7029	30	16400	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7030	31	16401	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7031	32	16402	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7032	33	16403	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
7033	34	16404	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7034	35	16405	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7035	36	16406	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
7036	37	16407	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7037	38	16408	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7038	39	16409	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
7039	40	16410	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7040	41	16411	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7041	42	16412	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7042	43	16413	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7043	44	16414	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
7044	45	16415	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7045	46	16416	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7046	47	16417	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
7047	48	16418	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7048	49	16419	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7049	50	16420	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7050	51	16421	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7051	52	16422	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7052	53	16423	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
7053	54	16424	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7054	55	16425	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7055	56	16426	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
7056	57	16427	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7057	58	16428	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7058	59	16429	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
7059	60	16430	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7060	61	16431	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7061	62	16432	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7062	63	16433	22/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
7063	1	16434	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7064	2	16435	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
7065	3	16436	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7066	4	16437	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7067	5	16438	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7068	6	16439	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7069	7	16440	23/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXU
7070	8	16441	23/07/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXZ
7071	9	16442	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
7072	10	16443	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
7073	11	16444	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7074	12	16445	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7075	13	16446	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7076	14	16447	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7077	15	16448	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
7078	16	16449	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7079	17	16450	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7080	18	16451	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7081	19	16452	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7082	20	16453	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
7083	21	16454	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7084	22	16455	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
7085	23	16456	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7086	24	16457	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7087	25	16458	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
7088	26	16459	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7089	27	16460	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7090	28	16461	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7091	29	16462	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7092	30	16463	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7093	31	16464	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7094	32	16465	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
7095	33	16466	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
7096	34	16467	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7097	35	16468	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7098	36	16469	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7099	37	16470	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
7100	38	16471	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7101	39	16472	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7102	40	16473	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7103	41	16474	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7104	42	16475	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA

7105	43	16476	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
7106	44	16477	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
7107	45	16478	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7108	46	16479	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7109	47	16480	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
7110	48	16481	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7111	49	16482	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7112	50	16483	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7113	51	16484	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7114	52	16485	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7115	53	16486	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7116	54	16487	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
7117	55	16488	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7118	56	16489	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7119	57	16490	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7120	58	16491	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
7121	59	16492	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7122	60	16493	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7123	61	16494	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7124	62	16495	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7125	63	16496	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7126	64	16497	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7127	65	16498	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
7128	66	16499	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7129	67	16500	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7130	68	16501	23/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
7131	1	16502	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7132	2	16503	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21CHF
7133	3	16504	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7134	4	16505	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
7135	5	16506	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7136	6	16507	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7137	7	16508	26/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBB
7138	8	16509	26/07/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19FVC
7139	9	16510	26/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MT21TVZ
7140	10	16511	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7141	11	16512	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7142	12	16513	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
7143	13	16514	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7144	14	16515	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7145	15	16516	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
7146	16	16517	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7147	17	16518	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7148	18	16519	26/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
7149	19	16520	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
7150	20	16521	26/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
7151	21	16522	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7152	22	16523	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
7153	23	16524	26/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
7154	24	16525	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7155	25	16526	26/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
7156	26	16527	26/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
7157	27	16528	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7158	28	16529	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
7159	29	16530	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7160	30	16531	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7161	31	16532	26/07/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVD
7162	32	16533	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
7163	33	16534	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7164	34	16535	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7165	35	16536	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
7166	36	16537	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7167	37	16538	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7168	38	16539	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
7169	39	16540	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7170	40	16541	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7171	41	16542	26/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
7172	1	16543	27/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7173	2	16544	27/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7174	3	16545	27/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7175	1	16546	28/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
7176	2	16547	28/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
7177	3	16548	28/07/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7178	4	929268	28/07/2021	170407	3900	Mixed Metals	0	EMR	CBDU188448	MJ17WKF
7179	1	16549	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7180	2	16550	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
7181	3	16551	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
7182	4	16552	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
7183	5	16553	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
7184	6	16554	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
7185	7	16555	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
7186	8	16556	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
7187	9	16557	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7188	10	16558	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
7189	11	16559	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
7190	12	16560	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
7191	13	16561	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
7192	14	16562	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
7193	15	16563	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
7194	16	16564	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
7195	17	16565	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7196	18	16566	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7197	19	16567	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
7198	20	16568	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
7199	21	16569	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
7200	22	16570	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
7201	23	16571	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
7202	24	16572	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
7203	25	16573	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
7204	26	16574	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7205	27	16575	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7206	28	16576	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
7207	29	16577	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
7208	30	16578	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
7209	31	16579	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
7210	32	16580	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
7211	33	16581	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
7212	34	16582	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7213	35	16583	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7214	36	16584	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
7215	37	16585	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
7216	38	16586	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
7217	39	16587	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
7218	40	16588	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
7219	41	16589	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
7220	42	16590	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7221	43	16591	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
7222	44	16592	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7223	45	16593	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
7224	46	16594	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
7225	47	16595	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
7226	48	16596	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
7227	49	16597	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
7228	50	16598	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7229	51	16599	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
7230	52	16600	02/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
7231	1	16602	03/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU

7232	2	16603	03/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7233	3	16604	03/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
7234	4	16605	03/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
7235	5	16606	03/08/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
7236	6	16607	03/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
7237	7	16608	03/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
7238	8	16609	03/08/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKK
7239	9	16610	03/08/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXV
7240	10	16611	03/08/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXP
7241	11	16612	03/08/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKK
7242	12	16613	03/08/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXV
7243	13	16614	03/08/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXP
7244	14	16615	03/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7245	15	16616	03/08/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVX
7246	16	16617	03/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
7247	17	16618	03/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
7248	18	16619	03/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
7249	19	16620	03/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
7250	20	16621	03/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
7251	21	16622	03/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
7252	22	16623	03/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
7253	23	16624	03/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7254	24	16625	03/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
7255	25	16626	03/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7256	26	16627	03/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
7257	27	16628	03/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
7258	28	16629	03/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
7259	29	16630	03/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7260	30	16631	03/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
7261	31	16632	03/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7262	1	16633	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7263	2	16634	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
7264	3	16635	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
7265	4	16636	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
7266	5	16637	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
7267	6	16638	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
7268	7	16639	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
7269	8	16640	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
7270	9	16641	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
7271	10	16642	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
7272	11	16643	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7273	12	16644	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
7274	13	16645	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXZ
7275	14	16646	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
7276	15	16647	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
7277	16	16648	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
7278	17	16649	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
7279	18	16650	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
7280	19	16651	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
7281	20	16652	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
7282	21	16653	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
7283	22	16654	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
7284	23	16655	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
7285	24	16656	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
7286	25	16657	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
7287	26	16658	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
7288	27	16659	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
7289	28	16660	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
7290	29	16661	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
7291	30	16662	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
7292	31	16663	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
7293	32	16664	04/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
7294	1	PROVEC50597	11/08/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU90617	MK21CHF
7295	2	PROVEC50598	11/08/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU90617	MK21CHG
7296	3	PROVEC50599	11/08/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU90617	MK21BXL
7297	4	PROVEC50600	11/08/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU90617	MV20RKK
7298	5	PROVEC50601	11/08/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU90617	MK21BXV
7299	6	PROVEC50602	11/08/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU90617	MK21CHF
7300	7	PROVEC50603	11/08/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU90617	MK21CHG
7301	8	PROVEC50604	11/08/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU90617	MK21BXL
7302	9	PROVEC50605	11/08/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU90617	MV20RKK
7303	10	PROVEC50606	11/08/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU90617	MK21BXV
7304	11	PROVEC50607	11/08/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU90617	MK21CHG
7305	12	PROVEC50608	11/08/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU90617	MK21CHF
7306	13	PROVEC50609	11/08/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU90617	MK21BXL
7307	14	PROVEC50610	11/08/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU90617	MV20RKK
7308	15	PROVEC50611	11/08/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU90617	MK21BXV
7309	1	PROVEC50612	12/08/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU90617	MK21BXL
7310	2	PROVEC50613	12/08/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU90617	MK21BXL
7311	3	PROVEC50614	12/08/2021	170503	3900	Hydrocarbons	9	Maw Green	CBDU90617	MK21BXL
7312	1	16665	16/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7313	2	16666	16/08/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVW
7314	3	16667	16/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
7315	4	16668	16/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
7316	5	16669	16/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7317	6	16670	16/08/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
7318	7	16671	16/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7319	8	16672	16/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
7320	9	16673	16/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV18FVD
7321	10	16674	16/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
7322	11	16675	16/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7323	12	16676	16/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
7324	13	16677	16/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7325	14	16678	16/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7326	15	16679	16/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
7327	16	16680	16/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
7328	17	16681	16/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
7329	18	16682	16/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV18FVD
7330	19	16683	16/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7331	20	16684	16/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZUB
7332	21	16685	16/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7333	22	16686	16/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7334	23	16687	16/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
7335	24	16688	16/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
7336	25	16689	16/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
7337	26	16690	16/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV18FVD
7338	27	16691	16/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7339	28	16692	16/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
7340	29	16693	16/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7341	30	16694	16/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RB69ZVC
7342	31	16695	16/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
7343	32	16696	16/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7344	33	16697	16/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
7345	34	16698	16/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
7346	35	16699	16/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV18FVD
7347	36	16700	16/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
7348	37	16701	16/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7349	38	16702	16/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7350	39	16703	16/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7351	40	16704	16/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
7352	41	16705	16/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
7353	42	16706	16/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
7354	43	16707	16/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7355	1	16708	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7356	2	16709	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7357	3	16710	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7358	4	16711	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD

7359	5	16712	17/08/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
7360	6	16713	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
7361	7	16714	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7362	8	16715	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7363	9	16716	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7364	10	16717	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7365	11	16718	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7366	12	16719	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7367	13	16720	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7368	14	16721	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7369	15	16722	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
7370	16	16723	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7371	17	16724	17/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
7372	18	16725	17/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
7373	19	16726	17/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
7374	20	16727	17/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
7375	21	16728	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7376	22	16729	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7377	23	16730	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7378	24	16731	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7379	25	16732	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7380	26	16733	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7381	27	16734	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
7382	28	16735	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7383	29	16736	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7384	30	16737	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7385	31	16738	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7386	32	16739	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7387	33	16740	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7388	34	16741	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
7389	35	16742	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7390	36	16743	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7391	37	16744	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7392	38	16745	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18UBB
7393	39	16746	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7394	40	16747	17/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
7395	41	16748	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7396	42	16749	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7397	43	16750	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
7398	44	16751	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
7399	45	16752	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV692VA
7400	46	16753	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7401	47	16754	17/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
7402	48	16755	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
7403	49	16756	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7404	50	16757	17/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
7405	51	16758	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
7406	52	16759	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7407	53	16760	17/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
7408	1	16761	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7409	2	16762	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
7410	3	16763	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7411	4	16764	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
7412	5	16765	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
7413	6	16766	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7414	7	16767	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7415	8	16768	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7416	9	16769	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
7417	10	16770	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
7418	11	16771	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7419	12	16772	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7420	13	16773	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7421	14	16774	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
7422	15	16775	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7423	16	16776	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
7424	17	16777	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7425	18	16778	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
7426	19	16779	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7427	20	16780	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
7428	21	16781	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7429	22	16782	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7430	23	16783	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
7431	24	16784	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7432	25	16785	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
7433	26	16786	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7434	27	16787	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
7435	28	16788	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7436	29	16789	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
7437	30	16790	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7438	31	16791	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7439	32	16792	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
7440	33	16793	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7441	34	16794	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
7442	35	16795	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7443	36	16796	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
7444	37	16797	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
7445	38	16798	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7446	39	16799	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7447	40	16800	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7448	41	16801	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
7449	42	16802	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7450	43	16803	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
7451	44	16804	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
7452	45	16805	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7453	46	16806	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVC
7454	47	16807	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7455	48	16808	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7456	49	16809	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
7457	50	16810	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7458	51	16811	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7459	52	16812	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVE
7460	53	16813	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV18FVD
7461	54	16814	18/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7462	1	16815	23/03/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7463	2	16816	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7464	3	16817	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7465	4	16818	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7466	5	16819	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7467	6	16820	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
7468	7	16821	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7469	8	16822	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7470	9	16823	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7471	10	16824	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7472	11	16825	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7473	12	16826	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7474	13	16827	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7475	14	16828	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
7476	15	16829	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7477	16	16830	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7478	17	16831	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7479	18	16832	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7480	19	16833	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7481	20	16834	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7482	21	16835	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7483	22	16836	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
7484	23	16837	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7485	24	16838	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD

7486	25	16839	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7487	26	16840	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7488	27	16841	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7489	28	16842	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7490	29	16843	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
7491	30	16844	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7492	31	16845	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7493	32	16846	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7494	33	16847	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7495	34	16848	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7496	35	16849	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7497	36	16850	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
7498	37	16851	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7499	38	16852	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7500	39	16853	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7501	40	16854	23/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7502	1	PROVEC50615	24/08/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
7503	2	PROVEC50616	24/08/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBB
7504	3	16855	24/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
7505	4	16856	24/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
7506	5	16857	24/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7507	6	16858	24/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
7508	7	16859	24/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
7509	8	16860	24/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
7510	9	16861	24/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7511	10	16862	24/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
7512	11	16863	24/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
7513	12	16864	24/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
7514	13	PROVEC50617	24/08/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
7515	14	PROVEC50618	24/08/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBB
7516	15	16865	24/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7517	16	16866	24/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
7518	17	16867	24/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
7519	18	16868	24/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
7520	19	16869	24/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7521	20	16870	24/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
7522	21	16871	24/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
7523	22	16872	24/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
7524	23	16873	24/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
7525	24	16874	24/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7526	25	16875	24/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
7527	26	16876	24/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
7528	27	PROVEC50619	24/08/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
7529	28	PROVEC50620	24/08/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBB
7530	29	16877	24/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
7531	30	16878	24/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
7532	31	16879	24/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7533	32	16880	24/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
7534	33	16881	24/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
7535	34	16882	24/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
7536	35	16883	24/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
7537	1	PROVEC50621	25/08/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
7538	2	PROVEC50622	25/08/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBB
7539	3	16884	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
7540	4	16885	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7541	5	16886	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7542	6	16887	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
7543	7	16888	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
7544	8	16889	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
7545	9	16903	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
7546	10	16904	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
7547	11	16905	25/08/2021	170503	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7548	12	16906	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
7549	13	16907	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
7550	14	16908	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
7551	15	16909	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7552	16	16910	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7553	17	16911	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7554	18	16912	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
7555	19	16913	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7556	20	16914	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7557	21	PROVEC50623	25/08/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
7558	22	PROVEC50624	25/08/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBB
7559	23	16915	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
7560	24	16916	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7561	25	16917	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7562	26	16918	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
7563	27	16919	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7564	28	16920	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7565	29	16921	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
7566	30	PROVEC50625	25/08/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
7567	31	PROVEC50626	25/08/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBB
7568	32	16922	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7569	33	16923	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7570	34	16924	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
7571	35	16925	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
7572	36	16926	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7573	37	16927	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7574	38	16928	25/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
7575	1	PROVEC50627	26/08/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
7576	2	16929	26/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7577	3	16930	26/08/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
7578	4	16931	26/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
7579	5	16932	26/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7580	6	16933	26/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
7581	7	16934	26/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
7582	8	16935	26/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7583	9	16936	26/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
7584	10	16937	26/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7585	11	16938	26/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
7586	12	PROVEC50628	26/08/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
7587	13	16939	26/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
7588	14	16940	26/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7589	15	16941	26/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
7590	16	16942	26/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
7591	17	16943	26/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7592	18	16944	26/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
7593	19	16945	26/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
7594	20	16946	26/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7595	21	16947	26/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
7596	22	16948	26/08/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
7597	23	16949	26/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7598	24	PROVEC50629	26/08/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
7599	25	16950	26/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
7600	26	16951	26/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7601	27	16952	26/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
7602	28	16953	26/08/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7603	1	16954	27/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7604	2	16955	27/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7605	3	16956	27/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7606	4	16957	27/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7607	5	16958	27/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7608	6	16959	27/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7609	7	16960	27/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7610	8	16961	27/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
7611	9	16962	27/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
7612	10	16963	27/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB

7613	11	16964	27/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
7614	12	16965	27/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVC
7615	13	16966	27/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVD
7616	14	16967	27/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
7617	15	16968	27/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
7618	16	16969	27/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
7619	17	16970	27/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
7620	18	16971	27/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVC
7621	19	16972	27/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVD
7622	20	16973	27/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
7623	21	16974	27/08/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
7624	22	16975	27/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7625	23	16976	27/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7626	24	16977	27/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7627	25	16978	27/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7628	26	16979	27/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7629	27	16980	27/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7630	28	16981	27/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7631	29	16982	27/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7632	30	16983	27/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7633	31	16984	27/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7634	32	16985	27/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7635	1	16986	31/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7636	2	16987	31/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7637	3	16988	31/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7638	4	16989	31/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7639	5	16990	31/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7640	6	16991	31/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7641	7	16992	31/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7642	8	16993	31/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7643	9	16994	31/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7644	10	16995	31/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7645	11	16996	31/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7646	12	16997	31/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7647	13	16998	31/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7648	14	16999	31/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
7649	15	17000	31/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7650	16	17001	31/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7651	17	17002	31/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7652	18	17003	31/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7653	19	17004	31/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7654	20	17005	31/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7655	21	17006	31/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7656	22	17007	31/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7657	23	17008	31/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7658	24	17009	31/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
7659	25	17010	31/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7660	26	17011	31/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7661	27	17012	31/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7662	28	17013	31/08/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7663	1	17014	01/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
7664	2	17015	01/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
7665	3	17016	01/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
7666	4	17017	01/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
7667	5	17018	01/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
7668	6	17019	01/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
7669	7	17020	01/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
7670	8	17021	01/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
7671	9	17022	01/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
7672	10	17023	01/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
7673	11	17024	01/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
7674	12	17025	01/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
7675	13	17026	01/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
7676	1	16890	02/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
7677	2	16891	02/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
7678	3	16892	02/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7679	4	16893	02/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
7680	5	16894	02/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
7681	6	16895	02/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
7682	7	16896	02/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
7683	8	16897	02/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVW
7684	9	16898	02/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
7685	10	16899	02/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
7686	11	16900	02/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
7687	12	16901	02/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
7688	13	16902	02/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
7689	14	17027	02/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
7690	15	17028	02/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
7691	16	17029	02/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
7692	1	17030	03/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
7693	2	17031	03/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
7694	3	17032	03/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
7695	4	17033	03/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
7696	5	17034	03/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
7697	6	17035	03/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7698	7	17036	03/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
7699	8	17037	03/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
7700	9	17038	03/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
7701	10	17039	03/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
7702	11	17040	03/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
7703	12	17041	03/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
7704	13	17042	03/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
7705	14	17043	03/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
7706	15	17044	03/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7707	16	17045	03/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7708	17	17046	03/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7709	18	17047	03/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKK
7710	19	17048	03/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7711	20	17049	03/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7712	21	17050	03/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7713	22	17051	03/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20EKF
7714	23	17052	03/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7715	24	17053	03/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7716	25	17054	03/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7717	26	17055	03/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
7718	27	17056	03/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
7719	28	17057	03/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
7720	29	17058	03/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7721	30	17059	03/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7722	31	17060	03/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7723	32	17061	03/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
7724	33	17062	03/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7725	34	17063	03/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7726	35	17064	03/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7727	36	17065	03/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
7728	37	17066	03/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
7729	38	17067	03/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
7730	39	17068	03/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
7731	1	17069	06/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
7732	2	17070	06/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
7733	3	17071	06/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
7734	4	17072	06/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
7735	5	17073	06/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
7736	6	17074	06/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7737	7	17075	06/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
7738	8	17076	06/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
7739	9	17077	06/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN

7740	10	17078	06/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
7741	11	17079	06/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
7742	12	17080	06/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
7743	13	17081	06/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
7744	14	17082	06/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7745	15	17083	06/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
7746	16	17084	06/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKN
7747	17	17085	06/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7748	18	17086	06/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
7749	19	17087	06/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
7750	20	17088	06/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXP
7751	21	17089	06/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7752	22	17090	06/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
7753	23	17091	06/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
7754	24	17092	06/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
7755	25	17093	06/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
7756	26	17094	06/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7757	27	17095	06/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
7758	28	17096	06/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
7759	29	17097	06/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
7760	30	17098	06/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
7761	31	17099	06/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
7762	32	17100	06/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
7763	33	17101	06/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
7764	34	17102	06/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7765	35	17103	06/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
7766	36	17104	06/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
7767	37	17105	06/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
7768	38	17106	06/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
7769	39	17107	06/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7770	40	17108	06/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
7771	41	17109	06/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
7772	42	30030	06/09/2021	170107	3900	Concrete/Hard Materials	9	Ashton Old Rd	CBDU90617	MT21TVV
7773	43	17110	06/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
7774	44	17111	06/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7775	45	17112	06/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
7776	46	17113	06/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
7777	47	17114	06/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
7778	1	17115	07/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
7779	2	17116	07/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
7780	3	17117	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
7781	4	17118	07/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
7782	5	17119	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7783	6	17120	07/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
7784	7	17121	07/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
7785	8	17122	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7786	9	17123	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
7787	10	17124	07/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
7788	11	17125	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7789	12	17126	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
7790	13	17127	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7791	14	17128	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
7792	15	17129	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
7793	16	17130	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7794	17	17131	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
7795	18	17132	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7796	19	17133	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
7797	20	17134	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
7798	21	17135	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7799	22	17136	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
7800	23	17137	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
7801	24	17138	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7802	25	17139	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
7803	26	17140	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
7804	27	17141	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7805	28	17142	07/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
7806	29	17143	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
7807	30	17144	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
7808	31	17145	07/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
7809	32	17146	07/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
7810	33	17147	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7811	34	17148	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
7812	35	17149	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
7813	36	17150	07/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
7814	37	17151	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7815	38	17152	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
7816	39	17153	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
7817	40	17154	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
7818	41	17155	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7819	42	17156	07/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
7820	43	17157	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7821	44	17158	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7822	45	17159	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
7823	46	17160	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
7824	47	17161	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
7825	48	17162	07/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7826	49	17163	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
7827	50	17164	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
7828	51	17165	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7829	52	17166	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
7830	53	17167	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7831	54	17168	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7832	55	17169	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
7833	56	17170	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
7834	57	17171	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
7835	58	17172	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXZ
7836	59	17173	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
7837	60	17174	07/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
7838	61	17175	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
7839	62	17176	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
7840	63	17177	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7841	64	17178	07/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
7842	1	17179	08/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
7843	2	17180	08/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7844	3	17181	08/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
7845	4	17182	08/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
7846	5	17183	08/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
7847	6	17184	08/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7848	7	17185	08/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
7849	8	17186	08/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
7850	9	17187	08/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7851	10	17188	08/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXP
7852	11	17189	08/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
7853	12	PROVEC50630	08/09/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVD
7854	13	PROVEC50631	08/09/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVC
7855	14	17190	08/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
7856	15	PROVEC50632	08/09/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVA
7857	16	17191	08/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
7858	17	17192	08/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKJ
7859	18	17193	08/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
7860	19	17194	08/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
7861	20	17195	08/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
7862	21	17196	08/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKK
7863	22	17197	08/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
7864	23	17198	08/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
7865	24	17199	08/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKJ
7866	25	17200	08/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF

7867	26	17201	08/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
7868	27	PROVEC50633	08/09/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVD
7869	28	PROVEC50634	08/09/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVC
7870	29	PROVEC50635	08/09/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVA
7871	30	17202	08/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BXV
7872	31	17203	08/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXW
7873	32	17204	08/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7874	33	17205	08/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
7875	34	17206	08/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
7876	35	17207	08/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
7877	36	17208	08/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7878	37	17209	08/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
7879	38	17210	08/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKJ
7880	39	17211	08/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
7881	40	17212	08/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
7882	41	17213	08/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7883	42	17214	08/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
7884	43	17215	08/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
7885	44	17216	08/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7886	45	PROVEC50636	08/09/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV693ZVD
7887	46	PROVEC50637	08/09/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYH
7888	47	PROVEC50638	08/09/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV693ZVC
7889	48	PROVEC50639	08/09/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV693ZVA
7890	49	17217	08/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
7891	50	17218	08/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7892	51	17219	08/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
7893	52	17220	08/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	T21TVU
7894	53	17221	08/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
7895	54	17222	08/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7896	55	17223	08/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
7897	56	17224	08/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7898	1	17225	09/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7899	2	17226	09/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
7900	3	17227	09/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
7901	4	17228	09/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
7902	5	17229	09/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7903	6	17230	09/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
7904	7	17231	09/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
7905	8	17232	09/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
7906	9	PROVEC50640	09/09/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYH
7907	10	PROVEC50641	09/09/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVD
7908	11	PROVEC50642	09/09/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVC
7909	12	17233	09/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKK
7910	13	17234	09/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
7911	14	17235	09/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVZ
7912	15	17236	09/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
7913	16	17237	09/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
7914	17	17238	09/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
7915	18	17239	09/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
7916	19	17240	09/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
7917	20	17241	09/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKK
7918	21	17242	09/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVZ
7919	22	17243	09/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
7920	23	17244	09/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
7921	24	17245	09/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
7922	25	PROVEC50643	09/09/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYH
7923	26	PROVEC50644	09/09/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVD
7924	27	PROVEC50645	09/09/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVC
7925	28	17246	09/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
7926	29	17247	09/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
7927	30	17248	09/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7928	31	17249	09/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVZ
7929	32	17250	09/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
7930	33	17251	09/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7931	34	17252	09/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
7932	35	17253	09/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
7933	36	17254	09/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
7934	37	17255	09/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
7935	38	17256	09/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
7936	39	17257	09/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7937	40	17258	09/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7938	41	17259	09/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
7939	42	17260	09/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
7940	43	17261	09/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7941	44	17262	09/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
7942	45	PROVEC50646	09/09/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVD
7943	46	PROVEC50647	09/09/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYH
7944	47	PROVEC50648	09/09/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVC
7945	48	17263	09/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKJ
7946	49	17264	09/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
7947	50	17265	09/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7948	51	17266	09/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
7949	52	17267	09/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
7950	53	17268	09/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
7951	1	PROVEC50649	10/09/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
7952	2	PROVEC50650	10/09/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYL
7953	3	PROVEC50651	10/09/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYH
7954	4	PROVEC50652	10/09/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBB
7955	5	PROVEC50653	10/09/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVC
7956	6	PROVEC50654	10/09/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV69KTT
7957	7	PROVEC50655	10/09/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	RV69ZVB
7958	8	17269	10/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVW
7959	9	17270	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7960	10	17271	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
7961	11	17272	10/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKJ
7962	12	17273	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
7963	13	17274	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
7964	14	17275	10/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKN
7965	15	17276	10/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
7966	16	17277	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
7967	17	17278	10/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVO
7968	18	17279	10/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
7969	19	17280	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
7970	20	17281	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
7971	21	17282	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
7972	22	17283	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
7973	23	17284	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
7974	24	17285	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
7975	25	17286	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
7976	26	17287	10/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVW
7977	27	17288	10/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKJ
7978	28	17289	10/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKN
7979	29	17290	10/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
7980	30	17291	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
7981	31	17292	10/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
7982	32	17293	10/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVO
7983	33	PROVEC50656	10/09/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MK21BYH
7984	34	PROVEC50657	10/09/2021	170503	3900	Hydrocarbons	14	Maw Green	CBDU90617	MV19UBA
7985	35	17294	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
7986	36	17295	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
7987	37	17296	10/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7988	38	17297	10/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
7989	39	17298	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
7990	40	17299	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
7991	41	17300	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
7992	42	17301	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
7993	43	17302	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN

7994	44	17303	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
7995	45	17304	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
7996	46	17305	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
7997	47	17306	10/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
7998	48	17307	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
7999	49	17308	10/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
8000	50	17309	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8001	51	17310	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
8002	52	17311	10/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
8003	53	17312	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
8004	54	17313	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8005	55	17314	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8006	56	17315	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8007	57	17316	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
8008	58	17317	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
8009	59	17318	10/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
8010	60	17319	10/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
8011	61	17320	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8012	62	17321	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
8013	63	17322	10/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
8014	64	17323	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
8015	65	17324	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8016	66	17325	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8017	67	17326	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8018	68	17327	10/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
8019	69	17328	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
8020	70	17329	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
8021	71	17330	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8022	72	17331	10/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
8023	1	17332	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
8024	2	17333	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8025	3	17334	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
8026	4	17335	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8027	5	17336	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8028	6	17337	13/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
8029	7	17338	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8030	8	17339	13/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVX
8031	9	17340	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8032	10	17341	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8033	11	17342	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
8034	12	17343	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8035	13	17344	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8036	14	17345	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8037	15	17346	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
8038	16	17347	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8039	17	17348	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8040	18	17349	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8041	19	17350	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
8042	20	17351	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8043	21	17352	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
8044	22	17353	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8045	23	17354	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8046	24	17355	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
8047	25	17356	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
8048	26	17357	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8049	27	17358	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8050	28	17359	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8051	29	17360	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8052	30	17361	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8053	31	17362	13/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXZ
8054	32	17363	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8055	33	17364	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8056	34	17365	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
8057	35	17366	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8058	36	17367	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
8059	37	17368	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8060	38	17369	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8061	39	17370	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
8062	40	17371	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
8063	41	17372	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8064	42	17373	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8065	43	17374	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8066	44	17375	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8067	45	17376	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8068	46	17377	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8069	47	17378	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
8070	48	17379	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8071	49	17380	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
8072	50	17381	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8073	51	17382	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8074	52	17383	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8075	53	17384	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8076	54	17385	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
8077	55	17386	13/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXV
8078	56	17387	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8079	57	17388	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8080	58	17389	13/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8081	1	17390	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8082	2	17391	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8083	3	17392	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8084	4	17393	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8085	5	17394	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8086	6	17395	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8087	7	17396	14/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
8088	8	17397	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
8089	9	17398	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
8090	10	17399	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8091	11	17400	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8092	12	17401	14/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
8093	13	17402	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8094	14	17403	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8095	15	17404	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
8096	16	17405	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8097	17	17406	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8098	18	17407	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
8099	19	17408	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
8100	20	17409	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8101	21	17410	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
8102	22	17411	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8103	23	17412	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8104	24	17413	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8105	25	17414	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
8106	26	17415	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8107	27	17416	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8108	28	17417	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
8109	29	17418	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8110	30	17419	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	K21BXV
8111	31	17420	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8112	32	17421	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8113	33	17422	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8114	34	17423	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8115	35	17424	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
8116	36	17425	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8117	37	17426	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8118	38	17427	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8119	39	17428	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
8120	40	17429	14/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ

8121	1	17430	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8122	2	17431	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8123	3	17432	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
8124	4	17433	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8125	5	17434	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
8126	6	17435	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXZ
8127	7	17436	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8128	8	17437	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8129	9	17438	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
8130	10	17439	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8131	11	17440	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
8132	12	17441	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
8133	13	17442	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8134	14	17443	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
8135	15	17444	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8136	16	17445	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8137	17	17446	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8138	18	17447	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV19UBB
8139	19	17448	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8140	20	17449	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
8141	21	17450	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
8142	22	17451	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
8143	23	17452	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
8144	24	17453	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RJK
8145	25	17454	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8146	26	17455	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8147	27	17456	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8148	28	17457	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
8149	29	17458	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
8150	30	17459	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8151	31	17460	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
8152	32	17461	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8153	33	17462	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
8154	34	17463	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
8155	35	17464	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8156	36	17465	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
8157	37	17466	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
8158	38	17467	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BYL
8159	39	17468	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
8160	40	17469	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
8161	41	17470	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
8162	42	17471	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8163	43	17472	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8164	44	17473	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
8165	45	17474	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8166	46	17475	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
8167	47	17476	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
8168	48	17477	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
8169	49	17478	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
8170	50	17479	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
8171	51	17480	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
8172	52	17481	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
8173	53	17482	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8174	54	17483	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
8175	55	17484	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8176	56	17485	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8177	57	17486	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
8178	58	17487	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
8179	59	17488	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
8180	60	17489	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
8181	61	17490	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
8182	62	17491	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
8183	63	17492	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8184	64	17493	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
8185	65	17494	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
8186	66	17495	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
8187	67	17496	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8188	68	17497	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
8189	69	17498	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
8190	70	17499	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8191	71	17500	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
8192	72	17501	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV59ZVC
8193	73	17502	15/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
8194	74	17503	15/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
8195	1	17504	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8196	2	17505	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
8197	3	17506	16/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXV
8198	4	17507	16/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKN
8199	5	17508	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8200	6	17509	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8201	7	17510	16/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
8202	8	17511	16/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVC
8203	9	17512	16/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKK
8204	10	17513	16/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVD
8205	11	17514	16/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVB
8206	12	17515	16/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
8207	13	17516	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8208	14	17517	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8209	15	17518	16/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
8210	16	17519	16/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
8211	17	17520	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8212	18	17521	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
8213	19	17522	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8214	20	17523	16/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVD
8215	21	17524	16/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVC
8216	22	17525	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8217	23	17526	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
8218	24	17527	16/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVB
8219	25	17528	16/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
8220	26	17529	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8221	27	17530	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8222	28	17531	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8223	29	17532	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8224	30	17533	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
8225	31	17534	16/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVD
8226	32	17535	16/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVC
8227	33	17536	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8228	34	17537	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8229	35	17538	16/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVB
8230	36	17539	16/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
8231	37	17540	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8232	38	17541	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8233	39	17542	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
8234	40	17543	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8235	41	17544	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8236	42	17545	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
8237	43	17546	16/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVD
8238	44	17547	16/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVC
8239	45	17548	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8240	46	17549	16/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
8241	47	17550	16/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVB
8242	48	17551	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8243	49	17552	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8244	50	17553	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8245	51	17554	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
8246	52	17555	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8247	53	17556	16/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD

8248	54	17557	16/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8249	55	17558	16/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
8250	56	17559	16/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
8251	1	17560	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8252	2	17561	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
8253	3	17562	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8254	4	17563	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
8255	5	17564	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8256	6	17565	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8257	7	17566	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8258	8	17567	17/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXV
8259	9	17568	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8260	10	17569	17/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
8261	11	17570	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8262	12	17571	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8263	13	17572	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8264	14	17573	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
8265	15	17574	17/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
8266	16	17575	17/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
8267	17	17576	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8268	18	17577	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8269	19	17578	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8270	20	17579	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8271	21	17580	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8272	22	17581	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8273	23	17582	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8274	24	17583	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8275	25	17584	17/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
8276	26	17585	17/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
8277	27	17586	17/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXV
8278	28	17587	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8279	29	17588	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8280	30	17589	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8281	31	17590	17/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
8282	32	17591	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8283	33	17592	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8284	34	17593	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8285	35	17594	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8286	36	17595	17/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
8287	37	17596	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8288	38	17597	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8289	39	17598	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8290	40	17599	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8291	41	17600	17/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
8292	42	17601	17/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXV
8293	43	17602	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8294	44	17603	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8295	45	17604	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8296	46	17605	17/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
8297	47	17606	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8298	48	17607	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8299	49	17608	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8300	50	17609	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8301	51	17610	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8302	52	17611	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8303	53	17612	17/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
8304	54	17613	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8305	55	17614	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8306	56	17615	17/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
8307	57	17616	17/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
8308	58	17617	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8309	59	17618	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8310	60	17619	17/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
8311	61	17620	17/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKK
8312	62	17621	17/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVX
8313	63	17622	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8314	64	17623	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8315	65	17624	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8316	66	17625	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8317	67	17626	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8318	68	17627	17/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8319	1	17628	20/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVW
8320	2	17629	20/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
8321	3	17630	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8322	4	17631	20/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
8323	5	17632	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8324	6	17633	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8325	7	17634	20/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BXP
8326	8	17635	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8327	9	17636	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8328	10	17637	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8329	11	17638	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8330	12	17639	20/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
8331	13	17640	20/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKJ
8332	14	17641	20/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
8333	15	17642	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8334	16	17643	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8335	17	17644	20/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
8336	18	17645	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8337	19	17646	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8338	20	17647	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8339	21	17648	20/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
8340	22	17649	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8341	23	17650	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8342	24	17651	20/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21YVW
8343	25	17652	20/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXP
8344	26	17653	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8345	27	17654	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8346	28	17655	20/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
8347	29	17656	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8348	30	17657	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8349	31	17658	20/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
8350	32	17659	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8351	33	17660	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8352	34	17661	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8353	35	17662	20/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
8354	36	17663	20/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
8355	37	17664	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8356	38	17665	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8357	39	17666	20/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXP
8358	40	17667	20/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21VW
8359	41	17668	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8360	42	17669	20/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
8361	43	17670	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8362	44	17671	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8363	45	17672	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8364	46	17673	20/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
8365	47	30031	20/09/2021	170107	3900	Concrete/Hard Materials	9	Ashton Old Rd	CBDU90617	MK21BXN
8366	48	17674	20/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXP
8367	49	30032	20/09/2021	170107	3900	Concrete/Hard Materials	9	Ashton Old Rd	CBDU90617	MV20RLY
8368	50	30033	20/09/2021	170107	3900	Concrete/Hard Materials	9	Ashton Old Rd	CBDU90617	MV20RKF
8369	51	30034	20/09/2021	170107	3900	Concrete/Hard Materials	9	Ashton Old Rd	CBDU90617	MT21TVW
8370	52	30035	20/09/2021	170107	3900	Concrete/Hard Materials	9	Ashton Old Rd	CBDU90617	MV20RLY
8371	53	17675	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MC20RKN
8372	54	17676	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8373	55	17677	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
8374	56	17678	20/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH

8375	57	17679	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8376	58	17680	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MCV20RKK
8377	59	17681	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8378	60	17682	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXZ
8379	61	17683	20/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8380	1	17684	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8381	2	17685	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8382	3	17686	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8383	4	17687	21/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
8384	5	17688	21/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXZ
8385	6	17689	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8386	7	17690	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8387	8	17691	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8388	9	17692	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8389	10	17693	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8390	11	17694	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
8391	12	17695	21/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXP
8392	13	17696	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
8393	14	17697	21/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVW
8394	15	17698	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8395	16	17699	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8396	17	17700	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8397	18	17701	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8398	19	17702	21/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
8399	20	17703	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8400	21	17704	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8401	22	17705	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8402	23	17706	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8403	24	17707	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8404	25	17708	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
8405	26	17709	21/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVW
8406	27	17710	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8407	28	17711	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8408	29	17712	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8409	30	17713	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8410	31	17714	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8411	32	17715	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8412	33	17716	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8413	34	17717	21/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
8414	35	17718	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8415	36	17719	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8416	37	17720	21/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVW
8417	38	17721	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8418	39	17722	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8419	40	17723	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8420	41	17724	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8421	42	17725	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8422	43	17726	21/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
8423	44	17727	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8424	45	17728	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8425	46	17729	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8426	47	17730	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8427	48	17731	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXZ
8428	49	17732	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8429	50	17733	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8430	51	17734	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8431	52	17735	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
8432	53	17736	21/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
8433	54	17737	21/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
8434	1	17738	22/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVW
8435	2	17739	22/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
8436	3	17740	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8437	4	17741	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8438	5	17742	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
8439	6	17743	22/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
8440	7	17744	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8441	8	17745	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
8442	9	17746	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8443	10	17747	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8444	11	17748	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8445	12	17749	22/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVB
8446	13	17750	22/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXV
8447	14	17751	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8448	15	17752	22/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVA
8449	16	17753	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
8450	17	17754	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8451	18	17755	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8452	19	17756	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8453	20	17757	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8454	21	17758	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8455	22	17759	22/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
8456	23	17760	22/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
8457	24	17761	22/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVW
8458	25	17762	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
8459	26	17763	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8460	27	17764	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8461	28	17765	22/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVA
8462	29	17766	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8463	30	17767	22/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVB
8464	31	17768	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
8465	32	17769	22/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKN
8466	33	17770	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8467	34	17771	22/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
8468	35	17772	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8469	36	17773	22/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
8470	37	17774	22/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVW
8471	38	17775	22/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
8472	39	17776	22/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXV
8473	40	17777	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
8474	41	17778	22/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
8475	42	17779	22/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
8476	43	17780	22/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
8477	44	17781	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
8478	45	17782	22/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
8479	46	17783	22/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
8480	47	17784	22/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVW
8481	48	17785	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8482	49	17786	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8483	50	17787	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8484	51	17788	22/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
8485	52	17789	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
8486	53	17790	22/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
8487	54	17791	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8488	55	17792	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8489	56	17793	22/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
8490	57	17794	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8491	58	17795	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8492	59	17796	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
8493	60	17797	22/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8494	1	17798	23/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVW
8495	2	17799	23/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8496	3	17800	23/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
8497	4	17801	23/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
8498	5	17802	23/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKN
8499	6	17803	23/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8500	7	17804	23/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXZ
8501	8	17805	23/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF

8502	9	17806	23/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
8503	10	17807	23/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21CHF
8504	11	17808	23/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
8505	12	17809	23/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
8506	13	17810	23/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8507	14	17811	23/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8508	15	17812	23/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8509	16	17813	23/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
8510	17	17814	23/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8511	18	17815	23/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
8512	19	17816	23/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8513	20	17817	23/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8514	21	17818	23/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
8515	22	17819	23/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8516	23	17820	23/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8517	24	17821	23/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21CHF
8518	25	17822	23/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8519	26	17823	23/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
8520	27	17824	23/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8521	28	17825	23/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
8522	29	17826	23/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8523	30	17827	23/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
8524	31	17828	23/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8525	32	17829	23/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8526	33	17830	23/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
8527	34	17831	23/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
8528	35	17832	23/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8529	1	17833	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
8530	2	17834	24/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
8531	3	17835	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
8532	4	17836	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8533	5	17837	24/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXU
8534	6	17838	24/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKN
8535	7	17839	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8536	8	17840	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
8537	9	17841	24/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21CHF
8538	10	17842	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
8539	11	17843	24/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
8540	12	17844	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8541	13	17845	24/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
8542	14	17846	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8543	15	17847	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
8544	16	17848	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
8545	17	17849	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
8546	18	17850	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8547	19	17851	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8548	20	17852	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
8549	21	17853	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
8550	22	17854	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
8551	23	17855	24/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
8552	24	17856	24/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKN
8553	25	17857	24/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21CHF
8554	26	17858	24/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
8555	27	17859	24/09/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
8556	28	17860	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8557	29	17861	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
8558	30	17862	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
8559	31	17863	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8560	32	17864	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8561	33	17865	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
8562	34	17866	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8563	35	17867	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
8564	36	17868	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8565	37	17869	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
8566	38	17870	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
8567	39	17871	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8568	40	17872	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8569	41	17873	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
8570	42	17874	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8571	43	17875	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8572	44	17876	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
8573	45	17877	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
8574	46	17878	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8575	47	17879	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8576	48	17880	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
8577	49	17881	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8578	50	17882	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8579	51	17883	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
8580	52	17884	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
8581	53	17885	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8582	54	17886	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8583	55	17887	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
8584	56	17888	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8585	57	17889	24/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8586	1	17890	27/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
8587	2	17891	27/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8588	3	17892	27/09/2002	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXZ
8589	4	17893	27/09/1983	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8590	5	17894	27/09/1964	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
8591	6	17895	27/09/1945	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
8592	7	17896	27/09/1926	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXU
8593	8	17897	27/09/1907	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8594	9	17898	27/09/2002	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8595	10	17899	27/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
8596	11	17900	27/09/2002	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8597	12	17901	27/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
8598	13	17902	27/09/2002	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8599	14	17903	27/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8600	15	17904	27/09/2002	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8601	16	17905	27/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
8602	17	17906	27/09/2002	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8603	18	17907	27/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
8604	19	17908	27/09/2002	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8605	20	17909	27/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
8606	21	17910	27/09/2002	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
8607	22	17911	27/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8608	23	17912	27/09/2002	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8609	24	17913	27/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
8610	25	17914	27/09/2002	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8611	26	17915	27/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
8612	27	17916	27/09/2002	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8613	28	17917	27/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
8614	29	17918	27/09/2002	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8615	30	17919	27/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8616	31	17920	27/09/2002	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
8617	32	17921	27/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
8618	33	17922	27/09/2002	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8619	34	17923	27/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
8620	35	17924	27/09/2002	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
8621	36	17925	27/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8622	37	17926	27/09/2002	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8623	38	17927	27/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8624	39	17928	27/09/2002	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8625	40	17929	27/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
8626	41	17930	27/09/2002	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8627	42	17931	27/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8628	43	17932	27/09/2002	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN

8629	44	17933	27/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
8630	45	17934	27/09/2002	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8631	46	17935	27/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
8632	47	17936	27/09/2002	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8633	48	17937	27/09/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8634	49	17938	27/09/2040	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
8635	50	17939	27/09/2059	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8636	51	17940	27/09/2078	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8637	1	17941	29/09/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
8638	2	17942	29/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
8639	3	17943	29/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
8640	4	17944	29/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
8641	5	17945	29/09/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
8642	1	17946	01/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
8643	2	17947	01/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
8644	3	17948	01/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
8645	4	17949	01/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
8646	5	17950	01/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
8647	6	17951	01/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
8648	7	17952	01/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
8649	8	17953	01/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
8650	9	17954	01/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
8651	10	17955	01/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
8652	11	17956	01/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
8653	12	17957	01/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
8654	13	17958	01/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
8655	14	17959	01/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
8656	15	17960	01/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
8657	16	17961	01/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
8658	1	17962	04/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8659	2	17963	04/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
8660	3	17964	04/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8661	4	17965	04/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXW
8662	5	17966	04/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8663	6	17967	04/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8664	7	17968	04/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8665	8	17969	04/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
8666	9	17970	04/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8667	10	17971	04/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8668	11	17972	04/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8669	12	17973	04/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8670	13	17974	04/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8671	14	17975	04/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8672	15	17976	04/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
8673	16	17977	04/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8674	17	17978	04/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8675	18	17979	04/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8676	1	17980	05/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
8677	2	17981	05/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8678	3	17982	05/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVZ
8679	4	17983	05/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8680	5	17984	05/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8681	6	17985	05/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVZ
8682	7	17986	05/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
8683	8	17987	05/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8684	9	17988	05/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8685	10	17989	05/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8686	1	17990	07/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8687	2	17991	07/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8688	3	17992	07/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8689	4	17993	07/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8690	5	17994	07/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
8691	6	17995	07/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8692	7	17996	07/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8693	8	17997	07/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8694	9	17998	07/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8695	10	17999	07/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8696	11	18000	07/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8697	12	18001	07/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8698	13	18002	07/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8699	14	18003	07/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8700	15	18004	07/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8701	16	18005	07/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8702	17	18006	07/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVX
8703	18	18007	07/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKK
8704	19	18008	07/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
8705	20	18009	07/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RLY
8706	21	18010	07/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8707	22	18011	07/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8708	1	18012	08/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
8709	2	18013	08/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVX
8710	3	18014	08/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
8711	4	18015	08/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
8712	5	18016	08/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8713	6	18017	08/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8714	7	18018	08/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVX
8715	8	18019	08/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8716	9	18020	08/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
8717	10	18021	08/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
8718	11	18022	08/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
8719	12	18023	08/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8720	13	18024	08/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8721	14	18025	08/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
8722	15	18026	08/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVX
8723	16	18027	08/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
8724	17	18028	08/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
8725	18	18029	08/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
8726	19	18030	08/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RLY
8727	20	18031	08/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
8728	21	18032	08/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
8729	22	18033	08/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVX
8730	23	18034	08/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
8731	24	18035	08/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
8732	25	18036	08/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RLY
8733	26	18037	08/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
8734	1	18038	11/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8735	2	18039	11/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8736	3	18040	11/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8737	4	18041	11/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8738	5	18042	11/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8739	6	18043	11/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8740	7	18044	11/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8741	8	18045	11/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVX
8742	9	18046	11/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
8743	10	18047	11/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8744	11	18048	11/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8745	12	18049	11/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
8746	13	18050	11/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8747	14	18051	11/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8748	15	18052	11/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8749	16	18053	11/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
8750	17	18054	11/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RLY
8751	18	18055	11/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
8752	19	18056	11/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKJ
8753	20	18057	11/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
8754	21	18058	11/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RLY
8755	22	18059	11/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN

8756	23	18060	11/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKJ
8757	24	18061	11/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
8758	25	18062	11/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVX
8759	26	18063	11/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RLY
8760	27	18064	11/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
8761	28	18065	11/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8762	29	18066	11/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8763	30	18067	11/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8764	31	18068	11/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8765	1	18069	12/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
8766	2	18070	12/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
8767	3	18071	12/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
8768	4	18072	12/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVW
8769	5	18073	12/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXW
8770	6	18074	12/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
8771	7	18075	12/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
8772	8	18076	12/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
8773	9	18077	12/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
8774	10	18078	12/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
8775	11	18079	12/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
8776	12	18080	12/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
8777	13	18081	12/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVW
8778	14	18082	12/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
8779	15	18083	12/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RLY
8780	16	18084	12/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
8781	17	18085	12/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
8782	18	18086	12/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
8783	19	18087	12/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
8784	20	18088	12/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVW
8785	21	18089	12/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
8786	22	18090	12/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
8787	23	18091	12/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
8788	24	18092	12/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
8789	1	18093	15/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
8790	2	18094	15/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8791	3	18095	15/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8792	4	18096	15/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8793	5	18097	15/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8794	6	18099	15/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8795	7	18100	15/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8796	1	18101	18/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
8796	2	18102	18/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
8796	3	18103	18/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8796	4	18104	18/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
8796	5	18105	18/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8796	6	18106	18/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
8796	7	18107	18/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8796	8	18108	18/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
8796	9	18109	18/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8796	10	18110	18/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8796	11	18111	18/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
8796	12	18112	18/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
8796	13	18113	18/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
8796	14	18114	18/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8796	15	18115	18/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8796	16	18116	18/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
8796	17	18117	18/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
8796	18	18118	18/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKN
8796	19	18119	18/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8796	20	18120	18/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8796	21	18121	18/10/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVA
8796	22	18122	18/10/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVC
8796	23	18123	18/10/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
8796	24	18124	18/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8796	25	18125	18/10/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
8797	26	18126	18/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
8798	27	18127	18/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8799	28	18128	18/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8800	29	18129	18/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8801	30	18130	18/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKN
8802	31	18131	18/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
8803	32	18132	18/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
8804	33	18133	18/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8805	34	18134	18/10/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVC
8806	35	18135	18/10/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
8807	36	18136	18/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8808	37	18137	18/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
8809	38	18138	18/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKK
8810	39	18139	18/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
8811	40	18140	18/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVW
8812	41	18141	18/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKN
8813	42	18142	18/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
8814	43	18143	18/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8815	44	18144	18/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
8816	45	18145	18/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
8817	1	18146	19/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
8818	2	18147	19/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8819	3	18148	19/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8820	4	18149	19/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8821	5	18150	19/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVZ
8822	6	18151	19/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8823	7	18152	19/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXZ
8824	8	18153	19/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8825	9	18154	19/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8826	10	18155	19/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8827	11	18156	19/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8828	12	18157	19/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
8829	13	18158	19/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8830	14	18159	19/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8831	15	18160	19/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXZ
8832	16	18161	19/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8833	17	18162	19/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
8834	18	18163	19/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8835	19	18164	19/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8836	20	18165	19/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8837	21	18166	19/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
8838	22	18167	19/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8839	23	18168	19/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
8840	24	18169	19/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BYZ
8841	25	18170	19/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8842	26	18171	19/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
8843	27	18172	19/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8844	28	18173	19/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8845	29	18174	19/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
8846	1	18175	20/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
8847	2	18176	20/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8848	3	18177	20/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8849	4	18178	20/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8850	5	18179	20/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8851	6	18180	20/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
8852	7	18181	20/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8853	8	18182	20/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8854	9	18183	20/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8855	10	18184	20/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
8856	11	18185	20/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8857	12	18186	20/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKJ
8858	13	18187	20/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP

8859	14	18188	20/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8860	15	18189	20/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8861	16	18190	20/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
8862	17	18191	20/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
8863	18	18192	20/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8864	19	18193	20/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8865	20	18194	20/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8866	21	18195	20/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8867	22	18196	20/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8868	23	18197	20/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8869	24	18198	20/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8870	25	18199	20/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
8871	1	18200	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8872	2	18201	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8873	3	18202	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8874	4	18203	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8875	5	18204	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
8876	6	18205	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
8877	7	18206	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8878	8	18207	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8879	9	18208	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8880	10	18209	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
8881	11	18210	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8882	12	18211	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8883	13	18212	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8884	14	18213	21/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVO
8885	15	18214	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
8886	16	18215	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8887	17	18216	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8888	18	18217	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8889	19	18218	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
8890	20	18219	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8891	21	18220	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8892	22	18221	21/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVO
8893	23	18222	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8894	24	18223	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8895	25	18224	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8896	26	18225	21/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
8897	27	18226	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8898	28	18227	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8899	29	18228	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8900	30	18229	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8901	31	18230	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8902	32	18231	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
8903	33	18232	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
8904	34	18233	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8905	35	18234	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8906	36	18235	21/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
8907	1	18236	22/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21CHF
8908	2	18237	22/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
8909	3	18238	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8910	4	18239	22/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
8911	5	18240	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
8912	6	18241	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
8913	7	18242	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8914	8	18243	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8915	9	18244	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
8916	10	18245	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8917	11	18246	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8918	12	18247	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
8919	13	18248	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK20RKJ
8920	14	18249	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8921	15	18250	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
8922	16	18251	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8923	17	18252	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8924	18	18253	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8925	19	18254	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8926	20	18255	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
8927	21	18256	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
8928	22	18257	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8929	23	18258	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
8930	24	18259	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8931	25	18260	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
8932	26	18261	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8933	27	18262	22/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21CHF
8934	28	18263	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8935	29	18264	22/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
8936	30	18265	22/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
8937	31	18266	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8938	32	18267	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
8939	33	18268	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8940	34	18269	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
8941	35	18270	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8942	36	18271	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8943	37	18272	22/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21CHF
8944	38	18273	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
8945	39	18274	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
8946	40	18275	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8947	41	18276	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
8948	42	18277	22/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXL
8949	43	18278	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
8950	44	18279	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
8951	45	18280	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
8952	46	18281	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8953	47	18282	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
8954	48	18283	22/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8955	1	18284	25/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXW
8956	2	18285	25/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8957	3	18286	25/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
8958	4	18287	25/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8959	5	18288	25/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
8960	6	18289	25/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
8961	7	18290	25/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVO
8962	8	18291	25/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
8963	9	18292	25/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8964	10	18293	25/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8965	11	18294	25/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKJ
8966	12	18295	25/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
8967	13	18296	25/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8968	14	18297	25/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
8969	15	18298	25/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
8970	16	18299	25/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
8971	17	18300	25/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
8972	18	18301	25/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8973	19	18302	25/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKJ
8974	20	18303	25/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8975	21	18304	25/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8976	22	18305	25/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
8977	23	18306	25/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
8978	24	18307	25/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
8979	25	18308	25/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8980	26	18309	25/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8981	27	18310	25/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8982	28	18311	25/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8983	29	18312	25/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
8984	30	18313	25/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
8985	31	18314	25/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKJ

8986	32	18315	25/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8987	33	18316	25/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
8988	34	18317	25/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8989	35	18318	25/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
8990	36	18319	25/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
8991	37	18320	25/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
8992	38	18321	25/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
8993	39	18322	25/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
8994	40	18323	25/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
8995	41	18324	25/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
8996	1	18325	26/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXW
8997	2	18326	26/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVW
8998	3	18327	26/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
8999	4	18328	26/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9000	5	18329	26/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9001	6	18330	26/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
9002	7	18331	26/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVW
9003	8	18332	26/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVO
9004	9	18333	26/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9005	10	18334	26/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9006	11	18335	26/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9007	12	18336	26/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9008	13	18337	26/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
9009	14	18338	26/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVW
9010	15	18339	26/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9011	16	18340	26/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9012	17	18341	26/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9013	18	18342	26/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKJ
9014	19	18343	26/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
9015	20	18344	26/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVW
9016	21	18345	26/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVX
9017	22	18346	26/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
9018	23	18347	26/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
9019	24	18348	26/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9020	25	18349	26/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
9021	26	18350	26/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
9022	27	18351	26/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9023	28	18352	26/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9024	1	18353	27/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
9025	2	18354	27/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
9026	3	18355	27/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
9027	4	18356	27/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVO
9028	5	18357	27/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXL
9029	6	18358	27/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
9030	7	18359	27/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXP
9031	8	18360	27/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
9032	9	18361	27/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKK
9033	10	18362	27/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
9034	11	18363	27/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
9035	12	18364	27/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
9036	13	18365	27/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
9037	14	18366	27/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
9038	15	18367	27/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
9039	16	18368	27/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKK
9040	17	18369	27/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
9041	18	18370	27/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
9042	19	18371	27/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9043	20	18372	27/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
9044	21	18373	27/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
9045	22	18374	27/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKK
9046	23	18375	27/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9047	24	18376	27/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
9048	25	18377	27/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
9049	26	18378	27/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
9050	27	18379	27/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKK
9051	28	18380	27/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
9052	29	18381	27/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
9053	30	18382	27/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
9054	31	18383	27/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9055	32	18384	27/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
9056	33	18385	27/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
9057	34	18386	27/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
9058	35	18387	27/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9059	36	18388	27/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9060	37	18389	27/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
9061	1	18390	28/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9062	2	18391	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
9063	3	18392	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
9064	4	18393	28/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXL
9065	5	18394	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
9066	6	18395	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
9067	7	18396	28/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVO
9068	8	18397	28/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
9069	9	18398	28/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXP
9070	10	18399	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9071	11	18400	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9072	12	PROVEC50658	28/10/2021	170503	3900	Hazardous	9	Maw Green	CBDU90617	MV20RKF
9073	13	PROVEC50659	28/10/2021	170503	3900	Hazardous	9	Maw Green	CBDU90617	MK21BXN
9074	14	18401	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
9075	15	18402	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
9076	16	18403	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9077	17	18404	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
9078	18	18405	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
9079	19	18406	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
9080	20	18407	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9081	21	18408	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
9082	22	18409	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
9083	23	18410	28/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9084	24	18411	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9085	25	18412	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
9086	26	18413	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
9087	27	18414	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
9088	28	18415	28/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9089	29	18416	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
9090	30	18417	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
9091	31	PROVEC50660	28/10/2021	170503	3900	Hazardous	9	Maw Green	CBDU90617	MV20RKF
9092	32	PROVEC50661	28/10/2021	170503	3900	Hazardous	9	Maw Green	CBDU90617	MK21BXN
9093	33	18418	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
9094	34	18419	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
9095	35	18420	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
9096	36	18421	28/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9097	37	18422	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
9098	38	18423	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
9099	39	18424	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
9100	40	18425	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
9101	41	18426	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9102	42	18427	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
9103	43	18428	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
9104	44	18429	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
9105	45	18430	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
9106	46	18431	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
9107	47	18432	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
9108	48	18433	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
9109	49	18434	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
9110	50	18435	28/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9111	51	18436	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
9112	52	18437	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV

9113	53	PROVEC50662	28/10/2021	170503	3900	Hazardous	9	Maw Green	CBDU90617	MV20RKF
9114	54	PROVEC50663	28/10/2021	170503	3900	Hazardous	9	Maw Green	CBDU90617	MK21BXN
9115	55	18438	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9116	56	18439	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
9117	57	18440	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
9118	58	18441	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
9119	59	18442	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
9120	60	18443	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	RV69ZVA
9121	61	18444	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
9122	62	18445	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9123	63	18446	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
9124	64	18447	28/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
9125	1	18448	29/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9126	2	18449	26/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
9127	3	18450	26/10/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
9128	4	18451	26/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
9129	5	18452	26/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
9130	6	18453	26/10/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXL
9131	7	18454	26/10/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
9132	8	18455	26/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9133	9	18456	26/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
9134	10	18457	26/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
9135	11	18458	26/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9136	12	18459	26/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9137	13	18460	26/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9138	14	18461	26/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9139	15	18462	26/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9140	16	18463	26/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9141	17	18464	26/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9142	18	18465	26/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9143	19	18466	26/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9144	20	18467	26/10/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
9145	21	18468	26/10/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
9146	22	18469	26/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
9147	23	18470	26/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9148	24	18471	26/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
9149	25	18472	26/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9150	26	18473	26/10/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
9151	27	18474	26/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9152	28	18475	26/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9153	29	18476	26/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9154	30	18477	26/10/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
9155	31	18478	26/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9156	32	18479	26/10/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
9157	33	18480	26/10/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
9158	34	18481	26/10/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVD
9159	35	18482	26/10/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	RV69ZVB
9160	36	18483	26/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9161	37	18484	26/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9162	38	18485	26/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9163	39	18486	26/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9164	40	18487	26/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9165	41	18488	26/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9166	42	18489	26/10/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
9167	43	18490	26/10/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
9168	44	18491	26/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9169	45	18492	26/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9170	46	18493	26/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9171	47	18494	26/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9172	48	18495	26/10/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
9173	49	18496	26/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
9174	50	18497	26/10/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
9175	1	18498	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9176	2	18499	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
9177	3	18500	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
9178	4	18501	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9179	5	18502	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
9180	6	18503	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
9181	7	18504	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9182	8	18505	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9183	9	18506	01/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXL
9184	10	18507	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9185	11	18508	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9186	12	18509	01/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
9187	13	18510	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9188	14	PROVEC50664	01/11/2021	170503	3900	Hazardous	9	Maw Green	CBDU90617	MK21BXN
9189	15	18511	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
9190	16	18512	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
9191	17	18513	01/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVO
9192	18	18514	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9193	19	18515	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
9194	20	18516	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
9195	21	18517	01/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXP
9196	22	18518	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXZ
9197	23	18519	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
9198	24	18520	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9199	25	18521	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9200	26	18522	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
9201	27	18523	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
9202	28	18524	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9203	29	18525	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
9204	30	18526	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9205	31	18527	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
9206	32	18528	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXZ
9207	33	18529	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9208	34	PROVEC50665	01/11/2021	170503	3900	Hazardous	9	Maw Green	CBDU90617	MK21BXN
9209	35	18530	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9210	36	18531	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
9211	37	18532	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9212	38	18533	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9213	39	18534	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
9214	40	18535	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
9215	41	18536	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
9216	42	18537	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
9217	43	18538	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9218	44	18539	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9219	45	18540	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9220	46	18541	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
9221	47	18542	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXZ
9222	48	18543	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
9223	49	18544	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9224	50	18545	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
9225	51	18546	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
9226	52	18547	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9227	53	18548	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9228	54	PROVEC50666	01/11/2021	170503	3900	Hazardous	9	Maw Green	CBDU90617	MK21BXN
9229	55	18549	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9230	56	18550	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV29RKN
9231	57	18551	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9232	58	18552	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
9233	59	18553	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
9234	60	18554	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
9235	61	18555	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXZ
9236	62	18556	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9237	63	18557	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9238	64	18558	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
9239	65	18559	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD

9240	66	18560	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9241	67	18561	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
9242	68	18562	01/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
9243	69	18563	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
9244	70	18564	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXZ
9245	71	18565	01/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9246	1	18566	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9247	2	18567	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
9248	3	18568	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9249	4	18569	02/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
9250	5	18570	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
9251	6	18571	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
9252	7	18572	02/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
9253	8	18573	02/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXZ
9254	9	18574	02/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
9255	10	18575	02/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
9256	11	18576	02/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXL
9257	12	18577	02/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
9258	13	18578	02/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9259	14	18579	02/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9260	15	18580	02/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVO
9261	16	18581	02/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXP
9262	17	18582	02/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
9263	18	18583	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9264	19	18584	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9265	20	18585	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9266	21	18586	02/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
9267	22	18587	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9268	23	18588	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
9269	24	18589	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9270	25	18590	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
9271	26	18591	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
9272	27	18592	02/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
9273	28	18593	02/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9274	29	18594	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9275	30	18595	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9276	31	18596	02/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
9277	32	18597	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9278	33	18598	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9279	34	18599	02/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
9280	35	18600	02/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
9281	36	18601	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9282	37	18602	02/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
9283	38	18603	02/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9284	39	18604	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9285	40	18605	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9286	41	18606	02/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXP
9287	42	18607	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9288	43	18608	02/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
9289	44	18609	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9290	45	18610	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9291	46	18611	02/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9292	47	18612	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9293	48	18613	02/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
9294	49	18614	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9295	50	18615	02/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
9296	51	18616	02/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
9297	52	18617	02/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
9298	53	18618	02/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBA
9299	54	18619	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9300	55	18620	02/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
9301	56	18621	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9302	57	18622	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9303	58	18623	02/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
9304	59	18624	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9305	60	18625	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9306	61	18626	02/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9307	62	18627	02/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
9308	63	18628	02/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
9309	64	18629	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9310	65	18630	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
9311	66	18631	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBA
9312	67	18632	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9313	68	18633	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9314	69	18634	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9315	70	18635	02/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9316	71	18636	02/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9317	72	18637	02/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
9318	1	18638	03/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
9319	2	18639	03/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
9320	3	18640	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
9321	4	18641	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9322	5	18642	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
9323	6	18643	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
9324	7	18644	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
9325	8	18645	03/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
9326	9	18646	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9327	10	18647	03/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXL
9328	11	18648	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9329	12	18649	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
9330	13	18650	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
9331	14	18651	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9332	15	18652	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9333	16	PROVEC50667	03/11/2021	170503	3900	Hazardous	14	Maw Green	CBDU90617	MK21BYH
9334	17	PROVEC50668	03/11/2021	170503	3900	Hazardous	14	Maw Green	CBDU90617	MK21BYL
9335	18	18653	03/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9336	19	18654	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
9337	20	18655	03/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
9338	21	18656	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
9339	22	18657	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9340	23	18658	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9341	24	18659	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
9342	25	18660	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9343	26	18661	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9344	27	18662	03/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
9345	28	18663	03/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9346	29	18664	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
9347	30	18665	03/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
9348	31	18666	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
9349	32	18667	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9350	33	18668	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9351	34	18669	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9352	35	18670	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9353	36	PROVEC50669	03/11/2021	170503	3900	Hazardous	14	Maw Green	CBDU90617	MK21BYH
9354	37	PROVEC50670	03/11/2021	170503	3900	Hazardous	14	Maw Green	CBDU90617	MK21BYL
9355	38	18671	03/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9356	39	18672	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
9357	40	18673	03/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
9358	41	18674	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
9359	42	18675	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9360	43	18676	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
9361	44	18677	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9362	45	18678	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9363	46	18679	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
9364	47	18680	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
9365	48	18681	03/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9366	49	18682	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW

9367	50	18683	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
9368	51	18684	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
9369	52	18685	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9370	53	18686	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
9371	54	18687	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9372	55	18688	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9373	56	18689	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
9374	57	18690	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
9375	58	PROVEC50671	03/11/2021	170503	3900	Hazardous	14	Maw Green	CBDU90617	MK21BYH
9376	59	18691	03/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9377	60	18692	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9378	61	18693	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
9379	62	PROVEC50672	03/11/2021	170503	3900	Hazardous	14	Maw Green	CBDU90617	MK21BYL
9380	63	18694	03/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
9381	64	18695	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9382	65	18696	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9383	66	18697	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
9384	67	18698	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
9385	68	18699	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
9386	69	18700	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9387	70	18701	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9388	71	18702	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
9389	72	18703	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
9390	73	18704	03/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9391	74	18705	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
9392	75	18706	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9393	76	18707	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
9394	77	18708	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9395	78	18709	03/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
9396	1	18710	04/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9397	2	18711	04/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
9398	3	18712	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9399	4	18713	04/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
9400	5	18714	04/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
9401	6	18715	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9402	7	18716	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
9403	8	18717	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9404	9	18718	04/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
9405	10	18719	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9406	11	18720	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
9407	12	18721	04/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9408	13	18722	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9409	14	18723	04/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
9410	15	18724	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9411	16	18725	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9412	17	18726	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
9413	18	18727	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9414	19	18728	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
9415	20	18729	04/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9416	21	18730	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
9417	22	18731	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9418	23	18732	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9419	24	18733	04/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
9420	25	18734	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
9421	26	18735	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9422	27	18736	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9423	28	18737	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
9424	29	18738	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
9425	30	18739	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
9426	31	18740	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
9427	32	18741	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9428	33	18742	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9429	34	18743	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
9430	35	18744	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
9431	36	18745	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9432	37	18746	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
9433	38	18747	04/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9434	39	18748	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
9435	40	18749	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9436	41	18750	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9437	42	18751	04/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
9438	43	18752	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9439	44	18753	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9440	45	18754	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
9441	46	18755	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
9442	47	18756	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9443	48	18757	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
9444	49	18758	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
9445	50	18759	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
9446	51	18760	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9447	52	18761	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
9448	53	18762	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
9449	54	18763	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9450	55	18764	04/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9451	56	18765	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9452	57	18766	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9453	58	18767	04/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
9454	59	18768	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
9455	60	18769	04/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXU
9456	61	18770	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9457	62	18771	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9458	63	18772	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
9459	64	18773	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
9460	65	18774	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9461	66	18775	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
9462	67	18776	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9463	68	18777	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9464	69	18778	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9465	70	18779	04/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9466	71	18780	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9467	72	18781	04/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
9468	73	18782	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
9469	74	18783	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9470	75	18784	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9471	76	18785	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9472	77	18786	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
9473	78	18787	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9474	79	18788	04/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9475	1	18789	05/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
9476	2	18790	05/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXL
9477	3	18791	05/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
9478	4	18792	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
9479	5	18793	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9480	6	18794	05/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9481	7	18795	05/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
9482	8	18796	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9483	9	18797	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
9484	10	18798	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9485	11	18799	05/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
9486	12	18800	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9487	13	18801	05/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9488	14	18802	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9489	15	18803	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
9490	16	18804	05/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
9491	17	18805	05/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
9492	18	18806	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
9493	19	18807	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW

9494	20	18808	05/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9495	21	18809	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
9496	22	18810	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9497	23	18811	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9498	24	18812	05/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9499	25	18813	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9500	26	18814	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
9501	27	18815	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9502	28	18816	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
9503	29	18817	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
9504	30	18818	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9505	31	18819	05/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
9506	32	18820	05/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
9507	33	18821	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
9508	34	18822	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9509	35	18823	05/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9510	36	18824	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
9511	37	18825	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
9512	38	18826	05/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9513	39	18827	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9514	40	18828	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9515	41	18829	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9516	42	18830	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
9517	43	18831	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
9518	44	18832	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9519	45	18833	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
9520	46	18834	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
9521	47	18835	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9522	48	18836	05/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
9523	49	18837	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
9524	50	18838	05/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
9525	51	18839	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
9526	52	18840	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9527	53	18841	05/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9528	54	18842	05/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9529	55	18843	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
9530	56	18844	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9531	57	18845	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9532	58	18846	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
9533	59	18847	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9534	60	18848	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9535	61	18849	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
9536	62	18850	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9537	63	18851	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
9538	64	18852	05/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
9539	65	18853	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9540	66	18854	05/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
9541	67	18855	05/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9542	68	18856	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9543	69	18857	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
9544	70	18858	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9545	71	18859	05/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9546	72	18860	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9547	73	18861	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
9548	74	18862	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9549	75	18863	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9550	76	18864	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9551	77	18865	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
9552	78	18866	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9553	79	18867	05/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
9554	80	18868	05/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9555	81	18869	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
9556	82	18870	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9557	83	18871	05/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9558	84	18872	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
9559	85	18873	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9560	86	18874	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9561	87	18875	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
9562	88	18876	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9563	89	18877	05/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
9564	1	18878	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
9565	2	18879	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
9566	3	18880	08/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
9567	4	18881	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXZ
9568	5	18882	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
9569	6	18883	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9570	7	18884	08/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
9571	8	18885	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9572	9	18886	08/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXL
9573	10	18887	08/11/2021	170504	3900	Non-haz soils & stones	0	Fletcher Bank	CBDU90617	MV20RKK
9574	11	18888	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9575	12	18889	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
9576	13	18890	08/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
9577	14	18891	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
9578	15	18892	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
9579	16	18893	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
9580	17	18894	08/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9581	18	18895	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
9582	19	18896	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
9583	20	18897	08/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9584	21	18898	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9585	22	18899	08/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
9586	23	18900	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
9587	24	18901	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9588	25	18902	08/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
9589	26	18903	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9590	27	18904	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9591	28	18905	08/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9592	29	18906	08/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9593	30	18907	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
9594	31	18908	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9595	32	18909	08/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
9596	33	18910	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
9597	34	18911	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9598	35	18912	08/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
9599	36	18913	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9600	37	18914	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9601	38	18915	08/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9602	39	18916	08/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9603	40	18917	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9604	41	18918	08/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
9605	42	18919	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
9606	43	18920	08/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
9607	44	18921	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9608	45	18922	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9609	46	18923	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9610	47	18924	08/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9611	48	18925	08/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9612	49	18926	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9613	50	18927	08/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
9614	51	18928	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
9615	52	18929	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9616	53	18930	08/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
9617	54	18931	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9618	55	18932	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9619	56	18933	08/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9620	57	18934	08/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT

9621	58	18935	08/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
9622	59	18936	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9623	60	18937	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9624	61	18938	08/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
9625	62	18939	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9626	63	18940	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9627	64	18941	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
9628	65	18942	08/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
9629	66	18943	08/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9630	67	18944	08/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9631	68	18945	08/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
9632	69	18946	08/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9633	1	18947	09/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9634	2	18948	09/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
9635	3	18949	09/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
9636	4	18950	09/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
9637	5	18951	09/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
9638	6	18952	09/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXU
9639	7	18953	09/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
9640	8	18954	09/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9641	9	18955	09/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
9642	10	18956	09/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
9643	11	18957	09/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9644	12	18958	09/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
9645	13	18959	09/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9646	14	18960	09/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
9647	15	18961	09/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
9648	16	18962	09/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9649	17	18963	09/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
9650	18	18964	09/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9651	19	18965	09/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9652	20	18966	09/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
9653	21	18967	09/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9654	22	18968	09/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9655	23	18969	09/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9656	24	18970	09/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9657	25	18971	09/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
9658	26	18972	09/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
9659	27	18973	09/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
9660	28	18974	09/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
9660	29	18975	09/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
9660	30	18976	09/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9660	31	18977	09/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9660	32	18978	09/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9660	33	18979	09/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9660	34	18980	09/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
9660	35	18981	09/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
9660	36	18982	09/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
9660	37	18983	09/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9660	38	18984	09/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9661	39	18985	09/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9662	40	18986	09/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9663	41	18987	09/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXL
9664	42	18988	09/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9665	43	18989	09/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
9666	44	18990	09/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9667	45	18991	09/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
9668	46	18992	09/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
9669	47	18993	09/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
9670	48	18994	09/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9671	49	18995	09/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9672	50	18996	09/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9673	51	18997	09/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXL
9674	52	18998	09/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
9675	53	18999	09/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9676	54	19000	09/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
9677	55	19001	09/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
9678	1	19002	10/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
9679	2	19003	10/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9680	3	19004	10/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVW
9681	4	19005	10/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
9682	5	19006	10/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXU
9683	6	19007	10/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
9684	7	19008	10/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
9685	8	19009	10/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
9686	9	19010	10/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKN
9687	10	19011	10/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
9688	11	19012	10/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
9689	12	19013	10/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
9690	13	19014	10/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
9691	14	19015	10/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9692	15	19016	10/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
9693	16	19017	10/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXL
9694	17	19018	10/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
9695	18	19019	10/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9696	19	19020	10/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9697	20	19021	10/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKK
9698	21	19022	10/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9699	22	19023	10/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9700	23	19024	10/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9701	24	19025	10/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
9702	25	19026	10/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVW
9703	26	19027	10/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9704	27	19028	10/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
9705	28	19029	10/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKN
9706	29	19030	10/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21CHF
9707	30	19031	10/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9708	31	19032	10/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
9709	32	19033	10/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
9710	33	19034	10/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
9711	34	19035	10/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKK
9712	35	19036	10/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9713	36	19037	10/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9714	37	19038	10/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
9715	38	19039	10/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVW
9716	39	19040	10/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9717	40	19041	10/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
9718	41	19042	10/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKN
9719	42	19043	10/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9720	43	19044	10/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9721	44	19045	10/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
9722	45	19046	10/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
9723	46	19047	10/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
9724	47	19048	10/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21CHF
9725	48	19049	10/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKK
9726	49	19050	10/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVW
9727	50	19051	10/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
9728	51	19052	10/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9729	52	19053	10/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9730	53	19054	10/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9731	54	19055	10/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKN
9732	55	19056	10/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9733	56	19057	10/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
9734	57	19058	10/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
9735	58	19059	10/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
9736	59	19060	10/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
9737	60	19061	10/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT

9738	61	19062	10/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9739	62	19063	10/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
9740	63	19064	10/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9741	64	19065	10/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9742	65	19066	10/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9743	66	19067	10/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
9744	67	19068	10/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
9745	68	19069	10/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
9746	1	19070	11/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
9747	2	19071	11/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9748	3	19072	11/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21CHF
9749	4	19073	11/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
9750	5	19074	11/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
9751	6	19075	11/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
9752	7	19076	11/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9753	8	19077	11/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9754	9	19078	11/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9755	10	19079	11/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
9756	11	19080	11/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
9757	12	19081	11/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
9758	13	19082	11/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9759	14	19083	11/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9760	15	19084	11/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9761	16	19085	11/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
9762	17	19086	11/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
9763	18	19087	11/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
9764	19	19088	11/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21CHF
9765	20	19089	11/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
9766	21	19090	11/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
9767	22	19091	11/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9768	23	19092	11/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9769	24	19093	11/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9770	25	19094	11/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
9771	26	19095	11/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
9772	27	19096	11/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
9773	28	19097	11/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
9774	29	19098	11/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9775	30	19099	11/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
9776	31	19100	11/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9777	32	19101	11/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21CHF
9778	33	19102	11/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
9779	34	19103	11/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9780	35	19104	11/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
9781	36	19105	11/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
9782	37	19106	11/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
9783	38	19107	11/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9784	39	19108	11/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9785	40	19109	11/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
9786	41	19110	11/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9787	42	19111	11/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
9788	43	19112	11/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9789	44	19113	11/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9790	45	19114	11/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
9791	46	19115	11/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9792	47	19116	11/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9793	48	19117	11/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
9794	1	19118	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9795	2	19119	12/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21CHF
9796	3	19120	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
9797	4	19121	12/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
9798	5	19122	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9799	6	19123	12/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
9800	7	19124	12/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9801	8	19125	12/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21CHG
9802	9	19126	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
9803	10	19127	12/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKN
9804	11	19128	12/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
9805	12	19129	12/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
9806	13	19130	12/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXL
9807	14	19131	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
9808	15	19132	12/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9809	16	19133	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9810	17	19134	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9811	18	19135	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9812	19	19136	12/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9813	20	19137	12/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXY
9814	21	19138	12/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
9815	22	19139	12/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
9816	23	19140	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9817	24	19141	12/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
9818	25	19142	12/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9819	26	19143	12/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
9820	27	19144	12/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
9821	28	19145	12/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
9822	29	19146	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9823	30	19147	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9824	31	19148	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9825	32	19149	12/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21CHF
9826	33	19150	12/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9827	34	19151	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9828	35	19152	12/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
9829	36	19153	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9830	37	19154	12/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
9831	38	19155	12/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
9832	39	19156	12/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
9833	40	19157	12/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
9834	41	19158	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9835	42	19159	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9836	43	19160	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9837	44	19161	12/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21CHF
9838	45	19162	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
9839	46	19163	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
9840	47	19164	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9841	48	19165	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
9842	49	19166	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9843	50	19167	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9844	51	19168	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9845	52	19169	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9846	53	19170	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
9847	54	19171	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9848	55	19172	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
9849	56	19173	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9850	57	19174	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9851	58	19175	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
9852	59	19176	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9853	60	19177	12/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
9854	61	19178	12/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
9855	1	19179	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
9856	2	19180	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9857	3	19181	15/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXU
9858	4	19182	15/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
9859	5	19183	15/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
9860	6	19184	15/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXZ
9861	7	19185	15/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21CHG
9862	8	19186	15/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVZ
9863	9	19187	15/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXL
9864	10	19188	15/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKN

9865	11	19189	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9866	12	19190	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
9867	13	19191	15/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
9868	14	19192	15/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9869	15	19193	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
9870	16	19194	15/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
9871	17	19195	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9872	18	19196	15/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
9873	19	19197	15/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
9874	20	19198	15/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
9875	21	19199	15/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
9876	22	19200	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9877	23	19201	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
9878	24	19202	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9879	25	19203	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
9880	26	19204	15/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9881	27	19205	15/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
9882	28	19206	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
9883	29	19207	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9884	30	19208	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9885	31	19209	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9886	32	19210	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
9887	33	19211	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9888	34	19212	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
9889	35	19213	15/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9890	36	19214	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
9891	37	19215	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9892	38	19216	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9893	39	19217	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9894	40	19218	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
9895	41	19219	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9896	42	19220	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
9897	43	19221	15/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9898	44	19222	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
9899	45	19223	15/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
9900	46	19224	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9901	47	19225	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9902	48	19226	15/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
9903	49	19227	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9904	50	19228	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
9905	51	19229	15/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
9906	52	19230	15/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9907	53	19231	15/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9908	54	19232	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9909	55	19233	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9910	56	19234	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9911	57	19235	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9912	58	19236	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
9913	59	19237	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9914	60	19238	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9915	61	19239	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9916	62	19240	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
9917	63	19241	15/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
9918	1	19242	16/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
9919	2	19243	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9920	3	19244	16/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
9921	4	19245	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9922	5	19246	16/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
9923	6	19247	16/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXZ
9924	7	19248	16/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
9925	8	19249	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
9926	9	19250	16/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9927	10	19251	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9928	11	19252	16/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
9929	12	19253	16/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
9930	13	19254	16/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
9931	14	19255	16/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXV
9932	15	19256	16/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
9933	16	19257	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
9934	17	19258	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9935	18	19259	16/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
9936	19	19260	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9937	20	19261	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9938	21	19262	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
9939	22	19263	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9940	23	19264	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9941	24	19265	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
9942	25	19266	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9943	26	19267	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
9944	27	19268	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9945	28	19269	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
9946	29	19270	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
9947	30	19271	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9948	31	19272	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9949	32	19273	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9950	33	19274	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
9951	34	19275	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9952	35	19276	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
9953	36	19277	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
9954	37	19278	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9955	38	19279	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9956	39	19280	16/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
9957	40	19281	16/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
9958	41	19282	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9959	42	19283	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9960	43	19284	16/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
9961	44	19285	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9962	45	19286	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
9963	46	19287	16/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
9964	47	19288	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
9965	48	19289	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9966	49	19290	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
9967	50	19291	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9968	51	19292	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
9969	52	19293	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
9970	53	19294	16/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9971	1	19295	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
9972	2	19296	17/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXZ
9973	3	19297	17/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
9974	4	19298	17/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21CHF
9975	5	19299	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9976	6	19300	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
9977	7	19301	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9978	8	19302	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9979	9	19303	17/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
9980	10	19304	17/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
9981	11	19305	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9982	12	19306	17/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXV
9983	13	19307	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
9984	14	19308	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
9985	15	19309	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9986	16	19310	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9987	17	19311	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9988	18	19312	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9989	19	19313	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
9990	20	19314	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
9991	21	19315	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA

9992	22	19316	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9993	23	19317	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
9994	24	19318	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
9995	25	19319	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
9996	26	19320	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
9997	27	19321	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
9998	28	19322	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
9999	29	19323	17/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
10000	30	19324	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
10001	31	19325	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
10002	32	19326	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
10003	33	19327	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
10004	34	19328	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10005	35	19329	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
10006	36	19330	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
10007	37	19331	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
10008	38	19332	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
10009	39	19333	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
10010	40	19334	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10011	41	19335	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
10012	42	19336	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
10013	43	19337	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
10014	44	19338	17/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
10015	1	19339	18/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
10016	2	19340	18/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
10017	3	19341	18/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10018	4	19342	18/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
10019	5	19343	18/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
10020	6	19344	18/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
10021	7	19345	18/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
10022	8	19346	18/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
10023	9	19347	18/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
10024	10	19348	18/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
10025	11	19349	18/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
10026	12	19350	18/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
10027	13	19351	18/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
10028	14	19352	18/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
10029	15	19353	18/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
10030	16	19354	18/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
10031	17	19355	18/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
10032	18	19356	18/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10033	19	19357	18/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
10034	20	19358	18/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
10035	21	19359	18/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
10036	22	19360	18/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
10037	23	19361	18/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
10038	24	19362	18/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
10039	25	19363	18/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10040	26	19364	18/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
10041	27	19365	18/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
10042	28	19366	18/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
10043	29	19367	18/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
10044	30	19368	18/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
10045	31	19369	18/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
10046	32	19370	18/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10047	33	19371	18/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
10048	34	19372	18/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
10049	35	19373	18/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
10050	36	19374	18/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
10051	37	19375	18/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
10052	38	19376	18/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
10053	39	19377	18/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10054	40	19378	18/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
10055	41	19379	18/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
10056	42	19380	18/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
10057	43	19381	18/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
10058	44	19382	18/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
10059	45	19383	18/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
10060	46	19384	18/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
10061	47	19385	18/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10062	48	19386	18/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
10063	49	19387	18/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
10064	50	19388	18/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
10065	51	19389	18/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
10066	1	19390	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
10067	2	19391	19/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10068	3	19392	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
10069	4	19393	19/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXU
10070	5	19394	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
10071	6	19395	19/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXZ
10072	7	19396	19/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXO
10073	8	19397	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
10074	9	19398	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
10075	10	19399	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
10076	11	19400	19/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXL
10077	12	19401	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
10078	13	19402	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
10079	14	19403	19/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
10080	15	19404	19/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
10081	16	19405	19/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
10082	17	19406	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
10083	18	19407	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
10084	19	19408	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
10085	20	19409	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
10086	21	19410	19/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
10087	22	19411	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
10088	23	19412	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
10089	24	19413	19/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10090	25	19414	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
10091	26	19415	19/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
10092	27	19416	19/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
10093	28	19417	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
10094	29	19418	19/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
10095	30	19419	19/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
10096	31	19420	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
10097	32	19421	19/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10098	33	19422	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
10099	34	19423	19/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
10100	35	19424	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
10101	36	19425	19/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
10102	37	19426	19/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
10103	38	19427	19/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
10104	39	19428	19/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10105	40	19429	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
10106	41	19430	19/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
10107	42	19431	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
10108	43	19432	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
10109	44	19433	19/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
10110	45	19434	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
10111	46	19435	19/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
10112	47	19436	19/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
10113	48	19437	19/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10114	49	19438	19/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
10115	50	19439	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
10116	51	19440	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
10117	52	19441	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
10118	53	19442	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP

10119	54	19443	19/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
10120	55	19444	19/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
10121	56	19445	19/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10122	57	19446	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
10123	58	19447	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
10124	59	19448	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
10125	60	19449	19/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
10126	61	19450	19/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
10127	62	19451	19/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
10128	1	19452	22/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVU
10129	2	19453	22/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXU
10130	3	19454	22/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
10131	4	19455	22/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
10132	5	19456	22/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
10133	6	19457	22/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10134	7	19458	22/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKN
10135	8	19459	22/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
10136	9	19460	22/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
10137	10	19461	22/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
10138	11	19462	22/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21CHF
10139	12	19463	22/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
10140	13	19464	22/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXM
10141	14	19465	22/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
10142	15	19466	22/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
10143	16	19467	22/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
10144	17	19468	22/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
10145	18	19469	22/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
10146	19	19470	22/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
10147	20	19471	22/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
10148	21	19472	22/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
10149	22	19473	22/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
10150	23	19474	22/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
10151	24	19475	22/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
10152	25	19476	22/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
10153	26	19477	22/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
10154	27	19478	22/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
10155	28	19479	22/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
10156	29	19480	22/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
10157	30	19481	22/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
10158	31	19482	22/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
10159	32	19483	22/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
10160	33	19484	22/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
10161	34	19485	22/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10162	35	19486	22/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
10163	36	19487	22/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
10164	37	19488	22/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
10165	38	19489	22/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
10166	39	19490	22/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
10167	40	19491	22/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
10168	41	19492	22/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10169	42	19493	22/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
10170	43	19494	22/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
10171	44	19495	22/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
10172	45	19496	22/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
10173	46	19497	22/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
10174	47	19498	22/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
10175	48	19499	22/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
10176	49	19500	22/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
10177	50	19501	22/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
10178	51	19502	22/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10179	52	19503	22/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
10180	53	19504	22/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
10181	54	19505	22/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
10182	55	19506	22/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
10183	56	19507	22/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
10184	57	19508	22/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
10185	58	19509	22/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
10186	59	19510	22/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
10187	60	19511	22/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
10188	61	19512	22/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
10189	62	19513	22/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
10190	63	19514	22/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
10191	64	19515	22/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
10192	65	19516	22/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
10193	66	19517	22/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVA
10194	67	19518	22/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
10195	68	19519	22/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
10196	69	19520	22/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVO
10197	70	19521	22/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21CHG
10198	71	19522	22/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
10199	72	19523	22/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
10200	73	19524	22/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
10201	74	19525	22/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
10202	75	19526	22/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
10203	76	19527	22/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
10204	77	19528	22/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXL
10205	78	19529	22/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10206	1	19530	23/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10207	2	19531	23/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
10208	3	19532	23/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXO
10209	4	19533	23/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
10210	5	19534	23/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXZ
10211	6	19535	23/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
10212	7	19536	23/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXU
10213	8	19537	23/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
10214	9	19538	23/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
10215	10	19539	23/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
10216	11	19540	23/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
10217	12	19541	23/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
10218	13	19542	23/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
10219	14	19543	23/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
10220	15	19544	23/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
10221	16	19545	23/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
10222	17	19546	23/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
10223	18	19547	23/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
10224	19	19548	23/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVZ
10225	20	19549	23/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
10226	21	19550	23/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
10227	22	19551	23/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
10228	23	19552	23/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10229	24	19553	23/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
10230	25	19554	23/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
10231	26	19555	23/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
10232	27	19556	23/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
10233	28	19557	23/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
10234	29	19558	23/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
10235	30	19559	23/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
10236	31	19560	23/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
10237	32	19561	23/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
10238	33	19562	23/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10239	34	19563	23/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
10240	35	19564	23/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
10241	36	19565	23/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
10242	37	19566	23/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
10243	38	19567	23/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
10244	39	19568	23/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
10245	40	19569	23/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY

10246	41	19570	23/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
10247	42	19571	23/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
10248	43	19572	23/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
10249	44	19573	23/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
10250	45	19574	23/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
10251	46	19575	23/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
10252	47	19576	23/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
10253	48	19577	23/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
10254	49	19578	23/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
10255	50	19579	23/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
10256	51	19580	23/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
10257	52	19581	23/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
10258	53	19582	23/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
10259	54	19583	23/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVO
10260	55	19584	23/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
10261	56	19585	23/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
10262	57	19586	23/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
10263	1	19587	24/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10264	2	19588	24/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXU
10265	3	19589	24/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXZ
10266	4	19590	24/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
10267	5	19591	24/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
10268	6	19592	24/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
10269	7	19593	24/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXL
10270	8	19594	24/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
10271	9	19595	24/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXM
10272	10	19596	24/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
10273	11	19597	24/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
10274	12	19598	24/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKF
10275	13	19599	24/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
10276	14	19600	24/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
10277	15	19601	24/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
10278	16	19602	24/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
10279	17	19603	24/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXO
10280	18	19604	24/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
10281	19	19605	24/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
10282	20	19606	24/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10283	21	19607	24/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
10284	22	19608	24/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
10285	23	19609	24/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
10286	24	19610	24/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVO
10287	25	19611	24/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
10288	26	19612	24/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
10289	27	19613	24/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
10290	28	19614	24/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10291	29	19615	24/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
10292	30	19616	24/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
10293	31	19617	24/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
10294	32	19618	24/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
10295	33	19619	24/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
10296	34	19620	24/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVA
10297	35	19621	24/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
10298	36	19622	24/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
10299	37	19623	24/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
10300	38	19624	24/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
10301	39	19625	24/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
10302	40	19626	24/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVO
10303	41	19627	24/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
10304	42	19628	24/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
10305	43	19629	24/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVA
10306	44	19630	24/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
10307	45	19631	24/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
10308	46	19632	24/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
10309	47	19633	24/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
10310	48	19634	24/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
10311	49	19635	24/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
10312	50	19636	24/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	M21BYH
10313	51	19637	24/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVA
10314	52	19638	24/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
10315	53	19639	24/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVV
10316	54	19640	24/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
10317	55	19641	24/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
10318	56	19642	24/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
10319	57	19643	24/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
10320	58	19644	24/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVO
10321	1	19645	25/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10322	2	19646	25/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
10323	3	19647	25/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXU
10324	4	19648	25/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXL
10325	5	19649	25/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
10326	6	19650	25/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
10327	7	19651	25/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
10328	8	19652	25/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
10329	9	19653	25/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
10330	10	19654	25/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
10331	11	19655	25/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
10332	12	19656	25/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
10333	13	19657	25/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
10334	14	19658	25/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
10335	15	19659	25/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
10336	16	19660	25/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
10337	17	19661	25/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
10338	18	19662	25/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
10339	19	19663	25/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10340	20	19664	25/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
10341	21	19665	25/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
10342	22	19666	25/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
10343	23	19667	25/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
10344	24	19668	25/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
10345	25	19669	25/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
10346	26	19670	25/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
10347	27	19671	25/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
10348	28	19672	25/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
10349	29	19673	25/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
10350	30	19674	25/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX21ORT
10351	31	19675	25/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10352	32	19676	25/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
10353	33	19677	25/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
10354	34	19678	25/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
10355	35	19679	25/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
10356	36	19680	25/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
10357	37	19681	25/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
10358	38	19682	25/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
10359	39	19683	25/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10360	40	19684	25/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVO
10361	41	19685	25/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
10362	42	19686	25/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
10363	43	19687	25/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX21ORT
10364	44	19688	25/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
10365	45	19689	25/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
10366	46	19690	25/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXX
10367	47	19691	25/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
10368	48	19692	25/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
10369	49	19693	25/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
10370	50	19694	25/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10371	51	19695	25/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
10372	52	19696	25/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX21ORT

10373	53	19697	25/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
10374	54	19698	25/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
10375	55	19699	25/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXL
10376	56	19700	25/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
10377	57	19701	25/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
10378	58	19702	25/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXM
10379	59	19703	25/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVA
10380	60	19704	25/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
10381	61	19705	25/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
10382	62	19706	25/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
10383	63	19707	25/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV69KTT
10384	64	19708	25/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21CHF
10385	65	19709	25/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
10386	66	19710	25/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MX21ORT
10387	67	19711	25/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
10388	68	19712	25/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVO
10389	69	19713	25/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
10390	70	19714	25/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
10391	71	19715	25/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
10392	72	19716	25/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
10393	73	19717	25/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXM
10394	74	19718	25/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
10395	75	19719	25/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
10396	76	19720	25/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10397	77	19721	25/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX21ORT
10398	1	19722	26/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
10399	2	19723	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
10400	3	19724	26/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVA
10401	4	19725	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
10402	5	19726	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
10403	6	19727	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
10404	7	19728	26/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
10405	8	19729	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
10406	9	19730	26/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
10407	10	19731	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
10408	11	19732	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
10409	12	19733	26/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
10410	13	19734	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
10411	14	19735	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
10412	15	19736	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
10413	16	19737	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
10414	17	19738	26/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
10415	18	19739	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
10416	19	19740	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
10417	20	19741	26/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
10418	21	19742	26/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
10419	22	19743	26/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
10420	23	19744	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
10421	24	19745	26/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
10422	25	19746	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
10423	26	19747	26/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
10424	27	19748	26/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVO
10425	28	19749	26/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
10426	29	19750	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
10427	30	19751	26/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
10428	31	19752	26/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVZ
10429	32	19753	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
10430	33	19754	26/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
10431	34	19755	26/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
10432	35	19756	26/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXV
10433	36	19757	26/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVW
10434	37	19758	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
10435	38	19759	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
10436	39	19760	26/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
10437	40	19761	26/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
10438	41	19762	26/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
10439	42	19763	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
10440	43	19764	26/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
10441	44	19765	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
10442	45	19766	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
10443	46	19767	26/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
10444	47	19768	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
10445	48	19769	26/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
10446	49	19770	26/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
10447	50	19771	26/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
10448	51	19772	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BVX
10449	52	19773	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
10450	53	19774	26/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
10451	54	19775	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
10452	55	19776	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
10453	56	19777	26/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVX
10454	57	19778	26/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
10455	58	19779	26/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
10456	59	19780	26/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
10457	60	19781	26/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
10458	61	19782	26/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
10459	62	19783	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
10460	63	19784	26/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
10461	64	19785	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
10462	65	19786	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXM
10463	66	19787	26/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVW
10464	67	19788	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
10465	68	19789	26/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXM
10466	69	19790	26/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
10467	70	19791	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
10468	71	19792	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
10469	72	19793	26/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
10470	73	19794	26/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
10471	74	19795	26/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXV
10472	75	19796	26/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX21ORT
10473	76	19797	26/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
10474	77	19798	26/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
10475	78	19799	26/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
10476	79	19800	26/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVW
10477	80	19801	26/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
10478	81	19802	26/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
10479	82	19803	26/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVX
10480	83	19804	26/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
10481	84	19805	26/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
10482	85	19806	26/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
10483	1	19807	29/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
10484	2	19808	29/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
10485	3	19809	29/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
10486	4	19810	29/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKN
10487	5	19811	29/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXV
10488	6	19812	29/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
10489	7	19813	29/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
10490	8	19814	29/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVV
10491	9	19815	29/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
10492	10	19816	29/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
10493	11	19817	29/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
10494	12	19818	29/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
10495	13	19819	29/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
10496	14	19820	29/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
10497	15	19821	29/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
10498	16	19822	29/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXP
10499	17	19823	29/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN

10500	18	19824	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXU
10501	19	19825	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXZ
10502	20	19826	29/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXO
10503	21	19827	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
10504	22	19828	29/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXV
10505	23	19829	29/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
10506	24	19830	29/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKN
10507	25	19831	29/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
10508	26	19832	29/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
10509	27	19833	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVW
10510	28	19834	29/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
10511	29	19835	29/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
10512	30	19836	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
10513	31	19837	29/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
10514	32	19838	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
10515	33	19839	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
10516	34	19840	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXU
10517	35	19841	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXZ
10518	36	19842	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
10519	37	19843	29/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
10520	38	19844	29/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
10521	39	19845	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVW
10522	40	19846	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
10523	41	19847	29/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
10524	42	19848	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
10525	43	19849	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
10526	44	19850	29/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXV
10527	45	19851	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
10528	46	19852	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXU
10529	47	19853	29/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
10530	48	19854	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXM
10531	49	19855	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
10532	50	19856	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXZ
10533	51	19857	29/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
10534	52	19858	29/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
10535	53	19859	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
10536	54	19860	29/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
10537	55	19861	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
10538	56	19862	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
10539	57	19863	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXU
10540	58	19864	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
10541	59	19865	29/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
10542	60	19866	29/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXZ
10543	61	19867	29/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
10544	62	19868	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
10545	63	19869	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
10546	64	19870	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXM
10547	65	19871	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXU
10548	66	19872	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
10549	67	19873	29/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
10550	68	19874	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
10551	69	19875	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVZ
10552	70	19876	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXZ
10553	71	19877	29/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
10554	72	19878	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
10555	73	19879	29/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
10556	74	19880	29/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
10557	75	19881	29/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
10558	76	19882	29/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
10559	1	19883	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVW
10560	2	19884	30/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
10561	3	19885	30/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
10562	4	19886	30/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
10563	5	19887	30/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
10564	6	19888	30/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHG
10565	7	19889	30/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
10566	8	19890	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
10567	9	19891	30/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKF
10568	10	19892	30/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
10569	11	19893	30/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVB
10570	12	19894	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
10571	13	19895	30/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
10572	14	19896	30/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
10573	15	19897	30/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
10574	16	19898	30/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
10575	17	19899	30/11/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
10576	18	19900	30/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
10577	19	19901	30/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
10578	20	19902	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
10579	21	19903	30/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
10580	22	19904	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVW
10581	23	19905	30/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
10582	24	19906	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
10583	25	19907	30/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
10584	26	19908	30/11/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
10585	27	19909	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
10586	28	19910	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
10587	29	19911	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVX
10588	30	19912	30/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
10589	31	19913	30/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
10590	32	19914	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
10591	33	19915	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXV
10592	34	19916	30/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
10593	35	19917	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVW
10594	36	19918	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21CHG
10595	37	19919	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
10596	38	19920	30/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
10597	39	19921	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXZ
10598	40	19922	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
10599	41	19923	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
10600	42	19924	30/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
10601	43	19925	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
10602	44	19926	30/11/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
10603	45	19927	30/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
10604	46	19928	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVX
10605	47	19929	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVZ
10606	48	19930	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
10607	49	19931	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
10608	50	19932	30/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
10609	51	19933	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXV
10610	52	19934	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVW
10611	53	19935	30/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
10612	54	19936	30/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
10613	55	19937	30/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
10614	56	19938	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVZ
10615	57	19939	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
10616	58	19940	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
10617	59	19941	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
10618	60	19942	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
10619	61	19943	30/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
10620	62	19944	30/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
10621	63	19945	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
10622	64	19946	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
10623	65	19947	30/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
10624	66	19948	30/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
10625	67	19949	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXV
10626	68	19950	30/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC

10627	69	19951	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVW
10628	70	19952	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKK
10629	71	19953	30/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
10630	72	19954	30/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
10631	73	19955	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXW
10632	74	19956	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
10633	75	19957	30/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
10634	76	19958	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXN
10635	77	19959	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXU
10636	78	19960	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RLY
10637	79	19961	30/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
10638	80	19962	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXV
10639	81	19963	30/11/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVZ
10640	82	19964	30/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
10641	83	19965	30/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
10642	84	19966	30/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVB
10643	85	19967	30/11/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
10644	86	19968	30/11/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10645	1	19969	01/12/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10646	2	19970	01/12/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYH
10647	3	19971	01/12/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
10648	4	19972	01/12/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
10649	5	19973	01/12/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
10650	6	19974	01/12/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
10651	7	19975	01/12/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
10652	8	19976	01/12/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
10653	9	19977	01/12/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVC
10654	10	19978	01/12/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKN
10655	11	19979	01/12/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVD
10656	12	19980	01/12/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
10657	13	19981	01/12/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK2BXN
10658	14	19982	01/12/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVU
10659	15	19983	01/12/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
10660	16	19984	01/12/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
10661	17	19985	01/12/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXM
10662	18	19986	01/12/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXP
10663	19	19987	01/12/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
10664	20	19988	01/12/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXL
10665	21	19989	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVA
10666	22	19990	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
10667	23	19991	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
10668	24	19992	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
10669	25	19993	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
10670	26	19994	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
10671	27	19995	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
10672	28	19996	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVA
10673	29	19997	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
10674	30	19998	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
10675	31	19999	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
10676	32	20000	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
10677	33	20001	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
10678	34	20002	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
10679	35	20003	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVA
10680	36	20004	01/12/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BYH
10681	37	20005	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
10682	38	20006	01/12/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVX
10683	39	20007	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
10684	40	20008	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
10685	41	20009	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
10686	42	20010	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
10687	43	20011	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVA
10688	44	20012	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
10689	45	20013	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
10690	46	20014	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
10691	47	20015	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
10692	48	20016	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
10693	49	20017	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
10694	50	20018	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYH
10695	51	20019	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBB
10696	52	20020	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYJ
10697	53	20021	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MK21BYL
10698	54	20022	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVC
10699	55	20023	01/12/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10700	56	20024	01/12/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXL
10701	57	20025	01/12/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVZ
10702	58	20026	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV19UBA
10703	59	20027	01/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	RV69ZVD
10704	60	20028	01/12/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
10705	61	20029	01/12/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVX
10706	1	20030	02/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
10707	2	20031	02/12/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXO
10708	3	20032	02/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
10709	4	20033	02/12/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
10710	5	20034	02/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
10711	6	20035	02/12/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKN
10712	7	20036	02/12/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXW
10713	8	20037	02/12/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
10714	9	20038	02/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
10715	10	20039	02/12/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
10716	11	20040	02/12/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
10717	12	20041	02/12/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
10718	13	20042	02/12/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXP
10719	14	20043	02/12/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RLY
10720	15	20044	02/12/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
10721	16	20045	02/12/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVZ
10722	17	20046	02/12/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXN
10723	18	20047	02/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
10724	19	20048	02/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
10725	20	20049	02/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
10726	21	20050	02/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
10727	22	20051	02/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
10728	23	20052	02/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
10729	24	20053	02/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
10730	25	20054	02/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
10731	26	20055	02/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
10732	27	20056	02/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
10733	28	20057	02/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
10733	29	20058	02/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
10733	30	20059	02/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
10733	31	20060	02/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
10733	32	20061	02/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
10734	33	20062	02/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
10735	34	20063	02/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
10736	35	20064	02/12/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYL
10737	36	20065	02/12/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MV19UBB
10738	37	20066	02/12/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	MK21BYJ
10739	38	20067	02/12/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKF
10740	39	20068	02/12/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKJ
10741	40	20069	02/12/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MK21BXX
10742	41	20070	02/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MV69KTT
10743	42	20071	02/12/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVO
10744	43	20072	02/12/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MV20RKN
10745	44	20073	02/12/2021	170504	3900	Non-haz soils & stones	9	Woolston	CBDU90617	MT21TVV
10746	45	20074	02/12/2021	170504	3900	Non-haz soils & stones	14	Woolston	CBDU90617	MX21ORT
10747	46	20075	02/12/2021	170504	3900	Non-haz soils & stones	14	Fletcher Bank	CBDU90617	RV69ZVA
10748	1	20076	03/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
10749	2	20077	03/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB

10750	3	20078	03/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
10751	4	20079	03/12/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVW
10752	5	20080	03/12/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXZ
10753	6	20081	03/12/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MV20RKN
10754	7	20082	03/12/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MT21TVV
10755	8	20083	03/12/2021	170504	3900	Non-haz soils & stones	9	Buckton Vale	CBDU90617	MK21BXN
10756	9	20084	03/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ
10757	10	20085	03/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYL
10758	11	20086	03/12/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVZ
10759	12	20087	03/12/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKJ
10760	13	20088	03/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV69KTT
10761	14	20089	03/12/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21BXX
10762	15	20090	03/12/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MV20RKK
10763	16	20091	03/12/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MK21CHF
10764	17	20092	03/12/2021	170504	3900	Non-haz soils & stones	9	Fletcher Bank	CBDU90617	MT21TVO
10765	18	20093	03/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYH
10766	19	20094	03/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MV19UBB
10767	20	20095	03/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MX21ORT
10768	21	20096	03/12/2021	170504	3900	Non-haz soils & stones	14	Buckton Vale	CBDU90617	MK21BYJ

Waste Disposal and Import Summary

PROVECTUS

Truck ticket No.	Date	Material Classification	Amount 8 wh = 19T artic = 28T	Supplier
220378	16/03/2021	Type 1	19	Buckton Vale
221522	16/03/2021	Type 1	19	Buckton Vale
178407	16/03/2021	Type 1	19	Buckton Vale
184021	16/03/2021	Type 1	19	Buckton Vale
219101	16/03/2021	Type 1	19	Buckton Vale
220381	16/03/2021	Type 1	19	Buckton Vale
221526	16/03/2021	Type 1	19	Buckton Vale
204744	16/03/2021	Type 1	19	Buckton Vale
178410	16/03/2021	Type 1	19	Buckton Vale
184023	16/03/2021	Type 1	19	Buckton Vale
219104	16/03/2021	Type 1	19	Buckton Vale
221513	16/03/2021	6F5	19	Buckton Vale
215498	16/03/2021	6F5	19	Buckton Vale
220374	16/03/2021	6F5	19	Buckton Vale
219092	16/03/2021	6F5	19	Buckton Vale
197639	16/03/2021	6F5	19	Buckton Vale
184015	16/03/2021	6F5	19	Buckton Vale
184017	16/03/2021	6F5	19	Buckton Vale
221516	16/03/2021	6F5	19	Buckton Vale
178401	16/03/2021	6F5	19	Buckton Vale
219095	16/03/2021	6F5	19	Buckton Vale
178404	16/03/2021	6F5	19	Buckton Vale
184019	16/03/2021	6F5	19	Buckton Vale
221519	16/03/2021	6F5	19	Buckton Vale
219098	16/03/2021	6F5	19	Buckton Vale
204773	18/03/2021	6"clean	19	Fletcher Bank
222919	23/03/2021	20mm C	19	Buckton Vale
222922	23/03/2021	20mm C	19	Buckton Vale
222926	23/03/2021	20mm C	19	Buckton Vale
222932	23/03/2021	20mm C	19	Buckton Vale
223085	25/03/2021	6F5	19	Buckton Vale
204269	25/03/2021	6F5	19	Buckton Vale
221480	25/03/2021	6F5	19	Buckton Vale
223886	25/03/2021	20mm C	19	Buckton Vale
224133	25/03/2021	20mm C	19	Buckton Vale
183766	25/03/2021	6F5	19	Buckton Vale
219140	25/03/2021	20mm C	19	Buckton Vale
224137	25/03/2021	6F5	19	Buckton Vale
183768	25/03/2021	6F5	19	Buckton Vale
219143	25/03/2021	6F5	19	Buckton Vale
223087	25/03/2021	6F5	19	Buckton Vale
204271	25/03/2021	6F5	19	Buckton Vale
221482	25/03/2021	6F5	19	Buckton Vale
223889	25/03/2021	6F5	19	Buckton Vale
223892	25/03/2021	6F5	19	Buckton Vale

223089	25/03/2021	6F5	19	Buckton Vale
221485	25/03/2021	Type 1	19	Buckton Vale
204273	25/03/2021	Type 1	19	Buckton Vale
219146	25/03/2021	6F5	19	Buckton Vale
224140	25/03/2021	6F5	19	Buckton Vale
183770	25/03/2021	Type 1	19	Buckton Vale
224143	25/03/2021	Type 1	19	Buckton Vale
222782	25/03/2021	Type 1	19	Buckton Vale
195043	25/03/2021	Type 1	19	Buckton Vale
220592	25/03/2021	Type 1	19	Buckton Vale
180487	25/03/2021	Type 1	19	Buckton Vale
189196	25/03/2021	Type 1	19	Buckton Vale
223898	25/03/2021	Type 1	19	Buckton Vale
221489	25/03/2021	Type 1	19	Buckton Vale
204277	25/03/2021	Type 1	19	Buckton Vale
217423	25/03/2021	Type 1	19	Buckton Vale
219149	25/03/2021	Type 1	19	Buckton Vale
204275	25/03/2021	Type 1	19	Buckton Vale
221487	25/03/2021	Type 1	19	Buckton Vale
223895	25/03/2021	Type 1	19	Buckton Vale
223091	25/03/2021	20mm C	19	Buckton Vale
223093	25/03/2021	Type 1	19	Buckton Vale
223095	25/03/2021	Type 1	19	Buckton Vale
223097	25/03/2021	Type 1	19	Buckton Vale
203474	26/03/2021	6F5	19	Buckton Vale
219152	26/03/2021	Type 1	19	Buckton Vale
204285	26/03/2021	Type 1	19	Buckton Vale
223152	26/03/2021	Type 1	19	Buckton Vale
203470	26/03/2021	6F5	19	Buckton Vale
221491	26/03/2021	6F5	19	Buckton Vale
224147	26/03/2021	6F5	19	Buckton Vale
183773	26/03/2021	6F5	19	Buckton Vale
219155	26/03/2021	Type 1	19	Buckton Vale
204288	26/03/2021	Type 1	19	Buckton Vale
223155	26/03/2021	Type 1	19	Buckton Vale
221493	26/03/2021	6F5	19	Buckton Vale
219158	26/03/2021	Type 1	19	Buckton Vale
221694	26/03/2021	Type 1	19	Buckton Vale
221691	26/03/2021	Type 1	19	Buckton Vale
224149	26/03/2021	6F5	19	Buckton Vale
183775	26/03/2021	6F5	19	Buckton Vale
223158	26/03/2021	Type 1	19	Buckton Vale
221495	26/03/2021	6F5	19	Buckton Vale
203478	26/03/2021	6F5	19	Buckton Vale
2219697	26/03/2021	Type 1	19	Buckton Vale
219161	26/03/2021	Type 1	19	Buckton Vale
183777	26/03/2021	6F5	19	Buckton Vale
224053	26/03/2021	6F5	19	Buckton Vale
204294	26/03/2021	Type 1	19	Buckton Vale
223161	26/03/2021	Type 1	19	Buckton Vale
221551	26/03/2021	Type 1	19	Buckton Vale
203481	26/03/2021	6F5	19	Buckton Vale

217430	26/03/2021	6F5	19	Buckton Vale
220503	26/03/2021	Type 1	19	Buckton Vale
224057	26/03/2021	6F5	19	Buckton Vale
222701	26/03/2021	Type 1	19	Buckton Vale
204297	26/03/2021	Type 1	19	Buckton Vale
191057	26/03/2021	6F5	19	Buckton Vale
217964	26/03/2021	6F5	19	Buckton Vale
200517	26/03/2021	6F5	19	Buckton Vale
223164	26/03/2021	Type 1	19	Buckton Vale
203801	29/03/2021	6F5	19	Buckton Vale
223021	29/03/2021	6"clean	19	Buckton Vale
219176	29/03/2021	6F5	19	Buckton Vale
221402	29/03/2021	6F5	19	Buckton Vale
223174	29/03/2021	6F5	19	Buckton Vale
200798	29/03/2021	6F5	19	Buckton Vale
203804	29/03/2021	6F5	19	Buckton Vale
223201	29/03/2021	6F5	19	Buckton Vale
223176	29/03/2021	6F5	19	Buckton Vale
221404	29/03/2021	6F5	19	Buckton Vale
223019	29/03/2021	6F5	19	Buckton Vale
203807	29/03/2021	6F5	19	Buckton Vale
219182	29/03/2021	6F5	19	Buckton Vale
223023	29/03/2021	6F5	19	Buckton Vale
219179	29/03/2021	6F5	19	Buckton Vale
223180	29/03/2021	6F5	19	Buckton Vale
221406	29/03/2021	6F5	19	Buckton Vale
223204	29/03/2021	6F5	19	Buckton Vale
221408	29/03/2021	6F5	19	Buckton Vale
223183	29/03/2021	6F5	19	Buckton Vale
223207	29/03/2021	6F5	19	Buckton Vale
219185	29/03/2021	6F5	19	Buckton Vale
223025	29/03/2021	6F5	19	Buckton Vale
203810	29/03/2021	6F5	19	Buckton Vale
203823	30/03/2021	Type 1	19	Fletcher Bank
183785	30/03/2021	Type 1	19	Fletcher Bank
203373	30/03/2021	Type 1	19	Fletcher Bank
204673	30/03/2021	Type 1	19	Fletcher Bank
223220	30/03/2021	Type 1	19	Fletcher Bank
163734	30/03/2021	Type 1	19	Fletcher Bank
221420	30/03/2021	Type 1	19	Fletcher Bank
221418	30/03/2021	Type 1	19	Fletcher Bank
163732	30/03/2021	Type 1	19	Fletcher Bank
203821	30/03/2021	20mm C	19	Buckton Vale
223035	30/03/2021	6F5	19	Fletcher Bank
183784	30/03/2021	Type 1	19	Fletcher Bank
203371	30/03/2021	Type 1	19	Fletcher Bank
223218	30/03/2021	Type 1	19	Fletcher Bank
204671	30/03/2021	Type 1	19	Fletcher Bank
163730	30/03/2021	6F5	19	Fletcher Bank
221416	30/03/2021	6F5	19	Fletcher Bank
223033	30/03/2021	20mm C	19	Buckton Vale
203818	30/03/2021	6F5	19	Fletcher Bank

183783	30/03/2021	Type 1	19	Fletcher Bank
204669	30/03/2021	20mm C	19	Buckton Vale
223216	30/03/2021	20mm C	19	Buckton Vale
203369	30/03/2021	6F5	19	Fletcher Bank
221414	30/03/2021	6F5	19	Fletcher Bank
163728	30/03/2021	6F5	19	Fletcher Bank
223213	30/03/2021	6F5	19	Fletcher Bank
203367	30/03/2021	6F5	19	Fletcher Bank
204666	30/03/2021	Type 1	19	Fletcher Bank
183782	30/03/2021	Type 1	19	Fletcher Bank
223031	30/03/2021	6F5	19	Fletcher Bank
203816	30/03/2021	6F5	19	Fletcher Bank
223029	30/03/2021	6F5	19	Fletcher Bank
203814	30/03/2021	6F5	19	Fletcher Bank
221412	30/03/2021	6F5	19	Fletcher Bank
163726	30/03/2021	6F5	19	Fletcher Bank
183781	30/03/2021	6F5	19	Fletcher Bank
204664	30/03/2021	6F5	19	Fletcher Bank
203365	30/03/2021	6F5	19	Fletcher Bank
223211	30/03/2021	6F5	19	Fletcher Bank
76229	31/03/2021	6F5	28	Fletcher Bank
203380	31/03/2021	6F5	19	Buckton Vale
219902	31/03/2021	6F5	19	Buckton Vale
224094	31/03/2021	6F5	19	Buckton Vale
221425	31/03/2021	6F5	19	Buckton Vale
223199	31/03/2021	6F5	19	Buckton Vale
96857	31/03/2021	6F5	28	Fletcher Bank
73480	31/03/2021	6F5	28	Fletcher Bank
76227	31/03/2021	6F5	28	Fletcher Bank
96855	31/03/2021	6F5	28	Fletcher Bank
70853	31/03/2021	6F5	28	Fletcher Bank
74171	31/03/2021	6F5	28	Fletcher Bank
74169	31/03/2021	6F5	28	Fletcher Bank
76226	31/03/2021	6F5	28	Fletcher Bank
70851	31/03/2021	6F5	28	Fletcher Bank
73478	31/03/2021	6F5	28	Fletcher Bank
96853	31/03/2021	6F5	28	Fletcher Bank
221423	31/03/2021	6F5	19	Buckton Vale
223196	31/03/2021	6F5	19	Buckton Vale
224091	31/03/2021	6F5	19	Buckton Vale
200549	31/03/2021	6F5	19	Buckton Vale
203377	31/03/2021	6F5	19	Buckton Vale
219905	31/03/2021	6F5	19	Buckton Vale
74173	31/03/2021	6F5	28	Fletcher Bank
70855	31/03/2021	6F5	28	Fletcher Bank
73482	31/03/2021	6F5	28	Fletcher Bank
221427	31/03/2021	6F5	19	Buckton Vale
224752	31/03/2021	6F5	19	Buckton Vale
224097	31/03/2021	6F5	19	Buckton Vale
203383	31/03/2021	6F5	19	Buckton Vale
76231	31/03/2021	Type 1	28	Fletcher Bank
70857	31/03/2021	Type 1	28	Fletcher Bank

74175	31/03/2021	Type 1	28	Fletcher Bank
73456	31/03/2021	Type 1	28	Fletcher Bank
74177	31/03/2021	Type 1	28	Fletcher Bank
70859	31/03/2021	Type 1	28	Fletcher Bank
76233	31/03/2021	Type 1	28	Fletcher Bank
203387	31/03/2021	6F5	19	Buckton Vale
219908	31/03/2021	6F5	19	Buckton Vale
221429	31/03/2021	6F5	19	Buckton Vale
224151	31/03/2021	6F5	19	Buckton Vale
224755	31/03/2021	6F5	19	Buckton Vale
73484	31/03/2021	Type 1	28	Fletcher Bank
96860	31/03/2021	Type 1	28	Fletcher Bank
220538	31/03/2021	6F5	19	Buckton Vale
203391	31/03/2021	6F5	19	Buckton Vale
219970	31/03/2021	6F5	19	Buckton Vale
223240	31/03/2021	6F5	19	Buckton Vale
219911	31/03/2021	6F5	19	Buckton Vale
221431	31/03/2021	6F5	19	Buckton Vale
224154	31/03/2021	6F5	19	Buckton Vale
202021	31/03/2021	6F5	19	Buckton Vale
224757	31/03/2021	6F5	19	Buckton Vale
203842	31/03/2021	6F5	19	Buckton Vale
74179	01/04/2021	6F5	28	Fletcher Bank
76236	01/04/2021	6F5	28	Fletcher Bank
70862	01/04/2021	6F5	28	Fletcher Bank
96862	01/04/2021	6F5	28	Fletcher Bank
203394	01/04/2021	6F5	19	Fletcher Bank
73489	01/04/2021	6F5	28	Fletcher Bank
224157	01/04/2021	6F5	19	Fletcher Bank
76238	01/04/2021	6F5	28	Fletcher Bank
96864	01/04/2021	6F5	28	Fletcher Bank
219914	01/04/2021	6F5	19	Fletcher Bank
74181	01/04/2021	6F5	28	Fletcher Bank
203396	01/04/2021	6F5	19	Fletcher Bank
221435	01/04/2021	6F5	19	Fletcher Bank
224159	01/04/2021	6F5	19	Fletcher Bank
73491	01/04/2021	6F5	28	Fletcher Bank
76240	01/04/2021	6F5	28	Fletcher Bank
203398	01/04/2021	6F5	19	Fletcher Bank
221437	01/04/2021	6F5	19	Fletcher Bank
96866	01/04/2021	6F5	28	Fletcher Bank
70864	01/04/2021	6F5	28	Fletcher Bank
70866	01/04/2021	6F5	28	Fletcher Bank
219916	01/04/2021	6F5	19	Fletcher Bank
73493	01/04/2021	6F5	28	Fletcher Bank
224161	01/04/2021	6F5	19	Fletcher Bank
96868	01/04/2021	6F5	28	Fletcher Bank
76242	01/04/2021	6F5	28	Fletcher Bank
178955	01/04/2021	6F5	19	Fletcher Bank
219918	01/04/2021	6F5	19	Fletcher Bank
221439	01/04/2021	Type 1	19	Fletcher Bank
203302	01/04/2021	Type 1	19	Fletcher Bank

74184	01/04/2021	Type 1	28	Fletcher Bank
73495	01/04/2021	Type 1	28	Fletcher Bank
224163	01/04/2021	Type 1	19	Fletcher Bank
96870	01/04/2021	Type 1	28	Fletcher Bank
219920	01/04/2021	Type 1	19	Fletcher Bank
221441	01/04/2021	Type 1	19	Fletcher Bank
178957	01/04/2021	Type 1	19	Fletcher Bank
203303	01/04/2021	Type 1	19	Fletcher Bank
70869	01/04/2021	6F5	28	Fletcher Bank
202039	01/04/2021	Type 1	19	Buckton Vale
219986	01/04/2021	Type 1	19	Buckton Vale
74186	01/04/2021	Type 1	28	Fletcher Bank
178960	01/04/2021	Type 1	19	Fletcher Bank
221443	01/04/2021	Type 1	19	Fletcher Bank
219922	01/04/2021	Type 1	19	Fletcher Bank
223257	01/04/2021	Type 1	19	Buckton Vale
96872	01/04/2021	Type 1	28	Fletcher Bank
224167	01/04/2021	Type 1	19	Fletcher Bank
22310	01/04/2021	Type 1	19	Buckton Vale
203305	01/04/2021	Type 1	19	Fletcher Bank
73497	01/04/2021	Type 1	28	Fletcher Bank
224165	01/04/2021	Type 1	19	Fletcher Bank
71451	06/04/2021	Type 1	28	Fletcher Bank
70872	06/04/2021	Type 1	28	Fletcher Bank
50211	06/04/2021	Type 1	28	Fletcher Bank
73500	06/04/2021	Type 1	28	Fletcher Bank
96875	06/04/2021	Type 1	28	Fletcher Bank
71453	06/04/2021	Type 1	28	Fletcher Bank
96877	06/04/2021	Type 1	28	Fletcher Bank
73402	06/04/2021	Type 1	28	Fletcher Bank
50213	06/04/2021	Type 1	28	Fletcher Bank
70874	06/04/2021	Type 1	28	Fletcher Bank
71455	06/04/2021	Type 1	28	Fletcher Bank
50215	06/04/2021	Type 1	28	Fletcher Bank
73404	06/04/2021	Type 1	28	Fletcher Bank
96879	06/04/2021	Type 1	28	Fletcher Bank
71457	06/04/2021	Type 1	28	Fletcher Bank
70876	06/04/2021	Type 1	28	Fletcher Bank
50217	06/04/2021	Type 1	28	Fletcher Bank
73406	06/04/2021	Type 1	28	Fletcher Bank
96881	06/04/2021	Type 1	28	Fletcher Bank
70878	06/04/2021	Type 1	28	Fletcher Bank
71459	06/04/2021	Type 1	28	Fletcher Bank
73408	06/04/2021	Type 1	28	Fletcher Bank
96883	06/04/2021	Type 1	28	Fletcher Bank
50219	06/04/2021	Type 1	28	Fletcher Bank
71461	06/04/2021	6F5	28	Fletcher Bank
70880	06/04/2021	Type 1	28	Fletcher Bank
96885	06/04/2021	6F5	28	Fletcher Bank
217457	06/04/2021	Type 1	19	Buckton Vale
217911	06/04/2021	Type 1	19	Buckton Vale
223279	06/04/2021	Type 1	19	Buckton Vale

96887	07/04/2021	6F5	28	Fletcher Bank
70883	07/04/2021	6F5	28	Fletcher Bank
73410	07/04/2021	6F5	28	Fletcher Bank
96893	07/04/2021	6F5	28	Fletcher Bank
71469	07/04/2021	Type 1	28	Fletcher Bank
50227	07/04/2021	Type 1	28	Fletcher Bank
70888	07/04/2021	6F5	28	Fletcher Bank
71467	07/04/2021	Type 1	28	Fletcher Bank
52258	07/04/2021	Type 1	28	Fletcher Bank
50229	07/04/2021	Type 1	28	Fletcher Bank
96891	07/04/2021	6F5	28	Fletcher Bank
70890	07/04/2021	6F5	28	Fletcher Bank
50231	07/04/2021	Type 1	28	Fletcher Bank
223299	07/04/2021	Type 1	28	Fletcher Bank
96895	07/04/2021	6F5	28	Fletcher Bank
71471	07/04/2021	Type 1	28	Fletcher Bank
217477	07/04/2021	Type 1	28	Buckton Vale
222201	07/04/2021	Type 1	28	Buckton Vale
70892	07/04/2021	6F5	28	Fletcher Bank
201961	08/04/2021	Type 1	19	Buckton Vale
96897	08/04/2021	6F5	28	Fletcher Bank
70894	08/04/2021	6F5	28	Fletcher Bank
52261	08/04/2021	6F5	28	Fletcher Bank
96899	08/04/2021	6F5	28	Fletcher Bank
53511	08/04/2021	6F5	28	Fletcher Bank
222157	08/04/2021	Type 1	19	Buckton Vale
122910	08/04/2021	Type 1	19	Buckton Vale
52305	08/04/2021	6F5	28	Fletcher Bank
224778	08/04/2021	Type 1	19	Buckton Vale
201963	08/04/2021	Type 1	28	Buckton Vale
70897	08/04/2021	6F5	28	Fletcher Bank
52236	08/04/2021	6F5	19	Fletcher Bank
222651	08/04/2021	Type 1	19	Buckton Vale
74188	08/04/2021	6F5	28	Fletcher Bank
53513	08/04/2021	6F5	28	Fletcher Bank
122912	08/04/2021	Type 1	19	Buckton Vale
222159	08/04/2021	Type 1	19	Buckton Vale
52307	08/04/2021	6F5	28	Fletcher Bank
224782	08/04/2021	Type 1	19	Buckton Vale
122914	08/04/2021	Type 1	19	Buckton Vale
53515	08/04/2021	6F5	28	Fletcher Bank
52309	08/04/2021	6F5	28	Fletcher Bank
224783	08/04/2021	Type 1	19	Buckton Vale
52265	08/04/2021	6F5	28	Fletcher Bank
222653	08/04/2021	Type 1	19	Buckton Vale
52311	08/04/2021	6F5	28	Fletcher Bank
201965	08/04/2021	Type 1	19	Buckton Vale
50701	08/04/2021	6F5	28	Fletcher Bank
50703	08/04/2021	6F5	28	Fletcher Bank
52267	08/04/2021	6F5	19	Fletcher Bank
53517	08/04/2021	6F5	28	Fletcher Bank
122917	08/04/2021	Type 1	19	Buckton Vale

224785	08/04/2021	Type 1	19	Buckton Vale
222162	08/04/2021	Type 1	19	Buckton Vale
201967	08/04/2021	Type 1	28	Buckton Vale
52313	08/04/2021	6F5	28	Fletcher Bank
52269	08/04/2021	6F5	28	Fletcher Bank
53519	08/04/2021	6F5	28	Fletcher Bank
222165	08/04/2021	Type 1	19	Buckton Vale
220956	08/04/2021	Type 1	19	Buckton Vale
224787	08/04/2021	Type 1	19	Buckton Vale
50705	08/04/2021	6F5	28	Fletcher Bank
217499	08/04/2021	Type 1	19	Buckton Vale
74193	08/04/2021	6F5	28	Fletcher Bank
223322	08/04/2021	Type 1	19	Buckton Vale
222655	08/04/2021	Type 1	19	Buckton Vale
202052	08/04/2021	Type 1	19	Buckton Vale
74195	09/04/2021	Type 1	28	Fletcher Bank
50707	09/04/2021	6F5	28	Fletcher Bank
73423	09/04/2021	6F5	28	Fletcher Bank
52317	09/04/2021	Type 1	28	Fletcher Bank
71481	09/04/2021	6F5	28	Fletcher Bank
53522	09/04/2021	6F5	28	Fletcher Bank
201971	09/04/2021	Type 1	19	Buckton Vale
222656	09/04/2021	Type 1	19	Buckton Vale
50709	09/04/2021	6F5	28	Fletcher Bank
74197	09/04/2021	6F5	28	Fletcher Bank
224794	09/04/2021	Type 1	19	Buckton Vale
222167	09/04/2021	Type 1	19	Buckton Vale
122920	09/04/2021	Type 1	19	Buckton Vale
50241	09/04/2021	6F5	28	Fletcher Bank
52319	09/04/2021	6F5	28	Fletcher Bank
71483	09/04/2021	6F5	28	Fletcher Bank
73425	09/04/2021	6F5	28	Fletcher Bank
74199	09/04/2021	6F5	28	Fletcher Bank
224797	09/04/2021	Type 1	19	Buckton Vale
122922	09/04/2021	Type 1	19	Buckton Vale
201973	09/04/2021	Type 1	19	Buckton Vale
53524	09/04/2021	6F5	28	Fletcher Bank
222657	09/04/2021	Type 1	19	Buckton Vale
50712	09/04/2021	6F5	28	Fletcher Bank
201975	09/04/2021	Type 1	19	Buckton Vale
222658	09/04/2021	Type 1	19	Buckton Vale
53526	09/04/2021	6F5	28	Fletcher Bank
52701	09/04/2021	6F5	28	Fletcher Bank
222502	09/04/2021	Type 1	19	Buckton Vale
52321	09/04/2021	6F5	28	Fletcher Bank
71485	09/04/2021	6F5	28	Fletcher Bank
122924	09/04/2021	Type 1	19	Buckton Vale
73427	09/04/2021	6F5	28	Fletcher Bank
50243	09/04/2021	Type 1	28	Fletcher Bank
222169	09/04/2021	Type 1	19	Buckton Vale
50245	09/04/2021	6F5	28	Fletcher Bank
73429	09/04/2021	6F5	28	Fletcher Bank

52323	09/04/2021	6F5	28	Fletcher Bank
71487	09/04/2021	6F5	28	Fletcher Bank
122926	09/04/2021	Type 1	19	Buckton Vale
52703	09/04/2021	6F5	28	Fletcher Bank
53528	09/04/2021	6F5	28	Fletcher Bank
222505	09/04/2021	Type 1	19	Buckton Vale
50714	09/04/2021	6F5	28	Fletcher Bank
222659	09/04/2021	Type 1	19	Buckton Vale
201977	09/04/2021	Type 1	19	Buckton Vale
51786	09/04/2021	Type 1	28	Fletcher Bank
51788	09/04/2021	Type 1	28	Fletcher Bank
51794	09/04/2021	Type 1	28	Fletcher Bank
51790	09/04/2021	Type 1	28	Fletcher Bank
51792	09/04/2021	Type 1	28	Fletcher Bank
52705	09/04/2021	6F5	28	Fletcher Bank
122928	09/04/2021	Type 1	19	Buckton Vale
52325	09/04/2021	6F5	28	Fletcher Bank
73431	09/04/2021	6F5	28	Fletcher Bank
71489	09/04/2021	6F5	28	Fletcher Bank
222240	09/04/2021	Type 1	19	Buckton Vale
50247	09/04/2021	6F5	28	Fletcher Bank
222660	09/04/2021	Type 1	19	Buckton Vale
53530	09/04/2021	Type 1	28	Fletcher Bank
222506	09/04/2021	Type 1	19	Buckton Vale
201979	09/04/2021	Type 1	19	Buckton Vale
50716	09/04/2021	Type 1	28	Fletcher Bank
50719	12/04/2021	6F5	28	Fletcher Bank
53331	12/04/2021	6F5	28	Fletcher Bank
177758	12/04/2021	Type 1	19	Buckton Vale
201982	12/04/2021	Type 1	19	Buckton Vale
202157	12/04/2021	Type 1	19	Buckton Vale
73434	12/04/2021	6F5	28	Fletcher Bank
222183	12/04/2021	Type 1	19	Buckton Vale
73438	12/04/2021	Type 1	28	Fletcher Bank
222187	12/04/2021	Type 1	19	Buckton Vale
202163	12/04/2021	Type 1	19	Buckton Vale
201987	12/04/2021	Type 1	19	Buckton Vale
177764	12/04/2021	Type 1	19	Buckton Vale
53336	12/04/2021	Type 1	28	Fletcher Bank
52707	12/04/2021	Type 1	28	Fletcher Bank
222185	12/04/2021	Type 1	19	Buckton Vale
73436	12/04/2021	Type 1	28	Fletcher Bank
202160	12/04/2021	Type 1	19	Buckton Vale
201985	12/04/2021	Type 1	19	Buckton Vale
177761	12/04/2021	Type 1	19	Buckton Vale
53333	12/04/2021	Type 1	28	Fletcher Bank
73440	12/04/2021	Type 1	28	Fletcher Bank
50722	12/04/2021	Type 1	28	Fletcher Bank
50724	12/04/2021	Type 1	28	Fletcher Bank
177768	12/04/2021	Type 1	19	Buckton Vale
53338	12/04/2021	Type 1	28	Fletcher Bank
20189	12/04/2021	Type 1	19	Buckton Vale

202166	12/04/2021	Type 1	19	Buckton Vale
50726	12/04/2021	Type 1	28	Fletcher Bank
177771	12/04/2021	Type 1	19	Buckton Vale
71497	12/04/2021	Type 1	28	Fletcher Bank
52333	12/04/2021	Type 1	28	Fletcher Bank
51807	12/04/2021	Type 1	28	Fletcher Bank
53340	12/04/2021	Type 1	28	Fletcher Bank
52710	12/04/2021	Type 1	28	Fletcher Bank
201991	12/04/2021	Type 1	19	Buckton Vale
53534	12/04/2021	Type 1	28	Fletcher Bank
51186	12/04/2021	Type 1	28	Fletcher Bank
50306	12/04/2021	Type 1	28	Fletcher Bank
202170	12/04/2021	Type 1	19	Buckton Vale
73442	12/04/2021	Type 1	28	Fletcher Bank
52712	13/04/2021	Type 1	28	Fletcher Bank
50728	13/04/2021	Type 1	28	Fletcher Bank
50730	13/04/2021	Type 1	28	Fletcher Bank
53342	13/04/2021	Type 1	28	Fletcher Bank
50311	13/04/2021	Type 1	28	Buckton Vale
53344	13/04/2021	Type 1	28	Fletcher Bank
53538	13/04/2021	Type 1	28	Fletcher Bank
50732	13/04/2021	Type 1	28	Fletcher Bank
52338	13/04/2021	Type 1	28	Buckton Vale
50314	13/04/2021	Type 1	28	Buckton Vale
53346	13/04/2021	Type 1	28	Fletcher Bank
53540	13/04/2021	Type 1	28	Fletcher Bank
52714	13/04/2021	Type 1	28	Fletcher Bank
74402	13/04/2021	Type 1	28	Fletcher Bank
50734	13/04/2021	Type 1	28	Fletcher Bank
52340	13/04/2021	Type 1	28	Buckton Vale
74405	13/04/2021	Type 1	28	Fletcher Bank
50318	13/04/2021	Type 1	28	Buckton Vale
53542	13/04/2021	Type 1	28	Fletcher Bank
50736	13/04/2021	Type 1	28	Fletcher Bank
53348	13/04/2021	Type 1	28	Fletcher Bank
52716	13/04/2021	Type 1	28	Fletcher Bank
52342	13/04/2021	Type 1	28	Buckton Vale
50321	13/04/2021	Type 1	28	Buckton Vale
74407	13/04/2021	Type 1	28	Fletcher Bank
53544	13/04/2021	Type 1	28	Fletcher Bank
50738	13/04/2021	Type 1	28	Fletcher Bank
52718	13/04/2021	Type 1	28	Fletcher Bank
52344	13/04/2021	Type 1	28	Buckton Vale
53350	13/04/2021	Type 1	28	Fletcher Bank
50324	13/04/2021	Type 1	28	Buckton Vale
74409	13/04/2021	Type 1	28	Fletcher Bank
50740	14/04/2021	Type 1	28	Fletcher Bank
74411	14/04/2021	Type 1	28	Fletcher Bank
50327	14/04/2021	Type 1	28	Fletcher Bank
50742	14/04/2021	Type 1	28	Fletcher Bank
74413	14/04/2021	Type 1	28	Fletcher Bank
52347	14/04/2021	Type 1	28	Buckton Vale

74451	14/04/2021	Type 1	28	Fletcher Bank
50329	14/04/2021	Type 1	28	Fletcher Bank
50744	14/04/2021	Type 1	28	Fletcher Bank
53161	14/04/2021	Type 1	28	Fletcher Bank
53163	14/04/2021	Type 1	28	Fletcher Bank
74415	14/04/2021	Type 1	28	Fletcher Bank
52349	14/04/2021	Type 1	28	Buckton Vale
744753	14/04/2021	Type 1	28	Fletcher Bank
50331	14/04/2021	Type 1	28	Fletcher Bank
50746	14/04/2021	Type 1	28	Fletcher Bank
74417	14/04/2021	Type 1	28	Fletcher Bank
53165	14/04/2021	Type 1	28	Fletcher Bank
52101	14/04/2021	Type 1	28	Buckton Vale
74455	14/04/2021	Type 1	28	Fletcher Bank
50333	14/04/2021	Type 1	28	Fletcher Bank
74419	14/04/2021	Type 1	28	Fletcher Bank
53167	14/04/2021	Type 1	28	Fletcher Bank
52103	14/04/2021	Type 1	28	Buckton Vale
74457	14/04/2021	Type 1	28	Fletcher Bank
50335	14/04/2021	Type 1	28	Fletcher Bank
74421	14/04/2021	Type 1	28	Fletcher Bank
53169	14/04/2021	Type 1	28	Fletcher Bank
50749	14/04/2021	Type 1	28	Fletcher Bank
52105	14/04/2021	Type 1	28	Buckton Vale
74459	14/04/2021	Type 1	28	Fletcher Bank
74352	15/04/2021	Type 1	28	Fletcher Bank
74423	15/04/2021	Type 1	28	Fletcher Bank
52720	15/04/2021	Type 1	28	Fletcher Bank
52665	15/04/2021	Type 1	28	Fletcher Bank
74354	15/04/2021	Type 1	28	Fletcher Bank
50338	15/04/2021	Type 1	28	Fletcher Bank
74425	15/04/2021	Type 1	28	Fletcher Bank
74462	15/04/2021	Type 1	28	Fletcher Bank
53172	15/04/2021	Type 1	28	Fletcher Bank
52722	15/04/2021	Type 1	28	Fletcher Bank
74356	15/04/2021	Type 1	28	Fletcher Bank
52667	15/04/2021	Type 1	28	Fletcher Bank
50340	15/04/2021	Type 1	28	Fletcher Bank
74464	15/04/2021	Type 1	28	Fletcher Bank
53174	15/04/2021	Type 1	28	Fletcher Bank
52724	15/04/2021	Type 1	28	Fletcher Bank
52729	16/04/2021	6F5	19	Fletcher Bank
74430	16/04/2021	6F5	19	Fletcher Bank
74362	16/04/2021	6F5	19	Fletcher Bank
74470	16/04/2021	6F5	19	Fletcher Bank
52602	16/04/2021	6F5	19	Fletcher Bank
53181	16/04/2021	6F5	19	Fletcher Bank
52731	16/04/2021	6F5	19	Fletcher Bank
74432	16/04/2021	6F5	19	Fletcher Bank
74473	16/04/2021	6F5	19	Fletcher Bank
52604	16/04/2021	6F5	19	Fletcher Bank
53183	16/04/2021	6F5	19	Fletcher Bank

52733	16/04/2021	6F5	19	Fletcher Bank
74434	16/04/2021	6F5	19	Fletcher Bank
52606	16/04/2021	6F5	19	Fletcher Bank
53185	16/04/2021	6F5	19	Fletcher Bank
52735	16/04/2021	6F5	19	Fletcher Bank
74436	16/04/2021	6F5	19	Fletcher Bank
74474	16/04/2021	6F5	19	Fletcher Bank
52608	16/04/2021	6F5	19	Fletcher Bank
53187	16/04/2021	6F5	19	Fletcher Bank
52737	16/04/2021	6F5	19	Fletcher Bank
74476	16/04/2021	6F5	19	Fletcher Bank
74438	16/04/2021	6F5	19	Fletcher Bank
74365	16/04/2021	6F5	19	Fletcher Bank
52610	16/04/2021	6F5	19	Fletcher Bank
50767	23/04/2021	Type 1	28	Fletcher Bank
71138	23/04/2021	Type 1	28	Fletcher Bank
50414	23/04/2021	Type 1	28	Fletcher Bank
75615	23/04/2021	Type 1	28	Fletcher Bank
93302	23/04/2021	20mm C	28	Buckton Vale
74395	23/04/2021	6F5	28	Fletcher Bank
50412	23/04/2021	Type 1	28	Fletcher Bank
75613	23/04/2021	Type 1	28	Fletcher Bank
93304	23/04/2021	20mm C	28	Buckton Vale
52851	23/04/2021	6F5	28	Fletcher Bank
93306	23/04/2021	20mm C	28	Buckton Vale
52853	23/04/2021	6F5	28	Fletcher Bank
50770	23/04/2021	Type 1	28	Fletcher Bank
71140	23/04/2021	Type 1	28	Fletcher Bank
53451	23/04/2021	6F5	28	Fletcher Bank
52641	23/04/2021	6F5	28	Fletcher Bank
52645	23/04/2021	6F5	28	Fletcher Bank
53453	23/04/2021	6F5	28	Fletcher Bank
50791	28/04/2021	6F5	28	Fletcher Bank
90101	28/04/2021	6F5	28	Fletcher Bank
51839	28/04/2021	6F5	28	Fletcher Bank
53580	28/04/2021	6F5	28	Fletcher Bank
92325	28/04/2021	6F5	28	Fletcher Bank
50795	28/04/2021	6F5	28	Fletcher Bank
53584	28/04/2021	6F5	28	Fletcher Bank
50793	28/04/2021	6F5	28	Fletcher Bank
51841	28/04/2021	6F5	28	Fletcher Bank
53582	28/04/2021	6F5	28	Fletcher Bank
92327	28/04/2021	6F5	28	Fletcher Bank
90102	28/04/2021	6F5	28	Fletcher Bank
93260	28/04/2021	6F5	28	Fletcher Bank
90103	28/04/2021	6F5	28	Fletcher Bank
53588	28/04/2021	6F5	28	Fletcher Bank
51844	28/04/2021	6F5	28	Fletcher Bank
50799	28/04/2021	6F5	28	Fletcher Bank
93262	28/04/2021	6F5	28	Fletcher Bank
50797	28/04/2021	6F5	28	Fletcher Bank
92334	28/04/2021	6F5	28	Fletcher Bank

72080	29/04/2021	Type 1	28	Fletcher Bank
92339	29/04/2021	Type 1	28	Fletcher Bank
51849	29/04/2021	6F5	28	Fletcher Bank
90204	29/04/2021	6F5	28	Fletcher Bank
72081	29/04/2021	Type 1	28	Fletcher Bank
93263	29/04/2021	6F5	28	Fletcher Bank
90206	29/04/2021	6F5	28	Fletcher Bank
93265	29/04/2021	6F5	28	Fletcher Bank
90208	29/04/2021	6F5	28	Fletcher Bank
92340	29/04/2021	Type 1	28	Fletcher Bank
53127	29/04/2021	Type 1	28	Fletcher Bank
72082	29/04/2021	Type 1	28	Fletcher Bank
92343	29/04/2021	Type 1	28	Fletcher Bank
53129	29/04/2021	Type 1	28	Fletcher Bank
93349	30/04/2021	Type 1	28	Fletcher Bank
53494	30/04/2021	Type 1	28	Fletcher Bank
52893	30/04/2021	Type 1	28	Fletcher Bank
53499	04/05/2021	Type 1	28	Buckton Vale
93276	04/05/2021	Type 1	28	Fletcher Bank
211919	04/05/2021	Type 1	19	Fletcher Bank
91403	04/05/2021	Type 1	28	Buckton Vale
211806	04/05/2021	Type 1	19	Fletcher Bank
93402	04/05/2021	Type 1	28	Fletcher Bank
210972	04/05/2021	Type 1	19	Fletcher Bank
13603	04/05/2021	Type 1	28	Fletcher Bank
52895	04/05/2021	Type 1	28	Buckton Vale
92260	04/05/2021	Type 1	28	Fletcher Bank
223638	04/05/2021	Type 1	19	Fletcher Bank
93278	04/05/2021	Type 1	28	Fletcher Bank
13605	04/05/2021	Type 1	28	Fletcher Bank
92263	04/05/2021	Type 1	28	Fletcher Bank
52897	04/05/2021	Type 1	28	Buckton Vale
223640	04/05/2021	Type 1	19	Fletcher Bank
93404	04/05/2021	Type 1	28	Fletcher Bank
211807	04/05/2021	Type 1	19	Fletcher Bank
211921	04/05/2021	Type 1	19	Fletcher Bank
223642	04/05/2021	Type 1	19	Fletcher Bank
92265	04/05/2021	Type 1	28	Fletcher Bank
52899	04/05/2021	Type 1	28	Buckton Vale
13607	04/05/2021	Type 1	28	Fletcher Bank
210974	04/05/2021	Type 1	19	Fletcher Bank
91406	04/05/2021	Type 1	28	Buckton Vale
93280	04/05/2021	Type 1	28	Fletcher Bank
13609	04/05/2021	Type 1	28	Fletcher Bank
221809	04/05/2021	Type 1	19	Fletcher Bank
93406	04/05/2021	Type 1	28	Fletcher Bank
90563	04/05/2021	Type 1	28	Fletcher Bank
211923	04/05/2021	Type 1	19	Fletcher Bank
93282	04/05/2021	Type 1	28	Fletcher Bank
91410	04/05/2021	Type 1	28	Buckton Vale
222088	04/05/2021	Type 1	19	Buckton Vale
92267	04/05/2021	Type 1	28	Fletcher Bank

223644	04/05/2021	Type 1	19	Fletcher Bank
211811	04/05/2021	Type 1	19	Fletcher Bank
224209	04/05/2021	Type 1	19	Buckton Vale
52901	04/05/2021	Type 1	28	Buckton Vale
93408	04/05/2021	Type 1	28	Fletcher Bank
211925	04/05/2021	Type 1	19	Fletcher Bank
54067	05/05/2021	Type 1	28	Fletcher Bank
91413	05/05/2021	Type 1	28	Buckton Vale
50878	05/05/2021	Type 1	28	Fletcher Bank
91435	07/05/2021	Type 1	28	Fletcher Bank
214198	07/05/2021	Type 1	19	Fletcher Bank
52921	07/05/2021	6F5	28	Fletcher Bank
91439	07/05/2021	6F5	28	Buckton Vale
226851	07/05/2021	Type 1	19	Fletcher Bank
91441	07/05/2021	6F5	28	Fletcher Bank
226853	07/05/2021	Type 1	19	Fletcher Bank
93741	10/05/2021	6F5	28	Fletcher Bank
91450	10/05/2021	6F5	28	Fletcher Bank
53959	11/05/2021	6F5	28	Fletcher Bank
75674	11/05/2021	6F5	28	Fletcher Bank
53960	11/05/2021	6F5	28	Fletcher Bank
75675	11/05/2021	6F5	28	Fletcher Bank
75676	11/05/2021	6F5	28	Fletcher Bank
53961	11/05/2021	6F5	28	Fletcher Bank
53962	11/05/2021	6F5	28	Fletcher Bank
75646	11/05/2021	6F5	28	Fletcher Bank
52929	11/05/2021	6F5	28	Fletcher Bank
75648	11/05/2021	6F5	28	Fletcher Bank
52931	11/05/2021	6F5	28	Fletcher Bank
222139	11/05/2021	20mm C	19	Buckton Vale
53964	11/05/2021	6F5	28	Fletcher Bank
93748	11/05/2021	6F5	28	Fletcher Bank
75677	11/05/2021	6F5	28	Fletcher Bank
75650	11/05/2021	6F5	28	Fletcher Bank
52933	11/05/2021	6F5	28	Fletcher Bank
210774	12/05/2021	6F5	19	Fletcher Bank
226960	12/05/2021	6F5	19	Fletcher Bank
221743	12/05/2021	6F5	19	Fletcher Bank
50897	12/05/2021	Type 1	28	Buckton Vale
73161	12/05/2021	Type 1	28	Buckton Vale
226868	12/05/2021	6F5	19	Fletcher Bank
91553	12/05/2021	Type 1	28	Buckton Vale
210776	12/05/2021	6F5	19	Fletcher Bank
226962	12/05/2021	6F5	19	Fletcher Bank
221745	12/05/2021	6F5	19	Fletcher Bank
226870	12/05/2021	6F5	19	Fletcher Bank
50899	12/05/2021	Type 1	28	Buckton Vale
52938	12/05/2021	Type 1	28	Buckton Vale
73164	12/05/2021	Type 1	28	Buckton Vale
91557	12/05/2021	Type 1	28	Buckton Vale
223107	12/05/2021	20mm C	19	Buckton Vale

226964	12/05/2021	6F5	19	Fletcher Bank
226872	12/05/2021	6F5	19	Fletcher Bank
90112	12/05/2021	Type 1	28	Buckton Vale
210778	12/05/2021	6F5	19	Fletcher Bank
211747	12/05/2021	6F5	19	Fletcher Bank
73167	12/05/2021	Type 1	28	Buckton Vale
91560	12/05/2021	Type 1	28	Fletcher Bank
210780	12/05/2021	6F5	19	Fletcher Bank
223111	12/05/2021	20mm C	19	Buckton Vale
226966	12/05/2021	6F5	19	Fletcher Bank
226874	12/05/2021	6F5	19	Fletcher Bank
212523	12/05/2021	6F5	19	Fletcher Bank
221749	12/05/2021	6F5	19	Fletcher Bank
90114	12/05/2021	Type 1	28	Buckton Vale
52942	12/05/2021	Type 1	28	Buckton Vale
73170	12/05/2021	Type 1	28	Buckton Vale
91563	12/05/2021	Type 1	28	Buckton Vale
226968	12/05/2021	6F5	19	Fletcher Bank
226876	12/05/2021	6F5	19	Fletcher Bank
212525	12/05/2021	6F5	19	Fletcher Bank
210782	12/05/2021	6F5	19	Fletcher Bank
205351	12/05/2021	Type 1	19	Buckton Vale
91566	12/05/2021	Type 1	28	Buckton Vale
52944	12/05/2021	Type 1	28	Buckton Vale
223115	12/05/2021	Type 1	19	Buckton Vale
73173	12/05/2021	Type 1	28	Buckton Vale
213447	13/05/2021	Type 1	19	Buckton Vale
90120	13/05/2021	6F5	28	Fletcher Bank
50935	13/05/2021	6F5	28	Fletcher Bank
90609	13/05/2021	6F5	28	Fletcher Bank
50933	13/05/2021	6F5	28	Fletcher Bank
91125	13/05/2021	6F5	28	Fletcher Bank
53980	13/05/2021	6F5	28	Fletcher Bank
91126	13/05/2021	6F5	28	Fletcher Bank
53982	13/05/2021	6F5	28	Fletcher Bank
97238	13/05/2021	75mm C	28	Buckton Vale
52952	13/05/2021	75mm C	28	Buckton Vale
90611	13/05/2021	6F5	28	Fletcher Bank
91575	13/05/2021	6F5	28	Buckton Vale
73182	13/05/2021	75mm C	28	Buckton Vale
90267	13/05/2021	75mm C	28	Buckton Vale
94018	13/05/2021	75mm C	28	Buckton Vale
52955	14/05/2021	75mm C	28	Buckton Vale
91579	14/05/2021	75mm C	28	Buckton Vale
90615	14/05/2021	75mm C	28	Buckton Vale
91582	14/05/2021	75mm C	28	Buckton Vale
52957	14/05/2021	75mm C	28	Buckton Vale
90617	14/05/2021	75mm C	28	Buckton Vale
91453	14/05/2021	75mm C	28	Buckton Vale
91585	14/05/2021	75mm C	28	Buckton Vale
90620	14/05/2021	75mm C	28	Buckton Vale
91455	14/05/2021	75mm C	28	Buckton Vale

52961	14/05/2021	75mm C	28	Buckton Vale
91588	14/05/2021	75mm C	28	Buckton Vale
75695	14/05/2021	75mm C	28	Buckton Vale
205369	14/05/2021	20mm C	19	Buckton Vale
50941	14/05/2021	Type 1	28	Buckton Vale
213372	14/05/2021	Type 1	19	Buckton Vale
90623	14/05/2021	75mm C	19	Buckton Vale
214501	14/05/2021	Type 1	19	Buckton Vale
212212	14/05/2021	20mm C	19	Buckton Vale
90625	17/05/2021	Type 1	28	Buckton Vale
91592	17/05/2021	Type 1	28	Buckton Vale
92803	17/05/2021	Type 1	28	Buckton Vale
210909	19/05/2021	6"clean	19	Fletcher Bank
226998	19/05/2021	6"clean	19	Fletcher Bank
205489	19/05/2021	6"clean	19	Fletcher Bank
205702	19/05/2021	6"clean	19	Fletcher Bank
91526	25/05/2021	75mm C	28	Fletcher Bank
52996	25/05/2021	75mm C	28	Fletcher Bank
52998	25/05/2021	75mm C	28	Fletcher Bank
91529	25/05/2021	75mm C	28	Fletcher Bank
90661	25/05/2021	75mm C	28	Fletcher Bank
90659	25/05/2021	75mm C	28	Fletcher Bank
92372	25/05/2021	75mm C	28	Fletcher Bank
92373	25/05/2021	75mm C	28	Fletcher Bank
90664	26/05/2021	Type 1	28	Fletcher Bank
91531	26/05/2021	Type 1	28	Fletcher Bank
53001	26/05/2021	Type 1	28	Fletcher Bank
92374	26/05/2021	Type 1	28	Fletcher Bank
57166	26/05/2021	Type 1	28	Fletcher Bank
91532	26/05/2021	Type 1	28	Fletcher Bank
53002	26/05/2021	Type 1	28	Fletcher Bank
92375	26/05/2021	Type 1	28	Fletcher Bank
91535	27/05/2021	Type 1	28	Buckton Vale
92376	27/05/2021	6f5	28	Buckton Vale
93851	27/05/2021	6F5	28	Buckton Vale
57167	27/05/2021	6F5	28	Buckton Vale
91536	27/05/2021	6F5	28	Buckton Vale
92377	27/05/2021	6F5	28	Buckton Vale
93852	27/05/2021	6F5	28	Buckton Vale
91059	27/05/2021	6F5	28	Buckton Vale
57168	27/05/2021	6F5	28	Buckton Vale
92378	27/05/2021	Type 1	28	Buckton Vale
91537	27/05/2021	6F5	28	Buckton Vale
53003	27/05/2021	6F5	28	Buckton Vale
93853	27/05/2021	Type 1	28	Buckton Vale
57169	27/05/2021	Type 1	28	Buckton Vale
91061	27/05/2021	6F5	28	Buckton Vale
91538	27/05/2021	Type 1	28	Buckton Vale
92379	27/05/2021	Type 1	28	Buckton Vale
93854	27/05/2021	Type 1	28	Buckton Vale
90665	28/05/2021	Type 1	28	Buckton Vale

93855	28/05/2021	Type 1	28	Buckton Vale
57170	28/05/2021	Type 1	28	Buckton Vale
92380	28/05/2021	Type 1	28	Buckton Vale
93856	28/05/2021	Type 1	28	Buckton Vale
92381	28/05/2021	Type 1	28	Buckton Vale
90666	28/05/2021	Type 1	28	Buckton Vale
92382	28/05/2021	Type 1	28	Buckton Vale
57171	28/05/2021	Type 1	28	Buckton Vale
90667	28/05/2021	Type 1	28	Buckton Vale
93857	28/05/2021	Type 1	28	Buckton Vale
90671	01/06/2021	Type 1	28	Fletcher Bank
57178	01/06/2021	Type 1	28	Fletcher Bank
90673	01/06/2021	Type 1	28	Fletcher Bank
93862	01/06/2021	Type 1	28	Fletcher Bank
93864	01/06/2021	Type 1	28	Fletcher Bank
57179	01/06/2021	Type 1	28	Fletcher Bank
93866	02/06/2021	Type 1	28	Fletcher Bank
57187	02/06/2021	Type 1	28	Fletcher Bank
90678	02/06/2021	Type 1	28	Fletcher Bank
91541	02/06/2021	Type 1	28	Buckton Vale
54211	02/06/2021	Type 1	28	Fletcher Bank
53013	02/06/2021	Type 1	28	Fletcher Bank
92385	02/06/2021	Type 1	28	Fletcher Bank
93869	02/06/2021	Type 1	28	Fletcher Bank
57188	02/06/2021	Type 1	28	Fletcher Bank
90680	02/06/2021	Type 1	28	Fletcher Bank
91543	02/06/2021	Type 1	28	Buckton Vale
57189	02/06/2021	Type 1	28	Fletcher Bank
90682	02/06/2021	Type 1	28	Fletcher Bank
54214	02/06/2021	Type 1	28	Fletcher Bank
92388	02/06/2021	Type 1	28	Fletcher Bank
91545	02/06/2021	Type 1	28	Buckton Vale
93872	02/06/2021	Type 1	28	Fletcher Bank
57190	02/06/2021	Type 1	28	Fletcher Bank
90684	02/06/2021	Type 1	28	Fletcher Bank
54216	02/06/2021	Type 1	28	Fletcher Bank
91547	02/06/2021	Type 1	28	Buckton Vale
92390	02/06/2021	Type 1	28	Fletcher Bank
93874	02/06/2021	Type 1	28	Fletcher Bank
57191	02/06/2021	Type 1	28	Fletcher Bank
90686	02/06/2021	Type 1	28	Fletcher Bank
54218	02/06/2021	Type 1	28	Fletcher Bank
91549	02/06/2021	Type 1	28	Buckton Vale
92392	02/06/2021	Type 1	28	Fletcher Bank
93802	07/06/2021	Type 1	28	Buckton Vale
53017	07/06/2021	Type 1	28	Buckton Vale
92398	07/06/2021	Type 1	28	Buckton Vale
54221	07/06/2021	Type 1	28	Buckton Vale
93804	07/06/2021	Type 1	28	Buckton Vale
53019	07/06/2021	Type 1	28	Buckton Vale
92501	07/06/2021	Type 1	28	Buckton Vale
54223	07/06/2021	Type 1	28	Buckton Vale

92504	07/06/2021	Type 1	28	Buckton Vale
93806	07/06/2021	Type 1	28	Buckton Vale
53021	07/06/2021	Type 1	28	Buckton Vale
54225	07/06/2021	Type 1	28	Buckton Vale
53023	07/06/2021	6F5	28	Buckton Vale
92506	07/06/2021	6F5	28	Buckton Vale
93808	07/06/2021	6F5	28	Buckton Vale
54227	07/06/2021	6F5	28	Buckton Vale
53025	07/06/2021	6F5	28	Buckton Vale
92510	07/06/2021	6F5	28	Buckton Vale
90689	08/06/2021	6F5	28	Buckton Vale
92513	08/06/2021	6F5	28	Buckton Vale
53027	08/06/2021	6F5	28	Buckton Vale
54229	08/06/2021	6F5	28	Buckton Vale
92813	08/06/2021	6F5	28	Buckton Vale
90690	08/06/2021	6F5	28	Buckton Vale
92516	08/06/2021	6F5	28	Buckton Vale
93816	08/06/2021	6F5	28	Buckton Vale
53029	08/06/2021	6F5	28	Buckton Vale
54231	08/06/2021	6F5	28	Buckton Vale
90695	08/06/2021	6F5	28	Fletcher Bank
93894	09/06/2021	6F5	28	Fletcher Bank
91076	09/06/2021	Type 1	28	Buckton Vale
93896	09/06/2021	6F5	28	Buckton Vale
93823	09/06/2021	6F5	28	Buckton Vale
92523	09/06/2021	6F5	28	Buckton Vale
55111	09/06/2021	6F5	28	Buckton Vale
93898	09/06/2021	6F5	28	Buckton Vale
93835	15/06/2021	20mm C	28	Buckton Vale
93838	15/06/2021	20mm C	28	Buckton Vale
93842	15/06/2021	20mm C	28	Buckton Vale
90880	16/06/2021	6F5	28	Fletcher Bank
93846	16/06/2021	6F5	28	Fletcher Bank
55269	16/06/2021	6F5	28	Fletcher Bank
93240	16/06/2021	6F5	28	Fletcher Bank
56534	16/06/2021	6F5	28	Fletcher Bank
93242	16/06/2021	6F5	28	Fletcher Bank
55271	16/06/2021	6F5	28	Fletcher Bank
93848	16/06/2021	6F5	28	Fletcher Bank
90882	16/06/2021	6F5	28	Fletcher Bank
92452	16/06/2021	6F5	28	Fletcher Bank
56532	16/06/2021	6F5	28	Fletcher Bank
90774	16/06/2021	6F5	28	Fletcher Bank
55133	16/06/2021	6F5	28	Fletcher Bank
56554	16/06/2021	6F5	28	Fletcher Bank
53213	16/06/2021	6F5	28	Fletcher Bank
90776	16/06/2021	6F5	28	Fletcher Bank
56556	16/06/2021	6F5	28	Fletcher Bank
55135	16/06/2021	6F5	28	Fletcher Bank
53215	16/06/2021	6F5	28	Fletcher Bank
92454	16/06/2021	6F5	28	Fletcher Bank
55273	16/06/2021	6F5	28	Fletcher Bank

56051	16/06/2021	6F5	28	Fletcher Bank
90884	16/06/2021	6F5	28	Fletcher Bank
93244	16/06/2021	6F5	28	Fletcher Bank
56536	16/06/2021	6F5	28	Fletcher Bank
90778	16/06/2021	6F5	28	Fletcher Bank
56558	16/06/2021	6F5	28	Fletcher Bank
55275	16/06/2021	6F5	28	Fletcher Bank
53217	16/06/2021	6F5	28	Fletcher Bank
55137	16/06/2021	6F5	28	Fletcher Bank
90886	16/06/2021	6F5	28	Fletcher Bank
92456	16/06/2021	6F5	28	Fletcher Bank
90781	16/06/2021	Type 1	28	Buckton Vale
56559	16/06/2021	Type 1	28	Buckton Vale
56057	16/06/2021	Type 1	28	Buckton Vale
92459	16/06/2021	Type 1	28	Buckton Vale
93248	16/06/2021	Type 1	28	Buckton Vale
55138	16/06/2021	Type 1	28	Buckton Vale
56538	16/06/2021	Type 1	28	Buckton Vale
53219	16/06/2021	Type 1	28	Buckton Vale
90784	16/06/2021	Type 1	28	Buckton Vale
90887	17/06/2021	Type 1	28	Buckton Vale
55277	17/06/2021	Type 1	28	Buckton Vale
56561	17/06/2021	Type 1	28	Fletcher Bank
90787	17/06/2021	Type 1	28	Buckton Vale
92460	17/06/2021	Type 1	28	Buckton Vale
56059	17/06/2021	Type 1	28	Buckton Vale
55139	17/06/2021	Type 1	28	Buckton Vale
56563	17/06/2021	Type 1	28	Buckton Vale
92463	17/06/2021	Type 1	28	Buckton Vale
90790	17/06/2021	Type 1	28	Buckton Vale
56062	17/06/2021	Type 1	28	Buckton Vale
55142	17/06/2021	Type 1	28	Buckton Vale
56567	17/06/2021	Type 1	28	Buckton Vale
55280	17/06/2021	Type 1	28	Buckton Vale
56351	17/06/2021	Type 1	28	Buckton Vale
90793	17/06/2021	Type 1	28	Buckton Vale
92466	17/06/2021	Type 1	28	Buckton Vale
56065	17/06/2021	Type 1	28	Buckton Vale
55145	17/06/2021	Type 1	28	Buckton Vale
90890	17/06/2021	Type 1	28	Buckton Vale
56568	17/06/2021	Type 1	28	Buckton Vale
55282	17/06/2021	Type 1	28	Buckton Vale
56352	17/06/2021	Type 1	28	Buckton Vale
90797	17/06/2021	Type 1	28	Buckton Vale
92467	17/06/2021	Type 1	28	Buckton Vale
56066	17/06/2021	Type 1	28	Buckton Vale
55146	17/06/2021	Type 1	28	Buckton Vale
90893	17/06/2021	Type 1	28	Buckton Vale
91148	17/06/2021	Type 1	28	Buckton Vale
53044	18/06/2021	75mm C	28	Buckton Vale
210060	25/06/2021	Type 1	19	Buckton Vale
206036	25/06/2021	Type 1	19	Buckton Vale

213692	25/06/2021	Type 1	19	Buckton Vale
228865	25/06/2021	Type 1	19	Buckton Vale
208430	25/06/2021	Type 1	19	Buckton Vale
206038	25/06/2021	Type 1	19	Buckton Vale
55710	28/06/2021	Type 1	28	Buckton Vale
54271	28/06/2021	Type 1	28	Buckton Vale
55511	28/06/2021	Type 1	28	Buckton Vale
56579	28/06/2021	Type 1	28	Buckton Vale
53230	28/06/2021	Type 1	28	Fletcher Bank
53233	29/06/2021	Type 1	28	Buckton Vale
55713	29/06/2021	Type 1	28	Buckton Vale
228201	29/06/2021	Type 1	19	Buckton Vale
228881	29/06/2021	Type 1	19	Buckton Vale
225511	29/06/2021	Type 1	19	Buckton Vale
55718	30/06/2021	Type 1	28	Buckton Vale
55176	30/06/2021	Type 1	28	Buckton Vale
55177	30/06/2021	Type 1	28	Buckton Vale
55720	30/06/2021	Type 1	28	Buckton Vale
54276	30/06/2021	Type 1	28	Buckton Vale
55722	30/06/2021	Type 1	28	Buckton Vale
226262	02/07/2021	20mm C	19	Buckton Vale
214677	05/07/2021	Type 1	19	Buckton Vale
228499	05/07/2021	Type 1	19	Buckton Vale
226265	05/07/2021	Type 1	19	Buckton Vale
210071	05/07/2021	Type 1	19	Buckton Vale
230626	05/07/2021	Type 1	19	Buckton Vale
206281	05/07/2021	Type 1	19	Buckton Vale
210125	05/07/2021	Type 1	19	Buckton Vale
228401	05/07/2021	Type 1	19	Buckton Vale
210377	05/07/2021	Type 1	19	Buckton Vale
228573	05/07/2021	Type 1	19	Buckton Vale
214680	05/07/2021	Type 1	19	Buckton Vale
228575	05/07/2021	Type 1	19	Buckton Vale
210379	05/07/2021	Type 1	19	Buckton Vale
210127	05/07/2021	Type 1	19	Buckton Vale
227804	05/07/2021	Type 1	19	Buckton Vale
227798	05/07/2021	Type 1	19	Buckton Vale
214696	06/07/2021	75mm C	19	Buckton Vale
230636	06/07/2021	75mm C	19	Buckton Vale
210136	06/07/2021	75mm C	19	Buckton Vale
230646	07/07/2021	75mm C	19	Buckton Vale
226287	07/07/2021	75mm C	19	Buckton Vale
227821	07/07/2021	75mm C	19	Buckton Vale
232314	07/07/2021	75mm C	19	Buckton Vale
210089	07/07/2021	75mm C	19	Buckton Vale
206292	07/07/2021	75mm C	19	Buckton Vale
54284	08/07/2021	75mm C	28	Buckton Vale
232316	08/07/2021	75mm C	19	Buckton Vale
56419	08/07/2021	75mm C	28	Buckton Vale
56424	08/07/2021	75mm C	28	Buckton Vale
54286	08/07/2021	75mm C	28	Buckton Vale

56428	08/07/2021	75mm C	28	Buckton Vale
54288	08/07/2021	75mm C	28	Buckton Vale
231903	20/07/2021	Type 1	19	Buckton Vale
55621	20/07/2021	Type 1	28	Buckton Vale
55543	20/07/2021	Type 1	28	Buckton Vale
55886	20/07/2021	Type 1	28	Buckton Vale
90970	20/07/2021	Type 1	28	Buckton Vale
55625	20/07/2021	Type 1	28	Buckton Vale
55541	20/07/2021	Type 1	28	Buckton Vale
55883	20/07/2021	Type 1	28	Buckton Vale
90968	20/07/2021	Type 1	28	Buckton Vale
55623	20/07/2021	Type 1	28	Buckton Vale
55539	20/07/2021	Type 1	28	Buckton Vale
55880	20/07/2021	Type 1	28	Buckton Vale
90966	20/07/2021	Type 1	28	Buckton Vale
54808	20/07/2021	75mm C	28	Buckton Vale
231901	20/07/2021	Type 1	19	Buckton Vale
21048	20/07/2021	Type 1	19	Buckton Vale
210347	20/07/2021	Type 1	19	Buckton Vale
210346	20/07/2021	Type 1	19	Buckton Vale
210344	20/07/2021	Type 1	19	Buckton Vale
210345	20/07/2021	Type 1	19	Buckton Vale
210349	20/07/2021	Type 1	19	Buckton Vale
210350	20/07/2021	Type 1	19	Buckton Vale
210342	20/07/2021	Type 1	19	Buckton Vale
210343	20/07/2021	Type 1	19	Buckton Vale
231902	20/07/2021	Type 1	19	Buckton Vale
55627	20/07/2021	Type 1	28	Buckton Vale
90972	20/07/2021	Type 1	28	Buckton Vale
55889	20/07/2021	Type 1	28	Buckton Vale
231905	20/07/2021	Type 1	19	Buckton Vale
55545	20/07/2021	Type 1	28	Buckton Vale
54812	20/07/2021	20mm C	28	Buckton Vale
56012	26/07/2021	6f5	28	Buckton Vale
55754	26/07/2021	6f5	28	Buckton Vale
55467	26/07/2021	6f5	28	Buckton Vale
90994	26/07/2021	6f5	28	Buckton Vale
55469	27/07/2021	Type 1	28	Buckton Vale
56016	27/07/2021	Type 1	28	Buckton Vale
91939	27/07/2021	Type 1	28	Buckton Vale
56275	27/07/2021	Type 1	28	Buckton Vale
55756	27/07/2021	Type 1	28	Buckton Vale
56751	27/07/2021	Type 1	28	Buckton Vale
90996	27/07/2021	Type 1	28	Buckton Vale
56278	28/07/2021	6f5	28	Buckton Vale
91942	28/07/2021	6f5	28	Buckton Vale
90997	28/07/2021	6f5	28	Buckton Vale
56018	28/07/2021	6f5	28	Buckton Vale
35935	28/07/2021	6f5	28	Buckton Vale
55471	29/07/2021	Type 1	28	Buckton Vale
54830	29/07/2021	Type 1	28	Buckton Vale

56019	29/07/2021	Type 1	28	Buckton Vale
231594	03/08/2021	Type 1	19	Buckton Vale
91000	03/08/2021	Type 1	28	Buckton Vale
56022	03/08/2021	Type 1	28	Buckton Vale
233031	03/08/2021	Type 1	19	Buckton Vale
214788	03/08/2021	Type 1	19	Buckton Vale
205582	03/08/2021	Type 1	19	Buckton Vale
233035	03/08/2021	Type 1	19	Buckton Vale
56952	03/08/2021	Type 1	28	Buckton Vale
56025	03/08/2021	Type 1	28	Buckton Vale
214791	03/08/2021	Type 1	19	Buckton Vale
56030	03/08/2021	Type 1	28	Buckton Vale
56954	03/08/2021	Type 1	28	Buckton Vale
205585	03/08/2021	Type 1	19	Buckton Vale
57689	06/08/2021	Type 1	28	Buckton Vale
56033	06/08/2021	Type 1	28	Buckton Vale
92440	06/08/2021	Type 1	28	Buckton Vale
56752	06/08/2021	Type 1	28	Buckton Vale
55078	06/08/2021	Type 1	28	Buckton Vale
57801	06/08/2021	Type 1	28	Buckton Vale
55080	06/08/2021	Type 1	28	Buckton Vale
92441	06/08/2021	Type 1	28	Buckton Vale
56034	06/08/2021	Type 1	28	Buckton Vale
56753	06/08/2021	Type 1	28	Buckton Vale
57690	06/08/2021	Type 1	28	Buckton Vale
57802	06/08/2021	Type 1	28	Buckton Vale
92442	06/08/2021	Type 1	28	Buckton Vale
55082	06/08/2021	Type 1	28	Buckton Vale
57691	06/08/2021	Type 1	28	Buckton Vale
56035	06/08/2021	Type 1	28	Buckton Vale
56754	06/08/2021	Type 1	28	Buckton Vale
57804	06/08/2021	Type 1	28	Buckton Vale
56755	06/08/2021	Type 1	28	Buckton Vale
56036	06/08/2021	Type 1	28	Buckton Vale
55084	06/08/2021	Type 1	28	Buckton Vale
57692	06/08/2021	Type 1	28	Buckton Vale
92443	06/08/2021	Type 1	28	Buckton Vale
57803	06/08/2021	Type 1	28	Buckton Vale
56957	11/08/2021	75 mm C	28	Fletcher Bank
56037	11/08/2021	75 mm C	28	Fletcher Bank
55472	11/08/2021	75 mm C	28	Fletcher Bank
57752	11/08/2021	75 mm C	28	Fletcher Bank
55473	11/08/2021	75 mm C	28	Fletcher Bank
56038	11/08/2021	75 mm C	28	Fletcher Bank
56958	11/08/2021	75 mm C	28	Fletcher Bank
57753	11/08/2021	75 mm C	28	Fletcher Bank
234111	13/08/2021	6f5	19	Fletcher Bank
235416	13/08/2021	6f5	19	Fletcher Bank
236399	13/08/2021	6f5	19	Fletcher Bank
232230	13/08/2021	6f5	19	Fletcher Bank
203489	13/08/2021	6f5	19	Fletcher Bank
233165	13/08/2021	6f5	19	Fletcher Bank

234109	13/08/2021	6f5	19	Fletcher Bank
233331	13/08/2021	6f5	19	Fletcher Bank
229384	13/08/2021	6f5	19	Fletcher Bank
235805	13/08/2021	6f5	19	Fletcher Bank
236397	13/08/2021	6f5	19	Fletcher Bank
235413	13/08/2021	6f5	19	Fletcher Bank
232227	13/08/2021	6f5	19	Fletcher Bank
236394	13/08/2021	6f5	19	Fletcher Bank
233329	13/08/2021	6f5	19	Fletcher Bank
229382	13/08/2021	6f5	19	Fletcher Bank
203486	13/08/2021	6f5	19	Fletcher Bank
233162	13/08/2021	6f5	19	Fletcher Bank
233159	13/08/2021	6f5	19	Fletcher Bank
232224	13/08/2021	6f5	19	Fletcher Bank
235410	13/08/2021	6f5	19	Fletcher Bank
235803	13/08/2021	6f5	19	Fletcher Bank
234107	13/08/2021	6f5	19	Fletcher Bank
56762	16/08/2021	6f5	28	Buckton Vale
56964	16/08/2021	6f5	28	Buckton Vale
57762	16/08/2021	6f5	28	Buckton Vale
57759	16/08/2021	6f5	28	Buckton Vale
56962	16/08/2021	6f5	28	Buckton Vale
56760	16/08/2021	6f5	28	Buckton Vale
56960	16/08/2021	6f5	28	Buckton Vale
57756	16/08/2021	6f5	28	Buckton Vale
56757	16/08/2021	6f5	28	Buckton Vale
56966	16/08/2021	6f5	28	Buckton Vale
56764	16/08/2021	6f5	28	Buckton Vale
57765	16/08/2021	6f5	28	Buckton Vale
55493	19/08/2021	75 mm C	28	Buckton Vale
54915	19/08/2021	75 mm C	28	Buckton Vale
56979	19/08/2021	75 mm C	28	Buckton Vale
55768	19/08/2021	75 mm C	28	Buckton Vale
92581	27/08/2021	6f5	28	Fletcher Bank
55789	27/08/2021	6f5	28	Fletcher Bank
54930	27/08/2021	6f5	28	Fletcher Bank
57262	27/08/2021	6f5	28	Fletcher Bank
54994	27/08/2021	6f5	28	Fletcher Bank
54834	27/08/2021	6f5	28	Fletcher Bank
57779	27/08/2021	6f5	28	Fletcher Bank
54835	27/08/2021	Type 1	28	Buckton Vale
54997	27/08/2021	Type 1	28	Buckton Vale
57264	27/08/2021	Type 1	28	Buckton Vale
54933	27/08/2021	Type 1	28	Buckton Vale
55792	27/08/2021	Type 1	28	Buckton Vale
92583	27/08/2021	Type 1	28	Buckton Vale
57781	27/08/2021	Type 1	28	Buckton Vale
55793	27/08/2021	Type 1	28	Buckton Vale
54936	27/08/2021	Type 1	28	Buckton Vale
57266	27/08/2021	Type 1	28	Buckton Vale
92586	27/08/2021	Type 1	28	Buckton Vale
55000	27/08/2021	Type 1	28	Buckton Vale

54838	27/08/2021	Type 1	28	Buckton Vale
57783	27/08/2021	Type 1	28	Buckton Vale
92598	01/09/2021	Type 1	28	Buckton Vale
54351	01/09/2021	Type 1	28	Buckton Vale
54356	01/09/2021	Type 1	28	Buckton Vale
54360	01/09/2021	Type 1	28	Buckton Vale
229569	08/09/2021	Type 1	19	Buckton Vale
200200	08/09/2021	Type 1	19	Buckton Vale
242154	08/09/2021	Type 1	19	Buckton Vale
232034	08/09/2021	Type 1	19	Buckton Vale
237343	08/09/2021	Type 1	19	Buckton Vale
242156	08/09/2021	Type 1	19	Buckton Vale
232036	08/09/2021	Type 1	19	Buckton Vale
237344	08/09/2021	Type 1	19	Buckton Vale
222453	08/09/2021	Type 1	19	Buckton Vale
229573	08/09/2021	Type 1	19	Buckton Vale
229579	09/09/2021	Type 1	19	Buckton Vale
234040	09/09/2021	Type 1	19	Buckton Vale
222464	09/09/2021	Type 1	19	Buckton Vale
235012	09/09/2021	Type 1	19	Buckton Vale
242305	09/09/2021	Type 1	19	Buckton Vale
229582	09/09/2021	Type 1	19	Buckton Vale
234043	09/09/2021	Type 1	19	Buckton Vale
222460	09/09/2021	Type 1	19	Buckton Vale
235009	09/09/2021	Type 1	19	Buckton Vale
242302	09/09/2021	Type 1	19	Buckton Vale
241454	09/09/2021	20mm C	19	Buckton Vale
88357	16/09/2021	Type 1	28	Buckton Vale
54560	16/09/2021	Type 1	28	Buckton Vale
55326	16/09/2021	Type 1	28	Buckton Vale
56230	16/09/2021	Type 1	28	Buckton Vale
55329	16/09/2021	Type 1	28	Buckton Vale
56233	16/09/2021	Type 1	28	Buckton Vale
88359	16/09/2021	Type 1	28	Buckton Vale
54563	16/09/2021	Type 1	28	Buckton Vale
243787	16/09/2021	Type 1	28	Buckton Vale
55332	16/09/2021	Type 1	28	Buckton Vale
56236	16/09/2021	Type 1	28	Buckton Vale
54566	16/09/2021	Type 1	28	Buckton Vale
88361	16/09/2021	Type 1	28	Buckton Vale
55335	16/09/2021	6f5	28	Buckton Vale
56239	16/09/2021	6f5	28	Buckton Vale
54569	16/09/2021	6f5	28	Buckton Vale
88363	16/09/2021	6f5	28	Buckton Vale
252381	17/09/2021	Type 1	19	Buckton Vale
54577	17/09/2021	Type 1	28	Buckton Vale
88574	17/09/2021	Type 1	28	Buckton Vale
236845	17/09/2021	Type 1	19	Buckton Vale
243866	17/09/2021	Type 1	19	Buckton Vale
54583	20/09/2021	Type 1	28	Buckton Vale
53838	20/09/2021	Type 1	28	Buckton Vale

54580	20/09/2021	Type 1	28	Buckton Vale
53840	20/09/2021	Type 1	28	Buckton Vale
54586	20/09/2021	Type 1	28	Buckton Vale
54589	20/09/2021	Type 1	28	Buckton Vale
54593	21/09/2021	Type 1	28	Buckton Vale
240260	21/09/2021	Type 1	19	Buckton Vale
54596	21/09/2021	Type 1	28	Buckton Vale
54599	21/09/2021	Type 1	28	Buckton Vale
86252	21/09/2021	Type 1	28	Buckton Vale
86256	22/09/2021	Type 1	28	Buckton Vale
87309	22/09/2021	Type 1	28	Buckton Vale
56863	22/09/2021	Type 1	28	Buckton Vale
88377	22/09/2021	Type 1	28	Buckton Vale
87312	22/09/2021	Type 1	28	Buckton Vale
86259	22/09/2021	Type 1	28	Buckton Vale
56866	22/09/2021	Type 1	28	Buckton Vale
88379	22/09/2021	Type 1	28	Buckton Vale
86262	22/09/2021	Type 1	28	Buckton Vale
87315	22/09/2021	Type 1	28	Buckton Vale
211021	24/09/2021	Type 1	19	Buckton Vale
241372	24/09/2021	Type 1	19	Buckton Vale
244940	24/09/2021	Type 1	19	Buckton Vale
214958	24/09/2021	Type 1	19	Buckton Vale
241641	24/09/2021	Type 1	19	Buckton Vale
241369	24/09/2021	Type 1	19	Buckton Vale
211018	24/09/2021	Type 1	19	Buckton Vale
244937	24/09/2021	Type 1	19	Buckton Vale
241995	24/09/2021	Type 1	19	Buckton Vale
241639	24/09/2021	Type 1	19	Buckton Vale
57300	29/09/2021	Type 1	28	Buckton Vale
55552	29/09/2021	Type 1	28	Buckton Vale
181026	07/10/2021	75 mm C	19	Buckton Vale
239441	07/10/2021	75 mm C	19	Buckton Vale
240210	07/10/2021	75 mm C	19	Buckton Vale
244194	07/10/2021	75 mm C	19	Buckton Vale
240921	07/10/2021	75 mm C	19	Buckton Vale
240490	07/10/2021	75 mm C	19	Buckton Vale
181028	07/10/2021	75 mm C	19	Buckton Vale
244197	08/10/2021	75 mm C	19	Buckton Vale
239445	08/10/2021	75 mm C	19	Buckton Vale
243580	08/10/2021	75 mm C	19	Buckton Vale
240493	08/10/2021	75 mm C	19	Buckton Vale
243584	08/10/2021	75 mm C	19	Buckton Vale
239448	08/10/2021	75 mm C	19	Buckton Vale
240496	08/10/2021	75 mm C	19	Buckton Vale
243587	08/10/2021	75 mm C	19	Buckton Vale
240858	08/10/2021	75 mm C	19	Buckton Vale
240499	08/10/2021	75 mm C	19	Buckton Vale
240862	08/10/2021	75 mm C	19	Buckton Vale
243590	08/10/2021	75 mm C	19	Buckton Vale
240552	08/10/2021	75 mm C	19	Buckton Vale

240557	11/10/2021	6f5	19	Buckton Vale
239957	11/10/2021	Type 1	19	Buckton Vale
242500	11/10/2021	Type 1	19	Buckton Vale
238734	11/10/2021	6F5	19	Buckton Vale
240560	11/10/2021	6F5	19	Buckton Vale
239960	11/10/2021	Type 1	19	Buckton Vale
242497	11/10/2021	Type 1	19	Buckton Vale
238737	11/10/2021	6F5	19	Buckton Vale
240563	11/10/2021	6F5	19	Buckton Vale
237952	11/10/2021	Type 1	19	Buckton Vale
239963	11/10/2021	Type 1	19	Buckton Vale
238891	12/10/2021	6F5	19	Buckton Vale
58076	13/10/2021	75mm C	28	Buckton Vale
92062	13/10/2021	75mm C	28	Buckton Vale
58077	13/10/2021	75mm C	28	Buckton Vale
92064	13/10/2021	75mm C	28	Buckton Vale
92065	13/10/2021	75mm C	28	Buckton Vale
58078	13/10/2021	75mm C	28	Buckton Vale
87414	13/10/2021	6f5	28	Buckton Vale
88427	13/10/2021	6f5	28	Buckton Vale
86310	13/10/2021	6f5	28	Buckton Vale
57037	13/10/2021	6f5	28	Buckton Vale
87835	13/10/2021	6f5	28	Buckton Vale
87836	13/10/2021	6f5	28	Buckton Vale
57038	13/10/2021	6f5	28	Buckton Vale
240232	13/10/2021	6f5	28	Buckton Vale
86311	13/10/2021	6f5	28	Buckton Vale
88428	13/10/2021	6f5	28	Buckton Vale
87415	13/10/2021	6f5	28	Buckton Vale
87419	13/10/2021	6f5	28	Buckton Vale
88429	13/10/2021	6f5	28	Buckton Vale
88430	13/10/2021	6f5	28	Buckton Vale
86312	13/10/2021	6f5	28	Buckton Vale
87837	13/10/2021	6f5	28	Buckton Vale
86313	13/10/2021	6f5	28	Buckton Vale
92068	14/10/2021	6f5	28	Buckton Vale
87339	14/10/2021	6f5	28	Buckton Vale
88431	14/10/2021	6f5	28	Buckton Vale
92070	14/10/2021	6f5	28	Buckton Vale
88432	14/10/2021	6f5	28	Buckton Vale
87340	14/10/2021	6f5	28	Buckton Vale
238002	15/10/2021	6f5	19	Buckton Vale
237387	15/10/2021	6f5	19	Buckton Vale
240580	15/10/2021	6f5	19	Buckton Vale
234062	15/10/2021	6f5	19	Buckton Vale
237553	15/10/2021	6f5	19	Buckton Vale
234065	15/10/2021	6f5	19	Buckton Vale
240583	15/10/2021	6f5	19	Buckton Vale
87842	18/102021	6F5	28	Buckton Vale
55595	18/10/2021	6F5	28	Buckton Vale
86320	18/10/2021	6F5	28	Buckton Vale
89806	18/10/2021	6F5	28	Buckton Vale

247230	18/10/2021	6f5	19	Buckton Vale
55597	18/10/2021	6f5	28	Buckton Vale
87854	18/10/2021	6f5	28	Buckton Vale
241054	18/10/2021	6f5	19	Buckton Vale
247406	18/10/2021	6f5	19	Buckton Vale
241802	18/10/2021	6f5	19	Buckton Vale
214050	18/10/2021	6f5	19	Buckton Vale
240593	18/10/2021	6f5	19	Buckton Vale
238168	18/10/2021	6f5	19	Buckton Vale
243671	21/10/2021	6f5	19	Buckton Vale
246401	22/10/2021	6f5	19	Buckton Vale
245452	22/10/2021	6f5	19	Buckton Vale
243675	22/10/2021	6f5	19	Buckton Vale
237599	22/10/2021	6f5	19	Buckton Vale
237718	22/10/2021	6f5	19	Buckton Vale
238069	25/10/2021	6f5	19	Buckton Vale
245461	25/10/2021	6f5	19	Buckton Vale
238072	25/10/2021	6f5	19	Buckton Vale
245463	25/10/2021	6f5	19	Buckton Vale
245465	25/10/2021	6f5	19	Buckton Vale
245467	25/10/2021	6f5	19	Buckton Vale
238077	25/10/2021	6f5	19	Buckton Vale
245556	26/10/2021	6f5	19	Buckton Vale
241816	26/10/2021	6f5	19	Buckton Vale
245561	26/10/2021	6f5	19	Buckton Vale
241819	26/10/2021	6F5	19	Buckton Vale
241822	26/10/2021	6f5	19	Buckton Vale
247447	26/10/2021	6f5	19	Buckton Vale
194973	28/10/2021	20 mm C	19	Buckton Vale
247614	28/10/2021	20 mm C	19	Buckton Vale
91479	09/11/2021	6f5	28	Buckton Vale
89659	09/11/2021	6f5	28	Buckton Vale
55436	09/11/2021	6f5	28	Buckton Vale
91481	09/11/2021	6f5	28	Buckton Vale
89661	09/11/2021	6f5	28	Buckton Vale
55438	09/11/2021	6f5	28	Buckton Vale
91483	09/11/2021	6f5	28	Buckton Vale
89664	09/11/2021	6f5	28	Buckton Vale
55440	09/11/2021	6f5	28	Buckton Vale
91485	09/11/2021	6f5	28	Buckton Vale
89667	09/11/2021	6f5	28	Buckton Vale
55442	09/11/2021	6f5	28	Buckton Vale
89670	09/11/2021	6f5	28	Buckton Vale
57301	09/11/2021	6f5	28	Buckton Vale
55444	09/11/2021	6f5	28	Buckton Vale
57303	10/11/2021	Type 1	28	Buckton Vale
24311	10/11/2021	Type 1	19	Buckton Vale
86592	10/11/2021	Type 1	28	Buckton Vale
246772	10/11/2021	Type 1	19	Buckton Vale
247978	10/11/2021	Type 1	19	Buckton Vale
56665	10/11/2021	Type 1	28	Buckton Vale

55446	10/11/2021	Type 1	28	Buckton Vale
89673	10/11/2021	Type 1	28	Buckton Vale
247186	10/11/2021	Type 1	19	Buckton Vale
57305	10/11/2021	Type 1	28	Buckton Vale
243314	10/11/2021	Type 1	19	Buckton Vale
86595	10/11/2021	Type 1	28	Buckton Vale
246775	10/11/2021	Type 1	19	Buckton Vale
89676	10/11/2021	Type 1	28	Buckton Vale
56668	10/11/2021	Type 1	28	Buckton Vale
55448	10/11/2021	Type 1	28	Buckton Vale
247189	10/11/2021	Type 1	19	Buckton Vale
243317	10/11/2021	Type 1	19	Buckton Vale
57307	10/11/2021	Type 1	28	Buckton Vale
246778	10/11/2021	Type 1	19	Buckton Vale
86598	10/11/2021	Type 1	28	Buckton Vale
56671	10/11/2021	Type 1	28	Buckton Vale
55450	10/11/2021	Type 1	28	Buckton Vale
89679	10/11/2021	Type 1	28	Buckton Vale
57309	10/11/2021	Type 1	28	Buckton Vale
247192	10/11/2021	Type 1	19	Buckton Vale
243320	10/11/2021	Type 1	19	Buckton Vale
246781	10/11/2021	Type 1	19	Buckton Vale
54401	10/11/2021	Type 1	19	Buckton Vale
244611	10/11/2021	Type 1	28	Buckton Vale
56674	10/11/2021	Type 1	28	Buckton Vale
89682	10/11/2021	Type 1	28	Buckton Vale
57311	10/11/2021	Type 1	28	Buckton Vale
89682	10/11/2021	Type 1	28	Buckton Vale
56602	11/11/2021	Type 1	28	Buckton Vale
242573	11/11/2021	10mm clean	19	Buckton Vale
247987	11/11/2021	Type 1	19	Buckton Vale
54404	11/11/2021	Type 1	28	Buckton Vale
89684	11/11/2021	Type 1	28	Buckton Vale
56604	11/11/2021	Type 1	28	Buckton Vale
56677	11/11/2021	Type 1	28	Buckton Vale
57315	11/11/2021	Type 1	28	Buckton Vale
247990	11/11/2021	Type 1	19	Buckton Vale
56606	11/11/2021	Type 1	28	Buckton Vale
56681	11/11/2021	Type 1	28	Buckton Vale
89686	11/11/2021	Type 1	28	Buckton Vale
54407	11/11/2021	Type 1	28	Buckton Vale
57317	11/11/2021	Type 1	28	Buckton Vale
247993	11/11/2021	Type 1	19	Buckton Vale
56683	11/11/2021	Type 1	28	Buckton Vale
56608	11/11/2021	Type 1	28	Buckton Vale
54410	11/11/2021	Type 1	28	Buckton Vale
89688	11/11/2021	Type 1	28	Buckton Vale
242577	11/11/2021	10mm clean	19	Buckton Vale
57319	11/11/2021	Type 1	28	Buckton Vale
56610	11/11/2021	Type 1	28	Buckton Vale
56686	11/11/2021	Type 1	28	Buckton Vale
54413	11/11/2021	Type 1	28	Buckton Vale

242579	11/11/2021	10mm clean	19	Buckton Vale
247997	11/11/2021	Type 1	19	Buckton Vale
89690	11/11/2021	Type 1	28	Buckton Vale
57323	12/11/2021	Type 1	28	Buckton Vale
54418	12/11/2021	Type 1	28	Buckton Vale
89694	12/11/2021	Type 1	28	Buckton Vale
56614	12/11/2021	Type 1	28	Buckton Vale
56692	12/11/2021	Type 1	28	Buckton Vale
242583	12/11/2021	75mm C	19	Buckton Vale
89696	12/11/2021	75mm C	28	Buckton Vale
56616	12/11/2021	75mm C	28	Buckton Vale
56696	12/11/2021	75mm C	28	Buckton Vale
57325	12/11/2021	75mm C	28	Buckton Vale
54421	12/11/2021	75mm C	28	Buckton Vale
242585	12/11/2021	75mm C	19	Buckton Vale
56624	15/11/2021	75mm C	28	Buckton Vale
57334	15/11/2021	75mm C	28	Buckton Vale
57339	16/11/2021	6f5	28	Buckton Vale
56631	16/11/2021	6f5	28	Buckton Vale
56170	16/11/2021	6f5	28	Buckton Vale
88951	22/11/2021	75mm C	28	Buckton Vale
56194	22/11/2021	Type 1	28	Buckton Vale
88953	22/11/2021	75mm C	28	Buckton Vale
56197	22/11/2021	Type 1	28	Buckton Vale
88955	22/11/2021	75mm C	28	Buckton Vale
56699	22/11/2021	Type 1	28	Buckton Vale
88957	22/11/2021	75mm C	28	Buckton Vale
91002	22/11/2021	Type 1	28	Buckton Vale
87171	24/11/2021	6f5	28	Buckton Vale
91012	24/11/2021	6f5	28	Buckton Vale
97173	24/11/2021	6f5	28	Buckton Vale
91015	24/11/2021	6f5	28	Buckton Vale
91018	24/11/2021	6f5	28	Buckton Vale
87175	24/11/2021	6f5	28	Buckton Vale
91022	24/11/2021	6f5	28	Buckton Vale
87177	24/11/2021	6f5	28	Buckton Vale
87810	25/11/2021	6f5	28	Buckton Vale
87182	25/11/2021	6f5	28	Buckton Vale
87184	25/11/2021	6f5	28	Buckton Vale
87186	25/11/2021	6f5	28	Buckton Vale
93607	26/11/2021	6f5	28	Buckton Vale
87189	26/11/2021	6f5	28	Buckton Vale
91032	26/11/2021	6f5	28	Buckton Vale
88965	26/11/2021	6f5	28	Buckton Vale
93609	26/11/2021	6f5	28	Buckton Vale
87191	26/11/2021	6f5	28	Buckton Vale
91036	26/11/2021	6f5	28	Buckton Vale
88967	26/11/2021	6f5	28	Buckton Vale
93611	26/11/2021	6f5	28	Buckton Vale
87193	26/11/2021	6f5	28	Buckton Vale
86658	26/11/2021	6f5	28	Buckton Vale


91039	26/11/2021	6f5	28	Buckton Vale
88969	26/11/2021	6f5	28	Buckton Vale
93613	26/11/2021	6f5	28	Buckton Vale
87195	26/11/2021	6f5	28	Buckton Vale
86660	26/11/2021	6f5	28	Buckton Vale
91042	26/11/2021	6f5	28	Buckton Vale
86663	02/12/2021	6f5	28	Buckton Vale
93633	02/12/2021	6f5	28	Buckton Vale
88624	02/12/2021	6f5	28	Buckton Vale
88990	02/12/2021	6f5	28	Buckton Vale
70187	02/12/2021	6f5	28	Buckton Vale
86665	02/12/2021	6f5	28	Buckton Vale
93635	02/12/2021	6f5	28	Buckton Vale
88627	02/12/2021	6f5	28	Buckton Vale
88992	02/12/2021	6f5	28	Buckton Vale
70190	02/12/2021	6f5	28	Buckton Vale
93637	02/12/2021	6f5	28	Buckton Vale
86667	02/12/2021	6f5	28	Buckton Vale
88630	02/12/2021	6f5	28	Buckton Vale
88994	02/12/2021	6f5	28	Buckton Vale
70193	02/12/2021	6f5	28	Buckton Vale
86634	02/12/2021	6f5	28	Buckton Vale
93639	02/12/2021	6f5	28	Buckton Vale
88633	02/12/2021	6f5	28	Buckton Vale
88996	02/12/2021	6f5	28	Buckton Vale
70196	02/12/2021	6f5	28	Buckton Vale
239857	02/12/2021	6f5	19	Buckton Vale
257236	02/12/2021	20mm C	19	Buckton Vale
86636	02/12/2021	6f5	28	Buckton Vale
54547	03/12/2021	6f5	28	Buckton Vale
88637	03/12/2021	6f5	28	Buckton Vale
86639	03/12/2021	6f5	28	Buckton Vale
88999	03/12/2021	6f5	28	Buckton Vale
93642	03/12/2021	6f5	28	Buckton Vale
70200	03/12/2021	6f5	28	Buckton Vale
308216	03/12/2021	75mm C	19	GRS
13816	03/12/2021	75mm C	19	Tyrone
315260	03/12/2021	75mm C	19	GRS
17498	03/12/2021	75mm C	19	GRS
308217	03/12/2021	75mm C	19	GRS
315261	03/12/2021	75mm C	19	GRS
54550	03/12/2021	6f5	28	Buckton Vale
88639	03/12/2021	6f5	28	Buckton Vale
88901	03/12/2021	6f5	28	Buckton Vale
86641	03/12/2021	6f5	28	Buckton Vale
612151	03/12/2021	75mm C	19	GRS
93644	03/12/2021	6f5	28	Buckton Vale
70103	03/12/2021	6f5	28	Buckton Vale
308218	03/12/2021	75mm C	19	GRS
315262	03/12/2021	75mm C	19	GRS
88640	03/12/2021	6f5	28	Buckton Vale
54451	03/12/2021	6f5	28	Buckton Vale

88902	03/12/2021	6f5	28	Buckton Vale
86669	03/12/2021	6f5	28	Buckton Vale
612152	03/12/2021	75mm C	19	GRS
93646	03/12/2021	6f5	28	Buckton Vale
70107	03/12/2021	6f5	28	Buckton Vale
16783	03/12/2021	75mm C	19	GRS
308219	03/12/2021	75mm C	19	GRS
315263	03/12/2021	75mm C	19	GRS
17499	03/12/2021	75mm C	19	GRS
13818	03/12/2021	75mm C	19	GRS
612153	03/12/2021	75mm C	19	GRS
308220	03/12/2021	75mm C	19	GRS
54452	03/12/2021	6f5	28	Buckton Vale
88641	03/12/2021	6f5	28	Buckton Vale
88903	03/12/2021	6f5	28	Buckton Vale
86670	03/12/2021	6f5	28	Buckton Vale
93648	03/12/2021	6f5	28	Buckton Vale
16784	03/12/2021	75mm C	19	GRS
315264	03/12/2021	75mm C	19	GRS
70109	03/12/2021	6f5	28	Buckton Vale
308221	03/12/2021	75mm C	19	GRS
315265	03/12/2021	75mm C	19	GRS
14531	03/12/2021	75mm C	19	GRS
14689	03/12/2021	75mm C	19	GRS

APPENDIX E Waste Consignment Notes

(To be provided on request)

APPENDIX F Surveys

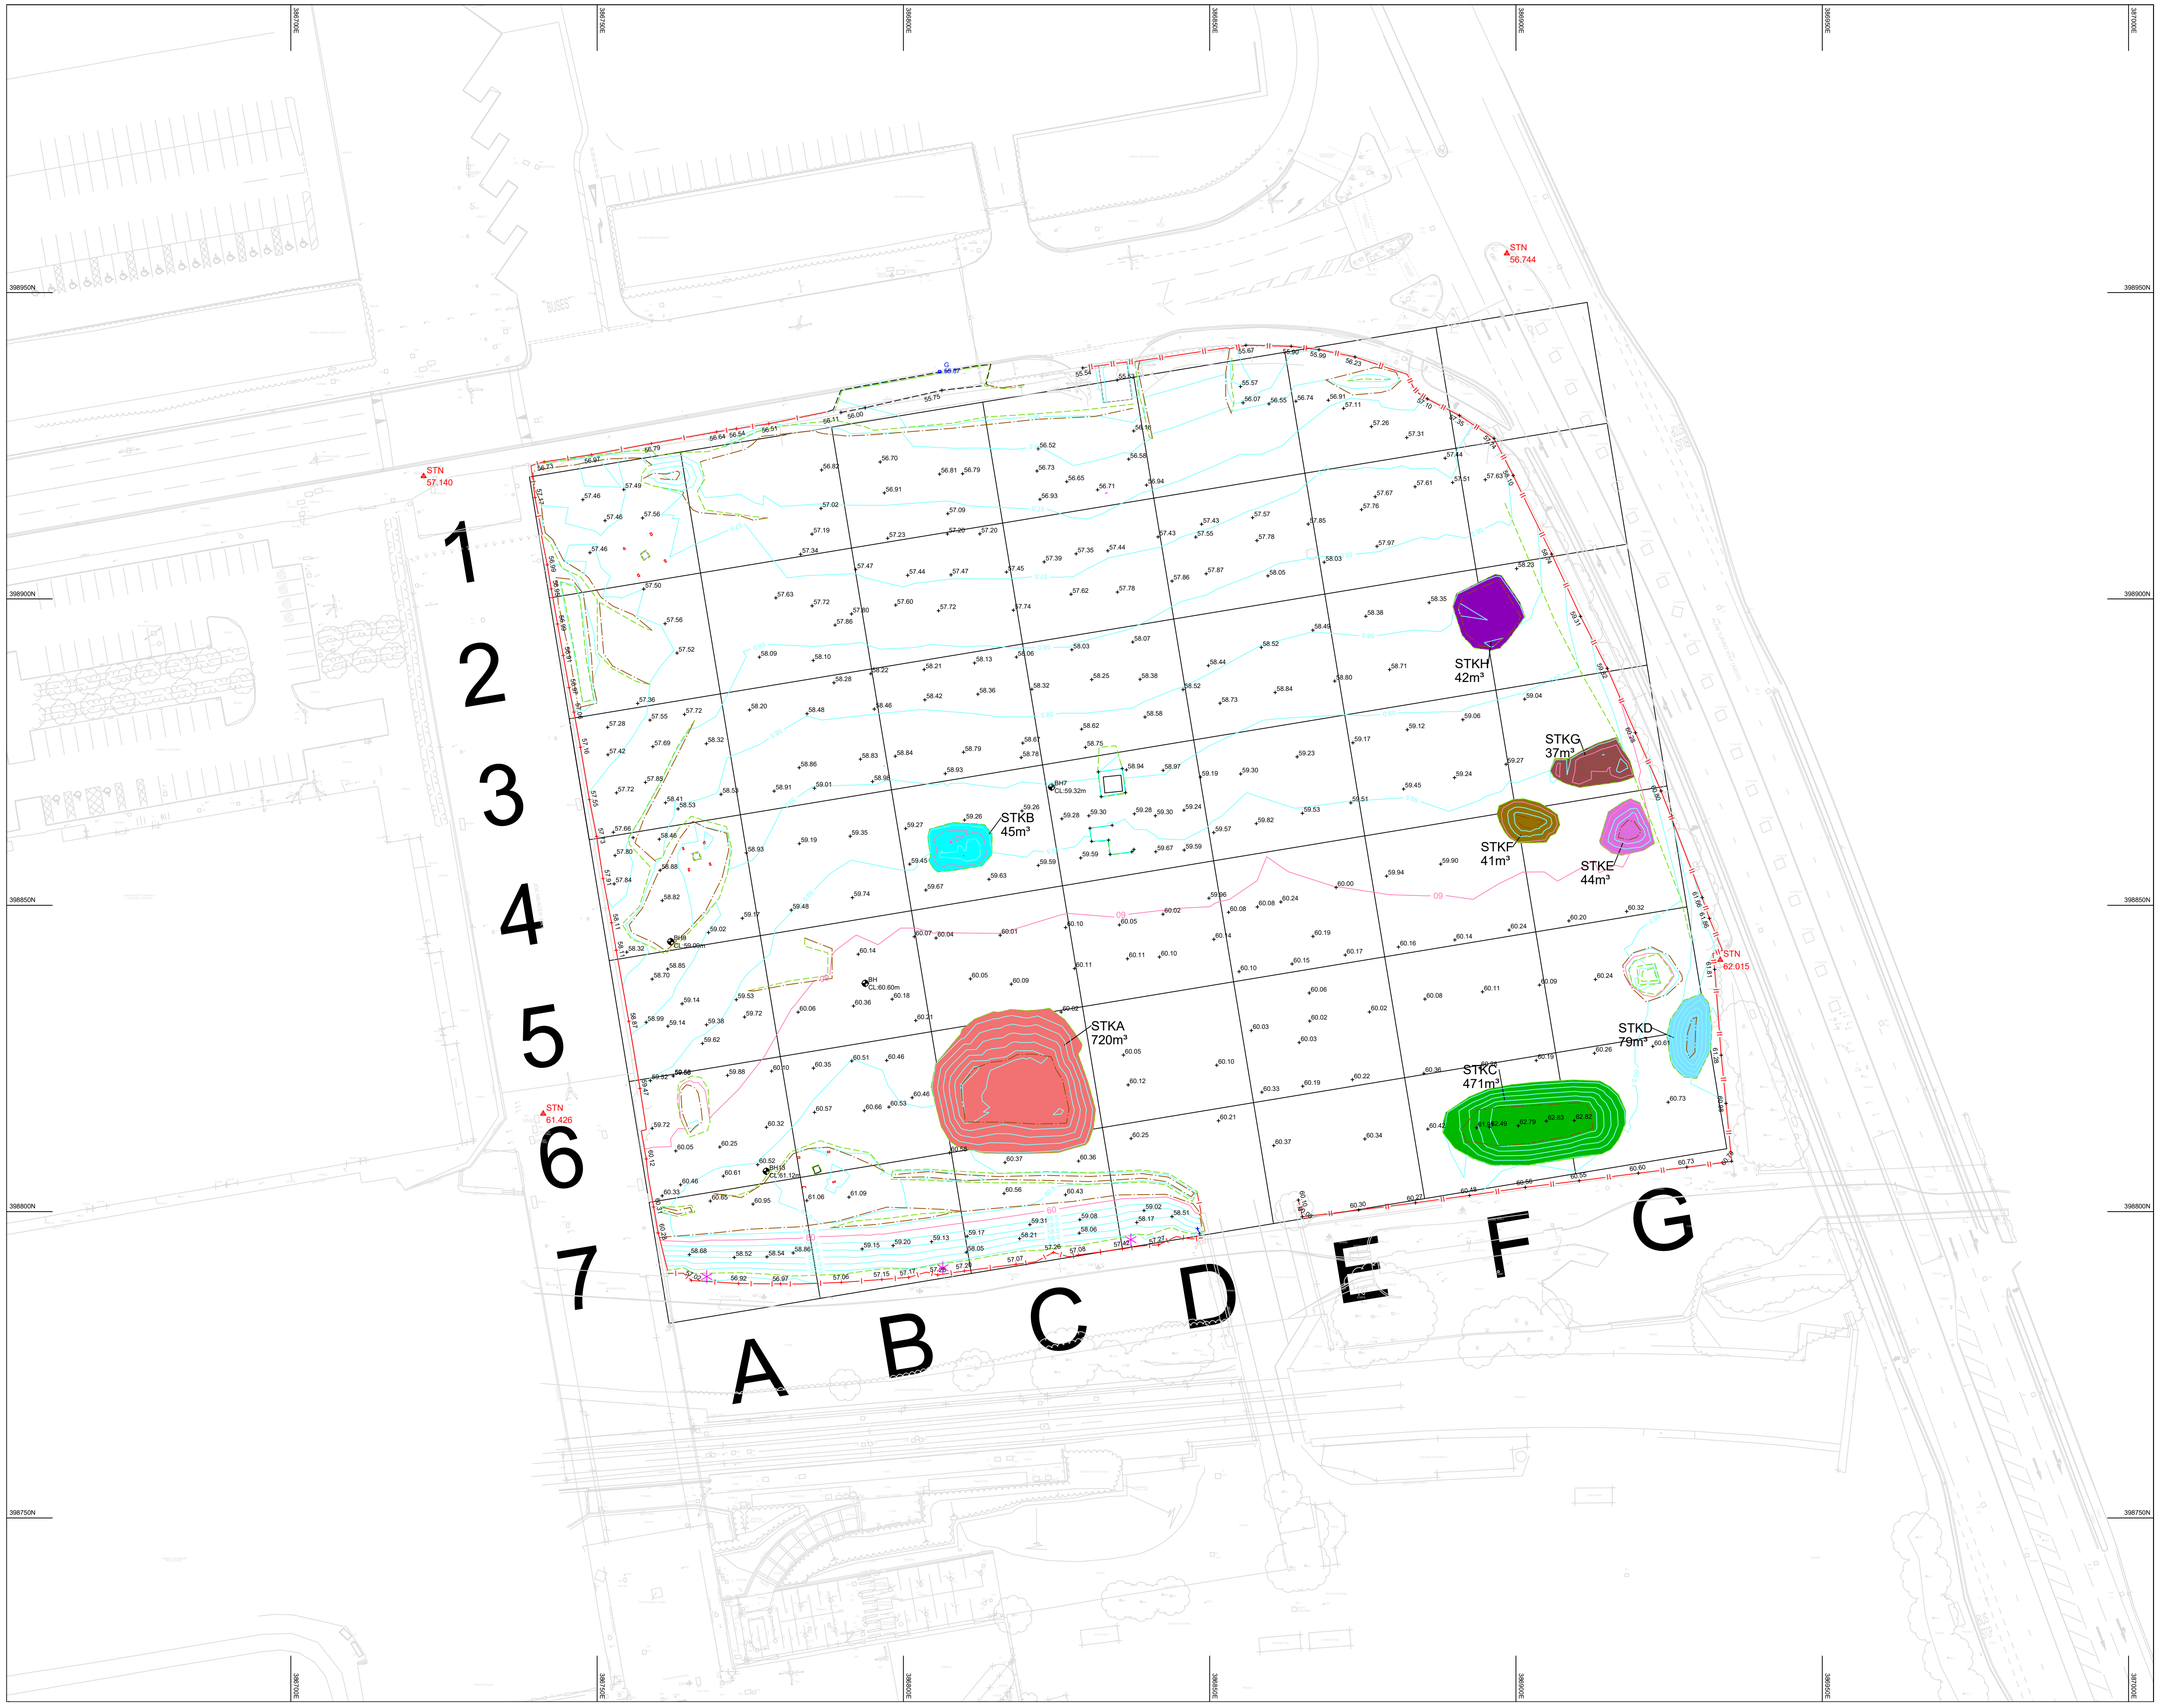

stafsurv
LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire, DE6 5HS
T 01283 584800 · F 01284 584844 · E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordinates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

Joint Site Survey 15-03-2021
(SITE GRID 20m x 25m)

SCALE


1:500 @ A1

DATE

15/03/2021

DRAWING No.

11523d-0

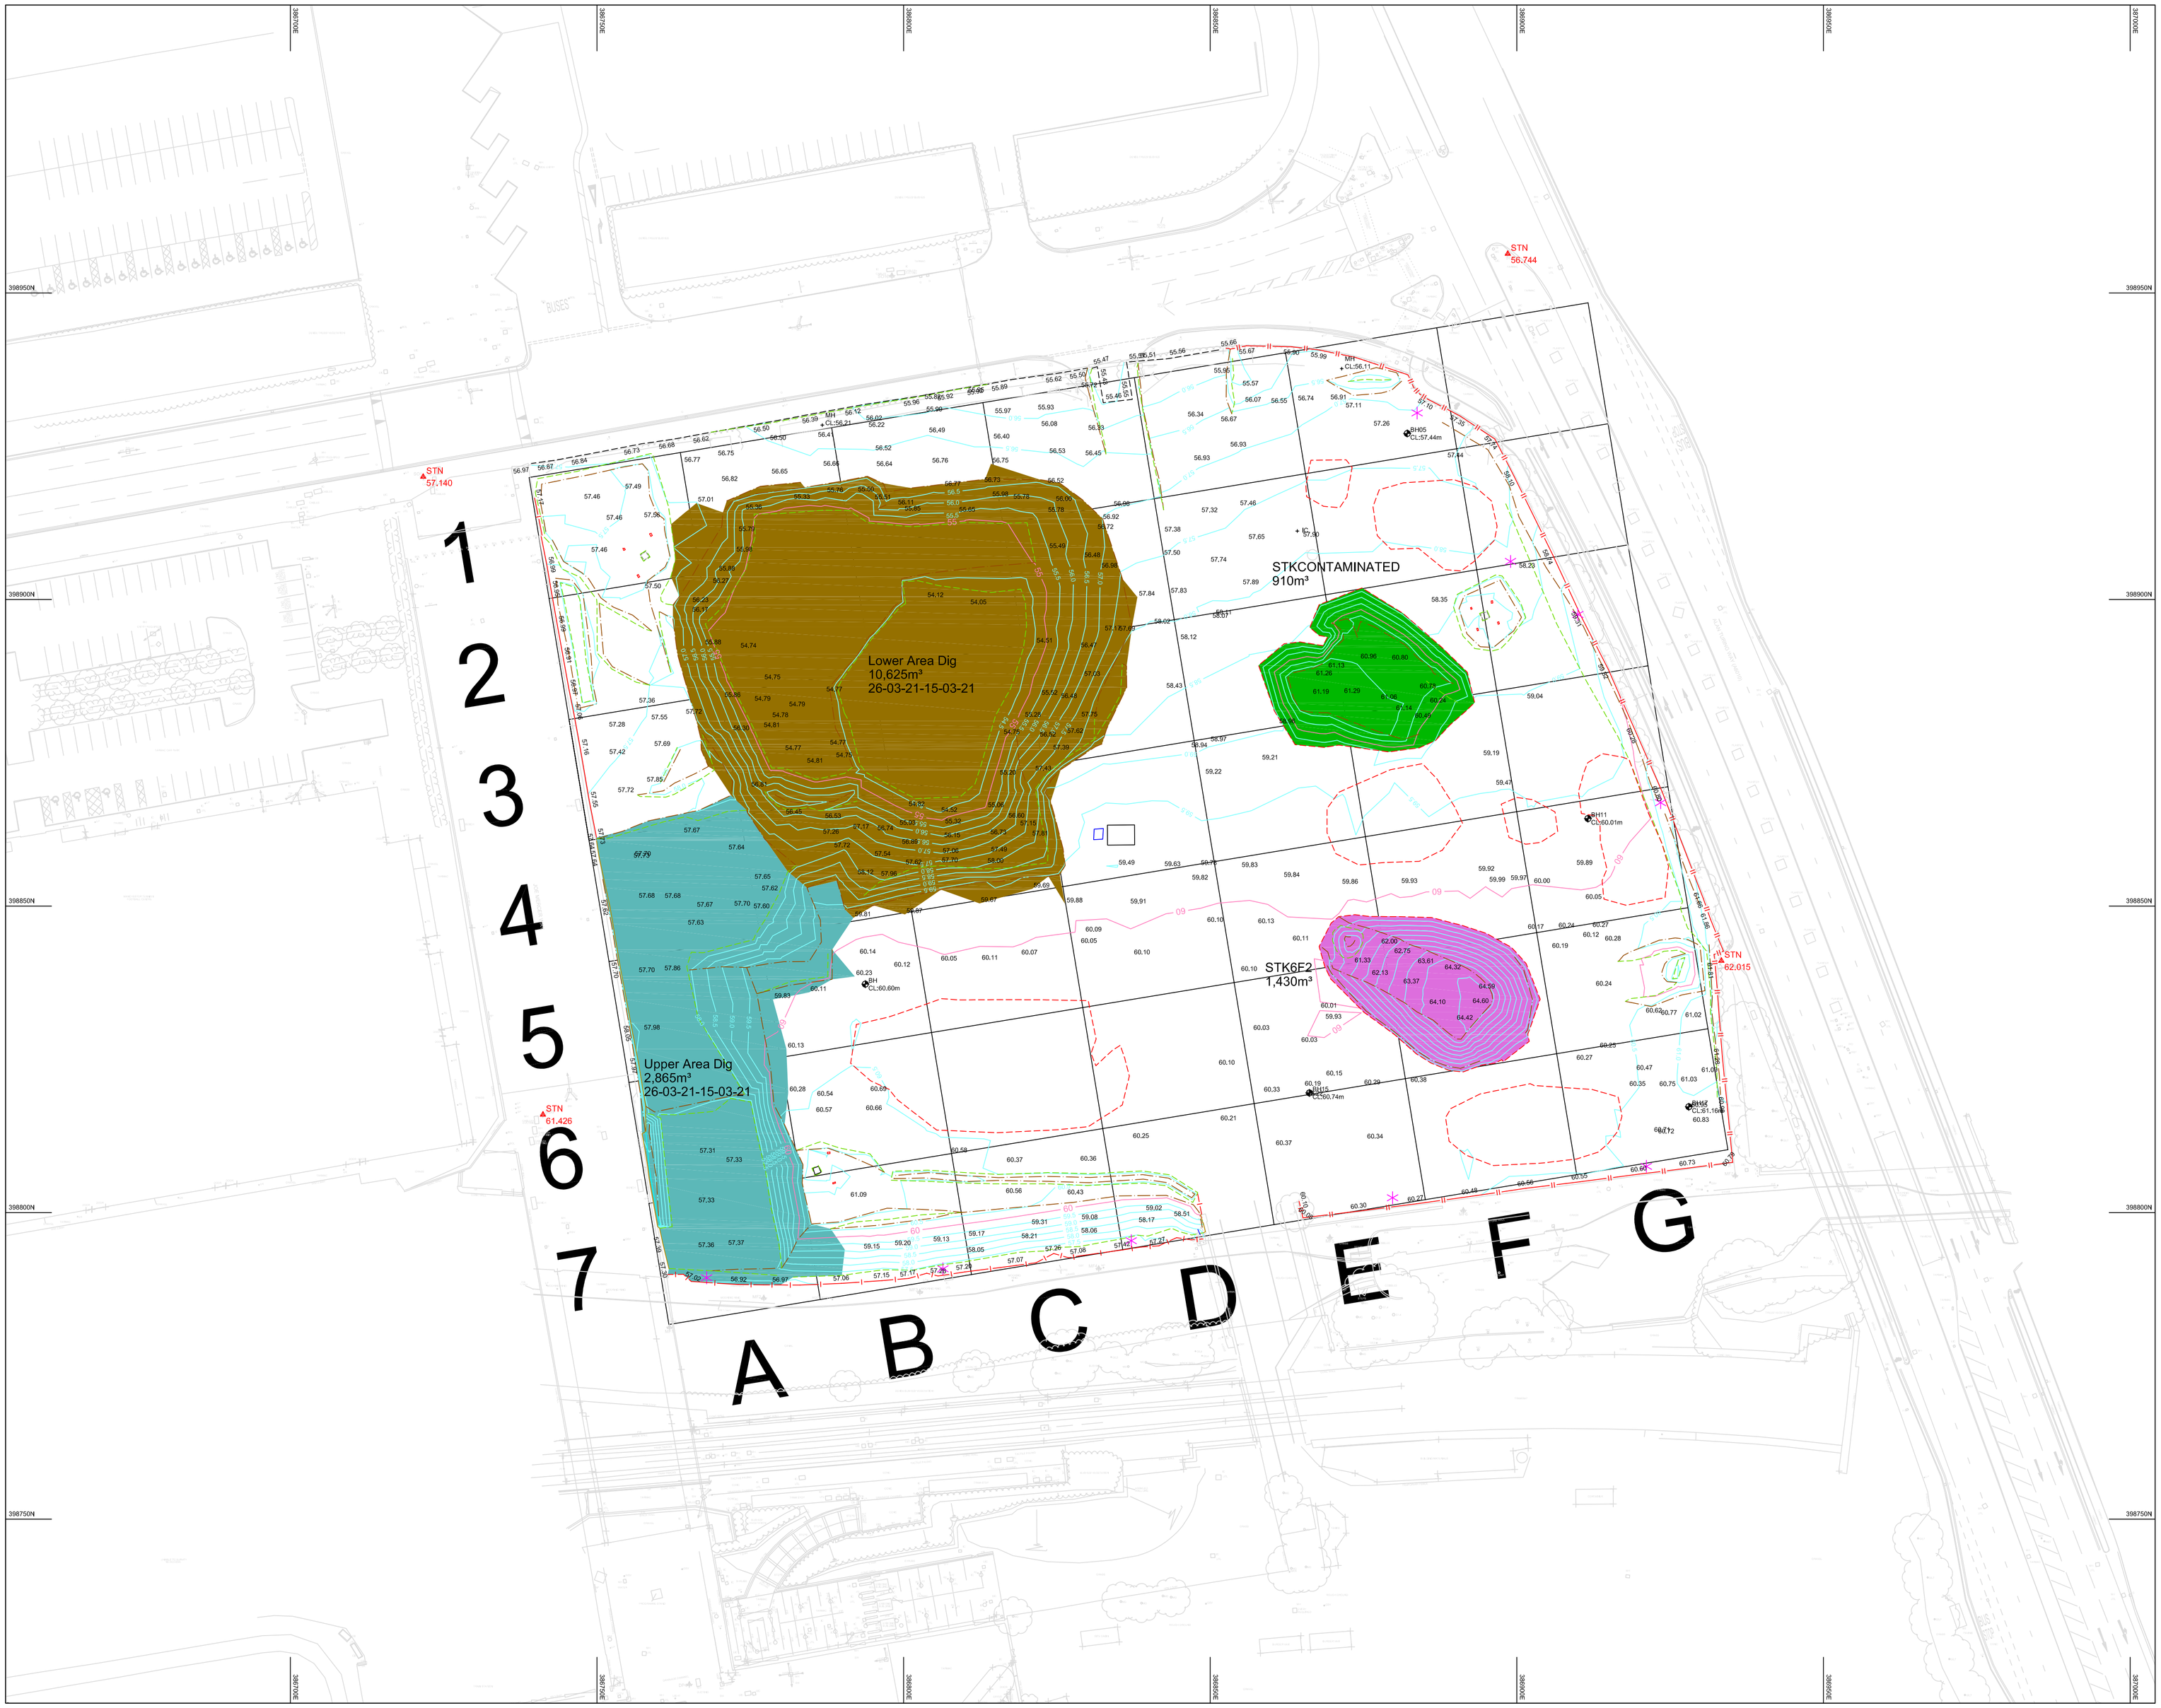

stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 - F 01284 584844 - E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordInates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.063	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

Site Survey 26-03-2021
(SITE GRID 20m x 25m)

SCALE


1:500 @ A1

DATE

26/03/2021

DRAWING No.

11523d-1

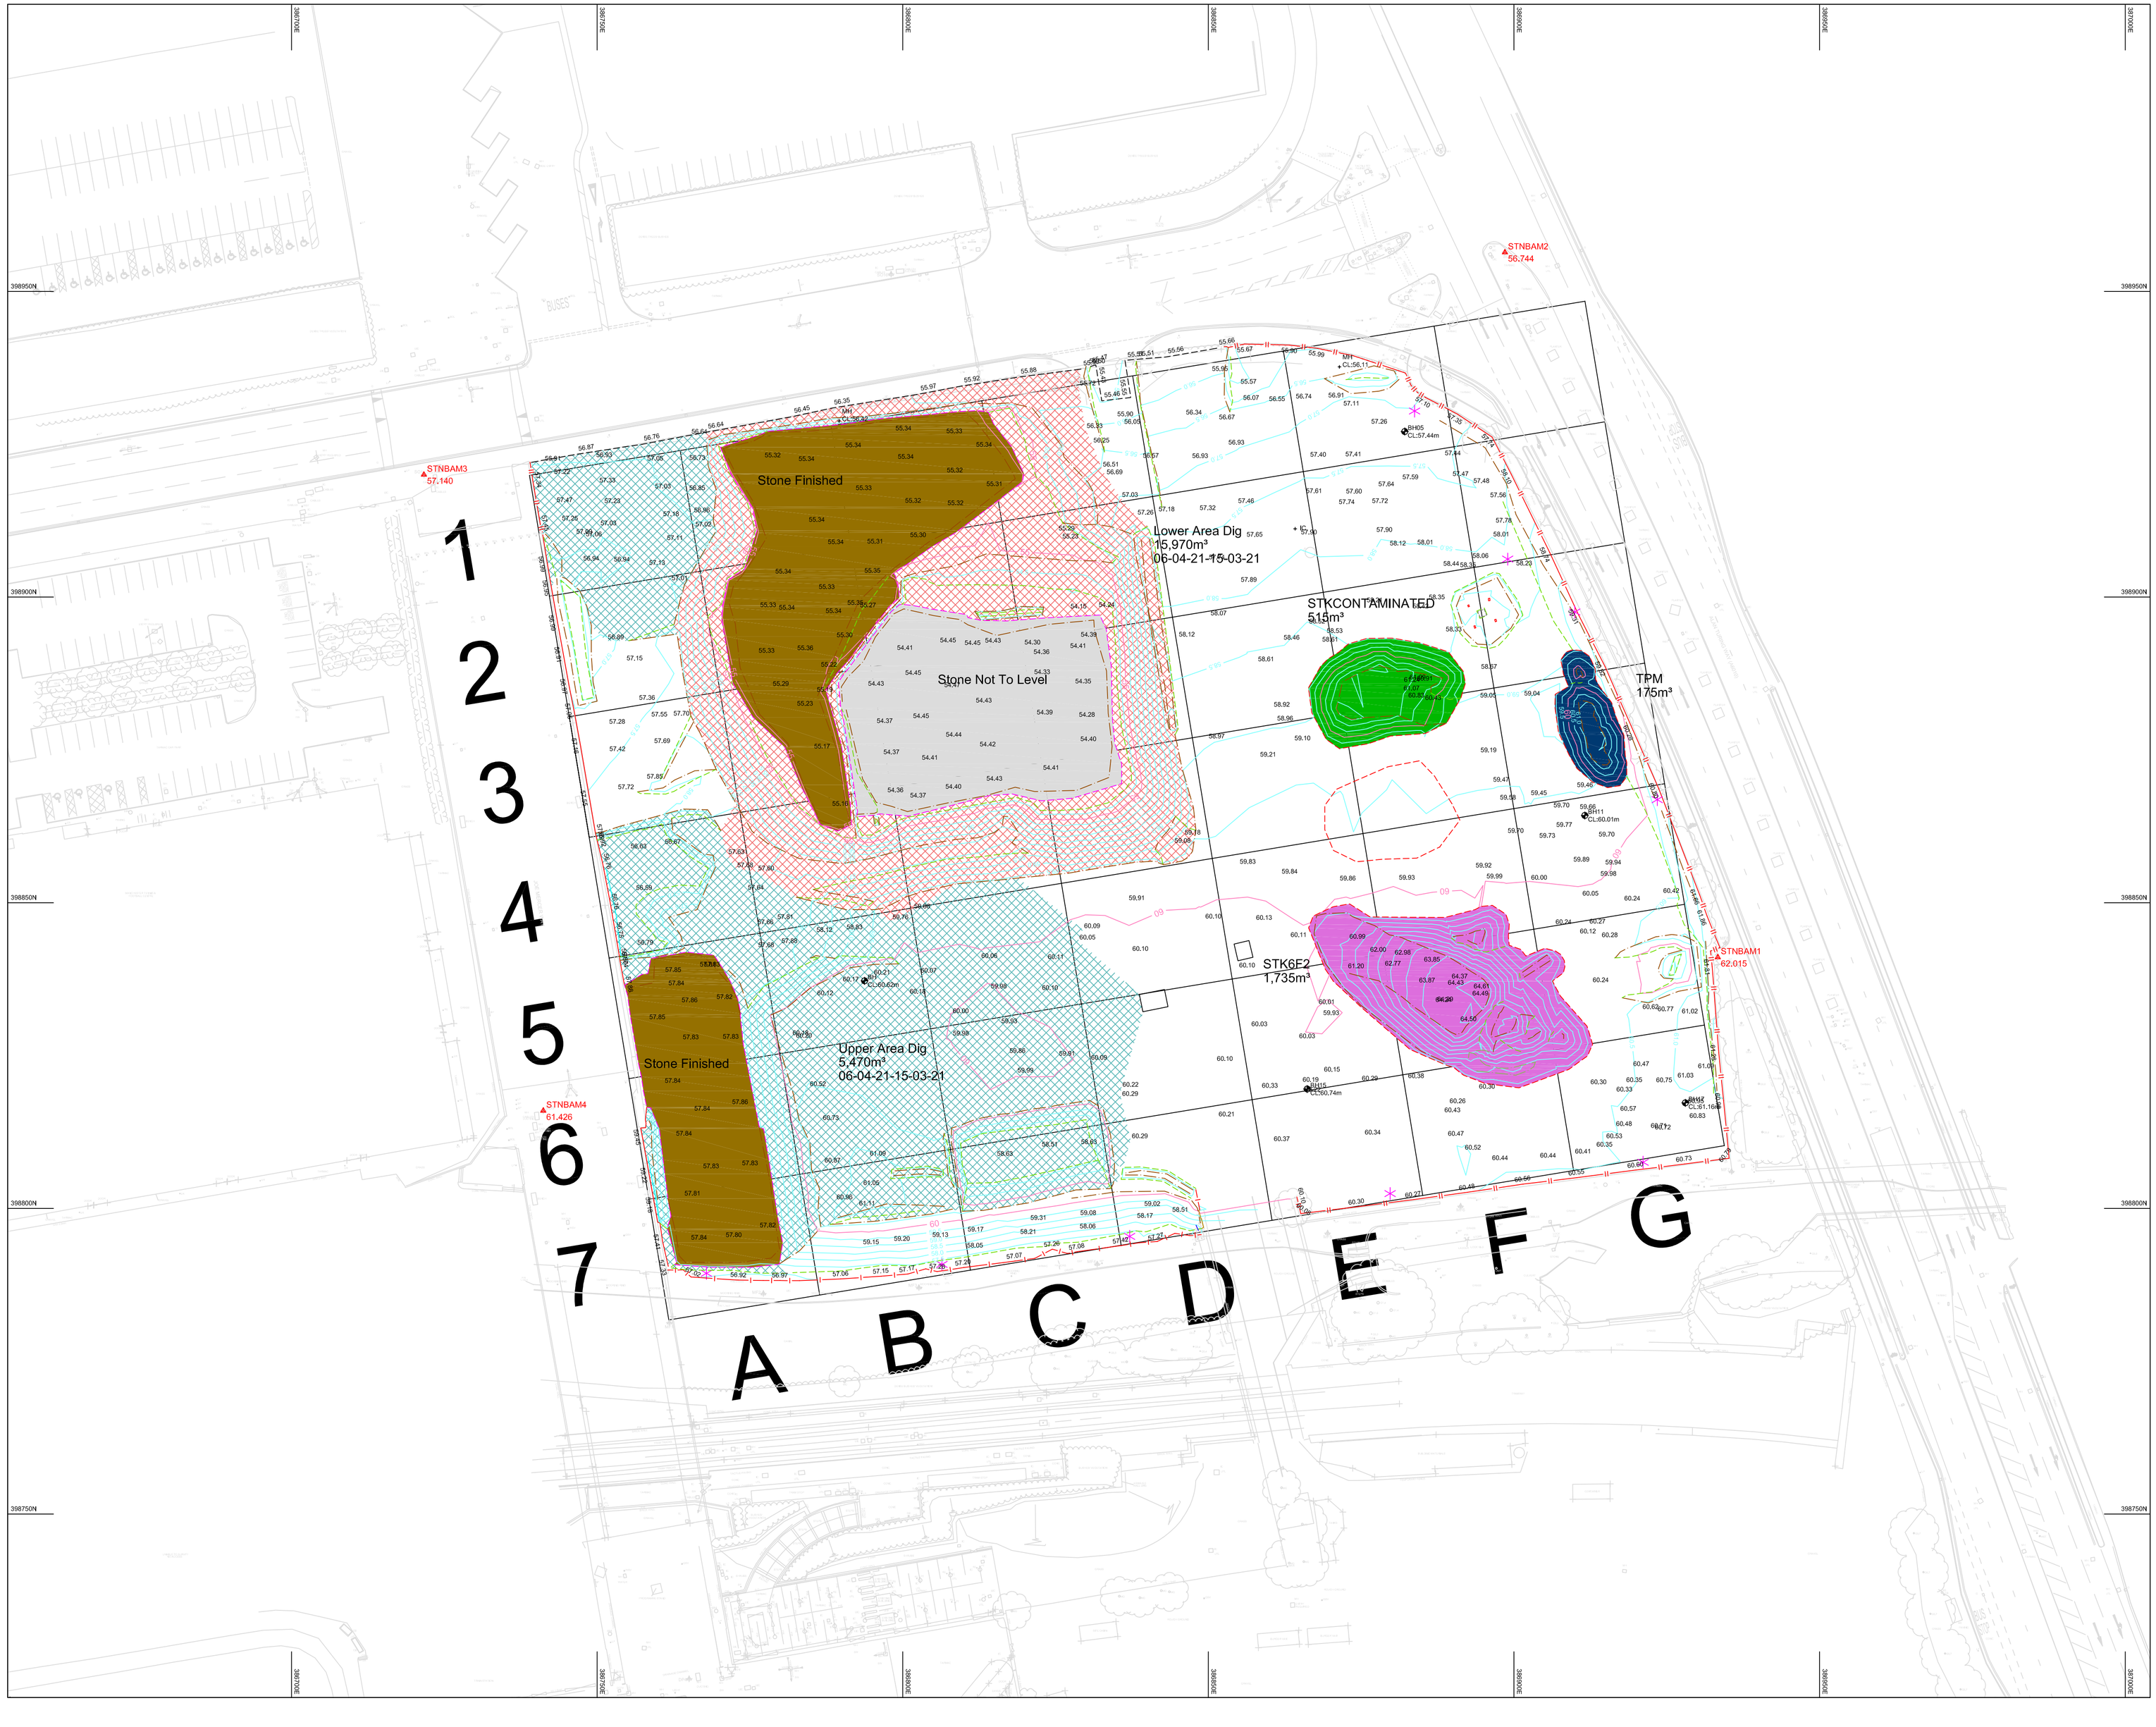

stafsurv
LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 - F 01284 584844 - E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordinates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.063	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114


PROJECT

Site Survey 06-04-2021
(SITE GRID 20m x 25m)

SCALE	DATE
1:500 @ A1	06/04/2021

DRAWING No.

11559d-0

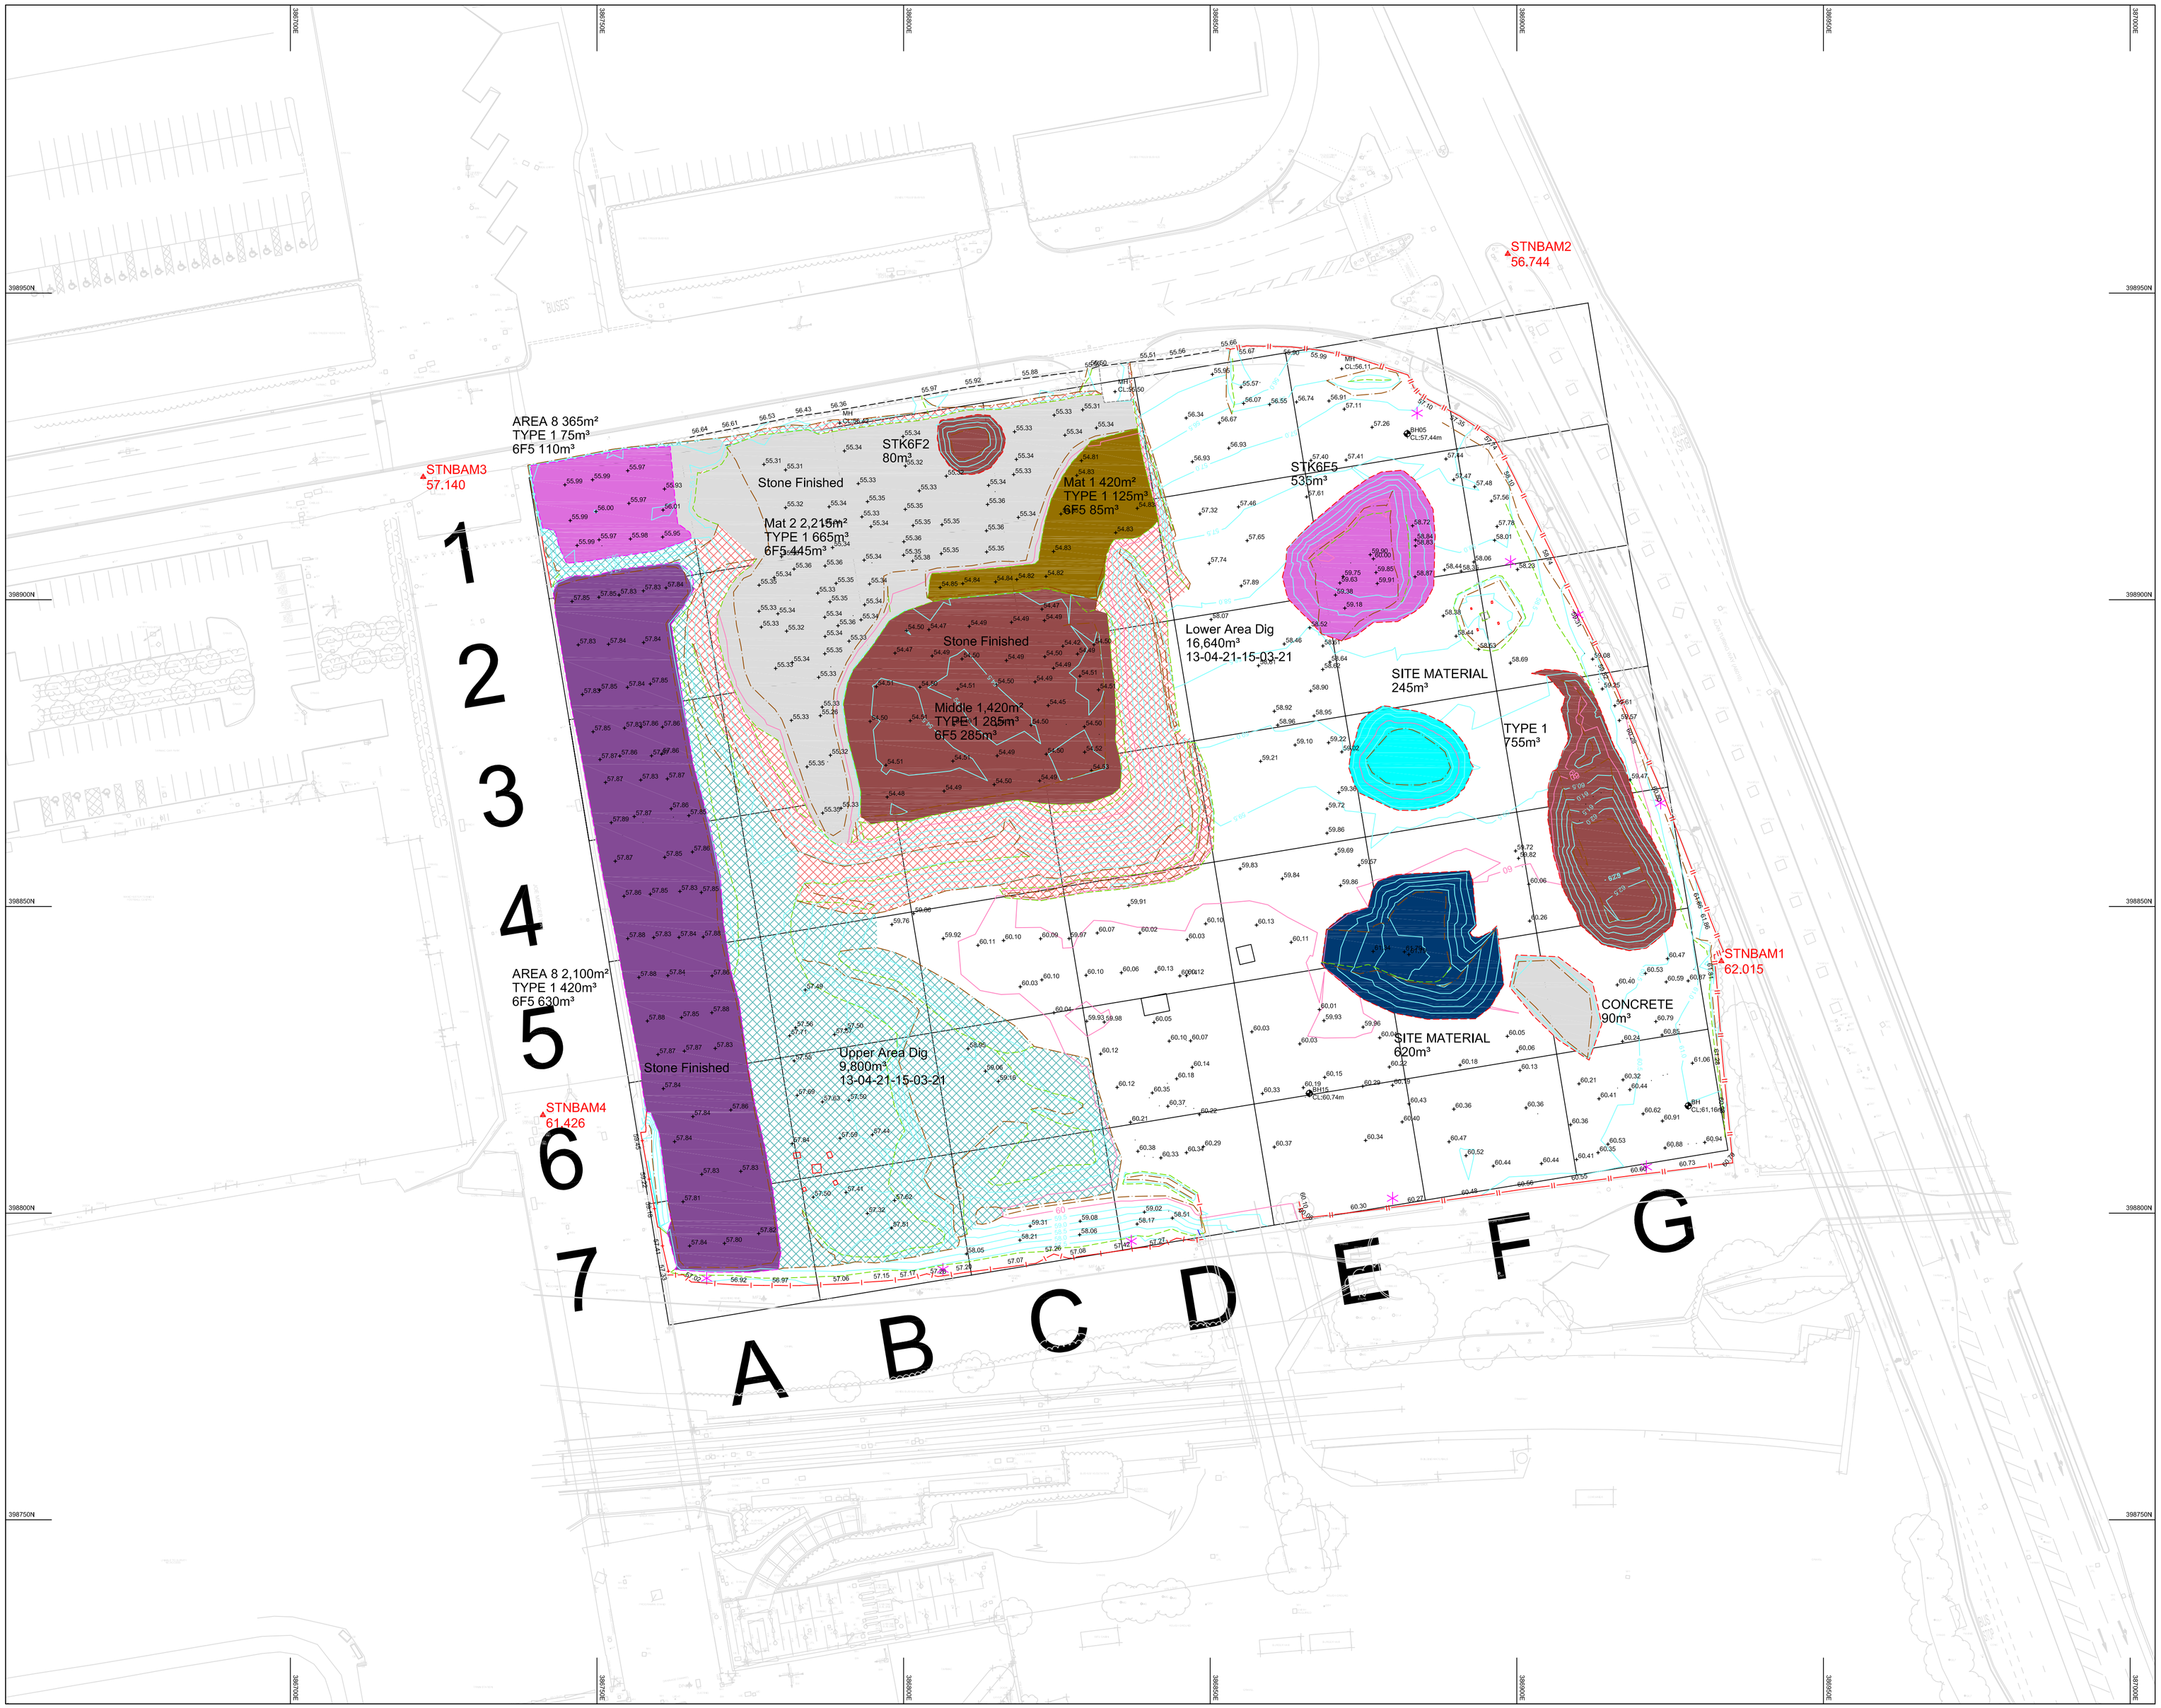

stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 · F 01284 584844 · E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordinates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

Site Survey 13-04-2021
(SITE GRID 20m x 25m)

SCALE


1:500 @ A1

DATE

13/04/2021

DRAWING No.

11559d-1

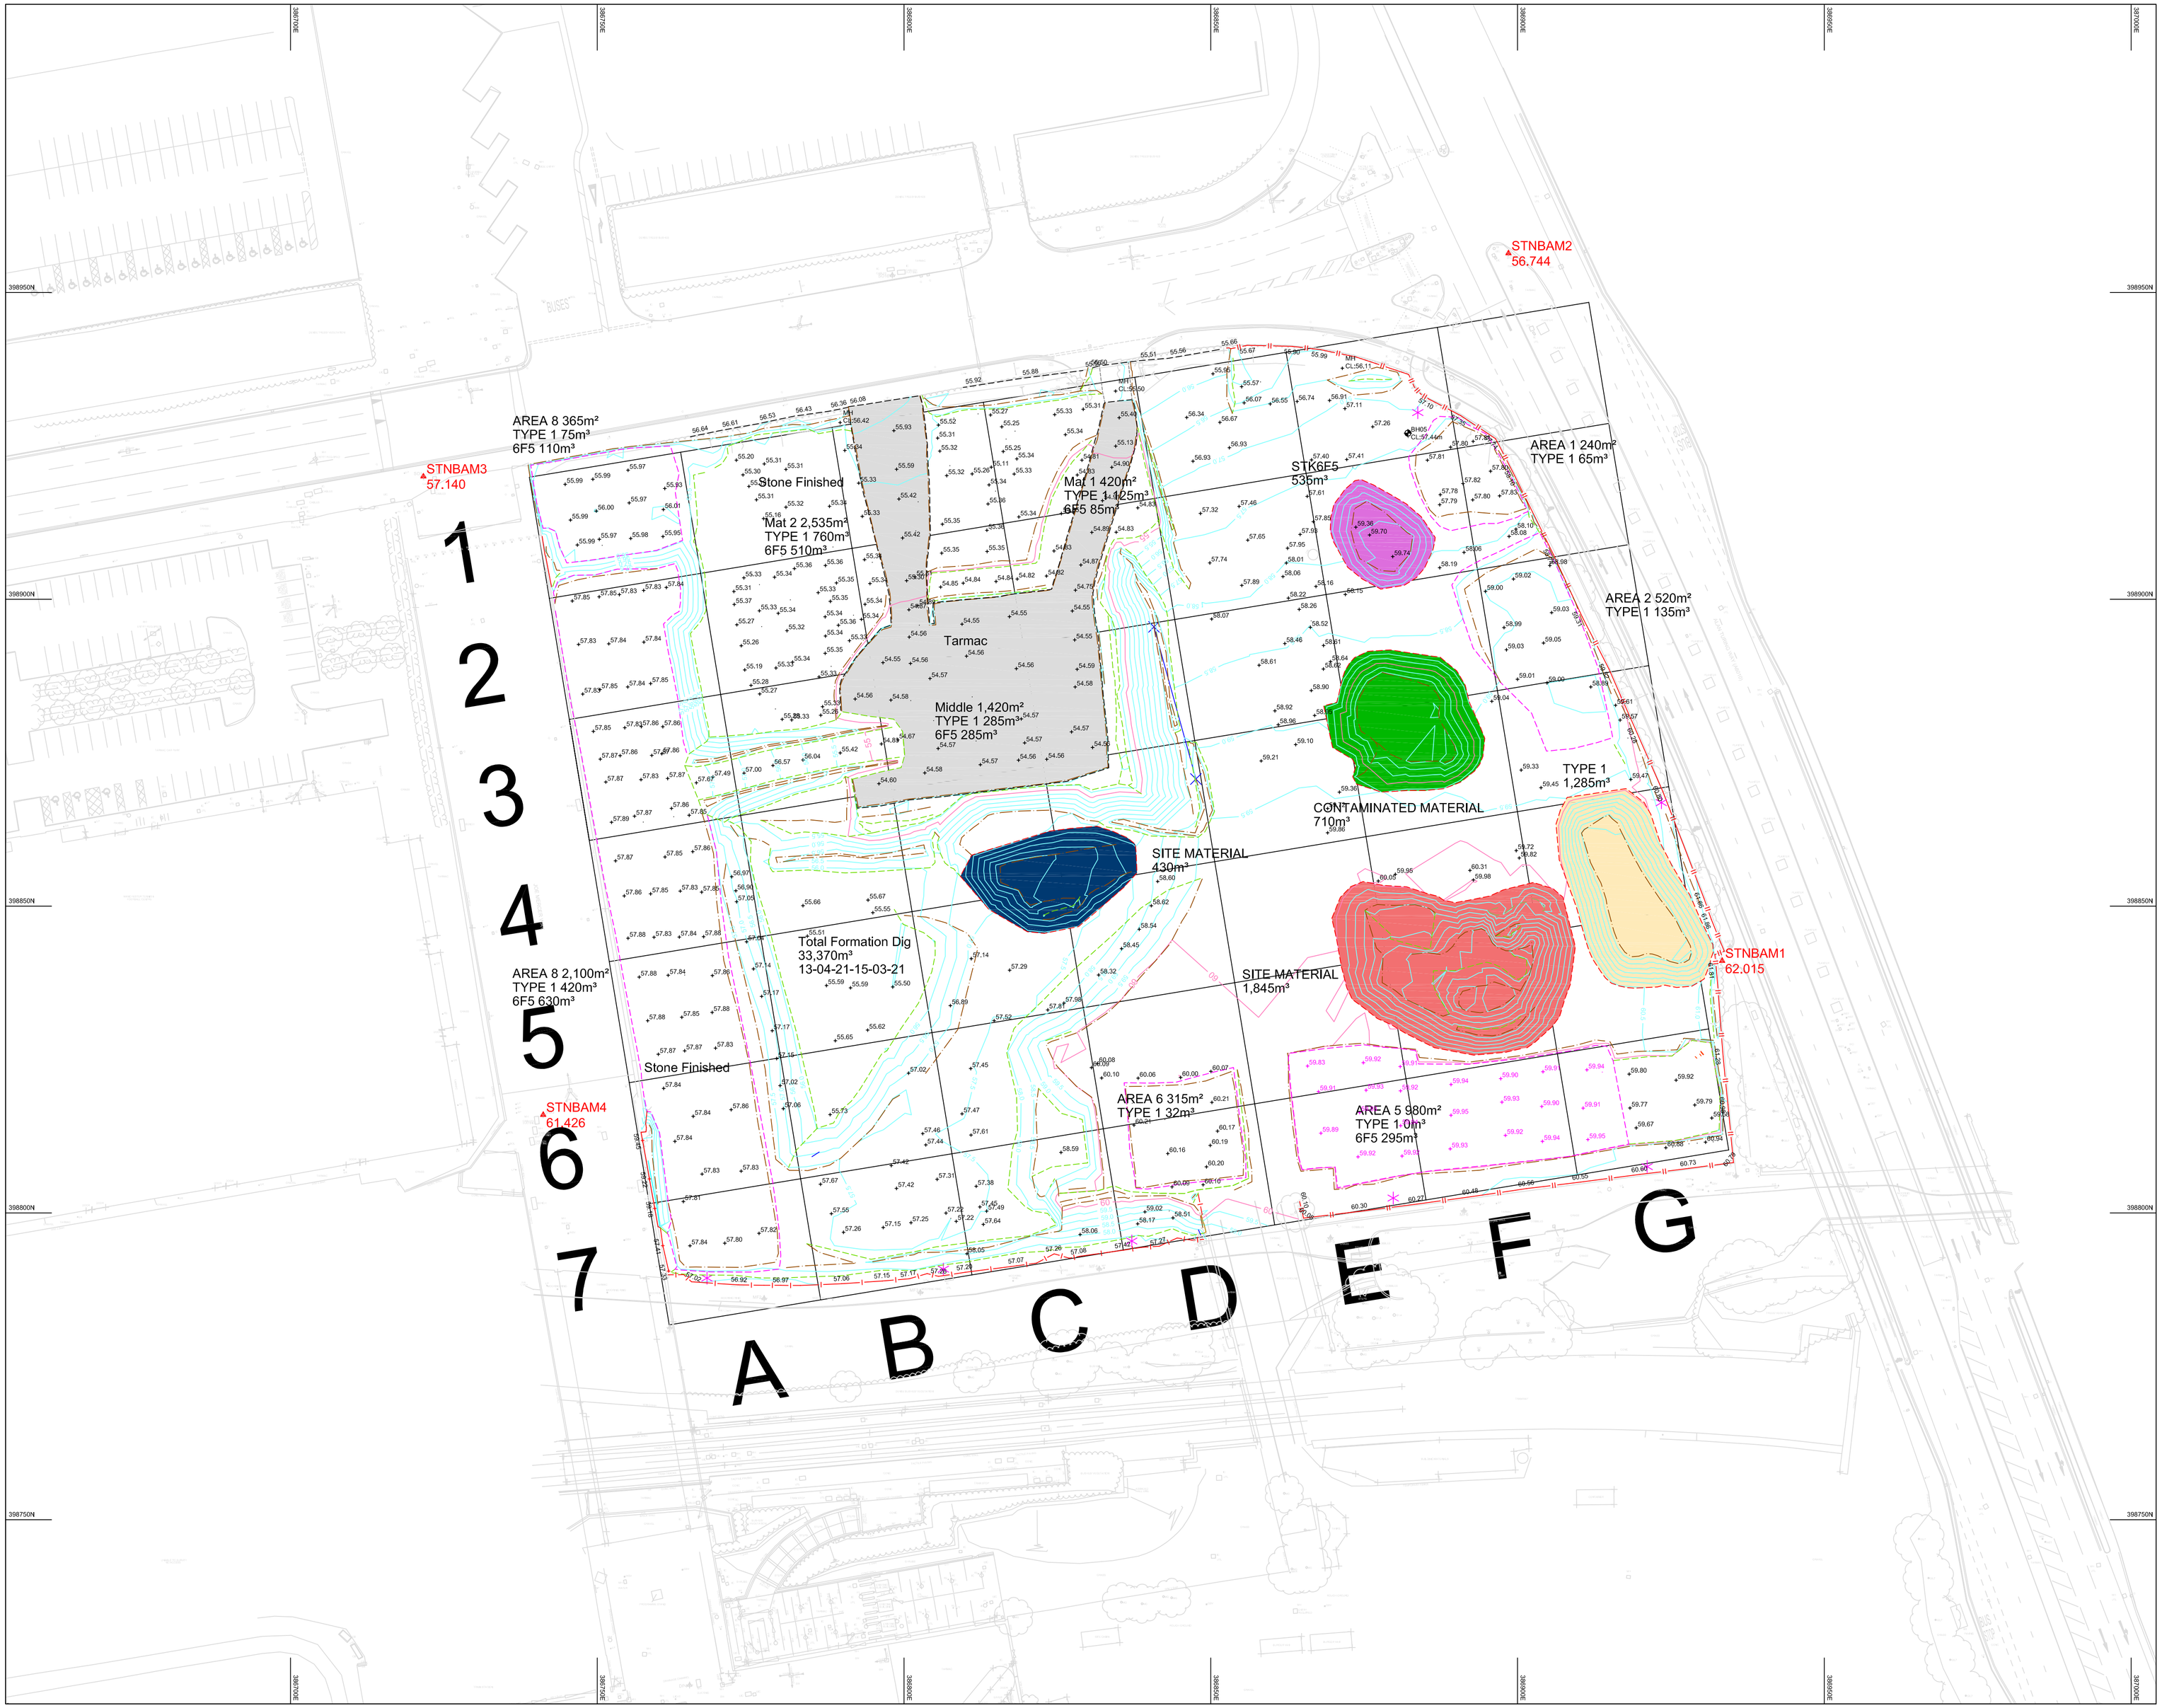

stafsurv
LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 - F 01284 584844 - E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordInates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.063	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

Site Survey 19-04-2021
(SITE GRID 20m x 25m)

SCALE
1:500 @ A1

DATE
19/04/2021

DRAWING No.

11559d-2



stafsurv
LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 · F 01284 584844 · E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordinates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT


Site Survey 30-04-2021
(SITE GRID 20m x 25m)

SCALE
1:500 @ A1

DATE
30/04/2021

DRAWING No.

11559d-3

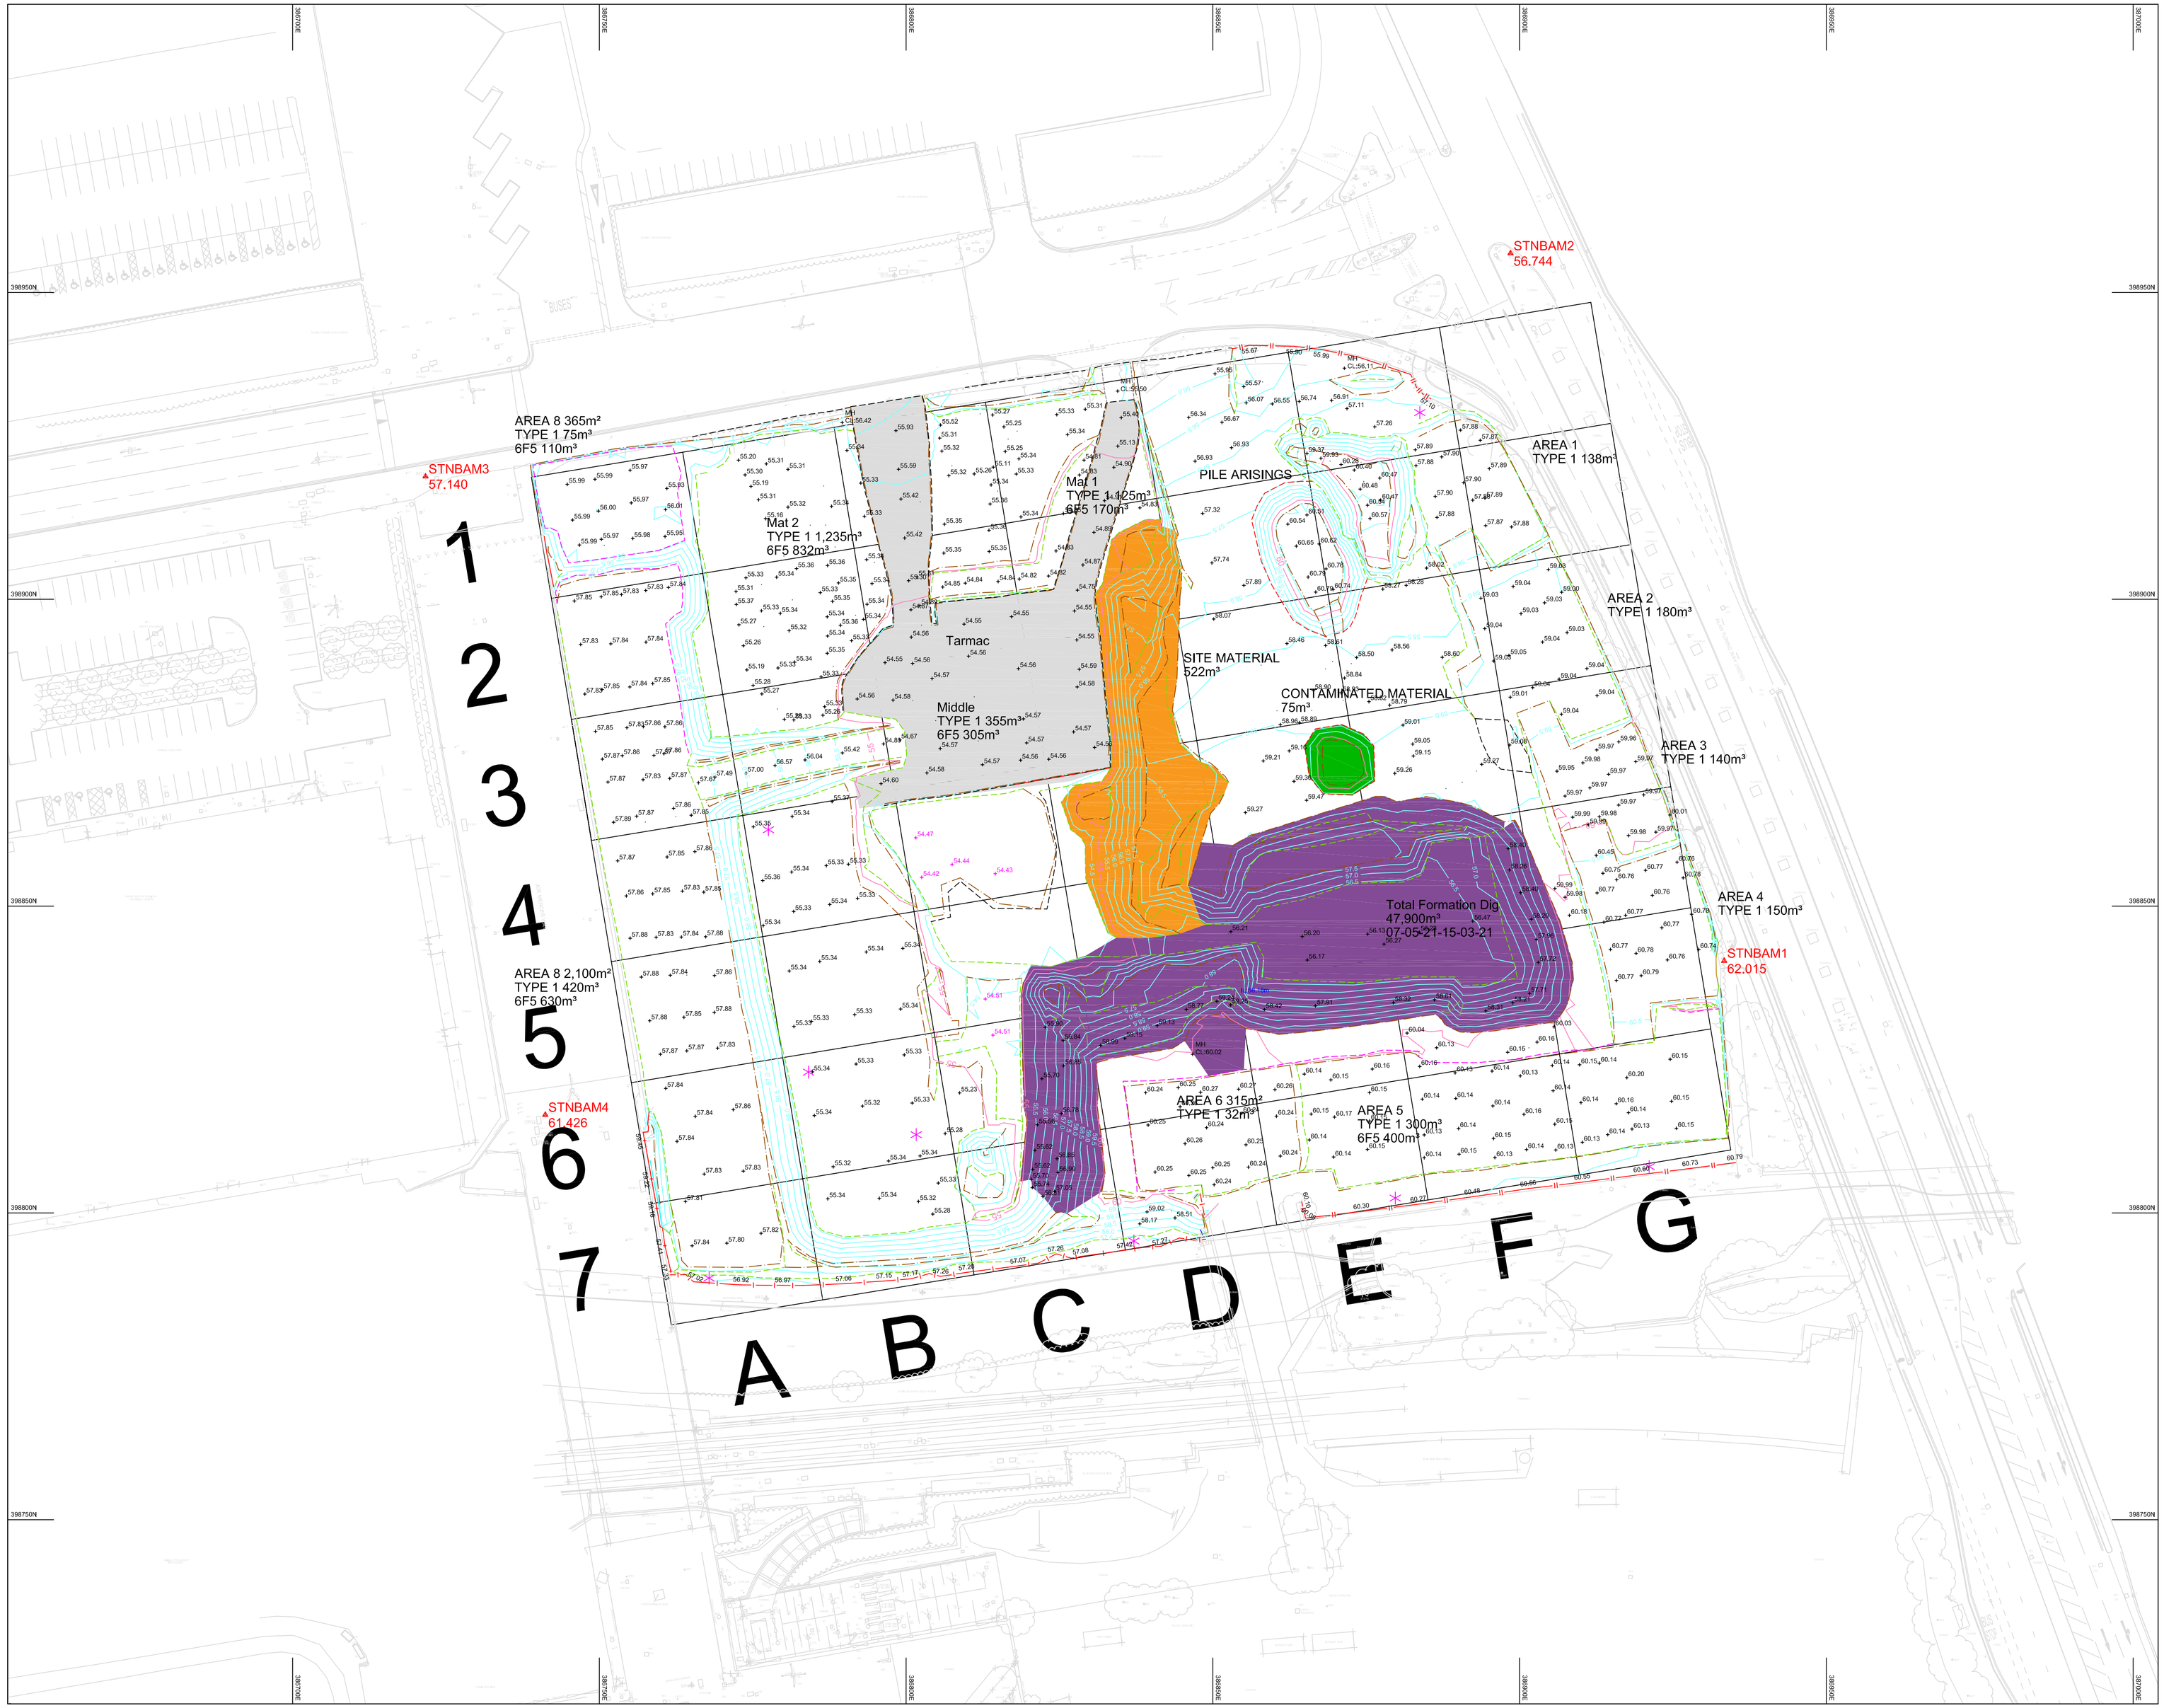

stafsurv
LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 - F 01284 584844 - E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordInates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

Site Survey 07-05-2021
(SITE GRID 20m x 25m)

SCALE

1:500 @ A1

DATE

07/05/2021

DRAWING No.

11618d-0



stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 · F 01284 584844 · E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordInates : SITE GRID

SURVEY STATIONS

Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

Site Survey 14-05-2021
(SITE GRID 20m x 25m)

SCALE

1:500 @ A1

DATE

14/05/2021

DRAWING No.

11618d-1



stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 > F 01284 584844 > E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordInates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

Site Survey 21-05-2021
(SITE GRID 20m x 25m)

SCALE

1:500 @ A1

DATE

21/05/2021

DRAWING No.

11618d-3



stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 - F 01284 584844 - E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordInates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

Site Survey 21-05-2021
(SITE GRID 20m x 25m)

SCALE


1:500 @ A1

DATE

11/06/2021

DRAWING No.

11684d-0

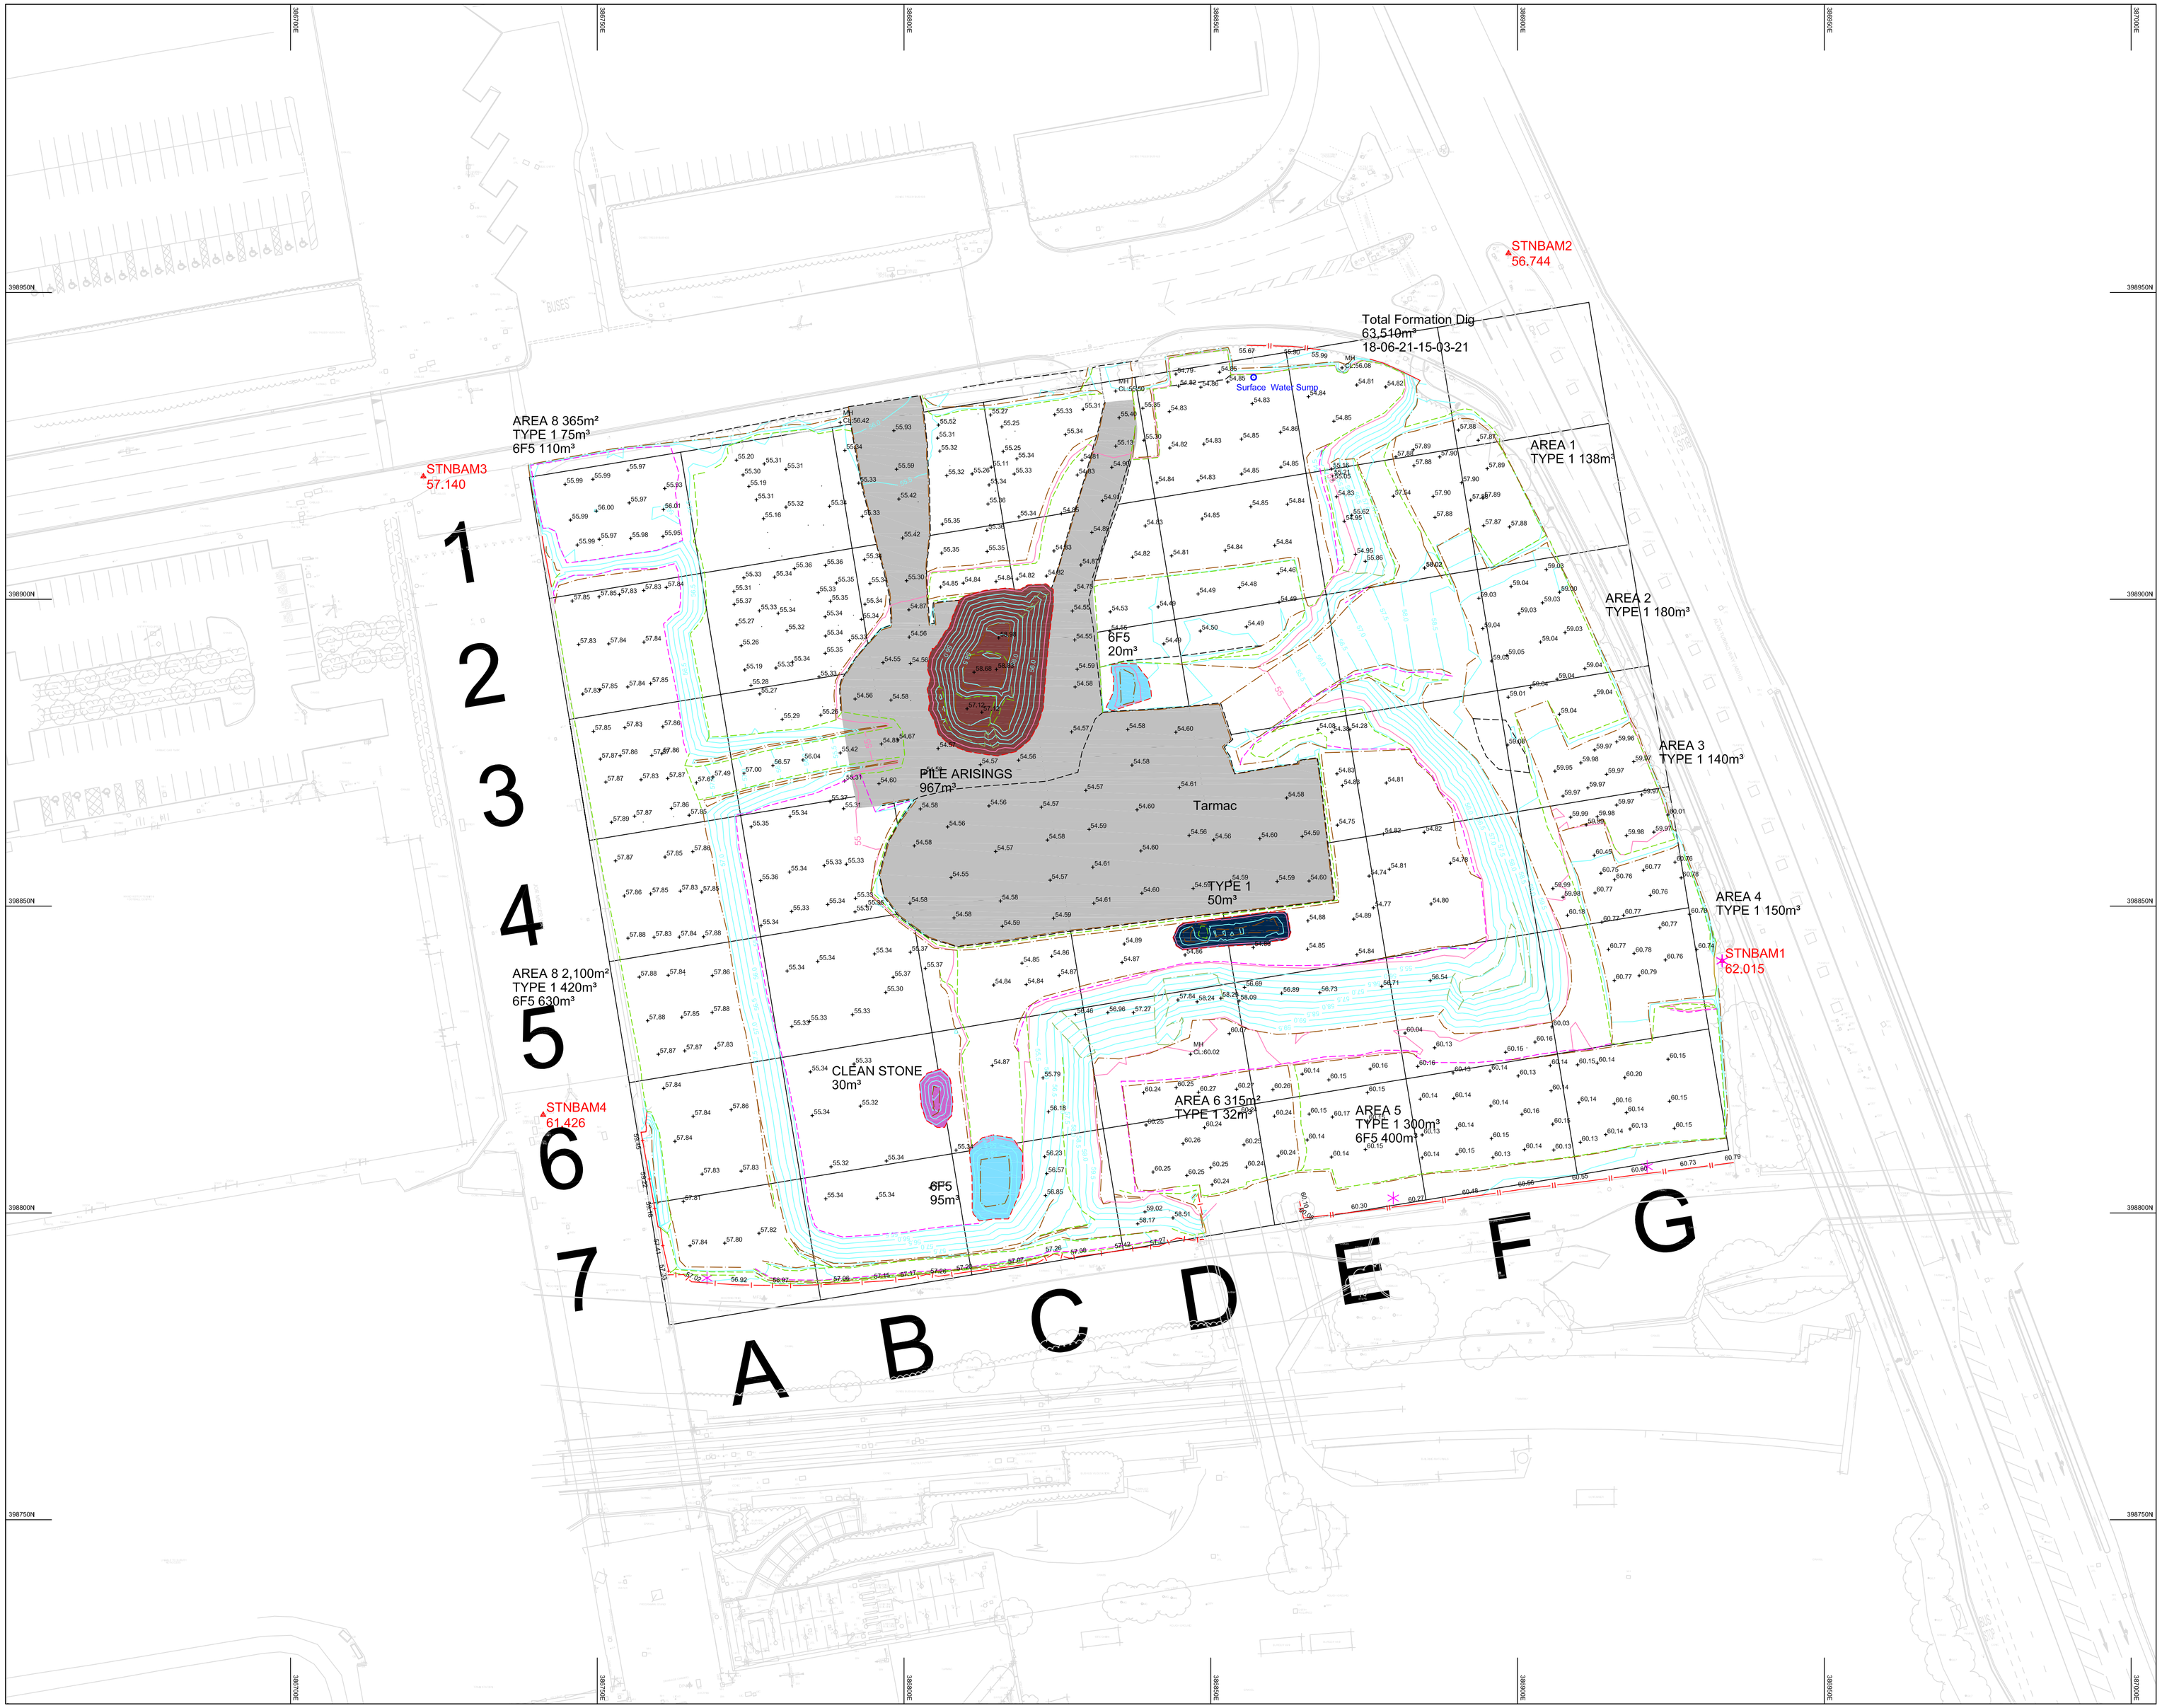

stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 · F 01284 584844 · E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordInates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

Site Survey 18-06-2021
(SITE GRID 20m x 25m)

SCALE


1:500 @ A1

DATE

18/06/2021

DRAWING No.

11684d-1

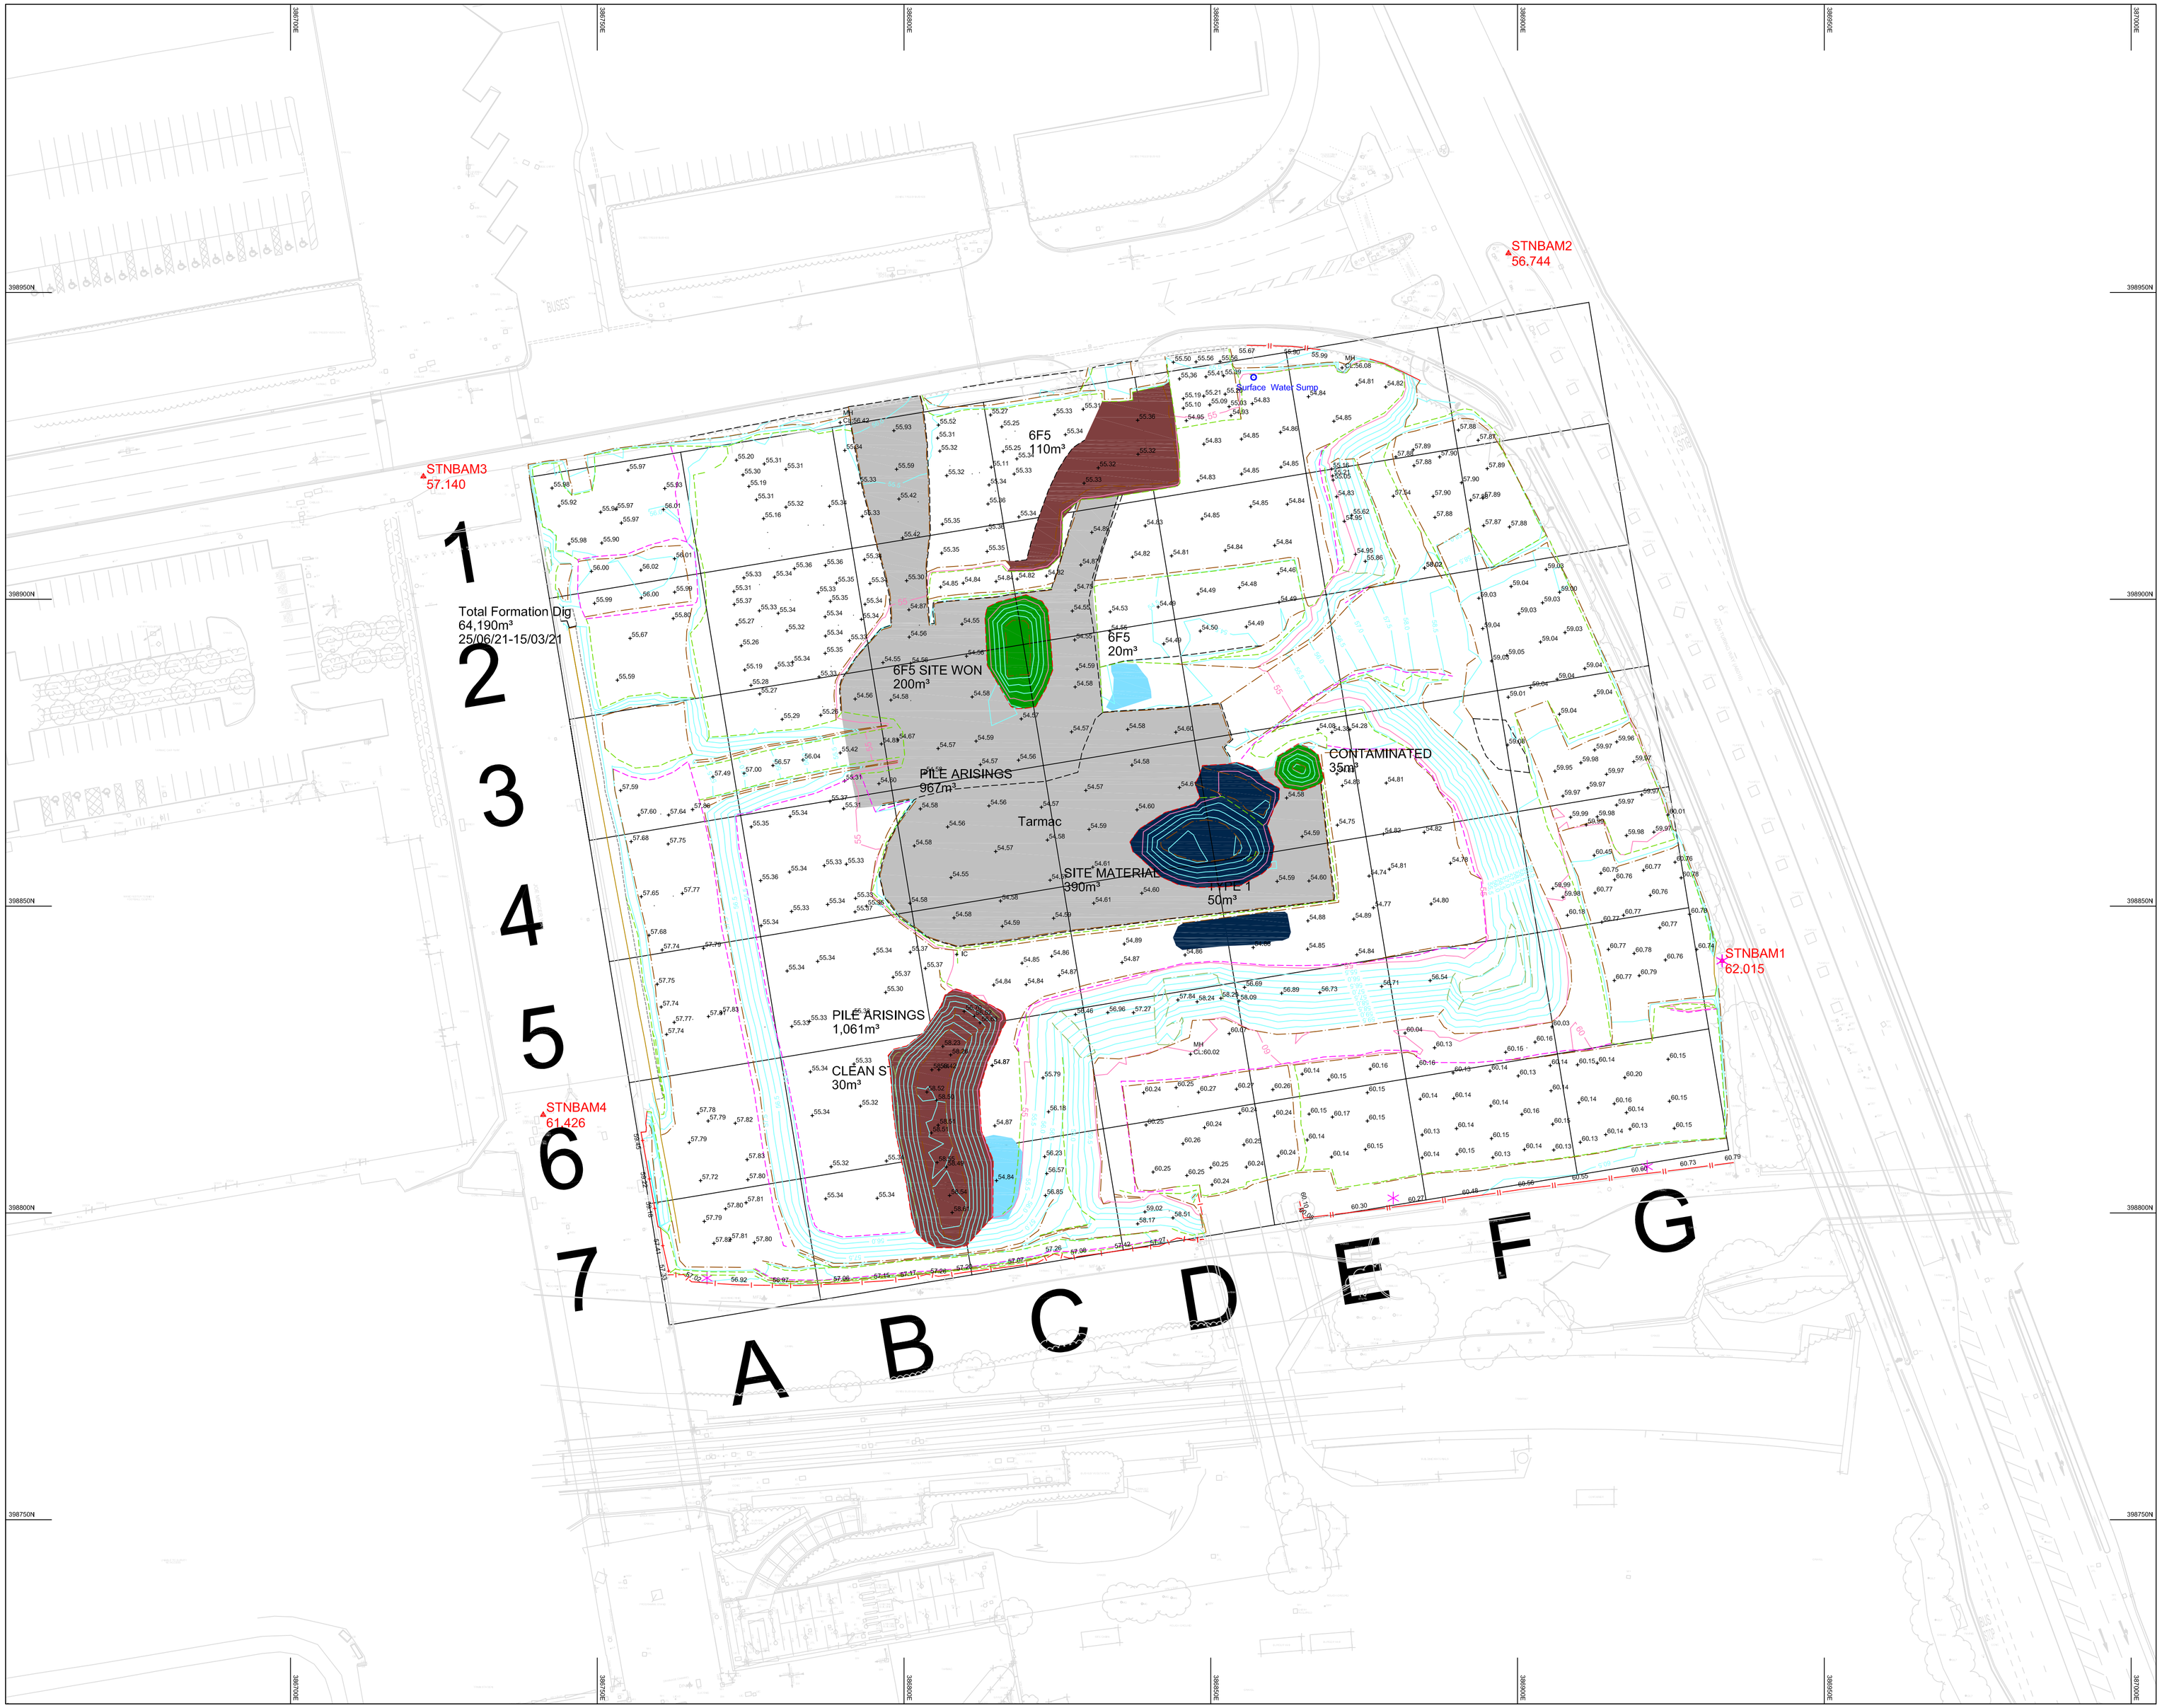

stafsurv
LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 - F 01284 584844 - E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordlnates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

Site Survey 25-06-2021
(SITE GRID 20m x 25m)

SCALE
1:500 @ A1

DATE
25/06/2021

DRAWING No.

11684d-2



stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 - F 01284 584844 - E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordInates : SITE GRID

SURVEY STATIONS

Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

Site Survey 02-07-2021
(SITE GRID 20m x 25m)

SCALE


1:500 @ A1

DATE

09/07/2021

DRAWING No.

11730d-2

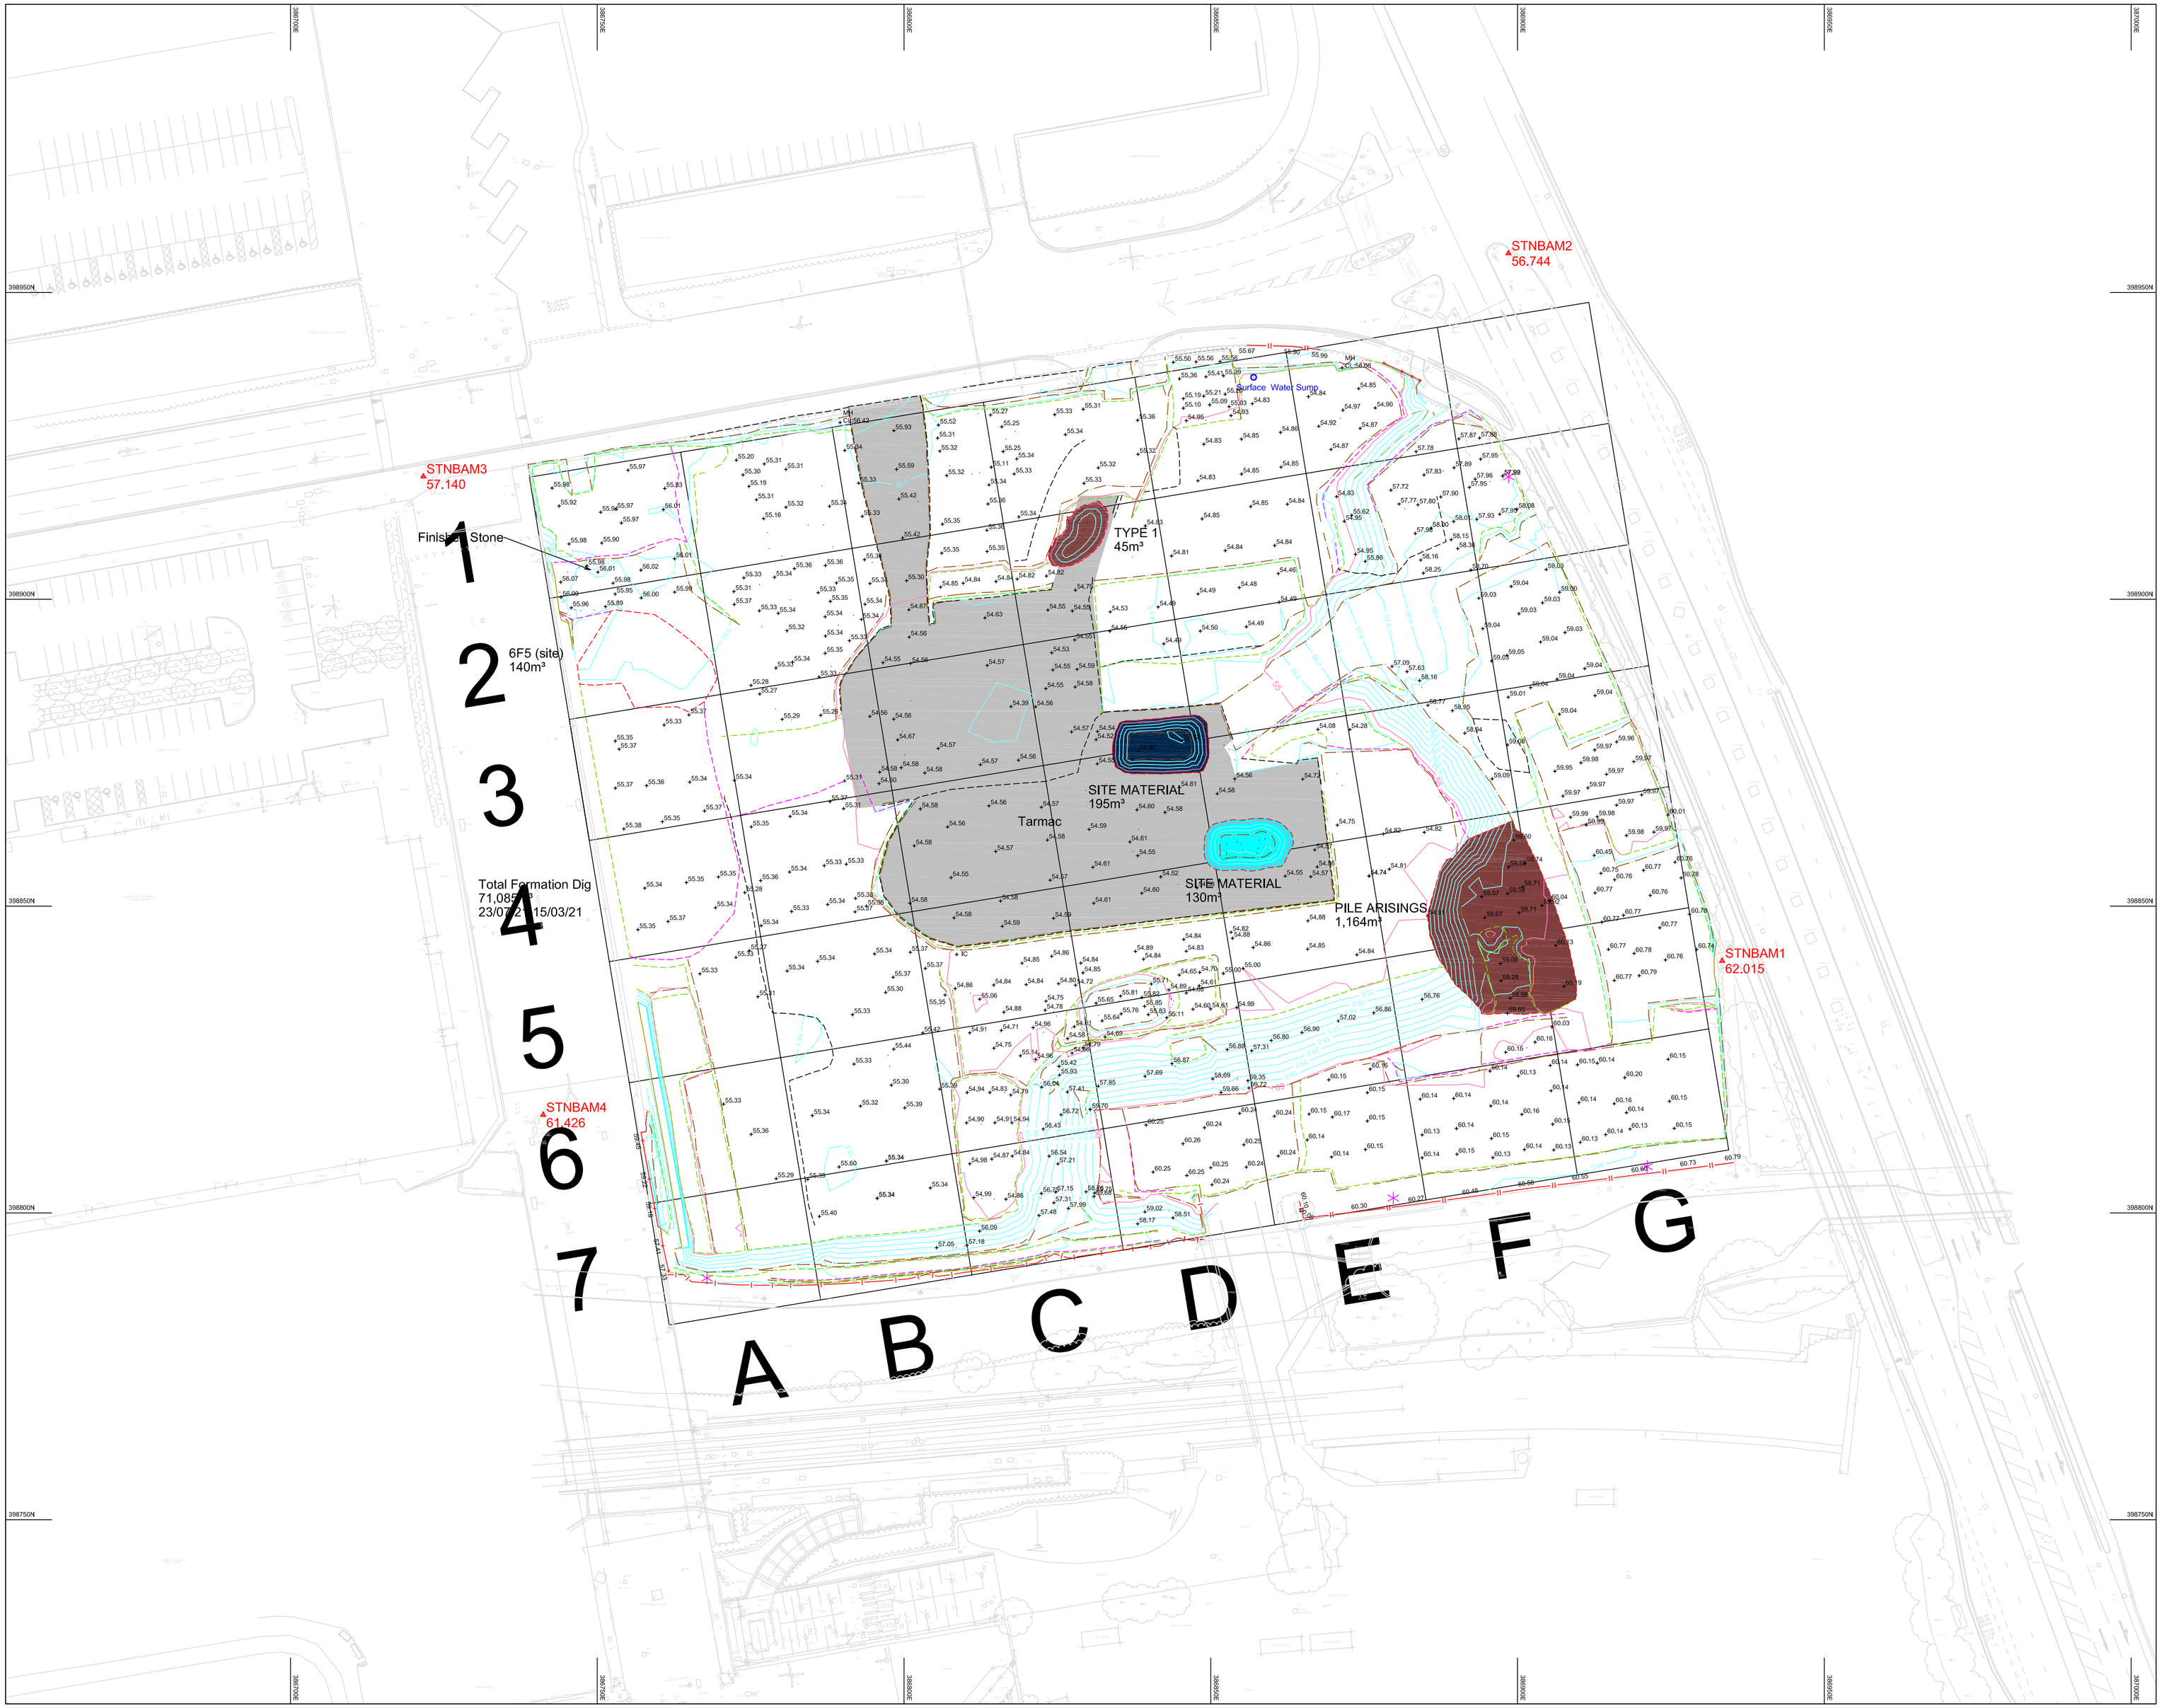

stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 - F 01284 584844 - E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordlnates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

Site Survey 30-07-2021
(SITE GRID 20m x 25m)

SCALE


1:500 @ A1

DATE

30/07/2021

DRAWING No.

11730d-4

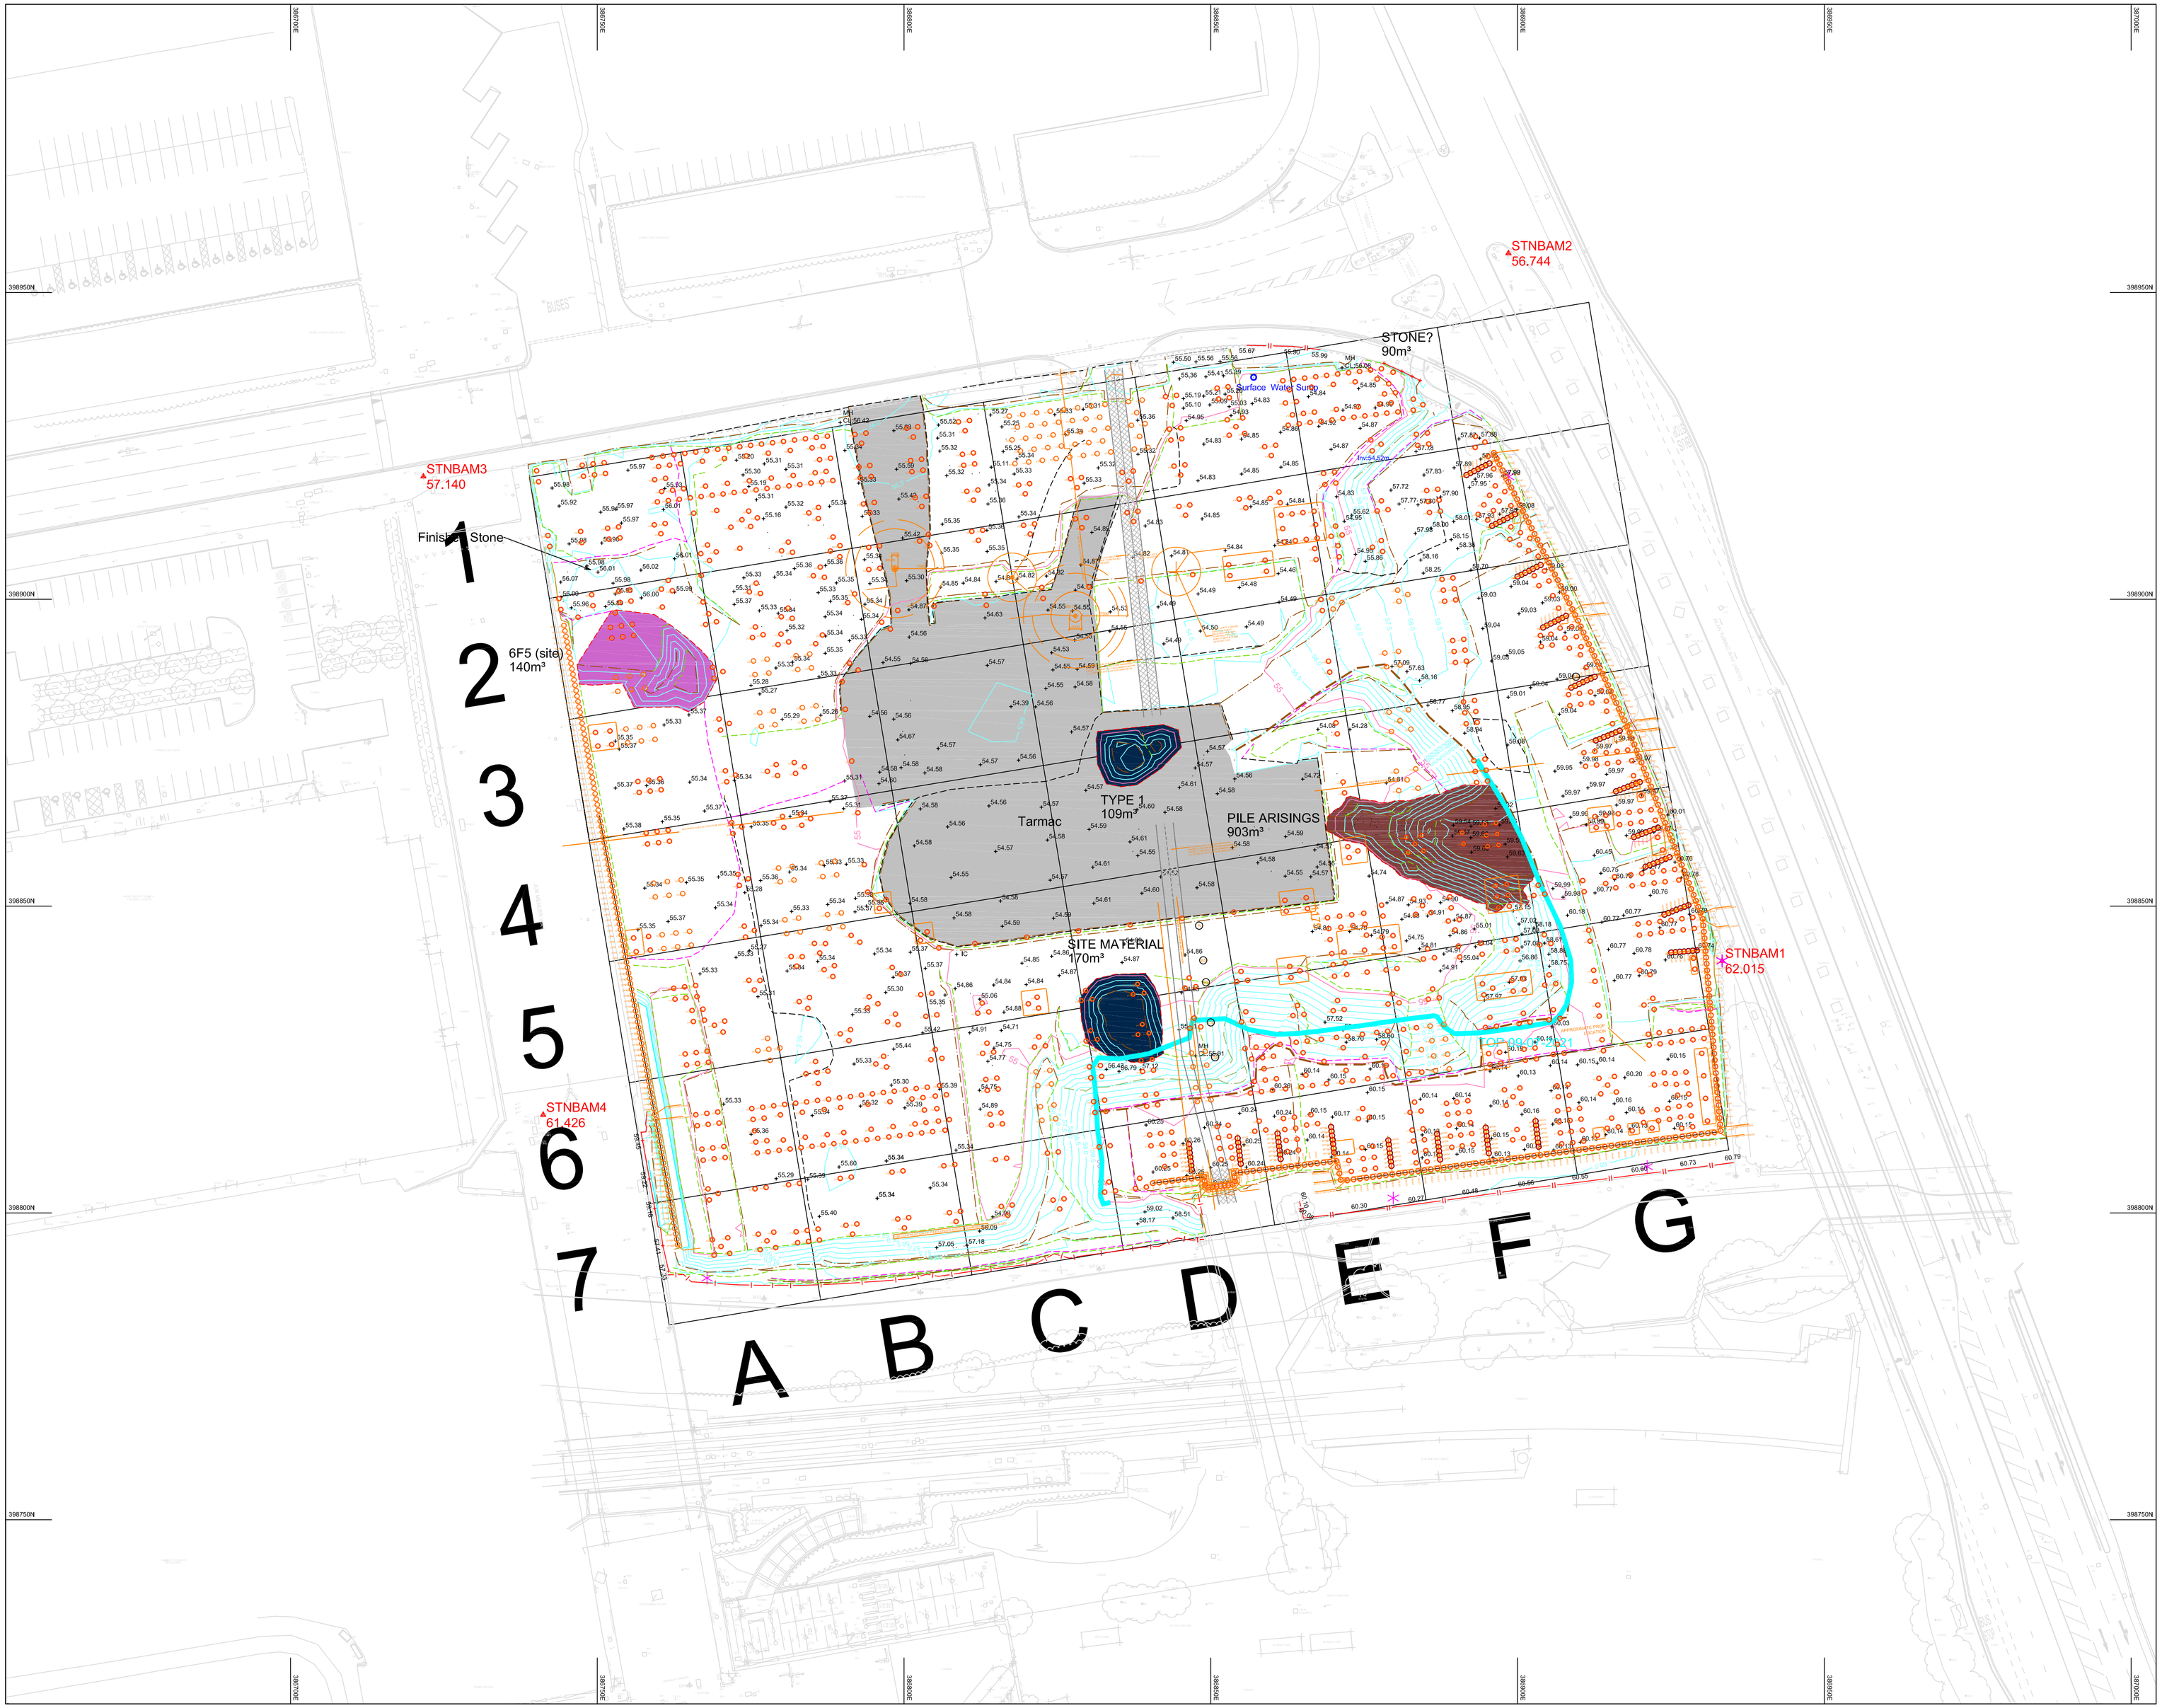

stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 · F 01284 584844 · E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordinates : SITE GRID

SURVEY STATIONS

Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

Site Survey 23-07-2021
(Pile Design)

SCALE
1:500 @ A1

DATE
23/07/2021

DRAWING No.

11730q-0



stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 · F 01284 584844 · E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordInates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.420

CLIENT

PROVECTUS

SITE

Project Bradford
101114


PROJECT

Site Survey 02-07-2021
(BRA-CSL-ZZ-ZZ-DR-X-00001)

SCALE	DATE
1:500 @ A1	02/07/2021

DRAWING No.

11730q-0

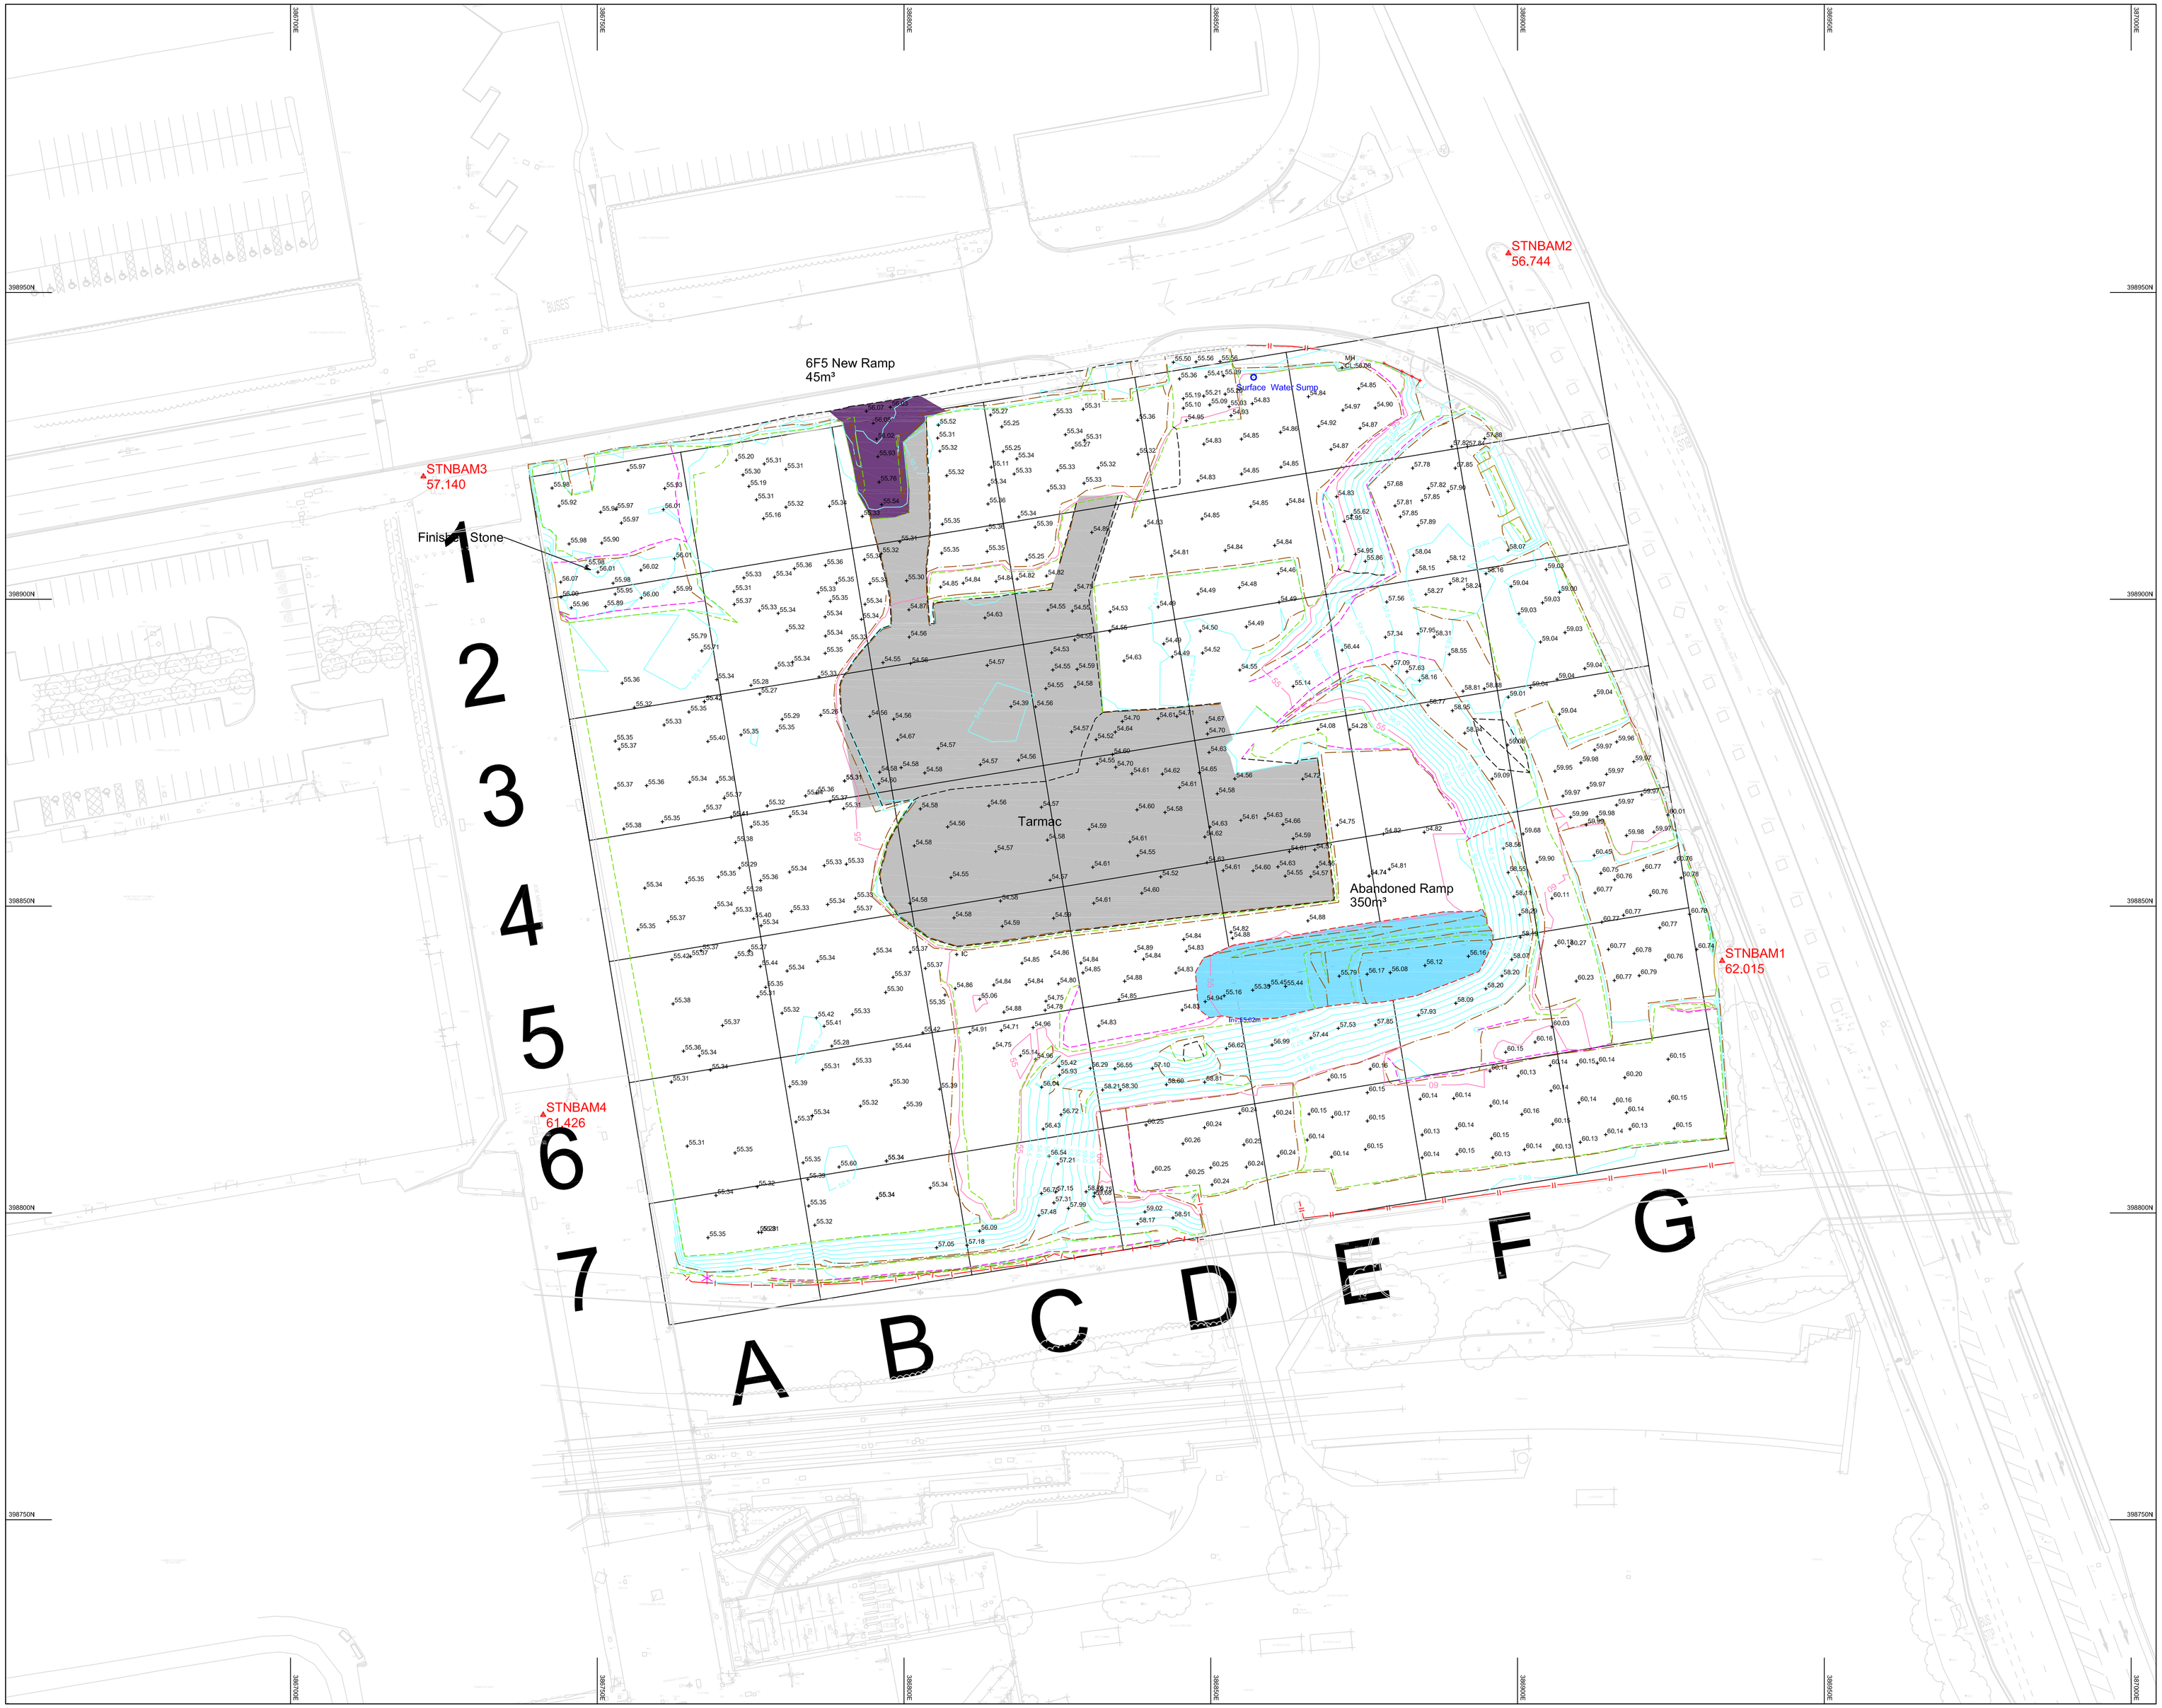

stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 F 01284 584844 E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordlnates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

Site Survey 06-08-2021
(SITE GRID 20m x 25m)

SCALE


1:500 @ A1

DATE

06/08/2021

DRAWING No.

11789d-0

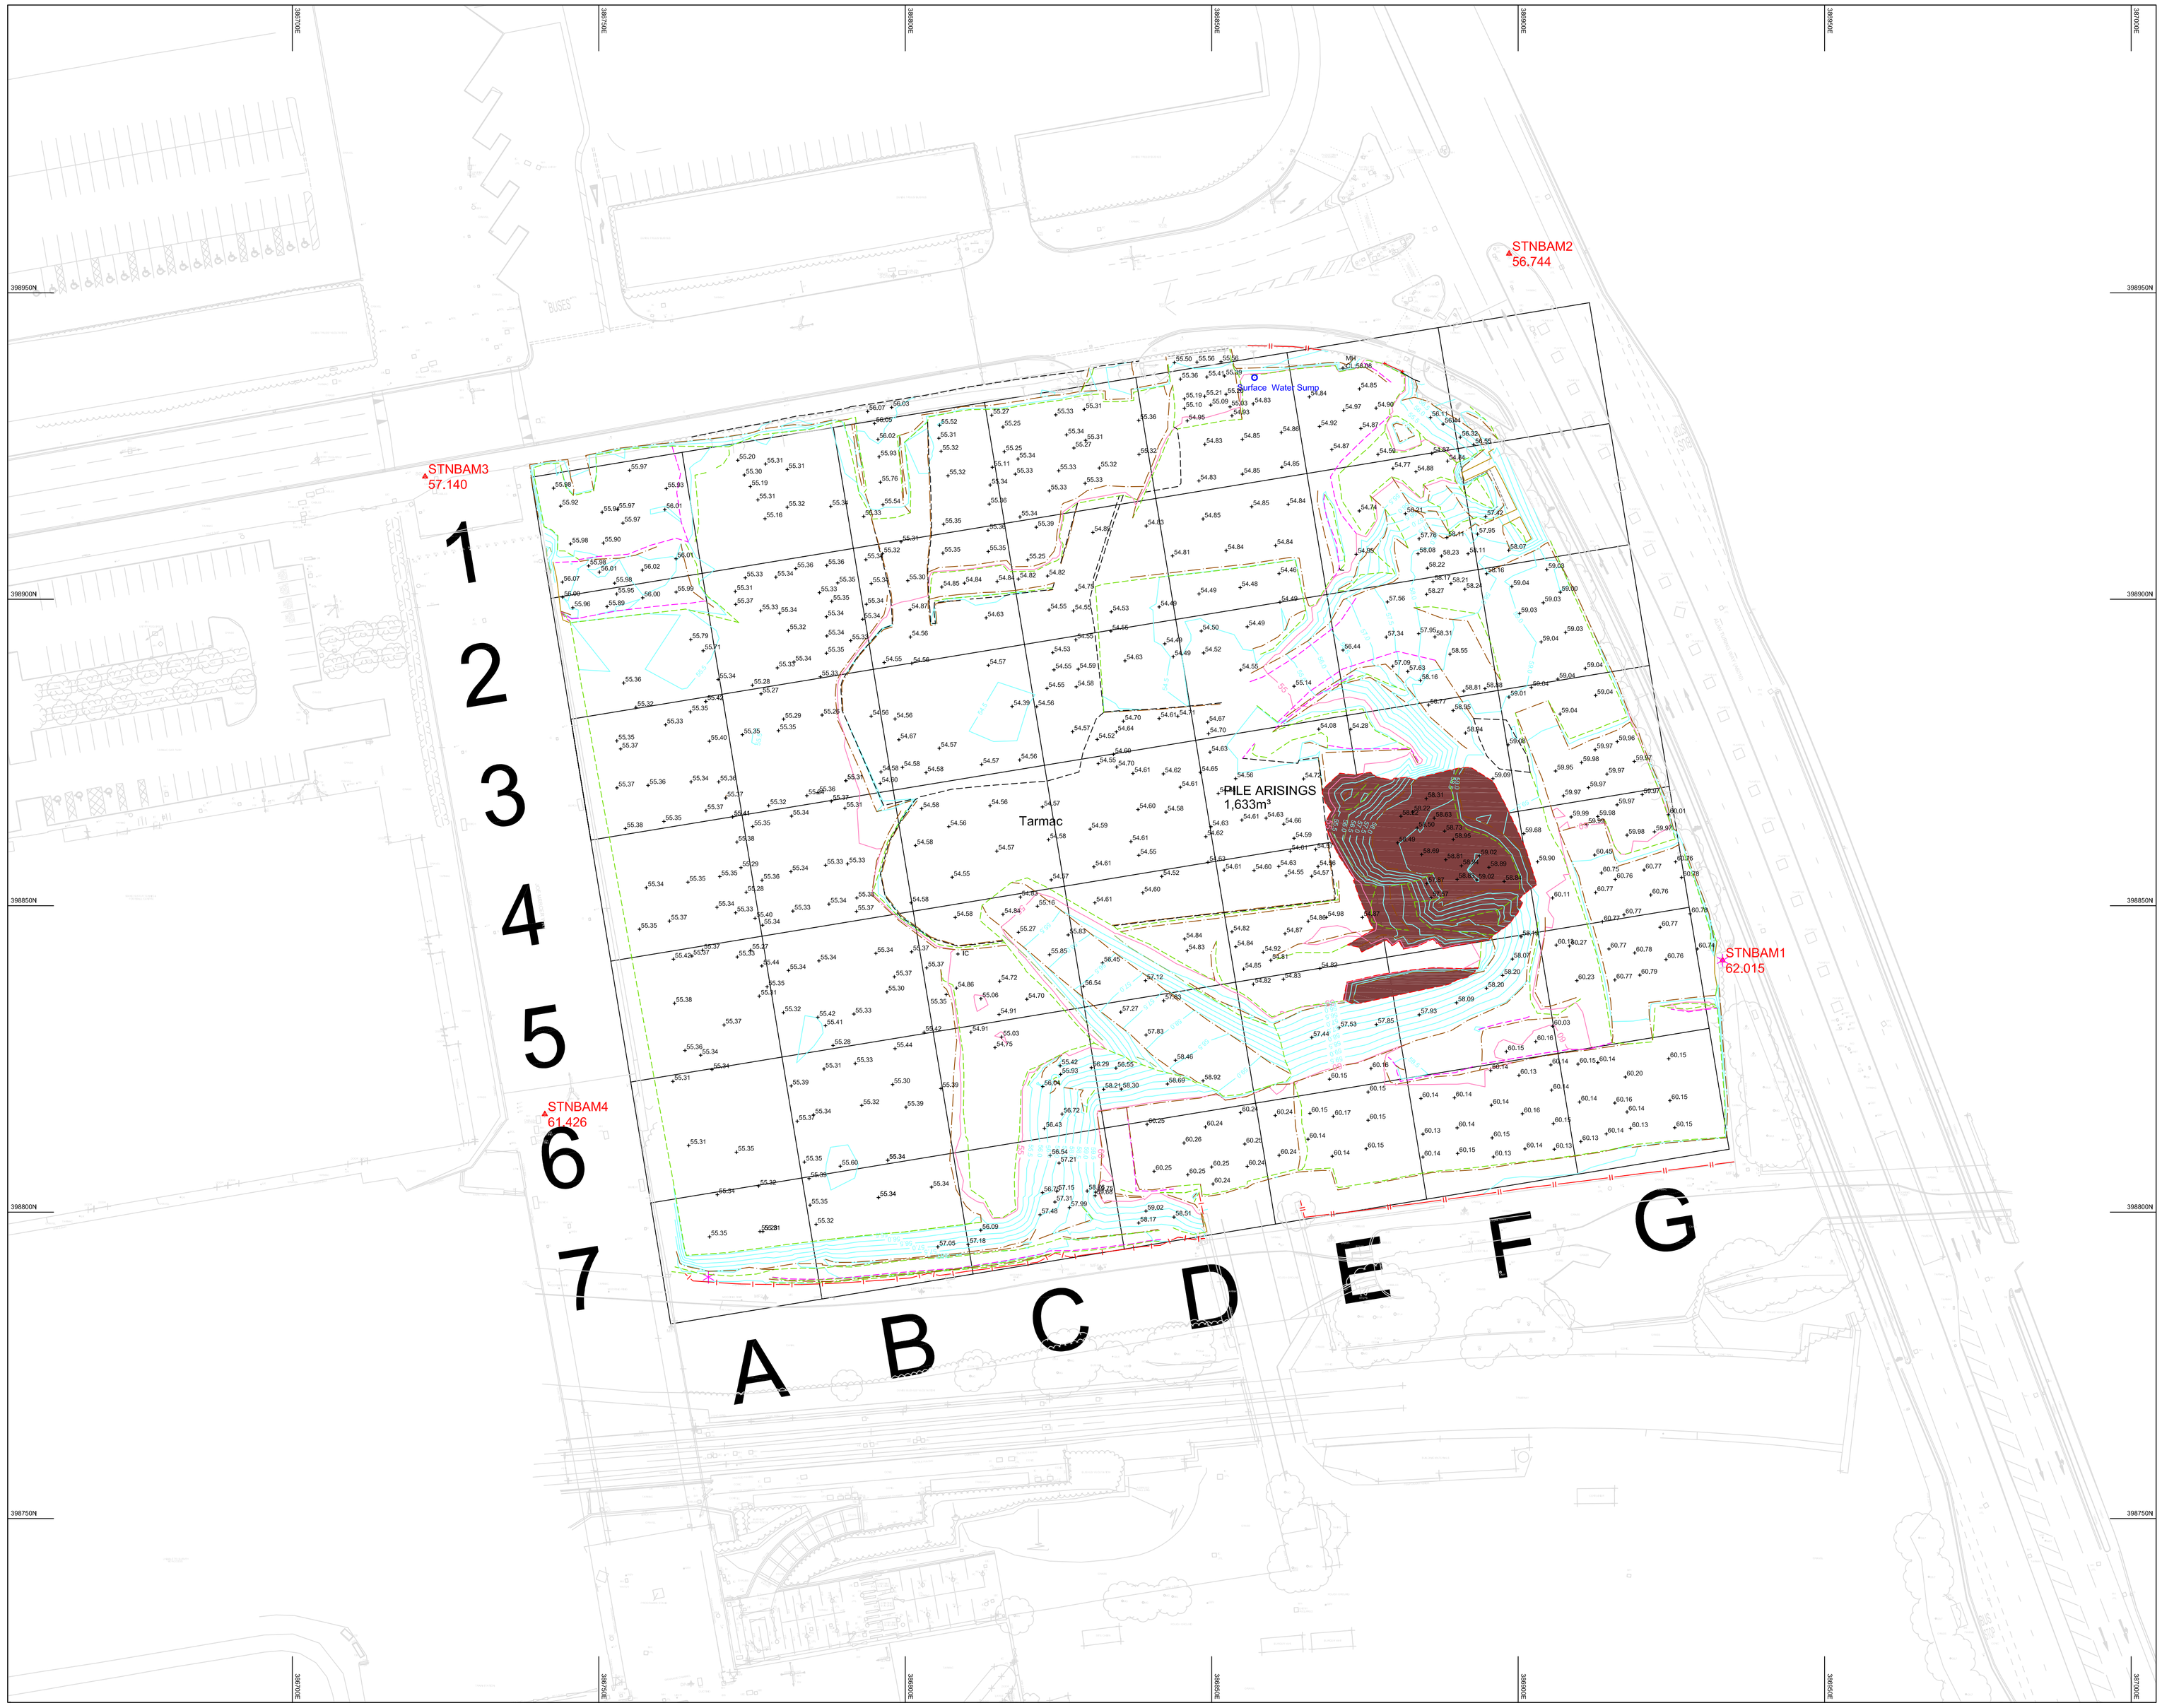

stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 · F 01284 584844 · E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordInates : SITE GRID

SURVEY STATIONS

Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

Site Survey 13-08-2021
(SITE GRID 20m x 25m)

SCALE

1:500 @ A1

DATE

13/08/2021

DRAWING No.

11789d-1



stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 · F 01284 584844 · E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordInates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

Site Survey 20-08-2021
(SITE GRID 20m x 25m)

SCALE	DATE
1:500 @ A1	20/08/2021

DRAWING No.

11789d-2



stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 F 01284 584844 E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordInates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

Site Survey 27-08-2021
(SITE GRID 20m x 25m)

SCALE	DATE
1:500 @ A1	27/08/2021

DRAWING No.

11789d-3



stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 · F 01284 584844 · E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordInates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

Site Survey 27-08-2021
(SITE GRID 20m x 25m)

SCALE


1:500 @ A1

DATE

03/09/2021

DRAWING No.

11851d-0

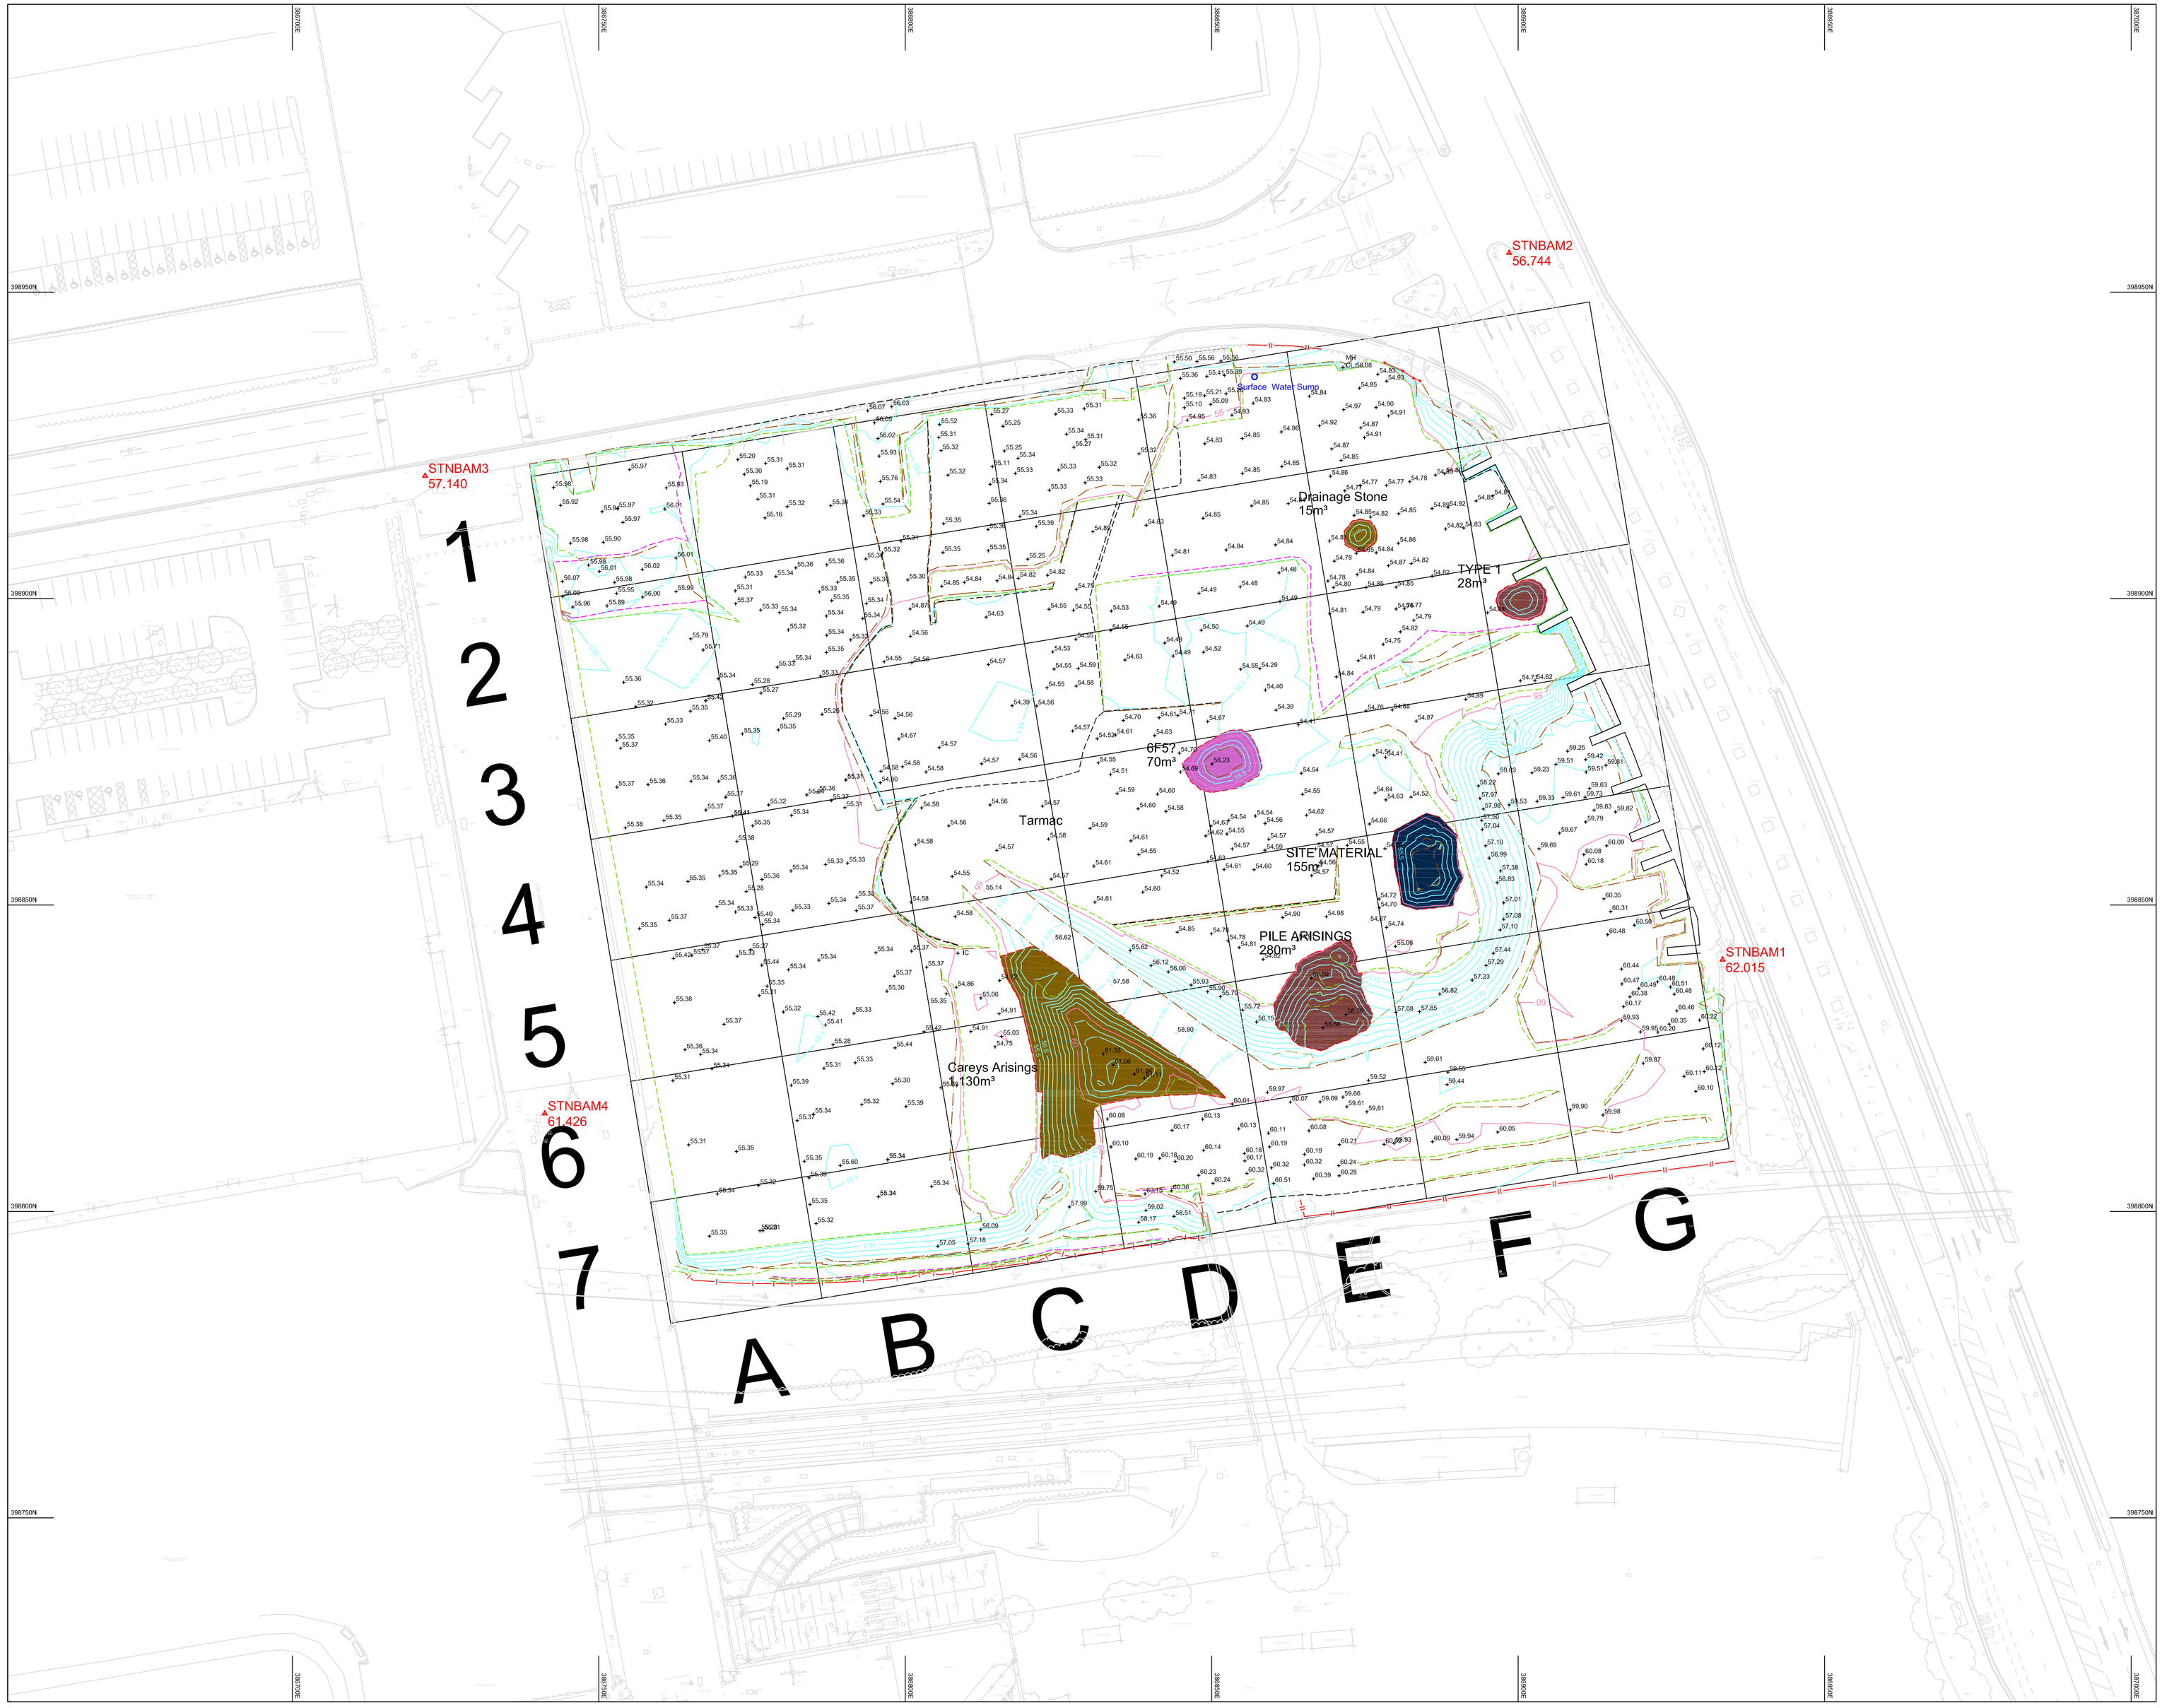

stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 F 01284 584844 E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordInates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

Site Survey 10-09-2021
(SITE GRID 20m x 25m)

SCALE	DATE
1:500 @ A1	10/09/2021

DRAWING No.

11851d-1



stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 · F 01284 584844 · E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordInates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114


PROJECT

Site Survey 17-09-2021
(SITE GRID 20m x 25m)

SCALE	DATE
1:500 @ A1	17/09/2021

DRAWING No.

11851d-2

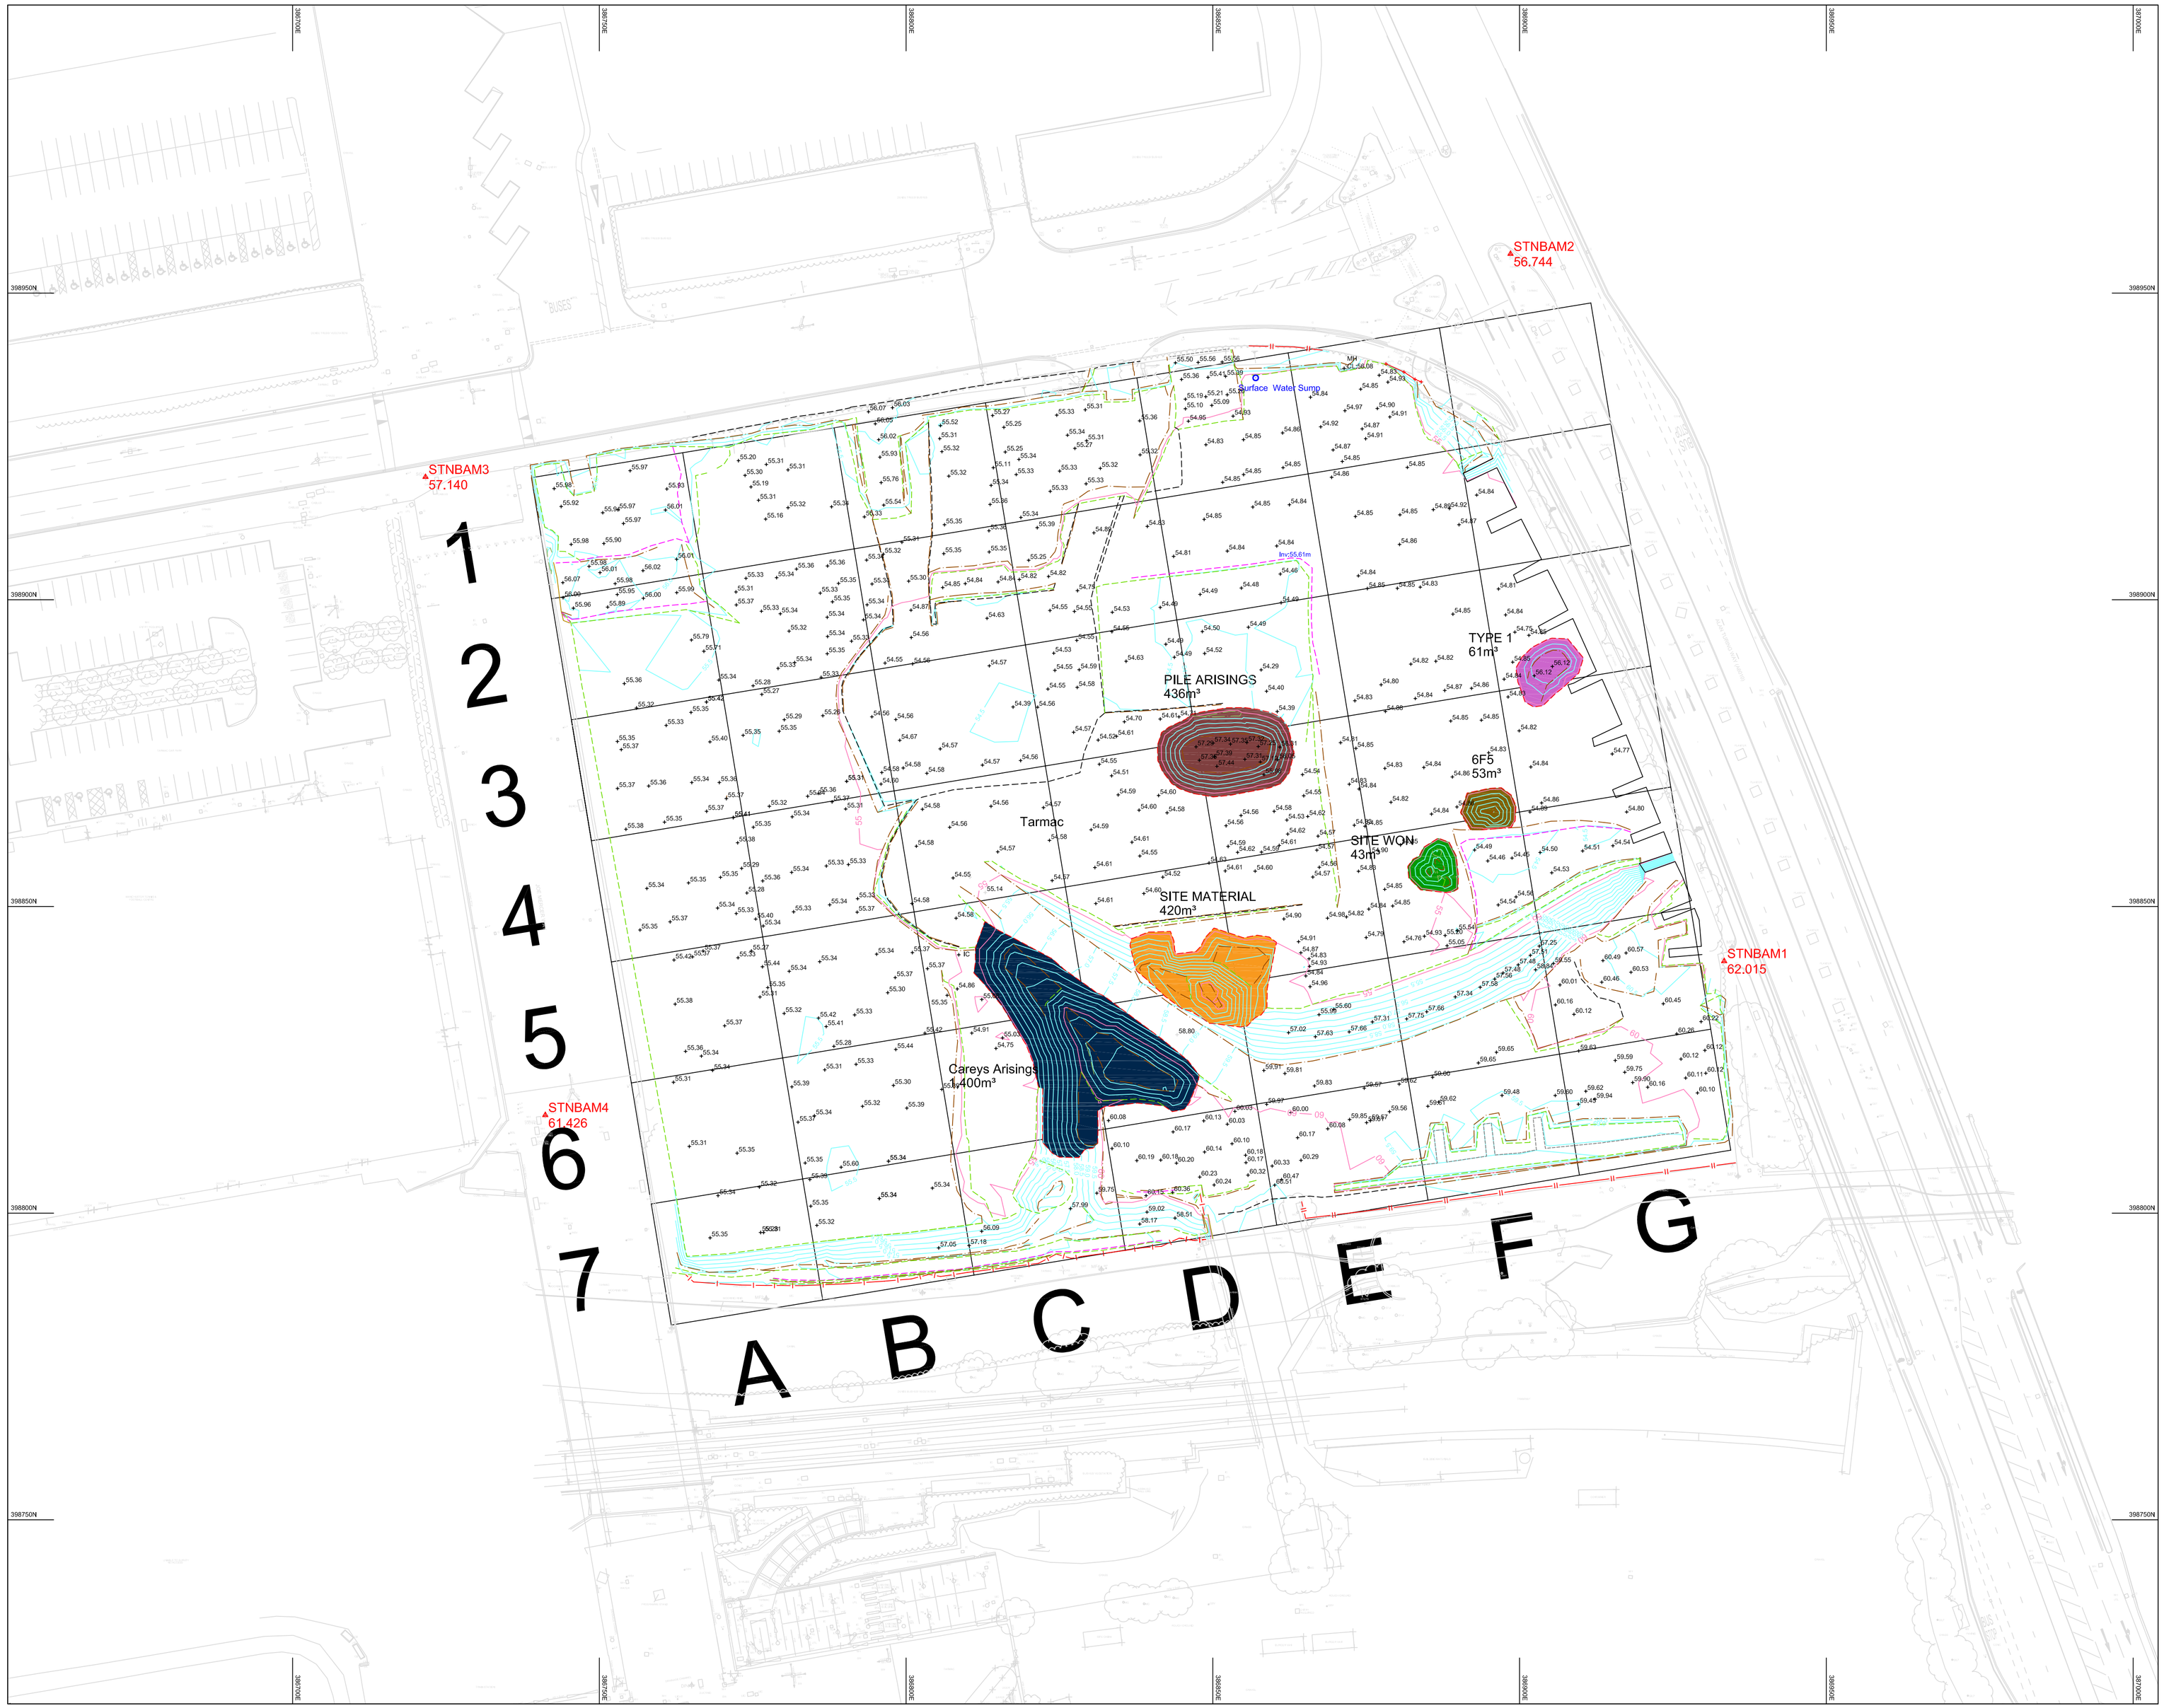

stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 · F 01284 584844 · E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordInates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

Site Survey 24-09-2021
(SITE GRID 20m x 25m)

SCALE


1:500 @ A1

DATE

24/09/2021

DRAWING No.

11851d-3

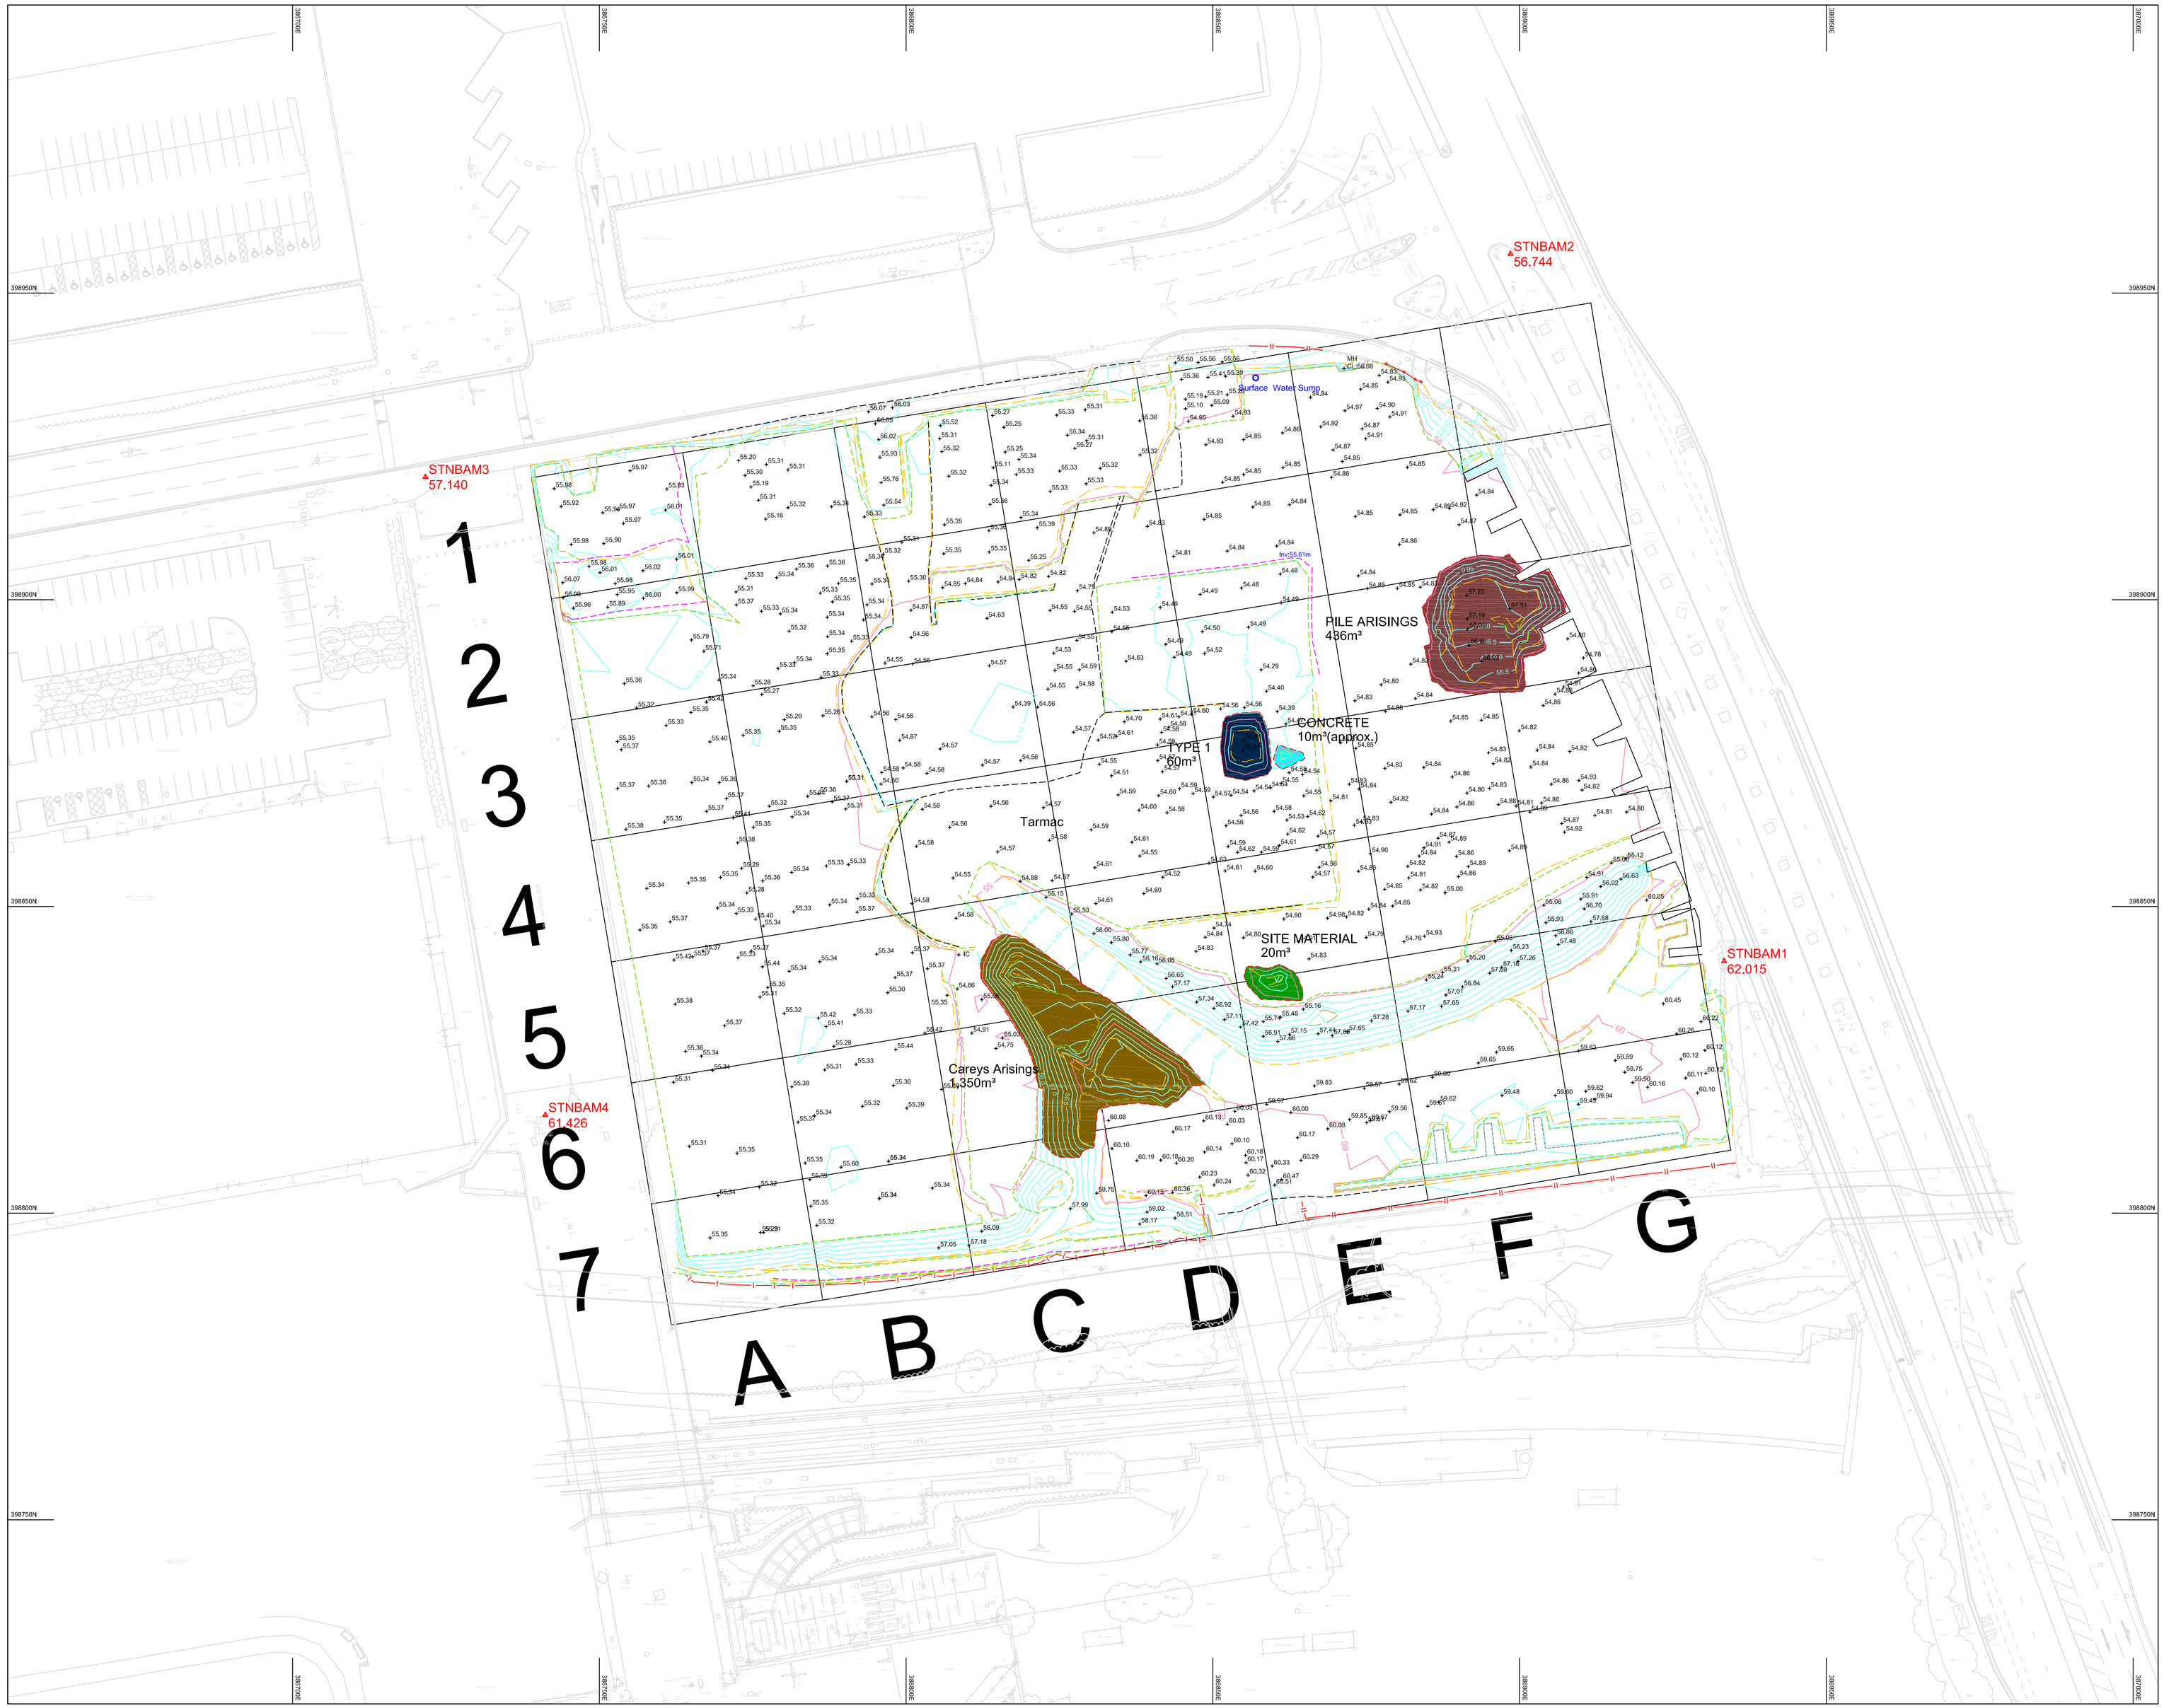

stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 - F 01284 584844 - E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordInates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

Site Survey 01-10-2021
(SITE GRID 20m x 25m)

SCALE


1:500 @ A1

DATE

01/10/2021

DRAWING No.

11897d-0

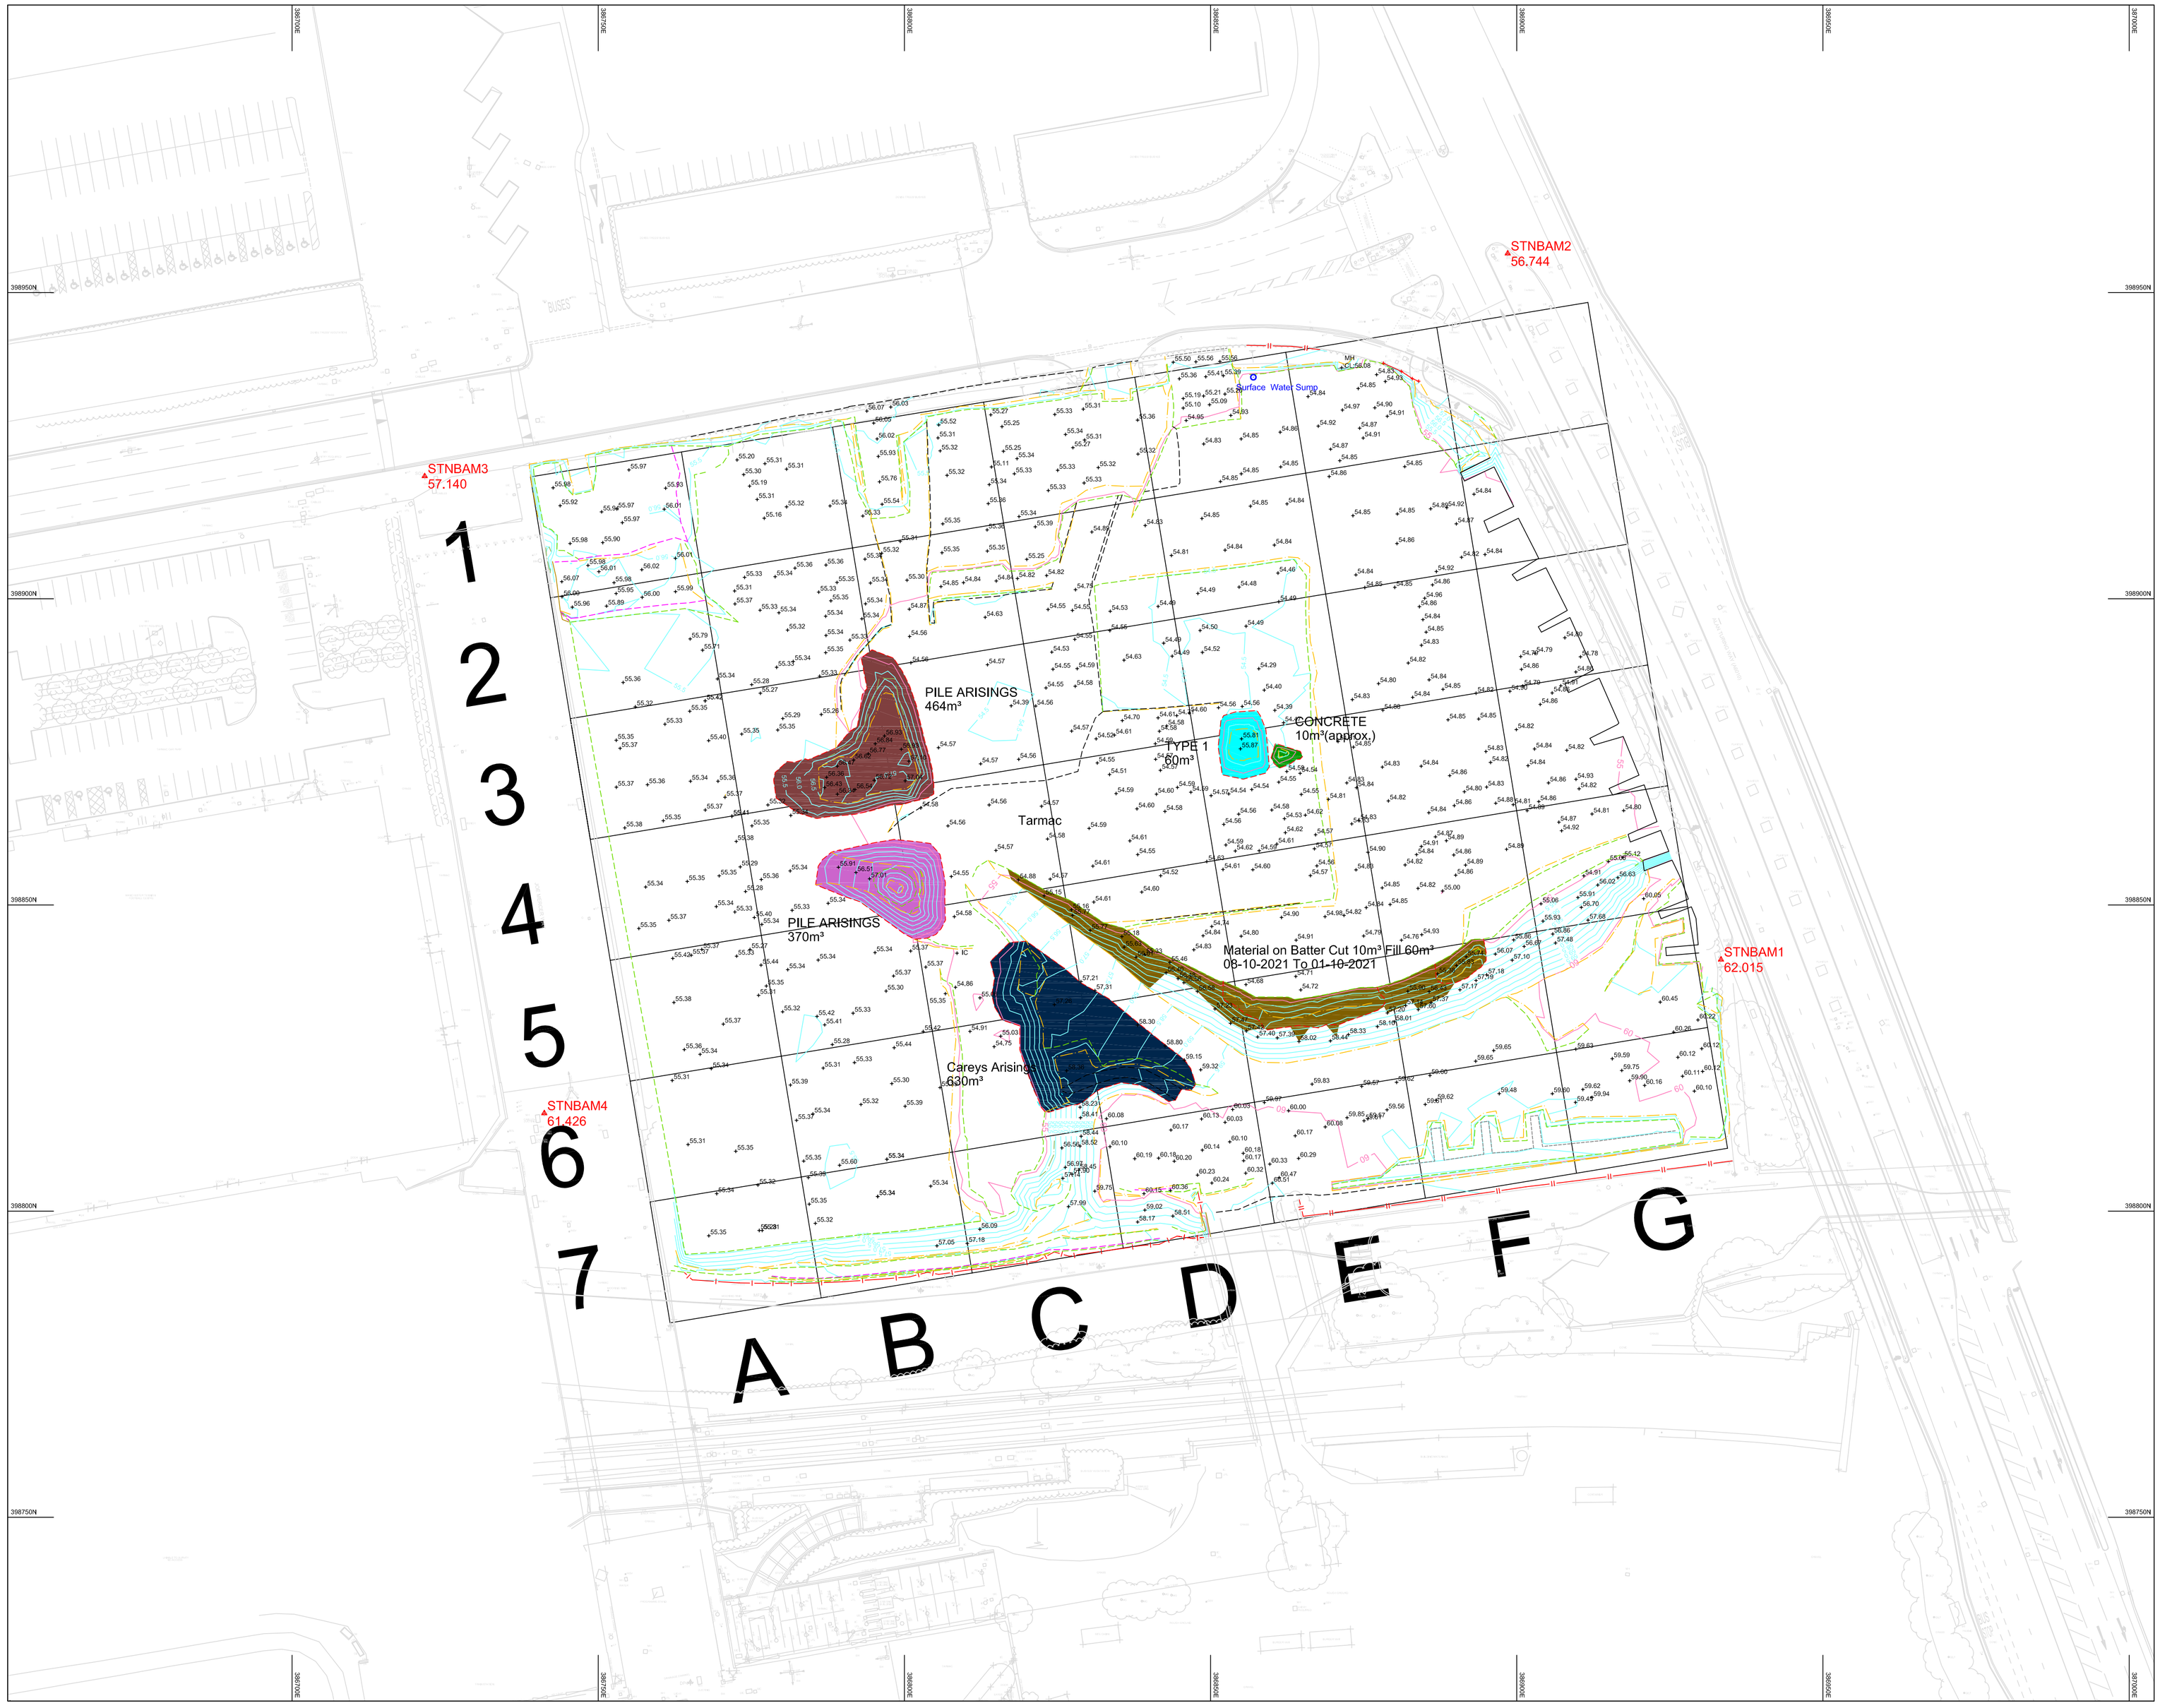

stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 F 01284 584844 E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordInates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.063	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

Site Survey 08-10-2021
(SITE GRID 20m x 25m)

SCALE

1:500 @ A1

DATE

08/10/2021

DRAWING No.

11897d-1



stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 F 01284 584844 E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordlnates : SITE GRID

SURVEY STATIONS

Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

Site Survey 15-10-2021
(SITE GRID 20m x 25m)

SCALE

1:500 @ A1

DATE

15/10/2021

DRAWING No.

11897d-2



stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 F 01284 584844 E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordlnates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

Site Survey 05-11-2021
(SITE GRID 20m x 25m)

SCALE	DATE
1:500 @ A1	05/11/2021

DRAWING No.

11963d-0



stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 - F 01284 584844 - E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordInates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

Site Survey 05-11-2021
(SITE GRID 20m x 25m)

SCALE


1:500 @ A1

DATE

12/11/2021

DRAWING No.

11963d-2

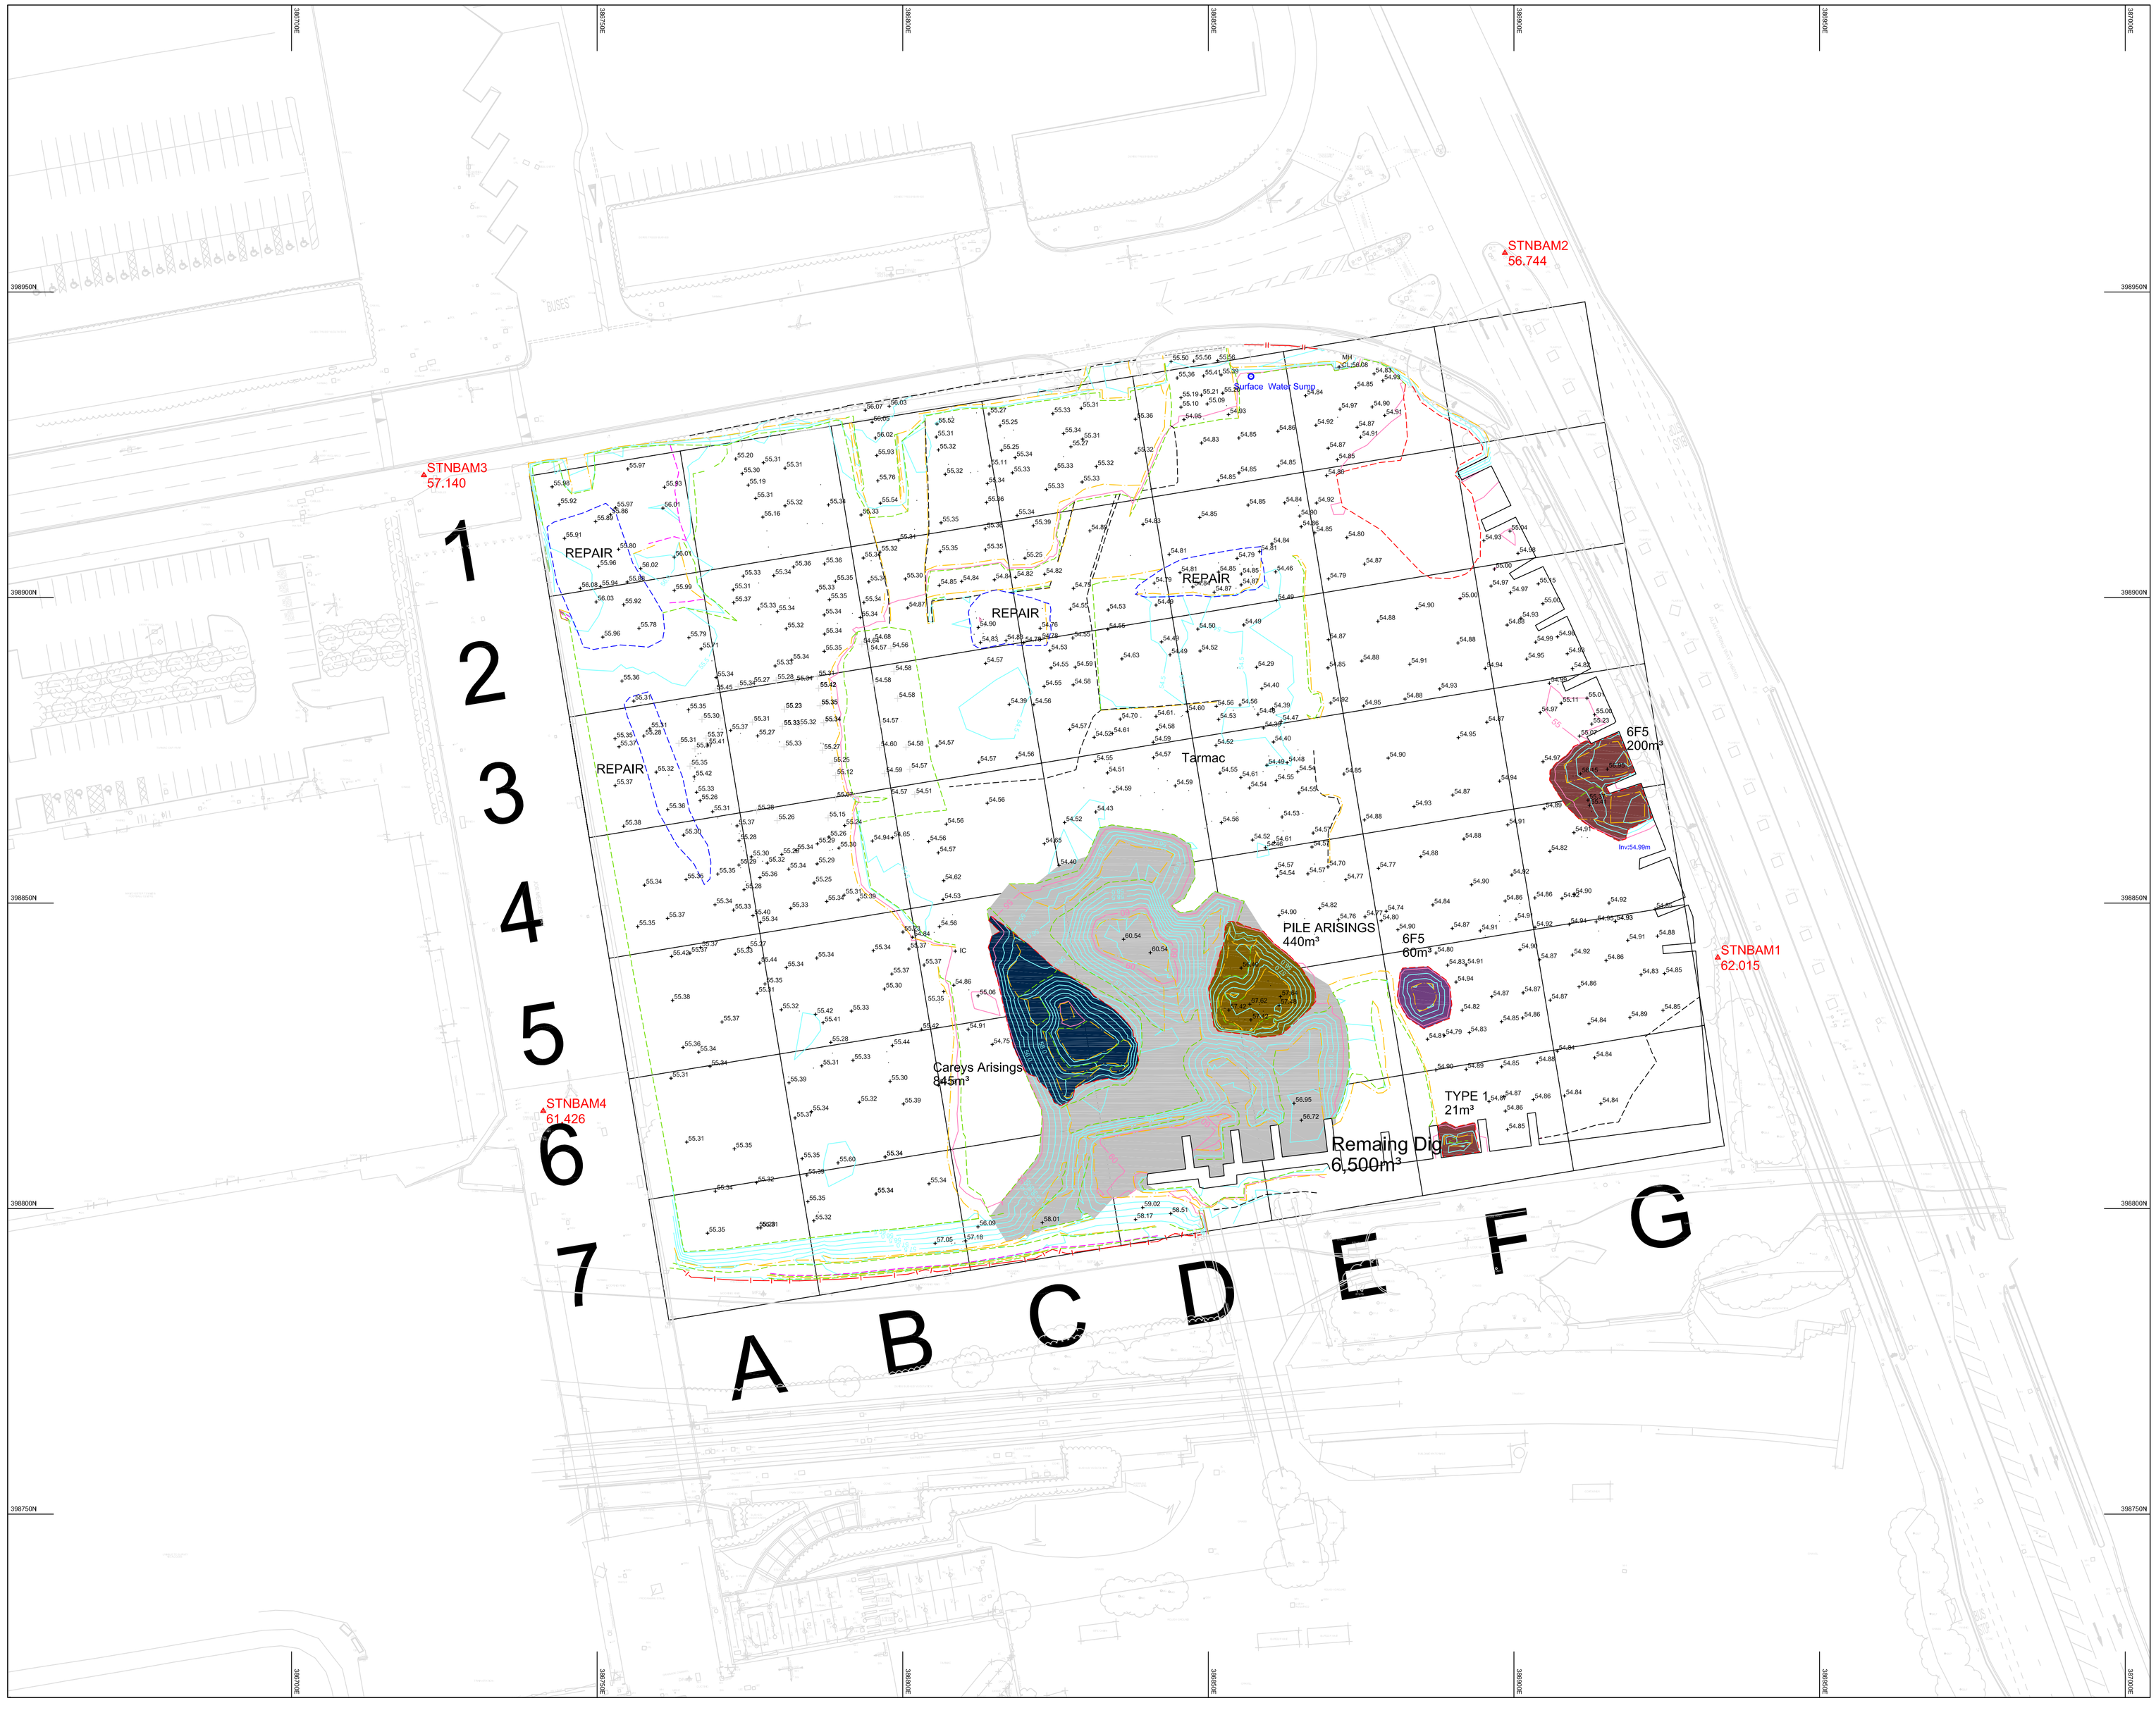

stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 - F 01284 584844 - E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordInates : SITE GRID

SURVEY STATIONS

Name	Easting	Northing	Height
DATUM1	386933.344	398841.063	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

Site Survey 19-11-2021
(SITE GRID 20m x 25m)

SCALE


1:500 @ A1

DATE

19/11/2021

DRAWING No.

11963d-3

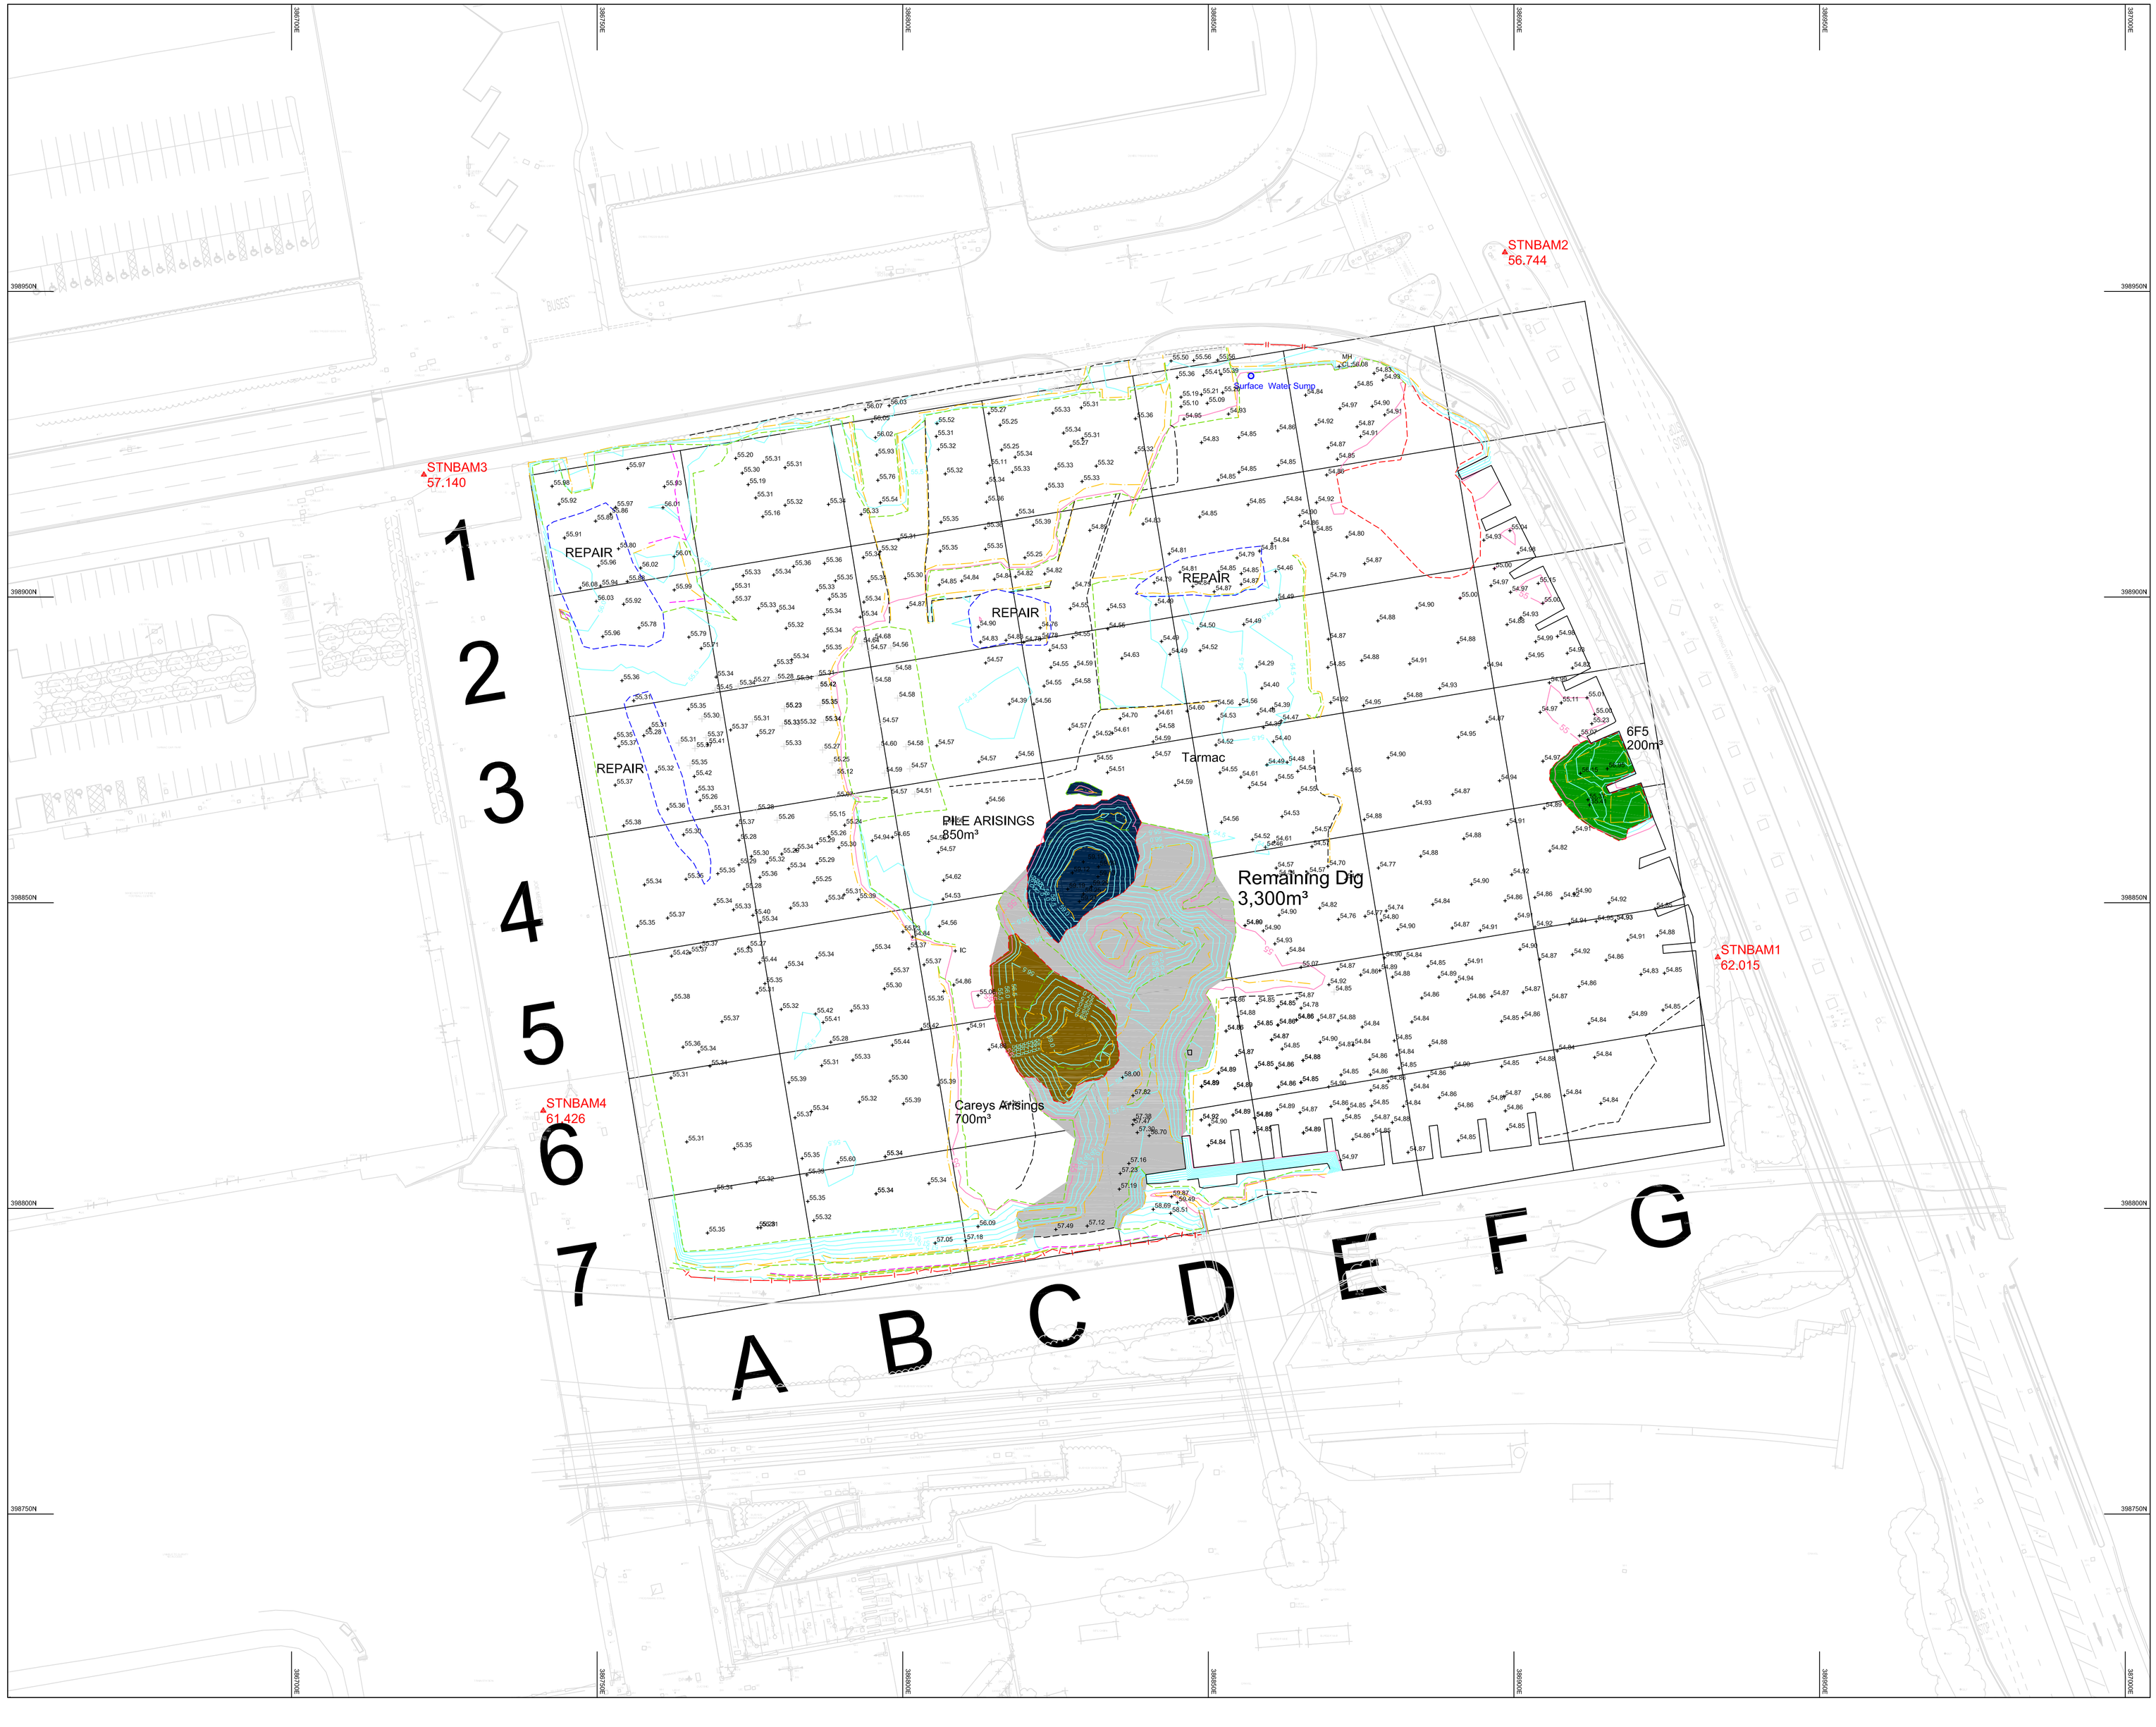

stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 · F 01284 584844 · E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordInates : SITE GRID

SURVEY STATIONS			
Name	Easting	Northing	Height
DATUM1	386933.344	398841.083	62.015
DATUM2	386898.512	398956.390	56.744
DATUM3	386721.675	398920.029	57.140
DATUM4	386741.198	398815.979	61.426

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

Site Survey 26-11-2021
(SITE GRID 20m x 25m)

SCALE	DATE
1:500 @ A1	26/11/2021

DRAWING No.

11963d-5

APPENDIX G Environmental Monitoring Forms

Proyectec Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	15.03.21	Com... Ref:	101114	Client:	BAM Construction Ltd	Assessor name	CN + JH
Daily Activity & Grid Ref.-	Environmental monitoring (not working).			General Notes:				PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	15:51				0.1	0.8	X	X	79.4	97.3		N	N	Right next to machine exhaust at BMP1	
BMP1															
BMP1															
BMP2	15:29				0.0	0.0	X	X	71.6	81.5		N	N		
BMP2															
BMP2															
BMP3	15:08				0.0	0.0	X	X	62.4	77.5		N	N		
BMP3															
BMP3					0.0	0.0									
BMP4	16:40				0.0	0.0	X	X	63.6	79.6		N	N		
BMP4															
BMP4															
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	14:08										X				
CMP2	14:11										X				
CMP3	14:13										X				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time:	N/A	Flow Meter (M^3):	N/A
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:			
9	SE	9	Overcast with sun	75% 6	Wet	1024	N/A	N/A	N/A			

Assessors Signature J. Abuse

Vectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	16.03.21	Contract No:	101114	Client:	BAM Construction Ltd	Assessor name:	JH
Daily Activity & Grid Ref.:	B1 + B2			General Notes:				PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	09:42				0.0	0.0	X	X	71.2	87.8		N	N		
BMP1	1:08				0.0	0.0			78.3	90.7				next to digging works	
BMP1	16:23				0.0	0.0									
BMP2	09:14				0.0	0.0	X	X	[illegible]	81.3		N	N		
BMP2	12:46				0.0	0.0			68.5	81.4					
BMP2	16:00				0.0	0.0									
BMP3	08:21				0.0	0.0	X	X	58.9	71.4		N	N		
BMP3	12:30				0.0	0.0	X	X	61.7	75.4		N	N		
BMP3	15:40				0.0	0.0									
BMP4	10:04				0.0	0.0	X	X	58.7	73.8		N	N		
BMP4	13:32				0.0	0.0			59.2	78.3					
BMP4	16:41				0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	17:03										N				
CMP2	16:58										N				
CMP3	16:55										N				

Meteorological and environmental conditions 09.00AM							WTP Inspection.		Time:		Flow Meter (M^3):	
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
10	WNW	8	Overcast + Showers	8	Wet	1026	N/A	N/A				

Assessors Signature: J. Hurst

Prover: Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	17.03.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	JH
Daily Activity & Grid Ref.:	B1 + B2					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	09.01	N			0.0	0.0	N	X	74.6	89.7		N	N		
BMP1	12.38	N			0.0	0.0									
BMP1	16.40	N			0.0	0.0									
BMP2	08.41	N			0.0	0.0	N	X	73.4	85.7		N	N		
BMP2	12.18	N			0.0	0.0									
BMP2	16.20	N			0.0	0.0									
BMP3	08.22	N			0.0	0.0	N	X	62.5	70.1		N	N		
BMP3	12.00	N			0.0	0.0									
BMP3	16.03	N			0.0	0.0									
BMP4	09.22	N			0.0	0.0	N	X	62.1	72.4		N	N		
BMP4	12.59	N			0.0	0.0									
BMP4	16.59	N			0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	17.10										N				
CMP2	17.13										N				
CMP3	17.15										N				

Meteorological and environmental conditions 08:06

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	Leaks / Over-topping (Y/N)	Time: 08:06	Flow Meter (M^3):	Equipment Impacted & Actions Taken to Rectify:
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar					
7	NW	7	Overcast, drizzle	7	wet	1035	N/A	N/A			

Assessors Signature J. Hurst

Prover — Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	18.03.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	JH
Daily Activity & Grid Ref.:	~~B1~~ B1 + B2					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	10:12	N			0.0	0.0	N	X	69.8	78.1		N	N		
BMP1	11:58	N			0.0	0.0									
BMP1	15:51	N			0.0	0.0									
BMP2	09:54	N			0.0	0.0	N	X	70.1	81.5		N	N		
BMP2	11:41	N			0.0	0.0									
BMP2	15:31	N			0.0	0.0									
BMP3	09:37	N			0.0	0.0	N	X	58.9	69.2		N	N		
BMP3	11:24	N			0.0	0.0									
BMP3	15:12	N			0.0	0.0									
BMP4	10:33	N			0.0	0.0	N	X	59.7	70.9		N	N		
BMP4	12:17	N			0.0	0.0									
BMP4	16:10	N			0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4	~~16:01~~														
CMP1	16:46										N				
CMP2	16:46										N				
CMP3	10:48										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time:	N/A	Flow Meter (M³):	N/A.
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:			
5	NW	6	overcast dry	7	wet	1032	N/A	N/A				

Assessors Signature: J Hurst.

Prover Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	19/03/21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	TH
Daily Activity & Grid Ref.:	C3 + C2			General Notes:				PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
911 BMP1	05:52	N	X		0.0	0.0	N	N	62.5	73.2		N	N		
BMP1	11:59	N	X		0.0	0.0									
BMP1	13:45	N	X		0.0	0.0									
910 BMP2	08:35	N	X		0.0	0.0	N	N	69.8	76.5		N	N		
BMP2	11:40	N	X		0.0	0.0									
BMP2	13:26	N	X		0.0	0.0									
909 BMP3	08:50	N	X		0.0	0.0	N	N	68.6	81.3		N	N		
BMP3	11:22	N	X		0.0	0.0									
BMP3	13:07	N	X		0.0	0.0									
912 BMP4	09:14	N	X		0.0	0.0	N	N	63.1	73.2		N	N		
BMP4	12:21	N	X		0.0	0.0									
BMP4	13:09	N	X		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	12:01										22				
CMP2	12:03										22				
CMP3	12:06										22				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time:	Flow Meter (M^3):	Equipment Impacted & Actions Taken to Rectify:
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar					
9	NNE	7	Dry Overcast	8	Dry	1030	N/A	N/A			

Assessors Signature J. Hurst

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	22/03/22	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	TH
Daily Activity & Grid Ref.:	B3 + B4.					General Notes:		PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Friabee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	09:46	N			0.0	6.0	N	N	71.5	79.6		N	N		
BMP1	13:02	N			0.0	0.0									
BMP1	15:51	N			0.0	0.0									
BMP2	09:26	N			0.0	0.0	N	N	70.9	76.7		N	N		
BMP2	12:41	N			0.0	0.0									
BMP2	15:28	N			0.0	0.0									
BMP3	09:04	N			0.0	0.0	N	N	68.3	76.4		N	N		
BMP3	12:22	N			0.0	0.0									
BMP3	15:10	N			0.0	0.0									
BMP4	10:06	N			0.0	0.0	N	N	65.7	73.8		N	N		
BMP4	13:24	N			0.0	0.0									
BMP4	16:12	N			0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	16:25										N				
CMP2	16:30										N				
CMP3	16:32										N.				

Meteorological and environmental conditions							WTP Inspection.		Time:	N/A.	Flow Meter (M^3):	N/A.
Wind speed	Wind Directio	Temp	Weather description	Cloud cover	Ground conditions	Barometric	System Working	Leaks / Over-topping	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
8		7	dry overcast.	7	dry.	1023	N/A	N/A				

Assessors Signature J. Hurst.

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	23.03.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	JM
Daily Activity & Grid Ref.:	AB + 6 + 7					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	10:49	N			0.0	0.0	N	N	70.3	74.9		N	N	Dust has started to increase as the day has progressed from initial observations this morning.	
BMP1	13:11	N			0.0	0.0									
BMP1	15:42	N			0.0	0.0									
BMP2	10:30	N			0.0	0.0	N	N	67.3	75.3		N	N		
BMP2	2:53	N			0.0	0.0									
BMP2	15:22	N			0.0	0.0									
BMP3	10:07	N			0.0	0.0	N	N	59.2	75.9		N	N	* If no rain tomorrow I recommend dust suppression measures taken tomorrow. If ground conditions dont improve.	
BMP3	12:36	N			0.0	0.0									
BMP3	15:04	N			0.0	0.0									
BMP4	11:13	N			0.0	0.0	N	N	58.8	75.1		N	N		
BMP4	13:25	N			0.0	0.0									
BMP4	16:02	N			0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1															
CMP2															
CMP3															

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time: N/A	Flow Meter (M^3): N/A
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
11	SW	8	dry Overcast	8	dry	1020	N/A	N/A	N/A	

Assessors Signature: J. Hurst.

Prove[illegible] Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	24.03.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	J H.
Daily Activity & Grid Ref.:	AS + 6 + 7.					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	09:43	N	N		0.0	0.0	N	N	71.2	80.3		N	N	* Dust supression not needed as rain in the night.	
BMP1	11:53	N	N		0.0	0.0									
BMP1	15:48	N	N		0	0									
BMP2	09:23	N	N		0.0	0.0	N	N	64.9	78.7		N	N	** Dust increased as day has progressed.	
BMP2	11:28	N	N		0.0	0.0									
BMP2	15:02	N	N		0.0	0									
BMP3	09:04	N	N		0.0	0.0	N	N	60.8	73.1		N	N		
BMP3	11:08	N	N		0.0	0.0									
BMP3	15:19	N	N		0.0	0.0									
BMP4	10:11	N	N		0.0	0.0	N	N	72.8	79.1		N	N.		
BMP4	12:21	N	N		0.0	0.0									
BMP4	16:14	N	N												
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	16:40										N				
CMP2	16:46										N				
CMP3	16:47										N				

Meteorological and environmental conditions							WTP Inspection.		Time: N/A	Flow Meter (M^3): N/A
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:	
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar				
8	WSW	9	Sunny & dry	2	Damp	1019	N/A	N/A	N/A	

Assessors Signature J. Murst

Prove... Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	25.03.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	JM
Daily Activity & Grid Ref.:	B3 + B4 + A7+6+5.					General Notes:		PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
S04 BMP1	09:06	N	N		0.0	0.0	N	N	70.1	89		N	N	*File S06 for loading of wagon from stock pile.	
BMP1	11:37	N	N		0.0	0.0									
BMP1	16:13	N	N		0.0	0.0									
S01 BMP2	08:41	N	N		0.0	0.0	N	N	71.6	81.5		N	N		
BMP2	11:34	N	N		0.0	0.0									
BMP2	15:49	N	N		0.0	0.0									
S00 BMP3	08:22	N	N		0.0	0.0	N	N	60.2	75.0		N	N		
BMP3	11:00	N	N		0.0	0.0									
BMP3	15:32	N	N		0.0	0.0									
BMP4	09:28	N	N		0.0	0.0	N	N	61.6	76.1		N	N	• Dust starting to increase. Not nuisance levels.	
BMP4	12:18	N	N		0.0	0.0									
BMP4	16:36	N	N												
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	17:11										N				
CMP2	17:14										N				
CMP3	17:16										N				



Meteorological and environmental conditions							WTP Inspection.		Time:	N/A	Flow Meter (M^3):	N/A
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
9	SW	8	Overcast, dry.	4	wet	1015	N/A	N/A	N/A.			

Assessors Signature: J Hurst.

Prove... Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	26.03.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	JH.
Daily Activity & Grid Ref.:	A4 (excavation) C3+C2 (6FS + Type1 Na)			General Notes:				PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	06:46	N	N		0.0	0.0	N	N	70.6	79.6		N	N	* file 600 + 601 for boundary monitoring at 07:03 & 07:20	
BMP1	12:01	N	N		0.0	0.0									
BMP1	16:00	N	N		0.0	0.0									
BMP2	08:13	N	N		0.0	0.6	N	N	68.1	75.4		N	N		
BMP2	11:40	N	N		0.0	0.0								* Heavy rain from 09am to around 11am.	
BMP2	15:37	N	N		0.0	0.0									
BMP3	07:56	N	N		0.0	0.0	N	N	57.4	68.7		N	N		
BMP3	11:21	N	N		0.0	0.0									
BMP3	15:15	N	N		0.0	0.0									
BMP4	09:05	N	N		0.0	0.0	N	N	59.9	65.3		N	N		
BMP4	12:29	N	N		0.0	0.0									
BMP4	16:24	N	N		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	17:10										N				
CMP2	17:12										N				
CMP3	17:13										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar
14	SSW	9°C	Overcast + Dry	7	Damp	1001

* 07:30am

WTP Inspection.

Time:	N/A	Flow Meter (M³):	N/A

System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:
N/A	N/A	N/A.

Assessors Signature: J. Hurst.

Prove **Environmental Monitoring Form 101114**

Site:	Project Bradford	Date:	29.03.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	TH
Daily Activity & Grid Ref.:	A6+A5+B4+B5+C1+B7.					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08:06	N	N		0.0	0.0	N	N	72.4	79.2		N	N	** 902 06:45am boundary noise monitoring of Road @ BMP2 with no loading.	
BMP1	10:41	N	N		0.0	0.0									
BMP1	14:42	N	N		0.0	0.0									
BMP2	09:34	N	N		0.0	0.0	N	N	73.8	79.5		N	N		
BMP2	10:18	N	N		0.0	0.0									
BMP2	14:15	N	N		0.0	0.0									
BMP3	09:57	N	N		0.0	0.0	N	N	62.1	75.9		N	N		
BMP3	09:10	N	N		0.0	0.0									
BMP3	13:51	N	N		0.0	0.0									
BMP4	08:27	N	N		0.0	0.0	N	N	59.3	68.7		N	N.		
BMP4	10:39	N	N		0.0	0.0									
BMP4	15:11	N	N		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	16:12										N				
CMP2	16:14										N				
CMP3	10:15										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time:	N/A	Flow Meter (M³):	N/A
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:			
13	SW	12	clear sky with some clouds, dry, mild.	3	wet.	1019	N/A	N/A	N/A.			

Assessors Signature: JMust

Prove Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	30.03.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	JH
Daily Activity & Grid Ref.:	[redacted] (C1+A4+D4 (A7)			General Notes:				PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
		(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08:31	N	N		0.0	0.0	N	N	76.3	83.5		N	N	[redacted]	
BMP1	11:16	N	N		0.0	0.0									
BMP1	13:59	N			0.0	0.0									
BMP2	08:11	N	N		0.0	0.0	N	N	75.6	84.7		N	N		
BMP2	10:49	N	N		0.0	0.0									
BMP2	13:40	N			0.0	0.0									
BMP3	07:24	N	N		0.0	0.0	N	N	59.3	71.8		N	N		
BMP3	10:28	N	N		0.0	0.0									
BMP3	13:23	N			0.0	0.0									
BMP4	07:47	N	N		0.0	0.0	N	N	57.2	69.7		N	N		
BMP4	10:07	N	N		0.0	0.0									
BMP4	14:19	N			0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:30										N/A				
CMP2	15:31										N/A				
CMP3	15:33										N/A				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time:	N/A	Flow Meter (M³):	N/A
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:			
4	S	7°	Dry Sunny Clear	0	Slightly Damp	1027	N/A	N/A	N/A			

Assessors Signature [signature]

Provec nvironmental Monitoring Form 101114

Site:	Project Bradford	Date:	31.03.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	JH
Daily Activity & Grid Ref.:	A7 C4 D4 + 3 + 2					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08:48	N	N		0.0	0.0	N	N	64.7	76.9		N	N	As Day progressed dust increased, not at nuisance level.	
BMP1	12:17	N	N		0.0	0.0									
BMP1	15:46				0.0	0.0									
BMP2	08:15	N	N		0.0	0.0	N	N	74.3	84.8		N	N		
BMP2	11:49	N	N		0.0	0.0									
BMP2	15:30				0.0	0.0									
BMP3	09:54	N	N		0.0	0.0	N	N	60.8	75.7		N	N		
BMP3	11:27	N	N		0.0	0.0									
BMP3	15:09				0.0	0.0									
BMP4	09:11	N	N		0.0	0.0	N	N	66.2	73.4		N	N		
BMP4	12:39	N	N		0.0	0.0									
BMP4	16:12				0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	16:30										N				
CMP2	10:51										N				
CMP3	16:32										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	N/A	Flow Meter (M³):	N/A
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
4	S	11	clear sky dry	1	dry	1020	N/A	N/A	N/A			

Assessors Signature J. Hurst

Proyectu... Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	01·04·21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	JM.
Daily Activity & Grid Ref.:	D1+D4+B3+B4+A7					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to)	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08:33	N	N		0.0	0.0	N	N	70.9	83.6		N	N	*Dust has began to increase as the day has progressed.	
BMP1	11:46	N	N		0.0	0.0									
BMP1	15:29	N	N		0.0	0.0									
BMP2	08:31	N	N		0.0	0.0	N	N	73.7	84.8		N	N		
BMP2	11:22	N	N		0.0	0.0									
BMP2	14:59	N	N		0.0	0.0								*Dust suppression measures in opperation	
BMP3	08:04	N	N		0.0	0.0	N	N	63.8	73.3		N	N		
BMP3	11:03	N	N		0.0	0.0									
BMP3	14:38	N	N		0.0	0.0									
BMP4	09:19	N	N		0.0	0.0	N	N	59.8	71.6		N	N		
BMP4	12:21	N	N		0.0	0.0									
BMP4	15:53	N	N		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	16:23										N				
CMP2	16:25										N				
CMP3	16:26										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	08:49	Flow Meter (M^3):	000745 (starting)
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
11	ENE	7°	dry, light cloud	2	Dry	1026	Y but not in use.	N	None and NO			

Assessors Signature: J Hurst.

Proveco Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	06.04.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	JH
Daily Activity & Grid Ref.:	A1 + B7 + D1			General Notes:				PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR Detectability	ODOUR Intensity	ODOUR Quality	VOC Average PID Reading	VOC Peak PID Reading	DUST Visual	DUST Frisbee Sampled	NOISE Average Reading	NOISE Peak Reading	CANAL Visible impacts from Site Run-off	HOUSEKEEPING Litter	HOUSEKEEPING Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	09:00	N	N		0.0	0.0	N	N	65.0	76.2		N	N	* Dust has increased as site traffic increased Dust suppression measures needed	
BMP1	11:57	N	N		0.0	0.0									
BMP1	14:25	N	N		0.0	0.0									
BMP2	08:43	N	N		0.0	0.0	N	N	73.6	83.9		N	N	* No action taken	
BMP2	11:31	N	N		0.0	0.0									
BMP2	01:59	N	N		0.0	0.0									
BMP3	08:24	N	N		0.0	0.0	N	N	56.3	65.2		N	N	* Noise monitoring at Flats on Alan Turing way Results:- 65.4 average 77.7 Peak @ 15:56.	
BMP3	11:11	N	N		0.0	0.0									
BMP3	04:41	N	N		0.0	0.0									
BMP4	09:19	N	N		0.0	0.0	N	N	60.8	73.9		N	N		
BMP4	12:16	N	N		0.0	0.0									
BMP4	14:44	N	N		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:28										N				
CMP2	15:29										N				
CMP3	15:32										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time: 09:05	Flow Meter (M^3): 1745
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
11	NW	2	Sun dry cold	0	dry	1022	Not in use	N	N/A	

Assessors Signature: JHurst

Project Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	07.04.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	J.M.
Daily Activity & Grid Ref.:	A4					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08:19	N	N		0.0	0.0	N	N	68.4	76.7		N	N	* Very little Site activity this morning	
BMP1	10:51	N	N		0.0	0.0									
BMP1	14:29	N	N		0.0	0.0									
BMP2	07:55	N	N		0.0	0.0	N	N	69.9	78.5		N	N	* Dust has significantly increased for the afternoon * No Action taken.	
BMP2	10:33	N	N		0.0	0.0									
BMP2	14:09	N	N		0.0	0.0									
BMP3	07:43	N	N		0.0	0.0	N	N	55.7	69.2		N	N		
BMP3	10:16	N	N		0.0	0.0									
BMP3	13:50	N	N		0.0	0.0									
BMP4	08:40	N	N		0.0	0.0	N	N	56.6	67.9		N	N		
BMP4	11:12	N	N		0.0	0.0									
BMP4	14:58	N	N		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:39										N				
CMP2	15:40										N				
CMP3	15:42										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	08:22	Flow Meter (M^3):	745
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
8	NW	1	Sun, Clear, Cold, dry	0	Dry	1024	Not in operation	N	N/A.			

Assessors Signature: J Hurst

Project Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	05·04·21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	JM.
Daily Activity & Grid Ref.:						General Notes:		PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1 to)	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08:46	N	2		0·0	0·0	N	N	68·1	76·5		N	N	* As days has progressed dust has significantly increased to nuisance levels. * On site sprinkler system deployed but having very little impact.	
BMP1	12:31	N	2		0·0	0·0									
BMP1	15:43	N	2		0·0	0·0									
BMP2	08:29	N	2		0·0	0·0	N	N	69·8	77·6		N	N		
BMP2	12:09	N	2		0·0	0·0									
BMP2	15:16	N	2		0·0	0·0									
BMP3	08:10	N	2		0·0	0·0	N	N	60·5	71·3		N	N		
BMP3	11:51	N	2		0·0	0·0									
BMP3	[illegible]	N	2		0·0	0·0									
BMP4	09:09	N	2		0·0	0·0	N	N	62·2	71·7		N	N		
BMP4	12:53	N	2		0·0	0·0									
BMP4	16:00	N	2		0·0	0·0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	16:47										2				
CMP2	16:48										2				
CMP3	16:50										2				

ASS

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time: 08:50	Flow Meter (M³): 745.
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
8	SW	5°C	overcast dry mild	7	Slightly damp	1020	Not in operation	N	N/A	

Assessors Signature: JMurdoch

Provect[illegible]nvironmental Monitoring Form 101114

Site:	Project Bradford	Date:	09-04-21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	JM.
Daily Activity & Grid Ref.:	A1+2+3 ~~1&6~~ +B7					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	09:18	N	N		0.0	0.0	N	N	59.8	78.3		N	N	As day has progressed dust has increased to nuisance levels & Dust suppression not in operation:	
BMP1	12:24	N	N		0.0	0.0									
BMP1	16:17	N	N		0.0	0.0									
BMP2	09:00	N	N		0.0	0.0	N	N	72.5	81.8		N	N		
BMP2	12:29	N	N		0.0	0.0									
BMP2	15:56	N	N		0.0	0.0									
BMP3	06:43	N	N		0.0	0.0	N	N	63.8	74.5		N	N		
BMP3	2:11	N	N		0.0	0.0									
BMP3	15:40	N	N		0.0	0.0									
BMP4	09:47	N	N		0.0	0.0	N	N	59.7	70.6		N	N		
BMP4	13:09	N	N		0.0	0.0									
BMP4	16:35	N	N		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	16:55										N				
CMP2	16:56										N				
CMP3	16:58										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time: 09:20	Flow Meter (M³): 745
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
5	W	6	Dry, overcast	7	Dry	1018	Not in operation	N	N/A.	

Assessors Signature [signature]

Project: Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	12-04-21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	CN
Daily Activity & Grid Ref.:	D6					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	11:35	N	N		0.0	0.0	N	N	67.5	78.8		N	N		
BMP1	14:48	N	N		0.0	0.0									
BMP1	16:57	N	N		0.0	0.0									
BMP2	11:31	N	N		0.0	0.0	N	N	68.2	78.2		N	N		
BMP2	14:27	N	N		0.0	0.0									
BMP2	16:37	N	N		0.0	0.0									
BMP3	11:00	N	N		0.0	0.0	N	N	61.3	71.7		N	N		
BMP3	14:05	N	N		0.0	0.0									
BMP3	16:23	N	N		0.0	0.0									
BMP4	12:22	N	N		0.0	0.0	N	N	69.6	79.6		N	N		
BMP4	15:19	N	N		0.0	0.0									
BMP4	17:22	N	N		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	13:27										N				
CMP2	13:28										N				
CMP3	13:55										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	Leaks / Over-topping (Y/N)	Time: 9:40	Flow Meter (M^3): 745
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
1	W	4	Sunny	0	DRY	1028	Not in Operation	N	n/a	

Assessors Signature: CN

Project Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	13.04.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	CN
Daily Activity & Grid Ref.:	C7, D4					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	8:31	N	N		0.0	0.0	N	N	66.4	78.8		N	N	* DUST LEVELS INCREASED PM - DUST SUPRESSION ACTIONED.	
BMP1	14:50	N	N		0.0	0.0									
BMP1	16:24	N	N		0.0	0.0									
BMP2	7:35	N	N		0.0	0.0	N	N	75.6	82.7		N	N		
BMP2	14:02	N	N		0.0	0.0									
BMP2	15:39	N	N		0.0	0.0									
BMP3	7:37	N	N		0.0	0.0	N	N	63.5	74.2		N	N		
BMP3	13:16	N	N		0.0	0.0									
BMP3	13:42	N	N		0.0	0.0									
BMP4	8:57	N	N		0.0	0.0	N	N	76.8	84.1		N	N		
BMP4	15:06	N	N		0.0	0.0									
BMP4	16:45	N	N		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	13:07										N				
CMP2	13:08										N				
CMP3	13:10										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	8:10	Flow Meter (M^3):	745
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
4	NW	3	Partly Sunny	4	Dry	1032	not in operation	N	n/a			

Assessors Signature.....

Project Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	14.06.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	CN
Daily Activity & Grid Ref.:						General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
		(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	10.51	N	N		0.0	0.0	N	N	67.5	72.7		N	N	*Medium level dust AM - dust Supression actioned	
BMP1	12.57	N	N		0.0	0.0									
BMP1	15.02	N	N		0.0	0.0									
BMP2	10.30	N	N		0.0	0.0	N	N	71.9	77.6		N	N		
BMP2	12.34	N	N		0.0	0.0									
BMP2	15.38	N	N		0.0	0.0									
BMP3	10.09	N	N		0.0	0.0	N	N	62.1	72.3		N	N		
BMP3	12.12	N	N		0.0	0.0									
BMP3	15.22	N	N		0.0	0.0									
BMP4	11.18	N	N		0.0	0.0	N	N	76.2	83.1		N	N		
BMP4	13.20	N	N		0.0	0.0									
BMP4	15.19	N	N		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	14.07										N				
CMP2	14.08										N				
CMP3	14.11										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time: 09:50	Flow Meter (M^3): 765
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
5	NE	7	Partly Sunny	4	Dry	1034	Not in operation	N	N/a	

Assessors Signature

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	15.04.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	CN
Daily Activity & Grid Ref.:						General Notes:		PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08:17	N	N		0.0	0.0	N	N	72.7	78.3		N	N	*generator next to monitoring station	
BMP1	11:24	N	N		0.0	0.0									
BMP1	15:29				0.0	0.0									
BMP2	08:46	N	N		0.0	0.0	N	N	72.9	77.6		N	N		
BMP2	12:10	N	N		0.0	0.0									
BMP2	14:38	N	N		0.0	0.0									
BMP3	09:19	N	N		0.0	0.0	N	N	64.8	69.9		N	N		
BMP3	12:34	N	N		0.0	0.0									
BMP3	14:36	N	N		0.0	0.0									
BMP4	09:47	N	N		0.0	0.0	N	N	69.3	74.7		N	N		
BMP4	11:43	N	N		0.0	0.0									
BMP4	15:49														
EMP1														*dust levels high- dust suppression actioned across site.	
EMP2															
EMP3															
EMP4															
CMP1	14:26										N				
CMP2	14:26										N				
CMP3	14:26										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	12:37	Flow Meter (M^3):	745
Wind speed	Wind Directio	Temp	Weather description	Cloud cover	Ground conditions	Baromet ric	System Working .	Leaks / Over-topping	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
3	SE	8	Sunny / dry	1	Dry		Not in operation	N	N/a			

Assessors Signature.....

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	16.04.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	CN
Daily Activity & Grid Ref.:	DJ,					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:31	N	N		0.0	0.0	N	N	71.2	77.8		N	N		
BMP1	12:30	N	N		0.0	0.0									
BMP1	15:02	N	N		0.0	0.0									
BMP2	07:58	N	N		0.0	0.0	N	N	70.6	75.2		N	N		
BMP2	11:54	N	N		0.0	0.0									
BMP2	15:52	N	N		0.0	0.0									
BMP3	08:00	N	N		0.0	0.0	N	N	62.3	67.9		N	N		
BMP3	11:35	N	N		0.0	0.0									
BMP3	15:45	N	N		0.0	0.0									
BMP4	08:14	N	N		0.0	0.0	N	N	88.3	89.9		N	N	next to sheet piling.	
BMP4	12:57	N	N		0.0	0.0									
BMP4	15:21	N	N		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	16:55										N				
CMP2	16:36										N				
CMP3	16:39										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	07:30	Flow Meter (M^3):	765
Wind speed	Wind Directio	Temp	Weather description	Cloud cover	Ground conditions	Baromet ric	System Working	Leaks / Over-topping	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
2	SE	3	SUNNY	0	Dry	1032	Not in operation	N	N/a			

Assessors Signature: CN

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	19.04.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	CN
Daily Activity & Grid Ref.:	F7, E7, D6, C6					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08:21	N	N		0.0	0.0	N	N	67.7	74.8		N	N	*Little activity on site AM.	
BMP1	12:21	N	N		0.0	0.0									
BMP1	15:16	N	N		0.0	0.0									
BMP2	07:55	N	N		0.0	0.0	N	N	68.3	73.4		N	N	*High dust levels produced by vehicles movement - dust suppression actioned across site.	
BMP2	12:02	N	N		0.0	0.0									
BMP2	15:48	N	N		0.0	0.0									
BMP3	08:21	N	N		0.0	0.0	N	N	61.5	67.8		N	N		
BMP3	11:36	N	N		0.0	0.0									
BMP3	15:40	N	N		0.0	0.0									
BMP4	07:38	N	N		0.0	0.0	N	N	63.3	68.2		N	N		
BMP4	13:02	N	N		0.0	0.0									
BMP4	16:17	N	N		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	14:08										N				
CMP2	14:09										N				
CMP3	14:11										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	09:25	Flow Meter (M³):	745
Wind speed	Wind Directio	Temp	Weather description	Cloud cover	Ground conditions	Baromet ric	System Working	Leaks / Over-topping	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
4	SE	7	sunny, dry	0	dry	1023	Not in operation	N	n/a			

Assessors Signature

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	20.04.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	CN
Daily Activity & Grid Ref.:	D6, C6, B6					General Notes:		PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08:39	N	N		0.0	0.0	N	N	67.5	73.3		N	N		
BMP1	11:25	N	N		0.0	0.0									
BMP1	16:40	N	N		0.0	0.0									
BMP2	08:52	N	N		0.0	0.0	N	N	68.4	74.9		N	N		
BMP2	10:57	N	N		0.0	0.0									
BMP2	15:05	N	N		0.0	0.0									
BMP3	08:02	N	N		0.0	0.0	N	N	65.8	71.4		N	N		
BMP3	10:35	N	N		0.0	0.0									
BMP3	15:23	N	N		0.0	0.0									
BMP4	09:24	N	N		0.0	0.0	N	N	71.6	78.7		N	N		
BMP4	11:49	N	N		0.0	0.0									
BMP4	15:48	N	N		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1															
CMP2															
CMP3															

Meteorological and environmental conditions							WTP Inspection.		Time:	08:38	Flow Meter (M^3):	745
Wind speed	Wind Directio	Temp	Weather description	Cloud cover	Ground conditions	Baromet ric	System Working	Leaks / Over-topping	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar	not in operation	N	N/a			
2	SW	8	Sunny	4	Dry	1019						

Assessors Signature

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	21.04.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	CN
Daily Activity & Grid Ref.:	F2, [illegible], CJ, D5					General Notes:		PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	09:19	N			0.0	0.0	N	N	71.3	73.6		N	N		
BMP1	11:15	N			0.0	0.0									
BMP1	14:48	N			0.0	0.0									
BMP2	08:39	N			0.0	0.0	N	N	65.2	71.8		N	N		
BMP2	11:37	N			0.0	0.0									
BMP2	15:10	N			0.0	0.0									
BMP3	08:33	N			0.0	0.0	N	N	66.5	72.5		N	N		
BMP3	11:39	N			0.0	0.0									
BMP3	15:32	N			0.0	0.0									
BMP4	08:05	N			0.0	0.0	N	N	68.7	73.4		N	N		
BMP4	12:30	N			0.0	0.0									
BMP4	15:50	N			0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	10:48										[illegible]	N			
CMP2	10:48										[illegible]	N			
CMP3	10:50										[illegible]	N			

Meteorological and environmental conditions						
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar
7	E	9	Partly Sunny	5	Dry	1024

WTP Inspection.		Time:	08:45	Flow Meter (M^3):	761
System Working	Leaks / Over-topping	Equipment Impacted & Actions Taken to Rectify:			
Not in operation	N	n/a			

Assessors Signature: CN

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	22.04.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	CN
Daily Activity & Grid Ref.:	G6, G5, G4, G3, C5, D5					General Notes:		PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:35	N			0.0	0.0	N	N	67.7	73.4		N	N		* 5 dust Suppression water bowsers in use across site
BMP1	12:36	N			0.0	0.0									
BMP1	15:15	N			0.0	0.0									
BMP2	07:36	N			0.0	0.0	N	N	76.8	82.3		N	N	* Work on piling mat/ dozer + excavator.	
BMP2	13:00	N			0.0	0.0									
BMP2	15:27	N			0.0	0.0									
BMP3	08:20	N			0.0	0.0	N	N	72.7	79.2		N	N	* Kilo working next to monitoring station.	
BMP3	13:19	N			0.0	0.0									
BMP3	15:45	N			0.0	0.0									
BMP4	08:38	N			0.0	0.0	N	N	73.3	79.6		N	N	* near Shanska	
BMP4	13:41	N			0.0	0.0									
BMP4	16:07	N			0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	10:32										N				
CMP2	13:33										N				
CMP3	15:35										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	08:55	Flow Meter (M^3):	745
Wind speed	Wind Directio	Temp	Weather description	Cloud cover	Ground conditions	Baromet ric	System Working	Leaks / Over-topping	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
3	N	6	Sunny	0	Dry	1028	not in operation	N	n/a			

Assessors Signature.....

Site:	Project Bradford	Date:	23-04-21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	CN
Daily Activity & Grid Ref.:	F6, G5, G4, G3, C5, D5					General Notes:	Visual Dust: (1=Minimal, 2- Acceptable, 3= High)	PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(1-3)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:47	N			0.0	0.0	1	N	67.4	73.4		N	N		
BMP1	12:04	N			0.0	0.0									
BMP1	14:35	N			0.0	0.0									
BMP2	08:17	N			0.0	0.0	1	N	75.6	81.3		N	N	* work on piling mat	
BMP2	12:24	N			0.0	0.0									
BMP2	14:52	N			0.0	0.0									
BMP3	08:47	N			0.0	0.0	1	N	71.7	77.2		N	N	* Kilo works	
BMP3	12:43	N			0.0	0.0									
BMP3	15:36	N			0.0	0.0									
BMP4	09:20	N			0.0	0.0	1	N	72.6	77.9		N	N	* Shanska works.	
BMP4	13:08	N			0.0	0.0									
BMP4	15:32	N			0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	11:37										N				
CMP2	11:37										N				
CMP3	11:39										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	12:55	Flow Meter (M^3):	765
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric	System Working	Leaks / Over-topping	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
4	SE	14	Sunny	0	Dry	1029	not in operation	N	n/a			

Assessors Signature CN

Site:	Project Bradford	Date:	26.04.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	CN
Daily Activity & Grid Ref.:	C7 D7 G6 G5.					General Notes:	Visual Dust: (1=Minimal, 2- Acceptable, 3= High)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(1-3)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:22	N			0.0	0.0	1	N	66.7	72.3		N	N		
BMP1	11:16	N			0.0	0.0									
BMP1	13:49	N			0.0	0.0									
BMP2	07:38	N			0.0	0.0	1	N	71.7	79.6		N	N		
BMP2	10:56	N			0.0	0.0									
BMP2	13:27	N			0.0	0.0									
BMP3	08:15	N			0.0	0.0	1	N	68.8	75.6		N	N		
BMP3	10:38	N			0.0	0.0									
BMP3	13:11	N			0.0	0.0									
BMP4	07:42	N			0.0	0.0	1	N	64.2	69.9		N	N		
BMP4	11:34	N			0.0	0.0									
BMP4	14:12	N			0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	14:30										N				
CMP2	14:31										N				
CMP3	14:33										N				

Meteorological and environmental conditions							WTP Inspection.		Time: 09:27	Flow Meter (M^3): 793
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric	System Working	Leaks / Over-topping	Equipment Impacted & Actions Taken to Rectify:	
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar				
1	SE	5	Sunny	4	Dry	1025	Not in action	NO	N/A.	

Assessors Signature: J. Hurst

Site:	Project Bradford	Date:	27.04.21.	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	J. Hurst
Daily Activity & Grid Ref.:	G6 t					General Notes:	Visual Dust: (1=Minimal, 2- Acceptable, 3= High)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(1-3)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:51	N	N		0.0	0.0	N	N	65.3	73.5		N	N		
BMP1	10:59	N	N		0.0	0.0								*Ad hoc noise monitoring during piling works on Sports City Way outside residential complex	
BMP1	13:44	N	N		0.0	0.0								Average: 71.7	
BMP2	07:33	N	N		0.0	0.6	N	N	72.7	80.1		N	N	Maximum: 80.4	
BMP2	10:39	N	N		0.0	0.0									
BMP2	13:17	N	N		0.0	0.0									
BMP3	07:15	N	N		0.0	0.0	N	N	70.4	75.9		N	N		
BMP3	10:21	N	N		0.0	0.0									
BMP3	13:00	N	N		0.0	0.0									
BMP4	08:09	N	N		0.0	0.0	N	N	66.6	73.1		N	N		
BMP4	11:28	N	N		0.0	0.0									
BMP4	15:06	N	N		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4	15:47														
CMP1	15:49										N				
CMP2	15:50										N				
CMP3											N				

Meteorological and environmental conditions						
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar
4	WNW	9	Dry, overcast.	6	Dry	1011

WTP Inspection.		Time: 07:54	Flow Meter (M^3): 745
System Working	Leaks / Over-topping	Equipment Impacted & Actions Taken to Rectify:	
Not in action	N	N/A.	

Assessors Signature: J. Hurst.

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	28.04.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	J.M
Daily Activity & Grid Ref.:	E6 tF6 - C4tC5tC6 B1, S6, 7					General Notes:	Visual Dust: (1=Minimal, 2- Acceptable, 3= High)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(1-3)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08:29	N	N		0.0	0.0	N	N	69.1	75.2		N	N		
BMP1	11:40	N	N		0.0	0.0									
BMP1	15:43	N	N		0.0	0.0									
BMP2	08:50	N	N		0.0	0.0	N	N	71.4	78.0		N	N		
BMP2	11:21	N	N		0.0	0.0									
BMP2	15:19	N	N		0.0	0.0									
BMP3	07:45	N	N		0.0	0.0	N	N	68.2	77.3		N	N		
BMP3	11:03	N	N		0.0	0.0									
BMP3	15:00	N	N		0.0	0.0									
BMP4	08:05	N	N		0.0	0.0	N	N	71.9	78.5		N	N		
BMP4	12:00	N	N		0.0	0.0									
BMP4	16:06	N	N		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	09:22										N				
CMP2	09:23										N				
CMP3	09:25										N				

Meteorological and environmental conditions						
Wind speed	Wind Directio	Temp	Weather description	Cloud cover	Ground conditions	Barometric
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar
11	NE	7	Dry, mild, overcast	8.7	Damp	1010

WTP Inspection.		Time:	07:41	Flow Meter (M^3):	745
System Working	Leaks / Over-topping	Equipment Impacted & Actions Taken to Rectify:			
Not in action	N	N/A			

Assessors Signature: J. Hurst

Site:	Project Bradford	Date:	29.04.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	TH
Daily Activity & Grid Ref.:	C6+f6 C4+C5+ B+C5, 6+7.					General Notes:	Visual Dust: (1=Minimal, 2- Acceptable, 3= High)	PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(1-3)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08:00	N	N		0.0	0.0	N	N	64.9	73.8				*Noise monitoring on Sports City way @ western gate of site during piling works Time: 08:50 Average: 61.7 Maximum: 76.5.	
BMP1	11:27	N	N		0.0	0.0									
BMP1	13:31	N	N		0.0	0.0									
BMP2	08:18	N	N		0.0	0.0	N	N	70.1	78.6					
BMP2	11:04	N	N		0.0	0.0									
BMP2	13:45	N	N		0.0	0.0									
BMP3	07:24	N	N		0.0	0.0	N	N	67.6	74.1					
BMP3	10:50	N	N		0.0	0.0									
BMP3	14:16	N	N		0.0	0.0									
BMP4	07:43	N	N		0.0	0.0	N	N	70.2	79.5				*Dust Suppression in action.	
BMP4	11:50	N	N		0.0	0.0									
BMP4	14:37	N	N		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4	15:03														
CMP1	15:04														
CMP2	15:06														
CMP3															

Meteorological and environmental conditions						
Wind speed	Wind Directio	Temp	Weather description	Cloud cover	Ground conditions	Baromet ric
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar
5	N	5	sunny, dry	2	Dry	1013

WTP Inspection.		Time:	07:15	Flow Meter (M^3):	745
System Working	Leaks / Over-topping	Equipment Impacted & Actions Taken to Rectify:			
Not in action	NO	N/A			

Assessors Signature: J. Hurst.

Site:	Project Bradford	Date:	30·04·21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	JM.
Daily Activity & Grid Ref.:	E6+F6 +C4+C5+ B+C5,6+7.					General Notes:	Visual Dust: (1=Minimal, 2- Acceptable, 3= High)	PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(1-3)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:26	N	N		0·0	0·0	N	N	66·7	73·1		N	N		
BMP1	10:27	N	N		0·0	0·0									
BMP1	13:14	N	N		0·0	0·0									
BMP2	07:38	N	N		0·0	0·6	N	N	69·9	76·8		N	N		
BMP2	10:50	N	N		0·0	0·0									
BMP2	13:35	N	N		0·0	0·0									
BMP3	07:56	N	N		0·0	0·0	N	N	63·0	71·5		N	N		
BMP3	11:09	N	N		0·0	0·0									
BMP3	13:49	N	N		0·0	0·0									
BMP4	08:15	N	N		0·0	0·0	N	N	70·8	78·4		N	N.		
BMP4	11:30	N	N		0·0	0·0									
BMP4	14:07	N	N		0·0	0·0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	12:33										N				
CMP2	12:34										N				
CMP3	13:36										N				

Meteorological and environmental conditions						
Wind speed	Wind Directio	Temp	Weather description	Cloud cover	Ground conditions	Barometric
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar
4	NNE	5	sunny, dry	2	Dry	1017

WTP Inspection.		Time:	06·50	Flow Meter (M³):	745
System Working	Leaks / Over-topping	Equipment Impacted & Actions Taken to Rectify:			
Not in action	NO	N/A			

Assessors Signature J. Hurst.

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	04.05.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	T.H
Daily Activity & Grid Ref.:	FS + FG					General Notes:	Visual Dust: (1=Minimal, 2- Acceptable, 3= High)	PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(1-3)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:52	N	N		0.0	0.0	N	N	68.0	77.2		N	N		
BMP1	11:07	N	N		0.0	0.0									
BMP1	13:35	N	N		0.0	0.0									
BMP2	08:11	N	N		0.0	0.0	N	N	70.8	76.5		N	N		
BMP2	11:30	N	N		0.0	0.0									
BMP2	13:57	N	N		0.0	0.0									
BMP3	08:29	N	N		0.0	0.0	N	N	65.1	72.9		N	N		
BMP3	11:51	N	N		0.0	0.0									
BMP3	14:19	N	N		0.0	0.0									
BMP4	08:53	N	N		0.0	0.0	N	N	69.6	75.4		N	N		
BMP4	12:15	N	N		0.0	0.0									
BMP4	14:38	N	N		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	10:30										N				
CMP2	10:31										N				
CMP3	10:32										N				

Meteorological and environmental conditions							WTP Inspection.		Time: 07:50	Flow Meter (M^3): 745
Wind speed	Wind Directio	Temp	Weather description	Cloud cover	Ground conditions	Baromet ric	System Working	Leaks / Over-topping	Equipment Impacted & Actions Taken to Rectify:	
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar				
17.	WNW	6°	Overcast + Showers	8	Wet	993	Not in action.	NO	N/A.	

Assessors Signature J. Hurst.

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	05.05.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	JH
Daily Activity & Grid Ref.:	FS + E6 + E6 + ES.					General Notes:	Visual Dust: (1=Minimal, 2- Acceptable, 3= High)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(1-3)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	09:30	N	N		0.0	0.0	N	N	67.2	72.3		N	N		
BMP1	10:41	N	N		0.0	0.0									
BMP1	14:02	N	N		0.0	0.0									
BMP2	09:33	N	N		0.0	0.0	N	N	69.5	73.7		N	N		
BMP2	10:57	N	N		0.0	0.0									
BMP2	14:30	N	N		0.0	0.0									
BMP3	09:51	N	N		0.0	0.0	N	N	65.0	71.4		N	N		
BMP3	11:20	N	N		0.0	0.0									
BMP3	14:49	N	N		0.0	0.0									
BMP4	08:08	N	N		0.0	0.0	N	N	66.5	73.7		N	N		
BMP4	11:37	N	N		0.0	0.0									
BMP4	15:10	N	N		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:27										N				
CMP2	15:28										N				
CMP3	15:30										N				

Meteorological and environmental conditions							WTP Inspection.		Time: 07:28	Flow Meter (M^3): 745
Wind speed	Wind Directio	Temp	Weather description	Cloud cover	Ground conditions	Barometric	System Working	Leaks / Over-topping	Equipment Impacted & Actions Taken to Rectify:	
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar				
11	NW	5	Wet, fog.	8	wet	1008	Not in action	NO	N/A	

Assessors Signature J. Hurst.

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	06.05.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	JM
Daily Activity & Grid Ref.:	~~[illegible]~~ ES + DS.					General Notes:	Visual Dust: (1=Minimal, 2- Acceptable, 3= High)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(1-3)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:12	N	N		0.0	0.0	N	N	63.1	71.2		N	N	* Very little site activity this morning	
BMP1	10:37	N	N		0.0	0.0									
BMP1	14:19	N	N		0.0	0.0									
BMP2	07:30	N	N		0.0	0.0	N	N	67.7	76.1		N	N	* Emp1 is N Emp2 is E Emp3 is S Emp4 is W	
BMP2	10:55	N	N		0.0	0.0									
BMP2	14:39	N	N		0.0	0.0									
BMP3	07:47	N	N		0.0	0.0	N	N	60.3	72.7		N	N		
BMP3	11:19	N	N		0.0	0.0									
BMP3	15:00	N	N		0.0	0.0									
BMP4	08:09	N	N		0.0	0.0	N	N	65.8	76.4		N	N	* Emp - Little site activity to note. * Emp - Not stood close enough to soil processing area.	
BMP4	11:46	N	N		0.0	0.0									
BMP4	15:28	N	N		0.0	0.0									
EMP1	15:52	N	N		0.0	0.0	N		68.2	77.5		N	N		
EMP2	16:08	N	N		0.0	0.0	N		72.5	79.1		N	N		
EMP3	16:23	N	N		0.0	0.0	N		71.4	80.6		N	N		
EMP4	16:38	N	N		0.0	0.0	N		72.7	80.9		N	N		
CMP1	12:06										N				
CMP2	12:07										N				
CMP3	12:09										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	06:47	Flow Meter (M³):	745.
Wind speed	Wind Directio	Temp	Weather description	Cloud cover	Ground conditions	Barometric	System Working	Leaks / Over-topping	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
6	WSW	3	overcast, cold	6/7	Wet	1006	Not in action	NO	N/A			

Assessors Signature J. Hurst.

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	07-05-24	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	T.M
Daily Activity & Grid Ref.:	ES + DS.					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
700 BMP1	08:00	N	N		0.0	0.0	N	N	76.4	75.9		N	N	* Screener in operation	
BMP1	09:47	N	N		0.0	0.0									
BMP1	12:14	N	N		0.0	0.0									
BMP2	08:17	N	N		0.0	0.0	N	N	71.1	78.8		N	N	* Emp very busy site activity	
BMP2	10:05	N	N		0.0	0.0								* Screening operations, see Rams 008.	
BMP2	12:38	N	N		0.0	0.0									
BMP3	08:25	N	N		0.0	0.0	N	N	66.3	74.2		N	N		
BMP3	10:33	N	N		0.0	0.0									
BMP3	12:59	N	N		0.0	0.0									
BMP4	07:59	N	N		0.0	0.0	N	N	76.3	84.1		N	N		
BMP4	10:56	N	N		0.0	0.0									
BMP4	13:22	N	N		0.0	0.0									
EMP1	13:40	N	N		0.0	0.0	N		79.3	96.5		N	N		
EMP2	13:36	N	N		0.0	0.0	N		80.2	97.0		N	N		
EMP3	14:11	N	N		0.0	0.0	N		78.9	95.0		N	N		
EMP4	14:27	N	N		0.0	0.0	N		79.9	94.8		N	N		
704 CMP1	11:09										N				
CMP2	11:11										N				
CMP3	11:12										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	06:40	Flow Meter (M³):	745.
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
5	WSW	6	Sunny, light cloud.	2	damp/wet	1014	Not in action	N	N/A.			

Assessors Signature J. Hurst

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	10·05·21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	J·H
Daily Activity & Grid Ref.:	E6 + F6.					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
1000 BMP1	08:30	N	N		0·0	0·0	0	N	73·2	83·7		N	N		
BMP1	10:51	N	N		0·0	0·0									
BMP1	14:05	N	N		0·0	0·0									
BMP2	08:49	N	N		0·0	0·0	0	N	69·5	81·2		N	N		
BMP2	11:07	N	N		0·0	0·0									
BMP2	14:28	N	N		0·0	0·0									
BMP3	08:09	N	N		0·0	0·0	0	N	63·7	76·6		N	N		
BMP3	11:29	N	N		0·0	0·0									
BMP3	14:51	N	N		0·0	0·0									
BMP4	07:30	N	N		0·0	0·0	0	N	72·6	81·3		N	N		
BMP4	11:57	N	N		0·0	0·0									
BMP4	15:15	N	N		0·0	0·0									
EMP1														* Screener not in operation No environmental monitoring undertaken	
EMP2															
EMP3															
EMP4															
CMP1	08:35										N				
CMP2	08:39										N				
CMP3	08:40										N.				

Meteorological and environmental conditions							WTP Inspection.		Time:	08·35	Flow Meter (M³):	745
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
11	S	11	Sunny intervals	5	wet·	994	Not in action	NO	N/A			

Assessors Signature: J. Hurst

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	J.M 11:05:21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	J.M
Daily Activity & Grid Ref.:	FS + ES + DS					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08:28	Y	0		0.0	0.0	0	N	70.1	79.3		N	N		
BMP1	10:40	N	2		0.0	0.0									
BMP1	14:47	N	2		0.0	0.0									
BMP2	07:51	Y	0		0.0	0.0	0	N	67.5	77.7		N	N		
BMP2	10:57	N	2		0.0	0.0									
BMP2	14:35	N	2		0.0	0.0									
BMP3	08:09	Y	0		0.0	0.0	0	N	65.8	77.1		N	N		
BMP3	11:16	N	2		0.0	0.0									
BMP3	14:49	N	2		0.0	0.0									
BMP4	07:30	Y	0		0.0	0.0	0	N	56.7	68.3		N	N		
BMP4	11:43	N	2		0.0	0.0									
BMP4	15:17	N	2		0.0	0.0									
EMP1														* Screener not in use no environmental monitoring undertaken.	
EMP2															
EMP3															
EMP4															
CMP1	11:50										N				
CMP2	11:51										N				
CMP3	11:53										N				

Meteorological and environmental conditions						
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar
6	SSE	10	Sunny, No rain	0	Wet	1006

WTP Inspection.		Time:	07:30	Flow Meter (M^3):	745
System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
Not inaction	N	N/A.			

Assessors Signature J Gilbert.

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	12.05.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	T.H.
Daily Activity & Grid Ref.:	F6 + E6					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	Detectability (Y/N)	Intensity (1-5)	Quality (Description)	Average PID Reading (ppm)	Peak PID Reading (ppm)	Visual (0=none, 1- Minor, 3= Excessive) (0-4)	Frisbee Sampled Y/N	Average Reading (dBa)	Peak Reading (dBa)	Visible Impacts from Site Run-off Y/N	Litter (Y/N)	Posts (Y/N)	(Description)	(Description)
BMP1	08:50	N	N		0.0	0.0	N	N	72.6	80.8		N	N		
BMP1	10:13	N	N		0.0	0.0									
BMP1	13:51	N	N		0.0	0.0									
202 → BMP2	09:37	N	N		0.0	0.0	N	N	63.4	74.0		N	N	*Bmp2 is Bmp3 and vice versa (wrote in the wrong box)	
BMP2	10:35	N	N		0.0	0.0									
BMP2	14:21	N	N		0.0	0.0									
201 → BMP3	11:20	N	N		0.0	0.0	N	N	64.5	73.7		N	N		
BMP3	10:53	N	N		0.0	0.0									
BMP3	14:39	N	N		0.0	0.0									
200 → BMP4	07:01	N	N		0.0	0.0	N	N	58.9	70.2		N	N		
BMP4	10:18	N	N		0.0	0.0									
BMP4	15:00	N	N		0.0	0.0									
EMP1														*Screener not in operation	
EMP2															
EMP3															
EMP4															
CMP1	09:17										N				
CMP2	09:18										N				
CMP3	09:20										N				

Meteorological and environmental conditions						
Wind speed (mph)	Wind Direction (e.g. N, SW)	Temp (°C)	Weather description (e.g. rain, sun, wet, dry)	Cloud cover (0 to 8)	Ground conditions (e.g. wet, dry)	Barometric Pressure mbar
5	SSW	8	Overcast, mild	7.	wet	1006

WTP Inspection.		Time:	06:42	Flow Meter (M³):	745.
System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
Not in action	N	N/A.			

Assessors Signature: J Hurst

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	13.05.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	J.H
Daily Activity & Grid Ref.:	E1 F1 G4.						General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test: ✓

	Location: MP or Grid Ref.	Time	ODOUR Detectability	ODOUR Intensity	ODOUR Quality	VOC Average PID Reading	VOC Peak PID Reading	DUST Visual (0=none, 1- Minor, 3=	DUST Frisbee Sampled	NOISE Average Reading	NOISE Peak Reading	CANAL Visible Impacts from Site Run-off	HOUSEKEEPING Litter	HOUSEKEEPING Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
300	BMP1	06:45	N	N		0.0	0.0	0	N	68.5	79.7		N	N		
	BMP1	09:58	N	N		0.0	0.0									
	BMP1	12:45	N	N		0.0	0.0									
303	BMP2	07:41	N	N		0.0	0.0	0	N	70.3	81.1		N	N		
	BMP2	10:16	N	N		0.0	0.0									
	BMP2	13:03	N	N		0.0	0.0									
302	BMP3	07:24	N	N		0.0	0.0	0	N	68.8	69.5		N	N		
	BMP3	10:39	N	N		0.0	0.0									
	BMP3	13:23	N	N		0.0	0.0									
301	BMP4	07:05	N	N		0.0	0.0	0	N	54.7	64.8		N	N		
	BMP4	10:36	N	N		0.0	0.0									
	BMP4	13:48	N	N		0.0	0.0									
	EMP1															
	EMP2														* Screener not in operation	
	EMP3															
	EMP4															
	CMP1	14:00										N				
	CMP2	14:01										N				
	CMP3	14:03										N				

Meteorological and environmental conditions							WTP Inspection.		Time: 06:42	Flow Meter (M³): 745
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:	
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar				
5	NNE	8	Overcast, mild	7	wet.	1008	Not in action	N	N/A.	

Assessors Signature J.Hurst

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	14.05.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	T.M
Daily Activity & Grid Ref.:	F4 D4 E4					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

	Location: MP or Grid Ref.	Time	ODOUR Detectability	ODOUR Intensity	ODOUR Quality	VOC Average PID Reading	VOC Peak PID Reading	DUST Visual (0=none, 1- Minor, 3=	DUST Frisbee Sampled	NOISE Average Reading	NOISE Peak Reading	CANAL Visible Impacts from Site Run-off	HOUSEKEEPING Litter	HOUSEKEEPING Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
400	BMP1	06:51	N	N		0.0	0.0	0	N	64.9	76.8		N	N		
	BMP1	09:40	N	N		0.0	0.0			58.7						
	BMP1	13:33	N	N		0.0	0.0									
402	BMP2	07:24	N	N		0.0	0.0	0	N	64.2	69.1		N	N		
	BMP2	09:57	N	N		0.0	0.0									
	BMP2	13:55	N	N		0.0	0.0									
403	BMP3	07:48	N	N		0.0	0.0	0	N	72.5	81.9		N	N		
	BMP3	10:14	N	N		0.0	0.0									
	BMP3	14:12	N	N		0.0	0.0									
401	BMP4	07:10	N	N		0.0	0.0	0	N	59.4	71.3		N	N		
	BMP4	10:39	N	N		0.0	0.0									
	BMP4	14:37	N	N		0.0	0.0									
	EMP1														A Screener not in action	
	EMP2															
	EMP3															
	EMP4															
	CMP1	15:01										N				
	CMP2	15:02										N				
	CMP3	15:04										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	07:04	Flow Meter (M^3):	745
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
5	ENE	8°	Overcast mild	8	wet	1011	Not in action	N	N/A			

Assessors Signature: J. Hurst

Site:	Project Bradford	Date:	17.05.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	J. H.
Daily Activity & Grid Ref.:	D4 E4 F4					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	06:52	N	N		0.0	0.0	N	N	63.9	74.4		N	N	* Dust frisbee sampled Friday 14.05.21 afternoon	
BMP1	10:07	N	N		0.0	0.0									
BMP1	13:31	N	N		0.0	0.0									
BMP2	07:30	N	N		0.0	0.0	N	N	58.7	68.5		N	N		
BMP2	10:25	N	N		0.0	0.0									
BMP2	13:49	N	N		0.0	0.0									
BMP3	07:12	N	N		0.0	0.0	N	N	56.5	69.6		N	N		
BMP3	10:49	N	N		0.0	0.0									
BMP3	14:00	N	N		0.0	0.0									
BMP4	07:51	N	N		0.0	0.0	N	N	67.6	78.8		N	N		
BMP4	11:04	N	N		0.0	0.0									
BMP4	14:23	N	N		0.0	0.0									
EMP1														* Screener not in operation.	
EMP2															
EMP3															
EMP4															
CMP1	14:31										N				
CMP2	14:32										N				
CMP3	14:34										N.				

Meteorological and environmental conditions							WTP Inspection.		Time: 06.47	Flow Meter (M^3): 745
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:	
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar				
4	NW	10	Sunny Spells & Cloud	6.	Wet.	1004	Not in action	N	N/A	

Assessors Signature J Hurst.

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	18.05.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	J.M.
Daily Activity & Grid Ref.:	F4 + D4 + F4					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Posts		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:30	N	0		0.0	0.0	N	N	60.5	72.0		N	N	*No wagons loading this morning.	
BMP1	10:23	N	0		0.0	0.0									
BMP1	12:48	N	0		0.0	0.0									
BMP2	08:47	N	0		0.0	0.0	N	N	73.8	84.6		N	N		
BMP2	10:40	N	0		0.0	0.0									
BMP2	13:07	N	0		0.0	0.0									
BMP3	08:54	N	0		0.0	0.0	N	N	56.6	66.1		N	N		
BMP3	10:58	N	0		0.0	0.0									
BMP3	13:30	N	0		0.0	0.0									
BMP4	09:13	N	0		0.0	0.0	N	N	56.1	69.8		N	N		
BMP4	11:20	N	0		0.0	0.0									
BMP4	13:51	N	0		0.0	0.0									
EMP1														*Screener not in action.	
EMP2															
EMP3															
EMP4															
CMP1	11:25										N				
CMP2	11:26										N				
CMP3	11:27										N				

800

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time: 06:49	Flow Meter (M^3): 745
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
5	SW	9	Sunny spells, mild	6	wet	1011	Not in action	N	N/A.	

Assessors Signature: J. Hurst.

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	19.05.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	J.M.
Daily Activity & Grid Ref.:	D4 + E4 + F4					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08:00	N	0		0.0	0.0	0	N	71.3	82.4		0	0		
BMP1	10:46	N	0		0.0	0.0									
BMP1	13:41	N	0		0.0	0.0									
BMP2	07:23	N	0		0.0	0.0	0	N	63.0	74.7		0	0		
BMP2	11:02	N	0		0.0	0.0									
BMP2	13:59	N	0		0.0	0.0									
BMP3	07:10	N	0		0.0	0.0	0	N	64.8	77.2		0	0		
BMP3	11:20	N	0		0.0	0.0									
BMP3	14:18	N	0		0.0	0.0									
BMP4	07:43	N	0		0.0	0.0	0	N	64.8	77.4		0	0		
BMP4	11:39	N	0		0.0	0.0									
BMP4	14:40	N	0		0.0	0.0									
EMP1														*Screener not in operation	
EMP2															
EMP3															
EMP4															
CMP1	14:54										N				
CMP2	14:55										N				
CMP3	14:56										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	Leaks / Over-topping (Y/N)	Time: 07:05	Flow Meter (M^3): 745
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
5	WSW	10	Sunny spells & mild.	6	Wet	1017	Not in action	N	N/A	

Assessors Signature: J.Hurst.

Site:	Project Bradford	Date:	20.05.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	J.H
Daily Activity & Grid Ref.:	C4 + D4.					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	09:58	N	0		0.0	0.0	0	N	65.4	75.6		Y	N		
BMP1	10:36	Y	0		0.0	0.0		Y				Y	Y		
BMP1	15:12	Y	0		0.0	0.0		Y				Y	Y		
BMP2	09:03	Y	0		0.0	0.0	0	Y	61.6	73.3		Y	Y		
BMP2	10:51	Y	0		0.0	0.0		Y				Y	Y		
BMP2	15:29	Y	0		0.0	0.0		Y				Y	Y		
BMP3	09:20	Y	0		0.0	0.0	0	Y	68.6	75.7		Y	Y		
BMP3	11:06	Y	0		0.0	0.0		Y				Y	Y		
BMP3	15:46	Y	0		0.0	0.0		Y				Y	Y		
BMP4	09:39	Y	0		0.0	0.0	0	N	58.4	69.9		Y	N		
BMP4	11:21	Y	0		0.0	0.0									
BMP4	15:02	Y	0		0.0	0.0									
EMP1														* Screener not in action	
EMP2															
EMP3															
EMP4															
CMP1	13:10										Y				
CMP2	13:12										Y				
CMP3	13:13										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time: 06:50	Flow Meter (M^3): 745
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
8	SSE	8	overcast, mild	8	wet	1014	Not in action	N	N/A	

Assessors Signature: J. Hurst

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	21-05-21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	TH
Daily Activity & Grid Ref.:	E4 + D4					General Notes:	Visual Dust: (0=none, 1= Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08:50	N	0		0.0	0.0	0	N	71.2	82.3		N	N		
BMP1	10:58	N	0		0.0	0.0									
BMP1	13:51	N	0		0.0	0.0									
BMP2	09:55	N	0		0.0	0.0	0	N	70.6	81.8		N	N		
BMP2	11:16	N	0		0.0	0.0									
BMP2	14:09	N	0		0.0	0.0									
BMP3	07:18	N	0		0.0	0.0	0	N	63.3	73.5		N	N		
BMP3	11:33	N	0		0.0	0.0									
BMP3	14:21	N	0		0.0	0.0									
BMP4	07:02	N	0		0.0	0.0	0	N	61.4	73.1		N	N		
BMP4	11:50	N	0		0.0	0.0									
BMP4	14:47	N	0		0.0	0.0									
EMP1														*Screener not in action.	
EMP2															
EMP3															
EMP4															
CMP1	15:38										N				
CMP2	15:39										N				
CMP3	15:41										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	06:57	Flow Meter (M^3):	745
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
12	SSW	10°	Overcast, rain	8	Wet	985	Not in action.	N	N/A			

Assessors Signature: J. Hurst

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	24.05.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	J.M
Daily Activity & Grid Ref.:	E4 + F4.					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	06:58	N	0		0.0	0.0	0	N	59.1	70.8		N	N		
BMP1	09:46	N	0		0.0	0.0									
BMP1	12:49	N	0		0.0	0.0									
BMP2	07:34	N	0		0.0	0.0	0	N	69.9	81.7		N	N		
BMP2	10:03	N	0		0.0	0.0									
BMP2	13:10	N	0		0.0	0.0									
BMP3	07:15	N	0		0.0	0.0	0	N	63.2	74.8		N	N		
BMP3	10:21	N	0		0.0	0.0									
BMP3	13:28	N	0		0.0	0.0									
BMP4	07:56	N	0		0.0	0.0	0	N	72.4	83.1		N	N		
BMP4	10:40	N	0		0.0	0.0									
BMP4	13:56	N	0		0.0	0.0									
EMP1														* Screener not in use.	
EMP2															
EMP3															
EMP4															
CMP1	14:15										N				
CMP2	14:16										N				
CMP3	14:18										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	08:13	Flow Meter (M^3):	745
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
6	SSW	9	Sunny spells mild.	4	wet.	1000	Not in action	N	N/A			

Assessors Signature: J. Lunt.

Site:	Project Bradford	Date:	25-05-21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	JH
Daily Activity & Grid Ref.:						General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	09:40	N	0		0.0	0.0	0	N	68.3	78.4		N	N		
BMP1	10:56	N	0		0.0	0.0									
BMP1	13:01	N	0		0.0	0.0									
BMP2	09:23	N	0		0.0	0.0	0	N	67.9	79.5		N	N		
BMP2	11:17	N	0		0.0	0.0									
BMP2	13:22	N	0		0.0	0.0									
BMP3	08:15	N	0		0.0	0.0	0	N	70.2	80.7		N	N		
BMP3	11:39	N	0		0.0	0.0									
BMP3	13:40	N	0		0.0	0.0									
BMP4	07:58	N	0		0.0	0.0	0	N	68.4	81.5		N	N		
BMP4	11:54	N	0		0.0	0.0									
BMP4	13:59	N	0		0.0	0.0									
EMP1														* Screener Not in action.	
EMP2															
EMP3															
EMP4															
CMP1	15:26										N				
CMP2	15:27										N				
CMP3	15:29										N				

Meteorological and environmental conditions							WTP Inspection.		Time: 07:30	Flow Meter (M³): 745
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:	
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar				
11	WNW	9	Overcast rain.	8	wet.	1011	Not in action	N	N/A.	

Assessors Signature J. Hurst.

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	~~TH~~ 26.05.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	T.H
Daily Activity & Grid Ref.:	E4					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:58	N	0		0.0	0.0	0	N	66.6	77.2		N	N	*No wagons loading this morning	
BMP1	10:16	N	0		0.0	0.0									
BMP1															
BMP2	07:42	N	0		0.0	0.0	0	N	58.4	69.9		N	N		
BMP2	10:29	N	0		0.0	0.0									
BMP2															
BMP3	07:30	N	0		0.0	0.0	0	N	55.1	66.5		N	N		
BMP3	10:45	N	0		0.0	0.0									
BMP3															
BMP4	07:13	N	0		0.0	0.0	0	N	54.2	64.8		N	N		
BMP4	11:07	N	0		0.0	0.0									
BMP4															
EMP1															
EMP2															
EMP3															
EMP4	12:16													*Screener not in operation	
CMP1	12:17										N				
CMP2	12:19										N				
CMP3											N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time: 06:50	Flow Meter (M³): 745
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
6	NW	8	Overcast, mild & dry	8	wet	1014	Not in action	N	N/A	

Assessors Signature: J Hurst

Site:	Project Bradford	Date:	27·05·21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	J·H·
Daily Activity & Grid Ref.:	F4 + E4							General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)

PID Bump Test: ✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	09:09	N	0		0·0	0·0	0	N	63·4	74·1		N	N	& No wagons loading today·	
BMP1	10:52	N	0		0·0	0·0									
BMP1	14:06	N	0		0·0	0·0									
BMP2	09:30	N	0		0·0	0·0	0	0	63·5	73·4		N	N		
BMP2	11:09	N	0		0·0	0·0									
BMP2	14:23	N	0		0·0	0·0									
BMP3	09:36	N	0		0·0	0·0	0	N	58·7	70·2		N	N·		
BMP3	11:26	N	0		0·0	0·0									
BMP3	14:40	N	0		0·0	0·0									
BMP4	09:21	N	0		0·0	0·0	0	N	58·1	68·7		N	N		
BMP4	10:45	N	0		0·0	0·0									
BMP4	15:00	N	0		0·0	0·0									
EMP1														& Screener not in action	
EMP2															
EMP3															
EMP4															
CMP1	10:35										N				
CMP2	10:36										N				
CMP3	10:38										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	Leaks / Overtopping (Y/N)
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar		
6	NW	8	Overcast, mild	8	Wet·	1014	Not in action	N

Time: 08:20

Flow Meter (M³): 745·

Equipment Impacted & Actions Taken to Rectify:

N/A·

Assessors Signature: J Hurst

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	25·05·21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	JH
Daily Activity & Grid Ref.:	C7 + C6					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:16	N	0		0·0	0·0	0	N	69·2	79·6		N	N	*No loading in the morning	
BMP1	11:03	N	0		0·0	0·0									
BMP1	14:12	N	0		0·0	0·0									
BMP2	07:26	N	0		0·0	0·0	0	N	63·4	74·5		N	N		
BMP2	11:30	N	0		0·0	0·0									
BMP2	14:29	N	0		0·0	0·0									
BMP3	07:42	N	0		0·0	0·0	0	N	61·6	72·0		N	N		
BMP3	11:47	N	0		0·0	0·0									
BMP3	14:50	N	0		0·0	0·0									
BMP4	07:59	N	0		0·0	0·0	0	N	71·8	83·7		N	N		
BMP4	12:03	N	0		0·0	0·0									
BMP4	15:10	N	0		0·0	0·0									
EMP1														*Screener not in action	
EMP2															
EMP3															
EMP4															
CMP1	10:31										N				
CMP2	10:32										N				
CMP3	10:33										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar
3	SW	12	Overcast mild	8	Wet	1023

WTP Inspection. Time: 07:05 — Flow Meter (M³): 745

System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:
Not in action	N	N/A -

Assessors Signature: J. Hurst.

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	01.06.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	J.M
Daily Activity & Grid Ref.:	E4 + D4.						General Notes:	Visual Dust: (0=none, 1= Some, 3= Excessive, 4= Unreasonable)	PID Bump Test: ✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	Detectability (Y/N)	Intensity (1-5)	Quality (Description)	Average PID Reading (ppm)	Peak PID Reading (ppm)	Visual (0=none, 1= Minor, 3=	Triaxo Sampled Y/N	Average Reading (dBa)	Peak Reading (dBa)	Visible Impacts from Site Run-off Y/N	Litter (Y/N)	Pests (Y/N)	(Description)	(Description)
BMP1	06:16	0	N		0.0	0.0	0	N	72.2	83.1		N	N	Ivanska Cement trucks Generating lots of dust whilst driving on the eastern side of Site.	
BMP1	10:23	0	N		0.0	0.0									
BMP1	13:41	0	N		0.0	0.0									
BMP2	07:33	0	N		0.0	0.0	0	N	66.0	78.8		N	N		
BMP2	10:49	0	N		0.0	0.0									
BMP2	13:57	0	N		0.0	0.0									
BMP3	07:16	0	N		0.0	0.0	0	N	66.4	79.2		N	N		
BMP3	11:09	0	N		0.0	0.0									
BMP5	14:20	0	N		0.0	0.0									
BMP4	07:38	0	N		0.0	0.0	6	N	70.2	81.9		N	N		
BMP4	11:25	0	N		0.0	0.0									
BMP4	14:41	0	N		0.0	0.0									
EMP1														* Screener not in action.	
EMP2															
EMP3															
EMP4															
CMP1	16:49										N				
CMP2	15:50										N				
CMP3	15:9										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time: 06:53	Flow Meter (M^3): 745
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Inspected & Actions Taken to Rectify:	
5	E	15	Clear skies warm	0	Dry	1017	Not in action	N	N/A	

Assessors Signature: J. Hurst

Prevoctus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	02·06·21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	T·H
Daily Activity & Grid Ref.:	F, E, D 4						General Notes:	Visual Dust: (0=none, 1= Some, 3= Excessive, 4= Unreasonable)	PID Bump Test: ✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1= Minor, 3=	Probes Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08:07	0	N		0·0	0·0	0	N	65·5	75·8		N	N	* 14 wagons on turn around this morning	
BMP1	11:13	0	N		0·0	0·0									
BMP1	14:31	0	N		0·0	0·0									
BMP2	09:50	0	N		0·0	0·0	0	N	61·2	72·7		N	N		
BMP2	11:36	0	N		0·0	0·0									
BMP2	14:58	0	N		0·0	0·0									
BMP3	09:33	0	N		0·0	0·0	0	N	56·0	66·5		N	N		
BMP3	11:48	0	N		0·0	0·0									
BMP3	15:15	0	N		0·0	0·0									
BMP4	09:12	0	N		0·0	0·0	0	N	64·5	71·9		N	N		
BMP4	12:09	0	N		0·0	0·0									
BMP4	15:30	0	N		0·0	0·0									
EMP1														* Screener not in action	
EMP2															
EMP3															
EMP4															
CMP1	0936										N				
CMP2	1657										N				
CMP3	1536										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Overtopping (Y/N)	Time: 08:12	Flow Meter (M³): 745
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
8	ENE	15°C	Clear skies, warm	0	Dry	1014	Not in action	N	N/A·	

Assessors Signature: J·Hurst·

Proveetus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	03-06-21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	T H
Daily Activity & Grid Ref.:	F4, E4, D4. Pile matt installation					General Notes:	Visual Dust (0=none, 1= Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1= Minor, 3= Excessive)	Frisbee Sampler	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Posts		
		(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08:14	0	0		0.0	0.0	0	N	71.6	83.5		N	N		
BMP1	10:51	0	0		0.0	0.0									
BMP1	14:20	0	0		0.0	0.0									
BMP2	09:50	0	0		0.0	0.0	0	N	66.8	79.3		N	N		
BMP2	11:06	0	0		0.0	0.0									
BMP2	14:37	0	0		0.0	0.0									
BMP3	09:38	0	0		0.0	0.0	0	N	63.6	73.1		N	N		
BMP3	11:24	0	0		0.0	0.0									
BMP3	14:35	0	0		0.0	0.0									
BMP4	09:22	0	0		0.0	0.0	0	N	62.4	73.6		N	N		
BMP4	11:53	0	0		0.0	0.0									
BMP4	15:15	0	0		0.0	0.0									
EMP1														* Screener not in action.	
EMP2															
EMP3															
EMP4															
CMP1	10:04										N				
CMP2	10:05										N				
CMP3	10:06										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP inspection. System Working	WTP inspection. Leaks / Overtopping	Time:	745	Flow Meter (M^3):	~~08:15~~
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:			
S	E	15	Overcast, warm	8	Dry	1016	Not in action	N	N/A			

Assessors Signature ✓

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	04-06-21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	J.H
Daily Activity & Grid Ref.:	F9 E9 D 4 t5 (Pile mats) D3 + F3					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:58	N	0		0·0	0·0	0	N	73·5	84·1		0	N	* No wagons loading today	
BMP1	10:21	N	0		0·0	0·0								* No excavation today	
BMP1	14:09	N	0		0·0	0·0								* Installation of pile mats in F9 E+ D9 4+5	
BMP2	07:40	N	0		0·0	0·0	0	N	64·9	75·7		0	N		
BMP2	10:57	N	0		0·0	0·0									
BMP2	14:27	N	0		0·0	0·0									
BMP3	07:22	N	0		0·0	0·0	0	N	65·1	66·9		0	N	* Dust being generated on eastern side of site by Dumpers (Carey's)	
BMP3	10:46	N	0		0·0	0·0									
BMP3	14:45	N	0		0·0	0·0									
BMP4	7:06	N	0		0·0	0·0	0	N	56·1	67·2		0	N	* Ram Construction in afternoon	
BMP4	11:20	N	0		0·0	0·0								* Screener not in action	
BMP4	15:04	N	0		0·0	0·0									
EMP1															
EMP2															
EMP3															
EMP4	6:53														
CMP1	15:54										N				
CMP2	15:55										N				
CMP5											N				

Meteorological and environmental conditions

Wind speed	Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time: 05:25	Flow Meter (M³): 07·45
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
3	NSW	10	Sunny dry	1	Dry	1023	Not in action	N	N/A	

Assessors Signature: J. Hurst

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	07·06·21·	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	J. H.

Daily Activity & Grid Ref.: E2 (Screener) F3 (ramp).

General Notes: Visual Dust: (0=none, 1= Some, 3= Excessive, 4= Unreasonable)

PID Bump Test: ✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0 = none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Posts		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	09:50	0	0		0·0	0·0	0	N	68·3	80·4		N	N	* wagon loading pfa arisings.	
BMP1	10:41	0	2		0·0	0·0									
BMP1	14:09	2	0		0·0	0·0									
BMP2	09:33	0	0		0·0	0·0	0	N	62·6	75·4		N	N	* CBR testing on LLPM Bowl	
BMP2	10:57	0	0		0·0	0·0									
BMP2	14:23	2	0		0·0	0·0									
BMP3	09:16	0	0		0·0	0·0	0	N	58·4	69·2		N	N	* Dust Generation on eastern side of Site by Caeys dumpers	
BMP3	11:58	0	2		0·0	0·0									
BMP3	14:40	2	0		0·0	0·0									
BMP4	09:00	0	0		0·0	0·0	0	N	55·7	67·3		N	N		
BMP4	11:36	0	2		0·0	0·0								* Crane brake down Slipped a track.	
BMP4	14:57	0	0		0·0	0·0									
EMP1	12:59	2	0		0·0	0·0	0		83·1	95·6		N	N	* lots of activity during	
EMP2	12:15	2	0		0·0	0·0	0		81·5	94·0		N	N	Screening, cement wagons	
EMP3	12:30	2	0		0·0	0·0	0		79·3	92·3		N	N	road sweeper, excavators	
EMP4	13:46	2	0						72·8	87·2		N	N	and caeys dumpers	
CMP1	15:39										N				
CMP2	15:40										N				
CMP3	15:42										N				

NESW

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time: 08:08	Flow Meter (M³): 745
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
3		15	Sunny with Clouds dry	2·	dry	1023	Not in action	N	N/A	

Assessors Signature: J. Hurst

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	08.06.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	T.H.
Daily Activity & Grid Ref.:	E2 + (E3 + F3) - Ramp					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	09:48	N	0		0.0	0.0	0	N	67.4	79.8		N	N	* Wagons loading at farm	
BMP1	10:57	N	0		0.0	0.0								* Dust Suppression in	
BMP1	13:43	N	0		0.0	0.0								operation @ 08:00am	
BMP2	09:35	N	0		0.0	0.0	0	N	66.7	72.4		N	N		
BMP2	11:15	N	0		0.0	0.0									
BMP2	13:59	N	0		0.0	0.0									
BMP3	09:16	N	0		0.0	0.0	0	N	58.3	65.9		N	N		
BMP3	11:32	N	0		0.0	0.0									
BMP3	14:16	N	0		0.0	0.0									
BMP4	09:00	N	0		0.0	0.0	0	N	60.6	71.7		N	N		
BMP4	11:47	N	0		0.0	0.0									
BMP4	14:35	N	0		0.0	0.0									
EMP1	09:46	N	0		0.0	0.0	0		83.7	97.6		N	N	* lots of site activity	
EMP2	10:01	N	0		0.0	0.0	0		74.0	95.8		N	N	Next to / During Screener	
EMP3	10:17	N	0		0.0	0.0	0		83.2	94.4		N	N	Caterpillumpers, cement	
EMP4	10:32	N	0		0.0	0.0	0		74.7	87.8		N	N	wagons, road sweeper	
CMP1	15:49										N			and loading also piling	
CMP2	15:56										N			works	
CMP3	15:9										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	08:20	Flow Meter (M^3):	745
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
4		13	Sunny with clouds Dry	2	Dry	1023	Not in action	N	N/A			

Assessors Signature: J Hurst

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	09.06.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	T.H.
Daily Activity & Grid Ref.:	E3+F3 (Ramp) E2 (dig).					General Notes:	Visual Dust (0=none, 1= Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1= Minor, 3= Frisbee Sampled		Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	10:45	N	0		0.0	0.0	0	N	72.1	83.4		N	N	* loading just before 7:00am	
BMP1	11:09	N	0		0.0	0.0									
BMP1	13:52	N	0		0.0	0.6								* Dust Supression	
BMP2	07:28	N	0		0.0	0.0	0	N	64.6	77.1		N	N	measures @ 07:15am	
BMP2	11:26	N	0		0.0	0.0								* BMP 3 Dust magital	
BMP2	14:09	N	0		0.0	0.0								brought forward closer	
BMP3	09:12	N	0		0.0	0.0	0	N	55.5	67.1		N	N	to pedestrian walkway	
BMP3	11:38	N	0		0.0	0.0								in A7 out of piers	
BMP3	14:26	N	0		0.0	0.0								pathway.	
BMP4	08:56	N	0		0.0	0.0	0	N	51.2	62.3		N	N		
BMP4	11:34	N	0		0.0	0.0									
BMP4	14:44	N	0		0.0	0.0									
EMP1	12:41	N	0		0.0	0.0	0		87.9	98.1		N	N	* Screener in dip surrounded	
EMP2	12:56	N	0		0.0	0.0	0		73.2	85.4		N	N	by bunding on 3 Sides	
EMP3	13:11	N	0		0.0	0.0	0		75.1	88.3		N	N		
EMP4	13:28	N	0		0.0	0.0	0		72.5	83.2		N	N		
CMP1	15:49										N				
CMP2	15:50										N				
CMP3	15:51										N				

NESW

Meteorological and environmental conditions							WTP Inspection.		Time:	08:10	Flow Meter (M^3):	745
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
6	S	17	Sunny dry	0	DRY	1020	Not in action	N	N/A			

Assessors Signature: J. Hurst

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	10·06·21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	JH
Daily Activity & Grid Ref.:	E1 + E2					General Notes:	Visual Dust: (0=none, 1= Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1= Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Posts		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	09:43	N	0		0·0	0·0	0	N	65·8	81·0		N	N	* Wagons loading before	
BMP1	10:38	N	0		0·0	0·0								7am leaving gate @ 7am	
BMP1	13:15	N	0		0·0	0·0									
BMP2	09:23	N	0		0·0	0·0	0	N	64·9	76·7		N	N		
BMP2	10:55	N	0		0·0	0·0									
BMP2	13:32	N	0		0·0	0·0									
BMP3	09:11	N	0		0·0	0·0	0	N	52·7	66·2		N	N		
BMP3	11:13	N	0		0·0	0·0									
BMP3	13:49	N	0		0·0	0·0									
BMP4	06:56	N	0		0·0	0·0	0	N	54·3	67·1		N	N		
BMP4	11:30	N	0		0·0	0·0									
BMP4	14:06	N	0		0·0	0·0									
EMP1	08:00	N	0		0·0	0·0	0		75·9	90·6		N	N		
EMP2	08:15	N	0		0·0	0·0	0		78·5	87·4		N	N		
EMP3	08:30	N	0		0·0	0·0	0		76·1	88·3		N	N		
EMP4	08:47	N	0		0·0	0·0	0		74·3	86·9		N	N		
CMP1	16:20										N				
CMP2	16:22										N				
CMP3	16:23										N				

2222

Meteorological and environmental conditions							WTP Inspection.		Time:	07:51	Flow Meter (M³):	6745
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Tanks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
7	SW	17	overcast, dry, warm	8	Dry	1019	Not in action	N	N/A			

Assessors Signature: J. Hurst

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	11.06.21	Contract Ref:	101114	Client:	RAM Construction Ltd	Assessor name:	J.H
Daily Activity & Grid Ref.:	E1 + F1 + F2					General Notes:	Visual Dust: (0=none, 1= Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1= Minor, 3= Moderate)	Frisbee Sampled	Average Reading	Peak Reading	Visible impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	09:51	N	0		0.0	0.0	0	N	69.5	81.1		N	N	* loading before 7am	
BMP1	10:51	N	0		0.0	0.0								left gate @ 7am Hust	
BMP1	13:14	N	0		0.0	0.0								and Ron Haz.	
BMP2	09:25	N	0		0.0	0.0	0	N	60.8	73.9		N	N	* Dust frizbees Samples	
BMP2	11:08	N	0		0.0	0.0								@ 08:30am Not on Hust	
BMP2	15:33	N	0		0.0	0.0								round of Monitoring checks.	
BMP3	09:09	N	0		0.0	0.0	0	N	57.2	68.3		N	N		
BMP3	11:25	N	0		0.0	0.0									
BMP3	15:30	N	0		0.0	0.0									
BMP4	06:35	N	0		0.0	0.0	0	N	52.4	63.3		N	N		
BMP4	11:42	N	0		0.0	0.0									
BMP4	14:06	N	0		0.0	0.0									
EMP1	06:41	N	0		0.0	0.0	0		79.1	92.4		N	N	* lots of activity around	
EMP2	08:53	N	0		0.0	0.0	0		75.4	88.0		N	N	Screener, cement wagons	
EMP3	06:43	N	0		0.0	0.0	0		83.8	98.3		N	N	Caleys tippers, road sweeper.	
EMP4	07:04	N	0		0.0	0.0	0		74.0	91.9		N	N		
CMP1	6:52										N				
CMP2	8:33										N				
CMP3	5:36										N				

N S E W

Meteorological and environmental conditions							WTP Inspection		Time:	08:09	Flow Meter (M³):	745
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Overtopping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar	Not in action	N	N/A			
10'	SW	16	Overcast, dry	8	Dry	1016						

Assessors Signature: J Hurst.

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	14·06·21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	TH
Daily Activity & Grid Ref.:	F1 + F2						General Notes:	Visual Dust: (0=none, 1= Some, 3= Excessive, 4= Unreasonable)	PID Bump Test: ✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1= Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
		(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	09:46	N	0		0·0	0·0	0	N	71·5	83·8		N	N	* Skanska Cement lorries generating dust on eastern side of Site	
BMP1	10:25	N	0		0·0	6·0									
BMP1	13:39	N	0		0·0	0·0									
BMP2	01:29	N	0		0·0	0·0	0	N	62·5	75·8		N	N		
BMP2	10:41	N	0		0·0	0·0									
BMP2	13:55	N	0		0·0	0·0									
BMP3	09:13	N	0		0·0	0·0	0	N	55·2	68·3		N	N		
BMP3	10:58	N	0		0·0	0·0									
BMP3	14:12	N	0		0·0	0·0									
BMP4	06:57	N	0		0·0	0·0	0	N	55·4	66·9		N	N		
BMP4	11:15	N	0		0·0	0·0									
BMP4	14:29	N	0		0·0	0·0									
EMP1														* Screener not in action	
EMP2															
EMP3															
EMP4															
CMP1	16:10										N				
CMP2	16:11										N				
CMP3	16:13										N				

Meteorological and environmental conditions							WTP Inspection.		Time: 08:00	Flow Meter (M^3): 745
Wind speed (mph)	Wind Direction (e.g. N, SW)	Temp (°C)	Weather description (e.g. rain, sun, wet, dry)	Cloud cover (0 to 8)	Ground conditions (e.g. wet, dry)	Barometric Pressure mbar	System Working (Y/N)	Leaks / Overtopping (Y/N)	Equipment Impacted & Actions Taken to Rectify:	
7·	N	17	Overcast, dry	8	Dry	1020	Not in action	N	N/A·	

Assessors Signature J. Hurst·

Provectus Environmental Monitoring Form 101114 T6

Site:	Project Bradford	Date:	15·06·21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	J.M.
Daily Activity & Grid Ref.:	E1 dig E3 Drainage.					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR: Detectability	ODOUR: Intensity	ODOUR: Quality	VOC: Average PID Reading	VOC: Peak PID Reading	DUST: Visual (0=none, 1- Minor, 3=	DUST: Frisbee Sampled	NOISE: Average Reading	NOISE: Peak Reading	CANAL: Visible Impacts from Site Run-off	HOUSEKEEPING: Litter	HOUSEKEEPING: Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08:02	N	0		0.0	0.0	0	N	70.4	83.2		N	N	* Hydrocarbon odour noticed during excavation @ E1, od not PID	
BMP1	10:52	N	0		0.0	0.0									
BMP1	13:39	N	0		0.0	0.0									
BMP2	07:45	N	0		0.0	0.0	0	N	69.8	80.9		N	N	monitoring undertaken. Results @ 0ppm @ 08:52 → 09:07	
BMP2	11:09	N	0		0.0	0.0									
BMP2	13:53	N	0		0.0	0.0									
BMP3	07:29	N	0		0.0	0.0	0	N	63.4	75.8		N	N		
BMP3	11:25	N	0		0.0	0.0									
BMP3	13:17	N	0		0.0	0.0									
BMP4	07:13	N	0		0.0	0.6	0	N	67.7	79.2		N	N	* Shanska Cement wagon and covers dumpers generating lots of dust on Ramps	
BMP4	11:45	N	0		0.0	0.0									
BMP4	13:36	N	0		0.0	0.0									
EMP1														* Screener not in action	
EMP2															
EMP5															
EMP4															
CMP1	08:39										N				
CMP2	08:40										N				
CMP3	08:42										N				

Meteorological and environmental conditions							WTP Inspection		Time:	08:20	Flow Meter (M³):	745
Wind speed (mph)	Wind Direction (e.g. N, SW)	Temp (°C)	Weather description (e.g. rain, sun, wet, dry)	Cloud cover (0 to 8)	Ground conditions (e.g. wet, dry)	Barometric (mbar)	System Working (Y/N)	Leaks / Overtopping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
3	SE	12	overcast, sunny spells	6	Dry	1023	Not in action	N	N/A			

Assessors Signature: J. Hurst

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	16.06.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	JH
Daily Activity & Grid Ref.:	E1+E2+F1						General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test: ✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3= Excessive)	Fribbee Sampler	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
		(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	10:59	N	0		0.0	0.0	0	N	63.8	77.9		N	N	*Loading before 7am out the gate at 7am	
BMP1	11:06	N	0		0.0	0.0									
BMP1	15:27	N	0		0.0	0.0								*Dust generated by Shunting and Careful on top of HL pile mats and Ramps	
BMP2	09:24	N	0		0.0	0.0	0	N	62.1	75.5		N	N		
BMP2	11:25	N	0		0.0	0.0									
BMP2	14:45	N	0		0.0	0.0									
BMP3	09:25	N	0		0	N	0.0	0.0	53.8	65.7		N	N	*DTS and Type 1 imports	
BMP3	11:40	N	0		0.0	0.0									
BMP3	15:01	N	0		0.0	0.0									
BMP4	09:09	N	0		0	N	0.0	0.0	62.6	73.3		N	N		
BMP4	11:46	N	0		0.0	0.0									
BMP4	15:15	N	0		0.0	0.0									
EMP1														*Screener not in action	
EMP2															
EMP3															
EMP4															
CMP1	09:04										N				
CMP2	09:05										N				
CMP3	09:07										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Overtopping (Y/N)	Time: 08:31	Flow Meter (M^3): 745
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
6	SSW	19	Sunny, dry	1	dry	1012	Not in action	N	N/A	

Assessors Signature J. Hurst

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	17·06·21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	TH
Daily Activity & Grid Ref.:	f1+E1 + E2 (Pile mat & installation)			General Notes:	Visual Dust: (0=none, 1= Some, 3= Excessive, 4= Unreasonable)			PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		ACCESS		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1= Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08:03	N	0		0·0	0·0	0	N	69·5	82·8		N	N	*Wagons loading @ 7:05am.	
BMP1	11:37	N	0		0·0	6·0									
BMP1	14:21	N	0		0·0	0·0									
BMP2	09:44	N	0		0·0	0·0	0	N	66·9	70·3		N	N	*Shansha and Carap generating dust upon East and Western ramps.	
BMP2	11:55	N	0		0·0	0·0									
BMP2	14:37	N	0		0·0	0·0									
BMP3	07:28	N	0		0·0	0·0	0	N	66·7	69·1		N	N		
BMP3	12:10	N	0		0·0	0·0									
BMP3	15:56	N	0		0·0	0·0									
BMP4	07:17	N	0		0·0	0·0	0	N	52·6	64·8		N	N	* Dust Suppression in action @ eastern ramp on Site.	
BMP4	12:26	N	0		0·0	0·0									
BMP4	14:14	N	0		0·0	0·0									
EMP1														* Screener not in action	
EMP2															
EMP3															
EMP4															
CMP1	12:35										N				
CMP2	12:36										N				
CMP3	12:37										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	06:57	Flow Meter (M³):	745·
Wind speed	Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
5·	NW	15	Overcast, dry	8	dry	1010	Not in action	N	N/A			

Assessors Signature: T. Hurst

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	15.06.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	T.M
Daily Activity & Grid Ref.:	G1 + F1 Pilenat and ramp.					General Notes:	Visual Dust: (0=none, 1= Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1= Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:53	N	0		0.0	0.0	0	N	71.7	83.2		N	0	* No wagons loading this morning.	
BMP1	09:48	N	0		0.0	0.0									
BMP1	12:51	N	0		0.0	0.0									
BMP2	07:34	N	0		0.0	0.0	0	N	62.5	74.1		N	0	* 1 load 75mm delivered.	
BMP2	10:20	N	0		0.0	0.0									
BMP2	13:09	N	0		0.0	0.0								* WSJ Bowzer dampening down Eastern and Western ramps	
BMP3	07:18	N	0		0.0	0.0	0	N	60.6	72.9		N	0		
BMP3	10:16	N	0		0.0	0.0									
BMP3	15:23	N	0		0.0	0.0									
BMP4	07:22	N	0		0.0	0.0	0	N	58.5	64.8		N	N		
BMP4	10:34	N	0		0.0	0.0									
BMP4	13:27	N	0		0.0	0.0									
EMP1														* Screener not in action	
EMP2															
EMP3															
EMP4															
CMP1	09:25										N				
CMP2	09:26										N				
CMP3	09:27										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Tanks Overtopping (Y/N)	Time: 06:55	Flow Meter (M³): 745
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
6.	N	14.	Sunny, light cloud dry.	2	Dry.	1018	Not in action	N	N/A.	

Assessors Signature: T. Must.

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	21.06.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	CN
Daily Activity & Grid Ref.:						General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08:43	N	0		0.0	0.0	0	N	64.3	72.4		N	N	*Some dust generated by wagons at the exit gate.	
BMP1	12:19	N	0		0.0	0.0									
BMP1	15:34	N	0		0.0	0.0									
BMP2	09:01	N	0		0.0	0.0	0	N	67.7	74.1		N	N		
BMP2	12:56	N	0		0.0	0.0									
BMP2	15:51	N	0		0.0	0.0									
BMP3	09:17	N	0		0.0	0.0	0	N	66.2	71.5		N	N	*Low activity across site.	
BMP3	12:58	N	0		0.0	0.0									
BMP3	16:09	N	0		0.0	0.0									
BMP4	09:36	N	0		0.0	0.0	0	N	57.2	64.8		N	N	* Piling on high level mat ended along grids	
BMP4	13:10	N	0		0.0	0.0									
BMP4	16:27	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	16:38										N				
CMP2	16:34										N				
CMP3	16:41										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time: 10:20	Flow Meter (M^3): 745
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
7	NE	14	OVERCAST, DRY	7	DRY		NOT IN ACTION	N	n/a	

Assessors Signature: CN

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	22.06.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	BW
Daily Activity & Grid Ref.:						General Notes:	Visual Dust: (0=none, 1= Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1= Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Posts		
		(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:13	Y	0		0.0	0.0	0	Y	60.8	73.4		Y	0		
BMP1	12:00	Y	0		0.0	0.0									
BMP1	15:09	Y	0		0.0	0.0									
BMP2	07:30	Y	0		0.0	0.0	0	Y	60.2	68.6		Y	0		
BMP2	12:17	Y	0		0.0	0.0								visible activity	
BMP2	15:26	Y	0		0.0	0.0								across site.	
BMP3	07:47	Y	0		0.0	0.0	0	Y	62.2	75.5		Y	0		
BMP3	12:38	Y	0		0.0	0.0									
BMP3	15:48	Y	0		0.0	0.0									
BMP4	08:03	Y	0		0.0	0.0	0	Y	58.5	70.4		Y	0		
BMP4	12:52	Y	0												
BMP4	16:00	Y	0												
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	16:20										Y				
CMP2	16:14										Y				
CMP3	16:13										Y				

Meteorological and environmental conditions							WTP inspection.		Time:	09:15	Flow Meter (M^3):	745
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						

Assessors Signature: BWallace

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	23.06.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	
Daily Activity & Grid Ref.:	A2						General Notes:	Visual Dust: (0=none, 1= Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1= Minor, 3=	Frisbee Sampler	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:05	Y	0		0.0	0.0	0	N	61.2	70.3		N	N		
BMP1	11:40	Y	0		0.0	0.0								"Cores & waggons moving stone creating dust on exit ramp infront of cabin	
BMP1	14:50	Y	0		0.0	0.0									
BMP2	07:11	Y	0		0.0	0.0	0	N	60.4	69.7		N	N		
BMP2	11:57	Y	0		0.0	0.0									
BMP2	15:57	Y	0		0.0	0.0									
BMP3	07:39	Y	0		0.0	0.0	0	N	63.1	75.3		N	N		
BMP3	12:14	Y	0		0.0	0.0									
BMP3	15:25	Y	0		0.0	0.0									
BMP4	07:58	Y	0		0.0	0.0	0	N	61.1	72.5		N	N		
BMP4	12:31	Y	0		0.0	0.0									
BMP4	15:42	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1											Y				
CMP2											Y				
CMP3											Y				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	Leaks / Overtopping (Y/N)	Time: 08:00	Flow Meter (M^3): 745
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	

Assessors Signature: [signature]

Prevectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	24.06.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	
Daily Activity & Grid Ref.:	A2 + A3					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampler	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Posts	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:00	Y	0		0.0	0.0	0	Y	65.6	70.2		Y	Y		
BMP1	11:08	Y	0		0.0	0.0									
BMP1	14:25	Y	0		0.0	0.0									
BMP2	07:17	Y	0		0.0	0.0	0	Y	64.8	71.5		Y	Y		
BMP2	11:25	Y	0		0.0	0.0									
BMP2	14:40	Y	0		0.0	0.0									
BMP3	07:34	Y	0		0.0	0.0	0	Y	67.1	75.9		Y	Y		
BMP3	12:02	Y	0		0.0	0.0									
BMP3	14:58	Y	0		0.0	0.0									
BMP4	07:51	Y	0		0.0	0.0	0	Y	63.5	69.4		Y	Y		
BMP4	12:55	Y	0		0.0	0.0									
BMP4	15:15	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:50										Y				
CMP2	15:51										Y				
CMP3	15:52										Y				

Meteorological and environmental conditions							WTP Inspection.		Time:	08:30	Flow Meter (M³):	745
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
9	E	18	Overcast, misty, very sweltering	7	dry		Y	Y				

Assessors Signature.....

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	25.06.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	
Daily Activity & Grid Ref.:	A2 + A3					General Notes:	Visual Dust: (0=none, 1= Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1= Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:05	Y	0		0.0	0.0	0	N	56.2	60.1		N	N		
BMP1	12:00	Y	0		0.0	0.0									
BMP1	15:15	Y	0		0.0	0.0									
BMP2	07:21	Y	0		0.0	0.0	0	N	63.9	70.5		N	N		
BMP2	12:17	Y	0		0.0	0.0									
BMP2	15:30	Y	0		0.0	0.0									
BMP3	07:59	Y	0		0.0	0.0	0	N	59.4	64.5		N	N		
BMP3	12:34	Y	0		0.0	0.0									
BMP3	15:49	Y	0		0.0	0.0									
BMP4	07:42	Y	0		0.0	0.0	0	N	61.3	67.3		N	N		
BMP4	12:51	Y	0		0.0	0.0									
BMP4	16:06	Y	0		0.0	0.0									
EMP1		[redacted]													
EMP2															
EMP3															
EMP4															
CMP1											Y				
CMP2											Y				
CMP3											Y				

Meteorological and environmental conditions							WTP Inspection		Time:	08:30	Flow Meter (M^3):	795
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
13	SW	13	WET + OVERCAST	7	WET		Y	N				

Assessors Signature.....

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	28.06.21.	Contract Ref:	101114	Client:	RAM Construction Ltd	Assessor name:	T.H.
Daily Activity & Grid Ref.:	A1+A2+A3					General Notes:	Visual Dust: (0=none, 1= Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1= Minor, 3=	Fribbee Sampled	Average Reading	Peak Reading	Visible impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:49	N	0		0.0	0.0	0	N	66.6	79.8		N	N		
BMP1	11:23	N	0		0.0	0.0									
BMP1	14:16	N	0		0.0	0.0									
BMP2	07:32	N	0		0.0	0.0	0	N	60.6	75.7		N	N		
BMP2	11:40	N	0		0.0	0.0									
BMP2	14:33	N	0		0.0	0.0									
BMP3	08:15	N	0		0.0	0.0	0	N	56.2	67.9		N	N		
BMP3	11:57	N	0		0.0	0.0									
BMP3	14:49	N	0		0.0	0.0									
BMP4	08:58	N	0		0.0	0.0	0	N	56.9	70.0		N	N		
BMP4	12:14	N	0		0.0	0.0									
BMP4	15:07	N	0		0.0	0.0									
EMP1														*Screener not in action	
EMP2															
EMP3															
EMP4															
CMP1	16:25										N				
CMP2	13:26										N				
CMP3	16:27										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	08:15	Flow Meter (M^3):	745.
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
6.	ENE	15	light cloud, dry	6	Dry		Not in acti	N.	N/A.			

Assessors Signature: J. Hurst.

Prevectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	29.06.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	J.M.
Daily Activity & Grid Ref.:	A1 + A2 + A3					General Notes:	Visual Dust: (0=none, 1= Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	/

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1= Minor, 3=	Frisbee Sampler	Average Reading	Peak Reading	Visible impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08:34	N	0		0.0	0.0	0	N	71.4	84.7		N	N	*UBU Bowser in action.	
BMP1	10:50	N	0		0.0	0.0									
BMP1	14:38	N	0		0.0	0.0									
BMP2	08:17	N	0		0.0	0.0	0	N	69.4	83.8		N	N		
BMP2	10:06	N	0		0.0	0.0									
BMP2	14:55	N	0		0.0	0.0									
BMP3	08:01	N	0		0.0	0.0	0	N	70.5	84.2		N	N		
BMP3	11:23	N	0		0.0	0.0									
BMP3	15:12	N	0		0.0	0.0									
BMP4	08:44	N	0		0.0	0.0	0	N	68.7	80.9		N	N		
BMP4	11:40	N	0.		0.0	0.0									
BMP4	14:30	N	0		0.0	0.0									
EMP1														*Screener not in action	
EMP2															
EMP3															
EMP4															
CMP1	09:18										N				
CMP2	09:19										N				
CMP3	09:21										N				

Meteorological and environmental conditions							WTP Inspection		Time:	08:45.	Flow Meter (M^3):	745
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
6.	NE	16	light cloud dry.	6	damp.	1017	Not in action	N	N/A.			

Assessors Signature J. Hurst.

Prevectas Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	30·06·21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	T·H·
Daily Activity & Grid Ref.:	A1 + A2 + A3						General Notes:	Visual Dust: (0=none, 1= Some, 3= Excessive, 4= Unreasonable)	PID Bump Test: ✓

Location: NP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1= Minor, 3= Excessive)	Fribbee Sampled	Average Reading	Peak Reading	Visible Imparts from Site Run-off	Litter	Pests		
		(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08:30	N	0		0·0	0·0	0	N	71·4	84·7		N	N		
BMP1	10:58	N	0		0·0	0·0									
BMP1	13:45	N	0		0·0	0·0									
BMP2	08:03	N	0		0·0	0·0	0	N	69·4	83·8		N	N		
BMP2	11:15	N	0		0·0	0·0									
BMP2	13:59	N	0		0·0	0·0									
BMP3	08:51	N	0		0·0	0·0	0	N	70·5	84·2		N	N		
BMP3	11:32	N	0		0·0	0·0									
BMP3	14:16	N	0		0·0	0·0									
BMP4	08:34	N	0		0·0	0·0	0	N	60·7	80·9		N	N		
BMP4	11:49	N	0		0·0	0·0									
BMP4	14:34	N	0		0·0	0·0									
EMP1														* Screener not in action.	
EMP2															
EMP3															
EMP4															
CMP1	1004										N				
CMP2	1005										N				
CMP3	1007										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar
6	NNE	16	Overcast, dry·	7	Dry	1017

WTP Inspection.

System Working (Y/N)	Leaks / Over-topping (Y/N)
Not in action	N

Time: 08:52 Flow Meter (M³): 745

Equipment Inspected & Actions Taken to Rectify:

N/A

Assessors Signature J·Hurst·

Proyectus Environmental Monitoring Form 101114 EH

Site:	Project Bradford	Date:	08/08/21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	J.M.
Daily Activity & Grid Ref.:	B3					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
		(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBA)	(dBA)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	06:59	Y	2		0.0	0.0	0	N	63.9	77.1		N	N	* Dust suppression	
BMP1	9:21	Y	2		0.0	0.0								Dislectus in action	
BMP1	13:21	Y	2		0.0	0.0								in afternoon	
BMP2	07:16	Y	2		0.0	0.0	0	N	61.0	74.8		N	N		
BMP2	10:06	Y	2		0.0	0.0									
BMP2	13:45	Y	2		0.0	0.0									
BMP3	07:51	Y	2		0.0	0.0	0	N	63.4	75.9		N	N		
BMP3	10:35	Y	2		0.0	0.0									
BMP3	14:02	Y	2		0.0	0.0									
BMP4	07:47	Y	2		0.0	0.0	0	N	63.9	74.6		N	N		
BMP4	10:53	N	0		0.0	0.0									
BMP4	14:19	N	0		0.0	0.0									
EMP1														* screener not in action	
EMP2															
EMP3															
EMP4															
CMP1	15:45										Y				
CMP2	15:46										Y				
CMP3	15:47										Y				

Meteorological and environmental conditions							WTP Inspection.		Time:	08:15	Flow Meter (M³):	745
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
3	NNW	16	Overcast dry	7	Dry	1019	Not in action	N	N/A			

Assessors Signature J. Hurst

Provectus Environmental Monitoring Form 181114 TH

Site:	Project Bradford	Date:	02-07-21	Contract Ref:	181114	Client:	BAM Construction Ltd	Assessor name:	TH
Daily Activity & Grid Ref.:	A4 + A3					General Notes:	Visual Dust: (0=none, 1= Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR: Detectability	ODOUR: Intensity	ODOUR: Quality	VOC: Average PID Reading	VOC: Peak PID Reading	DUST: Visual (0=none, 1= Minor, 3=	DUST: Frisbee Sampled	NOISE: Average Reading	NOISE: Peak Reading	CANAL: Visible impacts from Site Run-off	HOUSEKEEPING: Litter	HOUSEKEEPING: Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08:01	N	0		0.0	0.0	0	N	63.9	75.1		N	N	* UBM Bowser in action @ 07:50.	
BMP1	10:49	N	0		0.0	0.0									
BMP1	13:52	N	0		0.0	0.0									
BMP2	07:44	N	0		0.0	0.0	0	N	71.9	84.2		N	N		
BMP2	11:05	N	0		0.0	0.0									
BMP2	14:06	N	0		0.0	0.0									
BMP3	09:27	N	0		0.0	0.0	0	N	60.4	73.2		N	N		
BMP3	11:27	N	0		0.0	0.0									
BMP3	14:25	N	0		0.0	0.0									
BMP4	07:11	N	0		0.0	0.0	0	N	62.2	75.8		N	N		
BMP4	11:44	N	0		0.0	0.0									
BMP4	14:42	N	0		0.0	0.0									
EMP1														* Screener not in action	
EMP2															
EMP3															
EMP4															
CMP1	15:08										N				
CMP2	15:09										N				
CMP3	15:10										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	08:20	Flow Meter (M³):	745.
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
2	ENE	15	Overcast, dry	8	Dry.	1017	Not in action	N	N/A.			

Preventex Environmental Monitoring Form 181114 TH

Site:	Project Bradford	Date:	08-07-21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	C.N
Daily Activity & Grid Ref.:	A5, M6, E1					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	09:03	N	0		0.0	0.0	0	N	75.1	81.2		N	N	* roadsweeper nearby clearing debris on road. * Shoreline piling.	
BMP1	11:23	N	0		0.0	0.0									
BMP1	14:58	N	0		0.0	0.0									
BMP2	09:16	N	0		0.0	0.0	0	N	78.7	83.9		N	N		
BMP2	11:49	N	0		0.0	0.0									
BMP2	15:18	N	0		0.0	0.0									
BMP3	09:46	N	0		0.0	0.0	0	N	77.3	81.6		N	N		
BMP3	12:00	N	0		0.0	0.0									
BMP3	15:37	N	0		0.0	0.0									
BMP4	10:13	N	0		0.0	0.0	0	N	67.5	73.8		N	N		
BMP4	12:17	N	0		0.0	0.0									
BMP4	15:57	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:03										✓				
CMP2	15:04										✓				
CMP3	15:05										✓				

Meteorological and environmental conditions							WTP Inspection.		Time:		Flow Meter (M³):	745
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric	System Working (Y/N)	Liquid Overtopping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar	not in operation	N	n/a			
3	W	17	partly Cloudy, dry	4	Wet							

Assessors Signature: [signature]

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	07.07.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	C.N
Daily Activity & Grid Ref.:	A5, A6						General Notes:	Visual Dust: (0= none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test: ✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3+	Frisbee Sampled	Average Reading	Peak Reading	Visible impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07.26	N	0		0	0	0	N	62.6	73.8		N	N		
BMP1	12.42	N	0		0	0.1									
BMP1	14.46	N	0		0	0									
BMP2	07.45	N	0		0	0	0	N	72.7	78.2		N	N		
BMP2	12.54	N	0		0	0									
BMP2	15.18	N	0		0	0									
BMP3	08.04	N	0		0	0	0	N	69.6	75.1		N	N		
BMP3	13.22	N	0		0	0									
BMP3	15.14	N	0		0	0									
BMP4	08.22	N	0		0	0	0	N	67.2	74.6		N	N		
BMP4	15.43	N	0		0	0									
BMP4	16.33	N	0		0	0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15.58										N				
CMP2	15.54										N				
CMP3	16.01										N				

Meteorological and environmental conditions								WTP Inspection		Time:	08:30	Flow Meter (M³):	745
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure		System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar							
5	SW	16	cloudy, heavy rain	8	flooded			not in operation	N	n/a			

Assessors Signature: [signature]

Provectus Environmental Monitoring Form 181114 TH

Site:	Project Bradford	Date:	06.07.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	BG
Daily Activity & Grid Ref.:	A4, A5					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1= Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:01	Y	0		0.0	0.0	0	N	65.6	74.1		N	N		
BMP1	11:44	Y	0		0.0	0.0									
BMP1	14:52	Y	0		0.0	0.0									
BMP2	07:18	Y	0		0.0	0.0	0	N	61.4	70.3		N	N		
BMP2	11:02	Y	0		0.0	0.0									
BMP2	15:09	Y	0		0.0	0.0									
BMP3	07:56	Y	0		0.0	0.0	0	N	62.5	66.5		N	N		
BMP3	12:09	Y	0		0.0	0.0									
BMP3	15:26	Y	0		0.0	0.0									
BMP4	07:58	Y	0		0.0	0.0	0	N	60.7	69.2		N	N		
BMP4	12:36	Y	0		0.0	0.0									
BMP4	15:43	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:11										Y				
CMP2	15:19										Y				
CMP3	15:35										Y				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over topping (Y/N)	Time: 09:50	Flow Meter (M^3): 745
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
5	SW	24	Sun	2	Dry	1015	Y	Y	N/A	

Assessors Signature: [signature]

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	5-07-21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	T.H
Daily Activity & Grid Ref.:	P4					General Notes:	Visual Dust: (0=none, 1= Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1= Minor, 3+	Frisbee Sampled	Average Reading	Peak Reading	Visible inspects from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08:14	0	0		0.0	0.0	0	N	70.7	83.0		N	N	* Wagons loading	
BMP1	10:30	N	0		0.0	0.0								* Jet wash at Eastern	
BMP1	13:15	N	0		0.0	0.0								gate.	
BMP2	09:37	N	0		0.0	0.0	0	N	65.8	80.3		N	N		
BMP2	10:46	N	0		0.0	0.0									
BMP2	13:29	N	0		0.0	0.0									
BMP3	09:40	N	0		0.0	0.0	0	N	68.5	79.5		N	N		
BMP3	11:05	N	0		0.0	0.0									
BMP3	13:48	N	0		0.0	0.0									
BMP4	09:24	N	0		0.0	0.0	0	N	68.1	76.8		N	N		
BMP4	11:20	N	0		0.0	0.0									
BMP4	14:05	N	0		0.0	0.0									
EMP1														* Screener not in	
EMP2														action.	
EMP3															
EMP4															
CMP1	13:39										N				
CMP2	10:30										N				
CMP3	10:01										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time: 08:39	Flow Meter (M³): 745
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
7	SW	15	Overcast, wet	8	Wet	1003	Not in action	N	N/A	

Assessors Signature J. Hurst.

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	04.07.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	A5					General Notes:	Visual Dust: (0=none, 1= Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1= Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Imports from Site Run-off	Litter	Peels		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08:40	Y	2	0	0.0	0.0	0	Y	56.1	60.3		N	N		
BMP1	11:12	Y	2	0	0.0	0.0									
BMP1	15:34	Y	2	0	0.0	0.0									
BMP2	08:58	Y	2	0	0.0	0.0	0	Y	61.9	67.6		N	N		
BMP2	11:30	Y	2	0	0.0	0.0									
BMP2	15:12	Y	2	0	0.0	0.0									
BMP3	08:18	Y	2	0	0.0	0.0	0	Y	67.8	71.2		N	N		
BMP3	11:46	Y	2	0	0.0	0.0									
BMP3	15:44	Y	2	0	0.0	0.0									
BMP4	08:31	Y	2	0	0.0	0.0	0	Y	63.3	78.2		N	N		
BMP4	12:07	Y	2	0	0.0	0.0									
BMP4	16:26	Y	2	0	0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:09										Y				
CMP2	15:10										Y				
CMP3	15:12										Y				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time: 08:35	Flow Meter (M³): 745
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
2	S	16	Partly cloudy, dry.	3	Dry	1024	not in operation	n	n/a	

Assessors Signature: C.N

Prevention Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	15.07.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	CN
Daily Activity & Grid Ref.:	A7, A6, C7					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:24	N	0		0.0	0.0	0	N	67.8	72.3		N	N		
BMP1	12:11	N	0		0.0	0.0									
BMP1	16:58	N	0		0.0	0.0									
BMP2	12:25	N	0		0.0	0.0	0	N	71.6	78.9		N	N		
BMP2	09:45	N	0		0.0	0.0	[illegible]								
BMP2	16:51	N	0		0.0	0.0									
BMP3	08:05	N	0		0.0	0.0	0	N	62.1	66.7		N	N	Dust levels risen throughout day due to vehicle movement in + out of gate.	
BMP3	12:58	N	0		0.0	0.0									
BMP3	17:01	N	0		0.0	0.0									
BMP4	08:43	N	0		0.0	0.0	0	N	58.2	61.6		N	N		
BMP4	13:09	N	0		0.0	0.0									
BMP4	17:28	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	16:02										N				
CMP2	16:05										N				
CMP3	16:03										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time: 07:25	Flow Meter (M^3): 745
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
6	NE	16	Dry / Partly Sunny	4	Dry	1024	not in operation	N	N/a	

Assessors Signature: [signature]

Provectus Environmental Monitoring Form 181114 TH

Site:	Project Bradford	Date:	14.07.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	C.N
Daily Activity & Grid Ref.:	A6,					General Notes:	Visual Dust: (0=none, 1= Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR: Detectability	ODOUR: Intensity	ODOUR: Quality	VOC: Average PID Reading	VOC: Peak PID Reading	DUST: Visual (0=none, 1= Minor, 3=	DUST: Frisbee Sampled	NOISE: Average Reading	NOISE: Peak Reading	CANAL: Visible Impacts from Site Run-off	HOUSEKEEPING: Litter	HOUSEKEEPING: Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:17	N	0		0.0	0.0	0	N	65.2	73.7		N	N		
BMP1	11:10	N	0		0.0	0.0									
BMP1	14:47	N	0		0.0	0.0									
BMP2	07:35	N	0		0.0	0.0	0	N	76.1	79.5		N	N		
BMP2	11:[illegible]	N	0		0.0	0.0									
BMP2	15:03	N	0		0.0	0.0									
BMP3	07:50	N	0		0.0	0.0	0	N	57.4	62.2		N	N		
BMP3	11:[illegible]	N	0		0.0	0.0									
BMP3	15:24	N	0		0.0	0.0									
BMP4	08:12	N	0		0.0	0.0	0	N	58.2	61.7		N	N		
BMP4	12:05	N	0		0.0	0.0									
BMP4	15:13	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	16:27										N				
CMP2	16:33										N				
CMP3	16:28										N				

Meteorological and environmental conditions							WTP Inspection:		Time:	07:15	Flow Meter (M³):	765
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
8	NW	13	Partly Sunny/Dry	3	Dry	1028	Not in operation	N	n/a			

Assessors Signature: [signature]

Proactive Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	13.07.23	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C N
Daily Activity & Grid Ref.:	A5+A6					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	09:38	N	0		0.0	0.0	0	N	67.7	74.8		N	N		
BMP1	12:14	N	0		0.0	0.0									
BMP1	14:45	N	0		0.0	0.0									
BMP2	09:52	N	0		0.0	0.0	0	N	73.2	81.6		N	N		
BMP2	12:31	N	0		0.0	0.0									
BMP2	15:04	N	0		0.0	0.0									
BMP3	08:51	N	0		0.0	0.0	0	N	56.2	60.7		N	N		
BMP3	12:52	N	0		0.0	0.0									
BMP3	15:26	N	0		0.0	0.0									
BMP4	08:45	N	0		0.0	0.0	0	N	57.8	60.9		N	N		
BMP4	13:08	N	0		0.0	0.0									
BMP4	15:43	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	16:05										N				
CMP2	16:04										N				
CMP3	16:04										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection: System Working (Y/N)	WTP Inspection: Leaks / Overtopping (Y/N)	Time: 07:10	Flow Meter (M³): 765
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
8	N	15	Partly sunny	5	Dry/ Wet in places	1019	not in operation	N	n/a	

Assessors Signature: CN

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	12·07·21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	J·M
Daily Activity & Grid Ref.:	AS + A6					General Notes:	Visual Dust: (0= none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1–5)	(Description)	(ppm)	(ppm)	(0–4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	09:56	Y	2		0·0	0·0	0	N	66·8	79·2		N	0	* No wagons on site @ 7am	
BMP1	09:25	Y	2		0·0	0·0									
BMP1	12:48	Y	2		0·0	0·0									
BMP2	07:36	Y	2		0·0	0·0	0	N	59·8	71·7		N	0	* Road Sweeper in action @ 7am	
BMP2	09:42	Y	2		0·0	0·0									
BMP2	13:05	Y	2		0·0	0·0									
BMP3	07:20	Y	2		0·0	0·0	0	N	55·5	68·8		N	0	* little site activity this morning	
BMP3	09:58	Y	2		0·0	0·0									
BMP3	13:22	Y	2		0·0	0·0									
BMP4	07:04	N	2		0·0	6·0	0	0	53·1	65·6		N	0		
BMP4	10:15	N	2		0·0	0·0									
BMP4	13:39	N	2		0·0	0·0									
EMP1														* Screener not in action	
EMP2															
EMP3															
EMP4															
CMP1	15:40										N				
CMP2	15:47										N				
CMP3	15:44										N				

Meteorological and environmental conditions							WTP Inspection.		Time: 09:00	Flow Meter (M^3): 745
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:	
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar				
2	NE	15	Overcast mild	8	WET	1011	Not in action	N	N/A	

Assessors Signature: J. Hurst

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	16.07.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	BG
Daily Activity (& Grid Ref.):	A7					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1= Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Peels		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:19	2	0		0.0	0.0	0	2	65.7	69.3		2	2		
BMP1	12:06	2	0		0.0	0.0									
BMP1	16:45	2	0		0.0	0.0									
BMP2	07:27	2	0		0.0	0.0	0	2	70.4	76.9		2	2		
BMP2	12:17	2	0		0.0	0.0									
BMP2	15:03	2	0		0.0	0.0									
BMP3	07:49	2	0		0.0	0.0	0	2	61.5	64.7		2	2		
BMP3	12:54	2	0		0.0	0.0									
BMP3	15:36	2	0		0.0	0.0									
BMP4	08:02	2	0		0.0	0.0	0	2	60.8	66.2		2	2		
BMP4	12:52	2	0		0.0	0.0									
BMP4	15:57	2	0		0.0	0.0									
EMP1														Dust levels increased through the day as temp increased and plant / vehicle movements increased.	
EMP2															
EMP3															
EMP4															
CMP1	13:12										2				
CMP2	15:13										2				
CMP3	15:14										2				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time: 08:30	Flow Meter (M^3): 745
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
3	2	13	Sun	3	dry		2	2		

Assessors Signature: [signature]

Preventive Environmental Monitoring Form 101114 Tbl

Site:	Project Bradford	Date:	22.07.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	EW
Daily Activity & Grid Ref.:	D6, E6, F6, F1					General Notes:	Visual Dust: (0=none, 1= Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1= Minor, 3= Excessive, 4= Unreasonable)	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:00	Y	0		0.0	0.0	0	N	70.9	75.6		N	N		
BMP1	12:03	Y	0		0.0	0.0									
BMP1	15:10	Y	0		0.0	0.0									
BMP2	07:17	Y	0		0.0	0.0	0	N	68.3	73.7		N	N		
BMP2	12:26	Y	0		0.0	0.0									
BMP2	15:27	Y	0		0.0	0.0									
BMP3	07:34	Y	0		0.0	0.0	0	N	74.5	79.2		N	N		
BMP3	12:51	Y	0		0.0	0.0									
BMP3	15:44	Y	0		0.0	0.0									
BMP4	07:50	Y	0		0.0	0.0	0	N	65.9	70.1		N	N		
BMP4	15:14	Y	0		0.0	0.0									
BMP4	16:02	Y	0		0.0	0.0								considerably high dust levels increasing throughout day with increase in vehicle and plant movement.	
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:21										N				
CMP2	15:22										N				
CMP3	15:23										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	8:15	Flow Meter (M^3):	745
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
2	N	28	Sun	3	dry	1023	N	N	N/A			

Assessors Signature: E Walker

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	21.07.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	C.N
Daily Activity & Grid Ref.:	F6, A6, A7					General Notes:	Visual Dust (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampler	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	09:17	N	0		0.0	0.0	0	N	66.8	75.9		N	N		
BMP1	11:03	N	0		0.0	0.0								*Site dampened down by road sweeper - AM.	
BMP1	14:56	N	0		0.0	0.0									
BMP2	09:35	N	0		0.0	0.0	0	N	72.7	78.5		N	N		
BMP2	11:20	N	0		0.0	0.0									
BMP2	15:05	N	0		0.0	0.0									
BMP3	09:57	N	0		0.0	0.0	0	N	[illegible]	[illegible]		N	N		
BMP3	11:47	N	0		0.0	0.0			62.5	69.7					
BMP3	15:16	N	0		0.0	0.0									
BMP4	09:31	N	0		0.0	0.0	0	N	73.4	82.1		N	N		
BMP4	12.00	N	0		0.0	0.0									
BMP4	15:45	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	10:32										N				
CMP2	10:33										N				
CMP3	10:38										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	10:00	Flow Meter (M^3):	765
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)*	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
3	S	21	Sunny	0	Dry	1024	not in operation	N	N/a			

Assessors Signature: [signature]

Preventus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	20.07.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	RW
Daily Activity & Grid Ref.:	F6, A6, A7					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1= Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:00	N	0		0.0	0.0	0	N	65.2	66.1		N	N		
BMP1	12:10	N	0		0.0	0.0									
BMP1	15:59	N	0		0.0	0.0									
BMP2	07:17	N	0		0.0	0.0	0	N	71.6	75.9		N	N		
BMP2	12:21	N	0		0.0	0.0									
BMP2	15:59	N	0		0.0	0.0									
BMP3	07:54	N	0		0.0	0.0	0	N	68.4	72.3		N	N		
BMP3	12:44	N	0		0.0	0.0									
BMP3	15:35	N	0		0.0	0.0									
BMP4	07:51	N	0		0.0	0.0	0	N	62.1	65.7		N	N		
BMP4	15:08	N	0		0.0	0.0									
BMP4	15:52	N	0		0.0	0.0									
EMP1		NA													
EMP2															
EMP3															
EMP4															
CMP1	14:05										N				
CMP2	14:04										N				
CMP3	14:03										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	08:15	Flow Meter (M^3):	745
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Levels / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
3	N	26	Dry	0	Dry	1000	N	N	N/A			

Assessors Signature: [signature]

Prevention Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	19.07.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	EW
Daily Activity & Grid Ref.:	B4, B5, B6					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1= Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:10	Y	0		0.0	0.0	0	Y	64.1	67.9		Y	Y		
BMP1	12:00	Y	0		0.0	0.0									
BMP1	16:05	Y	0		0.0	0.0									
BMP2	07:27	Y	0		0.0	0.0	0	Y	74.3	79.5		Y	Y		
BMP2	12:17	Y	0		0.0	0.0									
BMP2	15:22	Y	0		0.0	0.0									
BMP3	07:44	Y	0		0.0	0.0	0	Y	70.2	76.4		Y	Y		
BMP3	12:54	Y	0		0.0	0.0									
BMP3	15:39	Y	0		0.0	0.0									
BMP4	08:01	Y	0		0.0	0.0	0	Y	69.0	74.1		Y	Y		
BMP4	12:52	Y	0		0.0	0.0									
BMP4	15:57	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:21										Y				
CMP2	15:22										Y				
CMP3	15:25										Y				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over topping (Y/N)	Time: 08:00	Flow Meter (M^3): 745
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Inspected & Actions Taken to Rectify:	
2	W	25	Sun	1	Dry	1023	Y	Y	N/A	

Assessors Signature: EWalker

Provectus Environmental Monitoring Form 181114 TH

Site:	Project Bradford	Date:	25-07-21	Contract Ref:	181114	Client:	BAM Construction Ltd	Assessor name:	C.N
Daily Activity & Grid Ref.:	D6, E6, F6, F1					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Imports from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:18	N	0		0.0	0.0	0	N	66.3	82.4		N	N		
BMP1	11:06	N	0		0.0	0.0									
BMP1	15:09	N	0		0.0	0.0									
BMP2	07:26	N	0		0.0	0.0	0	N	58.6	76.4		N	N		
BMP2	11:25	N	0		0.0	0.0									
BMP2	15:24	N	0		0.0	0.0									
BMP3	07:45	N	0		0.0	0.0	0	N	54.4	68.3		N	N		
BMP3	11:47	N	0		0.0	0.0									
BMP3	15:45	N	0		0.0	0.0									
BMP4													*	→ no safe access due to closed walkways + works close to monitoring point.	
BMP4															
BMP4															
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:57										N				
CMP2	15:28										N				
CMP3	15:34										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	08:10	Flow Meter (M³):	7465
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
4	ENE	18	Sunny	0	Dry	1019	not in operation	N	nla			

Assessors Signature: CN

Prevention Environmental Monitoring Form 181114 TH

Site:	Project Bradford	Date:	29.07.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	SW
Daily Activity & Grid Ref.:						General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1= Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:17	Y	0		0.0	0.0	0	N	66.9	76.2		Y	N		
BMP1	11:24	Y	0		0.0	0.0									
BMP1	15:06	N	0		0.0	0.0									
BMP2	07:34	Y	0		0.0	0.0	0	N	70.9	76.2		Y	N		
BMP2	11:41	Y	0		0.0	0.0									
BMP2	15:17	Y	0		0.0	0.0									
BMP3	07:51	Y	0		0.0	0.0	0	N	64.8	71.3		Y	N		
BMP3	11:55	Y	0		0.0	0.0									
BMP3	15:34	Y	0		0.0	0.0									
BMP4	08:08	Y	0		0.0	0.0	0	N	65.6	72.3		Y	N		
BMP4	11:15	Y	0		0.0	0.0									
BMP4	15:51	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:55										Y				
CMP2	15:52										Y				
CMP3	15:57										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	10:00	Flow Meter (M^3):	745
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Levels / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
13	SW	12	OVERCAST	8	DRY	1006	Y	N	N/A			

Assessors Signature: [signature]

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	28.07/21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	BG
Daily Activity & Grid Ref.:						General Notes:	Visual Dust (0=none, 1= Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1= Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:38	Y	0		0.0	0.0	0	N	66.7	76.9		N	N		
BMP1	11:42	Y	0		0.0	0.0									
BMP1	14:56	Y	0		0.0	0.0									
BMP2	07:29	Y	0		0.0	0.0	0	N	71.5	79.3		N	N		
BMP2	11:53	Y	0		0.0	0.0									
BMP2	15:12	Y	0		0.0	0.0									
BMP3	07:46	Y	0		0.0	0.0	0	N	55.1	60.2		N	N		
BMP3	12:17	Y	0		0.0	0.0									
BMP3	15:56	Y	0		0.0	0.0									
BMP4	08:03	Y	0		0.0	0.0	0	N	58.4	66.3		N	N		
BMP4	12:56	Y	0		0.0	0.0									
BMP4	15:49	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	18:08										Y				
CMP2	14:02										Y				
CMP3	14:03										Y				

Meteorological and environmental conditions							WTP Inspection.		Time:	08:10	Flow Meter (M^3):	745
Wind speed	Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
5	SW	15	Passing cloud	7	Dry	1004	Y	Y	N/A			

Assessors Signature: [signature]

Provectus Environmental Monitoring Form L01114 TH

Site:	Project Bradford	Date:	27.07.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	C.N
Daily Activity & Grid Ref.:	A7, A6, D6, E6, F6						General Notes:	Visual Dust: (0=none, 1= Some, 3= Excessive, 4= Unreasonable)	PID Bump Test: ✓

Location: MP or Grid Ref.	Time	DUSTCON Detectability	DUSTCON Intensity	DUSTCON Quality	VOC Average PID Reading	VOC Peak PID Reading	DUST Visual (0=none, 1= Minor, 3= Excessive)	DUST Friabee Sampled	NOISE Average Reading	NOISE Peak Reading	CANAL Visible Impacts from Site Run-off	HOUSEKEEPING Litter	HOUSEKEEPING Perth	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1-3)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08:24	N	0		0.0	0.0	0	N	65.3	78.4		N	N		
BMP1	12:17	N	0		0.0	0.0									
BMP1															
BMP2	07:50	N	0		0.0	0.0	0	N	63.8	75.5		N	N		
BMP2	11:39	N	0		0.0	0.0									
BMP2															
BMP3	07:43	N	0		0.0	0.0	0	N	56.6	69.8		N	N		
BMP3	11:57	N	0		0.0	0.0									
BMP3															
BMP4	08:04	N	0		0.0	0.0	0	N	59.1	76.6		N	N		
BMP4	11:19	N	0		0.0	0.0									
BMP4															
EMP1															
EMP2															
EMP3															
EMP4															
CMP1															
CMP2															
CMP3															

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar		
3	SW	18	overcast, dry	8	Dry	1008	Not Operational	N

Time: 08:47 Flow Meter (M³): ~~7~~ 745

Equipment Impacted & Actions Taken to Rectify: n/a

Assessors Signature: C.N

Provisius Environmental Monitoring Form 181114 TH

Site:	Project Bradford	Date:	26/07/21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	C.N
Daily Activity & Grid Ref.:	D6, E6, F6, A5					General Notes:	Visual Dust: (0=none, 1= Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1= Minor, 3=	Friobes Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:46	N	0		0.0	0.0	0	N	62.9	79.3		N	N		
BMP1	11:33	N	0		0.0	0.0									
BMP1	15:01	N	0		0.0	0.0									
BMP2	07:59	N	0		0.0	0.0	0	N	61.4	74.9		N	N		
BMP2	11:52	N	0		0.0	0.0									
BMP2	15:19	N	0		0.0	0.0									
BMP3	08:25	N	0		0.0	0.0	0	N	52.7	63.2		N	N		
BMP3	[redacted]	N	0		0.0	0.0									
BMP3	15:56	N	0		0.0	0.0									
BMP4	08:42	N	0		0.0	0.0	0	N	59.6	73.4		N	N		
BMP4	12:28	N	0		0.0	0.0									
BMP4	15:53	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	14:51										N/A				
CMP2	14:52														
CMP3	14:53														

12:10

Meteorological and environmental conditions							WTP Inspection.		Time:	11:30	Flow Meter (M³):	745
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
4	W	20	cloudy/partly sunny	7	Dry	1010	not in operation	N	n/a			

Assessors Signature: [signature]

Protective Environmental Monitoring Form 181114 TH

Site:	Project Bradford	Date:	30.07.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	EG
Daily Activity & Grid Ref.:						General Notes:	Visual Dust: (0=none, 1= Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1= Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:21	1	0		0.0	0.0	0	N	63.5	75.6		Y	N		
BMP1	11:48	1	0		0.0	0.0									
BMP1	14:55	2	0		0.0	0.0									
BMP2	07:19	1	0		0.0	0.0	0	N	74.2	80.9		N	N		
BMP2	12:05	1	0		0.0	0.0									
BMP2	15:10	1	0		0.0	0.0									
BMP3	07:35	2	0		0.0	0.0	0	N	68.7	74.3		N	N		
BMP3	12:22	2	0		0.0	0.0									
BMP3	15:28	2	0		0.0	0.0									
BMP4	07:52	1	0		0.0	0.0	0	N	60.8	75.9		N	N		
BMP4	12:39	1	0		0.0	0.0									
BMP4	16:35	1	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:50										1				
CMP2	15:51										1				
CMP3	15:52										1				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Overtopping (Y/N)	Time: 08:50	Flow Meter (M^3): 745
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Inspected & Actions Taken to Rectify:	
8	NE	13	Rain	8	wet	1002	Y	Y	N/A	

Assessors Signature: E Dalley

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	02.08.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	BW
Daily Activity & Grid Ref.:	D6, E6					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:06	Y	0		0.0	0.0	0	Y	71.3	72.8		Y	Y		
BMP1	11:23	Y	0		0.0	0.0									
BMP1	15:04	Y	0		0.0	0.0									
BMP2	07:25	Y	0		0.0	0.0	0	Y	56.2	60.9		Y	Y		
BMP2	11:40	Y	0		0.0	0.0									
BMP2	15:21	Y	0		0.0	0.0									
BMP3	07:42	Y	0		0.0	0.0	0	Y	53.4	61.6		Y	Y		
BMP3	11:58	Y	0		0.0	0.0									
BMP3	15:38	Y	0		0.0	0.0									
BMP4	07:59	Y	0		0.0	0.0	0	Y	58.1	71.5		Y	Y		
BMP4	12:15	Y	0		0.0	0.0									
BMP4	15:55	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:57										Y				
CMP2	15:58										Y				
CMP3	15:59										Y				

Meteorological and environmental conditions							WTP Inspection.		Time:	08:10	Flow Meter (M^3):	745
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
7	NW	18	Dry/cloudy	4	Dry	1014	Y	Y	N/A			

Assessors Signature.....

Site:	Project Bradford	Date:	03.08.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	D6, E6					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:14	Y	0		0.0	0.0	0	N	59.8	65.3		N	N		
BMP1	10:51	Y	0		0.0	0.0									
BMP1	14:03	Y	0		0.0	0.0									
BMP2	07:31	Y	0		0.0	0.0	0	N	61.2	69.5		N	N		
BMP2	11:08	Y	0		0.0	0.0									
BMP2	14:20	Y	0		0.0	0.0									
BMP3	07:48	Y	0		0.0	0.0	0	N	54.2	58.1		N	N		
BMP3	11:25	Y	0		0.0	0.0									
BMP3	14:37	Y	0		0.0	0.0									
BMP4	08:05	Y	0		0.0	0.0	0	N	56.8	60.4		N	N		
BMP4	11:42	Y	0		0.0	0.0									
BMP4	14:54	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:11										Y				
CMP2	15:12										Y				
CMP3	15:13										Y				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	Leaks / Over-topping (Y/N)	Time: 07:10	Flow Meter (M^3): 745
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
2	S	18	Dry, Sun	3	Dry	1014	Y	Y	N/A	

Assessors Signature .....

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	04-08-21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	E.N
Daily Activity & Grid Ref.:	E6, F6, D6					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07.20	N	0		0.0	0.0	0	N	68.2	76.8		N	N		
BMP1	11:10	N	0		0.0	0.0									
BMP1	4:30	N	0		0.0	0.0									
BMP2	07.40	N	0		0.0	0.0	0	N	75.6	79.7		N	N		
BMP2	11:28	N	0		0.0	0.0									
BMP2	4:48	N	0		0.0	0.0									
BMP3	07:58	N	0		0.0	0.0	0	N	57.5	63.4		N	N		
BMP3	11:47	N	0		0.0	0.0									
BMP3	5:08	N	0		0.0	0.0									
BMP4	08:20	N	0		0.0	0.0	0	N	58.3	66.5		N	N		
BMP4	12:04	N	0		0.0	0.0									
BMP4	15:25	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	13:15										N				
CMP2	13:16										N				
CMP3	13:16										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	9.00	Flow Meter (M^3):	745
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
4	SSW	15	Sunny/Dry	0	Dry	1013	not in operation	N	n/a			

Assessors Signature.....

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	05/08/21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	BW
Daily Activity & Grid Ref.:	A2					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:06	Y	0		0.0	0.0	0	N	71.5	74.7		N	N		
BMP1	11:42	Y	0		0.0	0.0									
BMP1	14:56	Y	0		0.0	0.0									
BMP2	07:23	Y	0		0.0	0.0	0	N	56.4	62.9		N	N		
BMP2	11:59	Y	0		0.0	0.0									
BMP2	15:13	Y	0		0.0	0.0									
BMP3	07:40	Y	0		0.0	0.0	0	N	58.5	61.3		N	N		
BMP3	12:16	Y	0		0.0	0.0									
BMP3	15:36	Y	0		0.0	0.0									
BMP4	07:55	Y	0		0.0	0.0	0	N	52.8	57.6		N	N		
BMP4	12:33	Y	0		0.0	0.0									
BMP4	15:47	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:50										Y				
CMP2	15:51										Y				
CMP3	15:52										Y				

Meteorological and environmental conditions							WTP Inspection.		Time:	10:00	Flow Meter (M^3):	745
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
1881	S	14	overcast	7	dry	1006	Y	Y	N/A			

Assessors Signature: [signature]

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	6.8.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	B1, B2					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	09:05	N	0		0.0	0.0	0	N	68.4	77.5		N	N		
BMP1	11:23	2	0		0.0	0.0									
BMP1	14:41	2	0		0.0	0.0									
BMP2	08:17	N	0		0.0	0.0	0	N	74.7	81.2		N	N		
BMP2	11:40	2	0		0.0	0.0									
BMP2	14:58	2	0		0.0	0.0									
BMP3	08:10	N	0		0.0	0.0	0	N	56.7	62.9		N	N		
BMP3	11:57	2	0		0.0	0.0									
BMP3	15:15	2	0		0.0	0.0									
BMP4	08:27	N	0		0.0	0.0	0	N	58.6	63.7		N	N		
BMP4	12:14	2	0		0.0	0.0									
BMP4	15:32	2	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:35										2				
CMP2	15:36										2				
CMP3	15:37										2				

Meteorological and environmental conditions							WTP Inspection.		Time:	09:30	Flow Meter (M^3):	745
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
10	SSW	15	Heavy rain	8	Wet	993	not in operation	N	N/a			

Assessors Signature .....

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	09.08.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	BW
Daily Activity & Grid Ref.:	B1, S3					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:03	Y	0		0.0	0.0	0	N	73	73.2		N	N	Water treatment	
BMP1	11:42	N	0		0.0	0.0								leaving site.	
BMP1	14:58	N	0		0.0	0.0									
BMP2	07:20	N	0		0.0	0.0	0	N	57	59.4		N	N		
BMP2	11:59	N	0		0.0	0.0									
BMP2	15:10	N	0		0.0	0.0									
BMP3	07:37	N	0		0.0	0.0	0	N	49.6	59.3		N	N		
BMP3	12:16	N	0		0.0	0.0									
BMP3	15:27	N	0		0.0	0.0									
BMP4	07:54	N	0		0.0	0.0	0	N	59.8	68.7		N	N		
BMP4	12:33	N	0		0.0	0.0									
BMP4	15:44	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:47										N				
CMP2	15:48										N				
CMP3	15:49										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time:	N/A	Flow Meter (M³):	N/A
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:			
5	SW	13	Passing cloud	5	Dry	1008	Y	N	N/A			

Assessors Signature: BWalley

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	10.08.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	BG
Daily Activity & Grid Ref.:	G3							General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)

PID Bump Test: ✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:43	Y	0		0.0	0.0	0	Y	69.1	73.9		N	N		
BMP1	11:24	Y	0		0.0	0.0									
BMP1	14:05	Y	0		0.0	0.0									
BMP2	07:20	Y	0		0.0	0.0	0	Y	64.5	70.2		N	N		
BMP2	11:41	Y	0		0.0	0.0									
BMP2	14:22	Y	0		0.0	0.0									
BMP3	07:37	Y	0		0.0	0.0	0	Y	68.6	69.4		N	N		
BMP3	11:58	Y	0		0.0	0.0									
BMP3	14:39	Y	0		0.0	0.0									
BMP4	07:54	Y	0		0.0	0.0	0	Y	61.2	66.8		N	N		
BMP4	12:15	Y	0		0.0	0.0									
BMP4	14:56	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	14:58										Y				
CMP2	14:59										Y				
CMP3	15:00										Y				

Meteorological and environmental conditions							WTP Inspection.		Time:	08:00	Flow Meter (M^3):	745
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
8	SSW	14	Broken cloud	5	DRY	1013	Y	Y	N/A			

Assessors Signature: [signature]

Site:	Project Bradford	Date:	11.08.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	
Daily Activity & Grid Ref.:	C6, G4, F4, F6					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:13	Y	0		0.0	0.0	0	Y	67.4	72.1		N	N		
BMP1	11:31	N	0		0.0	0.0									
BMP1	14:04	N	0		0.0	0.0									
BMP2	07:30	N	0		0.0	0.0	0	N	63.1	68.5		N	N		
BMP2	11:48	N	0		0.0	0.0									
BMP2	14:21	N	0		0.0	0.0									
BMP3	07:47	N	0		0.0	0.0	0	N	69.4	71.9		N	N		
BMP3	12:05	N	0		0.0	0.0									
BMP3	14:38	N	0		0.0	0.0									
BMP4	08:04	N	0		0.0	0.0	0	N	62.5	66.4		N	N		
BMP4	12:22	N	0		0.0	0.0									
BMP4	14:55	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:00										N				
CMP2	15:01										N				
CMP3	15:02										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time:	Flow Meter (M³):
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar				
4	SW	13	Broken cloud	6	Dry	1016	Y	N	N/A	N/A

Equipment Impacted & Actions Taken to Rectify: N/A

Assessors Signature: [signature]

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	~~12~~ 12.08.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	[illegible]
Daily Activity & Grid Ref.:	D6, D5, C5, G2, F2					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:08	Y	0		0.0	0.0	0	Y	67.4	73.8		N	N		
BMP1	11:11	N	0		0.0	0.0									
BMP1	14:02	N	0		0.0	0.0									
BMP2	07:25	N	0		0.0	0.0	0	N	71.5	78.9		N	N		
BMP2	11:25	N	0		0.0	0.0									
BMP2	14:19	N	0		0.0	0.0									
BMP3	07:42	N	0		0.0	0.0	0	N	62.1	67.5		N	N		
BMP3	11:45	N	0		0.0	0.0									
BMP3	14:36	N	0		0.0	0.0									
BMP4	07:55	N	0		0.0	0.0	0	N	60.8	63.7		N	N		
BMP4	12:02	N	0		0.0	0.0									
BMP4	14:53	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	14:59										N				
CMP2	15:00										N				
CMP3	15:01										N				

Meteorological and environmental conditions						
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar
5	SSE	11	Sun	2	Dry	1016

WTP Inspection.		Time:	08:10	Flow Meter (M³):	745
System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
Y	N	N/A			

Assessors Signature: [signature]

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	13.08.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	
Daily Activity & Grid Ref.:	DG, DS, CS, G2, F2					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:08	Y	0		0.0	0.0	0	Y	69.4	73.1		Y	Y		
BMP1	11:21	Y	0		0.0	0.0									
BMP1	14:12	Y	0		0.0	0.0									
BMP2	07:25	Y	0		0.0	0.0	0	Y	74.9	80.2		Y	Y		
BMP2	11:38	Y	0		0.0	0.0									
BMP2	14:29	Y	0		0.0	0.0									
BMP3	07:42	Y	0		0.0	0.0	0	Y	64.5	69.8		Y	Y		
BMP3	11:55	Y	0		0.0	0.0									
BMP3	14:46	Y	0		0.0	0.0									
BMP4	07:59	Y	0		0.0	0.0	0	Y	58.5	62.7		Y	Y		
BMP4	12:12	Y	0		0.0	0.0									
BMP4	15:03	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:16										Y				
CMP2	15:11										Y				
CMP3	15:12										Y				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time:	N/A	Flow Meter (M^3):	N/A
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:			
9	SSW	19	Sun	0	dry	1017	Y	Y	N/A			

Assessors Signature: E Dalley

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	16.08.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	BW
Daily Activity & Grid Ref.:	D6, D5, C5, G3, F3					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:15	2	0		0.0	0.0	0	2	66.8	71.2		2	2		
BMP1	11:42	2	0		0.0	0.0									
BMP1	14:13	2	0		0.0	0.0									
BMP2	07:32	2	0		0.0	0.0	0	2	70.3	76.9		2	2		
BMP2	11:59	2	0		0.0	0.0									
BMP2	14:30	2	0		0.0	0.0									
BMP3	07:49	2	0		0.0	0.0	0	2	64.5	68.4		2	2		
BMP3	12:16	2	0		0.0	0.0									
BMP3	14:47	2	0		0.0	0.0									
BMP4	08:06	2	0		0.0	0.0	0	2	62.7	65.6		2	2		
BMP4	12:33	2	0		0.0	0.0									
BMP4	15:04	2	0												
EMP1															
EMP2															
EMP3															
EMP4															
CMP1											2				
CMP2											2				
CMP3											2				

Meteorological and environmental conditions							WTP Inspection.		Time:	2/A	Flow Meter (M^3):	2/A
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Overtopping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
11	WNW	15	sun/cloud	6	Dry	1016	2	2	2/A			

Assessors Signature: [signature]

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	7.08.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	A2, F3, G3, D6, C5					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:22	N	0		0.0	0.0	0	N	57.5	67.2		N	N		
BMP1	10:45	N	0		0.0	0.0									
BMP1	14:41	N	0		0.0	0.0									
BMP2	07:59	N	0		0.0	0.0	0	N	71.8	79.5		N	N		
BMP2	11:01	N	0		0.0	0.0									
BMP2	15:38	N	0		0.0	0.0									
BMP3	08:14	N	0		0.0	0.0	0	N	55.9	64.1		N	N		
BMP3	11:38	N	0		0.0	0.0									
BMP3	15:33	N	0		0.0	0.0									
BMP4	07:57	N	0		0.0	0.0	0	N	57.9	64.3		N	N		
BMP4	11:21	N	0		0.0	0.0									
BMP4	15:17	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	10:33										N				
CMP2	10:34										N				
CMP3	10:36										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	—	Flow Meter (M^3):	—
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
3	W	16	Showers, wet	7	Wet	1018	n/a	n/a	n/a			

Assessors Signature.....

Provectus Environmental Monitoring Form 101114 TH

Site:	Project Bradford	Date:	18.08.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	CN
Daily Activity & Grid Ref.:	F2, D6, C5					General Notes:	Visual Dust: (0=none, 1- Some, 3= Excessive, 4= Unreasonable)	PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual (0=none, 1- Minor, 3=	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1-5)	(Description)	(ppm)	(ppm)	(0-4)	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07.52	N	0		0.0	0.0	0	N	59.8	65.3		N	N		
BMP1	11.05	N	0		0.0	0.0									
BMP1	14.38	N	0		0.0	0.0									
BMP2	07.43	N	0		0.0	0.0	0	N	68.7	78.4		N	N		
BMP2	11.22	N	0		0.0	0.0									
BMP2	14.55	N	0		0.0	0.0									
BMP3	08.53	N	0		0.0	0.0	0	N	63.4	75.6		N	N		
BMP3	11.56	N	0		0.0	0.0									
BMP3	15.37	N	0		0.0	0.0									
BMP4	08.17	N	0		0.0	0.0	0	N	62.7	69.5		N	N		
BMP4	11.40	N	0		0.0	0.0									
BMP4	15.15	N	0												
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	13.27										N				
CMP2	13.29										N				
CMP3	13.24										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	Leaks / Over-topping (Y/N)	Time: —	Flow Meter (M^3): —
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
14	W	15	Overcast, drizzle	6	Wet	1016	n/a	n/a	n/a	

Assessors Signature: CN

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	19.08.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	BC
Daily Activity & Grid Ref.:	7					General Notes:		PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:11	2	0		0.0	0.0	2	2	65.4	71.3		2	2		
BMP1	11:05	2	0		0.0	0.0									
BMP1	14:07	2	0		0.0	0.0									
BMP2	07:28	2	0		0.0	0.0	2	2	69.8	75.9		2	2		
BMP2	11:20	2	0		0.0	0.0									
BMP2	14:24	2	0		0.0	0.0									
BMP3	07:45	2	0		0.0	0.0	2	2	61.2	67.6		2	2		
BMP3	11:37	2	0		0.0	0.0									
BMP3	14:41	2	0		0.0	0.0									
BMP4	08:02	2	0		0.0	0.0	2	2	58.1	62.7		2	2		
BMP4	11:54	2	0		0.0	0.0									
BMP4	14:58	2	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:10										2				
CMP2	15:11										2				
CMP3	15:12										2				

Meteorological and environmental conditions							WTP Inspection.		Time:	N/A	Flow Meter (M^3):	N/A
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
4	SW	14	Overcast	8	wet	1013	2	2	N/A			

Assessors Signature: [signature]

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	20.08.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	BC
Daily Activity & Grid Ref.:						General Notes:		PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:18	2	0		0.0	0.0	2	2	67.8	76.3		2	2		
BMP1	11:21	2	0		0.0	0.0									
BMP1	14:03	2	0		0.0	0.0									
BMP2	07:35	2	0		0.0	0.0	2	2	69.2	73.1		2	2		
BMP2	11:38	2	0		0.0	0.0									
BMP2	14:20	2	0		0.0	0.0									
BMP3	07:52	2	0		0.0	0.0	2	2	61.2	68.9		2	2		
BMP3	11:55	2	0		0.0	0.0									
BMP3	14:38	2	0		0.0	0.0									
BMP4	08:09	2	0		0.0	0.0	2	2	56.5	62.6		2	2		
BMP4	12:12	2	0		0.0	0.0									
BMP4	14:55	2	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:15										2				
CMP2	15:16										2				
CMP3	15:17										2				

Meteorological and environmental conditions							WTP Inspection.		Time:	N/A	Flow Meter (M³):	N/A
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
4	1	15	Becher cloud	5	Dry	1014	2	2	N/A			

Assessors Signature: [signature]

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	23.08.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	BCW
Daily Activity & Grid Ref.:	FB, G2					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:11	2	0		0.0	0.0	2	2	70.2	73.9		2	2		
BMP1	11:23	2	0		0.0	0.0									
BMP1	14:04	2	0		0.0	0.0									
BMP2	07:28	2	0		0.0	0.0	2	2	55.4	62.5		2	2		
BMP2	11:40	2	0		0.0	0.0									
BMP2	14:21	2	0		0.0	0.0									
BMP3	07:45	2	0		0.0	0.0	2	2	54.1	60.3		2	2		
BMP3	11:57	2	0		0.0	0.0									
BMP3	14:38	2	0		0.0	0.0									
BMP4	08:02	2	0		0.0	0.0	2	2	46.8	56.6		2	2		
BMP4	12:14	2	0		0.0	0.0									
BMP4	14:55	2	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	14:57										2				
CMP2	14:58										2				
CMP3	14:59										2				

Meteorological and environmental conditions							WTP Inspection.		Time:	N/A	Flow Meter (M³):	N/A
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
6	NE	11	Sun	2	dry	1030	2	2	N/A			

Assessors Signature: [signature]

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	24.08.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	RJ
Daily Activity & Grid Ref.:	F3,G2					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:00	2	0		0.0	0.0	2	2	66.2	71.5		2	2		
BMP1	11:06	2	0		0.0	0.0									
BMP1	14:13	2	0		0.0	0.0									
BMP2	07:17	2	0		0.0	0.0	2	2	69.6	76.9		2	2		
BMP2	11:23	2	0		0.0	0.0									
BMP2	14:30	2	0		0.0	0.0									
BMP3	07:34	2	0		0.0	0.0	2	2	60.4	68.3		2	2		
BMP3	11:40	2	0		0.0	0.0									
BMP3	14:47	2	0		0.0	0.0									
BMP4	07:51	2	0		0.0	0.0	2	2	59.1	62.8		2	2		
BMP4	11:57	2	0		0.0	0.0									
BMP4	15:04	2	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1															
CMP2															
CMP3															

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time:	Flow Meter (M^3):
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar				
2	NE	15	cloud/ overcast	8	Dry	1032	2	2	N/A	N/A

Equipment Impacted & Actions Taken to Rectify:

N/A

Assessors Signature.....

Site:	Project Bradford	Date:	25.08.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	RJ
Daily Activity & Grid Ref.:	G1, F2					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:04	2	0		0.0	0.0	2	2	62.5	58.9		2	2		
BMP1	11:01	2	0		0.0	0.0									
BMP1	14:07	2	0		0.0	0.0									
BMP2	07:21	2	0		0.0	0.0	2	2	68.3	72.5		2	2		
BMP2	11:18	2	0		0.0	0.0									
BMP2	14:24	2	0		0.0	0.0									
BMP3	07:36	2	0		0.0	0.0	2	2	65.7	69.2		2	2		
BMP3	11:53	2	0		0.0	0.0									
BMP3	19:41	2	0		0.0	0.0									
BMP4	07:48	2	0		0.0	0.0	2	2	56.8	61.6		2	2		
BMP4	12:10	2	0		0.0	0.0									
BMP4	14:58	2	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:15										2				
CMP2	15:16										2				
CMP3	15:17										2				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time:	N/A	Flow Meter (M^3):	N/A
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:			
4-5	SW	15	overcast	7	Dry	1028	2	2	N/A			

Assessors Signature: RJ

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	26.08.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	B.W
Daily Activity & Grid Ref.:	G1, G2, F1, F2					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:24	N	0		0.0	0.0	N	N	60.2	63.1		N	N		
BMP1	11:03	N	0		0.0	0.0								• DUST LEVELS INCREASED	
BMP1	14:41	N	0		0.0	0.0								THROUGHOUT DAY -	
BMP2	07:43	N	0		0.0	0.0	N	N	68.7	73.9		N	N	DUST SUPRESSION ACTIONED.	
BMP2	11:21	N	0		0.0	0.0									
BMP2	14:58	N	0		0.0	0.0									
BMP3	08:05	N	0		0.0	0.0	N	N	55.4	59.1		N	N		
BMP3	11:40	N	0		0.0	0.0									
BMP3	15:21	N	0		0.0	0.0									
BMP4	08:23	N	0		0.0	0.0	N	N	70.7	78.2		N	N		
BMP4	11:58	N	0		0.0	0.0									
BMP4	15:41	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	13:33										N				
CMP2	13:34										N				
CMP3	13:35										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	N/A	Flow Meter (M³):	N/A
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)		(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
12	NNE	25	Sunny, dry	2	Dry	1026	N/A	N/A	N/A			

Assessors Signature: [signature]

Site:	Project Bradford	Date:	27.08.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	B.W
Daily Activity & Grid Ref.:	G1, F1, F2					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:57	2	0		0.0	0.0	2	2	62.3	67.9		2	2		
BMP1	10:48	2	0		0.0	0.0								• DUST LEVELS INCREASED	
BMP1	15:05	2	0		0.0	0.0								THROUGHOUT DAY -	
BMP2	07:54	2	0		0.0	0.0	2	2	74.1	79.6		2	2	DUST SUPPRESSION ACTIONED.	
BMP2	11:06	2	0		0.0	0.0									
BMP2	15:22	2	0		0.0	0.0									
BMP3	08:16	2	0		0.0	0.0	2	2	73.2	80.6		2	2		
BMP3	11:24	2	0		0.0	0.0									
BMP3	15:40	2	0		0.0	0.0									
BMP4	08:34	2	0		0.0	0.0	2	2	72.7	78.9		2	2		
BMP4	11:44	2	0		0.0	0.0									
BMP4	16:00	2	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	16:19										2				
CMP2	16:20										2				
CMP3	16:24										2				

Meteorological and environmental conditions							WTP Inspection.		Time:	N/A	Flow Meter (M^3):	N/A
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
6	ENE	20	Sunny, dry	1	Dry	1026	N/A	N/A	N/A			

Assessors Signature: E Callen

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	31.08.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	F3, E3, F6					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:22	N	0		0.0	0.0	N	N	65.3	65.5		N	N		
BMP1	11:35	N	0		0.0	0.0								* Dust created by Skanska concrete lorries on South side of site.	
BMP1	14:45	N	0		0.0	0.0									
BMP2	07:39	N	0		0.0	0.0	N	N	73.2	78.5		N	N		
BMP2	11:52	N	0		0.0	0.0									
BMP2	15:05	N	0		0.0	0.0									
BMP3	08:02	N	0		0.0	0.0	Y	N	56.7	62.9		N	N		
BMP3	12:10	N	0		0.0	0.0									
BMP3	15:23	N	0		0.0	0.0									
BMP4	08:19	N	0		0.0	0.0	N	N	61.8	64.7		N	N		
BMP4	12:27	N	0		0.0	0.0									
BMP4	15:40	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	14:05										N				
CMP2	14:06										N				
CMP3	14:06										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	✓	Flow Meter (M^3):	✓
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar	✓	✓	✓			
8	NE	15	DRY, OVERCAST	7	DRY	1033						

Assessors Signature.....

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	01.09.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	F3					General Notes:		PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:30	N	0		0.0	0.0	N	N	59.4	63.1		N	N		
BMP1	10:51	N	0		0.0	0.0									
BMP1	14:03	N	0		0.0	0.0									
BMP2	07:48	N	0		0.0	0.0	N	N	66.8	72.3		N	N		
BMP2	11:08	N	0		0.0	0.0									
BMP2	14:21	N	0		0.0	0.0									
BMP3	08:08	N	0		0.0	0.0	N	N	54.5	59.6		N	N		
BMP3	11:26	N	0		0.0	0.0									
BMP3	14:38	N	0		0.0	0.0									
BMP4	08:25	N	0		0.0	0.0	N	N	55.2	58.7		N	N		
BMP4	11:43	N	0		0.0	0.0									
BMP4	14:55	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:17										N				
CMP2	15:18										N				
CMP3	15:19										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	n/a	Flow Meter (M^3):	n/a
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar	n/a	n/a	n/a			
7	NE	14	DRY, OVERCAST	8	DRY	1034						

Assessors Signature.....

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	02.09.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	E3, F3, G3					General Notes:		PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:20	Y	0		0.0	0.0	N	N	62.7	70.1		N	N		
BMP1	11:35	Y	0		0.0	0.0									
BMP1	14:[illegible]	Y	0		0.0	0.0									
BMP2	07:35	Y	0		0.0	0.0	N	N	68.2	76.7		N	N		
BMP2	11:53	Y	0		0.0	0.0									
BMP2	14:48	Y	0		0.0	0.0									
BMP3	08:00	Y	0		0.0	0.0	N	N	55.5	61.4		N	N		
BMP3	12:15	Y	0		0.0	0.0									
BMP3	15:10	Y	0		0.0	0.0									
BMP4	08:17	Y	0		0.0	0.0	N	N	37.3	61.9		N	N		
BMP4	12:32	Y	0		0.0	0.0									
BMP4	15:27	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	16:05										Y				
CMP2	16:05										Y				
CMP3	16:07										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	n/a	Flow Meter (M^3):	n/a
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
2	NE	14	Overcast, dry	8	Dry	1020	n/a	n/a	N/A			

Assessors Signature [signature]

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	05.09.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	CN
Daily Activity & Grid Ref.:	F3, F4, G3, G4					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	09:46	Y	0		2.0	0.0	N	N	65.6	69.5		N	N		
BMP1	10:20	Y	0		0.0	0.0									
BMP1	14:50	Y	0		0.0	0.0									
BMP2	08:10	Y	0		0.0	0.0	N	N	70.7	77.2		N	N		
BMP2	10:38	Y	0		0.0	0.0									
BMP2	15:08	Y	0		0.0	0.0									
BMP3	08:45	Y	0		0.0	0.0	N	N	62.9	66.8		N	N		
11:00 BMP3	[illegible]	Y	0		0.0	0.0									
BMP3	15:28	Y	0		0.0	0.0									
BMP4	09:03	Y	0		0.0	0.0	N	N	57.3	64.3		N	N		
BMP4	11:17	Y	0		0.0	0.0									
BMP4	15:45	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:27										N				
CMP2	15:28										N				
CMP3	15:28										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	—	Flow Meter (M^3):	—
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
3	N	14	Partly Sunny	5	Dry	1025	—	—	—			

Assessors Signature: CN

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	13th 09.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	CN
Daily Activity & Grid Ref.:	G3, F3					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to 5)	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	09:55	N	0		0.0	0.0	N	N	68.8	79.9		N	N		
BMP1	11:00	N	0		0.0	0.0									
BMP1	14:38	N	0		0.0	0.0									
BMP2	09:13	N	0		0.0	0.0	N	N	70.6	81.4		N	N		
BMP2	11:17	N	0		0.0	0.0									
BMP2	14:54	N	0		0.0	0.0									
BMP3	08:35	N	0		0.0	0.0	N	N	65.3	76.7		N	N		
BMP3	11:39	N	0		0.0	0.0									
BMP3	15:14	N	0		0.0	0.0									
BMP4	08:35	N	0		0.0	0.0	N	N	60.2	69.4		N	N		
BMP4	11:55	N	0		0.0	0.0									
BMP4	15:30	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	13:47										N				
CMP2	13:49										N				
CMP3	13:48										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	—	Flow Meter (M^3):	
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar	—	—	—			
4	E	13	OVERCAST, DRIZZLE	8	WET	1019						

Assessors Signature.....

Site:	Project Bradford	Date:	14.09.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	F3, G3, F4, F5					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08.05	N	0		0.0	0.0	N	N	67.7	79.3		N	N	*BMP1 close to generator	
BMP1	11.03	N	0		0.0	0.0									
BMP1	14.00	N	0		0.0	0.0									
BMP2	08.21	N	0		0.0	0.0	N	N	71.5	80.6		N	N	*BMP2 adjacent to Careys Works.	
BMP2	11.20	N	0		0.0	0.0									
BMP2	14.16	N	0		0.0	0.0									
BMP3	08.38	N	0		0.0	0.0	N	N	63.8	70.2		N	N		
BMP3	11.40	N	0		0.0	0.0									
BMP3	14.37	N	0		0.0	0.0									
BMP4	08.45	N	0		0.0	0.0	N	N	59.2	65.7		N	N		
BMP4	11.57	N	0		0.0	0.0									
BMP4	14.34	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	13.45										N				
CMP2	13.44										N				
CMP3	13.46										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time:	Flow Meter (M^3):
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
4	NE	14	overcast, rain	8	Wet	1015	—	—	—	—

Assessors Signature.....

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	15.09.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	G4, G3, F4, F5					General Notes:		PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:10	N	0		0.0	0.0	N	N	66.2	77.1		N	N		
BMP1	10:43	N	0		0.0	0.0									
BMP1	14:15	N	0		0.0	0.0									
BMP2	07:26	N	0		0.0	0.0	N	N	63.7	75.9		N	N		
BMP2	11:00	N	0		0.0	0.0								* Site roads	
BMP2	14:52	N	0		0.0	0.0								increasingly dusty	
BMP3	07:46	N	0		0.0	0.0	N	N	55.4	60.3		N	N	as day has	
BMP3	11:20	N	0		0.0	0.0								progressed due to	
BMP3	14:52	N	0		0.0	0.0								vehicle movements	
BMP4	08:03	N	0		0.0	0.0	N	N	58.5	62.7		N	N		
BMP4	11:36	N	0		0.0	0.0									
BMP4	15:10	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	13:33										N				
CMP2	13:34										N				
CMP3	13:34										N				

Meteorological and environmental conditions						
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric
(mph)	(e.g. N, SW)	°C	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar
3	W	20	Sunny, dry	0	Dry	1015

WTP Inspection.		Time:	—	Flow Meter (M^3):	—
System Working	Leaks / Over-topping	Equipment Impacted & Actions Taken to Rectify:			
—	—	—			

Assessors Signature: C.N

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	16.09.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	BL
Daily Activity & Grid Ref.:	C4, C5, C4, C5					General Notes:		PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:12	Y	0		0.0	0.0	Y	Y	64.5	73.2		Y	Y		
BMP1	10:51	Y	0		0.0	0.0									
BMP1	14:01	Y	0		0.0	0.0									
BMP2	07:29	Y	0		0.0	0.0	Y	Y	66.8	76.9		Y	Y		
11:08 BMP2	[illegible]	Y	0		0.0	0.0									
BMP2	14:19	Y	0		0.0	0.0									
BMP3	07:46	Y	0		0.0	0.0	Y	Y	58.3	62.4		Y	Y		
BMP3	11:25	Y	0		0.0	0.0									
BMP3	14:37	Y	0		0.0	0.0									
BMP4	08:08	Y	0		0.0	0.0	Y	Y	53.1	60.7		Y	Y		
BMP4	11:42	Y	0		0.0	0.0									
BMP4	14:54	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:11										Y				
CMP2	15:12										Y				
CMP3	15:13										Y				

Meteorological and environmental conditions						
Wind speed	Wind Directio	Temp	Weather description	Cloud cover	Ground conditions	Baromet ric
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar
2	N	14	overcast	8	wet	1017

WTP Inspection.		Time:	N/A	Flow Meter (M^3):	N/A
System Working	Leaks / Over-topping	Equipment Impacted & Actions Taken to Rectify:			
N/A	N/A	N/A			

Assessors Signature: [signature]

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	17.09.21	Contract Ref:	101114	Client:	B&M Construction Ltd	Assessor name	BC
Daily Activity & Grid Ref.:		54, E4.				General Notes:		PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:11	Y	0		0.0	0.0	Y	✓	62.4	68.1		N	N		
BMP1	10:53	Y	0		0.0	0.0									
BMP1	14:01	Y	0		0.0	0.0									
BMP2	07:28	Y	0		0.0	0.0	Y	✓	69.9	72.2		N	N		
BMP2	10:50	Y	0		0.0	0.0									
BMP2	14:18	Y	0		0.0	0.0									
BMP3	07:45	Y	0		0.0	0.0	Y	✓	56.2	59.6		N	N		
BMP3	11:07	Y	0		0.0	0.0									
BMP3	14:35	Y	0		0.0	0.0									
BMP4	08:02	Y	0		0.0	0.0	Y	✓	54.8	57.7		N	N		
BMP4	11:24	Y	0		0.0	0.0									
BMP4	14:52	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:10										N				
CMP2	15:11										N				
CMP3	15:12										N				

Meteorological and environmental conditions						
Wind speed	Wind Directio	Temp	Weather description	Cloud cover	Ground conditions	Baromet ric
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar
2	N	12	Dry/clear	1	Dry	1012

WTP Inspection.		Time:		Flow Meter (M^3):	
System Working	Leaks / Over-topping	Equipment Impacted & Actions Taken to Rectify:			
N/A	N/A	N/A			

Assessors Signature: BC

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	20.09.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	F5, G5					General Notes:		PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:30	N	0		0.0	0.0	N	N	65.6	70.3		N	N		
BMP1	11:05	N	0		0.0	0.0									
BMP1	15:17	N	0		0.0	0.0									
BMP2	08:07	N	0		0.0	0.0	N	N	71.7	79.4		N	N		
BMP2	11:21	N	0		0.0	0.0									
BMP2	15:34	N	0		0.0	0.0									
BMP3	08:08	N	0		0.0	0.0	N	N	61.2	67.9		N	N		
BMP3	11:41	N	0		0.0	0.0									
BMP3	15:57	N	0		0.0	0.0									
BMP4	08:25	N	0		0.0	0.0	N	N	57.1	62.4		N	N		
BMP4	11:58	N	0		0.0	0.0									
BMP4	16:13	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	12:57										N				
CMP2	12:38										N				
CMP3	12:38										N				

Meteorological and environmental conditions						
Wind speed	Wind Directio	Temp	Weather description	Cloud cover	Ground conditions	Barometric
(mph)	(e.g. N, SW)	°C	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar
NW 7		19	Sunny, dry	0	Dry	1025

WTP Inspection.		Time:	—	Flow Meter (M^3):	—
System Working	Leaks / Over-topping	Equipment Impacted & Actions Taken to Rectify:			
—	—	—			

Assessors Signature.....

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	21.09.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	RJC
Daily Activity & Grid Ref.:	F4, G4, G3					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:09	Y	0		0.0	0.0	Y	Y	63.9	67.4		N	N		
BMP1	10:22	N	0		0.0	0.0									
BMP1	14:02	N	0		0.0	0.0									
BMP2	07:26	N	0		0.0	0.0	N	N	68.1	72.5		N	N		
BMP2	10:39	N	0		0.0	0.0									
BMP2	14:20	N	0		0.0	0.0									
BMP3	07:43	N	0		0.0	0.0	N	N	58.3	62.1		N	N		
BMP3	10:56	N	0		0.0	0.0									
BMP3	14:37	N	0		0.0	0.0									
BMP4	08:00	N	0		0.0	0.0	N	N	55.7	59.6		N	N		
BMP4	11:12	N	0		0.0	0.0									
BMP4	14:53	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:12										N				
CMP2	15:13										N				
CMP3	15:14										N				

Meteorological and environmental conditions						
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar
3	S	12	Overcast	7	Dry	1030

WTP Inspection.		Time:	N/A	Flow Meter (M^3):	N/A
System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
N/A	N/A	N/A			

Assessors Signature: [signature]

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	22.09.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	CN
Daily Activity & Grid Ref.:	F5, E6, G5			General Notes:				PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to 5)	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08:16	N	0		0.0	0.0	N	N	72.9	82.7		N	N	→ BMP1 adjacent to generator	
BMP1	11:35	Y	1	Hydrocarbon odour detected next to caravans digt stockpile	0.0	0.0									
BMP1	15:30	Y	1		0.0	0.0									
BMP2	08:33	N	0		0.0	0.0	N	N	65.5	78.7		N	N		
BMP2	11:52	N	0		0.0	0.0									
BMP2	15:48	N	0		0.0	0.0									
BMP3	08:57	N	0		0.0	0.0	N	N	69.2	74.7		N	N		
BMP3	12:10	N	0		0.0	0.0									
BMP3	16:08	N	0		0.0	0.0									
BMP4	09:21	N	0		0.0	0.0	N	N	62.7	73.4		N	N		
BMP4	12:27	N	0		0.0	0.0									
BMP4	16:25	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	13:47										N				
CMP2	13:47										N				
CMP3	13:48										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	—	Flow Meter (M^3):	—
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	°C	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar	—	—	—			
10	SSW	19	Partly Sunny, dry	6	Dry	1027						

Assessors Signature .....

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	23.09.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	F5, F6					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08.50	N	0		0.0	0.0	N	N	73.2	81.4		N	N		
BMP1	11.17	N	0		0.0	0.0									
BMP1	14.58	N	0		0.0	0.0									
BMP2	08.07	N	0		0.0	0.0	N	N	71.3	77.8		N	N		
BMP2	11.35	N	0		0.0	0.0									
BMP2	14.55	N	0		0.0	0.0									
BMP3	08.24	N	0		0.0	0.0	N	N	67.4	73.5		N	N		
BMP3	11.32	N	0		0.0	0.0									
BMP3	15.16	N	0		0.0	0.0									
BMP4	09.65	N	0		0.0	0.0	N	N	65.6	74.7		N	N		
BMP4	12.10	N	0		0.0	0.0									
BMP4	15.57	N	0		0.0	0.0									
EMP1	15.45	Y	1	Hydrocarbon odour	0.0	0.0								* Hydrocarbon odour detected from Carey's Stockpile - no VOCs recorded.	
EMP2	15.10	Y	1		0.0	0.0									
EMP3	15.55	Y	1		0.0	0.0									
EMP4	16.00	Y	1		0.0	0.0									
CMP1	08.52										N				
CMP2	08.53										N				
CMP3	08.37										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	n/a	Flow Meter (M^3):	n/a
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
14	N	15	Drizzle, partly Sunny.	6	Damp	1019	n/a	n/a	n/a			

Assessors Signature.....

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	24.09.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	BW
Daily Activity & Grid Ref.:	F5, F6					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:19	N	0		0.0	0.0	N	N	65.2	69.7		N	N		
BMP1	10:47	N	0		0.0	0.0									
BMP1	15:03	N	0		0.0	0.0									
BMP2	07:37	N	0		0.0	0.0	N	N	69.3	75.7		N	N		
BMP2	11:04	N	0		0.0	0.0									
BMP2	15:20	N	0		0.0	0.0									
BMP3	07:56	N	0		0.0	0.0	N	N	59.1	63.5		N	N		
BMP3	11:25	N	0		0.0	0.0									
BMP3	15:41	N	0		0.0	0.0									
BMP4	08:14	N	0		0.0	0.0	N	N	54.6	60.1		N	N		
BMP4	11:43	N	0		0.0	0.0									
BMP4	16:00	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	16:25										N				
CMP2	16:26										N				
CMP3	16:27										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	n/a	Flow Meter (M^3):	n/a
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
15	W	18	Overcast, dry	7	Dry	1013	n/a	n/a	n/a			

Assessors Signature: [signature]

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	27.09.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	E5					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:23	N	0		0.0	0.0	N	N	73.4	77.9		N	N		
BMP1	11:15	N	0		0.0	0.0									
BMP1	15:05	N	0		0.0	0.0									
BMP2	09:39	N	0		0.0	0.0	N	N	67.2	76.5		N	N		
BMP2	11:32	N	0		0.0	0.0									
BMP2	15:29	N	0		0.0	0.0									
BMP3	07:58	N	0		0.0	0.0	N	N	56.1	61.7		N	N		
BMP3	11:51	N	0		0.0	0.0									
BMP3	15:46	N	0		0.0	0.0									
BMP4	08:14	N	0		0.0	0.0	N	N	54.8	58.3		N	N		
BMP4	12:09	N	0		0.0	0.0									
BMP4	16:02	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	16:27										N				
CMP2	16:23										N				
CMP3	16:28										N				

Meteorological and environmental conditions						
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar
12	WSW	15	Heavy rain, sunny spells.	7	wet	1005

WTP Inspection.		Time:	n/a	Flow Meter (M³):	n/a
System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
n/a	n/a	n/a			

Assessors Signature: C.N

Site:	Project Bradford	Date:	28.09.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	F6, G6					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08:13	Y	0		0.0	0.0	N	N	76.1	82.3		N	N		
BMP1	11:47	Y	0		0.0	0.0									
BMP1	14:13	Y	0		0.0	0.0									
BMP2	08:30	Y	0		0.0	0.0	N	N	75.6	81.7		N	N		
BMP2	12:05	Y	0		0.0	0.0									
BMP2	14:30	Y	0		0.0	0.0									
BMP3	08:49	Y	0		0.0	0.0	N	N	66.8	74.3		N	N		
BMP3	12:25	Y	0		0.0	0.0									
BMP3	14:47	Y	0		0.0	0.0									
BMP4	09:08	Y	0		0.0	0.0	N	N	72.1	79.6		N	N		
BMP4	12:44	Y	0		0.0	0.0									
BMP4	15:04	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:22										N				
CMP2	15:23										N				
CMP3	15:24										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time:	n/a	Flow Meter (M³):	n/a
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:			
9	SSE	12	Showers, overcast	8	Wet	1012	n/a	n/a	n/a			

Assessors Signature.....

Site:	Project Bradford	Date:	29.09.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	F5, F6					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07.51	Y	0		0.0	0.0	N	N	68.2	76.1		N	N		
BMP1	10.47	N	0		0.0	0.0									
BMP1	15:00	N	0		0.0	0.0									
BMP2	08.08	N	0		0.0	0.0	N	N	74.4	79.5		N	N		
BMP2	11:07	N	0		0.0	0.0									
BMP2	15:17	N	0		0.0	0.0									
BMP3	08:27	N	0		0.0	0.0	N	N	71.6	82.3		N	N		
BMP3	11:26	N	0		0.0	0.0									
BMP3	15:35	N	0		0.0	0.0									
BMP4	08:49	N	0		0.0	0.0	N	N	71.5	78.3		N	N		
BMP4	11:48	N	0		0.0	0.0									
BMP4	15:38	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	13:16										N				
CMP2	13:17										N				
CMP3	13:17										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time:	n/a	Flow Meter (M^3):	n/a
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:			
6	SW	12	Partly Sunny, heavy Showers	5	Wet	1020	n/a	n/a	n/a			

Assessors Signature: C.N

Proyecto Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	30.09.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:						General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	09:28	Y	0		0.0	0.0	N	N	67.2	71.7		N	N		
BMP1	10:17	N	0		0.0	0.0									
BMP1	14:57	N	0		0.0	0.0									
BMP2	09:45	N	0		0.0	0.0	N	N	69.3	77.8		N	N		
BMP2	10:34	N	0		0.0	0.0									
BMP2	14:55	N	0		0.0	0.0									
BMP3	08:06	N	0		0.0	0.0	N	N	67.1	75.3		N	N		
BMP3	10:56	N	0		0.0	0.0									
BMP3	15:16	N	0		0.0	0.0									
BMP4	08:23	N	0		0.0	0.0	N	N	72.5	79.1		N	N		
BMP4	11:17	N	0		0.0	0.0									
BMP4	15:35	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	14:12										N				
CMP2	14:13										N				
CMP3	14:13										N				

Meteorological and environmental conditions						
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar
14	SW	14	Overcast, rain	8	Wet	1013

WTP Inspection.		Time:	n/a	Flow Meter (M^3):	n/a
System Working (Y/N)	Leaks / Over topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
n/a	n/a	n/a			

Assessors Signature.....

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	01.10.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	BC
Daily Activity & Grid Ref.:	C4					General Notes:			

PID Bump Test: ✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:11	2	0		0.0	0.0	2	2	62.7	68.5		2	2		
BMP1	10:53	2	0		0.0	0.0									
BMP1	14:05	2	0		0.0	0.0									
BMP2	07:28	2	0		0.0	0.0	2	2	66.3	71.9		2	2		
BMP2	11:10	2	0		0.0	0.0									
BMP2	14:22	2	0		0.0	0.0									
BMP3	07:45	2	0		0.0	0.0	2	2	57.4	68.1		2	2		
BMP3	11:27	2	0		0.0	0.0									
BMP3	14:39	2	0		0.0	0.0									
BMP4	08:02	2	0		0.0	0.0	2	2	55.2	59.6		2	2		
BMP4	11:44	2	0		0.0	0.0									
BMP4	15:02				0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:20										2				
CMP2	15:21										2				
CMP3	15:22										2				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time:	N/A	Flow Meter (M^3):	N/A
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:			
12	SSW	13	overcast/sunny	5	wet	1004	N/A	N/A	N/A			

Assessors Signature: 

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	04.10.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	G4					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:54	N	0		0.0	0.0	N	N	68.3	76.7		N	N		
BMP1	11:26	N	0		0.0	0.0									
BMP1	15:07	N	0		0.0	0.0									
BMP2	07:52	N	0		0.0	0.0	N	N	74.8	80.1		N	N		
BMP2	11:45	N	0		0.0	0.0									
BMP2	15:25	N	0		0.0	0.0									
BMP3	08:12	N	0		0.0	0.0	N	N	67.3	79.6		N	N		
BMP3	12:05	N	0		0.0	0.0									
BMP3	15:46	N	0		0.0	0.0									
BMP4	08:39	N	0		0.0	0.0	N	N	72.3	81.2		N	N		
BMP4	12:24	N	0		0.0	0.0									
BMP4	16:03	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	16:27										N				
CMP2	16:28										N				
CMP3	16:29										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time:	n/a	Flow Meter (M³):	n/a
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:			
6	SSW	10	Overcast, light Showers	7	Wet	1005	n/a	n/a	n/a			

Assessors Signature.....

Project Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	05.10.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	G4					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:20	Y	0		0.0	0.0	N	N	63.5	70.2		N	N		
BMP1	10:53	N	0		0.0	0.0									
BMP1	14:01	N	0		0.0	0.0									
BMP2	07:37	N	0		0.0	0.0									
BMP2	10:56	N	0		0.0	0.0	N	N	66.7	72.9		N	N		
BMP2	14:18	N	0		0.0	0.0									
BMP3	07:54	N	0		0.0	0.0									
BMP3	11:07	N	0		0.0	0.0	N	N	58.3	62.8		N	N		
BMP3	14:35	N	0		0.0	0.0									
BMP4	08:11	N	0		0.0	0.0									
BMP4	11:24	N	0		0.0	0.0	N	N	55.6	60.6		N	N		
BMP4	14:54	N	0		0.0	0.0									
EMP1					0.0	0.0									
EMP2															
EMP3															
EMP4															
CMP1	15:10										N				
CMP2	15:11										N				
CMP3	15:12										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar
8	NNW	10	Heavy rain	8	Wet	996

WTP Inspection.

Systems Working (Y/N)	Leaks / Over-topping (Y/N)
n/a	n/a

Time: n/a

Flow Meter (M^3): n/a

Equipment Impacted & Actions Taken to Rectify:

n/a

Assessors Signature.....

Provect: vironmental Monitoring Form 101114

Site:	Project Bradford	Date:	06.10.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	RW
Daily Activity & Grid Ref.:	B3, C3					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:03	Y	0		0.0	0.0	Y	Y	62.4	67.3		Y	Y		
BMP1	11:04	Y	0		0.0	0.0									
BMP1	14:12	Y	0		0.0	0.0									
BMP2	07:25	Y	0		0.0	0.0	Y	Y	66.2	71.8		Y	Y		
BMP2	11:21	Y	0		0.0	0.0									
BMP2	14:29	Y	0		0.0	0.0									
BMP3	07:42	Y	0		0.0	0.0	Y	Y	58.5	61.9		Y	Y		
BMP3	11:38	Y	0		0.0	0.0									
BMP3	14:46	Y	0		0.0	0.0									
BMP4	07:59	Y	0		0.0	0.0	Y	Y	56.7	60.4		Y	Y		
BMP4	11:55	Y	0		0.0	0.0									
BMP4	15:08	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:20										Y				
CMP2	15:21										Y				
CMP3	15:22										Y				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar
10	E	13	light cloud	4	wet	1020

WTP Inspection.

System Working (Y/N)	Leaks / Over-topping (Y/N)	Time:	N/A	Flow Meter (M^3):	N/A
N/A	N/A	Equipment Impacted & Actions Taken to Rectify:		N/A	

Assessors Signature: [signature]

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	07.10.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	B4					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
		(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:18	Y	0		0.0	0.0	N	N	67.2	71.5		Y	N		
BMP1	10:23	Y	0		0.0	0.0									
BMP1	14:02	Y	0		0.0	0.0									
BMP2	07:35	Y	0		0.0	0.0	N	N	69.8	74.1		Y	N		
BMP2	10:40	Y	0		0.0	0.0									
BMP2	14:19	Y	0		0.0	0.0									
BMP3	07:52	Y	0		0.0	0.0	N	N	57.7	62.6		Y	N		
BMP3	10:57	Y	0		0.0	0.0									
BMP3	14:36	Y	0		0.0	0.0									
BMP4	08:09	Y	0		0.0	0.0	N	N	55.4	60.9		Y	N		
BMP4	11:15	Y	0		0.0	0.0									
BMP4	14:53	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:15										Y				
CMP2	15:16										Y				
CMP3	15:17										Y				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time:	Flow Meter (M^3):
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar	n/a	n/a	n/a	n/a

Partly cloudy Sunny Spells

Equipment Impacted & Actions Taken to Rectify: n/a

Assessors Signature .....

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	08.10.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	B4							General Notes:	

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:27	N	0		0.0	0.0	N	N	62.1	69.7		N	N		
BMP1	11:05	N	0		0.0	0.0									
BMP1	14:04	N	0		0.0	0.0									
BMP2	07:46	N	0		0.0	0.0	N	N	70.3	75.6		N	N		
BMP2	11:27	N	0		0.0	0.0									
BMP2	14:21	N	0		0.0	0.0									
BMP3	08:05	N	0		0.0	0.0	N	N	54.6	57.1		N	N		
BMP3	11:42	N	0		0.0	0.0									
BMP3	14:40	N	0		0.0	0.0									
BMP4	08:24	N	0		0.0	0.0	N	N	65.9	77.4		N	N		
BMP4	12:00	N	0		0.0	0.0									
BMP4	15:01	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	13:43										N				
CMP2	13:44										N				
CMP3	13:44										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	n/a	Flow Meter (M^3):	n/a
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
4	SSW	19	Sunny, partly cloudy.	4	Dry	1029	n/a	n/a	n/a			

Assessors Signature .....

Proyectiv Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	11.10.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	B3							General Notes:	

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	PID Bump Test: ✓
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	09:28	N	0		0.0	0.0	N	N	73.5	81.3		N	N		
BMP1	10:37	N	0		0.0	0.0									
BMP1	15:02	N	0		0.0	0.0									
BMP2	09:44	N	0		0.0	0.0	N	N	74.9	83.1		N	N		
BMP2	10:54	N	0		0.0	0.0									
BMP2	15:19	N	0		0.0	0.0									
BMP3	08:05	N	0		0.0	0.0	N	N	60.4	64.8		N	N		
BMP3	11:15	N	0		0.0	0.0									
BMP3	15:39	N	0		0.0	0.0									
BMP4	08:23	N	0		0.0	0.0	N	N	63.1	74.5		N	N		
BMP4	11:35	N	0		0.0	0.0									
BMP4	15:47	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:38										N				
CMP2	15:54										N				
CMP3	15:54										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	n/a	Flow Meter (M^3):	n/a
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
2	W	15	Sunny, partly cloudy.	2	Dry	1031	n/a	n/a	n/a			

Assessors Signature.....

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	12.10.21	Contract Ref:	101114	Client:	8AM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	B3							General Notes:	

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	PID Bump Test: ✓
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:14	N	0		0.0	0.0	N	N	60.3	70.5		N	N		
BMP1	11:05	N	0		0.0	0.0									
BMP1	16:31	N	0		0.0	0.0									
BMP2	07:36	N	0		0.0	0.0	N	N	67.2	74.1		N	N		
BMP2	11:22	N	0		0.0	0.0									
BMP2	15:03	N	0		0.0	0.0									
BMP3	07:54	N	0		0.0	0.0	N	N	56.7	60.8		N	N		
BMP3	11:40	N	0		0.0	0.0									
BMP3	15:27	N	0		0.0	0.0									
BMP4	08:12	N	0		0.0	0.0	N	N	61.4	66.7		N	N		
BMP4	11:58	N	0		0.0	0.0									
BMP4	15:46	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	16:09										N				
CMP2	16:08										N				
CMP3	16:04										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time:	n/a	Flow Meter (M^3):	n/a
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:			
7	NW	14	Drizzle, overcast	8	Wet	1025	n/a	n/a	n/a			

Assessors Signature .....

Project: Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	13.10.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	F1, F2, G2							General Notes:	

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	PID Bump Test: ✓
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	08:10	N	0		0.0	0.0	N	N	67.9	78.8		N	N		
BMP1	11:55	N	0		0.0	0.0									
BMP1	15:08	N	0		0.0	0.0									
BMP2	08:27	N	0		0.0	0.0	N	N	62.1	78.2		N	N		
BMP2	12:11	N	0		0.0	0.0									
BMP2	15:26	N	0		0.0	0.0									
BMP3	08:48	N	0		0.0	0.0	N	N	61.3	77.4		N	N		
BMP3	12:29	N	0		0.0	0.0									
BMP3	15:44	N	0		0.0	0.0									
BMP4	09:06	N	0		0.0	0.0	N	N	71.7	79.2		N	N		
BMP4	12:47	N	0		0.0	0.0									
BMP4	16:03	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	16:12										N				
CMP2	16:12										N				
CMP3	16:13										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time:	Flow Meter (M³):
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar				
3	W	12	Overcast, drizzle	8	Wet	1027	n/a	n/a	n/a	n/a

Equipment Impacted & Actions Taken to Rectify:

n/a

Assessors Signature.....

Proyecty... Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	14.10.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	F1, F2, G2							General Notes:	

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:31	N	0		0.0	0.0	N	N	63.7	73.9		N	N		
BMP1	10:53	N	0		0.0	0.0									
BMP1	15:12	N	0		0.0	0.0									
BMP2	07:47	N	0		0.0	0.0	N	N	67.2	74.3		N	N		
BMP2	11:10	N	0		0.0	0.0									
BMP2	15:28	N	0		0.0	0.0									
BMP3	08:06	N	0		0.0	0.0	N	N	52.8	59.3		N	N		
BMP3	11:29	N	0		0.0	0.0									
BMP3	15:46	N	0		0.0	0.0									
BMP4	08:25	N	0		0.0	0.0	N	N	64.6	71.5		N	N		
BMP4	11:18	N	0		0.0	0.0									
BMP4	16:04	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	13:52										N				
CMP2	13:53										N				
CMP3	13:53										N				

PID Bump Test: ✓

Meteorological and environmental conditions							WTP Inspection.		Time:	n/a	Flow Meter (M^3):	n/a
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
8	WSW	13	Overcast, dry	8	Wet	1021	n/a	n/a	n/a			

Assessors Signature: ...

Proyecto Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	15.10.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	F1, F2							General Notes:	

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	PID Bump Test: ✓
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:45	N	0		0.0	0.0	N	Y	64.3	77.2		N	N		
BMP1	11:12	N	0		0.0	0.0									
BMP1	14:43	N	0		0.0	0.0									
BMP2	08:02	N	0		0.0	0.0									
BMP2	11:30	N	0		0.0	0.0	N	Y	66.7	80.1		N	N		
BMP2	15:00	N	0		0.0	0.0									
BMP3	08:21	N	0		0.0	0.0									
BMP3	11:49	N	0		0.0	0.0	N	Y	62.4	79.6		N	N		
BMP3	15:18	N	0		0.0	0.0									
BMP4	08:39	N	0		0.0	0.0									
BMP4	12:17	N	0		0.0	0.0	N	Y	70.2	81.5		N	N		
BMP4	15:36	N	0		0.0	0.0									
EMP1					0.0	0.0									
EMP2															
EMP3															
EMP4															
CMP1	15:54										N				
CMP2	15:55										N				
CMP3	15:55										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	n/a	Flow Meter (M^3):	n/a
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
5	NE	12	Sunny, dry	0	Wet	1022	n/a	n/a	n/a			

Assessors Signature: CN

Proyecta Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	18.10.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	RC
Daily Activity & Grid Ref.:	B3					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:15	Y	0		0.0	0.0	Y	Y	62.7	69.5		N	N		
BMP1	10:51	Y	0		0.0	0.0									
BMP1	14:00	Y	0		0.0	0.0									
BMP2	07:30	Y	0		0.0	0.0	Y	Y	64.2	71.8		N	N		
BMP2	11:08	Y	0		0.0	0.0									
BMP2	14:17	Y	0		0.0	0.0									
BMP3	07:47	Y	0		0.0	0.0	Y	Y	55.3	60.4		N	N		
BMP3	11:25	Y	0		0.0	0.0									
BMP3	14:25	Y	0		0.0	0.0									
BMP4	08:04	Y	0		0.0	0.0	N	N	52.5	58.6		N	N		
BMP4	11:42	N	0		0.0	0.0									
BMP4	14:43	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4	15:01														
CMP1	15:02										N				
CMP2	15:03										N				
CMP3											N				

Meteorological and environmental conditions							WTP Inspection.		Time:	N/A	Flow Meter (M^3):	N/A
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar	N/A	N/A	N/A			
4	N	11	overcast	7	wet	1013						

Assessors Signature: [signature]

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	19.10.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	RJ
Daily Activity & Grid Ref.:						General Notes:		PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:18	2	0		0.0	0.0	2	2	63.6	66.8		2	2		
BMP1	11:02	2	0		0.0	0.0									
BMP1	14:15	2	0		0.0	0.0									
BMP2	07:35	2	0		0.0	0.0	2	2	65.9	72.3		2	2		
BMP2	11:20	2	0		0.0	0.0									
BMP2	14:32	2	0		0.0	0.0									
BMP3	07:52	2	0		0.0	0.0	2	2	57.1	60.8		2	2		
BMP3	11:37	2	0		0.0	0.0									
BMP3	14:49	2	0		0.0	0.0									
BMP4	08:09	2	0		0.0	0.0	2	2	55.7	58.5		2	2		
BMP4	11:55	2	0		0.0	0.0									
BMP4	15:06	2	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:25										2				
CMP2	15:26										2				
CMP3	15:27										2				

Meteorological and environmental conditions						
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar
7	S	15	Rain	8	wet	1007

WTP Inspection.		Time:	2/A	Flow Meter (M³):	2/A
System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
2/A	2/A	2/A			

Assessors Signature: E Dalley

Provectu vironmental Monitoring Form 101114

Site:	Project Bradford	Date:	20.10.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	BG
Daily Activity & Grid Ref.:	F6, E6					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:10	2	0		0.0	0.0	2	2	65.3	70.1		2	2		
BMP1	10:37	2	0		0.0	0.0									
BMP1	15:03	2	0		0.0	0.0									
BMP2	07:27	2	0		0.0	0.0	2	2	67.8	73.5		2	2		
BMP2	10:53	2	0		0.0	0.0									
BMP2	15:19	2	0		0.0	0.0									
BMP3	07:45	2	0		0.0	0.0	2	2	66.9	69.2		2	2		
BMP3	11:11	2	0		0.0	0.0									
BMP3	15:38	2	0		0.0	0.0									
BMP4	08:03	2	0		0.0	0.0	2	2	54.5	57.6		2	2		
BMP4	11:29	2	0		0.0	0.0									
BMP4	16:00	2	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	16:14										2				
CMP2	16:15										2				
CMP3	16:15										2				

Meteorological and environmental conditions						
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar
3	S	11	Overcast	7	wet	998

WTP Inspection.		Time:	21A	Flow Meter (M^3):	21A
System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
21A	21A	21A			

Assessors Signature.....

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	21.10.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	F6, G6.					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:57	N	0		0.0	0.0	N	N	64.6	75.7		N	N		
BMP1	10:55	N	0		0.0	0.0									
BMP1	15:02	N	0		0.0	0.0									
BMP2	07:53	N	0		0.0	0.0	N	N	65.9	78.1		N	N		
BMP2	11:11	N	0		0.0	0.0									
BMP2	15:18	N	0		0.0	0.0									
BMP3	08:10	N	6		0.0	0.0	N	N	73.5	80.1		N	N		
BMP3	11:29	N	0		0.0	0.0									
BMP3	15:36	N	0		0.0	0.0									
BMP4	08:27	N	0		0.0	0.0	N	N	75.6	81.8		N	N		
BMP4	11:47	N	0		0.0	0.0									
BMP4	15:54	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	16:09										N				
CMP2	16:11										N				
CMP3	16:11										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time:	n/a	Flow Meter (M^3):	n/a
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:			
12	NW	10	Overcast, showers	8	Wet	1009	n/a	n/a	n/a			

Assessors Signature.....

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	22.10.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	F2, E6					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07.21	Y	0		0.0	0.0	N	N	64.2	77.8		N	N		
BMP1	11.19	Y	0		0.0	0.0									
BMP1	15.20	Y	0		0.0	0.0									
BMP2	09.34	Y	0		0.0	0.0	N	N	62.3	73.9		N	N		
BMP2	11.35	Y	0		0.0	0.0									
BMP2	15.35	Y	0		0.0	0.0									
BMP3	07.56	Y	0		0.0	0.0	N	N	55.6	62.1		N	N		
BMP3	11.54	Y	0		0.0	0.0									
BMP3	15.53	Y	0		0.0	0.0									
BMP4	08.13	Y	0		0.0	0.0	N	N	62.7	71.5		N	N		
BMP4	12.13	Y	0		0.0	0.0									
BMP4	16.10	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	13.42										Y				
CMP2	13.43										Y				
CMP3	13.43										N				

Meteorological and environmental conditions						
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure
(mph)	(e.g. N, SW)		(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar
11	NW	12	Partly Sunny, Showers	6	Wet	1019

WTP Inspection.		Time:	n/a	Flow Meter (M^3):	n/a
System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
n/a	n/a	n/a			

Assessors Signature.....

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	25.10.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C-N
Daily Activity & Grid Ref.:	F2, E6							General Notes:	

PID Bump Test: ✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	09:46	N	0		0.0	0.0	N	N	61.2	69.7		N	N		
BMP1	11:07	N	0		0.0	0.0									
BMP1	14:48	N	0		0.0	0.0									
BMP2	08:02	N	0		0.0	0.0	N	N	63.5	72.4		N	N		
BMP2	11:19	N	0		0.0	0.0									
BMP2	15:04	N	0		0.0	0.0									
BMP3	08:20	N	0		0.0	0.0	N	N	73.4	80.2		N	N		
BMP3	11:39	N	0		0.0	0.0									
BMP3	15:22	N	0		0.0	0.0									
BMP4	08:38	N	0		0.0	0.0	N	N	75.6	81.7		N	N		
BMP4	11:58	N	0		0.0	0.0									
BMP4	15:40	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	16:04										N				
CMP2	16:05										N				
CMP3	16:05										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time:	nla	Flow Meter (M^3):	nla
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:			
9	N	13	Sunny, occasional drizzle	3	Wet	1012	nla	nla	nla			

Assessors Signature.....

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	26.10.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	E6, F6, F2.					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07.10	N	0		0.0	0.0	N	N	62.7	71.2		N	N		
BMP1	11:18	N	0		0.0	0.0									
BMP1	15:01	N	0		0.0	0.0									
BMP2	07:27	N	0		0.0	0.0	N	N	61.2	68.3		N	N		
BMP2	11:34	N	0		0.0	0.0									
BMP2	15:17	N	0		0.0	0.0									
BMP3	07:48	N	0		0.0	0.0	N	N	56.4	59.1		N	N		
BMP3	11:53	N	0		0.0	0.0									
BMP3	15:35	N	0		0.0	0.0									
BMP4	08:06	N	0		0.0	0.0	N	N	58.3	63.5		N	N		
BMP4	12:12	N	0		0.0	0.0									
BMP4	15:53	N	0		0.0	0.0									
EMP1					0.0	0.0									
EMP2															
EMP3															
EMP4															
CMP1	16:01										N				
CMP2	16:01										N				
CMP3	16:02										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time:	n/a	Flow Meter (M^3):	n/a
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:			
10	SSW	16	Overcast, drizzle	7	Wet	1013	n/a	n/a	n/a			

Assessors Signature C.N

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	27.10.22	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	F6, E6					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:15	N	0		0.0	0.0	N	N	63.1	78.5		N	N		
BMP1	10:18	N	0		0.0	0.0									
BMP1	14:37	N	0		0.0	0.0									
BMP2	07:32	N	0		0.0	0.0	N	N	60.4	75.2		N	N		
BMP2	11:05	N	0		0.0	0.0									
BMP2	14:54	N	0		0.0	0.0									
BMP3	07:51	N	0		0.0	0.0	N	N	59.2	63.7		N	N		
BMP3	11:25	N	0		0.0	0.0									
BMP3	15:13	N	0		0.0	0.0									
BMP4	08:08	N	0		0.0	0.0	N	N	65.9	78.2		N	N		
BMP4	11:43	N	0		0.0	0.0									
BMP4	15:33	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	13:15										N				
CMP2	13:16										N				
CMP3	13:16										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	n/a	Flow Meter (M^3):	n/a
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
15	SW	16	Partly cloudy, sunny & dry.	3	Wet	1011	n/a	n/a	n/a			

Assessors Signature.....

Prevecty... Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	28.10.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	G6, F6, E6,					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:20	N	0		0.0	0.0	N	N	63.2	79.4		N	N		
BMP1	11:03	N	0		0.0	0.0									
BMP1	15:05	N	0		0.0	0.0									
BMP2	07:36	N	0		0.0	0.0	N	N	65.7	78.2		N	N		
BMP2	11:19	N	0		0.0	0.0									
BMP2	15:22	N	0		0.0	0.0									
BMP3	07:35	N	0		0.0	0.0	N	N	53.8	58.2		N	N		
BMP3	11:37	N	0		0.0	0.0									
BMP3	15:39	N	0		0.0	0.0									
BMP4	08:13	N	0		0.0	0.0	N	N	67.9	76.3		N	N		
BMP4	11:56	N	0		0.0	0.0									
BMP4	15:58	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	13:47										N				
CMP2	13:49										N				
CMP3	13:48										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure
(mph)	(e.g. N, SW)	°C	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar
13	S	16	cloud, patchy sunny, dry - some showers	3	Dry	1001

WTP Inspection.

Time:	n/a	Flow Meter (M^3):	n/a

System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:
n/a	n/a	n/a

Assessors Signature: CN

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	29.10.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	G6, F6, E6					General Notes:		PID Bump Test:	

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:14	N	0		0.0	0.0	N	N	65.7	77.7		N	N		
BMP1	11:33	N	0		0.0	0.0									
BMP1	15:15	N	0		0.0	0.0									
BMP2	07:30	N	0		0.0	0.0	N	N	69.3	77.1		N	N		
BMP2	11:50	N	0		0.0	0.0									
BMP2	15:31	N	0		0.0	0.0									
BMP3	07:48	N	0		0.0	0.0	N	N	56.2	60.3		N	N		
BMP3	12:09	N	0		0.0	0.0									
BMP3	15:49	N	0		0.0	0.0									
BMP4	08:06	N	0		0.0	0.0	N	N	62.4	68.7		N	N		
BMP4	12:27	N	0		0.0	0.0									
BMP4	16:07	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	13:19										N				
CMP2	13:20										N				
CMP3	13:24										N				

Meteorological and environmental conditions							WTP Inspection.		Time:	n/a	Flow Meter (M³):	n/a
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
16	SW	11	Partly Sunny, Heavy Showers	7	Wet	991	n/a	n/a	n/a			

Assessors Signature.....

Proactive Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	05.11.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	RC
Daily Activity & Grid Ref.:	G7, F7, E7					General Notes:		PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: WP or Grid Ref.	Time Start	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampler	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:18	Y	0		0.0	0.0	N	N	65.1	67.8		Y	N		
BMP1	10:33	Y	0		0.0	0.0									
BMP1	14:06	Y	0		0.0	0.0									
BMP2	07:30	Y	0		0.0	0.0	N	N	65.9	70.4		Y	N		
BMP2	10:50	Y	0		0.0	0.0									
BMP2	14:23	Y	0		0.0	0.0									
BMP3	07:47	Y	0		0.0	0.0	N	N	58.6	62.3		Y	N		
BMP3	11:07	Y	0		0.0	0.0									
BMP3	14:42	Y	0		0.0	0.0									
BMP4	08:04	Y	0		0.0	0.0	N	N	65.1	60.7		Y	N		
BMP4	11:34	Y	0		0.0	0.0									
BMP4	15:03	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:25										Y				
CMP2	15:26										Y				
CMP3	15:27										Y				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar
1	N	0	Fog	8	wet	1025

WTP Inspection.

System Working (Y/N)	Leaks / Over-topping (Y/N)
Y	Y

Time: N/A

Flow Meter (M^3): N/A

Equipment Impacted & Actions Taken to Rectify:

N/A

Assessors Signature: [signature]

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	04.11.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	EC
Daily Activity & Grid Ref.:	G7					General Notes:		PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Tribbee Sample	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Peels	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:15	Y	0		0.0	0.0	N	N	59.9	63.5		Y	Y		
BMP1	11:02	Y	0		0.0	0.0									
BMP1	14:07	Y	0		0.0	0.0									
BMP2	07:30	Y	0		0.0	0.0	N	N	65.8	70.1		Y	Y		
BMP2	11:19	Y	0		0.0	0.0									
BMP2	14:24	Y	0		0.0	0.0									
BMP3	07:52	Y	0		0.0	0.0	N	N	59.1	62.6		Y	Y		
BMP3	11:36	Y	0		0.0	0.0									
BMP3	14:41	Y	0		0.0	0.0									
BMP4	08:09	Y	0		0.0	0.0	N	N	55.8	59.1		Y	Y		
BMP4	11:53	Y	0		0.0	0.0									
BMP4	14:58	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:19										Y				
CMP2	15:20										Y				
CMP3	15:21										Y				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Overtopping (Y/N)	Time:	N/A	Flow Meter (M³):	N/A
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:			
7	N/W	4	Sun	3	Wet	1017	Y	Y	N/A			

Assessors Signature: [signature]

Prevextus Environmental Monitoring Form 181114

Site:	Project Bradford	Date:	03.11.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	BW
Daily Activity & Grid Ref.:	G7					General Notes:			PID Bump Test: ✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	Detectability (Y/N)	Intensity (1 to 6)	Quality (Description)	Average PID Reading (ppm)	Peak PID Reading (ppm)	Visual Y/N	Frisbee Sample Y/N	Average Reading (dBa)	Peak Reading (dBa)	Visible Impacts from Site Run-off Y/N	Litter (Y/N)	Pests (Y/N)	(Description)	(Description)
BMP1	07:35	Y	0		0.0	0.0	Y	Y	60.9	64.5		N	Y		
BMP1	10:51	Y	0		0.0	0.0									
BMP1	14:01	Y	0		0.0	0.0									
BMP2	07:30	Y	0		0.0	0.0	Y	Y	65.1	68.6		N	Y		
BMP2	11:08	Y	0		0.0	0.0									
BMP2	14:18	Y	0		0.0	0.0									
BMP3	07:47	Y	0		0.0	0.0	Y	Y	55.2	59.5		N	Y		
BMP3	11:25	Y	0		0.0	0.0									
BMP3	14:35	Y	0		0.0	0.0									
BMP4	08:04	Y	0		0.0	0.0	Y	Y	54.4	57.7		N	Y		
BMP4	11:42	Y	0		0.0	0.0									
BMP4	14:54	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:20										Y				
CMP2	15:21										Y				
CMP3	15:22										Y				

Meteorological and environmental conditions

Wind speed (mph)	Wind Direction (e.g. N, SW)	Temp (°C)	Weather description (e.g. rain, sun, wet, dry)	Cloud cover (0 to 8)	Ground conditions (e.g. wet, dry)	Barometric Pressure mbar
6	N	6	Overcast	7	Wet	1006

WTP Inspection.

Time:	N/A	Flow Meter (M^3):	N/A

System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:
Y	N	N/A

Assessors Signature: [signature]

Proyecta Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	02.11.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	GG
Daily Activity & Grid Ref.:	GG					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
		(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:18	Y	0		0.0	0.0	Y	N	62.4	69.5		N	N		
BMP1	11:01	Y	0		0.0	0.0									
BMP1	14:57	Y	0		0.0	0.0									
BMP2	07:35	Y	0		0.0	0.0	Y	N	65.7	71.1		N	N		
BMP2	11:18	Y	0		0.0	0.0									
BMP2	14:39	Y	0		0.0	0.0									
BMP3	07:54	Y	0		0.0	0.0	Y	N	56.2	60.9		N	N		
BMP3	11:35	Y	0		0.0	0.0									
BMP3	14:41	Y	0		0.0	0.0									
BMP4	08:01	Y	0		0.0	0.0	Y	N	54.8	58.3		N	N		
BMP4	11:52	Y	0		0.0	0.0									
BMP4	14:58	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:20										Y				
CMP2	15:21										Y				
CMP3	15:22										Y				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection, System Working (Y/N)	WTP Inspection, Leaks / Over-topping (Y/N)	Time:	N/A	Flow Meter (M³):	N/A
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar	N/A	N/A	Equipment Impacted & Actions Taken to Rectify:			
4	S	4	Partly Sunny	6	Dry	997			N/A			

Assessors Signature: GG

Proventia Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	01.11.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	C.N
Daily Activity & Grid Ref.:	C6, C7							General Notes:	

PID Bump Test: ✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Tribbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	09:11	2	0		0.0	0.0	2	2	65.1	67.5		2	2		
BMP1	10:53	2	0		0.0	0.0									
BMP1	12:17	2	0		0.0	0.0									
BMP2	07:23	2	0		0.0	0.0	2	2	65.2	71.9		2	2		
BMP2	11:40	2	0		0.0	0.0									
BMP2	14:34	2	0		0.0	0.0									
BMP3	07:46	2	0		0.0	0.0	2	2	58.6	62.7		2	2		
BMP3	11:27	2	0		0.0	0.0									
BMP3	14:51	2	0		0.0	0.0									
BMP4	08:02	2	0		0.0	0.0	2	2	54.5	59.3		2	2		
BMP4	11:44	2	0		0.0	0.0									
BMP4	15:08	2	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:45										2				
CMP2	15:26										2				
CMP3	15:21										2				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time:	n/a	Flow Meter (M^3):	n/a
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:			
18	SW	7	Rain	8	wet	987	n/a	n/a	n/a			

Assessors Signature: CN

Prevectas Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	12.1.24	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	CN
Daily Activity & Grid Ref.:	G7, F7, E7					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sample	Average Reading	Peak Reading	Visible impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to 5)	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	9:36	N	0		0.0	0.0	N	Y	69.3	78.2		N	N		
BMP1	10:45	N	0		0.0	0.0									
BMP1	13:07	N	0		0.0	0.0									
BMP2	9:52	N	0		0.0	0.0	N	Y	67.7	79.3		N	N		
BMP2	11:0	N	0		0.0	0.0									
BMP2	15:25	N	0		0.0	0.0									
BMP3	10:10	N	0		0.0	0.0	N	Y	60.4	66.7		N	N		
BMP3	11:20	N	0		0.0	0.0									
BMP3	15:41	N	0		0.0	0.0									
BMP4	8:25	N	0		0.0	0.0	N	Y	70.1	90.5		N	N		
BMP4	11:40	N	0		0.0	0.0									
BMP4	16:03	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1															
CMP2															
CMP3															

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time:	n/a	Flow Meter (M^3):	n/a
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Inspected & Actions Taken to Rectify:			
13	SW	13	Partly Sunny, showers	6	Wet	1003	n/a	n/a	n/a			

Assessors Signature: CN

Preventex Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	11.10.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	C.N
Daily Activity & Grid Ref.:	G7, F7, E7					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time: Start	ODOUR: Detectability (Y/N)	ODOUR: Intensity (1 to)	ODOUR: Quality (Description)	VOC: Average PID Reading (ppm)	VOC: Peak PID Reading (ppm)	DUST: Visual Y/N	DUST: Fribbee Sample Y/N	NOISE: Average Reading (dBa)	NOISE: Peak Reading (dBa)	CANAL: Visible Impacts from Site Run-off Y/N	HOUSEKEEPING: Litter (Y/N)	HOUSEKEEPING: Pests (Y/N)	COMMENTS (Description)	COMPLAINTS RECEIVED / ACTIONS REQUIRED (Description)
BMP1	07:23	N	0		0.0	0.0	N	N	64.3	71.4		N	N		
BMP1	11:07	N	0		0.0	0.0									
BMP1	15:10	N	0		0.0	0.0									
BMP2	07:39	N	0		0.0	0.0	N	N	65.7	73.9		N	N		
BMP2	11:24	N	0		0.0	0.0									
BMP2	15:26	N	0		0.0	0.0									
BMP3	08:00	N	0		0.0	0.0	N	N	59.8	75.2		N	N		
BMP3	11:39	N	0		0.0	0.0									
BMP3	15:43	N	0		0.0	0.0									
BMP4	08:18	N	0		0.0	0.0	N	N	67.7	76.2		N	N		
BMP4	12:20	N	0		0.0	0.0									
BMP4	16:01	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	16:23										N				
CMP2	16:24										N				
CMP3	16:24										N				

Meteorological and environmental conditions

Wind speed (mph)	Wind Direction (e.g. N, SW)	Temp (°C)	Weather description (e.g. rain, sun, wet, dry)	Cloud cover (0 to 8)	Ground conditions (e.g. wet, dry)	Barometric Pressure mbar	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)
5	S	12	Partly Sunny	5	Wet	1021	n/a	n/a

Time: n/a

Flow Meter (M³): n/a

Equipment Impacted & Actions Taken to Rectify:

n/a

Assessors Signature: [signature]

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	10.11.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	CN
Daily Activity & Grid Ref.:	G7, F7, E7					General Notes:			PID Bump Test: ✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sample	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
		(Y/N)	(1 to)	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:50	N	0		0.0	0.0	N	N	66.4	70.1		N	N		
BMP1	10:38	N	0		0.0	0.0									
BMP1	14:42	N	0		0.0	0.0									
BMP2	07:46	N	0		0.0	0.0	N	N	63.7	73.1		N	N		
BMP2	10:52	N	0		0.0	0.0									
BMP2	14:58	N	0		0.0	0.0									
BMP3	08:05	N	0		0.0	0.0	N	N	58.5	65.3		N	N		
BMP3	11:13	N	0		0.0	0.0									
BMP3	15:16	N	0		0.0	0.0									
BMP4	08:21	N	0		0.0	0.0	N	N	67.1	75.4		N	N		
BMP4	11:32	N	0		0.0	0.0									
BMP4	15:35	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	16:03										N				
CMP2	16:04										N				
CMP3	16:04										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar
3	SW	13	Overcast, drizzle	8	Wet	1023

WTP Inspection.

System Working (Y/N)	Leaks / Overtopping (Y/N)
n/a	n/a

Time: n/a

Flow Meter (M^3): n/a

Equipment Inspected & Actions Taken to Rectify:

n/a

Assessors Signature: [signature]

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	09.11.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	BL
Daily Activity & Grid Ref.:	G7, G7, E7					General Notes:		PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CAMAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sample	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Peels	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:45	Y	0		0.0	0.0	Y	Y	65.5	69.1		Y	Y		
BMP1	10:53	Y	0		0.0	0.0									
BMP1	14:04	Y	0		0.0	0.0									
BMP2	07:52	Y	0		0.0	0.0	Y	Y	66.7	72.6		Y	Y		
BMP2	11:10	Y	0		0.0	0.0									
BMP2	14:21	Y	0		0.0	0.0									
BMP3	07:48	Y	0		0.0	0.0	Y	Y	57.8	60.5		Y	Y		
BMP3	11:27	Y	0		0.0	0.0									
BMP3	14:38	Y	0		0.0	0.0									
BMP4	08:06	Y	0		0.0	0.0	Y	Y	55.4	59.2		Y	Y		
BMP4	11:44	Y	0		0.0	0.0									
BMP4	14:55	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:14										Y				
CMP2	15:15										Y				
CMP3	15:16										Y				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time: N/A	Flow Meter (M^3): N/A
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
7	SSW	12	Sun	2	Dry	1019	Y	Y	N/A	

Assessors Signature: [signature]

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	08.11.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	BC
Daily Activity & Grid Ref.:	C7, C7, E7					General Notes:		PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time: Start	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sample	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Posts	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		(Y/N)	(1 to)	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:14	Y	0		0.0	0.0	Y	Y	62.5	68.4		Y	Y		
BMP1	10:27	Y	0		0.0	0.0									
BMP1	14:02	Y	0		0.0	0.0									
BMP2	07:51	Y	0		0.0	0.0	Y	Y	64.9	70.3		Y	Y		
BMP2	10:44	Y	0		0.0	0.0									
BMP2	14:19	Y	0		0.0	0.0									
BMP3	07:48	Y	0		0.0	0.0	Y	Y	54.3	59.1		Y	Y		
BMP3	11:01	Y	0		0.0	0.0									
BMP3	14:36	Y	0		0.0	0.0									
BMP4	08:05	Y	0		0.0	0.0	Y	Y	55.2	56.7		Y	Y		
BMP4	11:15	Y	0		0.0	0.0									
BMP4	14:53	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:10										Y				
CMP2	15:11										Y				
CMP3	15:12										Y				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar
4	S	6	Sun	3	wet	1022

WTP Inspection.

System Working (Y/N)	Leaks / Over-topping (Y/N)	Time:	N/A	Flow Meter (M³):	N/A
Y	Y	Equipment Impacted & Actions Taken to Rectify:			
		N/A			

Assessors Signature: [signature]

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	19-11-21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	EG
Daily Activity & Grid Ref.:	E6, E7					General Notes:		PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sample	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1 to 5)	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:35	Y	0		0.0	0.0	Y	N/A	69.6	77.9		N	N		
BMP1	10:51	Y	0		0.0	0.0									
BMP1	13:59	Y	0		0.0	0.0									
BMP2	07:32	Y	0		0.0	0.0	Y	N/A	62.9	63.4		N	N		
BMP2	11:05	Y	0		0.0	0.0									
BMP2	14:16	Y	0		0.0	0.0									
BMP3	07:49	Y	0		0.0	0.0	Y	N/A	58.8	64.5		N	N		
BMP3	11:25	Y	0		0.0	0.0									
BMP3	14:33	Y	0		0.0	0.0									
BMP4	08:06	Y	0		0.0	0.0	Y	N/A	57.3	63.3		N	N		
BMP4	11:42	Y	0		0.0	0.0									
BMP4	14:50	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:01										Y				
CMP2	15:05										Y				
CMP3	15:09										Y				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	Leaks / Over-topping (Y/N)	Time: N/A	Flow Meter (M^3): N/A
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
7	SSW	10	Scattered Cloud	4	Wet	1029	Y	Y	N/A	

Assessors Signature: EGhalley

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	18.11.24	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	C.N
Daily Activity & Grid Ref.:	E6, E7					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sample	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to 5)	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:11	Y	0		0.0	0.0	N/A		63.5	70.3		N	N		
BMP1	10:34	Y	0		0.0	0.0								[redacted]	
BMP1	14:03	Y	0		0.0	0.0									
BMP2	07:28	Y	0		0.0	0.0	N/A		69.3	76.2		N	N	* Asbestos picked + Sampled	
BMP2	10:51	Y	0		0.0	0.0									
BMP2	14:20	Y	0		0.0	0.0									
BMP3	07:45	Y	0		0.0	0.0	N/A		55.3	60.2		N	N		
BMP3	11:08	Y	0		0.0	0.0									
BMP3	14:37	Y	0		0.0	0.0									
BMP4	08:02	Y	0		0.0	0.0	N/A		54.1	58.5		N	N		
BMP4	11:25	Y	0		0.0	0.0									
BMP4	14:54	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:13										N				
CMP2	15:14										N				
CMP3	15:15										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection: System Working (Y/N)	WTP Inspection: Leaks / Over-topping (Y/N)	Time: n/a	Flow Meter (M^3): n/a
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
11	NSW	12	Overcast, rain	8	Wet	1026	n/a	n/a	n/a	

Assessors Signature: [signature]

Prevectas Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	17/11/21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	SC
Daily Activity & Grid Ref.:	~~E5~~ E6, E7, C7					General Notes:		PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sample	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:09	Y	0		0.0	0.0	Y	N/A	67.3	75.5		N	N		
BMP1	10:50	Y	0		0.0	0.0									
BMP1	14:02	Y	0		0.0	0.0									
BMP2	07:26	Y	0		0.0	0.0	Y	N/A	64.8	70.6		N	N		
BMP2	11:12	Y	0		0.0	0.0									
BMP2	14:29	Y	0		0.0	0.0									
BMP3	07:43	Y	0		0.0	0.0	Y	N/A	57.8	64.7		N	N		
BMP3	11:29	Y	0		0.0	0.0									
BMP3	14:26	Y	0		0.0	0.0									
BMP4	08:01	Y	0		0.0	0.0	Y	N/A	56.7	60.2		N	N		
BMP4	11:46	Y	0		0.0	0.0									
BMP4	14:53	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:10										Y				
CMP2	15:11										Y				
CMP3	15:12										Y				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Overtopping (Y/N)	Time: N/A	Flow Meter (M³): N/A
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
6	SW	7	Overcast	6	Wet	1022	Y	N	N/A	

Assessors Signature: [signature]

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	16.11.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	RC
Daily Activity & Grid Ref.:	E6, E7					General Notes:		PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Fribee Sample	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Posts	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:12	Y	0		0.0	0.0	Y	Y	65.4	72.3		Y	Y		
BMP1	10:51	Y	0		0.0	0.0									
BMP1	14:06	Y	0		0.0	0.0									
BMP2	07:24	Y	0		0.0	0.0	Y	Y	67.8	75.1		Y	Y		
BMP2	11:08	Y	0		0.0	0.0									
BMP2	14:23	Y	0		0.0	0.0									
BMP3	07:47	Y	0		0.0	0.0	Y	Y	56.9	60.2		Y	Y		
BMP3	11:25	Y	0		0.0	0.0									
BMP3	14:40	Y	0		0.0	0.0									
BMP4	08:04	Y	0		0.0	0.0	Y	Y	55.7	59.6		Y	Y		
BMP4	11:42	Y	0		0.0	0.0									
BMP4	14:57	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:14										Y				
CMP2	15:15										Y				
CMP3	15:16										Y				

Meteorological and environmental conditions							WTP Inspection.		Time:	21A	Flow Meter (M^3):	21A
Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	System Working (Y/N)	Leaks / Over-topping (Y/N)	Equipment Impacted & Actions Taken to Rectify:			
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar						
4	S	9	Fog	8	wet	1021	Y	Y	21A			

Assessors Signature: [signature]

Provectas Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	15.11.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	C.N
Daily Activity & Grid Ref.:	97, 87, 67					General Notes:			PID Bump Test: ✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sample	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to 5)	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	09:14	N	0		0.0	0.0	N	N/A	65.7	71.6		N	N	* DUST FRISBEES DECOMMISSIONED	
BMP1	11:26	N	0		0.0	0.0									
BMP1	14:21	N	0		0.0	0.0									
BMP2	09:29	N	0		0.0	0.0	N	N/A	66.5	72.9		N	N		
BMP2	11:38	N	0		0.0	0.0									
BMP2	14:36	N	0		0.0	0.0									
BMP3	09:40	N	0		0.0	0.0	N	N/A	59.4	65.2		N	N	* ASBESTOS FOUND	
BMP3	12:00	N	0		0.0	0.0									
BMP3	14:55	N	0		0.0	0.0									
BMP4	08:08	N	0		0.0	0.0	N	N/A	53.7	58.4		N	N		
BMP4	12:15	N	0		0.0	0.0									
BMP4	15:12	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:30										N				
CMP2	15:31										N				
CMP3	15:32										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time:	n/a	Flow Meter (M^3):	n/a
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Inspected & Actions Taken to Rectify:			
3	S	11	Overcast, dry	8	Wet	1026	n/a	n/a	n/a			

Assessors Signature: C.N

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	26.11.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	DW
Daily Activity & Grid Ref.:	E5, E6					General Notes:		PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sample	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:11	Y	0		0.0	0.0	N	N/A	71.4	78.1		N	N		
BMP1	10:55	Y	0		0.0	0.0									
BMP1	14:02	Y	0		0.0	0.0									
BMP2	07:28	Y	0		0.0	0.0	N	N/A	64.5	69.7		N	N		
BMP2	11:10	Y	0		0.0	0.0									
BMP2	14:19	Y	0		0.0	0.0									
BMP3	07:45	Y	0		0.0	0.0	N	N/A	56.8	66.4		N	N		
BMP3	11:27	Y	0		0.0	0.0									
BMP3	14:36	Y	0		0.0	0.0									
BMP4	08:02	Y	0		0.0	0.0	N	N/A	54.2	58.8		N	N		
BMP4	11:44	Y	0		0.0	0.0									
BMP4	14:53	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1											N				
CMP2											N				
CMP3											N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time: N/A	Flow Meter (M³): N/A
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
14	SW	7	Rain	6	Wet	993	N	N	N/A	

Assessors Signature: DWalley

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	25.11.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	
Daily Activity & Grid Ref.:	E6, E7					General Notes:		PID Bump Test:	✓

		ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING			
Location: MP or Grid Ref.	Time	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sample	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests	COMMENTS	COMPLIANTS RECEIVED / ACTIONS REQUIRED
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:05	Y	0		0.0	0.0	Y	N/A	68.5	74.4		Y	Y		
BMP1	11:04	Y	0		0.0	0.0									
BMP1	14:01	Y	0		0.0	0.0									
BMP2	07:25	Y	0		0.0	0.0	Y	N/A	66.4	74.2		Y	Y		
BMP2	11:21	Y	0		0.0	0.0									
BMP2	14:18	Y	0		0.0	0.0									
BMP3	07:42	Y	0		0.0	0.0	Y	N/A	54.9	60.7		Y	Y		
BMP3	11:38	Y	0		0.0	0.0									
BMP3	14:35	Y	0		0.0	0.0									
BMP4	07:58	Y	0		0.0	0.0	Y	N/A	56.7	60.5		Y	Y		
BMP4	14:50	Y	0		0.0	0.0									
BMP4		Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:07														
CMP2	15:08														
CMP3	15:09														

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time: N/A	Flow Meter (M^3): N/A
(mph)	(e.g. N, SW)	°C	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
3	N	-2	Clear	0	Wet	1020	Y	Y	N/A	

Assessors Signature: [signature]

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	24-11-21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	EG
Daily Activity & Grid Ref.:	E6, E7					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sample	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to 5)	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:16	Y	0		0.0	0.0	Y	N/A	67.7	72.7		Y	Y		
BMP1	10:47	Y	0		0.0	0.0									
BMP1	14:02	Y	0		0.0	0.0									
BMP2	07:53	Y	0		0.0	0.0	Y	N/A	68.6	75.8		Y	Y		
BMP2	11:04	Y	0		0.0	0.0									
BMP2	14:19	Y	0		0.0	0.0									
BMP3	07:50	Y	0		0.0	0.0	Y	N/A	58.5	61.3		Y	Y		
BMP3	11:21	Y	0		0.0	0.0									
BMP3	14:36	Y	0		0.0	0.0									
BMP4	08:07	Y	0		0.0	0.0	Y	N/A	60.1	64.5		Y	Y		
BMP4	11:38	Y	0		0.0	0.0									
BMP4	14:53	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:11										Y				
CMP2	15:12										Y				
CMP3	15:13										Y				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	Leaks / Over-topping (Y/N)
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar		
6	SSW	7	Overcast	8	wet	1022	Y	Y

Time: N/A | Flow Meter (M³): N/A

Equipment Impacted & Actions Taken to Rectify:

N/A

Assessors Signature: [signature]

Preventive Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	23.11.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	RJ
Daily Activity & Grid Ref.:	E6, E7					General Notes:			

PID Bump Test: /

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sample	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
		(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:15	Y	0		0.0	0.0	Y	N/A	66.2	73.8		Y	Y		
BMP1	11:01	Y	0		0.0	0.0									
BMP1	14:12	Y	0		0.0	0.0									
BMP2	07:34	Y	0		0.0	0.0	Y	N/A	66.2	73.7		Y	Y		
BMP2	11:19	Y	0		0.0	0.0									
BMP2	14:29	Y	0		0.0	0.0									
BMP3	07:46	Y	0		0.0	0.0	Y	N/A	59.1	67.7		Y	Y		
BMP3	11:35	Y	0		0.0	0.0									
BMP3	14:47	Y	0		0.0	0.0									
BMP4	08:06	Y	0		0.0	0.0	Y	N/A	55.2	60.3		Y	Y		
BMP4	11:52	Y	0		0.0	0.0									
BMP4	15:04	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:23										Y				
CMP2	15:24										Y				
CMP3	15:25										Y				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time:	N/A	Flow Meter (M^3):	N/A
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:			
3	N	5	Overcast	8	wet	1033	N	N	N/A			

Assessors Signature: E Dalley

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	22.11.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name	EW
Daily Activity & Grid Ref:	E6, E7					General Notes:		PID Bump Test:	✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sample	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to)	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:12	Y	0		0.0	0.0	Y	N/A	70.1	76.2		N	N		
BMP1	10:55	Y	0		0.0	0.0									
BMP1	14:02	Y	0		0.0	0.0									
BMP2	07:28	Y	0		0.0	0.0	Y	N/A	65.1	71.2		N	N		
BMP2	11:10	Y	0		0.0	0.0									
BMP2	14:19	Y	0		0.0	0.0									
BMP3	07:56	Y	0		0.0	0.0	Y	N/A	56.4	62.1		N	N		
BMP3	11:27	Y	0		0.0	0.0									
BMP3	14:26	Y	0		0.0	0.0									
BMP4	08:05	Y	0		0.0	0.0	Y	N/A	66.4	72.4		N	N		
BMP4	11:44	Y	0		0.0	0.0									
BMP4	14:48	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1											Y				
CMP2											Y				
CMP3											Y				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP inspection. System Working (Y/N)	WTP inspection. Leaks / Over-topping (Y/N)	Time: N/A	Flow Meter (M³): N/A
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:	
2	N	-1	SUN	2	WET	1038	N	N	N/A	

Assessors Signature: E Dalley

Proveetus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	30.11.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assesser name	EJ
Daily Activity & Grid Ref.:	ES, E6					General Notes:			PID Bump Test:

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sampled	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
		(Y/N)	(1 to 5)	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:12	Y	0		0.0	0.0	Y	N/A	67.2	73.6		N	N		
BMP1	10:53	Y	0		0.0	0.0									
BMP1	14:05	Y	0		0.0	0.0									
BMP2	07:25	Y	0		0.0	0.0	Y	N/A	67.4	73.1		N	N		
BMP2	11:10	Y	0		0.0	0.0									
BMP2	14:22	Y	0		0.0	0.0									
BMP3	07:46	Y	0		0.0	0.0	Y	N/A	55.7	63.8		N	N		
BMP3	11:27	Y	0		0.0	0.0									
BMP3	14:39	Y	0		0.0	0.0									
BMP4	08:08	Y	0		0.0	0.0	Y	N/A	56.4	62.6		N	N		
BMP4	11:49	Y	0		0.0	0.0									
BMP4	14:56	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:14										N				
CMP2	15:15										N				
CMP3	15:16										N				

Meteorological and environmental conditions						
Wind speed	Wind Directio	Temp	Weather description	Cloud cover	Ground conditions	Baromet ric
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar
15	S	10	Rain	8	Wet	1011

WTP Inspection.		Time:	N/A	Flow Meter (M^3):	N/A
System Working	Leaks / Over-topping	Equipment Impacted & Actions Taken to Rectify:			
Y	N	N/A			

Assessors Signature: [signature]

Preventus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	29.11.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	E.C
Daily Activity & Grid Ref.:	E5, E6					General Notes:		PID Bump Test:	

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
		Detectability	Intensity	Quality	Average PID Reading	Peak PID Reading	Visual	Frisbee Sample	Average Reading	Peak Reading	Visible Impacts from Site Run-off	Litter	Pests		
	Start	(Y/N)	(1 to	(Description)	(ppm)	(ppm)	Y/N	Y/N	(dBa)	(dBa)	Y/N	(Y/N)	(Y/N)	(Description)	(Description)
BMP1	07:17	Y	0		0.0	0.0	Y	N/A	64.9	69.5		Y	Y		
BMP1	11:04	Y	0		0.0	0.0									
BMP1	14:40	Y	0		0.0	0.0									
BMP2	07:32	Y	0		0.0	0.0	Y	N/A	65.7	70.5		Y	Y		
BMP2	11:21	Y	0		0.0	0.0									
BMP2	14:27	Y	0		0.0	0.0									
BMP3	07:49	Y	0		0.0	0.0	Y	N/A	61.6	67.3		Y	Y		
BMP3	11:55	Y	0		0.0	0.0									
BMP3	14:38	Y	0		0.0	0.0									
BMP4	08:06	Y	0		0.0	0.0	Y	N/A	53.9	60.7		Y	Y		
BMP4	11:35	Y	0		0.0	0.0									
BMP4	14:56	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:48										Y				
CMP2	15:49										Y				
CMP3	15:50										Y				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric Pressure	WTP Inspection. System Working (Y/N)	WTP Inspection. Leaks / Over-topping (Y/N)	Time:	N / A	Flow Meter (M^3):	N / A
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar			Equipment Impacted & Actions Taken to Rectify:			
1	N	-4	Ice Fog	8	wet	1015	Y	Y	N / A			

Assessors Signature: E. Dalley

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	01.12.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	BW
Daily Activity & Grid Ref.:	DS							General Notes:	

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	PID Bump Test: ✓
	Start	Detectability (Y/N)	Intensity (1 to 6)	Quality (Description)	Average PID Reading (ppm)	Peak PID Reading (ppm)	Visual Y/N	Frisbee Sampled Y/N	Average Reading (dBa)	Peak Reading (dBa)	Visible impacts from Site Run-off Y/N	Litter (Y/N)	Fags (Y/N)	(Description)	COMPLAINTS RECEIVED / ACTIONS REQUIRED (Description)
BMP1	07:17	Y	0		0.0	0.0	N	N/A	64.8	71.1		N	N		
BMP1	10:52	Y	0		0.0	0.0									
BMP1	14:20	Y	0		0.0	0.0									
BMP2	07:54	Y	0		0.0	0.0	N	N/A	66.7	70.9		N	N		
BMP2	11:09	Y	0		0.0	0.0									
BMP2	14:26	Y	0		0.0	0.0									
BMP3	07:51	Y	0		0.0	0.0	N	N/A	58.4	64.9		N	N		
BMP3	11:26	Y	0		0.0	0.0									
BMP3	14:44	Y	0		0.0	0.0									
BMP4	08:08	Y	0		0.0	0.0	N	N/A	56.2	62.3		N	N		
BMP4	11:43	Y	0		0.0	0.0									
BMP4	15:03	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:21										N				
CMP2	15:22										N				
CMP3	15:23										N				

Meteorological and environmental conditions

Wind speed (mph)	Wind Direction (e.g. N, SW)	Temp (°C)	Weather description (e.g. rain, sun, wet, dry)	Cloud cover (0 to 8)	Ground conditions (e.g. wet, dry)	Barometric (mbar)
14	WNW	6	Rain	7	wet	996

WTP Inspection.

System Working	Leaks / Over-topping
N	N

Time: N/A

Flow Meter (M^3): N/A

Equipment Inspected & Actions Taken to Rectify:

N/A

Assessors Signature: [signature]

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	02.12.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	BC
Daily Activity & Grid Ref.:	DS							General Notes:	

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	PID Bump Test: /
	Start	Detectability (Y/N)	Intensity (1 to 5)	Quality (Description)	Average PID Reading (ppm)	Peak PID Reading (ppm)	Visual Y/N	Frisbee Sampled Y/N	Average Reading (dBa)	Peak Reading (dBa)	Visible Impacts from Site Run-off Y/N	Litter (Y/N)	Pests (Y/N)	(Description)	COMPLAINTS RECEIVED / ACTIONS REQUIRED (Description)
BMP1	07:30	Y	0		0.0	0.0	Y	N/A	66.8	78.5		N	N		
BMP1	11:03	Y	0		0.0	0.0									
BMP1	14:07	Y	0		0.0	0.0									
BMP2	07:27	Y	0		0.0	0.0	Y	N/A	69.6	76.8		N	N		
BMP2	11:20	Y	0		0.0	0.0									
BMP2	14:25	Y	0		0.0	0.0									
BMP3	07:40	Y	0		0.0	0.0	Y	N/A	57.1	64.3		N	N		
BMP3	11:37	Y	0		0.0	0.0									
BMP3	14:42	Y	0		0.0	0.0									
BMP4	08:01	Y	0		0.0	0.0	Y	N/A	55.7	60.4		N	N		
BMP4	11:54	Y	0		0.0	0.0									
BMP4	14:58	Y	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:15										Y				
CMP2	15:16										Y				
CMP3	15:17										Y				

Meteorological and environmental conditions

Wind speed (mph)	Wind Direction (e.g. N, SW)	Temp (°C)	Weather description (e.g. rain, sun, wet, dry)	Cloud cover (0 to 8)	Ground conditions (e.g. wet, dry)	Barometric (mbar)
9	NW	1	clear/sun	1	wet	1015

WTP Inspection.

System Working	Leaks / Over-topping
Y	Y

Time: N/A

Flow Meter (M^3): N/A

Equipment Impacted & Actions Taken to Rectify: N/A

Assessors Signature: E Dalley

Provectus Environmental Monitoring Form 101114

Site:	Project Bradford	Date:	03.12.21	Contract Ref:	101114	Client:	BAM Construction Ltd	Assessor name:	EW
Daily Activity & Grid Ref.:	DS							General Notes:	

PID Bump Test: ✓

Location: MP or Grid Ref.	Time	ODOUR			VOC		DUST		NOISE		CANAL	HOUSEKEEPING		COMMENTS	COMPLAINTS RECEIVED / ACTIONS REQUIRED
	Start	Detectibility (Y/N)	Intensity (1 to	Quality (Description)	Average PID Reading (ppm)	Peak PID Reading (ppm)	Visual Y/N	Friabes Sampled Y/N	Average Reading (dBa)	Peak Reading (dBa)	Visible inserts from Site Run-off Y/N	Litter (Y/N)	Pests (Y/N)	(Description)	(Description)
BMP1	07:11	Y	0		0.0	0.0	Y	N/A	68.7	76.4		N	N		
BMP1	11:05	N	0		0.0	0.0									
BMP1	14:10	N	0		0.0	0.0									
BMP2	07:25	N	0		0.0	0.0	Y	N/A	70.1	78.3		N	N		
BMP2	11:20	N	0		0.0	0.0									
BMP2	14:27	N	0		0.0	0.0									
BMP3	07:45	N	0		0.0	0.0	Y	N/A	59.8	64.5		N	N		
BMP3	11:37	N	0		0.0	0.0									
BMP3	14:44	N	0		0.0	0.0									
BMP4	08:03	N	0		0.0	0.0	Y	N/A	61.2	68.6		N	N		
BMP4	11:54	N	0		0.0	0.0									
BMP4	15:01	N	0		0.0	0.0									
EMP1															
EMP2															
EMP3															
EMP4															
CMP1	15:17										N				
CMP2	15:18										N				
CMP3	15:19										N				

Meteorological and environmental conditions

Wind speed	Wind Direction	Temp	Weather description	Cloud cover	Ground conditions	Barometric
(mph)	(e.g. N, SW)	(°C)	(e.g. rain, sun, wet, dry)	(0 to 8)	(e.g. wet, dry)	mbar
5	WSW	4	Overcast	7	wet	1002

WTP Inspection.

System Working	Leaks / Over-topping
N	N

Time: N/A

Flow Meter (M³): N/A

Equipment Impacted & Actions Taken to Rectify:

N/A

Assessors Signature: [signature]

APPENDIX H Asbestos Air Monitoring Results

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

2671

AIRBORNE FIBRE MONITORING

TE	15 April 2021		BACKGROUND		APPROX. ENCLOSURE AREA/VOL (m²/m³)	NA
ALYST NAME	Liam Carpenter		LEAK			
E ADDRESS	CLIENT name & address	Contractors Name & Address	CLEARANCE		MEASUREMENTS REQ'D	NA
ort city Way nchester 1 3DU	Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG	Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG	RE-ASSURANCE	YES	No. SAMPLES TAKEN	5
			PERSONAL		FILTER DIAM. (mm)	22
			STATIC		ASBESTOS REMOVAL OPERATION	
			RPE checks made	NA	Reassurance air testing during excavation works on site.	
			LAB REF: DN62 XNA			
ALYST SIGNATURE		EXPOSURE TIME (minutes)	NA	TYPE OF ASBESTOS (outside scope of UKAS accreditation)	Not known	

MPLE REF.	FILTER HEAD REF No.	PUMP REF No.	SAMPLE LOCATION	TYPE OF TEST	START TIME	END TIME	SAMPLE LENGTH	FLOW LITRE/min. START	FLOW LITRE/min. END	DUST DISTURB MINUTES	DUST DISTURB TYPE	LITRE	FIELDS	FIBRES	CONC. ACTUAL FIBRE/ml	CONC. REPORTED FIBRE/ml
'150421/01	54	39	Adjacent site perimeter fence	R	0941	1041	60	8.0	8.0	NA	NA	480	200	1.5	0.0007	<0.01
'150421/02	53	34	Adjacent site perimeter fence	R	0944	1044	60	8.0	8.0	NA	NA	480	200	3	0.0015	<0.01
'150421/03	51	33	Adjacent site perimeter fence	R	0948	1048	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
'150421/04	50	21	Adjacent site perimeter fence	R	0950	1050	60	8.0	8.0	NA	NA	480	200	2.5	0.0013	<0.01
'150421/05	49	14	Adjacent to stockpile	R	0952	1052	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
			End of samples													

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

UKAS TESTING 2671

AIRBORNE FIBRE MONITORING | REPORT No. 27443

ICROSCOPE REF:	MIC-06
ICROSCOPE SET UP:	YES
SE/NPL GROUP:	5
RATICULE DIAM. (microns)	100
_OWMETER:	HFM-12
TMOS. PRESSURE (mb):	998
EMPERATURE (°C):	7
/EATHER CONDITIONS:	Sunny
_OW CORRECTED:	NA
ORRECTED FLOW (l/min):	NA
IELD BLANK TAKEN	YES

VISUAL INSPECTION


UMBER OF INSPECTIONS:	NA
YPE OF RESPIRATOR	NA
NCLOSURE CLEAN:	NA
NCLOSURE INTACT:	NA
NTERIOR OF ENCL. DRY:	NA
.P.U. OFF AND SEALED	NA
OCK DOWN SPRAY USED	NA

Limit of Quantification

ie limit of quantification is 0.010 fibres /ml. where sample volumes of 0 litres or greater and at least 200 graticule fields are analysed. The sult may be reported as 'less than 0.01 fibres /ml'.
here sample volumes are less than 480 litres and/or less than 200 aticule fields are analysed then the limit of quantification may be eater than 0.01 fibres/ml.

is report must not be reproduced except in full without the approval 'Fourstage Environmental Ltd.'

APPROXIMATE SITE PLAN (X = SAMPLE)

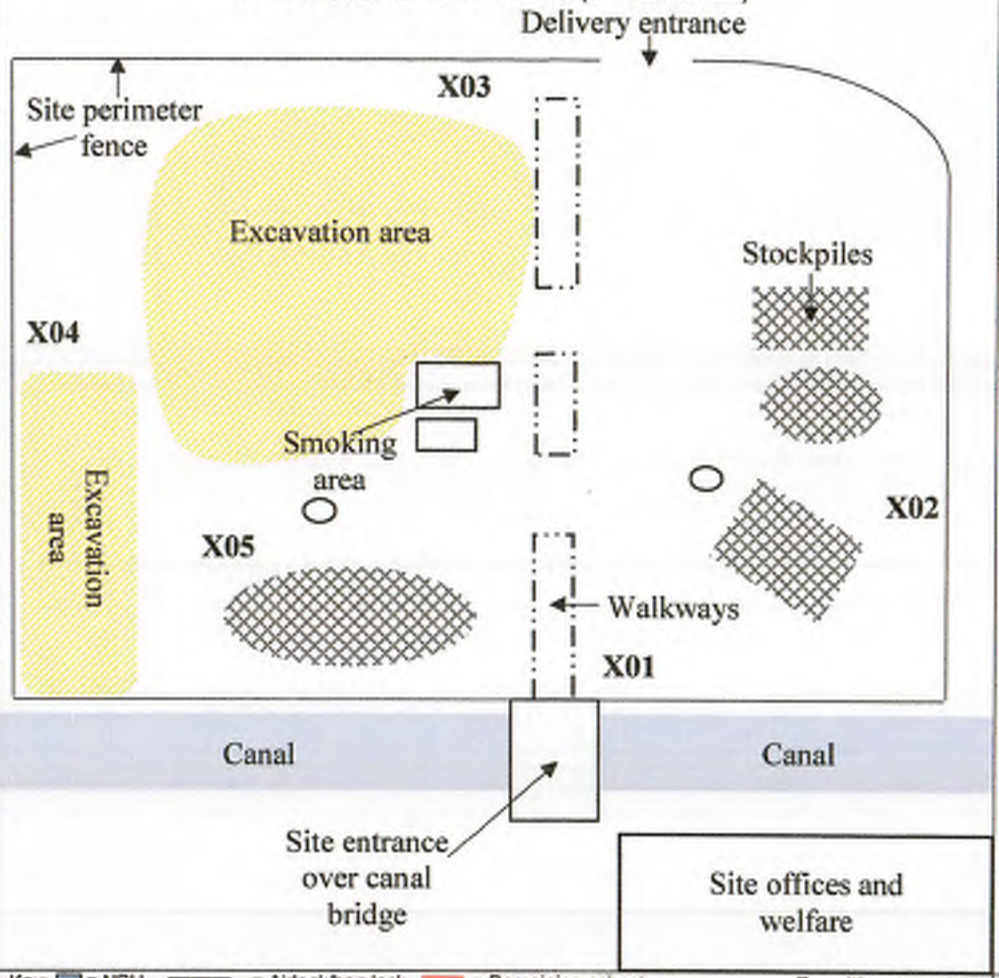

Key: = NPU = Airlock/bag lock = Remaining asbestos = Transit/waste route

The method used for sampling and the subsequent analysis as set out in HSG248 & in-house DOC/002

COMMENTS (outside scope of UKAS accreditation)

Reassurance air testing was undertaken to various locations on site while excavation works were being undertaken to various areas.

All results were satisfactory

Is generic Risk Assessment sufficient	YES	
Contractor's Representative Acknowledgement of diagram accuracy	NAME:	SIGNATURE:

FOURSTAGE ENVIRONMENTAL LTD.


5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

2671

AIRBORNE FIBRE MONITORING

TEST REPORT No. 27432

ATE	8 April 2021		BACKGROUND		APPROX. ENCLOSURE AREA/VOL (m^2/m^3)	NA
NALYST NAME	Liam Carpenter		LEAK			
TE ADDRESS	CLIENT name & address	Contractors Name & Address	CLEARANCE		MEASUREMENTS REQ'D	NA
port city Way anchester 11 3DU	Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG	Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG	RE-ASSURANCE	YES	No. SAMPLES TAKEN	5
			PERSONAL		FILTER DIAM. (mm)	22
			STATIC		ASBESTOS REMOVAL OPERATION	
			RPE checks made	NA	Reassurance air testing during excavation works on site.	
			LAB REF: DN62 XNA			

NALYST SIGNATURE 

EXPOSURE TIME (minutes) NA TYPE OF ASBESTOS (outside scope of UKAS accreditation) Not known

SAMPLE REF.	FILTER HEAD REF No.	PUMP REF No.	SAMPLE LOCATION	TYPE OF TEST	START TIME	END TIME	SAMPLE LENGTH	FLOW LITRE/min. START	FLOW LITRE/min. END	DUST DISTURB MINUTES	DUST DISTURB TYPE	LITRE	FIELDS	FIBRES	CONC. ACTUAL FIBRE/ml	CONC. REPORTED FIBRE/ml
2/080421/01	54	39	Adjacent site perimeter fence	R	1004	1104	62	8.0	8.0	NA	NA	480	200	2.5	0.013	<0.01
2/080421/02	53	34	Adjacent site perimeter fence	R	1006	1106	62	8.0	8.0	NA	NA	480	200	1.5	0.0007	<0.01
2/080421/03	51	33	Adjacent site perimeter fence	R	1009	1109	62	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
2/080421/04	50	21	Adjacent site perimeter fence	R	1011	1111	62	8.0	8.0	NA	NA	480	200	1.5	0.0007	<0.01
2/080421/05	49	14	Adjacent to stockpile	R	1013	1113	62	8.0	8.0	NA	NA	480	200	1	0.0005	<0.01
			End of samples													

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

UKAS TESTING 2671

AIRBORNE FIBRE MONITORING | REPORT No. 27432

CROSCOPE REF:	MIC-06
CROSCOPE SET UP:	YES
SE/NPL GROUP:	5
RATICULE DIAM. (microns)	100
OWMETER:	HFM-12
MOS. PRESSURE (mb):	998
MPERATURE (ºC):	7
EATHER CONDITIONS:	Sunny
OW CORRECTED:	NA
ORRECTED FLOW (l/min):	NA
ELD BLANK TAKEN	YES

VISUAL INSPECTION


JMBER OF INSPECTIONS:	NA
PE OF RESPIRATOR	NA
NCLOSURE CLEAN:	NA
NCLOSURE INTACT:	NA
TERIOR OF ENCL. DRY:	NA
P.U. OFF AND SEALED	NA
OCK DOWN SPRAY USED	NA

Limit of Quantification

e limit of quantification is 0.010 fibres /ml. where sample volumes of litres or greater and at least 200 graticule fields are analysed. The ult may be reported as 'less than 0.01 fibres /ml'.
here sample volumes are less than 480 litres and/or less than 200 ticule fields are analysed then the limit of quantification may be ater than 0.01 fibres/ml.

is report must not be reproduced except in full without the approval 'Fourstage Environmental Ltd.'

APPROXIMATE SITE PLAN (X = SAMPLE)

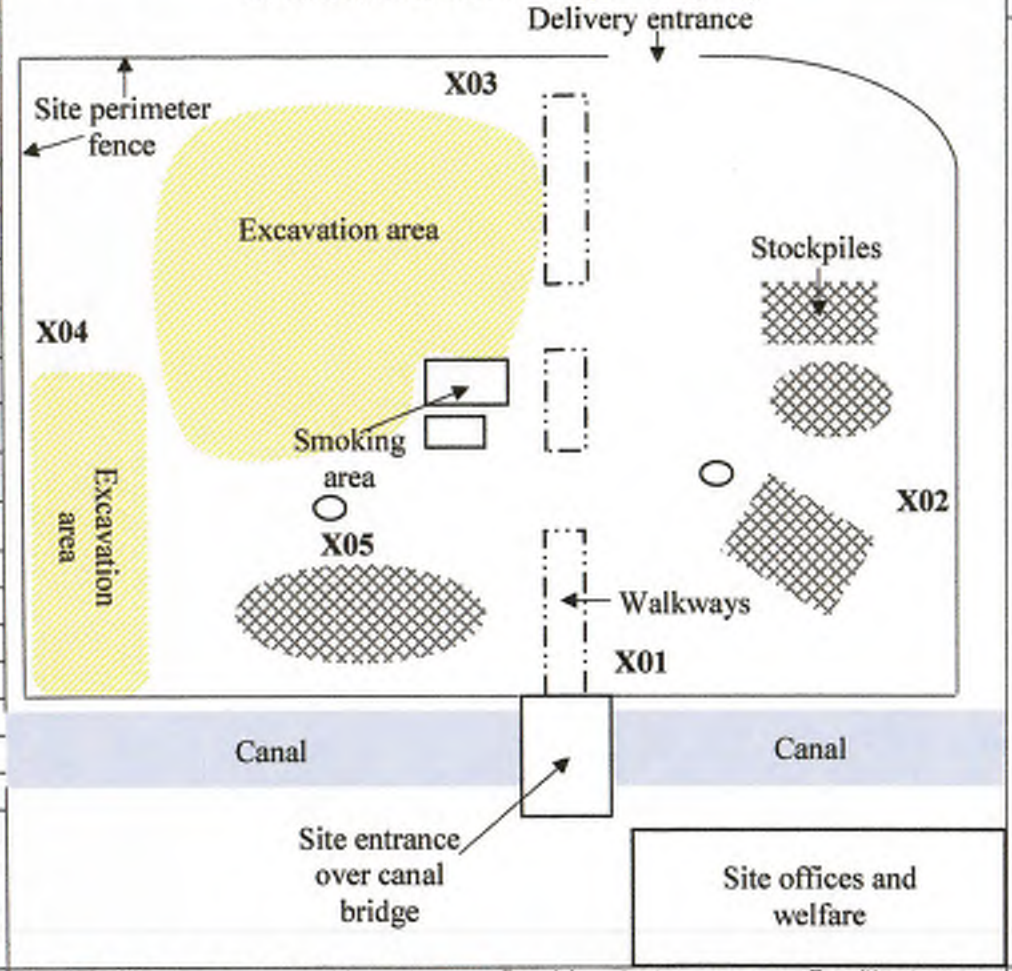

Key: NPU = Airlock/bag lock = Remaining asbestos = Transit/waste route

The method used for sampling and the subsequent analysis as set out in HSG248 & in-house DOC/002

Contractor's Representative Acknowledgement of diagram accuracy | NAME: [signature] | SIGNATURE: [signature]

COMMENTS (outside scope of UKAS accreditation)

Reassurance air testing was undertaken to various locations on site while excavation works were being undertaken to various areas.

All results were satisfactory

Is generic Risk Assessment sufficient: YES

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

2671

AIRBORNE FIBRE MONITORING

TEST REPORT No. 27423

ATE	31 March 2021	BACKGROUND		APPROX. ENCLOSURE AREA/VOL (m^2/m^3)	NA
NALYST NAME	Liam Carpenter	LEAK			
TE ADDRESS	CLIENT name & address: Provectus Remediation Ltd, Regent House, Bath Avenue, Wolverhampton, WV1 4EG / Contractors Name & Address: Provectus Remediation Ltd, Regent House, Bath Avenue, Wolverhampton, WV1 4EG	CLEARANCE		MEASUREMENTS REQ'D	NA
ort city Way, anchester, 11 3DU		RE-ASSURANCE	YES	No. SAMPLES TAKEN	5
		PERSONAL		FILTER DIAM. (mm)	22
		STATIC		ASBESTOS REMOVAL OPERATION	
		RPE checks made	NA	Reassurance air testing during excavation works on site.	
		LAB REF: DN62 XNA			
IALYST SIGNATURE		EXPOSURE TIME (minutes)	NA	TYPE OF ASBESTOS (outside scope of UKAS accreditation)	Not known

AMPLE REF.	FILTER HEAD REF No.	PUMP REF No.	SAMPLE LOCATION	TYPE OF TEST	START TIME	END TIME	SAMPLE LENGTH	FLOW LITRE/min. START	FLOW LITRE/min. END	DUST DISTURB MINUTES	DUST DISTURB TYPE	LITRE	FIELDS	FIBRES	CONC. ACTUAL FIBRE/ml	CONC. REPORTED FIBRE/ml
/310321/01	54	39	Adjacent site perimeter fence	R	1614	1714	62	8.0	8.0	NA	NA	496	194	2	0.0010	<0.01
/310321/02	53	34	Adjacent site perimeter fence	R	1617	1717	62	8.0	8.0	NA	NA	496	194	2.5	0.0013	<0.01
/310321/03	51	33	Adjacent site perimeter fence	R	1621	1721	62	8.0	8.0	NA	NA	496	194	1	0.0005	<0.01
/310321/04	50	21	Adjacent site perimeter fence	R	1625	1725	62	8.0	8.0	NA	NA	496	194	2	0.0010	<0.01
/310321/05	49	14	Adjacent to excavation works	R	1628	1728	62	8.0	8.0	NA	NA	496	194	3	0.0015	<0.01
			End of samples													

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

UKAS TESTING 2671

AIRBORNE FIBRE MONITORING | REPORT No. 27423

CROSCOPE REF:	MIC-06
CROSCOPE SET UP:	YES
SE/NPL GROUP:	5
RATICULE DIAM. (microns)	100
.OWMETER:	HFM-12
TMOS. PRESSURE (mb):	998
EMPERATURE (ºC):	19
'EATHER CONDITIONS:	Sunny
.OW CORRECTED:	NA
ORRECTED FLOW (l/min):	NA
ELD BLANK TAKEN	YES

VISUAL INSPECTION


UMBER OF INSPECTIONS:	NA
YPE OF RESPIRATOR	NA
NCLOSURE CLEAN:	NA
NCLOSURE INTACT:	NA
NTERIOR OF ENCL. DRY:	NA
.P.U. OFF AND SEALED	NA
OCK DOWN SPRAY USED	NA

Limit of Quantification

he limit of quantification is 0.010 fibres /ml. where sample volumes of 10 litres or greater and at least 200 graticule fields are analysed. The sult may be reported as 'less than 0.01 fibres /ml'.
here sample volumes are less than 480 litres and/or less than 200 aticule fields are analysed then the limit of quantification may be eater than 0.01 fibres/ml.

his report must not be reproduced except in full without the approval 'Fourstage Environmental Ltd.'

APPROXIMATE SITE PLAN (X = SAMPLE)

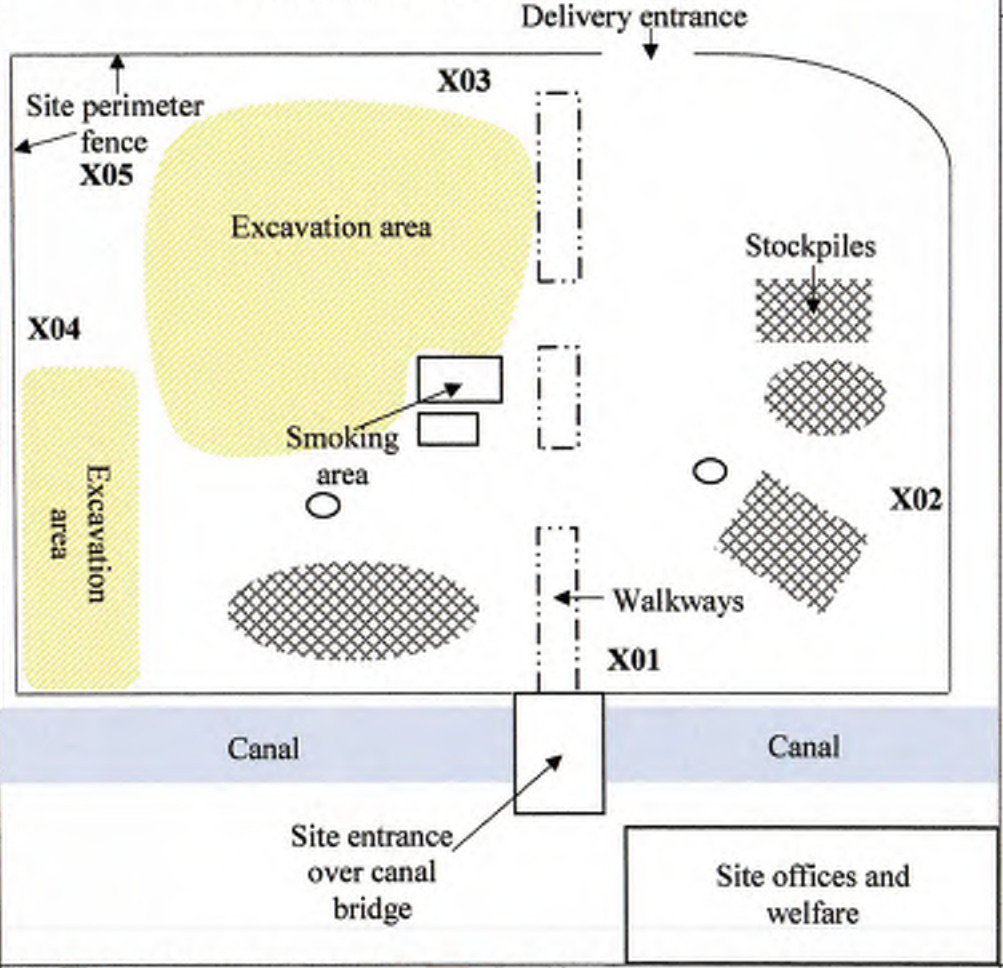

Key: ■ = NPU ▭▭▭ = Airlock/bag lock ▬ = Remaining asbestos – – – = Transit/waste route

The method used for sampling and the subsequent analysis as set out in HSG248 & in-house DOC/002

Is generic Risk Assessment sufficient: YES

Contractor's Representative Acknowledgement of diagram accuracy | NAME: T. Harrington | SIGNATURE:

COMMENTS (outside scope of UKAS accreditation)

Reassurance air testing was undertaken to various locations on site while excavation works were being undertaken to various areas.

All results were satisfactory

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

2671

AIRBORNE FIBRE MONITORING

TEST REPORT No. 27417

ATE	26 March 2021	BACKGROUND		APPROX. ENCLOSURE AREA/VOL (m^2/m^3)	NA
NALYST NAME	Liam Carpenter	LEAK			
TE ADDRESS	CLIENT name & address: Provectus Remediation Ltd, Regent House, Bath Avenue, Wolverhampton, WV1 4EG / Contractors Name & Address: Provectus Remediation Ltd, Regent House, Bath Avenue, Wolverhampton, WV1 4EG	CLEARANCE		MEASUREMENTS REQ'D	NA
ort city Way, anchester, 11 3DU		RE-ASSURANCE	YES	No. SAMPLES TAKEN	5
		PERSONAL		FILTER DIAM. (mm)	22
		STATIC		ASBESTOS REMOVAL OPERATION	
		RPE checks made	NA	Reassurance air testing during excavation works on site.	
		LAB REF: DN62 XNA			
ALYST SIGNATURE		EXPOSURE TIME (minutes)	NA	TYPE OF ASBESTOS (outside scope of UKAS accreditation)	Not known

AMPLE REF.	FILTER HEAD REF No.	PUMP REF No.	SAMPLE LOCATION	TYPE OF TEST	START TIME	END TIME	SAMPLE LENGTH	FLOW LITRE/min. START	FLOW LITRE/min. END	DUST DISTURB MINUTES	DUST DISTURB TYPE	LITRE	FIELDS	FIBRES	CONC. ACTUAL FIBRE/ml	CONC. REPORTED FIBRE/ml
/260321/01	54	39	Adjacent site perimeter fence	R	0934	1036	62	8.0	8.0	NA	NA	496	194	1	0.0005	<0.01
/260321/02	53	34	Adjacent site perimeter fence	R	0936	1038	62	8.0	8.0	NA	NA	496	194	2	0.0010	<0.01
/260321/03	51	33	Adjacent site perimeter fence	R	0938	1038	62	8.0	8.0	NA	NA	496	194	1.5	0.0007	<0.01
/260321/04	50	21	Adjacent site perimeter fence	R	0940	1042	62	8.0	8.0	NA	NA	496	194	1	0.0005	<0.01
/260321/05	49	14	Adjacent to smoking shelter	R	0944	1046	62	8.0	8.0	NA	NA	496	194	2.5	00013	<0.01

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

UKAS TESTING 2671

AIRBORNE FIBRE MONITORING | REPORT No. 27417

ICROSCOPE REF:	MIC-06
ICROSCOPE SET UP:	YES
SE/NPL GROUP:	5
RATICULE DIAM. (microns):	100
LOWMETER:	HFM-12
TMOS. PRESSURE (mb):	998
EMPERATURE (ºC):	9
/EATHER CONDITIONS:	Rainy
LOW CORRECTED:	NA
ORRECTED FLOW (l/min):	NA
IELD BLANK TAKEN	YES

VISUAL INSPECTION


UMBER OF INSPECTIONS:	NA
YPE OF RESPIRATOR	NA
NCLOSURE CLEAN:	NA
NCLOSURE INTACT:	NA
NTERIOR OF ENCL. DRY:	NA
I.P.U. OFF AND SEALED	NA
OCK DOWN SPRAY USED	NA

Limit of Quantification

he limit of quantification is 0.010 fibres /ml. where sample volumes of 30 litres or greater and at least 200 graticule fields are analysed. The sult may be reported as 'less than 0.01 fibres /ml'.
here sample volumes are less than 480 litres and/or less than 200 aticule fields are analysed then the limit of quantification may be eater than 0.01 fibres/ml.

his report must not be reproduced except in full without the approval f 'Fourstage Environmental Ltd.'

APPROXIMATE SITE PLAN (X = SAMPLE)

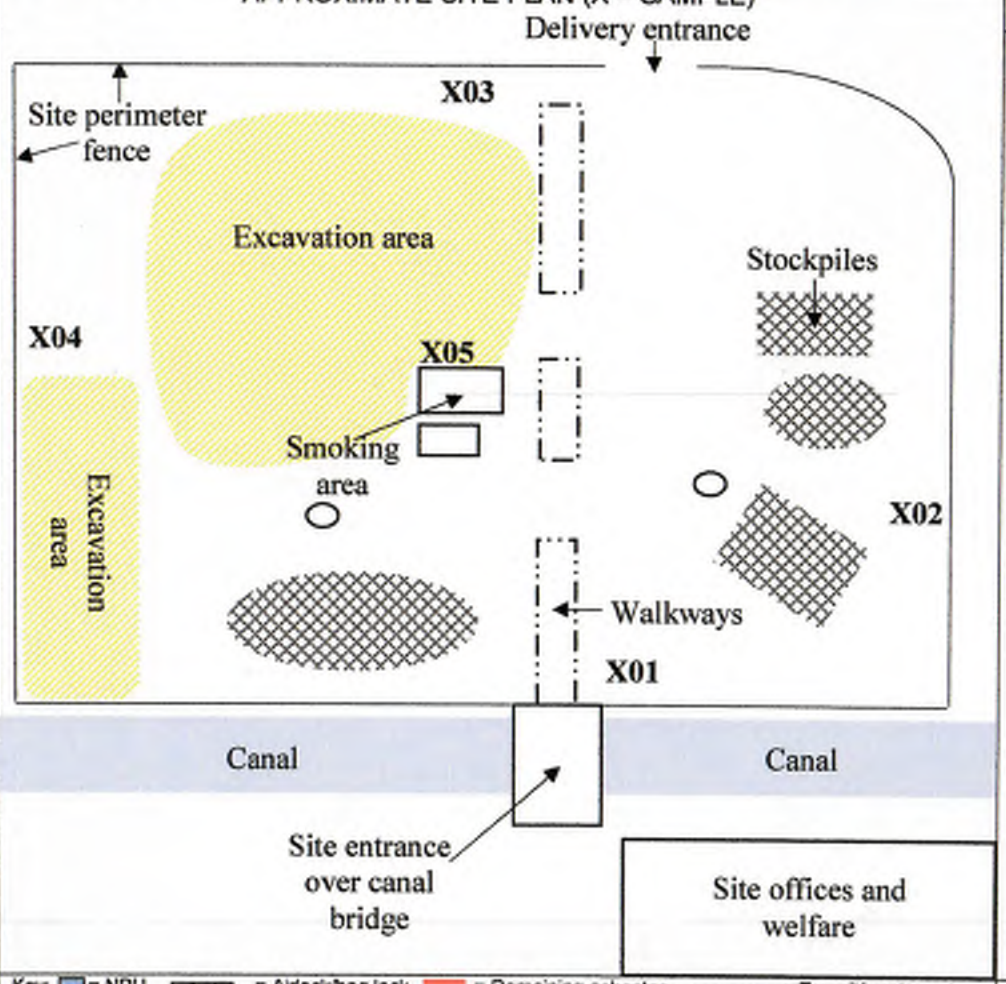

Key: = NPU = Airlock/bag lock = Remaining asbestos = Transit/waste route

The method used for sampling and the subsequent analysis as set out in HSG248 & in-house DOC/002

Contractor's Representative Acknowledgement of diagram accuracy	NAME:	SIGNATURE:	Is generic Risk Assessment sufficient: YES

COMMENTS (outside scope of UKAS accreditation)

Reassurance air testing was undertaken to various locations on site while excavation works were being undertaken to various areas.

All results were satisfactory

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

2671

AIRBORNE FIBRE MONITORING

TEST REPORT No. 27459

DATE	29 April 2021	BACKGROUND	
ANALYST NAME	Liam Carpenter	LEAK	
SITE ADDRESS	CLIENT name & address: Provectus Remediation Ltd, Regent House, Bath Avenue, Wolverhampton, WV1 4EG	CLEARANCE	
Sport city Way, Manchester, M11 3DU	Contractors Name & Address: Provectus Remediation Ltd, Regent House, Bath Avenue, Wolverhampton, WV1 4EG	RE-ASSURANCE	YES
		PERSONAL	
		STATIC	
		RPE checks made	NA
		LAB REF: DN62 XNA	

APPROX. ENCLOSURE AREA/VOL (m^2/m^3)	NA
MEASUREMENTS REQ'D	NA
No. SAMPLES TAKEN	5
FILTER DIAM. (mm)	22
ASBESTOS REMOVAL OPERATION	Reassurance air testing during excavation works on site.

ANALYST SIGNATURE

EXPOSURE TIME (minutes) NA

TYPE OF ASBESTOS (outside scope of UKAS accreditation) Not known

SAMPLE REF.	FILTER HEAD REF No.	PUMP REF No.	SAMPLE LOCATION	TYPE OF TEST	START TIME	END TIME	SAMPLE LENGTH	FLOW LITRE/min. START	FLOW LITRE/min. END	DUST DISTURB MINUTES	DUST DISTURB TYPE	LITRE	FIELDS	FIBRES	CONC. ACTUAL FIBRE/ml	CONC. REPORTED FIBRE/ml
52/290421/01	54	39	Adjacent site perimeter fence	R	0929	1029	60	8.0	8.0	NA	NA	480	200	1	0.0005	<0.01
52/290421/02	53	34	Adjacent site perimeter fence	R	0933	1033	60	8.0	8.0	NA	NA	480	200	3	0.0015	<0.01
52/290421/03	51	33	Adjacent site perimeter fence	R	0936	1036	60	8.0	8.0	NA	NA	480	200	2.5	0.0013	<0.01
52/290421/04	50	21	Adjacent site perimeter fence	R	0941	1041	60	8.0	8.0	NA	NA	480	200	1.5	0.0007	<0.01
52/290421/05	49	14	Adjacent to excavation area	R	0945	1045	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
			End of samples													

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

2671

AIRBORNE FIBRE MONITORING | REPORT No. 27459

MICROSCOPE REF:	MIC-06
MICROSCOPE SET UP:	YES
HSE/NPL GROUP:	5
GRATICULE DIAM. (microns)	100
FLOWMETER:	HFM-12
ATMOS. PRESSURE (mb):	998
TEMPERATURE (ºC):	14
WEATHER CONDITIONS:	Sunny
FLOW CORRECTED:	NA
CORRECTED FLOW (l/min):	NA
FIELD BLANK TAKEN	YES

VISUAL INSPECTION


NUMBER OF INSPECTIONS:	NA
TYPE OF RESPIRATOR	NA
ENCLOSURE CLEAN:	NA
ENCLOSURE INTACT:	NA
INTERIOR OF ENCL. DRY:	NA
N.P.U. OFF AND SEALED	NA
LOCK DOWN SPRAY USED	NA

Limit of Quantification

The limit of quantification is 0.010 fibres /ml. where sample volumes of 480 litres or greater and at least 200 graticule fields are analysed. The result may be reported as 'less than 0.01 fibres /ml'.
Where sample volumes are less than 480 litres and/or less than 200 graticule fields are analysed then the limit of quantification may be greater than 0.01 fibres/ml.

This report must not be reproduced except in full without the approval of 'Fourstage Environmental Ltd.'

APPROXIMATE SITE PLAN (X = SAMPLE)

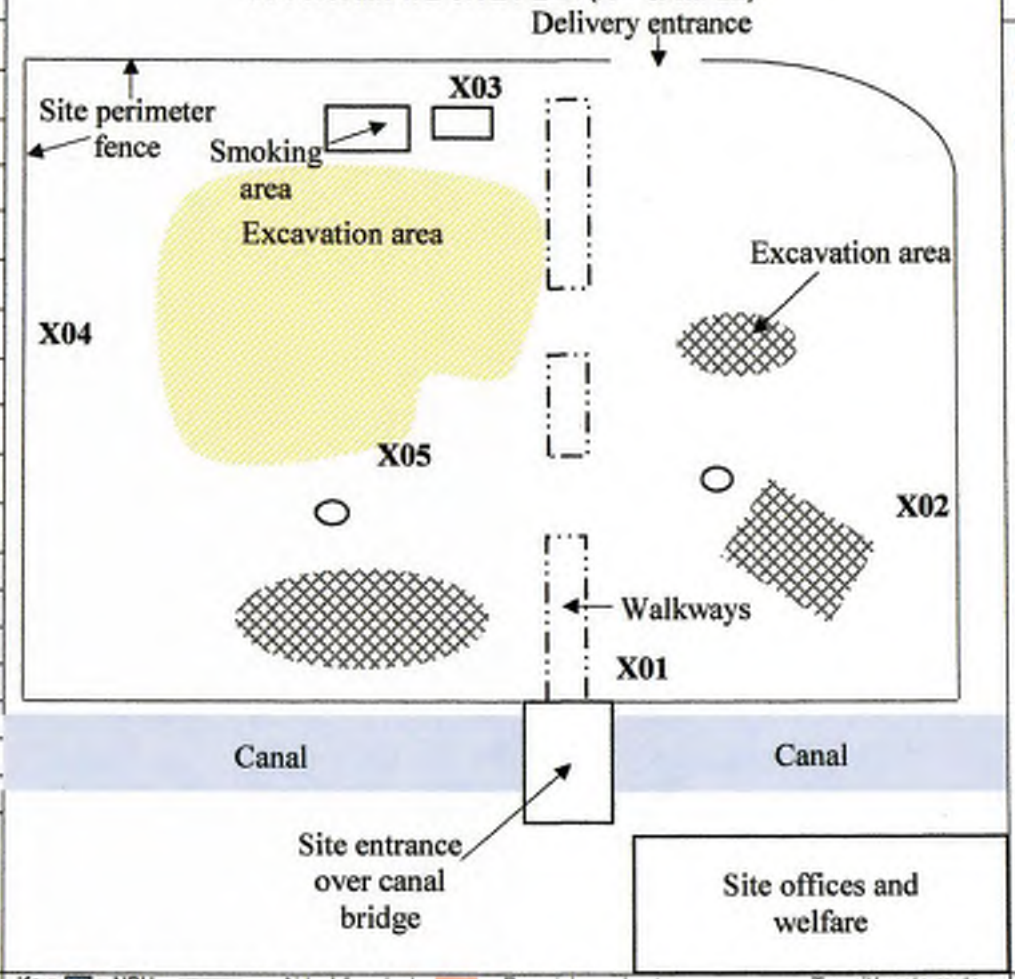

Key: = NPU = Airlock/bag lock = Remaining asbestos = Transit/waste route

The method used for sampling and the subsequent analysis as set out in HSG248 & in-house DOC/002

Contractor's Representative Acknowledgement of diagram accuracy | NAME: A Clifford | SIGNATURE:

COMMENTS
(outside scope of UKAS accreditation)

Reassurance air testing was undertaken to various locations on site while excavation works were being undertaken to various areas.

All results were satisfactory

Is generic Risk Assessment sufficient: YES

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

UKAS TESTING 2671

AIRBORNE FIBRE MONITORING

DATE	13 May 2021	TEST REPORT No.	27474
ANALYST NAME	Liam Carpenter	BACKGROUND	
SITE ADDRESS	CLIENT name & address: Provectus Remediation Ltd, Regent House, Bath Avenue, Wolverhampton, WV1 4EG	LEAK	
Sport city Way, Manchester, M11 3DU	Contractors Name & Address: Provectus Remediation Ltd, Regent House, Bath Avenue, Wolverhampton, WV1 4EG	CLEARANCE	
ANALYST SIGNATURE		RE-ASSURANCE: YES	APPROX. ENCLOSURE AREA/VOL (m²/m³): NA
		PERSONAL	MEASUREMENTS REQ'D: NA
		STATIC	No. SAMPLES TAKEN: 5
		RPE checks made: NA	FILTER DIAM. (mm): 22
		LAB REF: DN62 XNA	ASBESTOS REMOVAL OPERATIC
			Reassurance air testing during excavation works on site.

EXPOSURE TIME (minutes): NA

TYPE OF ASBESTOS (outside scope of UKAS accreditation): Not known

SAMPLE REF.	FILTER HEAD REF No.	PUMP REF No.	SAMPLE LOCATION	TYPE OF TEST	START TIME	END TIME	SAMPLE LENGTH	FLOW LITRE/min. START	FLOW LITRE/min. END	DUST DISTURB MINUTES	DUST DISTURB TYPE	LITRE	FIELDS	FIBRES	CONC. ACTUAL FIBRE/ml	CONC REPORT FIBRE/
52/130521/01	54	39	Adjacent site perimeter fence	R	0926	1026	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.0
52/130521/02	53	34	Adjacent site perimeter fence	R	0930	1030	60	8.0	8.0	NA	NA	480	200	2.5	0.0013	<0.0
52130521/03	51	33	Adjacent site perimeter fence	R	0933	1033	60	8.0	8.0	NA	NA	480	200	1	0.0005	<0.0
52/130521/04	50	21	Adjacent site perimeter fence	R	0939	1039	60	8.0	8.0	NA	NA	480	200	3	0.0015	<0.0
52/130521/05	49	14	Adjacent to excavation area	R	0944	1044	60	8.0	8.0	NA	NA	480	200	1.5	0.0007	<0.0
			End of samples													

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

UKAS TESTING 2671

AIRBORNE FIBRE MONITORING | REPORT No. 27474

MICROSCOPE REF:	MIC-06
MICROSCOPE SET UP:	YES
HSE/NPL GROUP:	5
GRATICULE DIAM. (microns)	100
FLOWMETER:	HFM-12
ATMOS. PRESSURE (mb):	1001
TEMPERATURE (ºC):	12
WEATHER CONDITIONS:	Sunny
FLOW CORRECTED:	NA
CORRECTED FLOW (l/min):	NA
FIELD BLANK TAKEN	YES

VISUAL INSPECTION


NUMBER OF INSPECTIONS:	NA
TYPE OF RESPIRATOR	NA
ENCLOSURE CLEAN:	NA
ENCLOSURE INTACT:	NA
INTERIOR OF ENCL. DRY:	NA
N.P.U. OFF AND SEALED	NA
LOCK DOWN SPRAY USED	NA

Limit of Quantification

The limit of quantification is 0.010 fibres /ml. where sample volumes of 480 litres or greater and at least 200 graticule fields are analysed. The result may be reported as 'less than 0.01 fibres /ml'.
Where sample volumes are less than 480 litres and/or less than 200 graticule fields are analysed then the limit of quantification may be greater than 0.01 fibres/ml.

This report must not be reproduced except in full without the approval of 'Fourstage Environmental Ltd.'

PPROXIMATE SITE PLAN (X = SAMPLE)

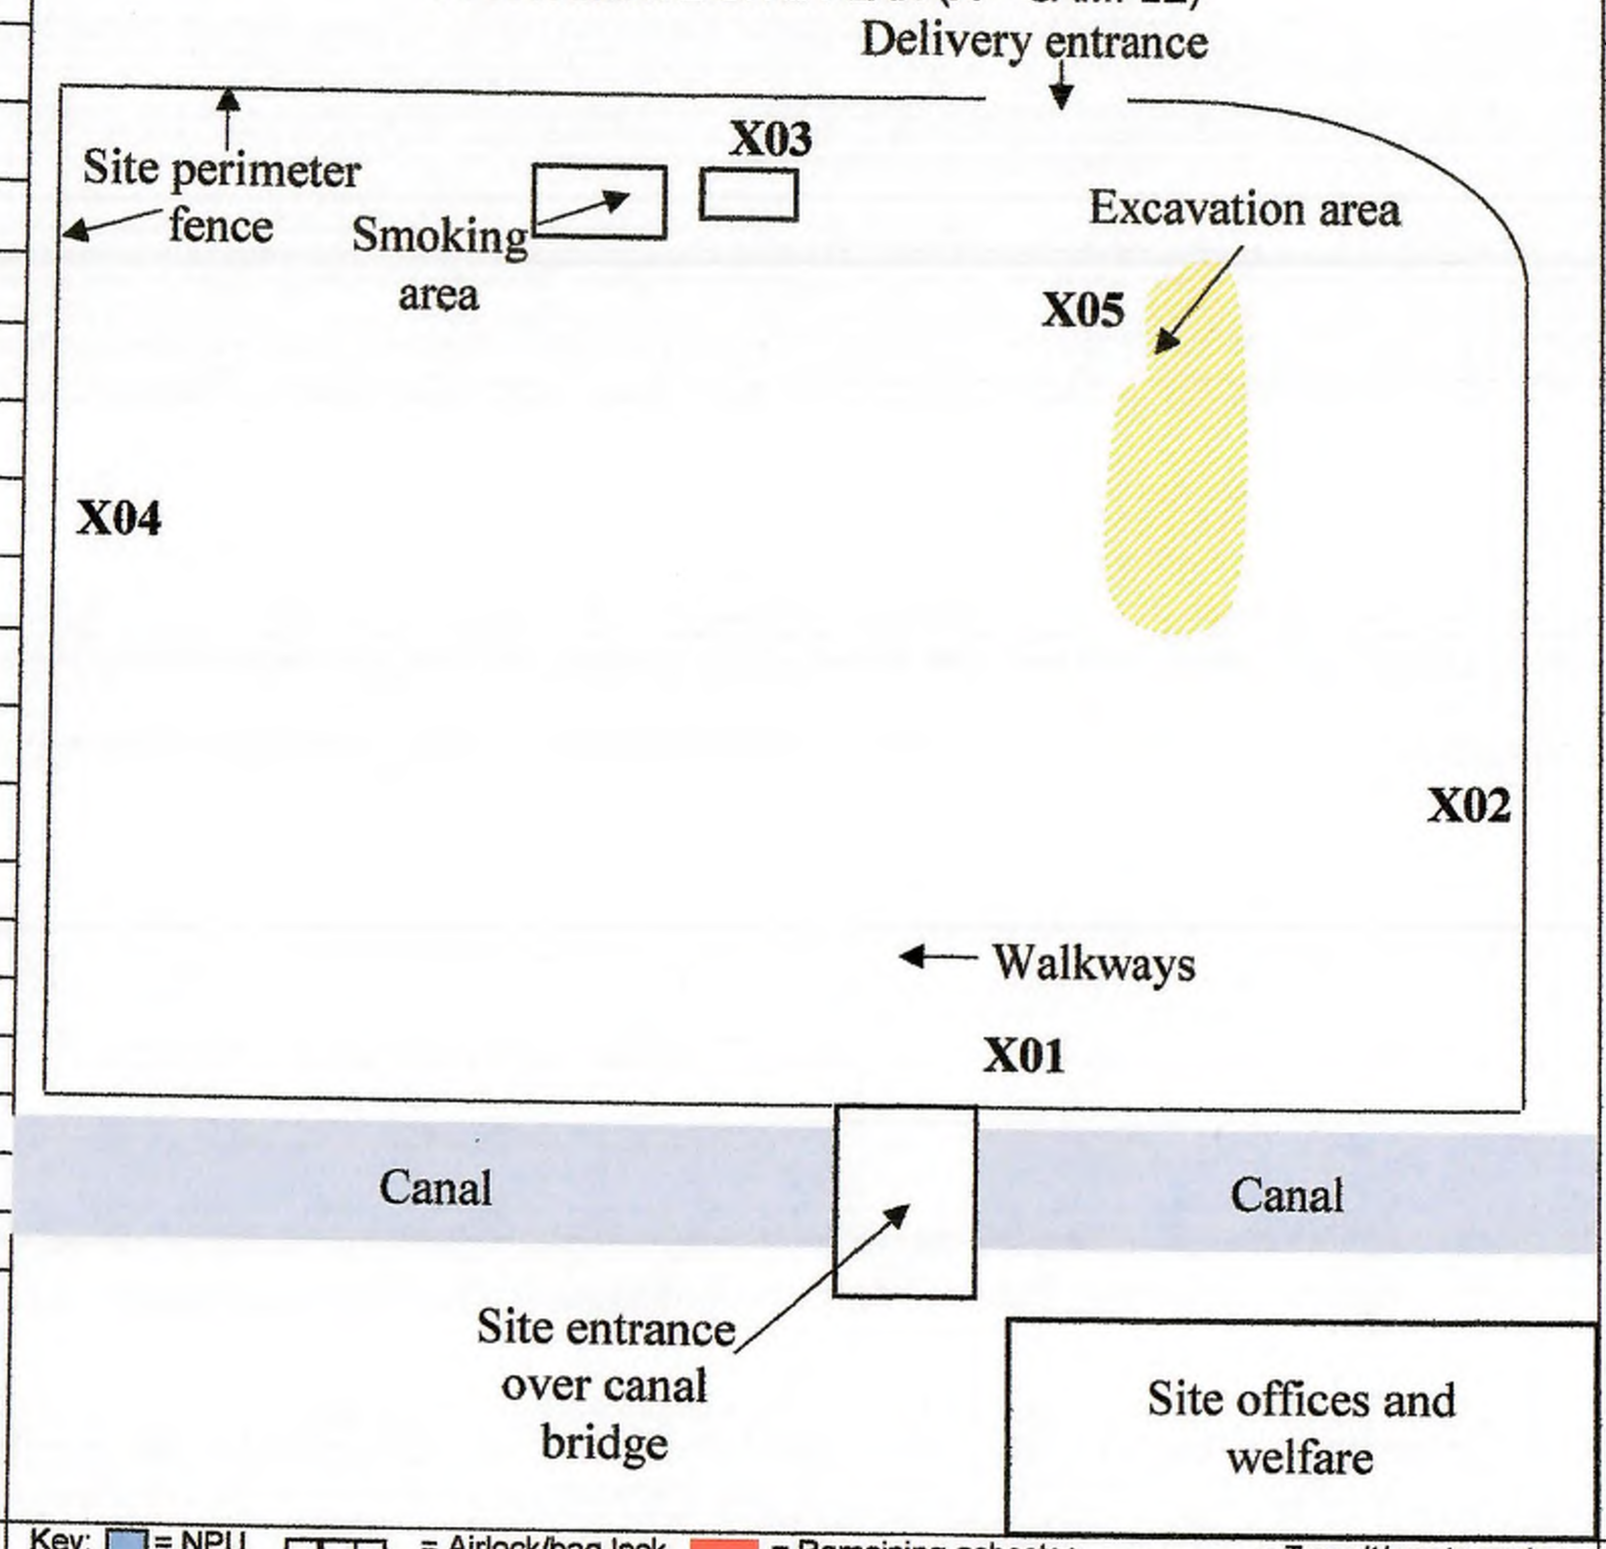

Key: = NPU = Airlock/bag lock = Remaining asbestos = Transit/waste route

The method used for sampling and the subsequent analysis as set out in HSG248 & in-house DOC/002

Contractor's Representative Acknowledgement of diagram accuracy | NAME: A. CLIFFORD | SIGNATURE: A. Clifford

COMMENTS (outside scope of UKAS accreditatic

Reassurance air testing wa undertaken to various locations on site while excavation works were bei undertaken to various area

All results were satisfactory

Is generic Risk Assessment sufficient | YE

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

UKAS TESTING 2671

AIRBORNE FIBRE MONITORING

DATE	20 May 2021		TEST REPORT No.	27483	
ANALYST NAME	Liam Carpenter		BACKGROUND		APPROX. ENCLOSURE AREA/VOL (m²/m³) NA
SITE ADDRESS	CLIENT name & address	Contractors Name & Address	LEAK		
Sport city Way Manchester M11 3DU	Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG	Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG	CLEARANCE		MEASUREMENTS REQ'D NA
			RE-ASSURANCE	YES	No. SAMPLES TAKEN 5
			PERSONAL		FILTER DIAM. (mm) 22
			STATIC		ASBESTOS REMOVAL OPERATION
			RPE checks made	NA	Reassurance air testing during excavation works on site.
ANALYST SIGNATURE			LAB REF: DN62 XNA		

EXPOSURE TIME (minutes) NA — TYPE OF ASBESTOS (outside scope of UKAS accreditation) Not known

SAMPLE REF.	FILTER HEAD REF No.	PUMP REF No.	SAMPLE LOCATION	TYPE OF TEST	START TIME	END TIME	SAMPLE LENGTH	FLOW LITRE/min. START	FLOW LITRE/min. END	DUST DISTURB MINUTES	DUST DISTURB TYPE	LITRE	FIELDS	FIBRES	CONC. ACTUAL FIBRE/ml	CONC. REPORTED FIBRE/ml
52/200521/01	54	39	Adjacent site perimeter fence	R	0733	0833	60	8.0	8.0	NA	NA	480	200	1	0.0005	<0.01
52/200521/02	53	34	Adjacent site perimeter fence	R	0735	0835	60	8.0	8.0	NA	NA	480	200	2.5	0.0013	<0.01
52200521/03	51	33	Adjacent site perimeter fence	R	0737	0827	60	8.0	8.0	NA	NA	480	200	3	0.0015	<0.01
52/200521/04	50	21	Adjacent site perimeter fence	R	0740	0840	60	8.0	8.0	NA	NA	480	200	1.5	0.0007	<0.01
52/200521/05	49	14	Adjacent to excavation area	R	0744	0844	60	8.0	8.0	NA	NA	480	200	1.5	0.0007	<0.01
			End of samples													

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

UKAS TESTING 2671

AIRBORNE FIBRE MONITORING | REPORT No. 27483

MICROSCOPE REF:	MIC-06
MICROSCOPE SET UP:	YES
HSE/NPL GROUP:	5
GRATICULE DIAM. (microns)	100
FLOWMETER:	HFM-12
ATMOS. PRESSURE (mb):	1001
TEMPERATURE (°C):	12
WEATHER CONDITIONS:	Sunny
FLOW CORRECTED:	NA
CORRECTED FLOW (l/min):	NA
FIELD BLANK TAKEN	YES

VISUAL INSPECTION


NUMBER OF INSPECTIONS:	NA
TYPE OF RESPIRATOR	NA
ENCLOSURE CLEAN:	NA
ENCLOSURE INTACT:	NA
INTERIOR OF ENCL. DRY:	NA
N.P.U. OFF AND SEALED	NA
LOCK DOWN SPRAY USED	NA

Limit of Quantification

The limit of quantification is 0.010 fibres /ml. where sample volumes of 480 litres or greater and at least 200 graticule fields are analysed. The result may be reported as 'less than 0.01 fibres /ml'.
Where sample volumes are less than 480 litres and/or less than 200 graticule fields are analysed then the limit of quantification may be greater than 0.01 fibres/ml.

This report must not be reproduced except in full without the approval of 'Fourstage Environmental Ltd.'

PPROXIMATE SITE PLAN (X = SAMPLE)

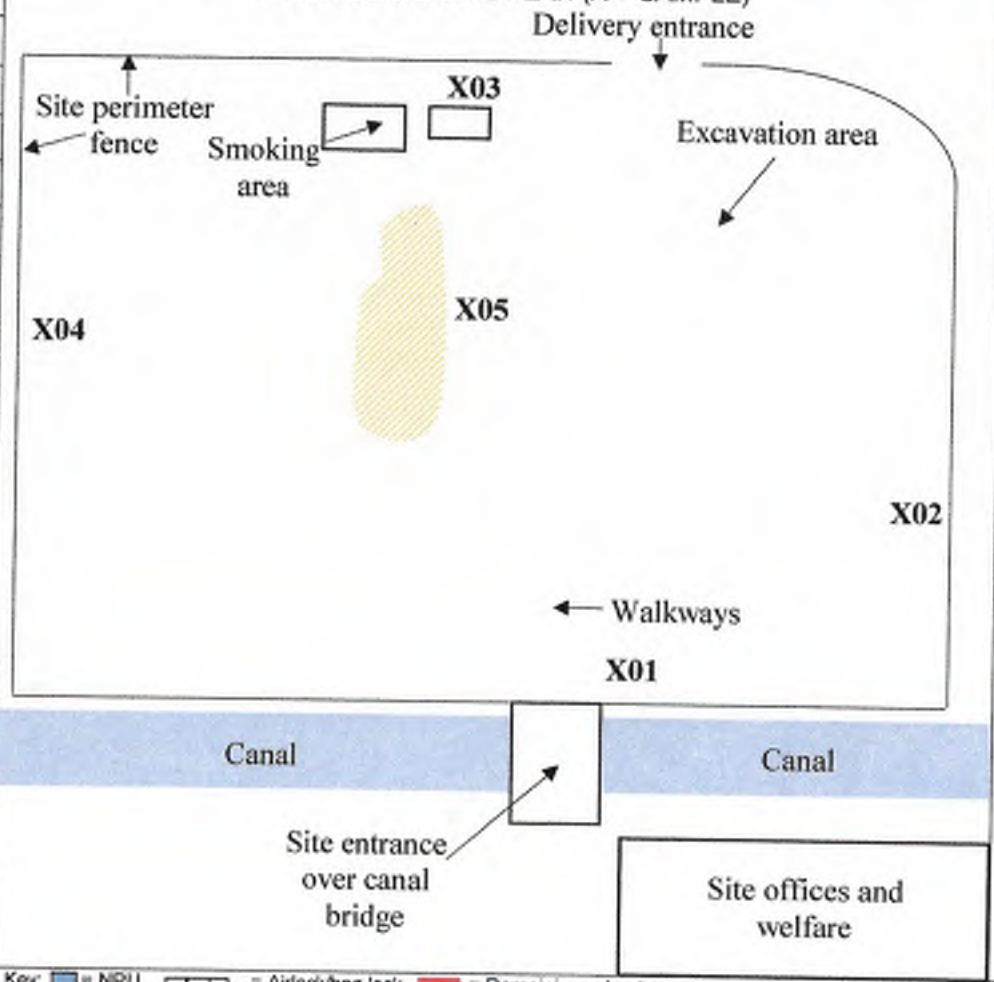

Key: ■ = NPU ▭▭▭ = Airlock/bag lock ■ = Remaining asbestos - - - = Transit/waste route

The method used for sampling and the subsequent analysis as set out in HSG248 & in-house DOC/002

Contractor's Representative Acknowledgement of diagram accuracy	NAME: T. Haigh	SIGNATURE:

COMMENTS (outside scope of UKAS accreditation)

Reassurance air testing was undertaken to various locations on site while excavation works were being undertaken to various areas.

All results were satisfactory

Is generic Risk Assessment sufficient	YES

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

UKAS TESTING 2671

AIRBORNE FIBRE MONITORING

TEST REPORT No. 27487

DATE	27 May 2021	BACKGROUND		APPROX. ENCLOSURE AREA/VOL (m²/m³)	NA
ANALYST NAME	Liam Carpenter	LEAK			
SITE ADDRESS	CLIENT name & address / Contractors Name & Address	CLEARANCE		MEASUREMENTS REQ'D	NA
Sport city Way Manchester M11 3DU	Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG / Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG	RE-ASSURANCE	YES	No. SAMPLES TAKEN	5
		PERSONAL		FILTER DIAM. (mm)	22
		STATIC		ASBESTOS REMOVAL OPERATIO	
		RPE checks made	NA	Reassurance air testing during excavation works on site.	
		LAB REF: DN62 XNA			

ANALYST SIGNATURE

EXPOSURE TIME (minutes) NA — TYPE OF ASBESTOS (outside scope of UKAS accreditation) Not known

SAMPLE REF.	FILTER HEAD REF No.	PUMP REF No.	SAMPLE LOCATION	TYPE OF TEST	START TIME	END TIME	SAMPLE LENGTH	FLOW LITRE/min. START	FLOW LITRE/min. END	DUST DISTURB MINUTES	DUST DISTURB TYPE	LITRE	FIELDS	FIBRES	CONC. ACTUAL FIBRE/ml	CONC REPORT FIBRE/
52/270521/01	54	39	Adjacent site perimeter fence	R	0929	1029	60	8.0	8.0	NA	NA	480	200	1	0.0005	<0.0
52/270521/02	53	34	Adjacent site perimeter fence	R	0933	1033	60	8.0	8.0	NA	NA	480	200	3	0.0015	<0.0
52270521/03	51	33	Adjacent site perimeter fence	R	0937	1037	60	8.0	8.0	NA	NA	480	200	2.5	0.0013	<0.0
52/270521/04	50	21	Adjacent site perimeter fence	R	0941	1041	60	8.0	8.0	NA	NA	480	200	1.5	0.0007	<0.0
52/270521/05	49	14	Adjacent to excavation area	R	0944	1044	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.0
			End of samples													

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

UKAS TESTING 2671

AIRBORNE FIBRE MONITORING | REPORT No. 27487

MICROSCOPE REF:	MIC-06
MICROSCOPE SET UP:	YES
HSE/NPL GROUP:	5
GRATICULE DIAM. (microns)	100
FLOWMETER:	HFM-12
ATMOS. PRESSURE (mb):	1001
TEMPERATURE (ºC):	16
WEATHER CONDITIONS:	Sunny
FLOW CORRECTED:	NA
CORRECTED FLOW (l/min):	NA
FIELD BLANK TAKEN	YES

VISUAL INSPECTION


NUMBER OF INSPECTIONS:	NA
TYPE OF RESPIRATOR	NA
ENCLOSURE CLEAN:	NA
ENCLOSURE INTACT:	NA
INTERIOR OF ENCL. DRY:	NA
N.P.U. OFF AND SEALED	NA
LOCK DOWN SPRAY USED	NA

Limit of Quantification

The limit of quantification is 0.010 fibres /ml. where sample volumes of 480 litres or greater and at least 200 graticule fields are analysed. The result may be reported as 'less than 0.01 fibres /ml'.
Where sample volumes are less than 480 litres and/or less than 200 graticule fields are analysed then the limit of quantification may be greater than 0.01 fibres/ml.

This report must not be reproduced except in full without the approval of 'Fourstage Environmental Ltd.'

PPROXIMATE SITE PLAN (X = SAMPLE)

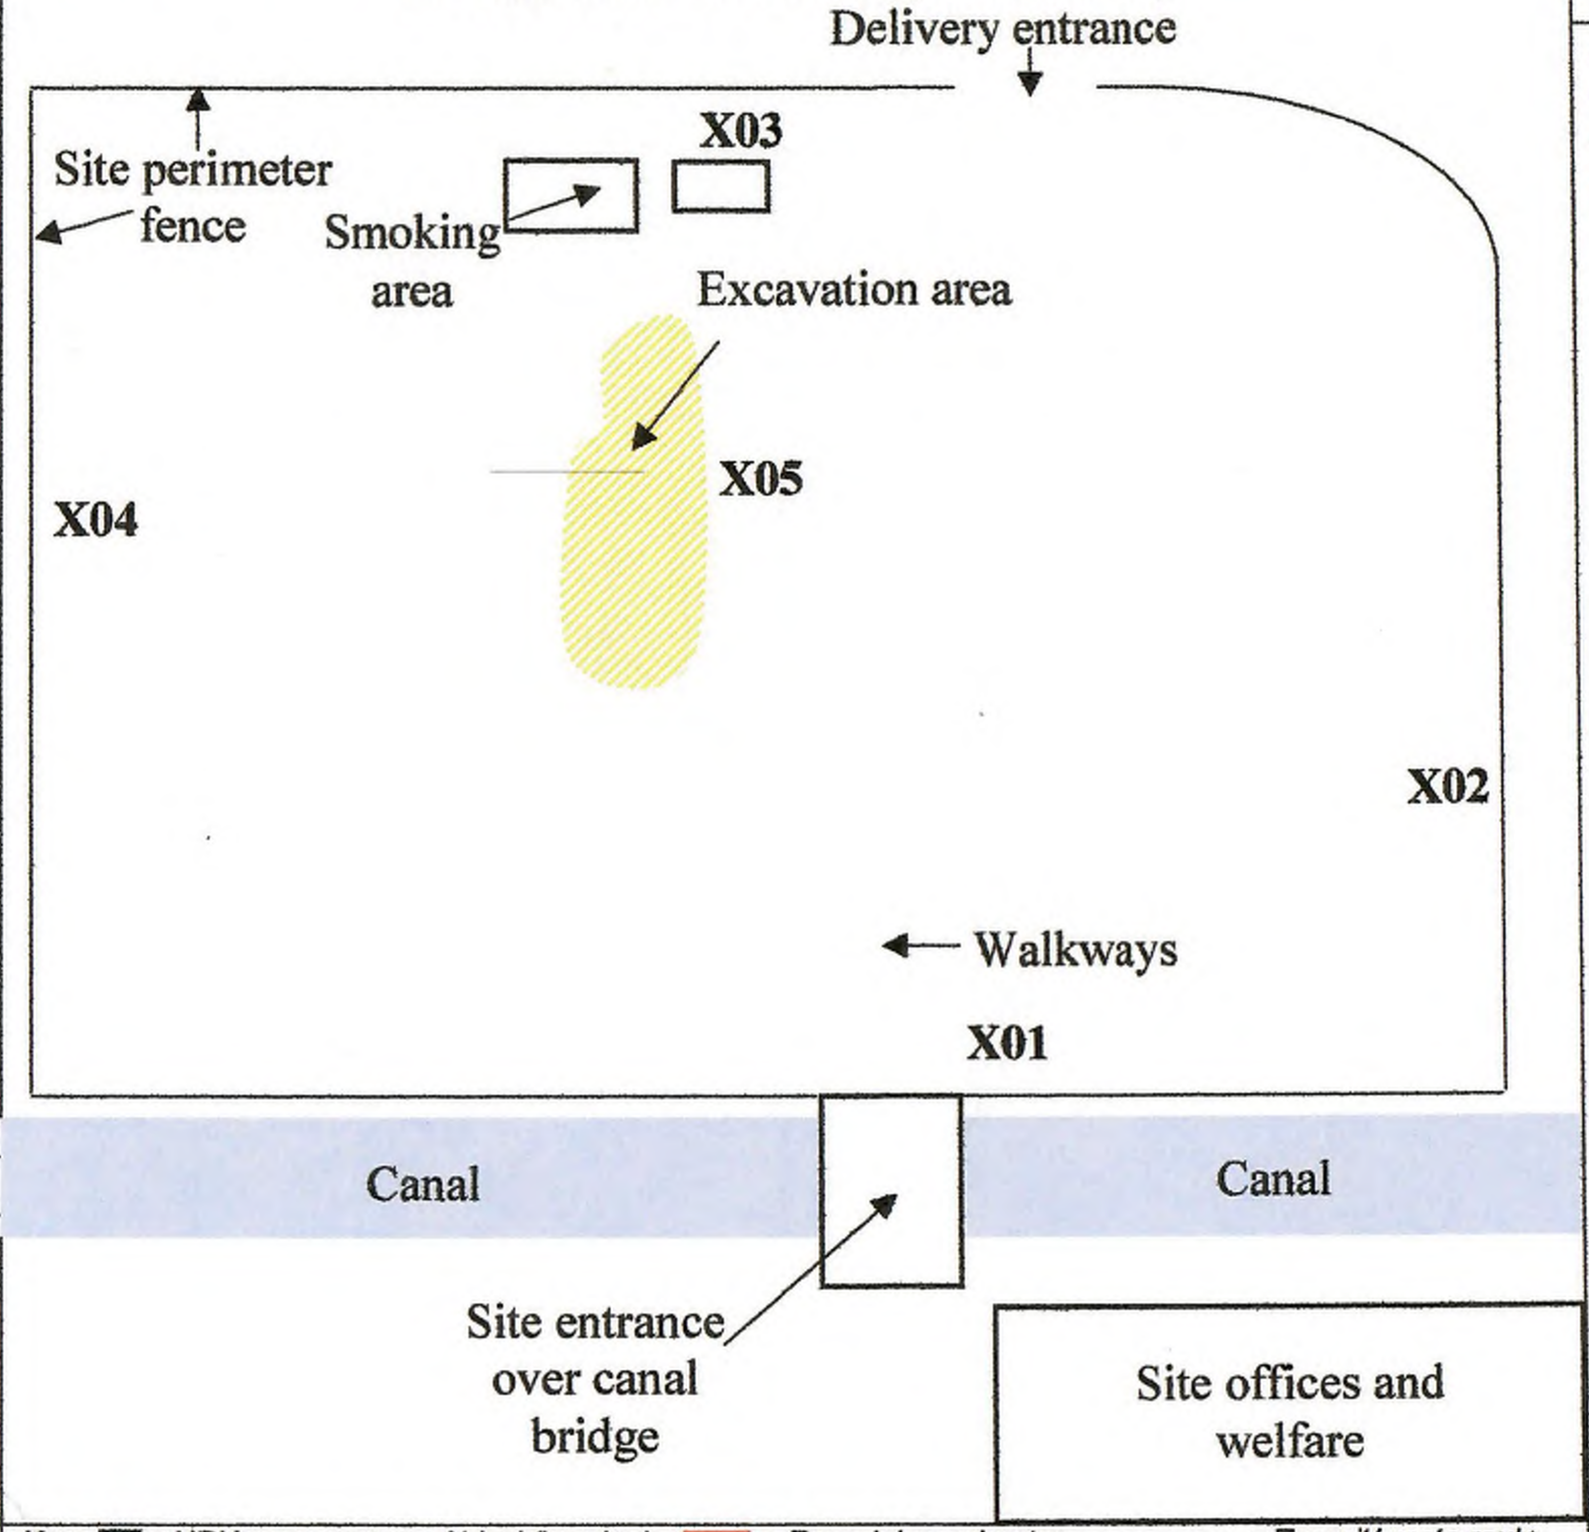

Key: = NPU = Airlock/bag lock = Remaining asbestos = Transit/waste route

The method used for sampling and the subsequent analysis as set out in HSG248 & in-house DOC/002

Contractor's Representative Acknowledgement of diagram accuracy | NAME: T Harrington | SIGNATURE:

COMMENTS (outside scope of UKAS accreditation)

Reassurance air testing was undertaken to various locations on site while excavation works were being undertaken to various areas

All results were satisfactory

Is generic Risk Assessment sufficient: YE

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

2671

AIRBORNE FIBRE MONITORING

TEST REPORT No. 27489

DATE	*1 June 2021*		**B**ACKGROUND		APPROX. ENCLOSURE AREA/VOL (m^2/m^3)	*NA*
ANALYST NAME	*Liam Carpenter*		**L**EAK			
SITE ADDRESS	CLIENT name & address	Contractors Name & Address	**C**LEARANCE		MEASUREMENTS REQ'D	*NA*
Sport city Way *Manchester* *M11 3DU*	*Provectus Remediation Ltd* *Regent House* *Bath Avenue* *Wolverhampton* *WV1 4EG*	*Provectus Remediation Ltd* *Regent House* *Bath Avenue* *Wolverhampton* *WV1 4EG*	**R**E-ASSURANCE	*YES*	No. SAMPLES TAKEN	*5*
			PERSONAL		FILTER DIAM. (mm)	*22*
			STATIC		ASBESTOS REMOVAL OPERATION	
			RPE checks made	*NA*	*Reassurance air testing during excavation works on site.*	
			LAB REF: **DN62 XNA**			

ANALYST SIGNATURE					EXPOSURE TIME (minutes)			*NA*		TYPE OF ASBESTOS (outside scope of UKAS accreditation)			*Not known*			
SAMPLE REF.	FILTER HEAD REF No.	PUMP REF No.	SAMPLE LOCATION	TYPE OF TEST	START TIME	END TIME	SAMPLE LENGTH	FLOW LITRE/min. START	FLOW LITRE/min. END	DUST DISTURB MINUTES	DUST DISTURB TYPE	LITRE	FIELDS	FIBRES	CONC. ACTUAL FIBRE/ml	CONC. REPORTED FIBRE/ml
52/010621/01	*54*	*39*	*Adjacent site perimeter fence*	*R*	*0935*	*1035*	*60*	*8.0*	*8.0*	*NA*	*NA*	*480*	*200*	*2*	*0.0010*	*<0.01*
52/010621/02	*53*	*34*	*Adjacent site perimeter fence*	*R*	*0939*	*1039*	*60*	*8.0*	*8.0*	*NA*	*NA*	*480*	*200*	*3*	*0.0015*	*<0.01*
52010621/03	*51*	*33*	*Adjacent site perimeter fence*	*R*	*0943*	*1043*	*60*	*8.0*	*8.0*	*NA*	*NA*	*480*	*200*	*1*	*0.0005*	*<0.01*
52/010621/04	*50*	*21*	*Adjacent site perimeter fence*	*R*	*0947*	*1047*	*60*	*8.0*	*8.0*	*NA*	*NA*	*480*	*200*	*1.5*	*0.0007*	*<0.01*
52/010621/05	*49*	*14*	*Adjacent to excavation area*	*R*	*0951*	*1051*	*60*	*8.0*	*8.0*	*NA*	*NA*	*480*	*200*	*2.5*	*0.0013*	*<0.01*
			End of samples													

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

2671

AIRBORNE FIBRE MONITORING	REPORT No.	27489


MICROSCOPE REF:	MIC-06
MICROSCOPE SET UP:	YES
HSE/NPL GROUP:	5
GRATICULE DIAM. (microns)	100
FLOWMETER:	HFM-12
ATMOS. PRESSURE (mb):	1001
TEMPERATURE (ºC):	16
WEATHER CONDITIONS:	Sunny
FLOW CORRECTED:	NA
CORRECTED FLOW (l/min):	NA
FIELD BLANK TAKEN	YES
VISUAL INSPECTION	
NUMBER OF INSPECTIONS:	NA
TYPE OF RESPIRATOR	NA
ENCLOSURE CLEAN:	NA
ENCLOSURE INTACT:	NA
INTERIOR OF ENCL. DRY:	NA
N.P.U. OFF AND SEALED	NA
LOCK DOWN SPRAY USED	NA

Limit of Quantification

The limit of quantification is 0.010 fibres /ml. where sample volumes of 480 litres or greater and at least 200 graticule fields are analysed. The result may be reported as 'less than 0.01 fibres /ml'.
Where sample volumes are less than 480 litres and/or less than 200 graticule fields are analysed then the limit of quantification may be greater than 0.01 fibres/ml.

This report must not be reproduced except in full without the approval of 'Fourstage Environmental Ltd.'

PPROXIMATE SITE PLAN (X = SAMPLE)

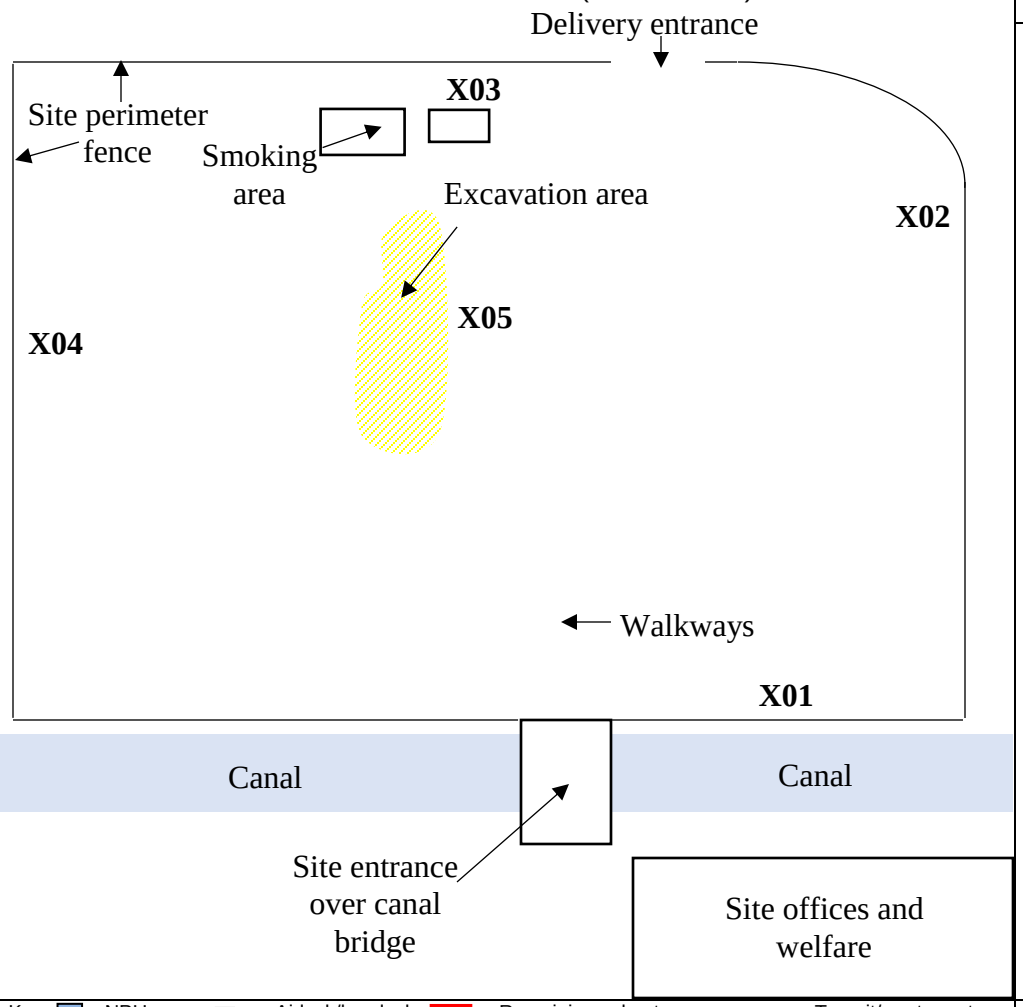

Key: = NPU = Airlock/bag lock = Remaining asbestos = Transit/waste route

The method used for sampling and the subsequent analysis as set out in HSG248 & in-house DOC/002

Contractor's Representative Acknowledgement of diagram accuracy	NAME:	SIGNATURE:

COMMENTS
(outside scope of UKAS accreditation)

Reassurance air testing was undertaken to various locations on site while excavation works were being undertaken to various areas.

All results were satisfactory

Is generic Risk Assessment sufficient	YES

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

UKAS TESTING 2671

AIRBORNE FIBRE MONITORING

TEST REPORT No. **27493**

DATE	10 June 2021	BACKGROUND		APPROX. ENCLOSURE AREA/VOL (m²/m³)	NA
ANALYST NAME	Liam Carpenter	LEAK			
SITE ADDRESS	CLIENT name & address / Contractors Name & Address	CLEARANCE		MEASUREMENTS REQ'D	NA
Sport city Way Manchester M11 3DU	Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG / Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG	RE-ASSURANCE	YES	No. SAMPLES TAKEN	5
		PERSONAL		FILTER DIAM. (mm)	22
		STATIC		ASBESTOS REMOVAL OPERATION	
		RPE checks made	NA	Reassurance air testing during excavation works on site.	
		LAB REF: DN62 XNA			

ANALYST SIGNATURE

EXPOSURE TIME (minutes) NA — TYPE OF ASBESTOS (outside scope of UKAS accreditation): Not known

SAMPLE REF.	FILTER HEAD REF No.	PUMP REF No.	SAMPLE LOCATION	TYPE OF TEST	START TIME	END TIME	SAMPLE LENGTH	FLOW LITRE/min. START	FLOW LITRE/min. END	DUST DISTURB MINUTES	DUST DISTURB TYPE	LITRE	FIELDS	FIBRES	CONC. ACTUAL FIBRE/ml	CONC. REPORTED FIBRE/ml
52/100621/01	54	39	Adjacent site perimeter fence	R	0939	1039	60	8.0	8.0	NA	NA	480	200	2.5	0.0013	<0.01
52/100621/02	53	34	Adjacent site perimeter fence	R	0943	1043	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
52/100621/03	51	33	Adjacent site perimeter fence	R	0946	1046	60	8.0	8.0	NA	NA	480	200	3	0.0015	<0.01
52/100621/04	50	21	Adjacent site perimeter fence	R	0949	1049	60	8.0	8.0	NA	NA	480	200	1.5	0.0007	<0.01
52/100621/05	49	14	Adjacent to excavation area	R	0954	1054	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
			End of samples													

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

2671

AIRBORNE FIBRE MONITORING | REPORT No. 27493

MICROSCOPE REF:	MIC-06
MICROSCOPE SET UP:	YES
HSE/NPL GROUP:	5
GRATICULE DIAM. (microns)	100
FLOWMETER:	HFM-12
ATMOS. PRESSURE (mb):	1001
TEMPERATURE (°C):	14
WEATHER CONDITIONS:	Sunny
FLOW CORRECTED:	NA
CORRECTED FLOW (l/min):	NA
FIELD BLANK TAKEN	YES

VISUAL INSPECTION


NUMBER OF INSPECTIONS:	NA
TYPE OF RESPIRATOR	NA
ENCLOSURE CLEAN:	NA
ENCLOSURE INTACT:	NA
INTERIOR OF ENCL. DRY:	NA
N.P.U. OFF AND SEALED	NA
LOCK DOWN SPRAY USED	NA

Limit of Quantification

The limit of quantification is 0.010 fibres /ml. where sample volumes of 480 litres or greater and at least 200 graticule fields are analysed. The result may be reported as 'less than 0.01 fibres /ml'.
Where sample volumes are less than 480 litres and/or less than 200 graticule fields are analysed then the limit of quantification may be greater than 0.01 fibres/ml.

This report must not be reproduced except in full without the approval of 'Fourstage Environmental Ltd.'

PPROXIMATE SITE PLAN (X = SAMPLE)

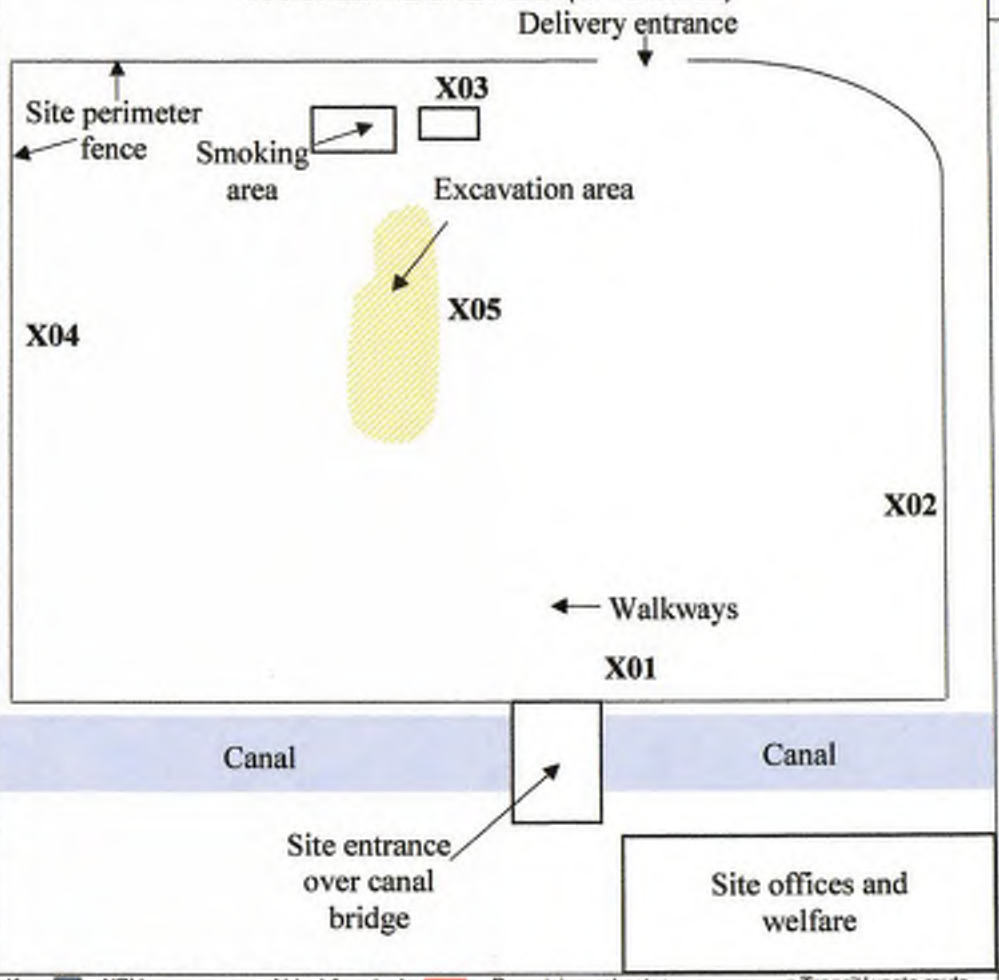

Key: = NPU = Airlock/bag lock = Remaining asbestos = Transit/waste route

The method used for sampling and the subsequent analysis as set out in HSG248 & in-house DOC/002

Contractor's Representative Acknowledgement of diagram accuracy	NAME:	SIGNATURE:

COMMENTS (outside scope of UKAS accreditation)

Reassurance air testing was undertaken to various locations on site while excavation works were being undertaken to various areas.

All results were satisfactory

Is generic Risk Assessment sufficient	YES

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

2671

AIRBORNE FIBRE MONITORING

TEST REPORT No. 27495

DATE	*16 June 2021*		**B**ACKGROUND		APPROX. ENCLOSURE AREA/VOL (m^2/m^3)	*NA*
ANALYST NAME	*Liam Carpenter*		**L**EAK			
SITE ADDRESS	CLIENT name & address	Contractors Name & Address	**C**LEARANCE		MEASUREMENTS REQ'D	*NA*
Sport city Way *Manchester* *M11 3DU*	*Provectus Remediation Ltd* *Regent House* *Bath Avenue* *Wolverhampton* *WV1 4EG*	*Provectus Remediation Ltd* *Regent House* *Bath Avenue* *Wolverhampton* *WV1 4EG*	**R**E-ASSURANCE	*YES*	No. SAMPLES TAKEN	*5*
			PERSONAL		FILTER DIAM. (mm)	*22*
			STATIC		ASBESTOS REMOVAL OPERATION	
			RPE checks made	*NA*	*Reassurance air testing during excavation works on site.*	
			LAB REF: **DN62 XNA**			

ANALYST SIGNATURE					EXPOSURE TIME (minutes)			*NA*		TYPE OF ASBESTOS (outside scope of UKAS accreditation)			*Not known*			
SAMPLE REF.	FILTER HEAD REF No.	PUMP REF No.	SAMPLE LOCATION	TYPE OF TEST	START TIME	END TIME	SAMPLE LENGTH	FLOW LITRE/min. START	FLOW LITRE/min. END	DUST DISTURB MINUTES	DUST DISTURB TYPE	LITRE	FIELDS	FIBRES	CONC. ACTUAL FIBRE/ml	CONC. REPORTED FIBRE/ml
52/160621/01	*54*	*39*	*Adjacent site perimeter fence*	*R*	*1033*	*1133*	*60*	*8.0*	*8.0*	*NA*	*NA*	*480*	*200*	*3.5*	*0.0018*	*<0.01*
52/160621/02	*53*	*34*	*Adjacent site perimeter fence*	*R*	*1036*	*1136*	*60*	*8.0*	*8.0*	*NA*	*NA*	*480*	*200*	*1.5*	*0.0007*	*<0.01*
52/160621/03	*51*	*33*	*Adjacent site perimeter fence*	*R*	*1039*	*1139*	*60*	*8.0*	*8.0*	*NA*	*NA*	*480*	*200*	*2.5*	*0.0013*	*<0.01*
52/160621/04	*50*	*21*	*Adjacent site perimeter fence*	*R*	*1044*	*1144*	*60*	*8.0*	*8.0*	*NA*	*NA*	*480*	*200*	*3*	*0.0015*	*<0.01*
52/160621/05	*49*	*14*	*Adjacent to excavation area*	*R*	*1049*	*1149*	*60*	*8.0*	*8.0*	*NA*	*NA*	*480*	*200*	*2*	*0.0010*	*<0.01*
			End of samples													

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

2671


AIRBORNE FIBRE MONITORING	REPORT No.	27495

MICROSCOPE REF:	MIC-06
MICROSCOPE SET UP:	YES
HSE/NPL GROUP:	5
GRATICULE DIAM. (microns)	100
FLOWMETER:	HFM-12
ATMOS. PRESSURE (mb):	1001
TEMPERATURE (ºC):	18
WEATHER CONDITIONS:	Sunny
FLOW CORRECTED:	NA
CORRECTED FLOW (l/min):	NA
FIELD BLANK TAKEN	YES
VISUAL INSPECTION	
NUMBER OF INSPECTIONS:	NA
TYPE OF RESPIRATOR	NA
ENCLOSURE CLEAN:	NA
ENCLOSURE INTACT:	NA
INTERIOR OF ENCL. DRY:	NA
N.P.U. OFF AND SEALED	NA
LOCK DOWN SPRAY USED	NA

Limit of Quantification

The limit of quantification is 0.010 fibres /ml. where sample volumes of 480 litres or greater and at least 200 graticule fields are analysed. The result may be reported as 'less than 0.01 fibres /ml'.
Where sample volumes are less than 480 litres and/or less than 200 graticule fields are analysed then the limit of quantification may be greater than 0.01 fibres/ml.

PPROXIMATE SITE PLAN (X = SAMPLE)

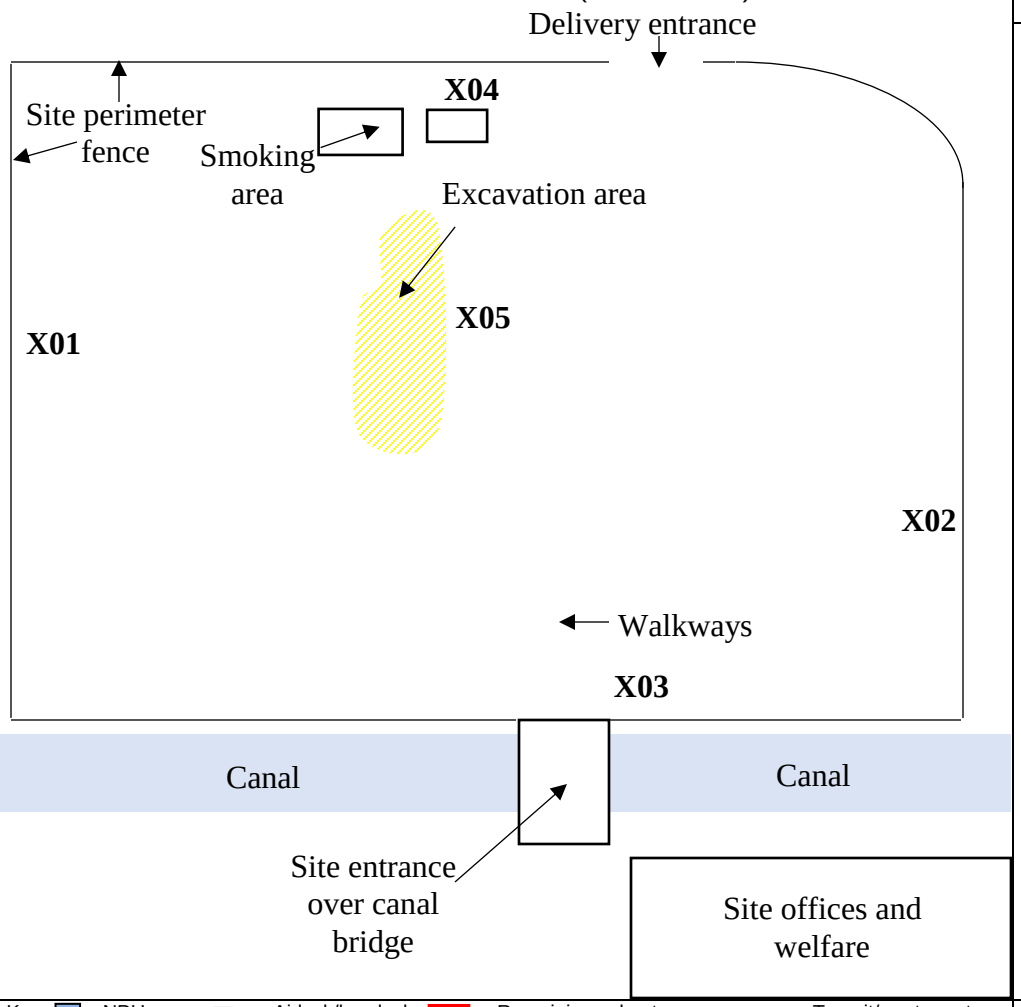

COMMENTS
(outside scope of UKAS accreditation)

Reassurance air testing was undertaken to various locations on site while excavation works were being undertaken to various areas.

All results were satisfactory

Key: = NPU = Airlock/bag lock = Remaining asbestos = Transit/waste route

The method used for sampling and the subsequent analysis as set out in HSG248 & in-house DOC/002

Is generic Risk Assessment sufficient: YES

Contractor's Representative Acknowledgement of diagram accuracy	NAME:	SIGNATURE:

This report must not be reproduced except in full without the approval of 'Fourstage Environmental Ltd.'

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

2671

AIRBORNE FIBRE MONITORING

TEST REPORT No. **30009**

DATE	25 June 2021		BACKGROUND		APPROX. ENCLOSURE AREA/VOL (m²/m³)	NA
ANALYST NAME	Liam Carpenter		LEAK			
SITE ADDRESS	CLIENT name & address	Contractors Name & Address	CLEARANCE		MEASUREMENTS REQ'D	NA
Sport city Way Manchester M11 3DU	Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG	Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG	RE-ASSURANCE	YES	No. SAMPLES TAKEN	5
			PERSONAL		FILTER DIAM. (mm)	22
			STATIC		ASBESTOS REMOVAL OPERATION	
			RPE checks made	NA	Reassurance air testing during excavation works on site.	
			LAB REF: DN62 XNA			

ANALYST SIGNATURE

EXPOSURE TIME (minutes) NA TYPE OF ASBESTOS (outside scope of UKAS accreditation) Not known

SAMPLE REF.	FILTER HEAD REF No.	PUMP REF No.	SAMPLE LOCATION	TYPE OF TEST	START TIME	END TIME	SAMPLE LENGTH	FLOW LITRE/min. START	FLOW LITRE/min. END	DUST DISTURB MINUTES	DUST DISTURB TYPE	LITRE	FIELDS	FIBRES	CONC. ACTUAL FIBRE/ml	CONC. REPORTED FIBRE/ml
52/250621/01	54	39	Adjacent site perimeter fence	R	1113	1213	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
52/250621/02	53	34	Adjacent site perimeter fence	R	1117	1217	60	8.0	8.0	NA	NA	480	200	3.5	0.0018	<0.01
52/250621/03	51	33	Adjacent site perimeter fence	R	1121	1221	60	8.0	8.0	NA	NA	480	200	1.5	0.0007	<0.01
52/250621/04	50	21	Adjacent site perimeter fence	R	1124	1224	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
52/250621/05	49	14	Adjacent to excavation area	R	1129	1229	60	8.0	8.0	NA	NA	480	200	1	0.0005	<0.01
			End of samples													

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

UKAS TESTING 2671

AIRBORNE FIBRE MONITORING — REPORT No. 30009

MICROSCOPE REF:	MIC-06
MICROSCOPE SET UP:	YES
HSE/NPL GROUP:	5
GRATICULE DIAM. (microns)	100
FLOWMETER:	HFM-12
ATMOS. PRESSURE (mb):	NA
TEMPERATURE (°C):	NA
WEATHER CONDITIONS:	Sunny
FLOW CORRECTED:	NA
CORRECTED FLOW (l/min):	NA
FIELD BLANK TAKEN	YES

VISUAL INSPECTION


NUMBER OF INSPECTIONS:	NA
TYPE OF RESPIRATOR	NA
ENCLOSURE CLEAN:	NA
ENCLOSURE INTACT:	NA
INTERIOR OF ENCL. DRY:	NA
N.P.U. OFF AND SEALED	NA
LOCK DOWN SPRAY USED	NA

Limit of Quantification

The limit of quantification is 0.010 fibres /ml. where sample volumes of 480 litres or greater and at least 200 graticule fields are analysed. The result may be reported as 'less than 0.01 fibres /ml'.
Where sample volumes are less than 480 litres and/or less than 200 graticule fields are analysed then the limit of quantification may be greater than 0.01 fibres/ml.

This report must not be reproduced except in full without the approval of 'Fourstage Environmental Ltd.'

PPROXIMATE SITE PLAN (X = SAMPLE)

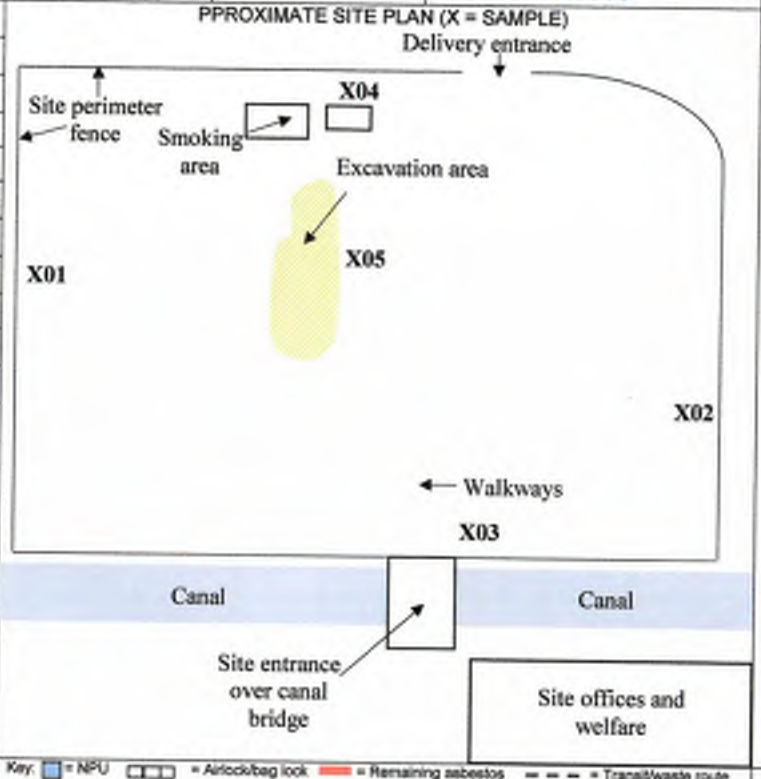

Key: = NPU = Airlock/bag lock = Remaining asbestos = Transit/waste route

The method used for sampling and the subsequent analysis as set out in HSG248 & in-house DOC/002

Contractor's Representative Acknowledgement of diagram accuracy — NAME: C. NICHOLSON — SIGNATURE:

Is generic Risk Assessment sufficient: YES

COMMENTS (outside scope of UKAS accreditation)

Reassurance air testing was undertaken to various locations on site while excavation works were being undertaken to various areas.

All results were satisfactory

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

2671

AIRBORNE FIBRE MONITORING

TEST REPORT No. **30028**

DATE	7 July 2021	BACKGROUND		APPROX. ENCLOSURE AREA/VOL (m²/m³)	NA
ANALYST NAME	Liam Carpenter	LEAK			
SITE ADDRESS	CLIENT name & address / Contractors Name & Address	CLEARANCE		MEASUREMENTS REQ'D	NA
Sport city Way Manchester M11 3DU	Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG / Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG	RE-ASSURANCE	YES	No. SAMPLES TAKEN	5
		PERSONAL		FILTER DIAM. (mm)	22
		STATIC		ASBESTOS REMOVAL OPERATION	
		RPE checks made	NA	Reassurance air testing during excavation works on site.	
		LAB REF: YR16 0WH			
ANALYST SIGNATURE		EXPOSURE TIME (minutes)	NA	TYPE OF ASBESTOS (outside scope of UKAS accreditation)	Not known

SAMPLE REF.	FILTER HEAD REF No.	PUMP REF No.	SAMPLE LOCATION	TYPE OF TEST	START TIME	END TIME	SAMPLE LENGTH	FLOW LITRE/min. START	FLOW LITRE/min. END	DUST DISTURB MINUTES	DUST DISTURB TYPE	LITRE	FIELDS	FIBRES	CONC. ACTUAL FIBRE/ml	CONC. REPORTED FIBRE/ml
52/070721/01	12	45	Adjacent site perimeter fence	R	1048	1148	60	8.0	8.0	NA	NA	480	200	3	0.0015	<0.01
52/070721/02	17	47	Adjacent site perimeter fence	R	1052	1152	60	8.0	8.0	NA	NA	480	200	1	0.0005	<0.01
52/070721/03	18	47	Adjacent site perimeter fence	R	1054	1154	60	8.0	8.0	NA	NA	480	200	2.5	0.0013	<0.01
52/070721/04	14	43	Adjacent site perimeter fence	R	1058	1158	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
52/070721/05	16	48	Adjacent to excavation area	R	1102	1202	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
			End of samples													

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

UKAS TESTING 2671

AIRBORNE FIBRE MONITORING | REPORT No. 30028

MICROSCOPE REF:	MIC-13
MICROSCOPE SET UP:	YES
HSE/NPL GROUP:	5
GRATICULE DIAM. (microns)	100
FLOWMETER:	HFM-12
ATMOS. PRESSURE (mb):	NA
TEMPERATURE (°C):	NA
WEATHER CONDITIONS:	Raining
FLOW CORRECTED:	NA
CORRECTED FLOW (l/min):	NA
FIELD BLANK TAKEN	YES

VISUAL INSPECTION


NUMBER OF INSPECTIONS:	NA
TYPE OF RESPIRATOR	NA
ENCLOSURE CLEAN:	NA
ENCLOSURE INTACT:	NA
INTERIOR OF ENCL. DRY:	NA
N.P.U. OFF AND SEALED	NA
LOCK DOWN SPRAY USED	NA

Limit of Quantification

The limit of quantification is 0.010 fibres /ml. where sample volumes of 480 litres or greater and at least 200 graticule fields are analysed. The result may be reported as 'less than 0.01 fibres /ml'.
Where sample volumes are less than 480 litres and/or less than 200 graticule fields are analysed then the limit of quantification may be greater than 0.01 fibres/ml.

This report must not be reproduced except in full without the approval of 'Fourstage Environmental Ltd.'

PPROXIMATE SITE PLAN (X = SAMPLE)

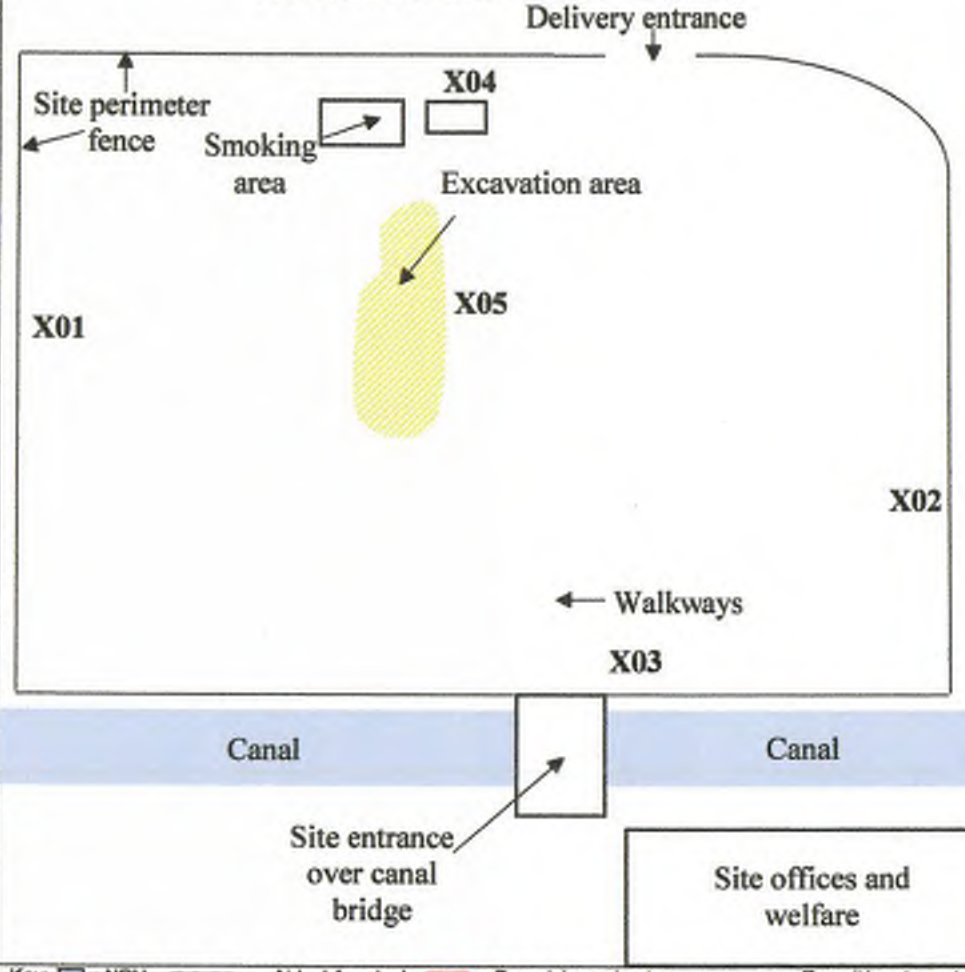

Key: = NPU = Airlock/bag lock = Remaining asbestos = Transit/waste route

The method used for sampling and the subsequent analysis as set out in HSG248 & in-house DOC/002

COMMENTS (outside scope of UKAS accreditation)

Reassurance air testing was undertaken to various locations on site while excavation works were being undertaken to various areas.

All results were satisfactory

Is generic Risk Assessment sufficient		YES
Contractor's Representative Acknowledgement of diagram accuracy	NAME: S. Lane-Hall	SIGNATURE:

Document Reference DOC/039/V17 (07-08-19)

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

2671

AIRBORNE FIBRE MONITORING

TEST REPORT No. **30045**

DATE	16 July 2021	BACKGROUND	
ANALYST NAME	Liam Carpenter	LEAK	
SITE ADDRESS	CLIENT name & address: Provectus Remediation Ltd, Regent House, Bath Avenue, Wolverhampton, WV1 4EG	CLEARANCE	
Sport city Way, Manchester, M11 3DU	Contractors Name & Address: Provectus Remediation Ltd, Regent House, Bath Avenue, Wolverhampton, WV1 4EG	RE-ASSURANCE	YES
		PERSONAL	
		STATIC	
		RPE checks made	NA
		LAB REF: YR16 0WH	

APPROX. ENCLOSURE AREA/VOL (m^2/m^3)	NA
MEASUREMENTS REQ'D	NA
No. SAMPLES TAKEN	5
FILTER DIAM. (mm)	22
ASBESTOS REMOVAL OPERATION	Reassurance air testing during excavation works on site.

ANALYST SIGNATURE

EXPOSURE TIME (minutes) NA

TYPE OF ASBESTOS (outside scope of UKAS accreditation) Not known

SAMPLE REF.	FILTER HEAD REF No.	PUMP REF No.	SAMPLE LOCATION	TYPE OF TEST	START TIME	END TIME	SAMPLE LENGTH	FLOW LITRE/min. START	FLOW LITRE/min. END	DUST DISTURB MINUTES	DUST DISTURB TYPE	LITRE	FIELDS	FIBRES	CONC. ACTUAL FIBRE/ml	CONC. REPORTED FIBRE/ml
52/160721/01	12	45	Adjacent site perimeter fence	R	1131	1231	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
52/160721/02	17	47	Adjacent site perimeter fence	R	1133	1233	60	8.0	8.0	NA	NA	480	200	2.5	0.0013	<0.01
52/160721/03	18	47	Adjacent site perimeter fence	R	1135	1235	60	8.0	8.0	NA	NA	480	200	1	0.0005	<0.01
52/160721/04	14	43	Adjacent site perimeter fence	R	1137	1237	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
52/160721/05	16	48	Adjacent to excavation area	R	1139	1239	60	8.0	8.0	NA	NA	480	200	3.5	0.0018	<0.01
			End of samples													

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

2671

AIRBORNE FIBRE MONITORING | REPORT No. 30045

MICROSCOPE REF:	MIC-13
MICROSCOPE SET UP:	YES
HSE/NPL GROUP:	5
GRATICULE DIAM. (microns)	100
FLOWMETER:	HFM-12
ATMOS. PRESSURE (mb):	NA
TEMPERATURE (ºC):	NA
WEATHER CONDITIONS:	Sunny
FLOW CORRECTED:	NA
CORRECTED FLOW (l/min):	NA
FIELD BLANK TAKEN	YES

VISUAL INSPECTION


NUMBER OF INSPECTIONS:	NA
TYPE OF RESPIRATOR	NA
ENCLOSURE CLEAN:	NA
ENCLOSURE INTACT:	NA
INTERIOR OF ENCL. DRY:	NA
N.P.U. OFF AND SEALED	NA
LOCK DOWN SPRAY USED	NA

Limit of Quantification

The limit of quantification is 0.010 fibres /ml. where sample volumes of 480 litres or greater and at least 200 graticule fields are analysed. The result may be reported as 'less than 0.01 fibres /ml'.
Where sample volumes are less than 480 litres and/or less than 200 graticule fields are analysed then the limit of quantification may be greater than 0.01 fibres/ml.

This report must not be reproduced except in full without the approval of 'Fourstage Environmental Ltd.'

PPROXIMATE SITE PLAN (X = SAMPLE)

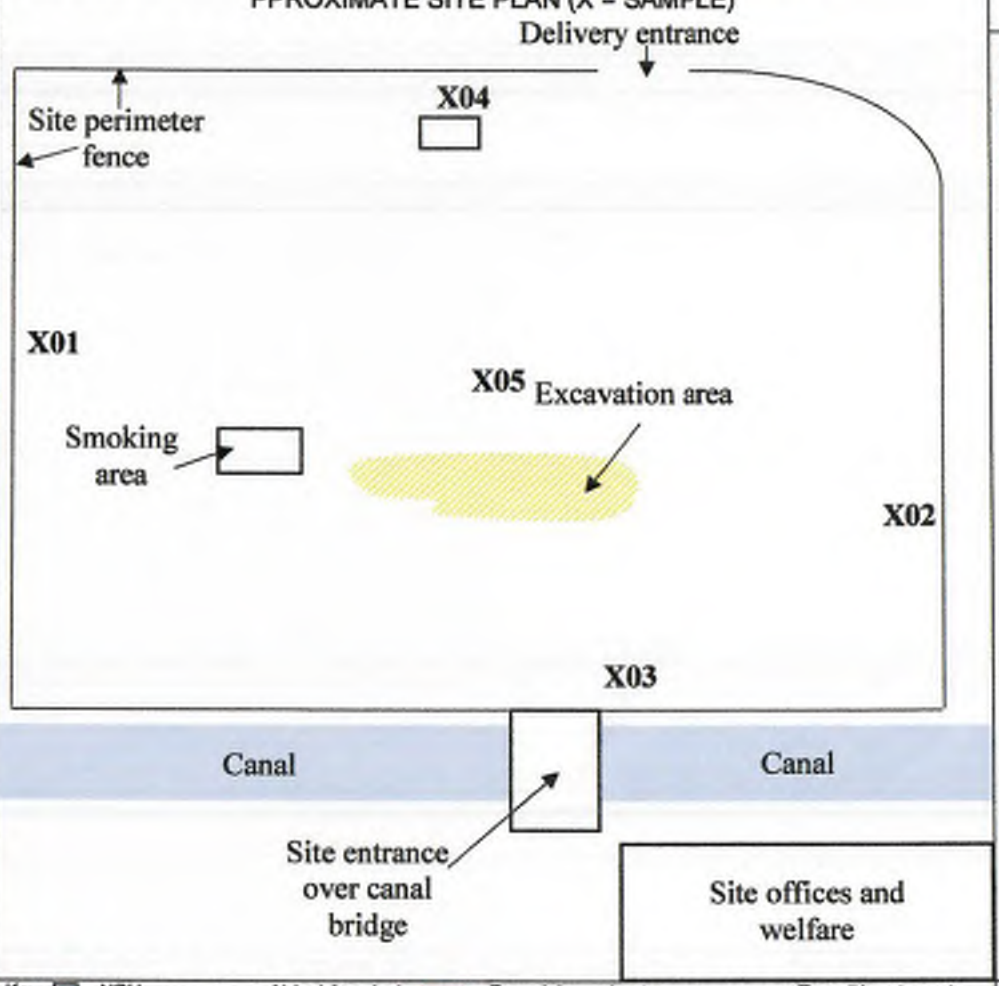

Key: = NPU = Airlock/bag lock = Remaining asbestos = Transit/waste route

The method used for sampling and the subsequent analysis as set out in HSG248 & in-house DOC/002

Contractor's Representative Acknowledgement of diagram accuracy	NAME:	SIGNATURE:

COMMENTS (outside scope of UKAS accreditation)

Reassurance air testing was undertaken to various locations on site while excavation works were being undertaken to various areas.

All results were satisfactory

Is generic Risk Assessment sufficient	YES

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

UKAS TESTING 2671

AIRBORNE FIBRE MONITORING

DATE	21 July 2021	TEST REPORT No.	30053	
ANALYST NAME	Liam Carpenter	BACKGROUND	APPROX. ENCLOSURE AREA/VOL (m^2/m^3)	NA
SITE ADDRESS	CLIENT name & address / Contractors Name & Address	LEAK		
Sport city Way Manchester M11 3DU	Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG	CLEARANCE	MEASUREMENTS REQ'D	NA
	Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG	RE-ASSURANCE: YES	No. SAMPLES TAKEN	5
		PERSONAL	FILTER DIAM. (mm)	22
		STATIC	ASBESTOS REMOVAL OPERATION	
		RPE checks made: NA	Reassurance air testing during excavation works on site.	
		LAB REF: YR16 0WH		
ANALYST SIGNATURE		EXPOSURE TIME (minutes) NA	TYPE OF ASBESTOS (outside scope of UKAS accreditation)	Not known

SAMPLE REF.	FILTER HEAD REF No.	PUMP REF No.	SAMPLE LOCATION	TYPE OF TEST	START TIME	END TIME	SAMPLE LENGTH	FLOW LITRE/min. START	FLOW LITRE/min. END	DUST DISTURB MINUTES	DUST DISTURB TYPE	LITRE	FIELDS	FIBRES	CONC. ACTUAL FIBRE/ml	CONC. REPORTED FIBRE/ml
52/210721/01	12	45	Adjacent site perimeter fence	R	1334	1434	60	8.0	8.0	NA	NA	480	200	3	0.0015	<0.01
52/210721/02	17	47	Adjacent site perimeter fence	R	1337	1437	60	8.0	8.0	NA	NA	480	200	1.5	0.0007	<0.01
52/210721/03	18	33	Adjacent site perimeter fence	R	1341	1441	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
52/210721/04	14	43	Adjacent site perimeter fence	R	1344	1444	60	8.0	8.0	NA	NA	480	200	2.5	0.0013	<0.01
52/210721/05	16	48	Adjacent to excavation area	R	1347	1447	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
			End of samples													

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

2671

AIRBORNE FIBRE MONITORING | REPORT No. 30053

MICROSCOPE REF:	MIC-13
MICROSCOPE SET UP:	YES
HSE/NPL GROUP:	5
GRATICULE DIAM. (microns)	100
FLOWMETER:	HFM-12
ATMOS. PRESSURE (mb):	NA
TEMPERATURE (ºC):	NA
WEATHER CONDITIONS:	Sunny
FLOW CORRECTED:	NA
CORRECTED FLOW (l/min):	NA
FIELD BLANK TAKEN	YES

VISUAL INSPECTION


NUMBER OF INSPECTIONS:	NA
TYPE OF RESPIRATOR	NA
ENCLOSURE CLEAN:	NA
ENCLOSURE INTACT:	NA
INTERIOR OF ENCL. DRY:	NA
N.P.U. OFF AND SEALED	NA
LOCK DOWN SPRAY USED	NA

Limit of Quantification

The limit of quantification is 0.010 fibres /ml. where sample volumes of 480 litres or greater and at least 200 graticule fields are analysed. The result may be reported as 'less than 0.01 fibres /ml'.
Where sample volumes are less than 480 litres and/or less than 200 graticule fields are analysed then the limit of quantification may be greater than 0.01 fibres/ml.

This report must not be reproduced except in full without the approval of 'Fourstage Environmental Ltd.'

PPROXIMATE SITE PLAN (X = SAMPLE)

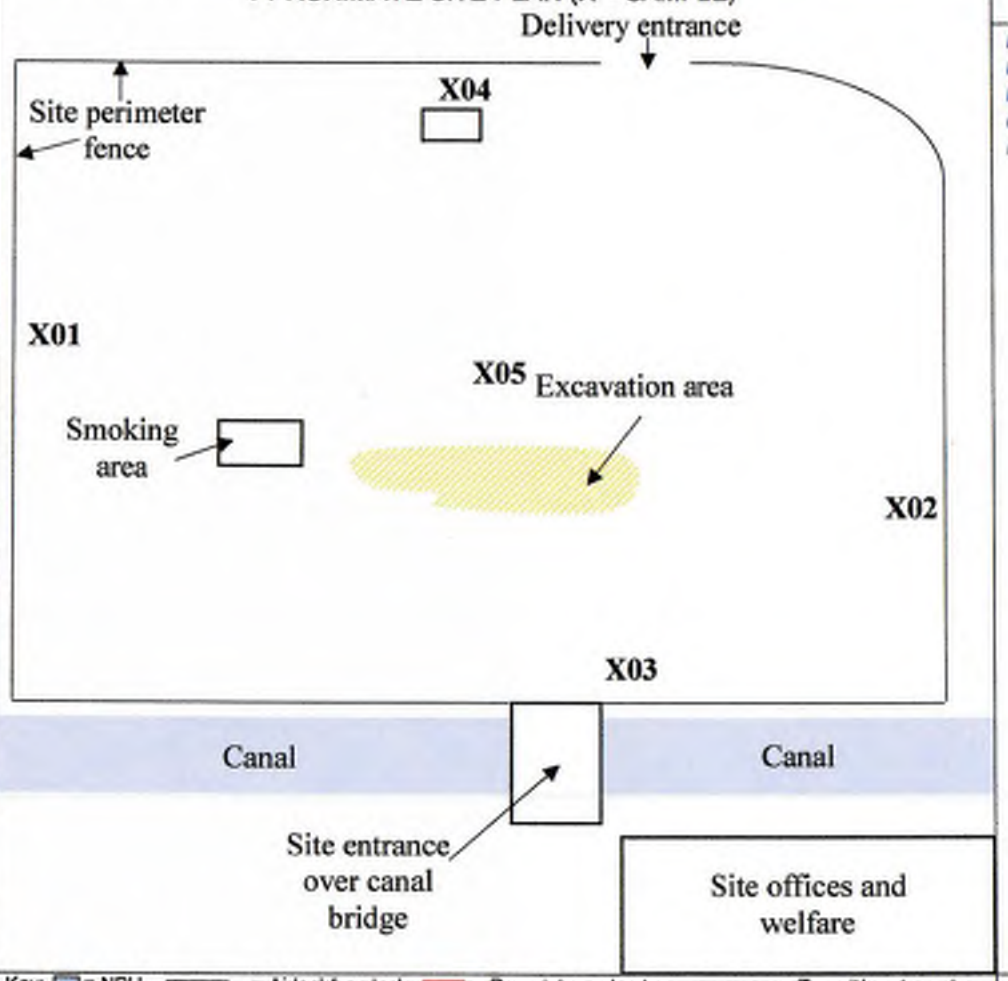

Key: = NPU = Airlock/bag lock = Remaining asbestos = Transit/waste route

The method used for sampling and the subsequent analysis as set out in HSG248 & in-house DOC/002

COMMENTS (outside scope of UKAS accreditation)

Reassurance air testing was undertaken to various locations on site while excavation works were being undertaken to various areas.

All results were satisfactory

Is generic Risk Assessment sufficient		YES
Contractor's Representative Acknowledgement of diagram accuracy	NAME:	SIGNATURE:

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

2671

AIRBORNE FIBRE MONITORING

TEST REPORT No. **30069**

DATE	29 July 2021	BACKGROUND		APPROX. ENCLOSURE AREA/VOL (m²/m³)	NA
ANALYST NAME	Liam Carpenter	LEAK			
SITE ADDRESS	CLIENT name & address / Contractors Name & Address	CLEARANCE		MEASUREMENTS REQ'D	NA
Sport city Way Manchester M11 3DU	Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG / Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG	RE-ASSURANCE	YES	No. SAMPLES TAKEN	5
		PERSONAL		FILTER DIAM. (mm)	22
		STATIC		ASBESTOS REMOVAL OPERATION	
		RPE checks made	NA	Reassurance air testing during excavation works on site.	
		LAB REF: YR16 0WH			

ANALYST SIGNATURE

EXPOSURE TIME (minutes) — NA — TYPE OF ASBESTOS (outside scope of UKAS accreditation) — Not known

SAMPLE REF.	FILTER HEAD REF No.	PUMP REF No.	SAMPLE LOCATION	TYPE OF TEST	START TIME	END TIME	SAMPLE LENGTH	FLOW LITRE/min. START	FLOW LITRE/min. END	DUST DISTURB MINUTES	DUST DISTURB TYPE	LITRE	FIELDS	FIBRES	CONC. ACTUAL FIBRE/ml	CONC REPORTED FIBRE/ml
52/290721/01	12	45	Adjacent site perimeter fence	R	0915	1003	48	10.0	10.0	NA	NA	480	200	1.5	0.0007	<0.01
52/290721/02	17	47	Adjacent site perimeter fence	R	0916	1004	48	10.0	10.0	NA	NA	480	200	3	0.0015	<0.01
52/290721/03	18	33	Adjacent site perimeter fence	R	0918	1006	48	10.0	10.0	NA	NA	480	200	2	0.0010	<0.01
52/290721/04	14	43	Adjacent site perimeter fence	R	0920	1008	48	10.0	10.0	NA	NA	480	200	2	0.0010	<0.01
52/290721/05	16	48	Adjacent to excavation area	R	0923	1011	48	10.0	10.0	NA	NA	480	200	2.5	0.0013	<0.01
			End of samples													

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

UKAS TESTING 2671

AIRBORNE FIBRE MONITORING | REPORT No. 30069

MICROSCOPE REF:	MIC-13
MICROSCOPE SET UP:	YES
HSE/NPL GROUP:	5
GRATICULE DIAM. (microns)	100
FLOWMETER:	HFM-12
ATMOS. PRESSURE (mb):	NA
TEMPERATURE (°C):	NA
WEATHER CONDITIONS:	NA
FLOW CORRECTED:	NA
CORRECTED FLOW (l/min):	NA
FIELD BLANK TAKEN	YES

VISUAL INSPECTION


NUMBER OF INSPECTIONS:	NA
TYPE OF RESPIRATOR	NA
ENCLOSURE CLEAN:	NA
ENCLOSURE INTACT:	NA
INTERIOR OF ENCL. DRY:	NA
N.P.U. OFF AND SEALED	NA
LOCK DOWN SPRAY USED	NA

Limit of Quantification

The limit of quantification is 0.010 fibres /ml. where sample volumes of 480 litres or greater and at least 200 graticule fields are analysed. The result may be reported as 'less than 0.01 fibres /ml'.
Where sample volumes are less than 480 litres and/or less than 200 graticule fields are analysed then the limit of quantification may be greater than 0.01 fibres/ml.

This report must not be reproduced except in full without the approval of 'Fourstage Environmental Ltd.'

PPROXIMATE SITE PLAN (X = SAMPLE)

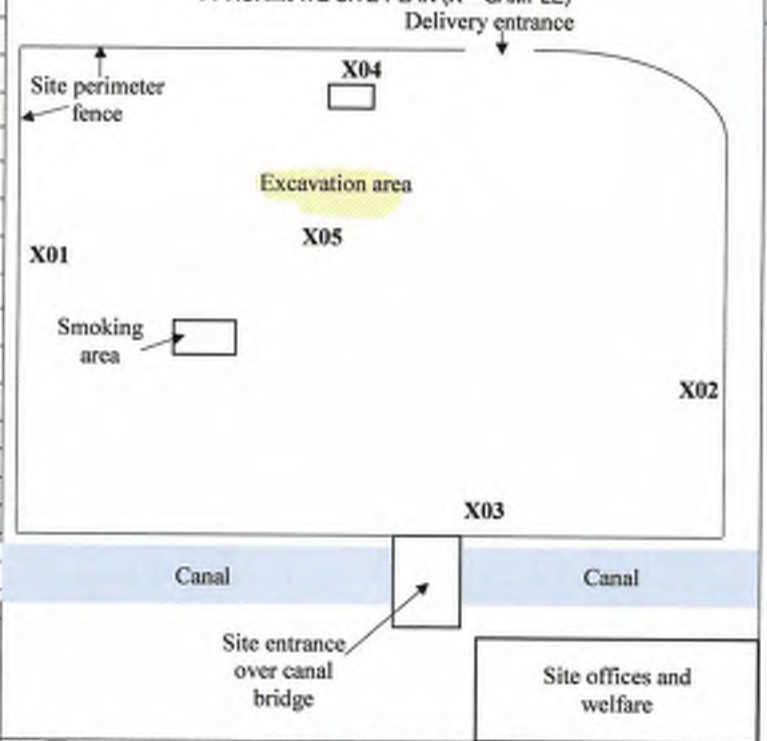

Key: = NPU = Airlock/bag lock = Remaining asbestos = Transit/waste route

The method used for sampling and the subsequent analysis as set out in HSG248 & in-house DOC/002

Is generic Risk Assessment sufficient: YES

Contractor's Representative Acknowledgement of diagram accuracy | NAME: T. Norman | SIGNATURE:

COMMENTS (outside scope of UKAS accreditation)

Reassurance air testing was undertaken to various locations on site while excavation works were being undertaken to various areas.

All results were satisfactory

FOURSTAGE ENVIRONMENTAL LTD.

5a CLA[illegible]UN STREET, CASTLE DONINGTON, DERBY, DE[illegible]2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

2671

AIRBORNE FIBRE MONITORING

TEST REPORT No. 30081

DATE	5 August 2021	BACKGROUND	
ANALYST NAME	Liam Carpenter	LEAK	
SITE ADDRESS	CLIENT name & address: Provectus Remediation Ltd, Regent House, Bath Avenue, Wolverhampton, WV1 4EG	CLEARANCE	
Sport city Way, Manchester, M11 3DU	Contractors Name & Address: Provectus Remediation Ltd, Regent House, Bath Avenue, Wolverhampton, WV1 4EG	RE-ASSURANCE	YES
		PERSONAL	
		STATIC	
		RPE checks made	NO
		LAB REF: YR16 0WH	

APPROX. ENCLOSURE AREA/DL (m²/m³)	NA
MEASUREMENTS REQ'D	NA
No. SAMPLES TAKEN	5
FILTER DIAM. (mm)	22
ASBESTOS REMOVAL OPERATION	Reassurance air testing during excavation works on site.

ANALYST SIGNATURE

EXPOSURE TIME (minutes) NA — TYPE OF ASBESTOS (outside scope of UKAS accreditation): Not known

SAMPLE REF.	FILTER HEAD REF No.	PUMP REF No.	SAMPLE LOCATION	TYPE OF TEST	START TIME	END TIME	SAMPLE LENGTH	FLOW LITRE/min. START	FLOW LITRE/min. END	DUST DISTURB MINUTES	DUST DISTURB TYPE	LITRE	FIELDS	FIBRES	CONC. ACTUAL FIBRE/ml	CONC. REPORTED FIBRE/ml
52/050821/02	12	45	Adjacent site perimeter fence	R	1428	1528	48	10.0	10.0	NA	NA	480	200	2.5	0.0013	<0.01
52/050821/03	17	47	Adjacent site perimeter fence	R	1430	1530	48	10.0	10.0	NA	NA	480	200	3.5	0.0018	<0.01
52/050821/04	18	33	Adjacent site perimeter fence	R	1431	1531	48	10.0	10.0	NA	NA	480	200	2	0.0010	<0.01
52/050821/05	14	43	Adjacent site perimeter fence	R	1431	1531	48	10.0	10.0	NA	NA	480	200	3	0.0015	<0.01
52/050821/06	16	48	Adjacent to excavation area	R	1435	1535	48	10.0	10.0	NA	NA	480	200	2.5	0.0013	<0.01
			End of samples													

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAYTON STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

UKAS TESTING 2671

AIRBORNE FIBRE MONITORING — REPORT No. 30081

MICROSCOPE REF:	MIC-13
MICROSCOPE SET UP:	YES
HSE/NPL GROUP:	5
GRATICULE DIAM. (microns)	100
FLOWMETER:	HFM-14
TIME PIECE:	TIM-02
STAGE MICROMETER:	SM-04
TEST SLIDE:	TS-04
WEATHER CONDITIONS:	Sunny
FIELD BLANK TAKEN	YES

VISUAL INSPECTION

NUMBER OF INSPECTIONS:	NA
TYPE OF RESPIRATOR	NA
ENCLOSURE CLEAN:	NA
ENCLOSURE INTACT:	NA
INTERIOR OF ENCL. DRY:	NA
N.P.U. OFF AND SEALED	NA
NO LOCK DOWN SPRAY USED	NA

Limit of Quantification

The limit of quantification is 0.210 fibres /ml, where sample volumes of 480 litres or greater and at least 200 graticule fields are analysed. The result may be reported as 'less than 0.01 fibres /ml'.


Where sample volumes are less than 480 litres and/or less than 200 graticule fields are analysed then the limit of quantification may be greater than 0.01 fibres/ml.

This report must not be reproduced except in full without the approval of "Fourstage Environmental Ltd."

VARIOUS PHOTOS HAVE BEEN TAKEN DURING THIS PROCESS AND ARE AVAILABLE ON REQUEST

THE REPORTED RESULTS ARE FOR RESPIRABLE FIBRES AND NOT NECESSARILY ASBESTOS FIBRES

PPROXIMATE SITE PLAN (X = SAMPLE)

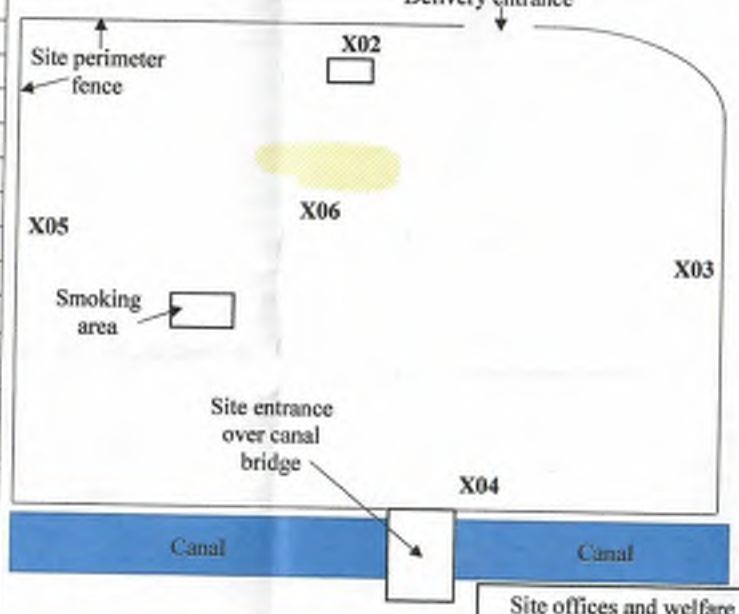

Key: = NPU = Airlock/bag lock = Remaining asbestos = Transit/waste route
= Vision Panels = Vacuum

The method used for sampling and the subsequent analysis as set out in HSG248 & in-house DOC/002

COMMENTS (Outside scope of UKAS accreditation)

Reassurance air testing was undertaken to various locations on site while excavation works were being undertaken to various areas.

All results were satisfactory

Is generic Risk Assessment sufficient

Contractor's Representative Acknowledgement of diagram accuracy — NAME: [illegible] SIGNATURE: [signature]

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

2671

AIRBORNE FIBRE MONITORING

TEST REPORT No. 30090

DATE	11 August 2021	BACKGROUND	
ANALYST NAME	Liam Carpenter	LEAK	
SITE ADDRESS	CLIENT name & address: Provectus Remediation Ltd, Regent House, Bath Avenue, Wolverhampton, WV1 4EG	CLEARANCE	
Sport city Way, Manchester, M11 3DU	Contractors Name & Address: Provectus Remediation Ltd, Regent House, Bath Avenue, Wolverhampton, WV1 4EG	RE-ASSURANCE	YES
		PERSONAL	
		STATIC	
		RPE checks made	NO
		LAB REF: YR16 0WH	

APPROX. ENCLOSURE AREA/VOL (m²/m³)	NA
MEASUREMENTS REQ'D	NA
No. SAMPLES TAKEN	5
FILTER DIAM. (mm)	22
ASBESTOS REMOVAL OPERATION	Reassurance air testing during excavation works on site.

ANALYST SIGNATURE

EXPOSURE TIME (minutes): NA

TYPE OF ASBESTOS (outside scope of UKAS accreditation): Not known

SAMPLE REF.	FILTER HEAD REF No.	PUMP REF No.	SAMPLE LOCATION	TYPE OF TEST	START TIME	END TIME	SAMPLE LENGTH	FLOW LITRE/min. START	FLOW LITRE/min. END	DUST DISTURB MINUTES	DUST DISTURB TYPE	LITRE	FIELDS	FIBRES	CONC. ACTUAL FIBRE/ml	CONC. REPORTED FIBRE/ml
52/110821/05	12	45	Adjacent site perimeter fence	R	1421	1521	60	8.0	8.0	NA	NA	480	200	3	0.0015	<0.01
52/110821/06	17	47	Adjacent site perimeter fence	R	1425	1525	60	8.0	8.0	NA	NA	480	200	1.5	0.0007	<0.01
52/110821/07	18	33	Adjacent to excavation area	R	1427	1527	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
52/110821/08	14	43	Adjacent site perimeter fence	R	1427	1527	60	8.0	8.0	NA	NA	480	200	1.5	0.0007	<0.01
52/110821/09	16	48	Adjacent site perimeter fence	R	1428	1528	60	8.0	8.0	NA	NA	480	200	2.5	0.0013	<0.01
			End of samples													

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

2671


AIRBORNE FIBRE MONITORING | REPORT No. 30090

MICROSCOPE REF:	MIC-13
MICROSCOPE SET UP:	YES
HSE/NPL GROUP:	5
GRATICULE DIAM. (microns)	100
FLOWMETER:	HFM-14
TIME PIECE:	TIM-02
STAGE MICROMETER:	SM-04
TEST SLIDE:	TS-04
WEATHER CONDITIONS:	Sunny
FIELD BLANK TAKEN	YES
VISUAL INSPECTION	
NUMBER OF INSPECTIONS:	NA
TYPE OF RESPIRATOR	NA
ENCLOSURE CLEAN:	NA
ENCLOSURE INTACT:	NA
INTERIOR OF ENCL. DRY:	NA
N.P.U. OFF AND SEALED	NA
NO LOCK DOWN SPRAY USED	NA

Limit of Quantification

The limit of quantification is 0.010 fibres /ml, where sample volumes of 480 litres or greater and at least 200 graticule fields are analysed. The result may be reported as 'less than 0.01 fibres /ml'.
Where sample volumes are less than 480 litres and/or less than 200 graticule fields are analysed than the limit of quantification may be greater than 0.01 fibres/ml.

PPROXIMATE SITE PLAN (X = SAMPLE)

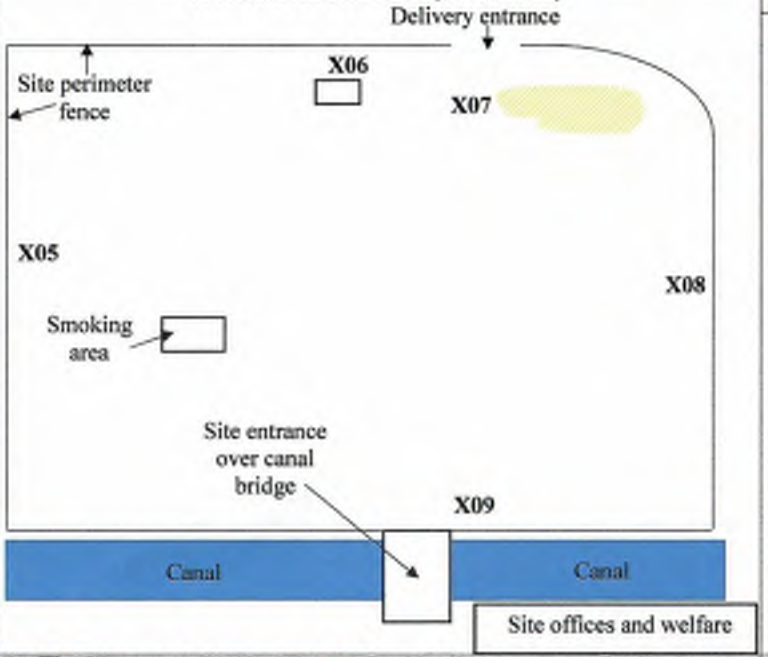

Key: = NPU = Airlock/bag lock = Remaining asbestos = Transit/waste route = Vision Panels = Vacuum

The method used for sampling and the subsequent analysis as set out in HSG248 & in-house DOC/002

COMMENTS
(Outside scope of UKAS accreditation)

Reassurance air testing was undertaken to various locations on site while excavation works were being undertaken to various areas.

All results were satisfactory

This report must not be reproduced except in full without the approval of "Fourstage Environmental Ltd."

VARIOUS PHOTOS HAVE BEEN TAKEN DURING THIS PROCESS AND ARE AVAILABLE ON REQUEST

THE REPORTED RESULTS ARE FOR RESPIRABLE FIBRES AND NOT NECESSARILY ASBESTOS FIBRES

Contractor's Representative Acknowledgement of diagram accuracy	NAME:	SIGNATURE:	Is generic Risk Assessment sufficient: YES

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

2671

AIRBORNE FIBRE MONITORING

TEST REPORT No. 30101

DATE	25 August 2021	BACKGROUND		APPROX. ENCLOSURE AREA/VOL (m²/m³)	NA
ANALYST NAME	Liam Carpenter	LEAK			
SITE ADDRESS	CLIENT name & address / Contractors Name & Address	CLEARANCE		MEASUREMENTS REQ'D	NA
Sport city Way Manchester M11 3DU	Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG / Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG	RE-ASSURANCE	YES	No. SAMPLES TAKEN	5
		PERSONAL		FILTER DIAM. (mm)	22
		STATIC		ASBESTOS REMOVAL OPERATION	
		RPE checks made	NO	Reassurance air testing during excavation works on site.	
		LAB REF: YR16 0WH			

ANALYST SIGNATURE

EXPOSURE TIME (minutes) NA — TYPE OF ASBESTOS (outside scope of UKAS accreditation) Not known

SAMPLE REF.	FILTER HEAD REF No.	PUMP REF No.	SAMPLE LOCATION	TYPE OF TEST	START TIME	END TIME	SAMPLE LENGTH	FLOW LITRE/min. START	FLOW LITRE/min. END	DUST DISTURB MINUTES	DUST DISTURB TYPE	LITRE	FIELDS	FIBRES	CONC. ACTUAL FIBRE/ml	CONC. REPORTED FIBRE/ml
52/250821/01	12	45	Adjacent site perimeter fence	R	0924	1024	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
52/250821/02	17	47	Adjacent to excavation area	R	0924	1024	60	8.0	8.0	NA	NA	480	200	1.5	0.0007	<0.01
52/250821/03	18	33	Adjacent site perimeter fence	R	0925	1025	60	8.0	8.0	NA	NA	480	200	2.5	0.0013	<0.01
52/250821/04	14	43	Adjacent site perimeter fence	R	0929	1029	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
52/250821/05	16	48	Adjacent site perimeter fence	R	0930	1030	60	8.0	8.0	NA	NA	480	200	1	0.0005	<0.01
			End of samples													

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

1671

AIRBORNE FIBRE MONITORING | REPORT No. 30101

MICROSCOPE REF:	MIC-13
MICROSCOPE SET UP:	YES
HSE/NPL GROUP:	5
GRATICULE DIAM. (microns)	100
FLOWMETER:	HFM-14
TIME PIECE:	TIM-02
STAGE MICROMETER:	SM-04
TEST SLIDE:	TS-04
WEATHER CONDITIONS:	Sunny
FIELD BLANK TAKEN	YES
VISUAL INSPECTION	
NUMBER OF INSPECTIONS:	NA
TYPE OF RESPIRATOR	NA
ENCLOSURE CLEAN:	NA
ENCLOSURE INTACT:	NA
INTERIOR OF ENCL. DRY:	NA
N.P.U. OFF AND SEALED	NA
NO LOCK DOWN SPRAY USED	NA

Limit of Quantification


The limit of quantification is 0.010 fibres /ml, where sample volumes of 480 litres or greater and at least 200 graticule fields are analysed. The result may be reported as 'less than 0.01 fibres /ml'.
Where sample volumes are less than 480 litres and/or less than 200 graticule fields are analysed then the limit of quantification may be greater than 0.01 fibres/ml.

This report must not be reproduced except in full without the approval of "Fourstage Environmental Ltd."

VARIOUS PHOTOS HAVE BEEN TAKEN DURING THIS PROCESS AND ARE AVAILABLE ON REQUEST

THE REPORTED RESULTS ARE FOR RESPIRABLE FIBRES AND NOT NECESSARILY ASBESTOS FIBRES

PPROXIMATE SITE PLAN (X = SAMPLE)

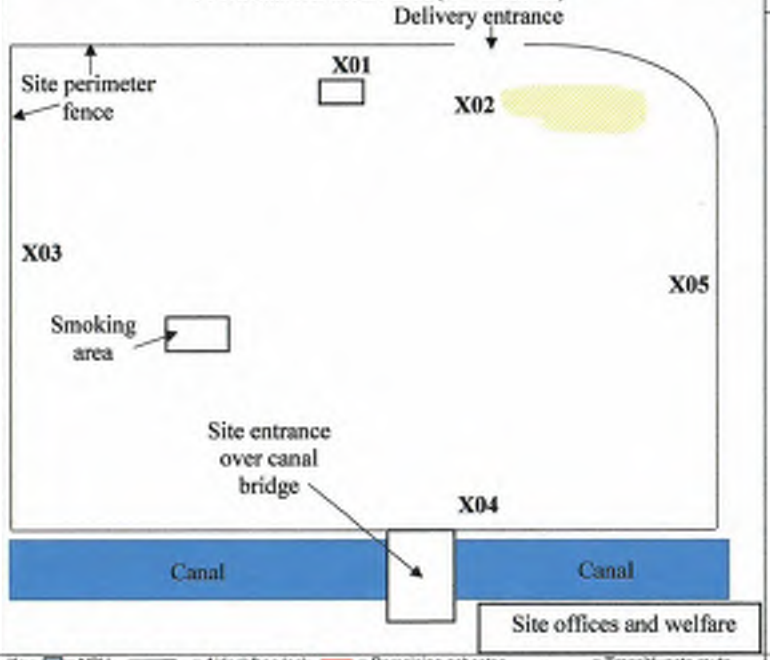

Key: = NPU = Airlock/bag lock = Remaining asbestos = Transit/waste route
= Vision Panels = Vacuum

The method used for sampling and the subsequent analysis as set out in HSG248 & in-house DOC/002

COMMENTS
(Outside scope of UKAS accreditation)

Reassurance air testing was undertaken to various locations on site while excavation works were being undertaken to various areas.

All results were satisfactory

Is generic Risk Assessment sufficient	YES		
Contractor's Representative Acknowledgement of diagram accuracy	NAME:	SIGNATURE:	

FOURSTAGE ENVIRONMENTAL LTD.

5a CL[illegible]GUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

UKAS TESTING 2671

AIRBORNE FIBRE MONITORING

TEST REPORT No. 30126

DATE	8 September 2021
ANALYST NAME	Liam Carpenter
SITE ADDRESS	Sport city Way Manchester M11 3DU
CLIENT name & address	Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG
Contractors Name & Address	Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG
ANALYST SIGNATURE	

BACKGROUND	
LEAK	
CLEARANCE	
RE-ASSURANCE	YES
PERSONAL	
STATIC	
RPE checks made	NO
LAB REF: YR16 0WH	

APPROX. ENCLOSURE AREA/VOL (m^2/m^3)	NA
MEASUREMENTS REQ'D	NA
No. SAMPLES TAKEN	5
FILTER DIAM. (mm)	22
ASBESTOS REMOVAL OPERATION	Reassurance air testing during excavation works on site.

EXPOSURE TIME (minutes) NA — TYPE OF ASBESTOS (outside scope of UKAS accreditation) Not known

SAMPLE REF.	FILTER HEAD REF No.	PUMP REF No.	SAMPLE LOCATION	TYPE OF TEST	START TIME	END TIME	SAMPLE LENGTH	FLOW LITRE/min. START	FLOW LITRE/min. END	DUST DISTURB MINUTES	DUST DISTURB TYPE	LITRE	FIELDS	FIBRES	CONC. ACTUAL FIBRE/ml	CONC. REPORTED FIBRE/ml
52/080921/03	11	45	Adjacent site perimeter fence	R	1439	1539	60	8.0	8.0	NA	NA	480	200	1	0.0005	<0.01
52/080921/04	12	47	Adjacent to excavation area	R	1439	1539	60	8.0	8.0	NA	NA	480	200	1.5	0.0007	<0.01
52/080921/05	13	33	Adjacent site perimeter fence	R	1441	1541	60	8.0	8.0	NA	NA	480	200	3	0.0015	<0.01
52/080921/06	14	43	Adjacent site perimeter fence	R	1442	1542	60	8.0	8.0	NA	NA	480	200	2.5	0.0013	<0.01
52/080921/07	18	48	Adjacent site perimeter fence	R	1443	1543	60	8.0	8.0	NA	NA	480	200	1.5	0.0007	<0.01
			End of samples													

FOURSTAGE ENVIRONMENTAL LTD.

5a C[illegible]GUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

UKAS TESTING 2671

AIRBORNE FIBRE MONITORING | REPORT No. 30126

MICROSCOPE REF:	MIC-13
MICROSCOPE SET UP:	YES
HSE/NPL GROUP:	5
GRATICULE DIAM. (microns)	100
FLOWMETER:	HFM-14
TIME PIECE:	TIM-02
STAGE MICROMETER:	SM-04
TEST SLIDE:	TS-04
WEATHER CONDITIONS:	Sunny
FIELD BLANK TAKEN	YES

VISUAL INSPECTION


NUMBER OF INSPECTIONS:	NA
TYPE OF RESPIRATOR	NA
ENCLOSURE CLEAN:	NA
ENCLOSURE INTACT:	NA
INTERIOR OF ENCL. DRY:	NA
N.P.U. OFF AND SEALED	NA
NO LOCK DOWN SPRAY USED	NA

Limit of Quantification

The limit of quantification is 0.010 fibres /ml. where sample volumes of 480 litres or greater and at least 200 graticule fields are analysed. The result may be reported as 'less than 0.01 fibres /ml'.

Where sample volumes are less than 480 litres and/or less than 200 graticule fields are analysed then the limit of quantification may be greater than 0.01 fibres/ml.

PPROXIMATE SITE PLAN (X = SAMPLE)

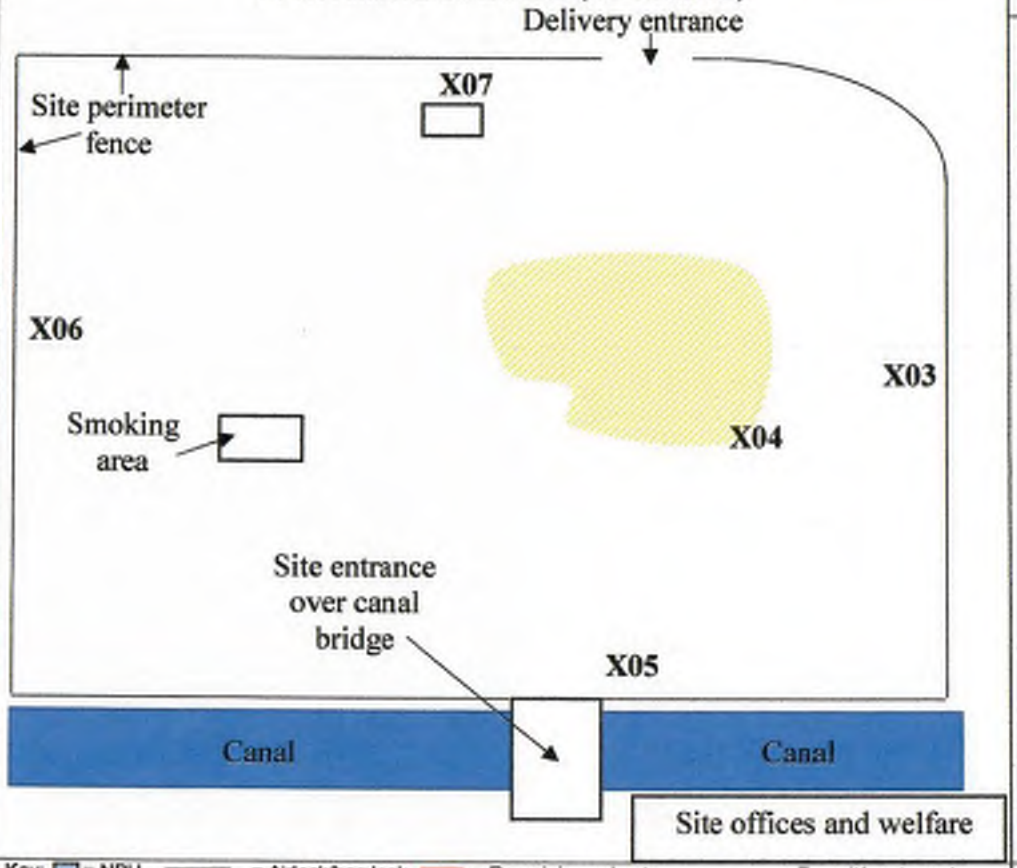

Key: NPU = Airlock/bag lock = Remaining asbestos = Transit/waste route = Vision Panels = Vacuum

The method used for sampling and the subsequent analysis as set out in HSG248 & in-house DOC/002

COMMENTS
(Outside scope of UKAS accreditation)

Reassurance air testing was undertaken to various locations on site while excavation works were being undertaken to various areas.

All results were satisfactory

Is generic Risk Assessment sufficient: YES

This report must not be reproduced except in full without the approval of "Fourstage Environmental Ltd."

VARIOUS PHOTOS HAVE BEEN TAKEN DURING THIS PROCESS AND ARE AVAILABLE ON REQUEST.

THE REPORTED RESULTS ARE FOR RESPIRABLE FIBRES AND NOT NECESSARILY ASBESTOS FIBRES

Contractor's Representative Acknowledgement of diagram accuracy | NAME: MATT [illegible] | SIGNATURE:

FOURSTAGE ENVIRONMENTAL LTD.

5a C[illegible]GUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

UKAS TESTING 2671

AIRBORNE FIBRE MONITORING

TEST REPORT No. 30137

DATE	17 September 2021	BACKGROUND	
ANALYST NAME	Liam Carpenter	LEAK	
SITE ADDRESS	CLIENT name & address: Provectus Remediation Ltd, Regent House, Bath Avenue, Wolverhampton, WV1 4EG	CLEARANCE	
Sport city Way, Manchester, M11 3DU	Contractors Name & Address: Provectus Remediation Ltd, Regent House, Bath Avenue, Wolverhampton, WV1 4EG	RE-ASSURANCE	YES
		PERSONAL	
		STATIC	
		RPE checks made	NO
		LAB REF: YR16 0WH	

APPROX. ENCLOSURE AREA/VOL (m²/m³)	NA
MEASUREMENTS REQ'D	NA
No. SAMPLES TAKEN	5
FILTER DIAM. (mm)	22
ASBESTOS REMOVAL OPERATION	Reassurance air testing during excavation works on site.

ANALYST SIGNATURE

EXPOSURE TIME (minutes) — NA

TYPE OF ASBESTOS (outside scope of UKAS accreditation) — Not known

SAMPLE REF.	FILTER HEAD REF No.	PUMP REF No.	SAMPLE LOCATION	TYPE OF TEST	START TIME	END TIME	SAMPLE LENGTH	FLOW LITRE/min. START	FLOW LITRE/min. END	DUST DISTURB MINUTES	DUST DISTURB TYPE	LITRE	FIELDS	FIBRES	CONC. ACTUAL FIBRE/ml	CONC. REPORTED FIBRE/ml
52/170921/05	11	45	Adjacent site perimeter fence	R	1238	1338	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
52/170921/06	12	47	Adjacent to excavation area	R	1238	1338	60	8.0	8.0	NA	NA	480	200	1	0.0005	<0.01
52/170921/07	13	33	Adjacent site perimeter fence	R	1241	1341	60	8.0	8.0	NA	NA	480	200	2.5	0.0013	<0.01
52/170921/08	14	43	Adjacent site perimeter fence	R	1241	1341	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
52/170921/09	18	48	Adjacent site perimeter fence	R	1242	1342	60	8.0	8.0	NA	NA	480	200	1.5	0.0007	<0.01
			End of samples													

FOURSTAGE ENVIRONMENTAL LTD.

5a C[illegible]'GUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

UKAS TESTING 2671

AIRBORNE FIBRE MONITORING | REPORT No. 30137

MICROSCOPE REF:	MIC-13
MICROSCOPE SET UP:	YES
HSE/NPL GROUP:	5
GRATICULE DIAM. (microns)	100
FLOWMETER:	HFM-14
TIME PIECE:	TIM-02
STAGE MICROMETER:	SM-04
TEST SLIDE:	TS-04
WEATHER CONDITIONS:	Sunny
FIELD BLANK TAKEN	YES


VISUAL INSPECTION

NUMBER OF INSPECTIONS:	NA
TYPE OF RESPIRATOR	NA
ENCLOSURE CLEAN:	NA
ENCLOSURE INTACT:	NA
INTERIOR OF ENCL. DRY:	NA
N.P.U. OFF AND SEALED	NA
NO LOCK DOWN SPRAY USED	NA

Limit of Quantification

The limit of quantification is 0.010 fibres /ml. where sample volumes of 480 litres or greater and at least 200 graticule fields are analysed. The result may be reported as 'less than 0.01 fibres /ml'.
Where sample volumes are less than 480 litres and/or less than 200 graticule fields are analysed then the limit of quantification may be greater than 0.01 fibres/ml.

PPROXIMATE SITE PLAN (X = SAMPLE)

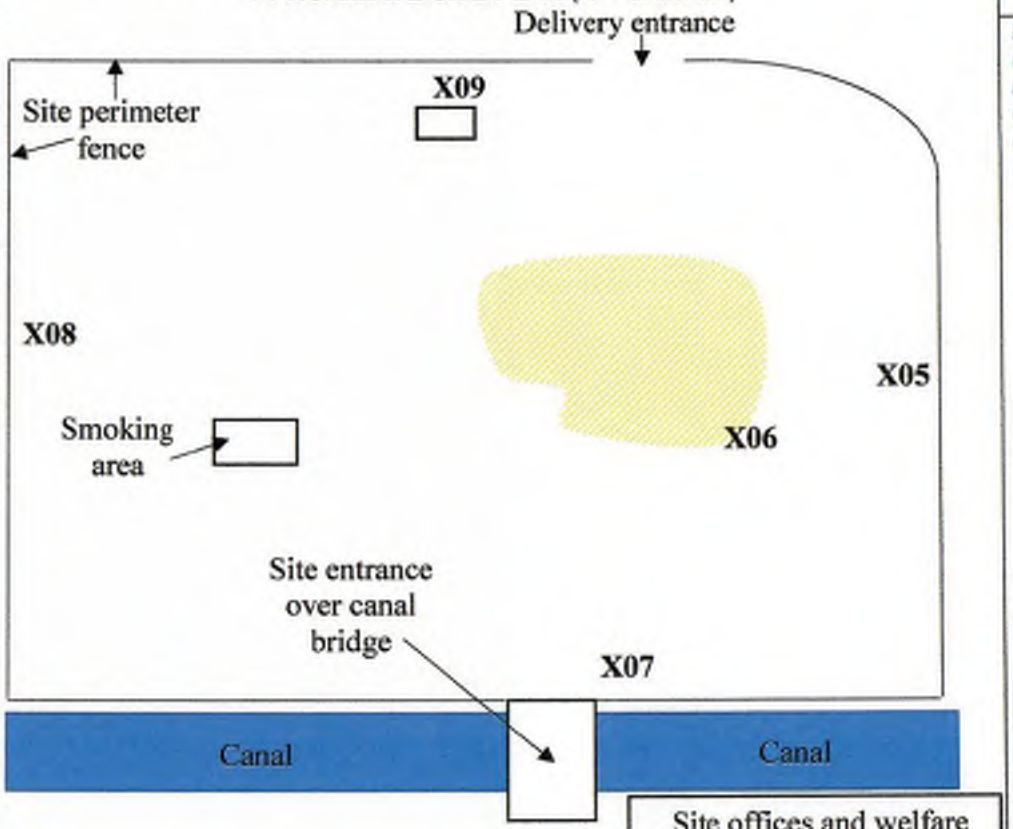

Key: = NPU = Airlock/bag lock = Remaining asbestos = Transit/waste route = Vision Panels = Vacuum

The method used for sampling and the subsequent analysis as set out in HSG248 & in-house DOC/002

COMMENTS (Outside scope of UKAS accreditation)

Reassurance air testing was undertaken to various locations on site while excavation works were being undertaken to various areas.

All results were satisfactory

Is generic Risk Assessment sufficient: YES

This report must not be reproduced except in full without the approval of "Fourstage Environmental Ltd."

VARIOUS PHOTOS HAVE BEEN TAKEN DURING THIS PROCESS AND ARE AVAILABLE ON REQUEST.

THE REPORTED RESULTS ARE FOR RESPIRABLE FIBRES AND NOT NECESSARILY ASBESTOS FIBRES

Contractor's Representative Acknowledgement of diagram accuracy — NAME: Nobody on Site — SIGNATURE: NA

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

07815 155266 — Liam

UKAS TESTING 2671

AIRBORNE FIBRE MONITORING

TEST REPORT No. 30141

DATE	21 September 2021
ANALYST NAME	Liam Carpenter
SITE ADDRESS	Sport city Way Manchester M11 3DU
CLIENT name & address	Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG
Contractors Name & Address	Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG
ANALYST SIGNATURE	

BACKGROUND		APPROX. ENCLOSURE AREA/VOL (m^2/m^3)	NA
LEAK			
CLEARANCE		MEASUREMENTS REQ'D	NA
RE-ASSURANCE	YES	No. SAMPLES TAKEN	5
PERSONAL		FILTER DIAM. (mm)	22
STATIC		ASBESTOS REMOVAL OPERATION	
RPE checks made	NO	Reassurance air testing during excavation works on site.	
LAB REF: YR16 0WH			

EXPOSURE TIME (minutes) — NA — TYPE OF ASBESTOS (outside scope of UKAS accreditation) — Not known

SAMPLE REF.	FILTER HEAD REF No.	PUMP REF No.	SAMPLE LOCATION	TYPE OF TEST	START TIME	END TIME	SAMPLE LENGTH	FLOW LITRE/min. START	FLOW LITRE/min. END	DUST DISTURB MINUTES	DUST DISTURB TYPE	LITRE	FIELDS	FIBRES	CONC. ACTUAL FIBRE/ml	CONC. REPORTED FIBRE/ml
52/210921/04	11	45	Adjacent site perimeter fence	R	1340	1440	60	8.0	8.0	NA	NA	480	200	2.5	0.0013	<0.01
52/210921/05	12	47	Adjacent to excavation area	R	1340	1440	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
52/210921/06	13	33	Adjacent to excavation area	R	1342	1442	60	8.0	8.0	NA	NA	480	200	2.5	0.0013	<0.01
52/210921/07	14	43	Adjacent to excavation area	R	1343	1443	60	8.0	8.0	NA	NA	480	200	1	0.0005	<0.01
52/210921/08	18	48	Adjacent site perimeter fence	R	1343	1443	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
			End of samples													

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

UKAS TESTING 2671

AIRBORNE FIBRE MONITORING

REPORT No. 30137

MICROSCOPE REF:	MIC-13
MICROSCOPE SET UP:	YES
HSE/NPL GROUP:	5
GRATICULE DIAM. (microns)	100
FLOWMETER:	HFM-14
TIME PIECE:	TIM-02
STAGE MICROMETER:	SM-04
TEST SLIDE:	TS-04
WEATHER CONDITIONS:	Sunny
FIELD BLANK TAKEN	YES

VISUAL INSPECTION

NUMBER OF INSPECTIONS:	NA
TYPE OF RESPIRATOR	NA
ENCLOSURE CLEAN:	NA
ENCLOSURE INTACT:	NA
INTERIOR OF ENCL. DRY:	NA
N.P.U. OFF AND SEALED	NA
NO LOCK DOWN SPRAY USED	NA

Limit of Quantification


The limit of quantification is 0.010 fibres /ml. where sample volumes of 460 litres or greater and at least 200 graticule fields are analysed. The result may be reported as 'less than 0.01 fibres /ml'.
Where sample volumes are less than 460 litres and/or less than 200 graticule fields are analysed than the limit of quantification may be greater than 0.01 fibres/ml.

This report must not be reproduced except in full without the approval of "Fourstage Environmental Ltd."

VARIOUS PHOTOS HAVE BEEN TAKEN DURING THIS PROCESS AND ARE AVAILABLE ON REQUEST.

THE REPORTED RESULTS ARE FOR RESPIRABLE FIBRES AND NOT NECESSARILY ASBESTOS FIBRES

PPROXIMATE SITE PLAN (X = SAMPLE)

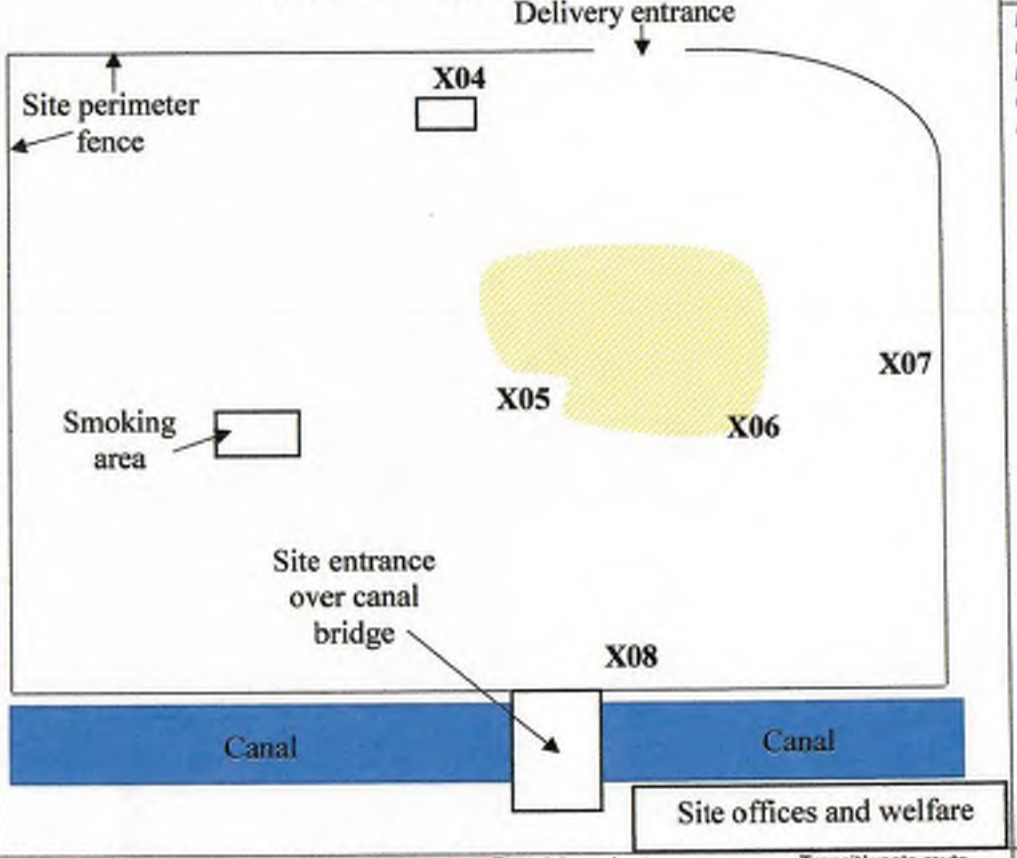

Key: = NPU = Airlock/bag lock = Remaining asbestos = Transit/waste route = Vision Panels = Vacuum

The method used for sampling and the subsequent analysis as set out in HSG248 & in-house DOC/002

Contractor's Representative Acknowledgement of diagram accuracy

NAME: T. Haright SIGNATURE:

COMMENTS
(Outside scope of UKAS accreditation)

Reassurance air testing was undertaken to various locations on site while excavation works were being undertaken to various areas.

All results were satisfactory

Is generic Risk Assessment sufficient: YES

FOURSTAGE ENVIRONMENTAL LTD.

5a CLA[illegible]UN STREET, CASTLE DONINGTON, DERBY, D[illegible] 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

UKAS TESTING 2671

AIRBORNE FIBRE MONITORING

TEST REPORT No. 30149

DATE	29 September 2021
ANALYST NAME	Liam Carpenter
SITE ADDRESS	Sport city Way Manchester M11 3DU
CLIENT name & address	Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG
Contractors Name & Address	Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG

BACKGROUND	
LEAK	
CLEARANCE	
RE-ASSURANCE	YES
PERSONAL	
STATIC	
RPE checks made	NO
LAB REF: YR16 0WH	

APPROX. ENCLOSURE AREA/VOL (m^2/m^3)	NA
MEASUREMENTS REQ'D	NA
No. SAMPLES TAKEN	4
FILTER DIAM. (mm)	22
ASBESTOS REMOVAL OPERATION	Reassurance air testing during excavation works on site.

ANALYST SIGNATURE [signature]

EXPOSURE TIME (minutes) NA

TYPE OF ASBESTOS (outside scope of UKAS accreditation) Not known

SAMPLE REF.	FILTER HEAD REF No.	PUMP REF No.	SAMPLE LOCATION	TYPE OF TEST	START TIME	END TIME	SAMPLE LENGTH	FLOW LITRE/min. START	FLOW LITRE/min. END	DUST DISTURB MINUTES	DUST DISTURB TYPE	LITRE	FIELDS	FIBRES	CONC. ACTUAL FIBRE/ml	CONC. REPORTED FIBRE/ml
52/290921/01	11	45	Site see plan	R	1229	1329	60	8.0	8.0	NA	NA	480	200	1.5	0.0007	<0.01
52/290921/02	12	47	Site see plan	R	1230	1330	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
52/290921/03	13	33	Site see plan	R	1231	1331	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
52/290921/04	14	43	Site see plan	R	1232	1332	60	8.0	8.0	NA	NA	480	200	2.5	0.0013	<0.01
			End of samples													

FOURSTAGE ENVIRONMENTAL LTD.

5a CLA UN STREET, CASTLE DONINGTON, DERBY, D 4 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

UKAS TESTING
2671

AIRBORNE FIBRE MONITORING — REPORT No. 30149

MICROSCOPE REF:	MIC-13
MICROSCOPE SET UP:	YES
HSE/NPL GROUP:	5
GRATICULE DIAM. (microns)	100
FLOWMETER:	HFM-14
TIME PIECE:	TIM-02
STAGE MICROMETER:	SM-04
TEST SLIDE:	TS-04
WEATHER CONDITIONS:	Rainy
FIELD BLANK TAKEN	YES

VISUAL INSPECTION

NUMBER OF INSPECTIONS:	NA
TYPE OF RESPIRATOR	NA
ENCLOSURE CLEAN:	NA
ENCLOSURE INTACT:	NA
INTERIOR OF ENCL. DRY:	NA
N.P.U. OFF AND SEALED	NA
NO LOCK DOWN SPRAY USED	NA

Limit of Quantification


The limit of quantification is 0.010 fibres /ml, where sample volumes of 480 litres or greater and at least 200 graticule fields are analysed. The result may be reported as 'less than 0.01 fibres /ml'.
Where sample volumes are less than 480 litres and/or less than 200 graticule fields are analysed then the limit of quantification may be greater than 0.01 fibres/ml.

This report must not be reproduced except in full without the approval of "Fourstage Environmental Ltd."

VARIOUS PHOTOS HAVE BEEN TAKEN DURING THIS PROCESS AND ARE AVAILABLE ON REQUEST.

THE REPORTED RESULTS ARE FOR RESPIRABLE FIBRES AND NOT NECESSARILY ASBESTOS FIBRES

PPROXIMATE SITE PLAN (X = SAMPLE)

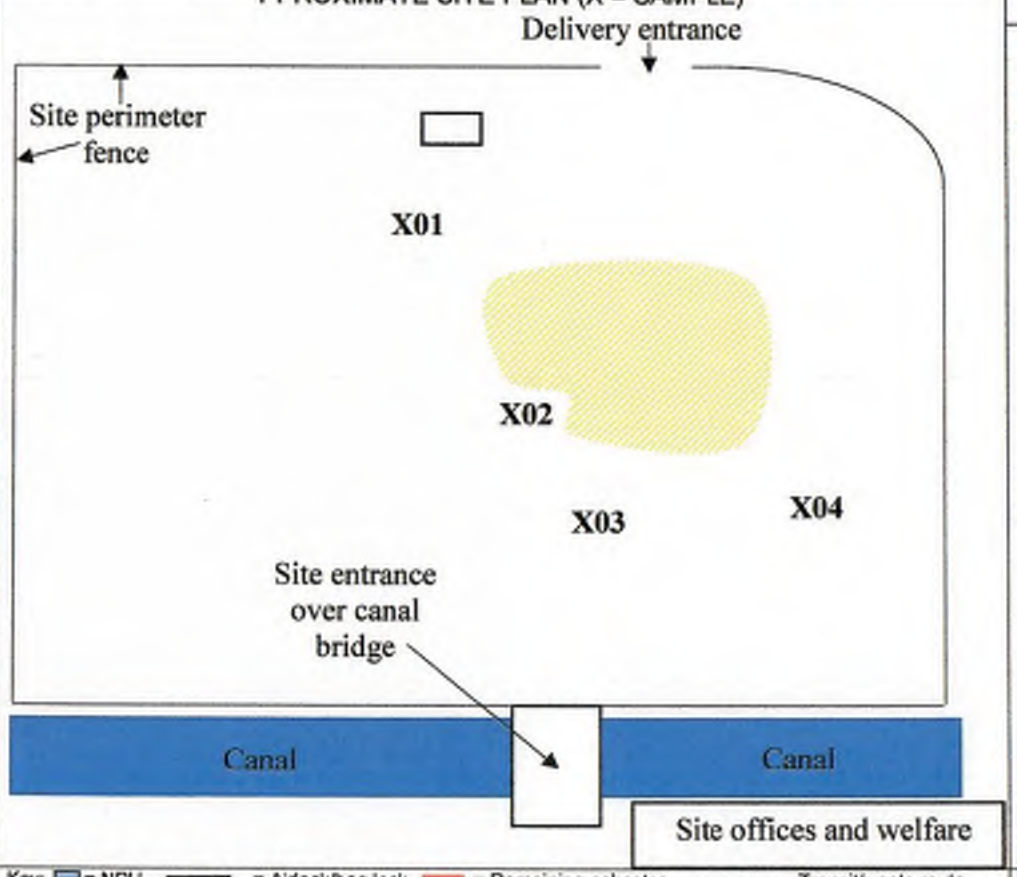

Key: = NPU = Airlock/bag lock = Remaining asbestos = Transit/waste route = Vision Panels = Vacuum

The method used for sampling and the subsequent analysis as set out in HSG248 & in-house DOC/002

Contractor's Representative Acknowledgement of diagram accuracy — NAME: Paul Somers — SIGNATURE:

COMMENTS
(Outside scope of UKAS accreditation)

Reassurance air testing was undertaken to various locations on site while excavation works were being undertaken to various areas.

All results were satisfactory

Is generic Risk Assessment sufficient	YES

Document Reference DOC/039/V18 (10-06-21)

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

2671

AIRBORNE FIBRE MONITORING

TEST REPORT No. **30112**

DATE	2 September 2021	BACKGROUND		APPROX. ENCLOSURE AREA/VOL (m^2/m^3)	NA
ANALYST NAME	Liam Carpenter	LEAK			
SITE ADDRESS	CLIENT name & address / Contractors Name & Address	CLEARANCE		MEASUREMENTS REQ'D	NA
Sport city Way Manchester M11 3DU	Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG	RE-ASSURANCE	YES	No. SAMPLES TAKEN	5
		PERSONAL		FILTER DIAM. (mm)	22
		STATIC		ASBESTOS REMOVAL OPERATION	
		RPE checks made	NO	Reassurance air testing during excavation works on site.	
		LAB REF: YR16 0WH			
ANALYST SIGNATURE		EXPOSURE TIME (minutes)	NA	TYPE OF ASBESTOS (outside scope of UKAS accreditation)	Not known

SAMPLE REF.	FILTER HEAD REF No.	PUMP REF No.	SAMPLE LOCATION	TYPE OF TEST	START TIME	END TIME	SAMPLE LENGTH	FLOW LITRE/min. START	FLOW LITRE/min. END	DUST DISTURB MINUTES	DUST DISTURB TYPE	LITRE	FIELDS	FIBRES	CONC. ACTUAL FIBRE/ml	CONC. REPORTED FIBRE/ml
52/020921/06	11	45	Adjacent site perimeter fence	R	1520	1620	60	8.0	8.0	NA	NA	480	200	1.5	0.0007	<0.01
52/020921/07	12	47	Adjacent to excavation area	R	1520	1620	60	8.0	8.0	NA	NA	480	200	3	0.0015	<0.01
52/020921/08	13	33	Adjacent site perimeter fence	R	1522	1622	60	8.0	8.0	NA	NA	480	200	2.5	0.0013	<0.01
52/020921/09	14	43	Adjacent site perimeter fence	R	1523	1623	60	8.0	8.0	NA	NA	480	200	1	0.0005	<0.01
52/020921/10	18	48	Adjacent site perimeter fence	R	1524	1624	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
			End of samples													

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

UKAS TESTING 2671

AIRBORNE FIBRE MONITORING	REPORT No.	30112

MICROSCOPE REF:	MIC-13
MICROSCOPE SET UP:	YES
HSE/NPL GROUP:	5
GRATICULE DIAM. (microns)	100
FLOWMETER:	HFM-14
TIME PIECE:	TIM-02
STAGE MICROMETER:	SM-04
TEST SLIDE:	TS-04
WEATHER CONDITIONS:	Cloudy
FIELD BLANK TAKEN	YES
VISUAL INSPECTION	
NUMBER OF INSPECTIONS:	NA
TYPE OF RESPIRATOR	NA
ENCLOSURE CLEAN:	NA
ENCLOSURE INTACT:	NA
INTERIOR OF ENCL. DRY:	NA
N.P.U. OFF AND SEALED	NA
NO LOCK DOWN SPRAY USED	NA

Limit of Quantification


The limit of quantification is 0.010 fibres /ml. where sample volumes of 480 litres or greater and at least 200 graticule fields are analysed. The result may be reported as 'less than 0.01 fibres /ml'.
Where sample volumes are less than 480 litres and/or less than 200 graticule fields are analysed then the limit of quantification may be greater than 0.01 fibres/ml.

This report must not be reproduced except in full without the approval of "Fourstage Environmental Ltd."

VARIOUS PHOTOS HAVE BEEN TAKEN DURING THIS PROCESS AND ARE AVAILABLE ON REQUEST.

THE REPORTED RESULTS ARE FOR RESPIRABLE FIBRES AND NOT NECESSARILY ASBESTOS FIBRES

PPROXIMATE SITE PLAN (X = SAMPLE)

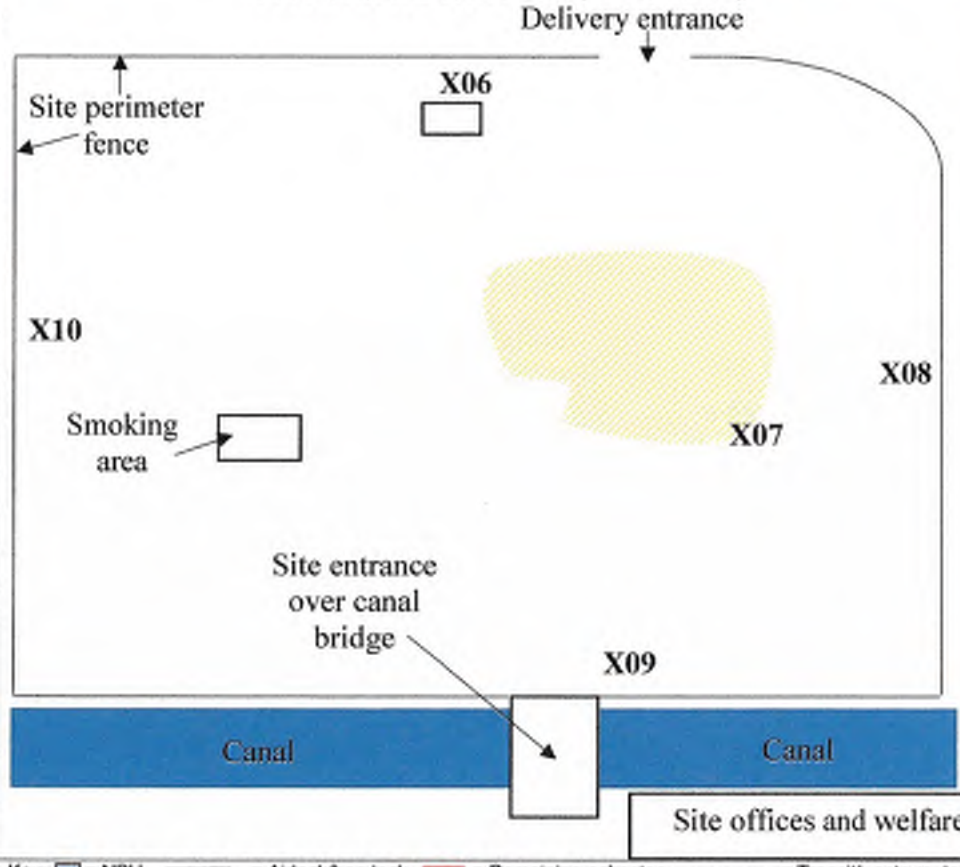

Key: = NPU = Airlock/bag lock = Remaining asbestos = Transit/waste route
= Vision Panels = Vacuum

The method used for sampling and the subsequent analysis as set out in HSG248 & in-house DOC/002

Contractor's Representative Acknowledgement of diagram accuracy	NAME:	SIGNATURE:

COMMENTS
(Outside scope of UKAS accreditation)

Reassurance air testing was undertaken to various locations on site while excavation works were being undertaken to various areas.

All results were satisfactory

Is generic Risk Assessment sufficient	YES

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

2671

AIRBORNE FIBRE MONITORING

TEST REPORT No. 30188

DATE	24 October 2021	BACKGROUND		APPROX. ENCLOSURE AREA/VOL (m^2/m^3)	NA
ANALYST NAME	Liam Carpenter	LEAK			
SITE ADDRESS	CLIENT name & address / Contractors Name & Address	CLEARANCE		MEASUREMENTS REQ'D	NA
Sport city Way Manchester M11 3DU	Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG / Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG	RE-ASSURANCE	YES	No. SAMPLES TAKEN	4
		PERSONAL		FILTER DIAM. (mm)	22
		STATIC		ASBESTOS REMOVAL OPERATION	
		RPE checks made	NO	Reassurance air testing during excavation works on site.	
		LAB REF: YR16 0WH			

ANALYST SIGNATURE

EXPOSURE TIME (minutes) NA — TYPE OF ASBESTOS (outside scope of UKAS accreditation) Not known

SAMPLE REF.	FILTER HEAD REF No.	PUMP REF No.	SAMPLE LOCATION	TYPE OF TEST	START TIME	END TIME	SAMPLE LENGTH	FLOW LITRE/min. START	FLOW LITRE/min. END	DUST DISTURB MINUTES	DUST DISTURB TYPE	LITRE	FIELDS	FIBRES	CONC. ACTUAL FIBRE/ml	CONC. REPORTED FIBRE/ml
52/241021/01	11	47	Site see plan	R	1054	1154	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
52/241021/02	12	45	Site see plan	R	1056	1156	60	8.0	8.0	NA	NA	480	200	2.5	0.0013	<0.01
52/241021/03	13	44	Site see plan	R	1058	1158	60	8.0	8.0	NA	NA	480	200	1.5	0.0007	<0.01
52/241021/04	14	43	Site see plan	R	1058	1158	60	8.0	8.0	NA	NA	480	200	2.5	0.0013	<0.01
			End of samples													

FOURSTAGE ENVIRONMENTAL LTD.

5a CLAPGUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

UKAS TESTING 2671

AIRBORNE FIBRE MONITORING

REPORT No. 30188

MICROSCOPE REF:	MIC-13
MICROSCOPE SET UP:	YES
HSE/NPL GROUP:	5
GRATICULE DIAM. (microns)	100
FLOWMETER:	HFM-14
TIME PIECE:	TIM-02
STAGE MICROMETER:	SM-04
TEST SLIDE:	TS-04
WEATHER CONDITIONS:	Rainy
FIELD BLANK TAKEN	YES

VISUAL INSPECTION

NUMBER OF INSPECTIONS:	NA
TYPE OF RESPIRATOR	NA
ENCLOSURE CLEAN:	NA
ENCLOSURE INTACT:	NA
INTERIOR OF ENCL. DRY:	NA
N.P.U. OFF AND SEALED	NA
NO LOCK DOWN SPRAY USED	NA

Limit of Quantification

The limit of quantification is 0.010 fibres /ml, where sample volumes of 480 litres or greater and at least 200 graticule fields are analysed. The result may be reported as 'less than 0.01 fibres /ml'.


Where sample volumes are less than 480 litres and/or less than 200 graticule fields are analysed then the limit of quantification may be greater than 0.01 fibres/ml.

This report must not be reproduced except in full without the approval of "Fourstage Environmental Ltd."

VARIOUS PHOTOS HAVE BEEN TAKEN DURING THIS PROCESS AND ARE AVAILABLE ON REQUEST.

THE REPORTED RESULTS ARE FOR RESPIRABLE FIBRES AND NOT NECESSARILY ASBESTOS FIBRES

PPROXIMATE SITE PLAN (X = SAMPLE)

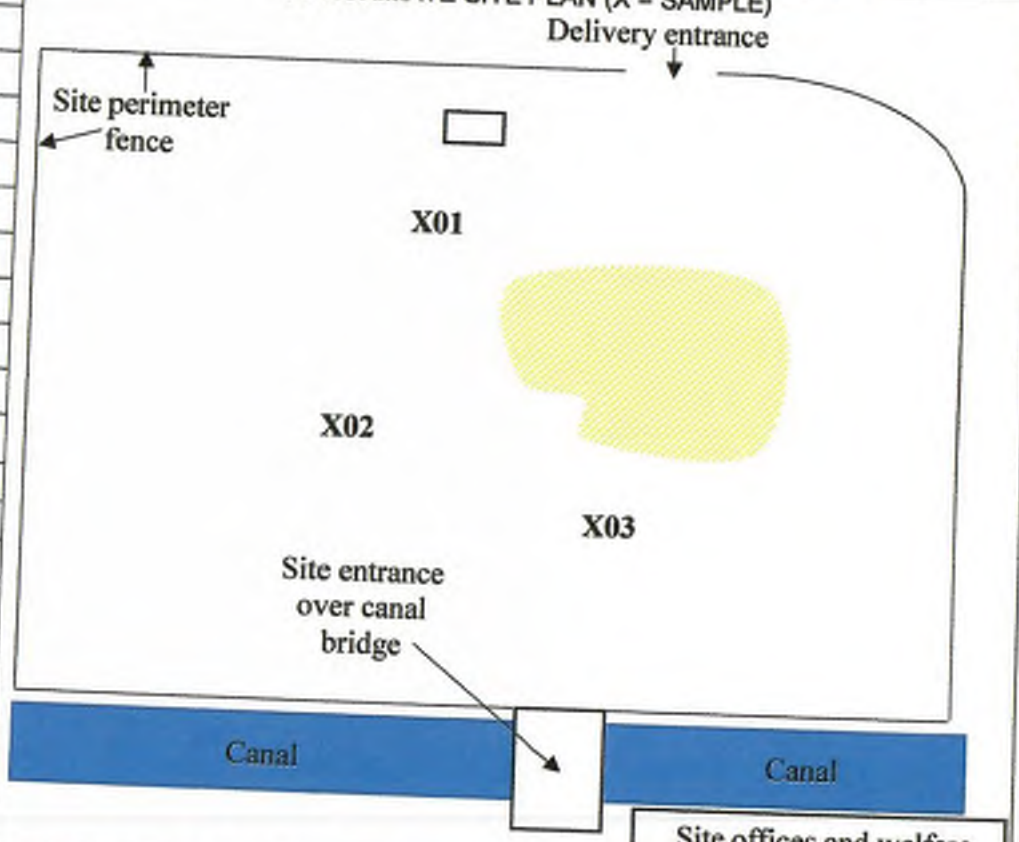

Key: = NPU = Airlock/bag lock = Remaining asbestos = Transit/waste route = Vision Panels = Vacuum

The method used for sampling and the subsequent analysis as set out in HSG248 & in-house DOC/002

Contractor's Representative Acknowledgement of diagram accuracy NAME: A- CLIFFORD SIGNATURE: A Clifford

COMMENTS (Outside scope of UKAS accreditation)

Reassurance air testing was undertaken to various locations on site while excavation works were being undertaken to various areas.

All results were satisfactory

Is generic Risk Assessment sufficient: YES

FOURSTAGE ENVIRONMENTAL LTD.

5a O[illegible]GUN STREET, CASTLE DONINGTON, DERBY, [illegible]74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

UKAS TESTING 2671

AIRBORNE FIBRE MONITORING

TEST REPORT No. **30202**

DATE	4 November 2021
ANALYST NAME	Liam Carpenter
SITE ADDRESS	Sport city Way Manchester M11 3DU
CLIENT name & address	Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG
Contractors Name & Address	Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG
ANALYST SIGNATURE	

BACKGROUND		
LEAK		
CLEARANCE		
RE-ASSURANCE	YES	
PERSONAL		
STATIC		
RPE checks made	NO	
LAB REF: YR16 0WH		

APPROX. ENCLOSURE AREA/VOL (m²/m³)	NA
MEASUREMENTS REQ'D	NA
No. SAMPLES TAKEN	4
FILTER DIAM. (mm)	22
ASBESTOS REMOVAL OPERATION	
Reassurance air testing during excavation works on site.	

EXPOSURE TIME (minutes) — NA

TYPE OF ASBESTOS (outside scope of UKAS accreditation) — Not known

SAMPLE REF.	FILTER HEAD REF No.	PUMP REF No.	SAMPLE LOCATION	TYPE OF TEST	START TIME	END TIME	SAMPLE LENGTH	FLOW LITRE/min START	FLOW LITRE/min END	DUST DISTURB MINUTES	DUST DISTURB TYPE	LITRE	FIELDS	FIBRES	CONC. ACTUAL FIBRE/ml	CONC. REPORTED FIBRE/ml
52/041121/04	11	47	Site see plan	R	1344	1444	60	8.0	8.0	NA	NA	480	200	3.5	0.0018	<0.01
52/041121/05	12	45	Site see plan	R	1344	1444	60	8.0	8.0	NA	NA	480	200	1.5	0.0007	<0.01
52/041121/06	13	44	Site see plan	R	1345	1445	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
52/041121/07	14	43	Site see plan	R	1346	1446	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
			End of samples													

FOURSTAGE ENVIRONMENTAL LTD.

5a C[illegible]GUN STREET, CASTLE DONINGTON, DERBY[illegible]74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

UKAS TESTING 2671

AIRBORNE FIBRE MONITORING | REPORT No. 30202

MICROSCOPE REF:	MIC-13
MICROSCOPE SET UP:	YES
HSE/NPL GROUP:	5
GRATICULE DIAM. (microns)	100
FLOWMETER:	HFM-14
TIME PIECE:	TIM-02
STAGE MICROMETER:	SM-04
TEST SLIDE:	TS-04
WEATHER CONDITIONS:	Cloudy
FIELD BLANK TAKEN	YES

VISUAL INSPECTION

NUMBER OF INSPECTIONS:	NA
TYPE OF RESPIRATOR	NA
ENCLOSURE CLEAN:	NA
ENCLOSURE INTACT:	NA
INTERIOR OF ENCL. DRY:	NA
N.P.U. OFF AND SEALED	NA
NO LOCK DOWN SPRAY USED	NA

Limit of Quantification


The limit of quantification is 0.010 fibres /ml. where sample volumes of 480 litres or greater and at least 200 graticule fields are analysed. The result may be reported as 'less than 0.01 fibres /ml'.
Where sample volumes are less than 480 litres and/or less than 200 graticule fields are analysed then the limit of quantification may be greater than 0.01 fibres/ml.

This report must not be reproduced except in full without the approval of "Fourstage Environmental Ltd."

VARIOUS PHOTOS HAVE BEEN TAKEN DURING THIS PROCESS AND ARE AVAILABLE ON REQUEST

THE REPORTED RESULTS ARE FOR RESPIRABLE FIBRES AND NOT NECESSARILY ASBESTOS FIBRES

PPROXIMATE SITE PLAN (X = SAMPLE)

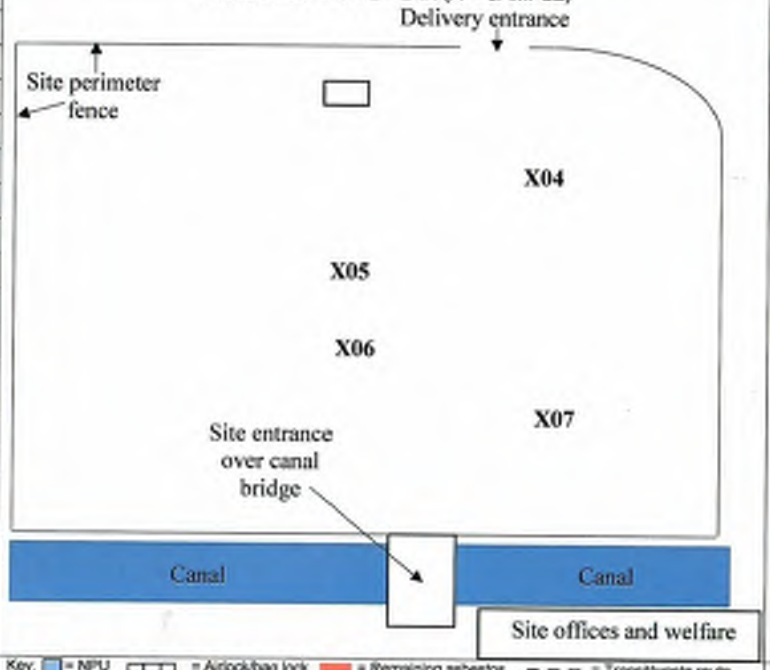

Key: = NPU = Airlock/bag lock = Remaining asbestos = Transit/waste route
= Vision Panels = Vacuum
The method used for sampling and the subsequent analysis as set out in HSG248 & in-house DOC/002

Contractor's Representative Acknowledgement of diagram accuracy | NAME: GUY SMITH | SIGNATURE: [signature]

COMMENTS (Outside scope of UKAS accreditation)

Reassurance air testing was undertaken to various locations on site while excavation works were being undertaken to various areas.

All results were satisfactory

Is generic Risk Assessment sufficient: YES

FOURSTAGE ENVIRONMENTAL LTD.

5a CL[illegible]GUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

2671

AIRBORNE FIBRE MONITORING

TEST REPORT No. 30209

DATE	9 November 2021	BACKGROUND	
ANALYST NAME	Liam Carpenter	LEAK	
SITE ADDRESS	CLIENT name & address: Provectus Remediation Ltd, Regent House, Bath Avenue, Wolverhampton, WV1 4EG	CLEARANCE	
Sport city Way, Manchester, M11 3DU	Contractors Name & Address: Provectus Remediation Ltd, Regent House, Bath Avenue, Wolverhampton, WV1 4EG	RE-ASSURANCE	YES
		PERSONAL	
		STATIC	
		RPE checks made	NO
		LAB REF: YR16 0WH	

APPROX. ENCLOSURE AREA/VOL (m²/m³)	NA
MEASUREMENTS REQ'D	NA
No. SAMPLES TAKEN	4
FILTER DIAM. (mm)	22
ASBESTOS REMOVAL OPERATION	Reassurance air testing during excavation works on site.

ANALYST SIGNATURE

EXPOSURE TIME (minutes) NA

TYPE OF ASBESTOS (outside scope of UKAS accreditation): Not known

SAMPLE REF.	FILTER HEAD REF No.	PUMP REF No.	SAMPLE LOCATION	TYPE OF TEST	START TIME	END TIME	SAMPLE LENGTH	FLOW LITRE/min. START	FLOW LITRE/min. END	DUST DISTURB MINUTES	DUST DISTURB TYPE	LITRE	FIELDS	FIBRES	CONC. ACTUAL FIBRE/ml	CONC. REPORTED FIBRE/ml
52/091121/01	11	47	Site see plan	R	1041	1141	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
52/091121/02	12	45	Site see plan	R	1041	1141	60	8.0	8.0	NA	NA	480	200	3	0.0015	<0.01
52/091121/03	13	44	Site see plan	R	1042	1142	60	8.0	8.0	NA	NA	480	200	1.5	0.0007	<0.01
52/091121/04	14	43	Site see plan	R	1042	1142	60	8.0	8.0	NA	NA	480	200	2.5	0.0013	<0.01
			End of samples													

FOURSTAGE ENVIRONMENTAL LTD.

5a CE[illegible]GUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

2671

AIRBORNE FIBRE MONITORING — REPORT No. 30209

MICROSCOPE REF:	MIC-13
MICROSCOPE SET UP:	YES
HSE/NPL GROUP:	5
GRATICULE DIAM. (microns)	100
FLOWMETER:	HFM-14
TIME PIECE:	TIM-02
STAGE MICROMETER:	SM-04
TEST SLIDE:	TS-04
WEATHER CONDITIONS:	Cloudy
FIELD BLANK TAKEN	YES


VISUAL INSPECTION

NUMBER OF INSPECTIONS:	NA
TYPE OF RESPIRATOR	NA
ENCLOSURE CLEAN:	NA
ENCLOSURE INTACT:	NA
INTERIOR OF ENCL. DRY:	NA
N.P.U. OFF AND SEALED	NA
NO LOCK DOWN SPRAY USED	NA

Limit of Quantification

The limit of quantification is 0.010 fibres /ml. where sample volumes of 480 litres or greater and at least 200 graticule fields are analysed. The result may be reported as 'less than 0.01 fibres /ml'.
Where sample volumes are less than 480 litres and/or less than 200 graticule fields are analysed then the limit of quantification may be greater than 0.01 fibres/ml.

PPROXIMATE SITE PLAN (X = SAMPLE)

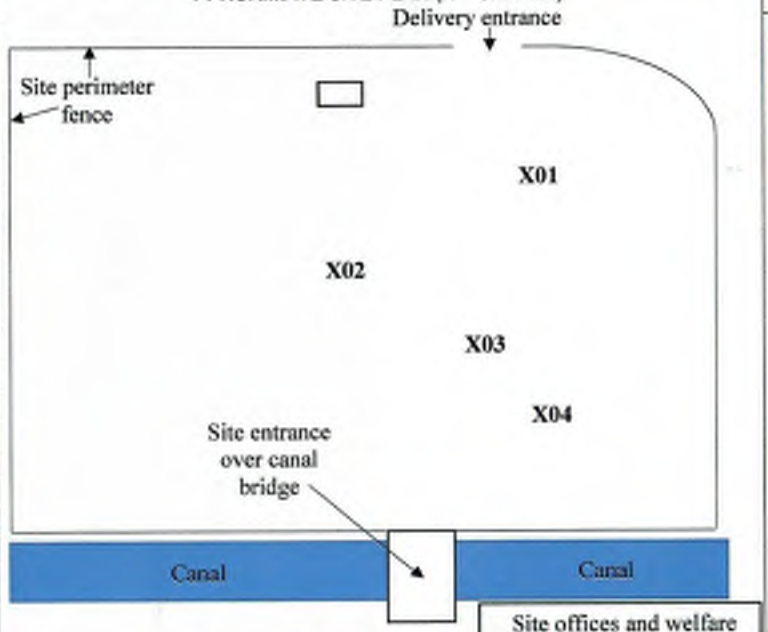

Key: = NPU = Airlock/bag lock = Remaining asbestos = Transit/waste route
= Visilon Panels = Vacuum
The method used for sampling and the subsequent analysis as set out in HSG248 & in-house DOC/002

COMMENTS
(Outside scope of UKAS accreditation)

Reassurance air testing was undertaken to various locations on site while excavation works were being undertaken to various areas.

All results were satisfactory

Is generic Risk Assessment sufficient: YES

This report must not be reproduced except in full without the approval of "Fourstage Environmental Ltd."

VARIOUS PHOTOS HAVE BEEN TAKEN DURING THIS PROCESS AND ARE AVAILABLE ON REQUEST.

THE REPORTED RESULTS ARE FOR RESPIRABLE FIBRES AND NOT NECESSARILY ASBESTOS FIBRES

Contractor's Representative Acknowledgement of diagram accuracy — NAME: T. Horrington — SIGNATURE:

FOURSTAGE ENVIRONMENTAL LTD.

5a CL GUN STREET, CASTLE DONINGTON, DERBY, 74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

2671

AIRBORNE FIBRE MONITORING

TEST REPORT No. 30217

DATE	16 November 2021	BACKGROUND		APPROX. ENCLOSURE AREA/VOL (m²/m³)	NA
ANALYST NAME	Liam Carpenter	LEAK			
SITE ADDRESS	CLIENT name & address / Contractors Name & Address	CLEARANCE		MEASUREMENTS REQ'D	NA
Sport city Way Manchester M11 3DU	Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG / Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG	RE-ASSURANCE	YES	No. SAMPLES TAKEN	4
		PERSONAL		FILTER DIAM. (mm)	22
		STATIC		ASBESTOS REMOVAL OPERATION	
		RPE checks made	NO	Reassurance air testing during excavation works on site.	
		LAB REF: YR16 0WH			

ANALYST SIGNATURE

EXPOSURE TIME (minutes) — NA — TYPE OF ASBESTOS (outside scope of UKAS accreditation) — Not known

SAMPLE REF.	FILTER HEAD REF No.	PUMP REF No.	SAMPLE LOCATION	TYPE OF TEST	START TIME	END TIME	SAMPLE LENGTH	FLOW LITRE/min. START	FLOW LITRE/min. END	DUST DISTURB MINUTES	DUST DISTURB TYPE	LITRE	FIELDS	FIBRES	CONC. ACTUAL FIBRE/ml	CONC. REPORTED FIBRE/ml
52/161121/01	11	47	Site see plan	R	1049	1149	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
52/161121/02	12	45	Site see plan	R	1050	1150	60	8.0	8.0	NA	NA	480	200	1.5	0.0007	<0.01
52/161121/03	13	44	Site see plan	R	1051	1151	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
52/161121/04	14	43	Site see plan	R	1052	1152	60	8.0	8.0	NA	NA	480	200	2.5	0.0013	<0.01
			End of samples													

FOURSTAGE ENVIRONMENTAL LTD.

5a C[illegible] GUN STREET, CASTLE DONINGTON, DERBY, [illegible]74 2LE
Telephone: 01332 812549 Email: info@fourstage.co.uk

UKAS TESTING 2671

AIRBORNE FIBRE MONITORING — REPORT No. 30217

MICROSCOPE REF:	MIC-13
MICROSCOPE SET UP:	YES
HSE/NPL GROUP:	5
GRATICULE DIAM. (microns)	100
FLOWMETER:	HFM-14
TIME PIECE:	TIM-02
STAGE MICROMETER:	SM-04
TEST SLIDE:	TS-04
WEATHER CONDITIONS:	Rainy
FIELD BLANK TAKEN	YES
VISUAL INSPECTION	
NUMBER OF INSPECTIONS:	NA
TYPE OF RESPIRATOR	NA
ENCLOSURE CLEAN:	NA
ENCLOSURE INTACT:	NA
INTERIOR OF ENCL. DRY:	NA
N.P.U. OFF AND SEALED	NA
NO LOCK DOWN SPRAY USED	NA

Limit of Quantification


The limit of quantification is 0.010 fibres /ml, where sample volumes of 480 litres or greater and at least 200 graticule fields are analysed. The result may be reported as 'less than 0.01 fibres /ml'.
Where sample volumes are less than 480 litres and/or less than 200 graticule fields are analysed then the limit of quantification may be greater than 0.01 fibres/ml.

This report must not be reproduced except in full without the approval of "Fourstage Environmental Ltd."

VARIOUS PHOTOS HAVE BEEN TAKEN DURING THIS PROCESS AND ARE AVAILABLE ON REQUEST.

THE REPORTED RESULTS ARE FOR RESPIRABLE FIBRES AND NOT NECESSARILY ASBESTOS FIBRES

PPROXIMATE SITE PLAN (X = SAMPLE)

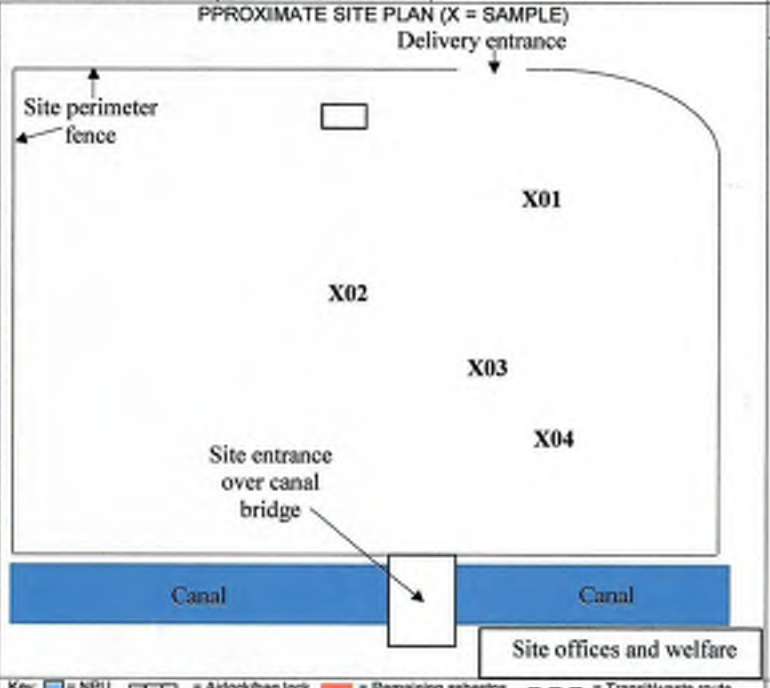

Key: = NPU = Airlock/bag lock = Remaining asbestos = Transit/waste route = Vision Panels = Vacuum

The method used for sampling and the subsequent analysis as set out in HSG248 & in-house DOC/002

COMMENTS (Outside scope of UKAS accreditation)

Reassurance air testing was undertaken to various locations on site while excavation works were being undertaken to various areas.

All results were satisfactory

Is generic Risk Assessment sufficient: YES

Contractor's Representative Acknowledgement of diagram accuracy — NAME: Guy Smith — SIGNATURE: [signature]

FOURSTAGE ENVIRONMENTAL LTD.

5a CL[illegible]GUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
Telephone: 01332 812549 Email: info@fourstage.co

2671

AIRBORNE FIBRE MONITORING

TEST REPORT No. 30225

DATE	25 November 2021	BACKGROUND		APPROX. ENCLOSURE AREA/VOL (m²/m³)	NA
ANALYST NAME	Liam Carpenter	LEAK			
SITE ADDRESS	CLIENT name & address / Contractors Name & Address	CLEARANCE		MEASUREMENTS REQ'D	NA
Sport city Way Manchester M11 3DU	Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV1 4EG (Client & Contractors)	RE-ASSURANCE	YES	No. SAMPLES TAKEN	4
		PERSONAL		FILTER DIAM. (mm)	22
		STATIC		ASBESTOS REMOVAL OPERATION	
		RPE checks made	NO	Reassurance air testing during excavation works on site.	
		LAB REF: YR16 0WH			

ANALYST SIGNATURE: [signature]

EXPOSURE TIME (minutes): NA

TYPE OF ASBESTOS (outside scope of UKAS accreditation): Not known

SAMPLE REF.	FILTER HEAD REF No.	PUMP REF No.	SAMPLE LOCATION	TYPE OF TEST	START TIME	END TIME	SAMPLE LENGTH	FLOW LITRE/min. START	FLOW LITRE/min. END	DUST DISTURB MINUTES	DUST DISTURB TYPE	LITRE	FIELDS	FIBRES	CONC. ACTUAL FIBRE/ml	CONC. REPORTED FIBRE/ml
52/251121/01	11	47	Site see plan	R	1131	1231	60	8.0	8.0	NA	NA	480	200	2.5	0.0013	<0.01
52/251121/02	12	45	Site see plan	R	1132	1232	60	8.0	8.0	NA	NA	480	200	1.5	0.0007	<0.01
52/251121/03	13	44	Site see plan	R	1133	1233	60	8.0	8.0	NA	NA	480	200	1	0.0005	<0.01
52/251121/04	14	43	Site see plan	R	1134	1234	60	8.0	8.0	NA	NA	480	200	2	0.0010	<0.01
			End of samples													

FOURSTAGE ENVIRONMENTAL LTD.

5a CL[illegible]GUN STREET, CASTLE DONINGTON, DERBY, DE74 2LE
[illegible]elephone: 01332 812549 Email: info@fourstage.co

UKAS TESTING 2671

AIRBORNE FIBRE MONITORING	REPORT No.	30225

MICROSCOPE REF:	MIC-13
MICROSCOPE SET UP:	YES
HSE/NPL GROUP:	5
GRATICULE DIAM. (microns)	100
FLOWMETER:	HFM-14
TIME PIECE:	TIM-02
STAGE MICROMETER:	SM-04
TEST SLIDE:	TS-04
WEATHER CONDITIONS:	Rainy
FIELD BLANK TAKEN	YES
VISUAL INSPECTION	
NUMBER OF INSPECTIONS:	NA
TYPE OF RESPIRATOR	NA
ENCLOSURE CLEAN:	NA
ENCLOSURE INTACT:	NA
INTERIOR OF ENCL. DRY:	NA
N.P.U. OFF AND SEALED	NA
NO LOCK DOWN SPRAY USED	NA

Limit of Quantification


The limit of quantification is 0.010 fibres /ml, where sample volumes of 480 litres or greater and at least 200 graticule fields are analysed. The result may be reported as 'less than 0.01 fibres /ml'.
Where sample volumes are less than 480 litres and/or less than 200 graticule fields are analysed then the limit of quantification may be greater than 0.01 fibres/ml.

This report must not be reproduced except in full without the approval of "Fourstage Environmental Ltd."

VARIOUS PHOTOS HAVE BEEN TAKEN DURING THIS PROCESS AND ARE AVAILABLE ON REQUEST

THE REPORTED RESULTS ARE FOR RESPIRABLE FIBRES AND NOT NECESSARILY ASBESTOS FIBRES

PPROXIMATE SITE PLAN (X = SAMPLE)

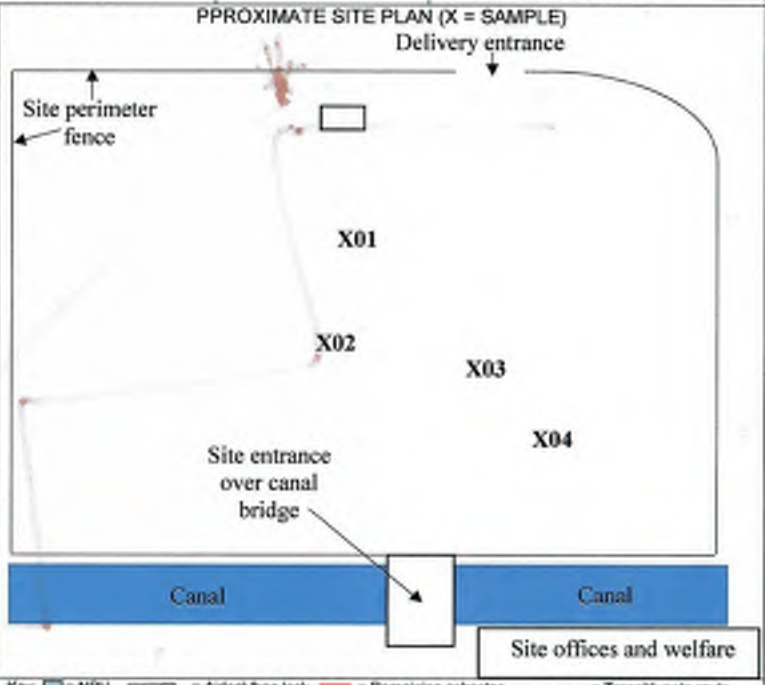

Key: = NPU = Airlock/bag lock = Remaining asbestos = Transit/waste route
= Vision Panels = Vacuum
The method used for sampling and the subsequent analysis as set out in HSG248 & in-house DOC/002

Contractor's Representative Acknowledgement of diagram accuracy — NAME: [illegible] — SIGNATURE: [illegible]

COMMENTS
(Outside scope of UKAS accreditation)

Reassurance air testing was undertaken to various locations on site while excavation works were being undertaken to various areas.

All results were satisfactory

Is generic Risk Assessment sufficient: YES

APPENDIX I Plate Bearing Test Results and Location Plan

Plate Test Results Tracker

PROVECTUS

BAM Ref	Mat	Row	Date	Max Deflection	Notes
1	LLW	A			HLM at 56 m aod - Pending design confirmation
2	LLW	A			HLM at 56 m aod - Pending design confirmation
3	LLW	C	07/04/2021	8.15	Tested before decremental release was requested and unavailable for subsequent retest
4	LLW	C	07/04/2021	7.56	Tested before decremental release was requested and unavailable for subsequent retest
5	LLE	E	18/06/2021	8.6	
6	LLE	E	18/06/2021	3	
7	LLW	B	13/04/2021	6.03	retest to 544kN/m2
8	LLW	B	13/04/2021	6.43	retest to 544kN/m3
9	LLW	D	22/06/2021	4.47	
10	CB	D	07/06/2021	11.71	
11	LLE	F	22/06/2021	11.97	
11a	LLE	F	26/07/2021	5.21	
12	LLE	F	10/09/2021	2.27	
13	LLW	A	21/07/2021	5.6	
14a	LLW	A	26/07/2021	4.32	
15	CB	C	29/03/2021	3.95	Tested before decremental release was requested and unavailable for subsequent retest
16	CB	C	29/03/2021	6.59	Tested before decremental release was requested and unavailable for subsequent retest
17	CB	E	22/06/2021	2.33	Max load achieved, test aborted before decremental release to allow concrete wagons up ramp
18	CB	E	22/06/2021 10/09/21	7.35 2.63	first test slightly wrong location
19	LLE	G	17/09/2021	2.18	
20	n/a	G	n/a	n/a	in Alan Turing Way
21	LLW	B	10/05/2021	11.97	
22	CB	B	03/06/2021	6.94	
22A	LLW	B	03/06/2021	15.08	Location set out by BAM
23	CB	D	07/06/2021	7.65	
24	CB	D	07/06/2021	14.46	
25	LLE	F	17/09/2021	1.9	
26	LLE	F	17/09/2021	3.25	
27	LLW	A	28/07/2021	3.68	
28	LLW	A	28/07/2021	4	
29	LLW	C	18/06/2021	4.99	
30	CB	C	07/06/2021	17.39	
31	LLE	E	18/05/2021	12.08	
32	LLE	E	03/06/2021	7.53	
33		G	N/A		Rig working- See 502 results as replacement to 1700kN
34	LLE	G	17/09/2021	1.92	
35	LLW	B	10/05/2021	11.69	Passed but without decremental release
35A	LLW	B	03/06/2021	9.74	Location set out by BAM
36	LLS	B	10/05/2021	12.16	
36A	LLW	B/C	03/06/2021	13.25	Location set out by BAM
37	LLS	D	02/12/2021	4.8	
38	LLS	D	02/12/2021	8.75	
39A	LLS	F	03/11/2021	15.39	
40	LLS	F	12/11/2021	10.86	
41A	LLW	A	28/07/2021	4	
42	LLW	A	28/07/2021	3.22	
43	LLW	C	28/07/2021	3.58	
44	LLS	C	02/12/2021	8.55	
45A	LLS	E	26.11.21	9.43	Moved due to access issues
46A	LLS	E	26.11.21	6.64	Moved due to access issues
47A	LLS	G	12/11/2021	13.47	Moved due to access issues
48A	LLE	G	12/11/2021	9.55	Moved due to access issues
49	HLW	A	13/04/2021	6.24	
50	HLW	A	13/04/2021	5.82	
51	HLW	A	07/04/2021	9.19	Pre-dates request for decremental release
52	HLW	A	07/04/2021	8.59	Pre-dates request for decremental release
53	HLE	G	23/04/2021	3.41	
54	HLE	G	23/04/2021	6.58	
55	HLE	G	23/04/2021	4.44	
56	HLS	G	27/04/2021	11.26	
57	HLS	F	23/04/2021	6.65	
58	HLS	D	23/04/2021	5.46	
NEC-1	HLE	F	22/10/2021	12.43	
NEC-2	HLE	G	22/10/2021	17.1	
501	NA	F	12/11/2021	5.15	
502	NA	G	12/11/2021	3.25	Replacement for PLT33
503	NA	G	12/11/2021	15.84	
504	NA	F	12/11/2021	11.68	



stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Derbyshire. DE6 5HS
T 01283 584800 F 01284 584844 E info@stafsurv.com

NOTES

Levels Relate To : SITE DATUM

Co-ordInates : SITE GRID

40 GL:54.88m As Built Location Higher

40 Proposed Location Higher

40 GL:54.88m As Built Location Lower

40 Proposed Location Lower

CLIENT

PROVECTUS

SITE

Project Bradford
101114

PROJECT

As Built Land CBR Test Locations
High & Low Level Areas

SCALE	DRAWING DATE
1:500 @ A1	14/12/2021

DRAWING No.

12037d-0

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4AJ
T | (01302) 353652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/2C Clients Reference: DN3046/2C	**REPORT NO:** DNR/63774C Report Date: 08/04/2021

Material Description:	Stone	Date Tested:	07/04/2021
Test Location:	PT 5A	Supplier/Source:	Not Stated
Weather:	Clear		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	88.7	1.76
4.0	180.5	3.55
6.0	271.4	5.24
8.0	363.1	6.61
10.0	435.1	7.66
12.0	507.7	8.35
14.0	544.4	9.19
16.0	0.0	6.58

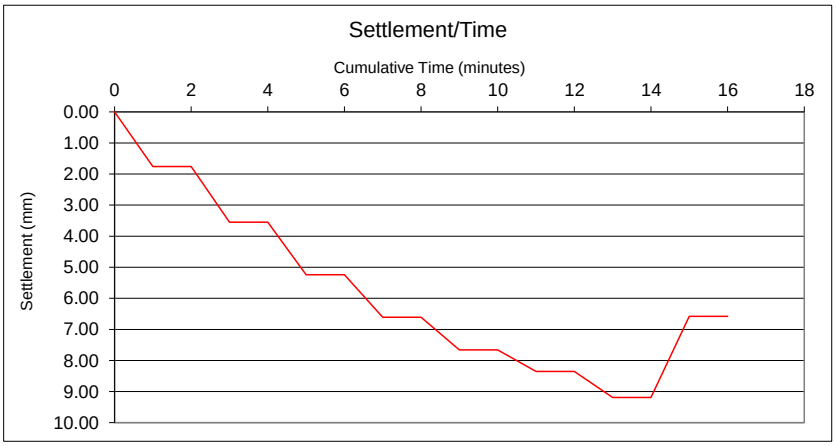

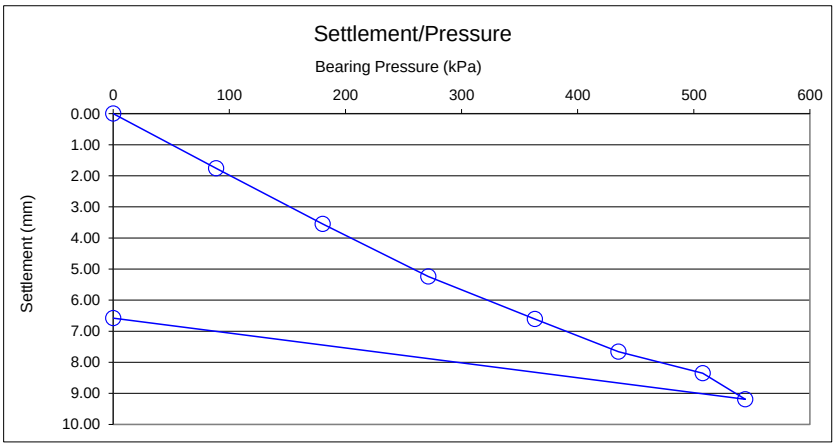


Plate Diameter	**600 mm**	Maximum Applied Pressure	**544.4 kPa**
Reaction Load	**33T**	Maximum Settlement	**9.19 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm) **N/A**			

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Gibbon Street, Manchester

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4AJ
T | (01302) 353652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/2D Clients Reference: DN3046/2D	**REPORT NO:** DNR/63774D Report Date: 08/04/2021

Material Description:	Stone	Date Tested:	07/04/2021
Test Location:	PT 6A	Supplier/Source:	Not Stated
Weather:	Clear		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	88.7	1.64
4.0	180.5	3.25
6.0	271.4	4.19
8.0	363.1	5.51
10.0	435.1	6.67
12.0	507.7	7.67
14.0	544.4	8.59
16.0	0.0	5.87

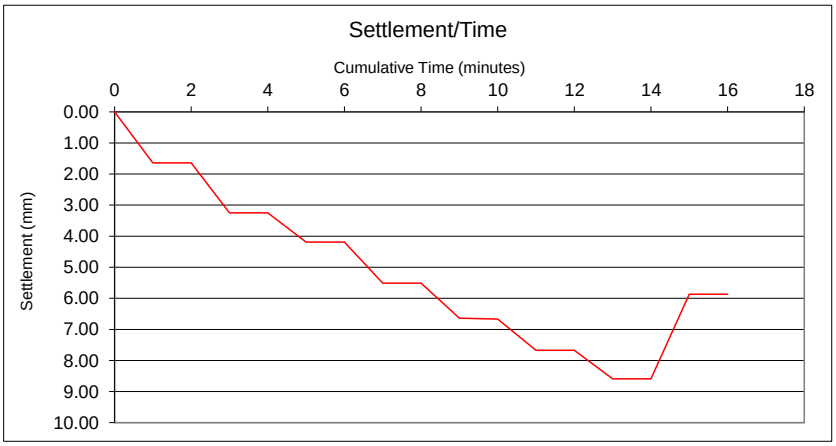

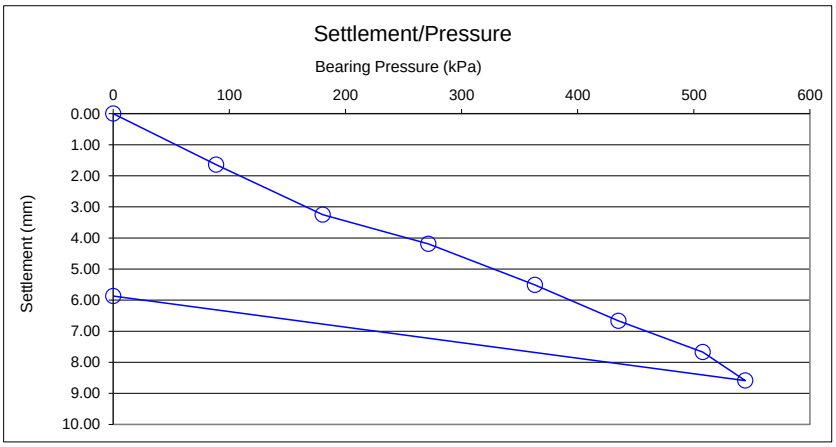


Plate Diameter	**600 mm**	Maximum Applied Pressure	**544.4 kPa**
Reaction Load	**33T**	Maximum Settlement	**8.59 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm) **N/A**			

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/3B Clients Reference: **DN3046/3B**	**REPORT NO:** **DNR/64253B** Report Date: 14/04/2021

Material Description:	6F2/Mot	Date Tested:	13/04/2021
Test Location:	PT 49	Supplier/Source:	Not Stated
Weather:	Clear		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	36.3	1.28
4.0	142.6	2.46
6.0	326.1	3.83
8.0	435.1	4.88
10.0	544.4	6.24
12.0	435.1	5.35
14.0	326.1	4.28
16.0	142.6	3.54
18.0	36.3	2.55
20.0	0.0	1.68

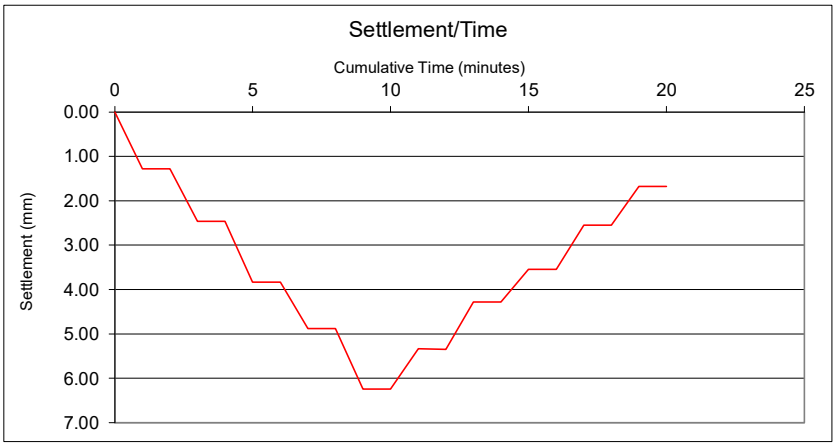

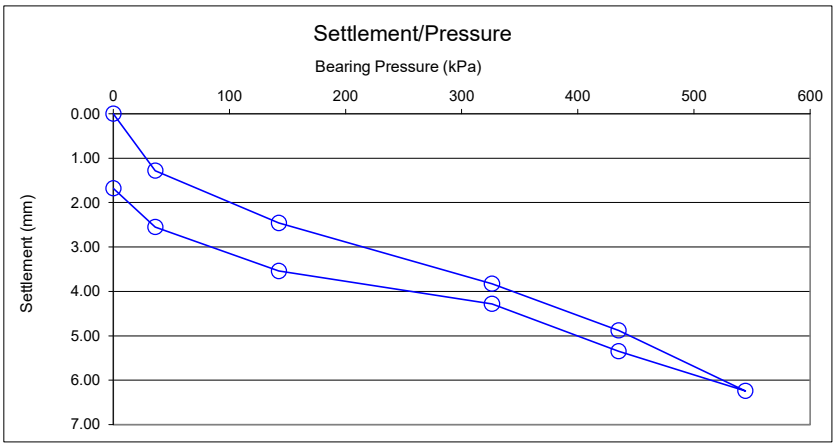


Plate Diameter	**600 mm**	Maximum Applied Pressure	**544.4 kPa**
Reaction Load	**33T**	Maximum Settlement	**6.24 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm) **N/A**			

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/3A Clients Reference: **DN3046/3A**	**REPORT NO: DNR/64253A** Report Date: 14/04/2021

Material Description:	6F2/Mot	Date Tested:	13/04/2021
Test Location:	PT 50	Supplier/Source:	Not Stated
Weather:	Clear		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	36.3	1.37
4.0	142.6	2.55
6.0	326.1	3.63
8.0	435.1	5.01
10.0	544.4	5.82
12.0	435.1	4.74
14.0	326.1	4.09
16.0	142.6	3.46
18.0	36.3	1.94
20.0	0.0	1.66

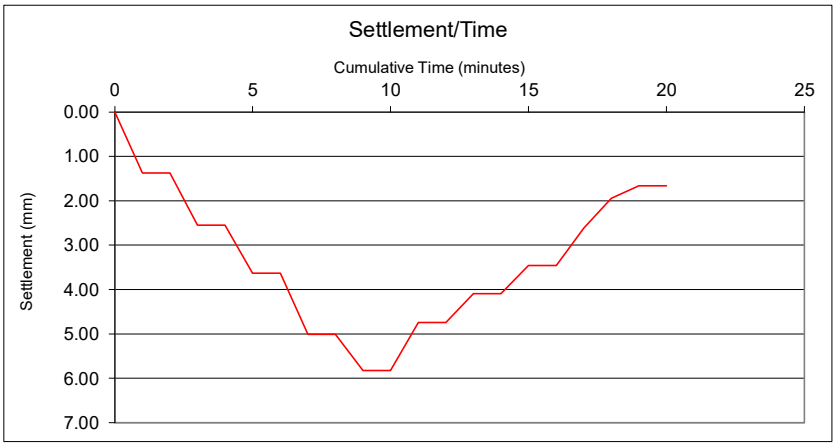

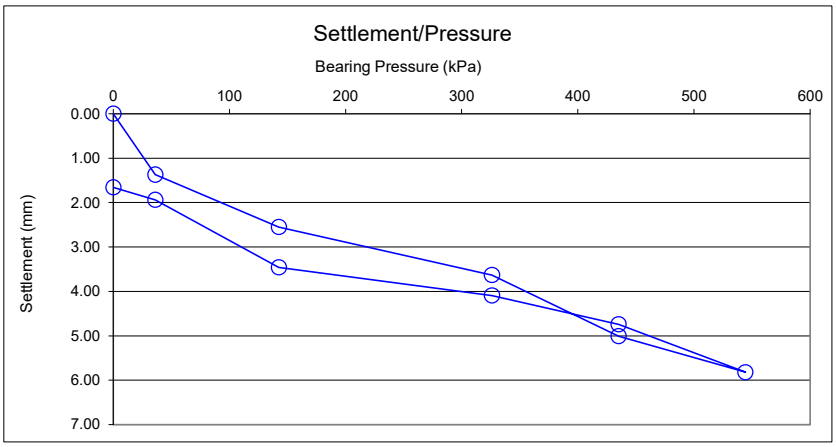


Plate Diameter	**600 mm**	Maximum Applied Pressure	**544.4 kPa**
Reaction Load	**33T**	Maximum Settlement	**5.82 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/4A Clients Reference: **DN3046/4A**	**REPORT NO:** **DNR/65862A** Report Date: 26/04/2021

Material Description:	Crush	Date Tested:	23/04/2021
Test Location:	53	Supplier/Source:	Not Stated
Weather:	Clear		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	76.5	0.47
4.0	151.6	1.30
6.0	300.9	2.02
8.0	452.1	2.53
10.0	542.1	3.41
12.0	452.1	3.04
14.0	300.9	2.67
16.0	151.6	2.31
18.0	76.5	1.90
20.0	0.0	1.22

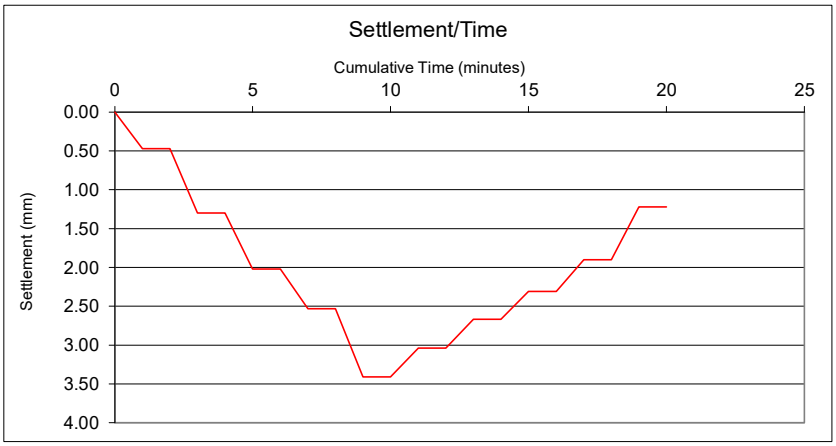

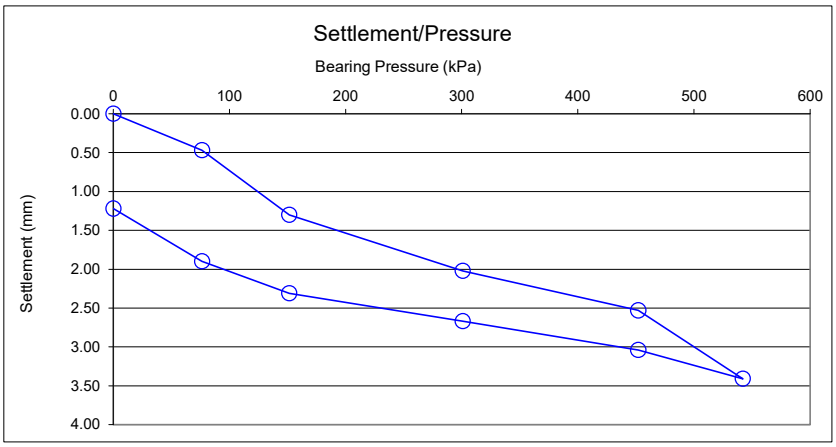


Plate Diameter	**600 mm**	Maximum Applied Pressure	**542.1 kPa**
Reaction Load	**30T**	Maximum Settlement	**3.41 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/4B Clients Reference: **DN3046/4B**	**REPORT NO:** **DNR/65862B** Report Date: 26/04/2021

Material Description:	Crush	Date Tested:	23/04/2021
Test Location:	54	Supplier/Source:	Not Stated
Weather:	Clear		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	76.5	2.23
4.0	151.6	3.71
6.0	300.9	5.11
8.0	452.1	5.79
10.0	542.1	6.58
12.0	452.1	5.46
14.0	300.9	4.73
16.0	151.6	3.68
18.0	76.5	2.55
20.0	0.0	1.67

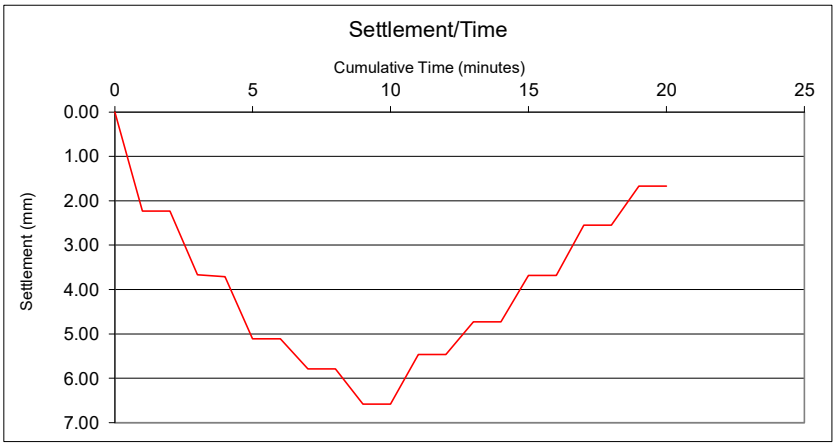

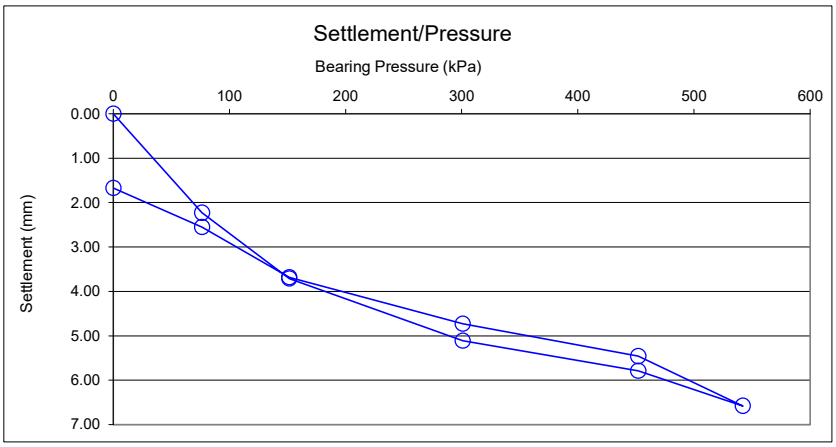


Plate Diameter	**600 mm**	Maximum Applied Pressure	**542.1 kPa**
Reaction Load	**30T**	Maximum Settlement	**6.58 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/4E Clients Reference: **DN3046/4E**	**REPORT NO:** **DNR/65862E** Report Date: 26/04/2021

Material Description:	Crush	Date Tested:	23/04/2021
Test Location:	55	Supplier/Source:	Not Stated
Weather:	Clear		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	76.5	1.08
4.0	151.6	2.20
6.0	300.9	3.14
8.0	452.1	3.78
10.0	542.1	4.44
12.0	452.1	3.95
14.0	300.9	3.57
16.0	151.6	2.76
18.0	76.5	2.19
20.0	0.0	0.84

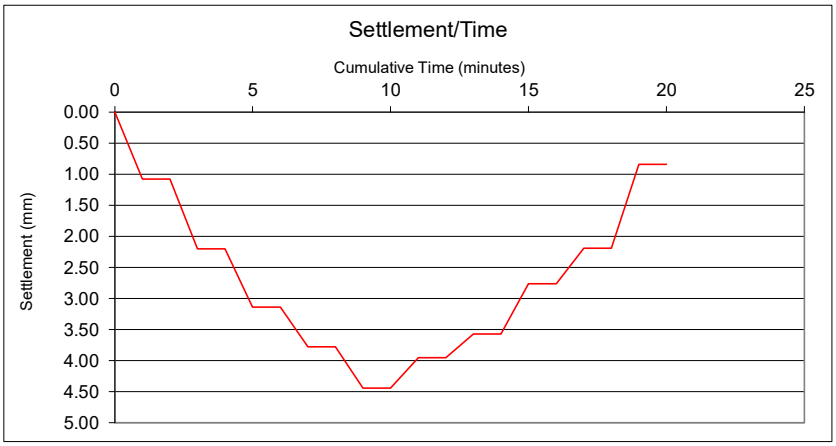

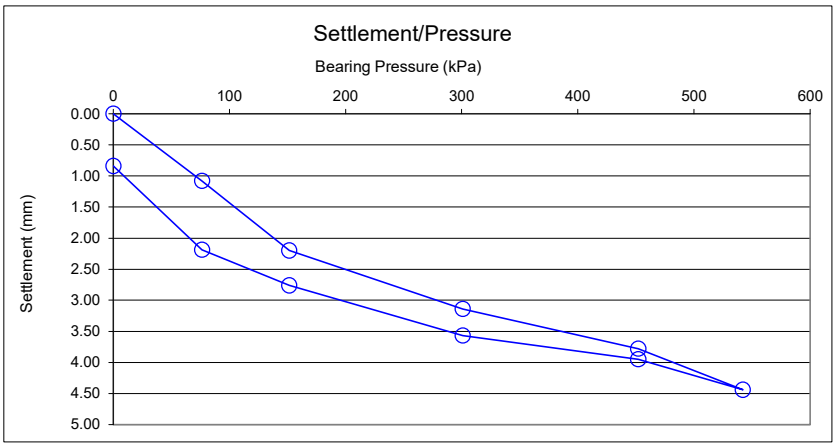


Plate Diameter	**600 mm**	Maximum Applied Pressure	**542.1 kPa**
Reaction Load	**30T**	Maximum Settlement	**4.44 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm) **N/A**			

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4AJ
T | (01302) 353652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/5 Clients Reference: DN3046/5	**REPORT NO:** DNR/66070 Report Date: 28/04/2021

Material Description:	Type 1	Date Tested:	27/04/2021
Test Location:	PT56	Supplier/Source:	Not Stated
Weather:	Overcast		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	107.7	1.22
4.0	214.8	2.97
6.0	326.1	5.05
8.0	435.1	7.57
10.0	544.4	11.26
12.0	435.1	11.04
14.0	326.1	10.86
16.0	214.8	10.66
18.0	107.7	9.34
20.0	0.0	5.89

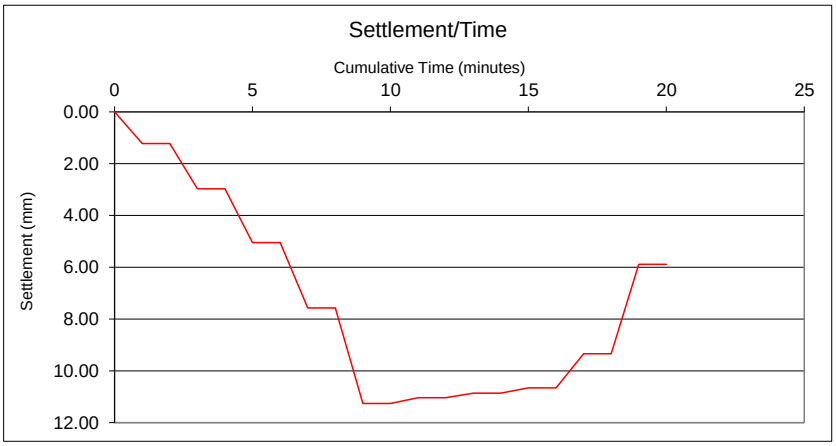

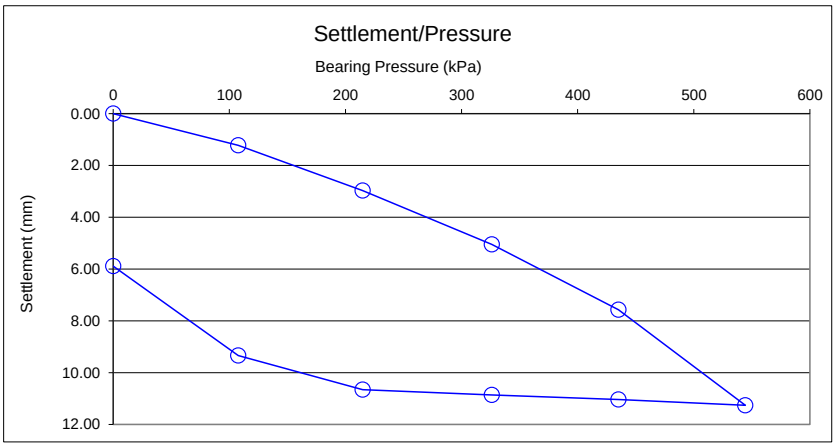


Plate Diameter	**600 mm**	Maximum Applied Pressure	**544.4 kPa**
Reaction Load	**Digger**	Maximum Settlement	**11.26 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/4C Clients Reference: **DN3046/4C**	**REPORT NO:** **DNR/65862C** Report Date: 26/04/2021

Material Description:	Crush	Date Tested:	23/04/2021
Test Location:	57	Supplier/Source:	Not Stated
Weather:	Clear		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	76.5	2.61
4.0	151.6	4.37
6.0	300.9	5.07
8.0	452.1	5.99
10.0	542.1	6.65
12.0	452.1	5.19
14.0	300.9	4.56
16.0	151.6	3.68
18.0	76.5	2.94
20.0	0.0	1.00

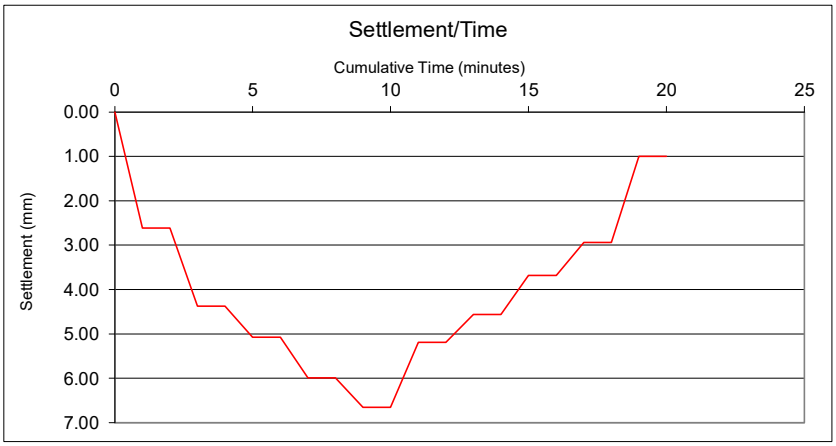

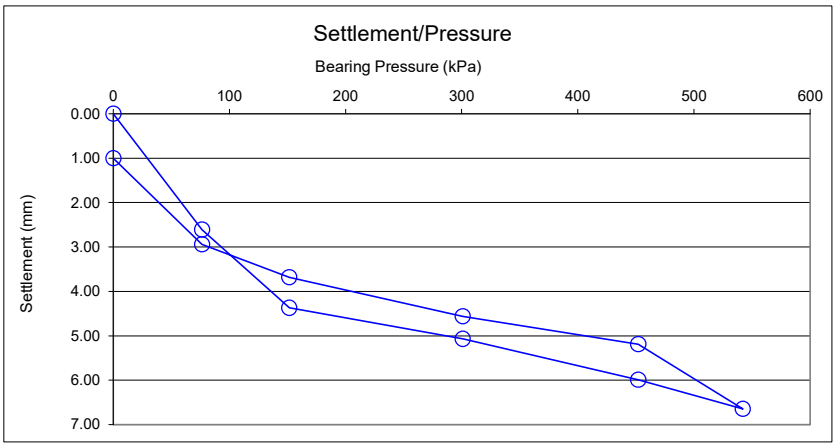


Plate Diameter	**600 mm**	Maximum Applied Pressure	**542.1 kPa**
Reaction Load	**30T**	Maximum Settlement	**6.65 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/4D Clients Reference: **DN3046/4D**	**REPORT NO:** **DNR/65862D** Report Date: 26/04/2021

Material Description:	Crush	Date Tested:	23/04/2021
Test Location:	58	Supplier/Source:	Not Stated
Weather:	Clear		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	76.5	1.46
4.0	151.6	2.57
6.0	300.9	4.09
8.0	452.1	5.00
10.0	542.1	5.46
12.0	452.1	4.83
14.0	300.9	4.08
16.0	151.6	3.53
18.0	76.5	2.45
20.0	0.0	1.46

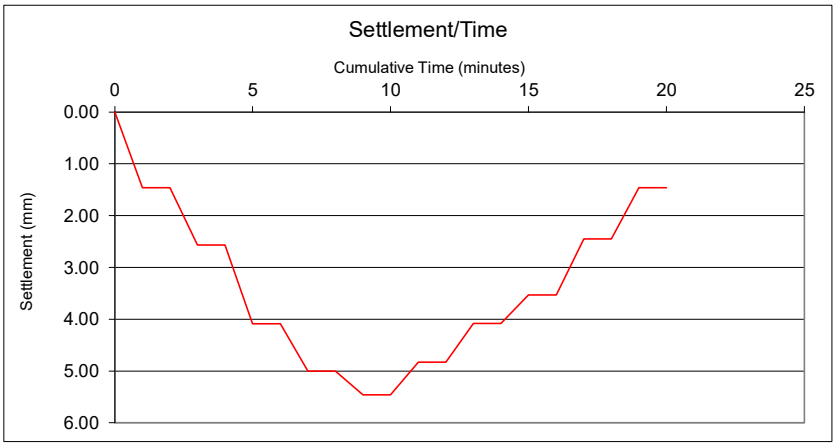

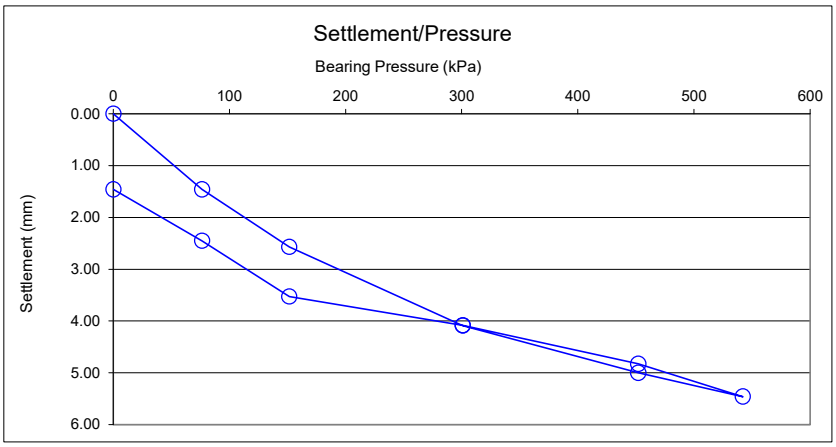


Plate Diameter	**600 mm**	Maximum Applied Pressure	**542.1 kPa**
Reaction Load	**30T**	Maximum Settlement	**5.46 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Issue No: 3 Revision: 2	Page ___ of ___	Issue Date: May-19	Issued By: C Cowling	SAMPLE NO DN3046/4

TEST WORKSHEET - TEST PROCEDURE No 15

Determination Settlement of Soil Material - Incremental Plate Loading Test
BS 1377: Part 9: 1990

(1)

Construction Testing Solutions Ltd

Material:	Crush	Client:	Proyectus Remediation Ltd		
Source:	N/S	Site:	Gibbon St, Manchester		
Supplier:	--	Location:	53		
Plate Diameter:	600 mm				
Jack Ref:	DON	Date:	23.4.21	Timer Ref:	3828
Weather Conditions:	Clear	Distance from edge of plate to wall of excavation:			— mm
Depth of Test:	Surface mm	Reaction Load:	30+		
Initial Seating Load Applied (Tonne / Bar / PSI /kN):	0.1	Note: Seating load must be the minimum detectable load given by the load measuring system			

Pressure Gauge Reading Ton/PSI/Bar	Calibrated Load kN	Mean Bearing Pressure kN/m² (kPa)	Time Minutes	Dial Gauge Readings (x0.01mm) 1	2	3	Settlement (x0.01mm) 1	2	3	Mean Settlement (x0.01mm)
CYCLE 1										
2.5	21.62	76.48	1				46	36	59	47
			2				46	36	59	47
			3							
			4							
			5							
5	42.85	151.54	1				104	112	174	130
			2				104	112	174	130
			3							
			4							
			5							
10	85.08	300.90	1				210	194	202	202
			2				210	194	202	202
			3							
			4							
			5							
15	127.83	452.12	1				272	260	229	253
			2				272	260	229	253
			3							
			4							
			5							
18	153.28	542.13	1				362	306	356	341
			2				362	306	356	341
			3							
			4							
			5							
15	127.83	452.12	1				310	282	319	303
			2				310	282	319	303
			3							
10	85.08	300.90	1				276	240	286	267
			2				276	240	286	267
			3							
5	42.85	151.54	1				250	207	236	231
			2				250	207	236	231
			3							
2.5	21.62	76.48	1				202	171	196	189
			2				202	171	196	189
			3							
0	0	0	1				146	107	112	121
			2				146	107	112	121
			3							

Tested By:	JMS	Checked By:	

Issue No: 9 Revision: 2	Page ___ of ___	Issue Date: May-19	Issued By: C Cowling	SAMPLE NO DN3046/4

TEST WORKSHEET - TEST PROCEDURE No 15
Determination Settlement of Soil Material - Incremental Plate Loading Test
BS 1377: Part 9: 1990

(2)

Construction Testing Solutions Ltd

Material:	Crush	Client:	Proventus Remediation Ltd		
Source:	N/S	Site:	Gibbon St, Manchester		
Supplier:	--	Location:	S4		
Plate Diameter:	600 mm				
Jack Ref:	DON	Date:	23.4.21	Timer Ref:	3828
Weather Conditions:	Clear	Distance from edge of plate to wall of excavation:			— mm
Depth of Test:	Surface mm	Reaction Load:	30+		
Initial Seating Load Applied (Tonne / Bar / PSI /kN):	0.1	Note: Seating load must be the minimum detectable load given by the load measuring system			

Pressure Gauge Reading Ton/PSI/Bar	Calibrated Load kN	Mean Bearing Pressure kN/m² (kPa)	Time Minutes	Dial Gauge Readings (x0.01mm) 1	2	3	Settlement (x0.01mm) 1	2	3	Mean Settlement (x0.01mm)
CYCLE 1										
2.5	21.62	76.48	1				196	199	274	223
			2				196	199	274	223
			3							
			4							
			5							
5	42.85	151.54	1				317	340	445	367
			2				317	340	445	367
			3							
			4							
			5							
10	85.08	300.90	1				606	411	517	511
			2				606	411	517	511
			3							
			4							
			5							
15	127.83	452.12	1				641	494	602	579
			2				641	494	602	579
			3							
			4							
			5							
18	153.28	542.13	1				665	614	694	657
			2				665	614	694	657
			3							
			4							
			5							
15	127.83	452.12	1				546	505	586	545
			2				546	505	586	545
			3							
10	85.08	300.90	1				490	422	506	472
			2				490	422	506	472
			3							
5	42.85	151.54	1				374	320	411	368
			2				374	320	411	368
			3							
2.5	21.62	76.48	1				250	188	326	254
			2				250	188	326	254
			3							
0	0	0	1				174	107	219	166
			2				174	107	219	166
			3							

Tested By:	JMS	Checked By:	

Issue No: 3 Revision: 2	Page ___ of ___	Issue Date: May-19	Issued By: C Cowling	SAMPLE NO DN3046/4

TEST WORKSHEET - TEST PROCEDURE No 15

Determination Settlement of Soil Material - Incremental Plate Loading Test
BS 1377: Part 9: 1990

(3)

Construction Testing Solutions Ltd

Material:	Crush	Client:	Proveltus Remediation Ltd		
Source:	N/S	Site:	Gibbon St, Manchester		
Supplier:	--	Location:	S7		
Plate Diameter:	600 mm				
Jack Ref:	DON	Date:	23.4.21	Timer Ref:	3828
Weather Conditions:	Clear	Distance from edge of plate to wall of excavation:		—	mm
Depth of Test:	Surface mm	Reaction Load:	30+		
Initial Seating Load Applied (Tonne / Bar / PSI /kN):	0.1	Note: Seating load must be the minimum detectable load given by the load measuring system			

Pressure Gauge Reading Ton/PSI/Bar	Calibrated Load kN	Mean Bearing Pressure kN/m² (kPa)	Time Minutes	Dial Gauge Readings (x0.01mm) 1	2	3	Settlement (x0.01mm) 1	2	3	Mean Settlement (x0.01mm)
CYCLE 1										
2.5	21.62	76.48	1				258	318	208	261
			2				258	318	208	261
			3							
			4							
			5							
5	42.85	151.54	1				422	499	396	437
			2				422	499	390	437
			3							
			4							
			5							
10	85.08	300.90	1				501	571	449	507
			2				501	571	449	507
			3							
			4							
			5							
15	127.83	452.12	1				617	670	511	599
			2				617	670	511	599
			3							
			4							
			5							
18	153.28	542.13	1				686	701	608	665
			2				686	701	608	665
			3							
			4							
			5							
15	127.83	452.12	1				474	612	470	518
			2				474	612	470	518
			3							
10	8508	300.90	1				396	586	386	456
			2				396	586	386	~~456~~ 456
			3							
5	42.85	151.54	1				301	501	302	368
			2				301	501	302	368
			3							
2.5	21.62	76.48	1				186	417	278	293
			2				186	417	278	293
			3							
0	0	0	1				99	112	90	100
			2				99	112	90	100
			3							

Tested By:	JMS	Checked By:	

Issue No: 3 Revision: 2	Page ___ of ___	Issue Date: May-19	Issued By: C Cowling	SAMPLE NO DN3046/4

TEST WORKSHEET - TEST PROCEDURE No 15
Determination Settlement of Soil Material - Incremental Plate Loading Test
BS 1377: Part 9: 1990

(4)

Construction Testing Solutions Ltd

Material:	Crush	Client:	Proveltus Remediation Ltd		
Source:	N/S	Site:	Gibbon St, Manchester		
Supplier:	--	Location:	S8		
Plate Diameter:	600 mm				
Jack Ref:	DON	Date:	23.4.21	Timer Ref:	3828
Weather Conditions:	Clear	Distance from edge of plate to wall of excavation:		—	mm
Depth of Test:	Surface mm	Reaction Load:	30+		
Initial Seating Load Applied (Tonne / Bar / PSI /kN):	0.1	Note: Seating load must be the minimum detectable load given by the load measuring system			

Pressure Gauge Reading Ton/PSI/Bar	Calibrated Load kN	Mean Bearing Pressure kN/m² (kPa)	Time Minutes	Dial Gauge Readings (x0.01mm) 1	2	3	Settlement (x0.01mm) 1	2	3	Mean Settlement (x0.01mm)
CYCLE 1										
2.5	21.62	76.48	1				140	98	199	145
			2				140	98	199	145
			3							
			4							
			5							
5	42.85	151.54	1				241	208	322	257
			2				241	208	322	257
			3							
			4							
			5							
10	85.08	300.90	1				399	401	428	409
			2				399	401	428	409
			3							
			4							
			5							
15	127.83	452.12	1				502	471	528	500
			2				502	471	528	500
			3							
			4							
			5							
18	153.28	542.13	1				528	501	608	579
			2				528	501	608	579
			3							
			4							
			5							
15	127.83	452.12	1				508	422	519	483
			2				508	422	519	483
			3							
10	85.08	300.90	1				422	362	439	407
			2				422	362	439	407
			3							
5	42.85	151.54	1				368	301	390	353
			2				368	301	390	353
			3							
2.5	21.62	76.48	1				227	196	312	245
			2				227	196	312	245
			3							
0	0	0	1				141	101	~~196~~	196/146
			2				141	101	196	146
			3							

Tested By:	JMS	Checked By:	

Issue No: 3 Revision: 2	Page ___ of ___	Issue Date: May-19	Issued By: C Cowling	SAMPLE NO DN3046/4

TEST WORKSHEET - TEST PROCEDURE No 15
Determination Settlement of Soil Material - Incremental Plate Loading Test
BS 1377: Part 9: 1990

(5)

Construction Testing Solutions Ltd

Material:	Crush	Client:	Proventus Remediation Ltd		
Source:	N/S	Site:	Gibbon St, Manchester		
Supplier:	--	Location:	SS		
Plate Diameter:	600 mm				
Jack Ref:	DON	Date:	23.4.21	Timer Ref:	3828
Weather Conditions:	Clear	Distance from edge of plate to wall of excavation:			— mm
Depth of Test:	Surface mm	Reaction Load:	30+		
Initial Seating Load Applied (Tonne / Bar / PSI /kN):	0.1	Note: Seating load must be the minimum detectable load given by the load measuring system			

Pressure Gauge Reading Ton/PSI/Bar	Calibrated Load kN	Mean Bearing Pressure kN/m² (kPa)	Time Minutes	Dial Gauge Readings (x0.01mm) 1	2	3	Settlement (x0.01mm) 1	2	3	Mean Settlement (x0.01mm)
CYCLE 1										
2.5	21.62	76.48	1				176	86	62	108
			2				176	86	62	108
			3							
			4							
			5							
5	42.85	151.54	1				281	206	174	220
			2				281	206	174	220
			3							
			4							
			5							
10	85.08	300.90	1				362	301	280	314
			2				362	301	280	314
			3							
			4							
			5							
15	127.83	452.12	1				411	396	326	377
			2				411	396	326	377
			3							
			4							
			5							
18	153.28	542.13	1				478	445	410	444
			2				478	445	410	444
			3							
			4							
			5							
15	127.83	452.12	1				411	406	368	~~395~~ 395
			2				411	406	368	395
			3							
10	85.08	300.90	1				399	376	296	357
			2				399	376	296	357
			3							
5	42.85	151.54	1				320	301	206	275
			2				320	301	206	275
			3							
2.5	21.62	76.48	1				296	246	116	252
			2				296	246	116	252
			3							
0	0	0	1				114	81	56	83
			2				114	81	56	83
			3							

Tested By:	JMS	Checked By:	

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Gibbon Street, Manchester

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Determination of Vertical Deformation - Plate Loading Test	Contract Test Reference:	DN3046/25A	**REPORT NO:**	**DNR/77974A**
BS1377: Part 9: 1990	Clients Reference:	**DN3046/25A**	Report Date:	23/06/2021

Material Description:	Type 1	Date Tested:	21/07/2021
Test Location:	PT42	Supplier/Source:	Not Stated
Weather:	Sunny		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
3.0	90.2	0.34
6.0	180.2	0.40
9.0	270.4	0.62
12.0	359.7	0.99
15.0	450.7	1.33
18.0	541.9	1.71
23.0	0.0	0.53

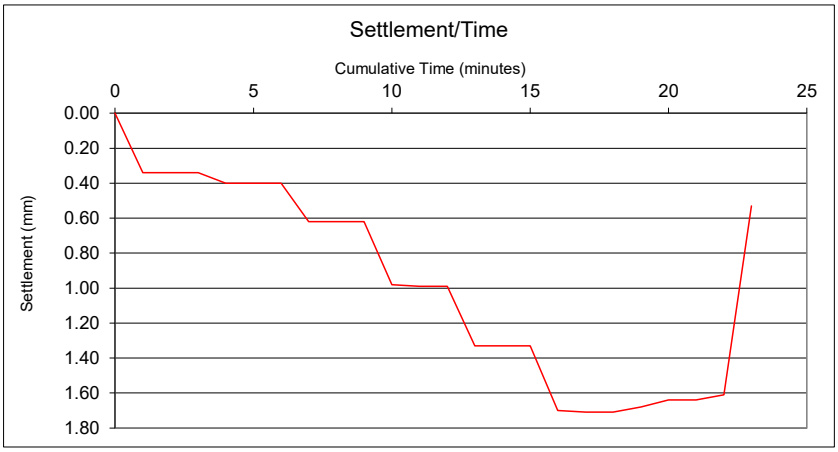

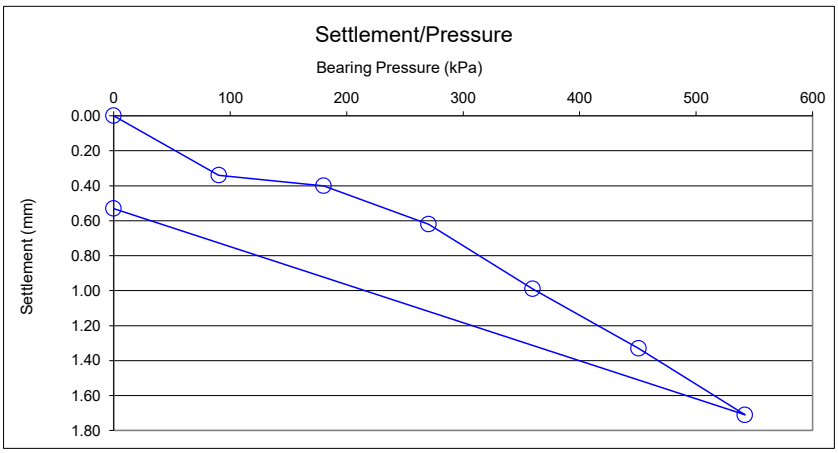


Plate Diameter	**600 mm**	Maximum Applied Pressure	**541.9 kPa**
Reaction Load	**Digger**	Maximum Settlement	**1.71 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/30A Clients Reference: DN3046/30A	**REPORT NO:** DNR/79784A Report Date: 12/08/2021

Material Description:	6F2	Date Tested:	11/08/2021
Test Location:	Crain 2	Supplier/Source:	Manchester/Tarmac
Weather:	Dry		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	105.2	0.88
3.0	210.4	1.26
4.0	209.9	1.26
6.0	337.6	1.92
8.0	420.9	2.24
10.0	541.9	2.76
12.0	420.9	2.71
14.0	337.6	2.68
16.0	210.4	2.52
18.0	105.2	1.59
20.0	0.0	1.06

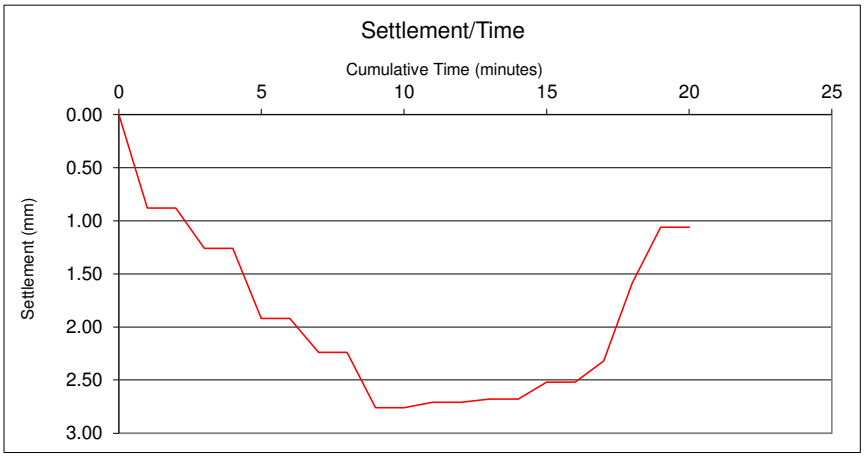

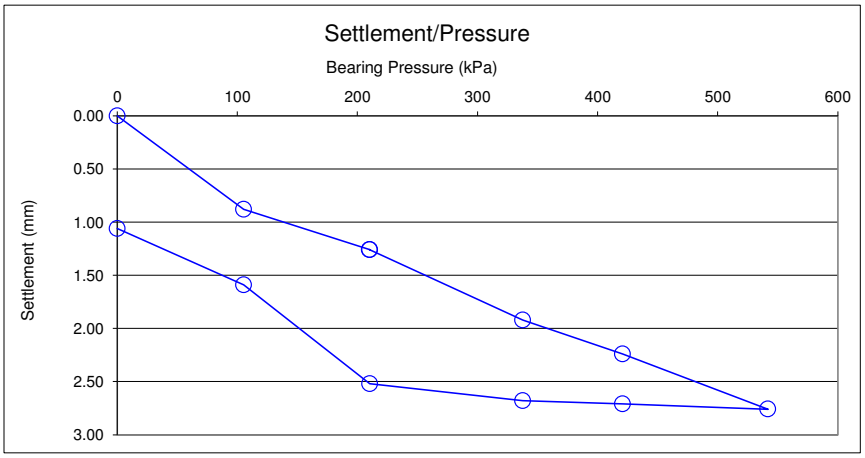


Plate Diameter	**600 mm**	Maximum Applied Pressure	**541.9 kPa**
Reaction Load	**90T**	Maximum Settlement	**2.76 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/30 Clients Reference: DN3046/30E	**REPORT NO:** DNR/79784B Report Date: 12/08/2021

Material Description:	6F2	Date Tested:	11/08/2021
Test Location:	Crain 3	Supplier/Source:	Manchester/Tarmac
Weather:	Dry		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	105.2	0.77
3.0	210.4	1.16
4.0	209.9	1.16
6.0	337.6	1.71
8.0	420.9	2.27
10.0	541.9	2.93
12.0	420.9	2.93
14.0	337.6	2.91
16.0	210.4	2.83
18.0	105.2	2.50
20.0	0.0	1.11

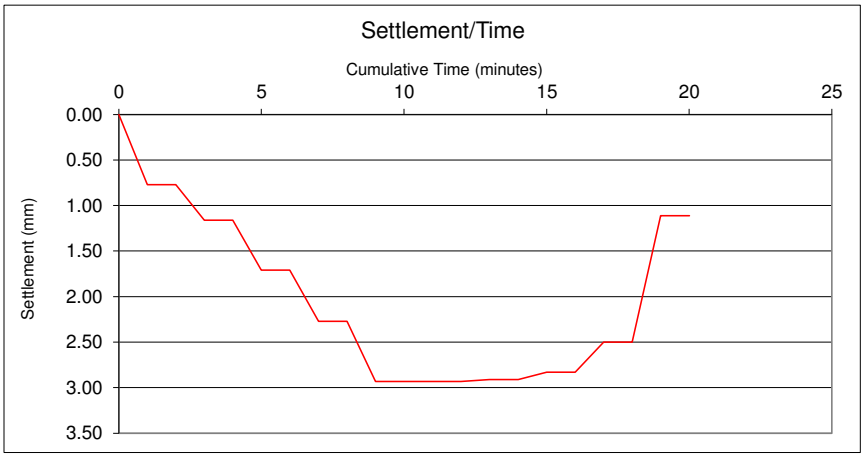

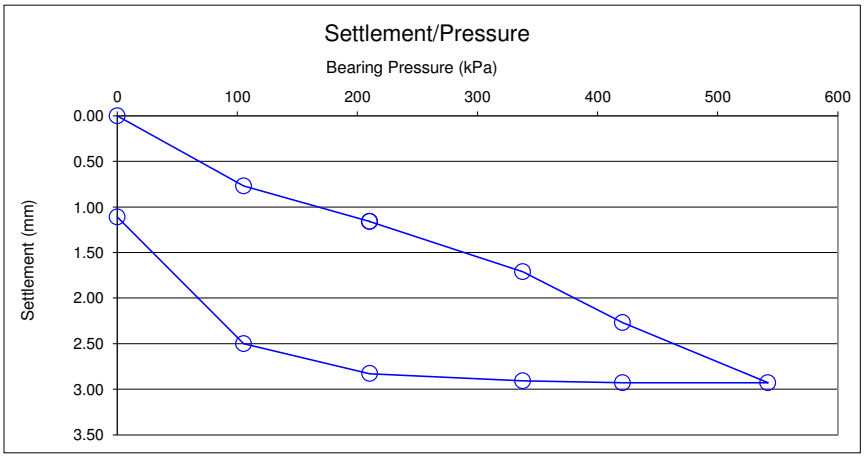


Plate Diameter	**600 mm**	Maximum Applied Pressure	**541.9 kPa**
Reaction Load	**90T**	Maximum Settlement	**2.93 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Boothams Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/31 Clients Reference: **DN3046/31**	**REPORT NO: DNR/79785** Report Date: 12/08/2021

Material Description:	6F5	Date Tested:	11/08/2021
Test Location:	Crain 1	Supplier/Source:	Manchester/Tarmac
Weather:	Dry		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	105.2	0.45
3.0	210.4	0.84
4.0	209.9	0.84
6.0	337.6	1.12
8.0	420.9	1.46
10.0	541.9	2.18
12.0	420.9	2.21
14.0	337.6	2.21
16.0	210.4	2.13
18.0	105.2	2.03
20.0	0.0	1.07

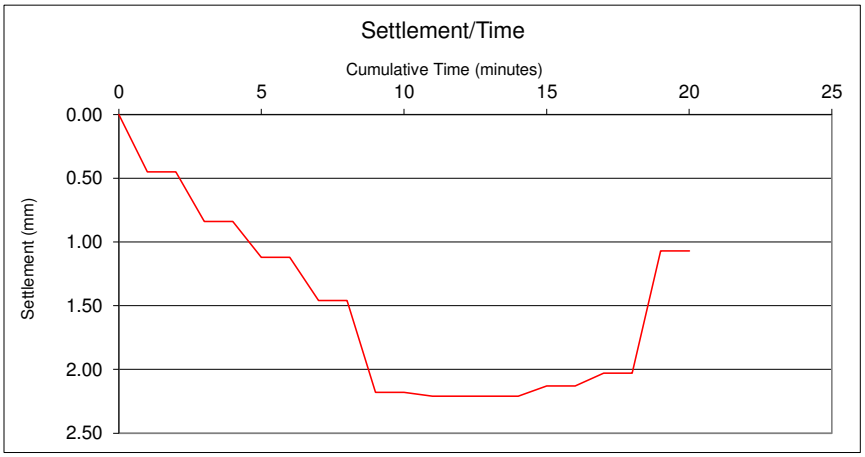

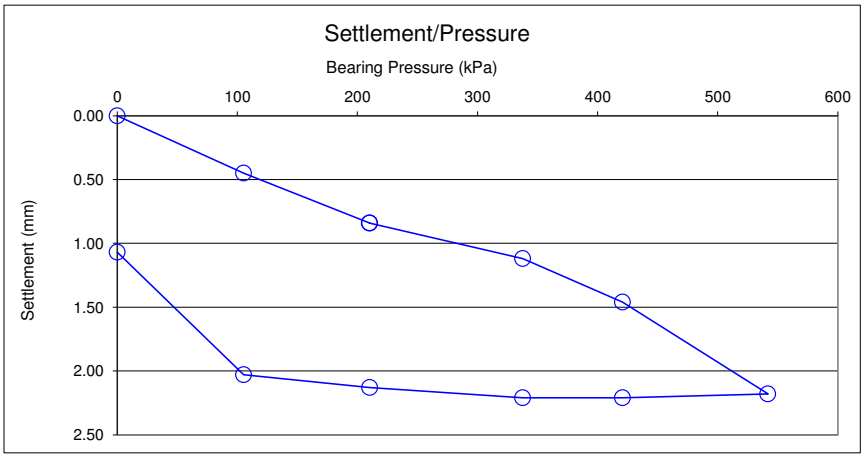


Plate Diameter	**600 mm**	Maximum Applied Pressure	**541.9 kPa**
Reaction Load	**90T**	Maximum Settlement	**2.21 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Gibbon Street, Manchester

Construction Testing Solutions

UKAS TESTING 4161

Bootham Lane Industrial Estate
Dunscroft
Doncaster
DN7 4JU


Tel: (01302) 352652
Email: enquiries@constructiontesting.co.uk
Web: www.constructiontesting.co.uk

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/37A Clients Reference: **DN3046/37A**	**REPORT NO: DNR/90669A** Report Date: 15/11/2021

TEST REPORT

Material Description:	Type 1	Date Tested:	12/11/2021
Test Location:	PTL S01	Supplier/Source:	Manchester/ Maher
Weather:	Dry		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	360.8	1.10
4.0	720.8	1.92
6.0	1081.7	2.68
8.0	1438.9	3.67
10.0	1802.8	5.15
12.0	1438.9	5.10
14.0	1081.7	5.10
16.0	720.8	5.05
18.0	360.8	3.16
20.0	0.0	1.73

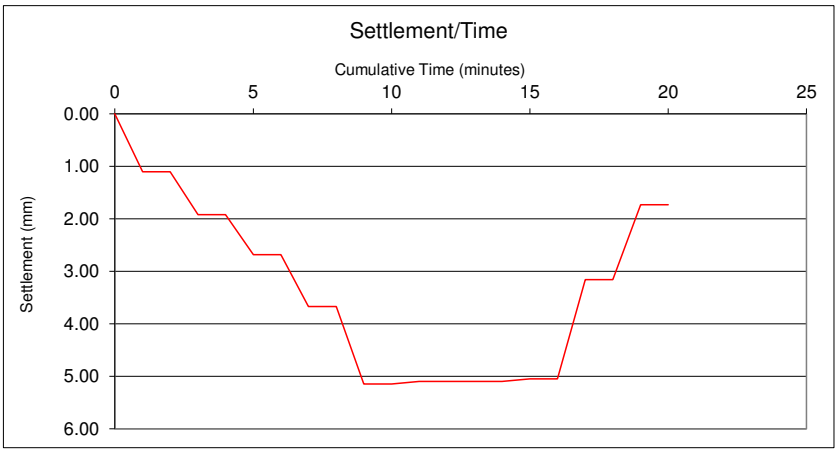

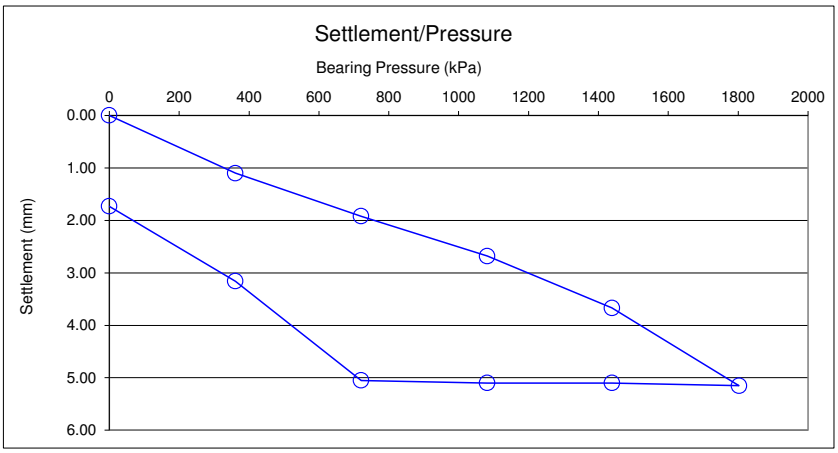


Plate Diameter	**300 mm**	Maximum Applied Pressure	**1802.8 kPa**
Reaction Load	**20T**	Maximum Settlement	**5.15 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Results relate only to the sample(s) as tested.
This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.
The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.
Testing carried out at client's site location.

Authorised Signatory

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.3 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Gibbon Street, Manchester

Construction Testing Solutions

UKAS TESTING 4161

Bootham Lane Industrial Estate
Dunscroft
Doncaster
DN7 4JU


Tel: (01302) 352652
Email: enquiries@constructiontesting.co.uk
Web: www.constructiontesting.co.uk

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/37E Clients Reference: **DN3046/37E**	**REPORT NO: DNR/90669B** Report Date: 15/11/2021

TEST REPORT

Material Description:	Type 1	Date Tested:	12/11/2021
Test Location:	PLT S02	Supplier/Source:	Manchester/ Maher
Weather:	Dry		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	360.8	0.80
4.0	720.8	1.37
6.0	1081.7	1.89
8.0	1438.9	2.51
10.0	1802.8	3.25
12.0	1438.9	3.25
14.0	1081.7	3.21
16.0	720.8	3.14
18.0	360.8	1.93
20.0	0.0	1.10

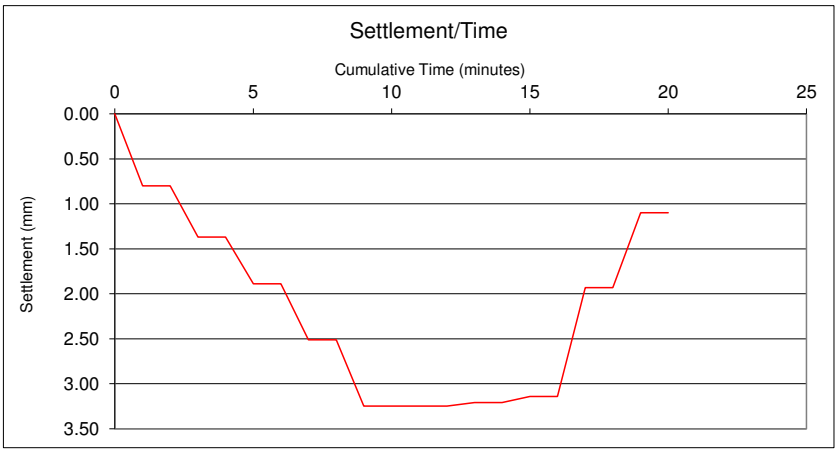

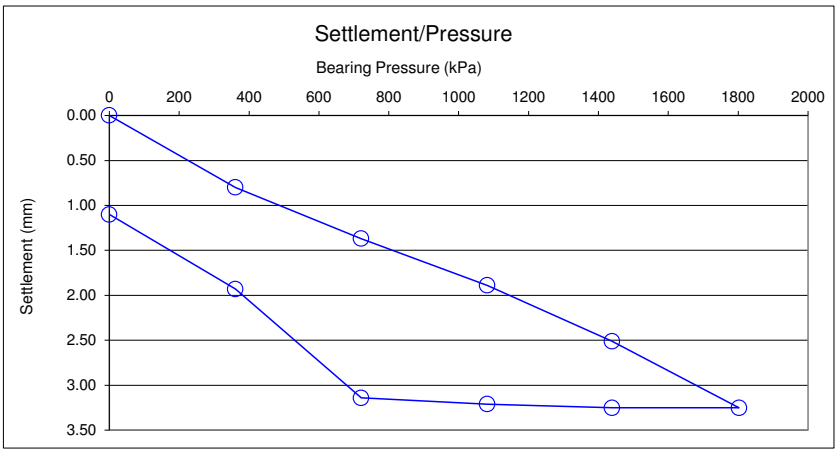


Plate Diameter	**300 mm**	Maximum Applied Pressure	**1802.8 kPa**
Reaction Load	**20T**	Maximum Settlement	**3.25 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Results relate only to the sample(s) as tested.
This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.
The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.
Testing carried out at client's site location.

Authorised Signatory

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.3 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Gibbon Street, Manchester

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft
Doncaster
DN7 4JU


Tel: (01302) 352652
Email: enquiries@constructiontesting.co.uk
Web: www.constructiontesting.co.uk

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/37C Clients Reference: DN3046/37C	**REPORT NO:**	**DNR/90669C** Report Date: 15/11/2021

TEST REPORT

Material Description:	Type 1	Date Tested:	12/11/2021
Test Location:	PLT S03	Supplier/Source:	Manchester/ Maher
Weather:	Dry		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	360.8	2.61
4.0	720.8	4.44
6.0	1081.7	7.37
8.0	1438.9	11.82
10.0	1802.8	15.84
12.0	1438.9	15.84
14.0	1081.7	15.76
16.0	720.8	15.63
18.0	360.8	7.65
20.0	0.0	4.29

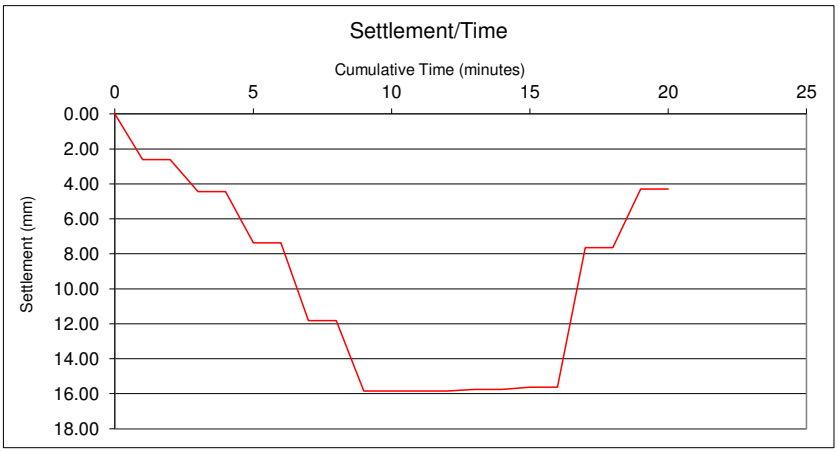

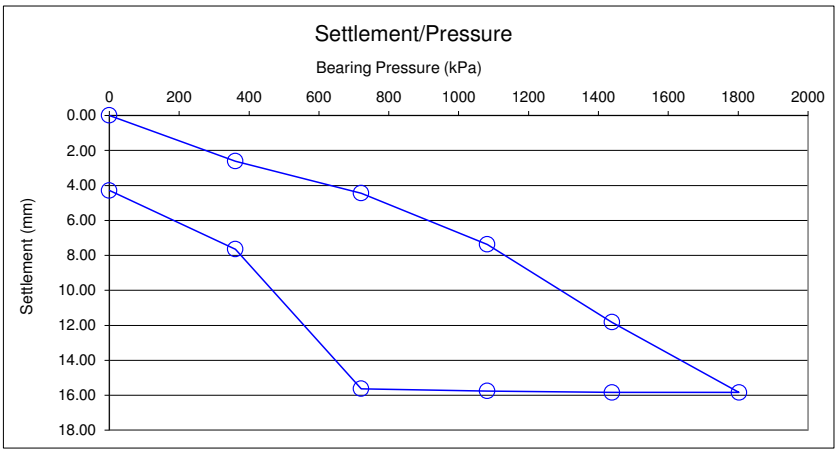


Plate Diameter	**300 mm**	Maximum Applied Pressure	**1802.8 kPa**
Reaction Load	**20T**	Maximum Settlement	**15.84 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Results relate only to the sample(s) as tested.
This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.
The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.
Testing carried out at client's site location.

Authorised Signatory

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.3 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Gibbon Street, Manchester

Construction Testing Solutions

Bootham Lane Industrial Estate
Dunscroft
Doncaster
DN7 4JU


Tel: (01302) 352652
Email: enquiries@constructiontesting.co.uk
Web: www.constructiontesting.co.uk

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference:	DN3046/37D	**REPORT NO:** **DNR/90669D**
	Clients Reference:	**DN3046/37D**	Report Date: 15/11/2021

TEST REPORT

Material Description:	Type 1	Date Tested:	12/11/2021
Test Location:	PLT S04	Supplier/Source:	Manchester/ Maher
Weather:	Dry		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	360.8	2.20
4.0	720.8	4.17
6.0	1081.7	7.38
8.0	1438.9	9.43
10.0	1802.8	11.68
12.0	1438.9	11.66
14.0	1081.7	11.58
16.0	720.8	7.49
18.0	360.8	5.33
20.0	0.0	3.46

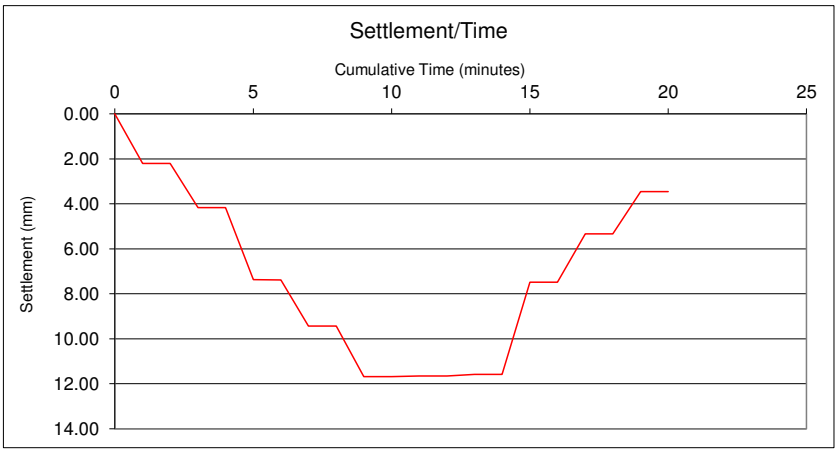

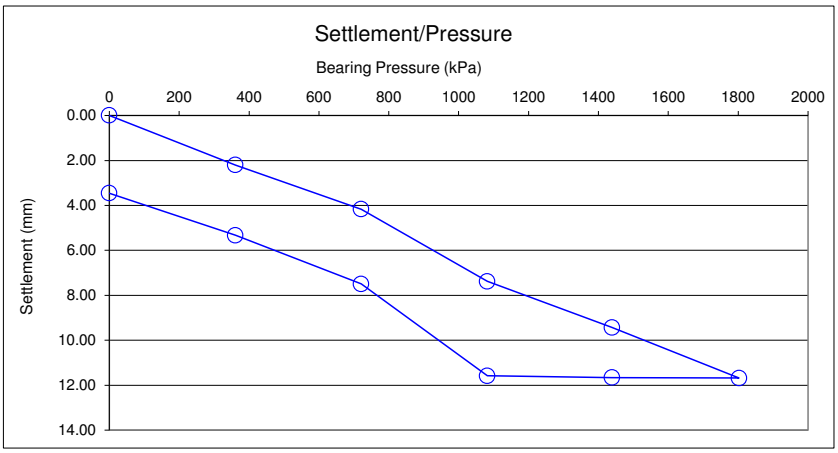


Plate Diameter	**300 mm**	Maximum Applied Pressure	**1802.8 kPa**
Reaction Load	**20T**	Maximum Settlement	**11.68 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Results relate only to the sample(s) as tested.
This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.
The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.
Testing carried out at client's site location.

Authorised Signatory

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.3 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Gibbon Street, Manchester

Construction Testing Solutions

Bootham Lane Industrial Estate
Dunscroft
Doncaster
DN7 4JU


Tel: (01302) 352652
Email: enquiries@constructiontesting.co.uk
Web: www.constructiontesting.co.uk

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference:	DN3046/38A	**REPORT NO:** **DNR/90670A**
	Clients Reference:	**DN3046/38A**	Report Date: 15/11/2021

TEST REPORT

Material Description:	Type 1	Date Tested:	12/11/2021
Test Location:	PLT 40	Supplier/Source:	Manchester/ Maher
Weather:	Dry		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	360.8	2.74
4.0	720.8	4.28
6.0	1081.7	6.14
8.0	1438.9	8.94
10.0	1802.8	10.86
12.0	1438.9	10.86
14.0	1081.7	10.78
16.0	720.8	10.16
18.0	360.8	7.23
20.0	0.0	3.48

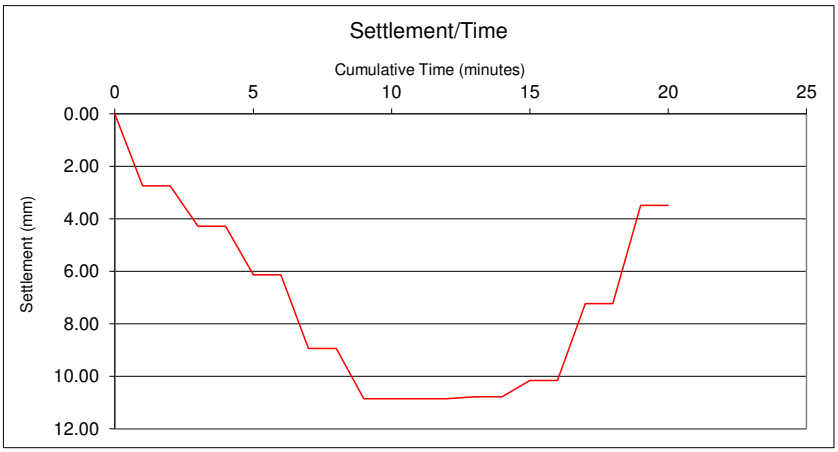

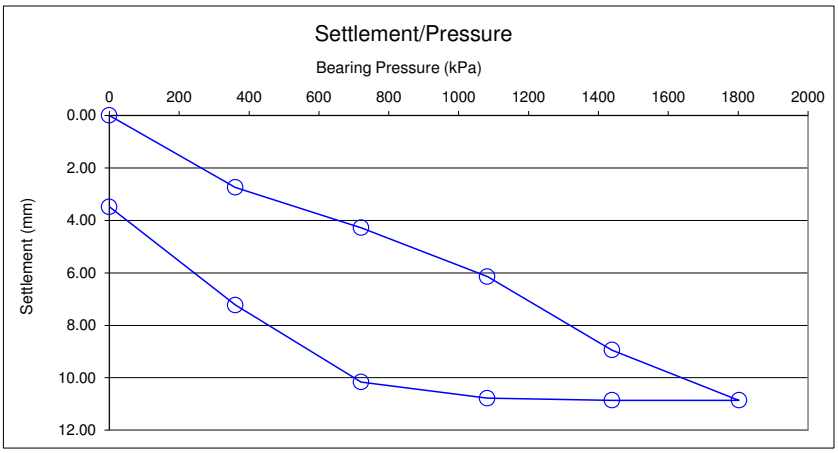


Plate Diameter	**300 mm**	Maximum Applied Pressure	**1802.8 kPa**
Reaction Load	**20T**	Maximum Settlement	**10.86 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Results relate only to the sample(s) as tested.
This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.
The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.
Testing carried out at client's site location.

Authorised Signatory

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.3 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Gibbon Street, Manchester

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft
Doncaster
DN7 4JU


Tel: (01302) 352652
Email: enquiries@constructiontesting.co.uk
Web: www.constructiontesting.co.uk

Determination of Vertical Deformation - Plate Loading Test	Contract Test Reference:	DN3046/38E	**REPORT NO:** **DNR/90670B**
BS1377: Part 9: 1990	Clients Reference:	**DN3046/38E**	Report Date: 15/11/2021

TEST REPORT

Material Description:	Type 1	Date Tested:	12/11/2021
Test Location:	PLT 47A	Supplier/Source:	Manchester/ Maher
Weather:	Dry		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	360.8	2.35
4.0	720.8	4.15
6.0	1081.7	6.86
8.0	1438.9	10.96
10.0	1802.8	13.47
12.0	1438.9	13.44
14.0	1081.7	13.44
16.0	720.8	11.51
18.0	360.8	8.29
20.0	0.0	4.92

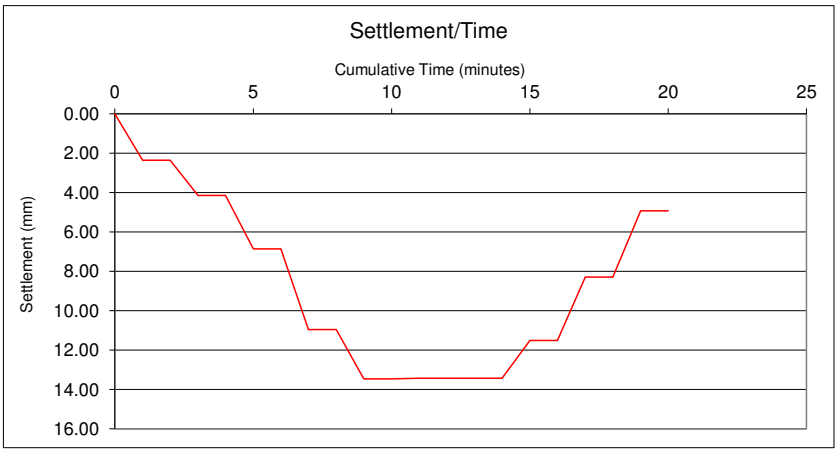

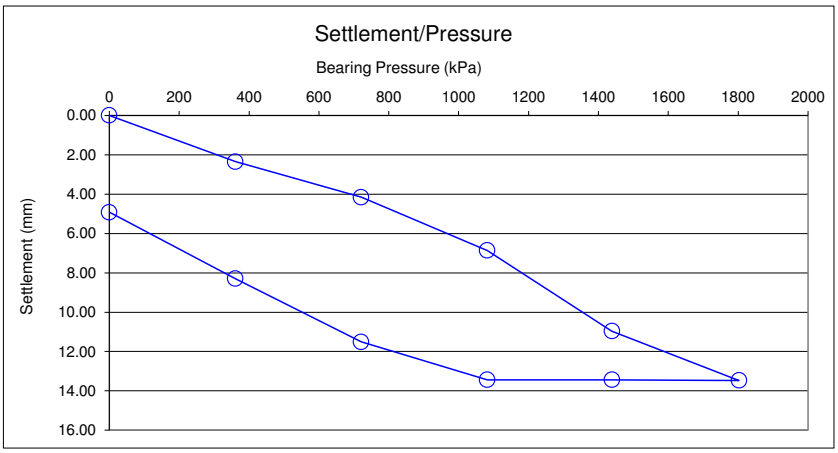


Plate Diameter	**300 mm**	Maximum Applied Pressure	**1802.8 kPa**
Reaction Load	**20T**	Maximum Settlement	**13.47 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Results relate only to the sample(s) as tested.
This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.
The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.
Testing carried out at client's site location.

Authorised Signatory

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.3 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4AJ
T | (01302) 353652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/10E Clients Reference: DN3046/10E	**REPORT NO:** DNR/68668 B Report Date: 08/06/2021

Material Description:	MOT Type 1	Date Tested:	07/06/2021
Test Location:	PT 10	Supplier/Source:	Meyer/ Fletcher Bank Quarry
Weather:	Dry		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	105.2	2.60
4.0	210.4	5.54
6.0	300.9	7.57
8.0	420.9	9.45
10.0	541.9	11.65
12.0	420.9	11.71
14.0	300.9	11.65
16.0	210.4	11.47
18.0	105.2	10.90
20.0	0.0	7.66

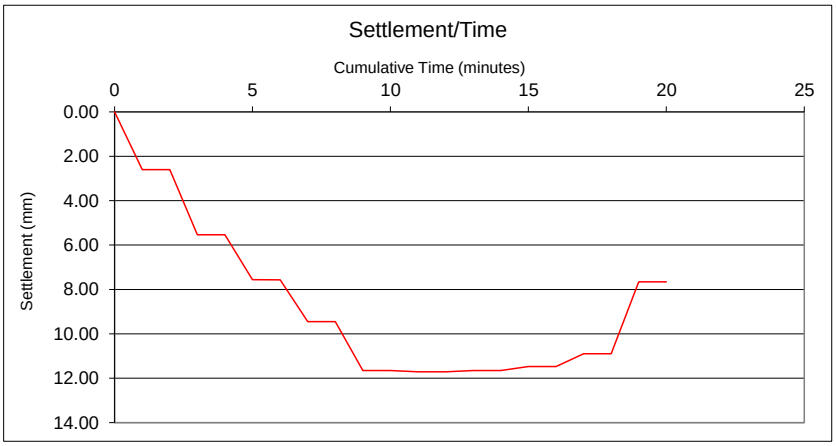

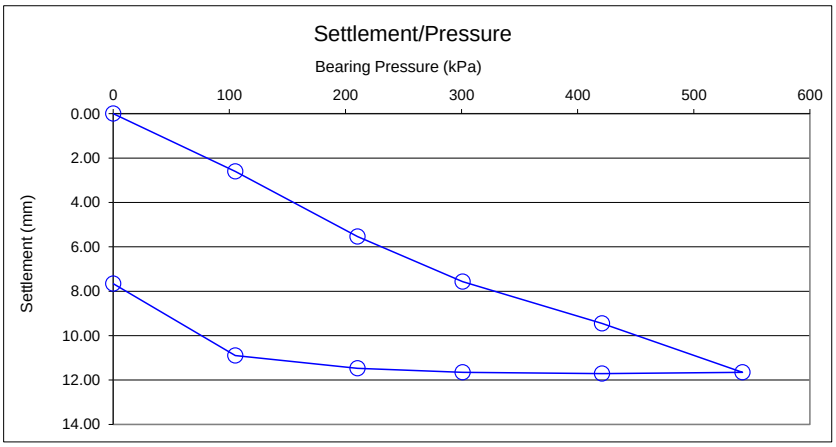


Plate Diameter	**600 mm**	Maximum Applied Pressure	**541.9 kPa**
Reaction Load	**36T**	Maximum Settlement	**11.71 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/6A Clients Reference: **DN3046/6A**	**REPORT NO:** **DNR/66879 A** Report Date: 12/05/2021

Material Description:	6F5-Wet	Date Tested:	10/05/2021
Test Location:	TEST 21	Supplier/Source:	Not Stated
Weather:	Clear		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	76.5	4.04
4.0	151.6	6.08
6.0	300.9	9.90
8.0	423.8	11.02
10.0	542.1	11.97
12.0	423.8	11.64
14.0	300.9	11.01
16.0	151.6	10.41
18.0	76.5	9.78
20.0	0.0	6.24

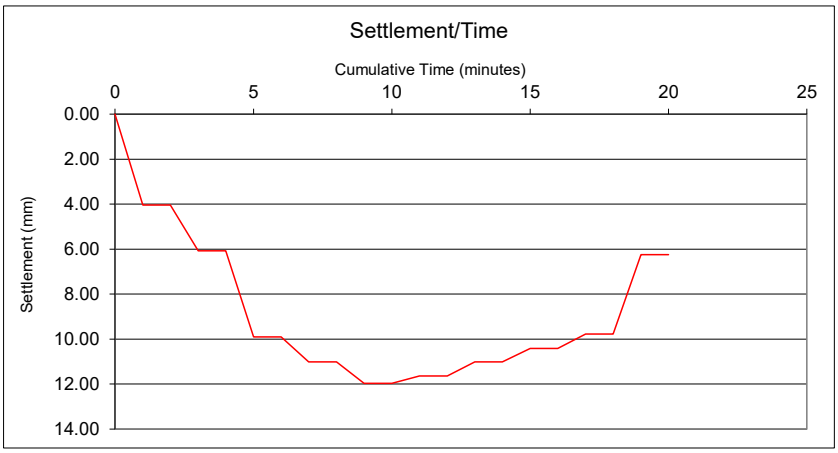

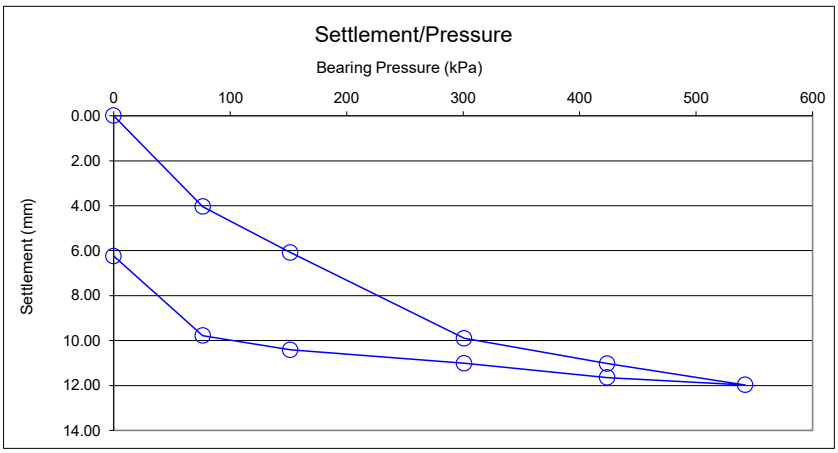


Plate Diameter	**600 mm**	Maximum Applied Pressure	**542.1 kPa**
Reaction Load	**19T**	Maximum Settlement	**11.97 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Gibbon Street, Manchester

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/9E Clients Reference: 9E	**REPORT NO:** DNR/68505E Report Date: 04/06/2021

Material Description:	MOT Type 1	Date Tested:	03/06/2021
Test Location:	PT 22	Supplier/Source:	Meyer/ Fletcher Bank Quarry
Weather:	Overcast		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
5.0	100.7	2.61
10.0	205.9	3.91
15.0	311.2	4.19
20.0	417.4	5.09
25.0	521.4	6.94
30.0	417.4	6.86
35.0	311.2	6.81
40.0	205.9	6.74
45.0	100.7	5.71
50.0	0.0	2.37

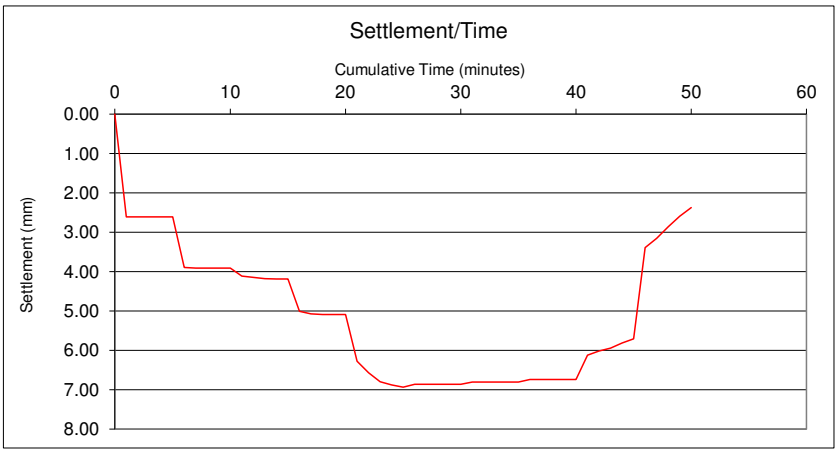

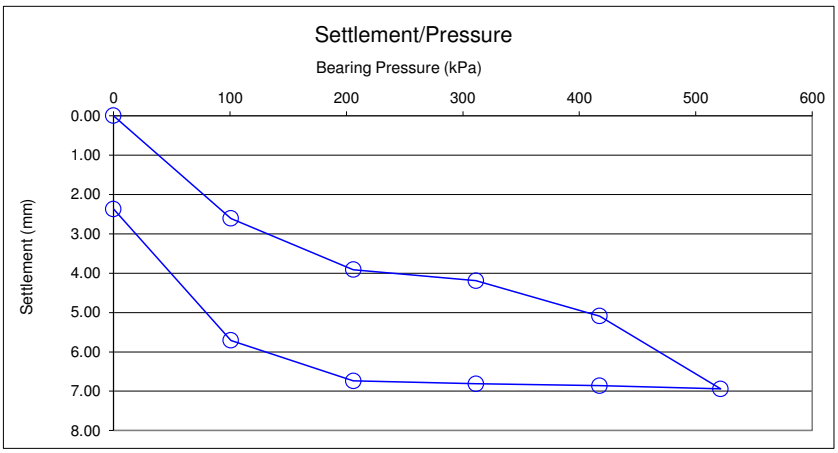


Plate Diameter	**600 mm**	Maximum Applied Pressure	**521.4 kPa**
Reaction Load	**36.5T**	Maximum Settlement	**6.94 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Gibbon Street, Manchester

Construction Testing Solutions
Bootham Lane Industrial Estate
Danscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/9D Clients Reference: 9D	**REPORT NO:** DNR/68505D Report Date: 04/06/2021

Material Description:	MOT Type 1	Date Tested:	03/06/2021
Test Location:	PT 22A	Supplier/Source:	Meyer/ Fletcher Bank Quarry
Weather:	Overcast		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
5.0	100.7	1.84
10.0	205.9	5.41
15.0	311.2	9.71
20.0	417.4	12.69
25.0	521.4	15.08
30.0	417.4	15.06
35.0	311.2	15.00
40.0	205.9	14.70
45.0	100.7	13.67
50.0	0.0	8.58

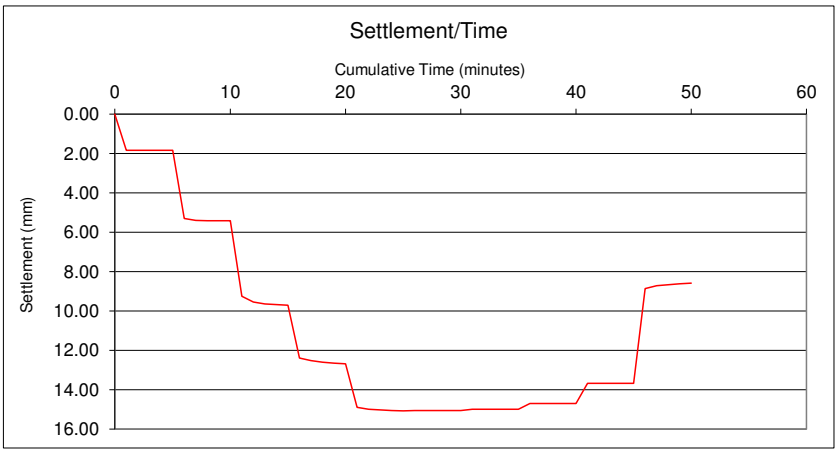

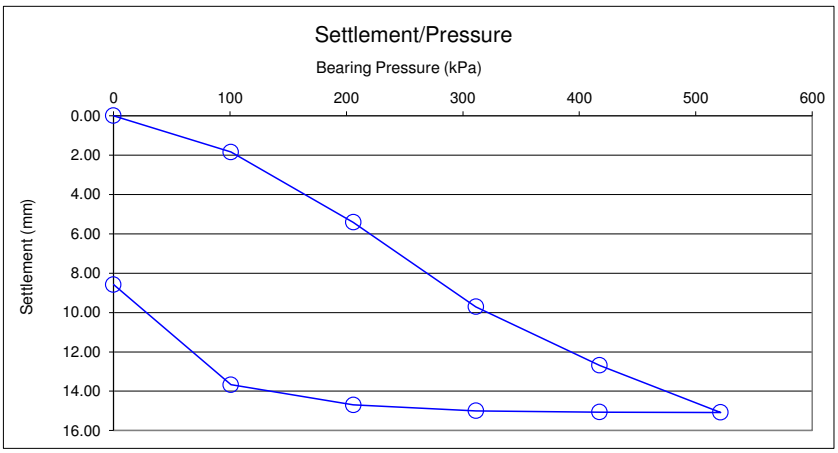


Plate Diameter	**600 mm**	Maximum Applied Pressure	**521.4 kPa**
Reaction Load	**36.5T**	Maximum Settlement	**15.08 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4AJ
T | (01302) 353652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/10[	**REPORT NO:** DNR/68668 D
	Clients Reference: DN3046/10[	Report Date: 08/06/2021

Material Description:	MOT Type 1	Date Tested:	07/06/2021
Test Location:	PT 23	Supplier/Source:	Meyer/ Fletcher Bank Quarry
Weather:	Dry		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	105.2	1.02
4.0	210.4	2.70
6.0	300.9	4.40
8.0	420.9	6.06
10.0	541.9	7.65
12.0	420.9	7.67
14.0	300.9	7.61
16.0	210.4	7.46
18.0	105.2	7.03
20.0	0.0	4.97

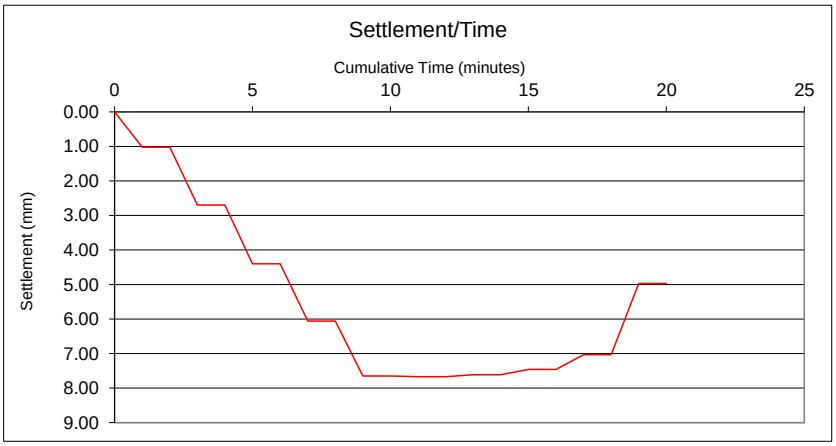

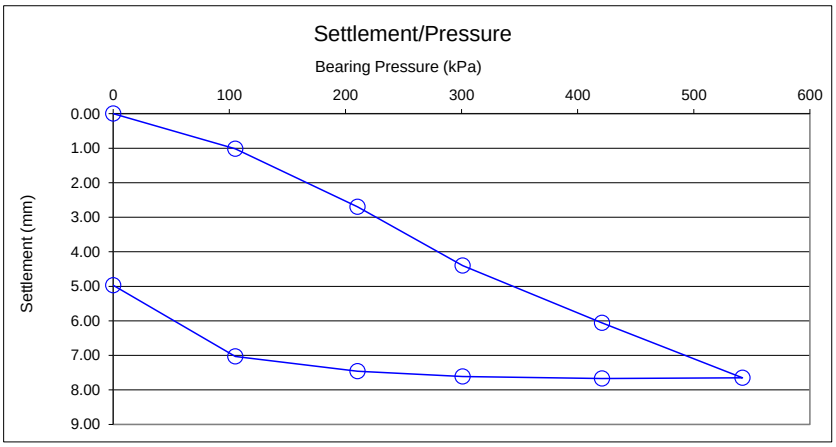


Plate Diameter	**600 mm**	Maximum Applied Pressure	**541.9 kPa**
Reaction Load	**36T**	Maximum Settlement	**7.67 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4AJ
T | (01302) 353652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/10A Clients Reference: DN3046/10A	**REPORT NO:** DNR/68668 A Report Date: 08/06/2021

Material Description:	MOT Type 1	Date Tested:	07/06/2021
Test Location:	24 pt	Supplier/Source:	Meyer/ Fletcher Bank Quarry
Weather:	Dry		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	105.2	6.11
4.0	210.4	9.20
6.0	300.9	10.99
8.0	420.9	12.80
10.0	541.9	14.46
12.0	420.9	14.34
14.0	300.9	14.25
16.0	210.4	13.71
18.0	105.2	13.18
20.0	0.0	10.62

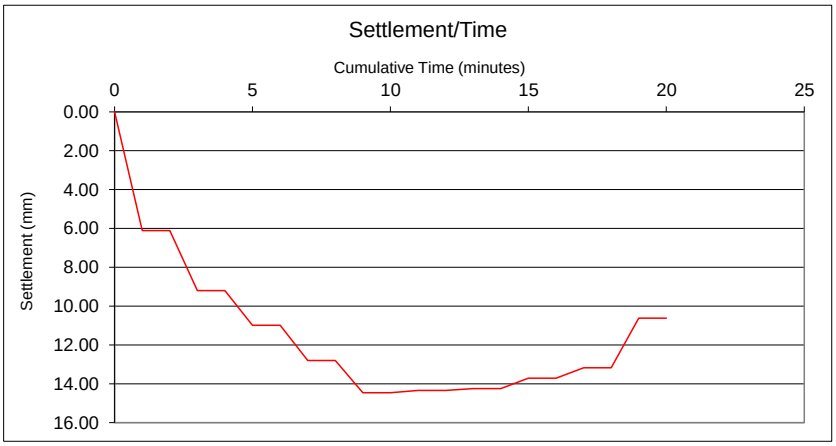

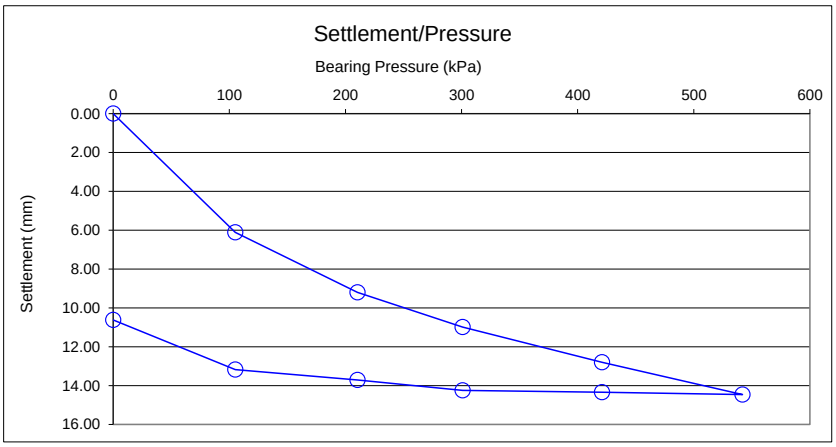


Plate Diameter	**600 mm**	Maximum Applied Pressure	**541.9 kPa**
Reaction Load	**36T**	Maximum Settlement	**14.46 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Gibbon Street, Manchester

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4AJ
T | (01302) 353652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/10C Clients Reference: DN3046/10C	**REPORT NO:** DNR/68668 C Report Date: 08/06/2021

Material Description:	MOT Type 1	Date Tested:	07/06/2021
Test Location:	PT 30	Supplier/Source:	Meyer/ Fletcher Bank Quarry
Weather:	Dry		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	105.2	1.25
4.0	210.4	4.01
6.0	300.9	8.02
8.0	420.9	13.02
10.0	541.9	17.39
12.0	420.9	17.38
14.0	300.9	17.39
16.0	210.4	17.30
18.0	105.2	16.54
20.0	0.0	12.09

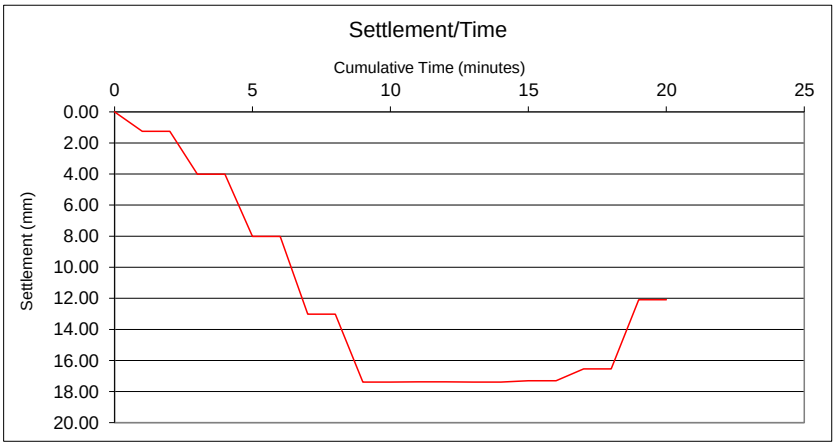

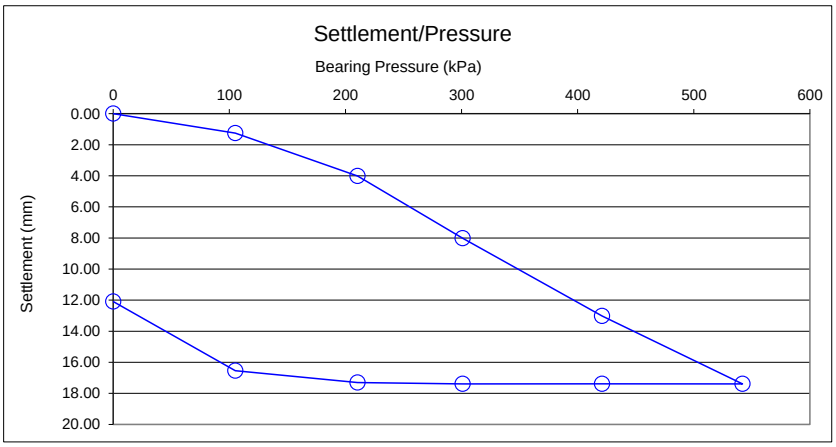


Plate Diameter	**600 mm**	Maximum Applied Pressure	**541.9 kPa**
Reaction Load	**36T**	Maximum Settlement	**17.39 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Gibbon Street, Manchester

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/7B Clients Reference: **DN3046/7B**	**REPORT NO:** **DNR/67607A** Report Date: 21/05/2021

Material Description:	6F5	Date Tested:	18/05/2021
Test Location:	Test 1 - PT31	Supplier/Source:	Not Stated
Weather:	Clear		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	76.5	3.23
4.0	151.6	5.83
6.0	300.9	8.74
8.0	452.1	10.36
10.0	542.1	12.08
12.0	452.1	10.30
14.0	300.9	10.30
16.0	151.6	10.26
18.0	76.5	7.15
20.0	0.0	4.39

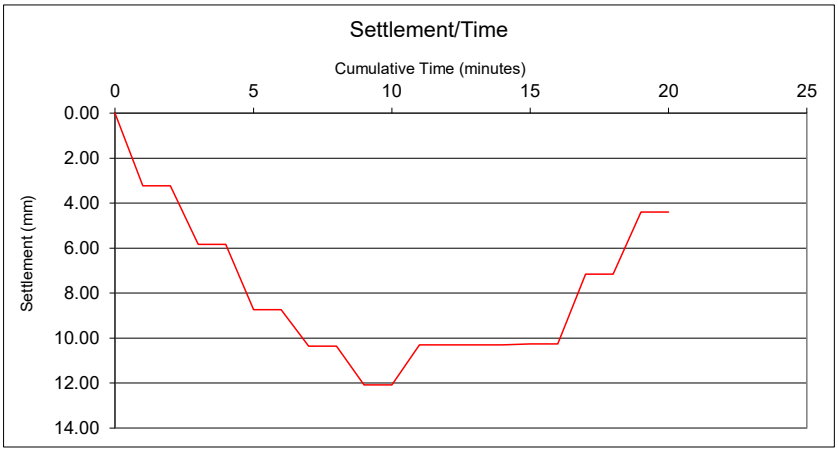

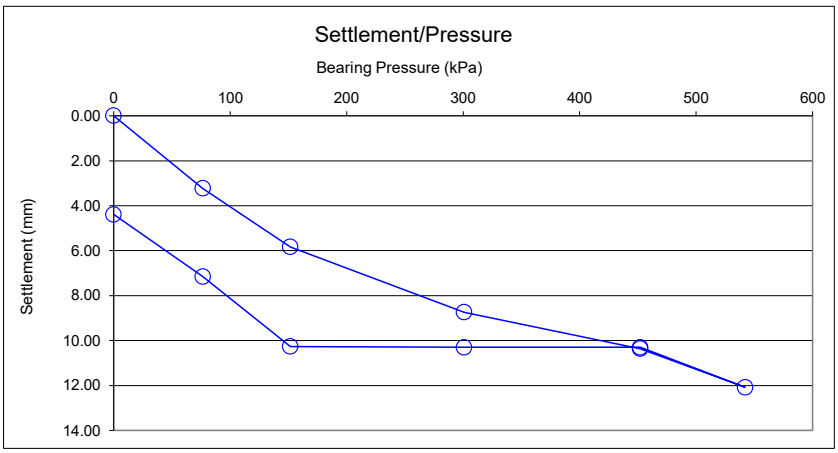


Plate Diameter	**600 mm**	Maximum Applied Pressure	**542.1 kPa**
Reaction Load	**21 Tonne**	Maximum Settlement	**12.08 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Gibbon Street, Manchester

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/9A Clients Reference: 9A	**REPORT NO:** DNR/68505A Report Date: 04/06/2021

Material Description:	MOT Type 1	Date Tested:	03/06/2021
Test Location:	PT 32	Supplier/Source:	Meyer/ Fletcher Bank Quarry
Weather:	Overcast		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
5.0	100.7	3.36
10.0	205.9	4.91
15.0	311.2	5.81
20.0	417.4	6.63
25.0	521.4	7.53
30.0	417.4	7.51
35.0	311.2	7.44
40.0	205.9	7.07
45.0	100.7	6.46
50.0	0.0	2.39

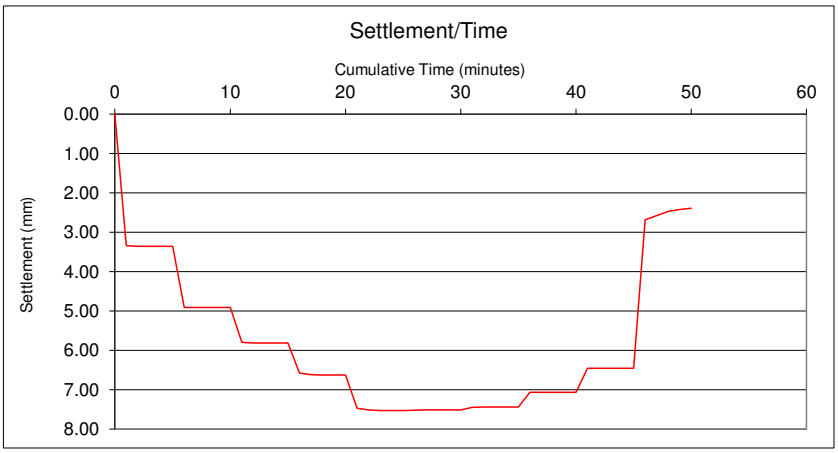

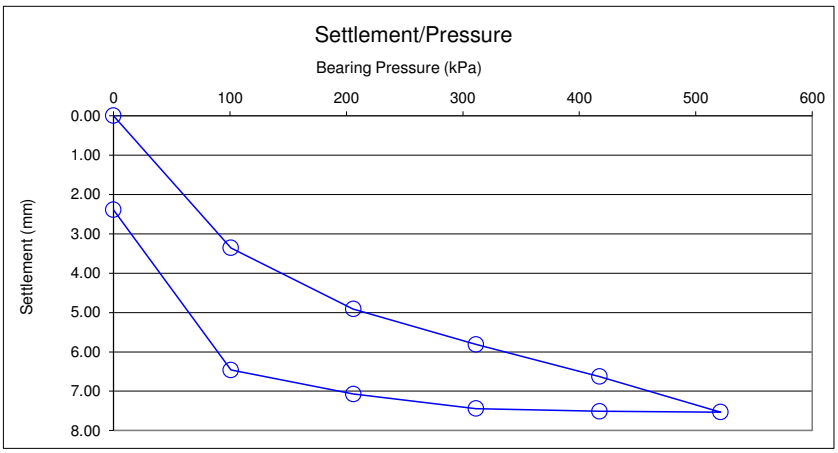


Plate Diameter	**600 mm**	Maximum Applied Pressure	**521.4 kPa**
Reaction Load	**36.5T**	Maximum Settlement	**7.53 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Gibbon Street, Manchester

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/9C Clients Reference: 9C	**REPORT NO:** DNR/68505C Report Date: 04/06/2021

Material Description:	MOT Type 1	Date Tested:	03/06/2021
Test Location:	PT 35A	Supplier/Source:	Meyer/ Fletcher Bank Quarry
Weather:	Overcast		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
5.0	100.7	3.77
10.0	205.9	6.17
15.0	311.2	7.72
20.0	417.4	8.60
25.0	521.4	9.74
30.0	417.4	9.68
35.0	311.2	9.59
40.0	205.9	9.26
45.0	100.7	8.71
50.0	0.0	5.23

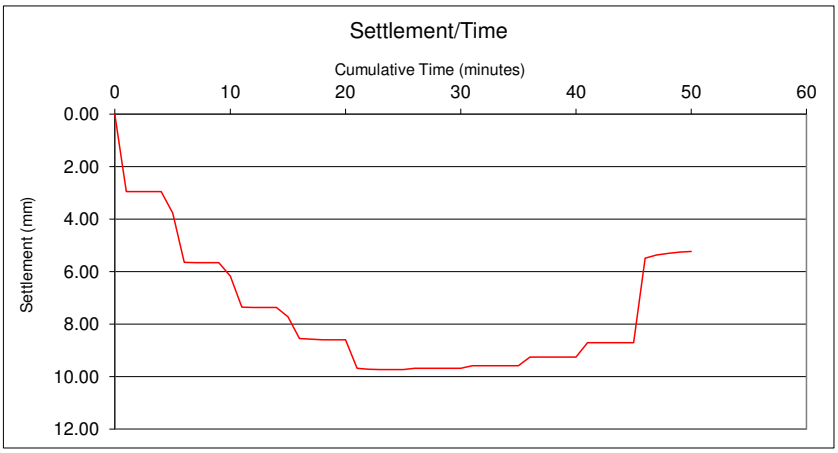

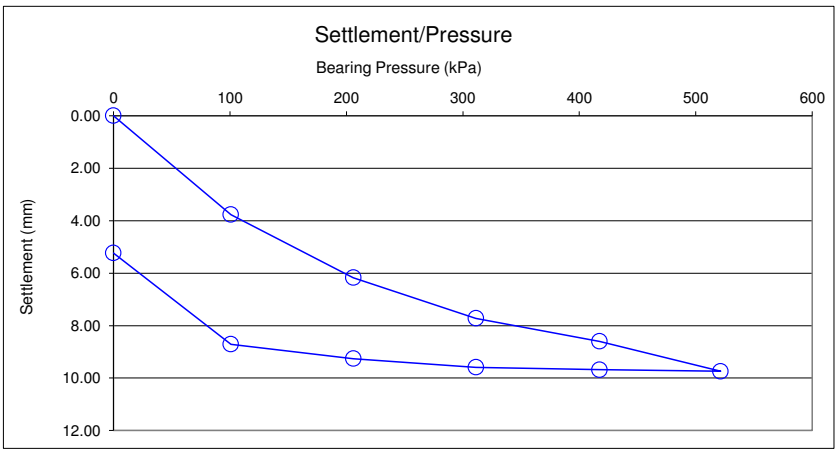


Plate Diameter	**600 mm**	Maximum Applied Pressure	**521.4 kPa**
Reaction Load	**36.5T**	Maximum Settlement	**9.74 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/6C Clients Reference: **DN3046/6C**	**REPORT NO:** **DNR/66879 C** Report Date: 12/05/2021

Material Description:	6F5-Wet	Date Tested:	10/05/2021
Test Location:	TEST 36	Supplier/Source:	Not Stated
Weather:	Clear		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	76.5	2.76
4.0	151.6	8.07
6.0	300.9	9.76
8.0	423.8	11.46
10.0	542.1	12.16
12.0	423.8	11.49
14.0	300.9	10.90
16.0	151.6	10.67
18.0	76.5	10.15
20.0	0.0	8.38

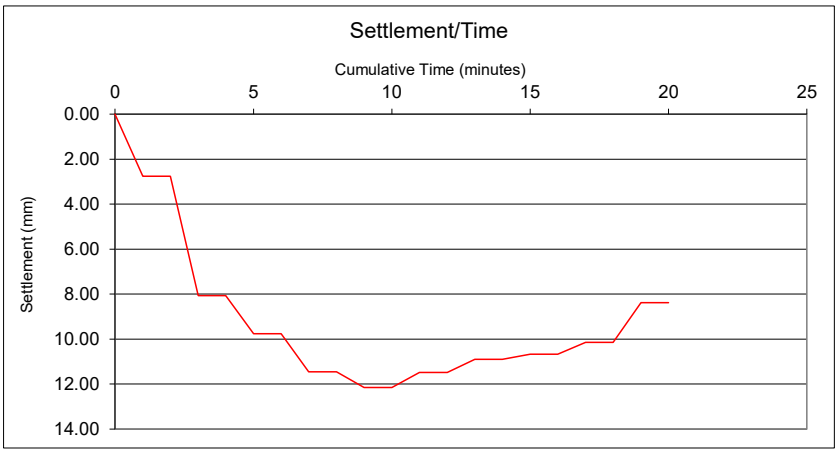

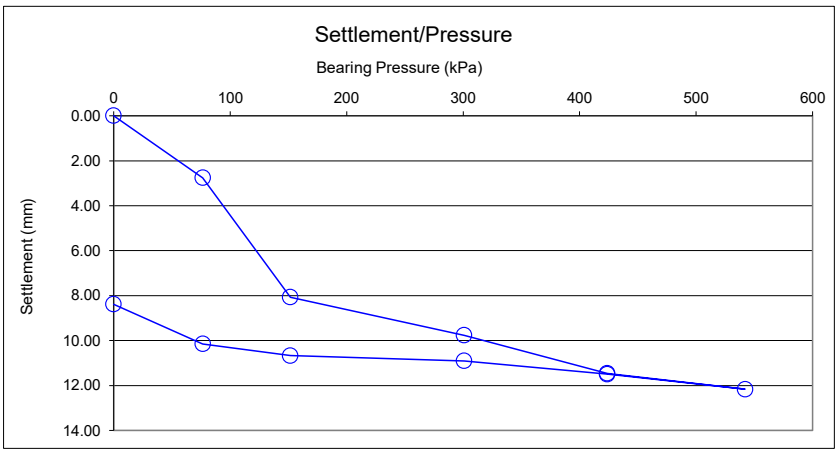


Plate Diameter	**600 mm**	Maximum Applied Pressure	**542.1 kPa**
Reaction Load	**19T**	Maximum Settlement	**12.16 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Gibbon Street, Manchester

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/9B Clients Reference: 9B	**REPORT NO:** DNR/68505B Report Date: 04/06/2021

Material Description:	MOT Type 1	Date Tested:	03/06/2021
Test Location:	PT 36A	Supplier/Source:	Meyer/ Fletcher Bank Quarry
Weather:	Overcast		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
5.0	100.7	3.85
10.0	205.9	6.22
15.0	311.2	8.89
20.0	417.4	11.08
25.0	521.4	13.25
30.0	417.4	13.23
35.0	311.2	13.13
40.0	205.9	12.83
45.0	100.7	12.03
50.0	0.0	7.14

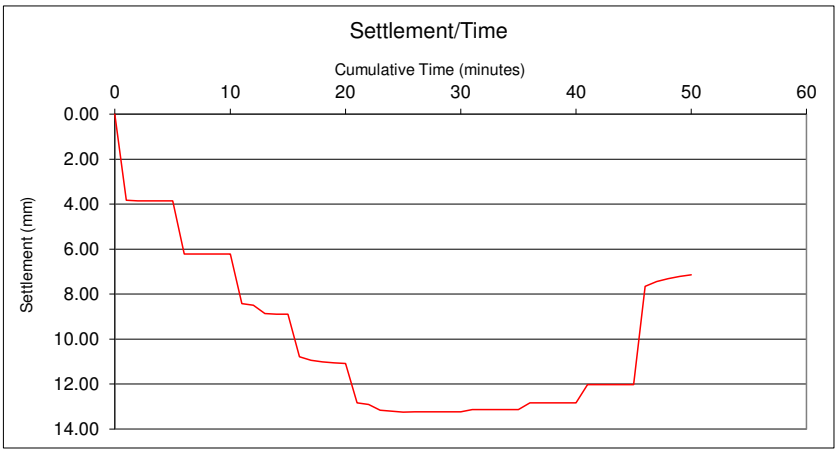

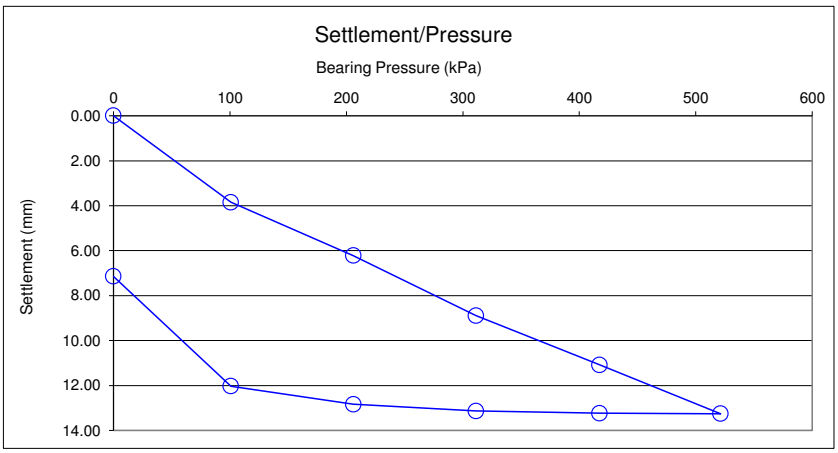


Plate Diameter	**600 mm**	Maximum Applied Pressure	**521.4 kPa**
Reaction Load	**36.5T**	Maximum Settlement	**13.25 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Gibbon Street, Manchester

Construction Testing Solutions

Bootham Lane Industrial Estate
Dunscroft
Doncaster
DN7 4JU


Tel: (01302) 352652
Email: enquiries@constructiontesting.co.uk
Web: www.constructiontesting.co.uk

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference:	DN3046/38A	**REPORT NO:** **DNR/90670A**
	Clients Reference:	**DN3046/38A**	Report Date: 15/11/2021

TEST REPORT

Material Description:	Type 1	Date Tested:	12/11/2021
Test Location:	PLT 40	Supplier/Source:	Manchester/ Maher
Weather:	Dry		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	360.8	2.74
4.0	720.8	4.28
6.0	1081.7	6.14
8.0	1438.9	8.94
10.0	1802.8	10.86
12.0	1438.9	10.86
14.0	1081.7	10.78
16.0	720.8	10.16
18.0	360.8	7.23
20.0	0.0	3.48

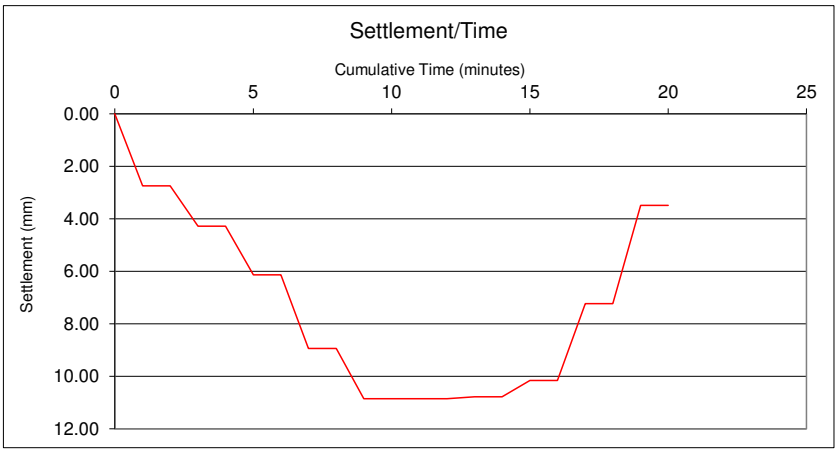

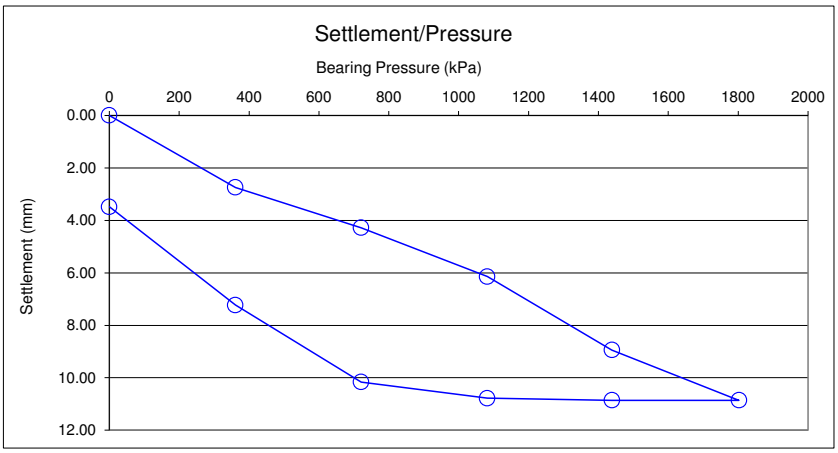


Plate Diameter	**300 mm**	Maximum Applied Pressure	**1802.8 kPa**
Reaction Load	**20T**	Maximum Settlement	**10.86 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Results relate only to the sample(s) as tested.
This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.
The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.
Testing carried out at client's site location.

Authorised Signatory

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.3 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Gibbon Street, Manchester

Construction Testing Solutions

Bootham Lane Industrial Estate
Dunscroft
Doncaster
DN7 4JU


Tel: (01302) 352652
Email: enquiries@constructiontesting.co.uk
Web: www.constructiontesting.co.uk

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference:	DN3046/41E	**REPORT NO: DNR/92374B**
	Clients Reference:	**DN3046/41E**	Report Date: 03/12/2021

TEST REPORT

Material Description:	Type 1	Date Tested:	02/12/2021
Test Location:	PLT 37	Supplier/Source:	Manchester/ Maher
Weather:	Wet		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	120.4	1.55
4.0	225.4	2.34
6.0	330.5	3.30
8.0	450.7	4.30
10.0	570.8	4.81
12.0	450.7	4.80
14.0	330.5	4.80
16.0	225.4	4.41
18.0	120.4	3.42
20.0	0.0	2.25

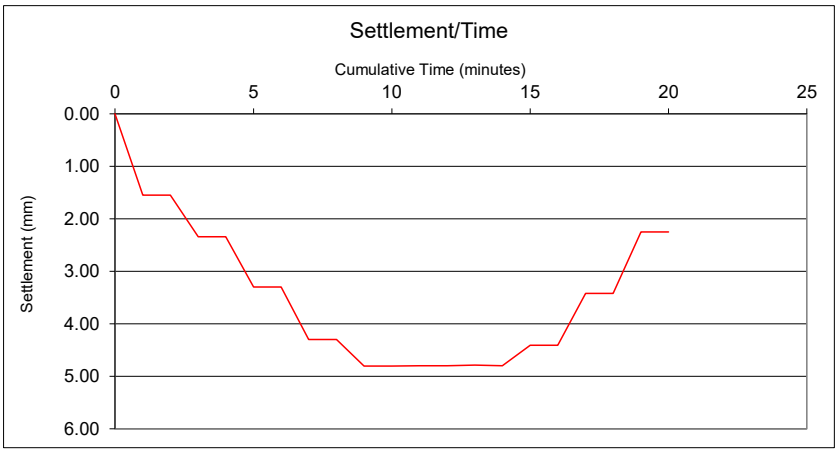

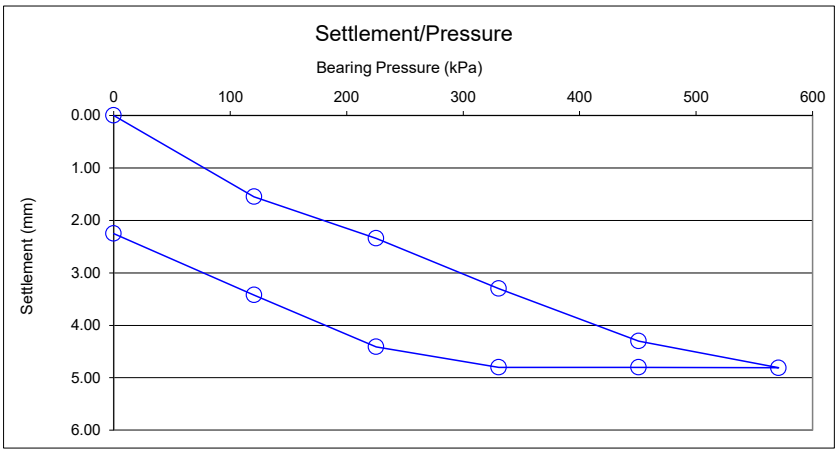


Plate Diameter	**600 mm**	Maximum Applied Pressure	**570.8 kPa**
Reaction Load	**26T**	Maximum Settlement	**4.81 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Results relate only to the sample(s) as tested.
This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.
The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.
Testing carried out at client's site location.

Authorised Signatory

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Gibbon Street, Manchester

Construction Testing Solutions

Bootham Lane Industrial Estate
Dunscroft
Doncaster
DN7 4JU


Tel: (01302) 352652
Email: enquiries@constructiontesting.co.uk
Web: www.constructiontesting.co.uk

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference:	DN3046/41C	**REPORT NO:** **DNR/92374C**
	Clients Reference:	**DN3046/41C**	Report Date: 03/12/2021

TEST REPORT

Material Description:	Type 1	Date Tested:	02/12/2021
Test Location:	PLT 44	Supplier/Source:	Manchester/ Maher
Weather:	Wet		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	120.4	1.82
4.0	225.4	3.40
6.0	330.5	4.87
8.0	450.7	6.55
10.0	570.8	8.55
12.0	450.7	8.55
14.0	330.5	8.50
16.0	225.4	8.14
18.0	120.4	5.79
20.0	0.0	3.25

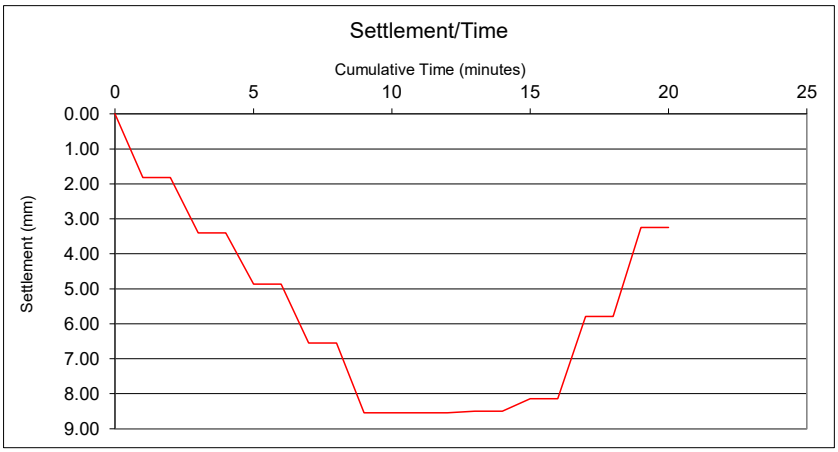

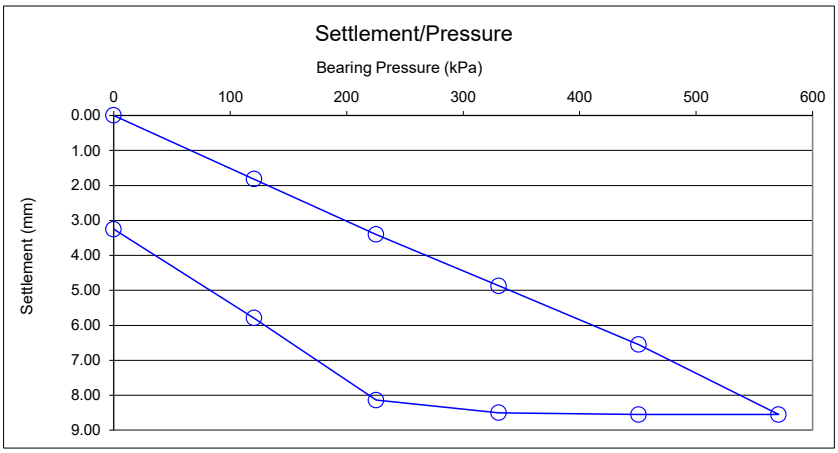


Plate Diameter	**600 mm**	Maximum Applied Pressure	**570.8 kPa**
Reaction Load	**26T**	Maximum Settlement	**8.55 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Results relate only to the sample(s) as tested.
This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.
The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.
Testing carried out at client's site location.

Authorised Signatory

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Gibbon Street, Manchester

Construction Testing Solutions

Bootham Lane Industrial Estate
Dunscroft
Doncaster
DN7 4JU


Tel: (01302) 352652
Email: enquiries@constructiontesting.co.uk
Web: www.constructiontesting.co.uk

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/40-	**REPORT NO:**	**DNR/91984-A**
	Clients Reference: **DN3046/40-**	Report Date:	29/11/2021

TEST REPORT

Material Description:	Type 1	Date Tested:	26/11/2021
Test Location:	PLT 45A	Supplier/Source:	Manchester/ Maher
Weather:	Wet		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	104.1	2.13
4.0	226.4	3.93
6.0	313.8	5.07
8.0	453.7	7.69
10.0	558.3	9.43
12.0	452.7	9.41
14.0	313.8	9.41
16.0	226.4	9.21
18.0	0.0	6.34

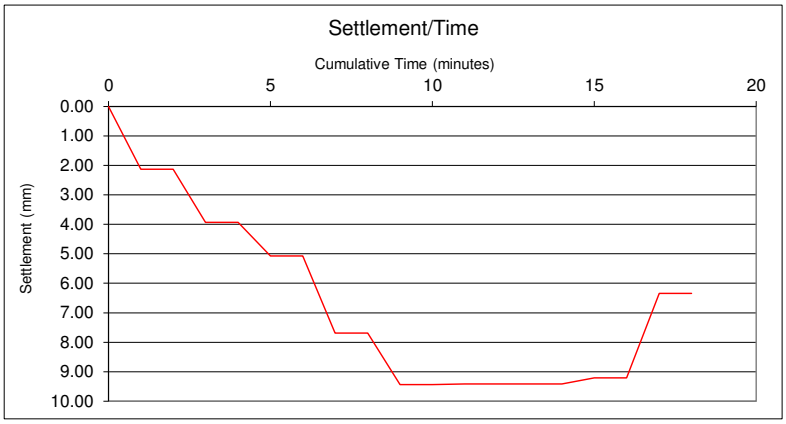

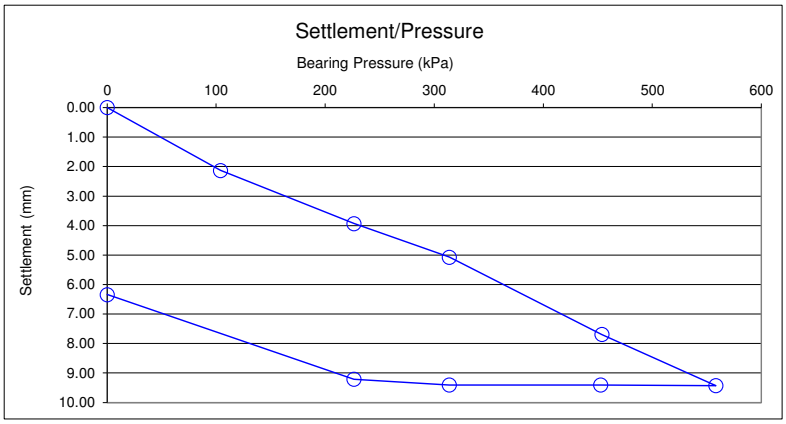


Plate Diameter	**600 mm**	Maximum Applied Pressure	**558.3 kPa**
Reaction Load	**20T**	Maximum Settlement	**9.43 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Results relate only to the sample(s) as tested.
This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.
The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.
Testing carried out at client's site location.

Authorised Signatory

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Gibbon Street, Manchester

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft
Doncaster
DN7 4JU


Tel: (01302) 352652
Email: enquiries@constructiontesting.co.uk
Web: www.constructiontesting.co.uk

Determination of Vertical Deformation - Plate Loading Test	Contract Test Reference:	DN3046/38E	**REPORT NO:** **DNR/90670B**
BS1377: Part 9: 1990	Clients Reference:	**DN3046/38E**	Report Date: 15/11/2021

TEST REPORT

Material Description:	Type 1	Date Tested:	12/11/2021
Test Location:	PLT 47A	Supplier/Source:	Manchester/ Maher
Weather:	Dry		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	360.8	2.35
4.0	720.8	4.15
6.0	1081.7	6.86
8.0	1438.9	10.96
10.0	1802.8	13.47
12.0	1438.9	13.44
14.0	1081.7	13.44
16.0	720.8	11.51
18.0	360.8	8.29
20.0	0.0	4.92

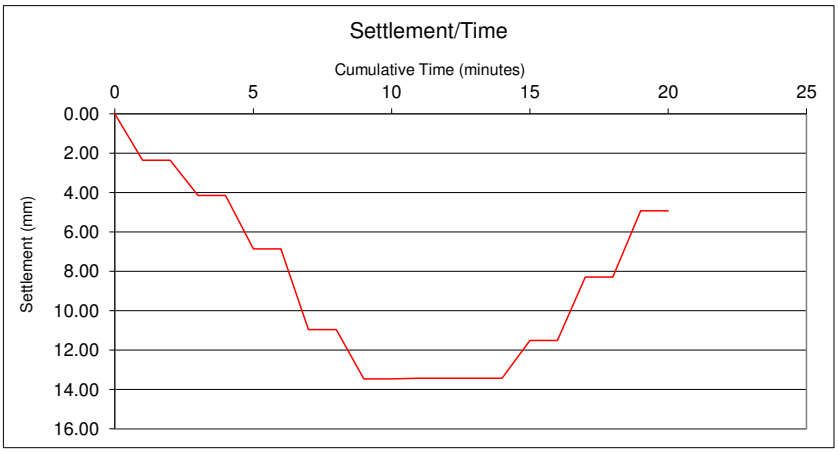

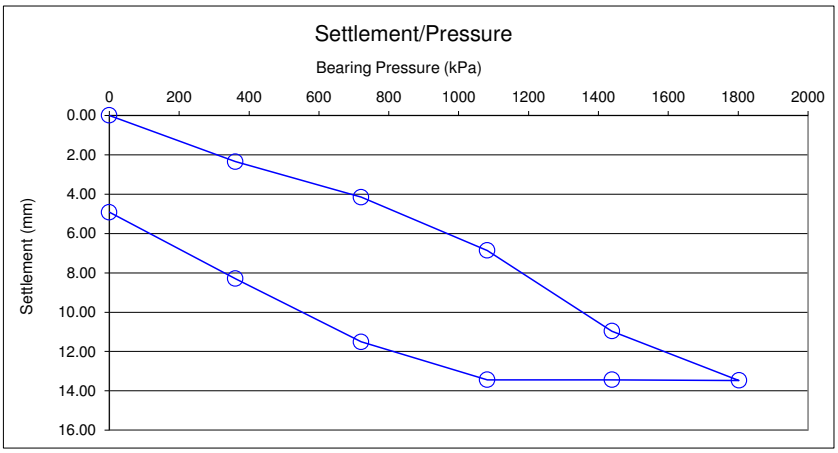


Plate Diameter	**300 mm**	Maximum Applied Pressure	**1802.8 kPa**
Reaction Load	**20T**	Maximum Settlement	**13.47 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Results relate only to the sample(s) as tested.
This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.
The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.
Testing carried out at client's site location.

Authorised Signatory

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.3 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Gibbon Street, Manchester

Construction Testing Solutions

UKAS TESTING 4161

Bootham Lane Industrial Estate
Dunscroft
Doncaster
DN7 4JU


Tel: (01302) 352652
Email: enquiries@constructiontesting.co.uk
Web: www.constructiontesting.co.uk

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/38C Clients Reference: DN3046/38C	**REPORT NO: DNR/90670C** Report Date: 15/11/2021

TEST REPORT

Material Description:	Type 1	Date Tested:	12/11/2021
Test Location:	PLT 48A	Supplier/Source:	Manchester/ Maher
Weather:	Dry		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	360.8	2.23
4.0	720.8	3.66
6.0	1081.7	5.20
8.0	1438.9	8.00
10.0	1802.8	9.55
12.0	1438.9	9.47
14.0	1081.7	9.46
16.0	720.8	9.43
18.0	360.8	6.10
20.0	0.0	3.79

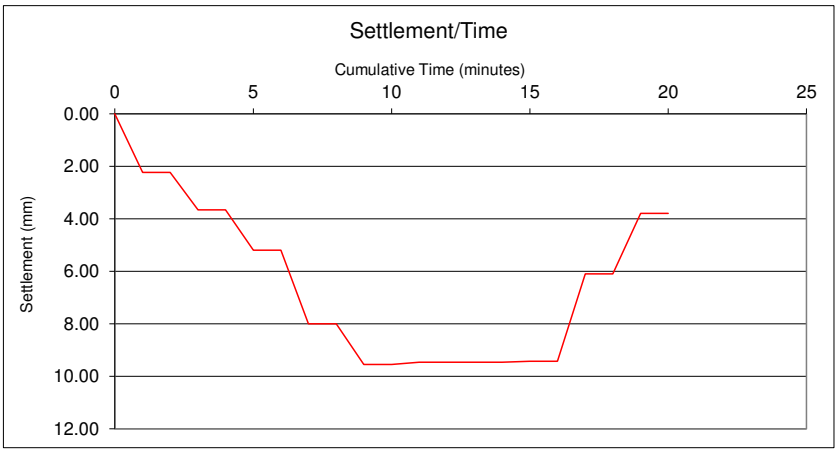

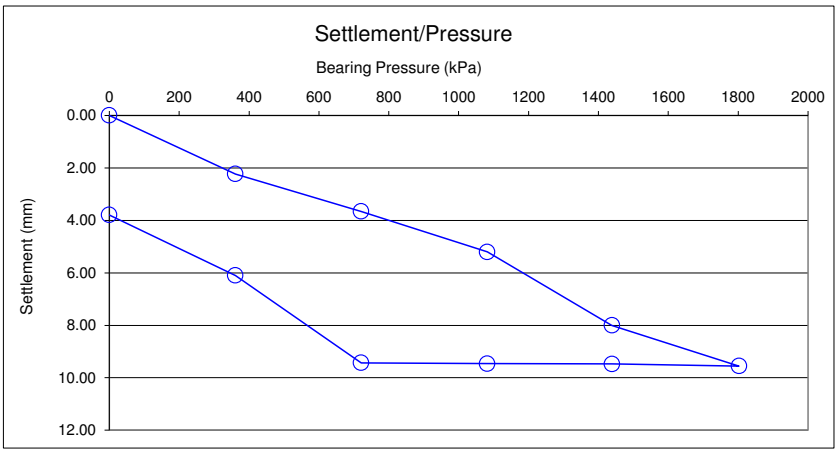


Plate Diameter	**300 mm**	Maximum Applied Pressure	**1802.8 kPa**
Reaction Load	**20T**	Maximum Settlement	**9.55 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Results relate only to the sample(s) as tested.
This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.
The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.
Testing carried out at client's site location.

Authorised Signatory

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.3 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4AJ
T | (01302) 353652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/6B Clients Reference: DN3046/6E	**REPORT NO:** DNR/66879 E Report Date: 12/05/2021

Material Description:	6F5	Date Tested:	10/05/2021
Test Location:	PT35	Supplier/Source:	Not Stated
Weather:	Clear		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	76.5	1.91
4.0	151.6	5.37
6.0	300.9	8.12
8.0	423.8	9.04
10.0	542.1	11.69
12.0	0.0	7.67

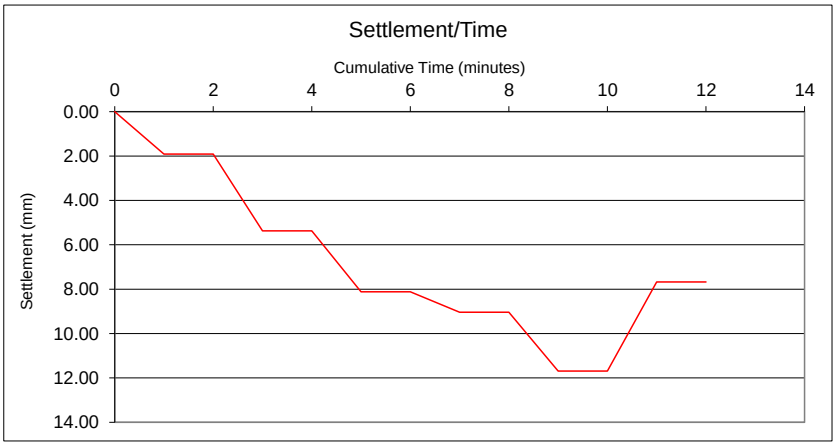

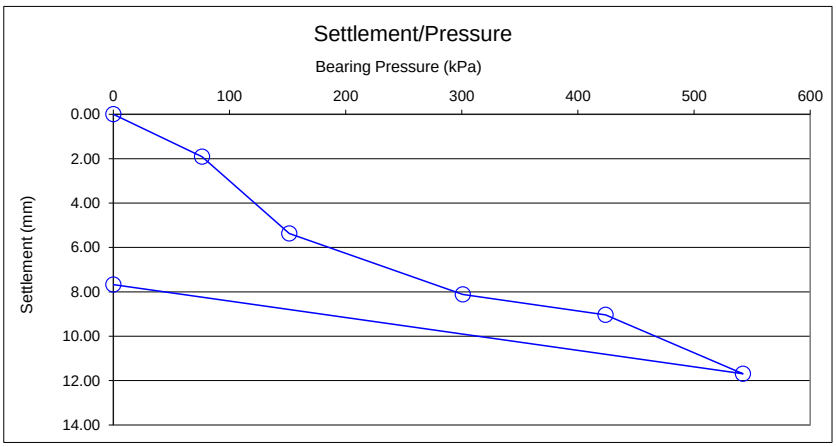


Plate Diameter	**600 mm**	Maximum Applied Pressure	**542.1 kPa**
Reaction Load	**19T**	Maximum Settlement	**11.69 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm) **N/A**			

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4AJ
T | (01302) 353652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/12A Clients Reference: DN3046/12A	**REPORT NO:** DNR/70172B Report Date: 21/06/2021

Material Description:	Type 1	Date Tested:	18/06/2021
Test Location:	PT 5	Supplier/Source:	Manchester
Weather:	Clear		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	105.2	0.74
4.0	210.4	3.03
6.0	330.5	5.00
8.0	450.7	6.80
10.0	570.8	8.58
12.0	450.7	8.60
14.0	330.5	8.51
16.0	210.4	8.07
18.0	105.2	7.33
20.0	0.0	3.71

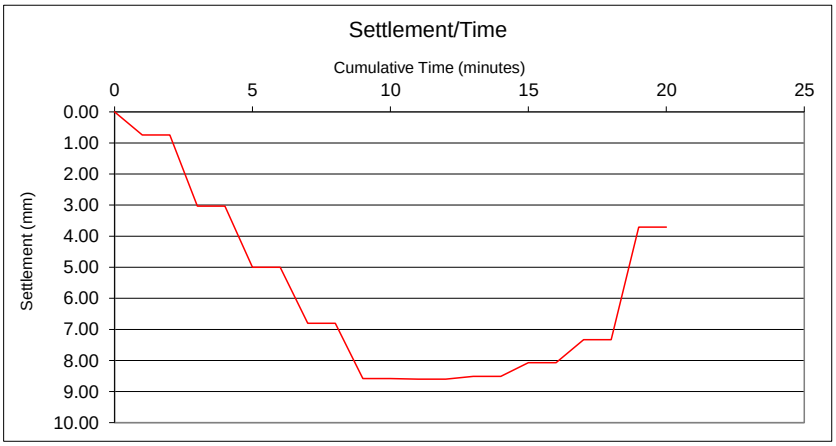

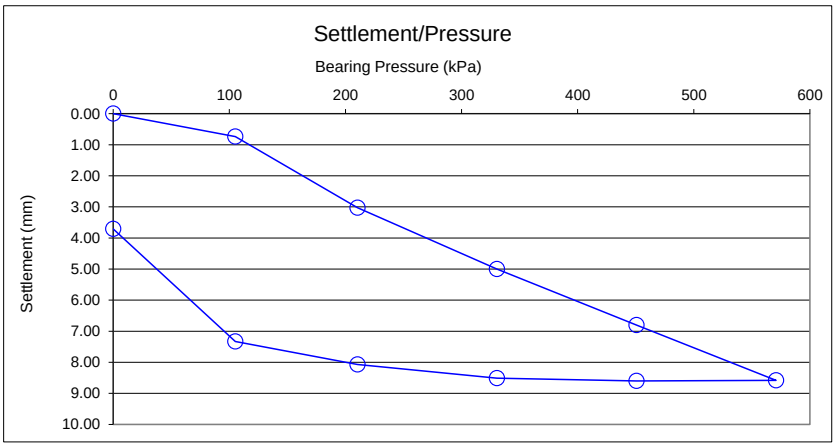


Plate Diameter	**600 mm**	Maximum Applied Pressure	**570.8 kPa**
Reaction Load	**33T**	Maximum Settlement	**8.6 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Gibbon Street, Manchester

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4AJ
T | (01302) 353652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/12A Clients Reference: DN3046/12A	**REPORT NO:** DNR/70172A Report Date: 21/06/2021

Material Description:	Type 1	Date Tested:	18/06/2021
Test Location:	PT 6	Supplier/Source:	Manchester
Weather:	Clear		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	105.2	0.45
4.0	210.4	0.78
6.0	330.5	1.67
8.0	450.7	2.38
10.0	570.8	2.99
12.0	450.7	3.00
14.0	330.5	2.98
16.0	210.4	2.92
18.0	105.2	2.84
20.0	0.0	1.84

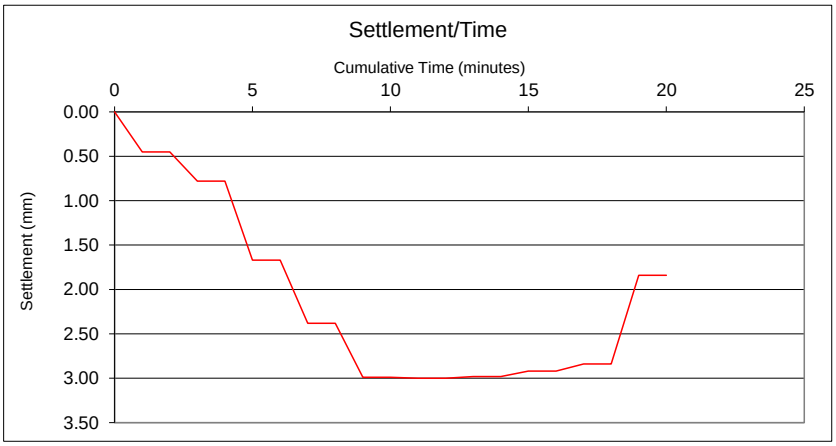

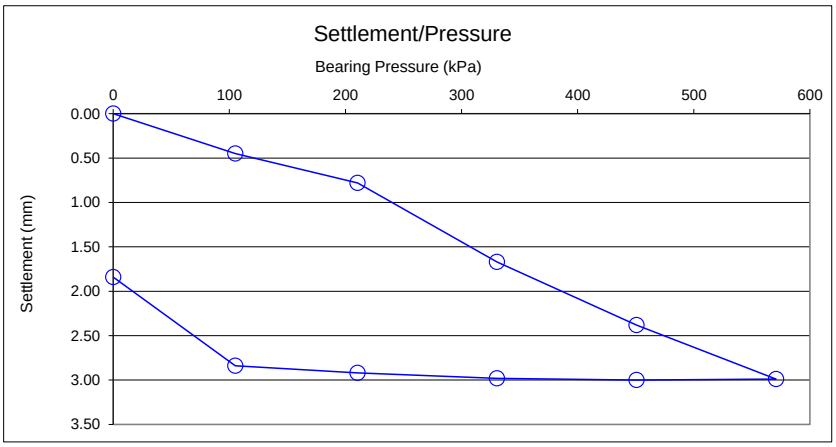


Plate Diameter	**600 mm**	Maximum Applied Pressure	**570.8 kPa**
Reaction Load	**33T**	Maximum Settlement	**3 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Gibbon Street, Manchester

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4AJ
T | (01302) 353652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/14D Clients Reference: DN3046/14D	**REPORT NO:** DNR/70396D Report Date: 23/06/2021

Material Description:	Type 1	Date Tested:	22/06/2021
Test Location:	PT9	Supplier/Source:	Not Stated
Weather:	Overcast		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	105.6	1.15
4.0	208.8	2.11
6.0	301.7	2.86
8.0	422.9	3.67
11.0	542.0	4.47
13.0	422.9	4.20
15.0	301.7	4.01
17.0	208.8	3.75
19.0	105.6	3.44
21.0	0.0	2.54

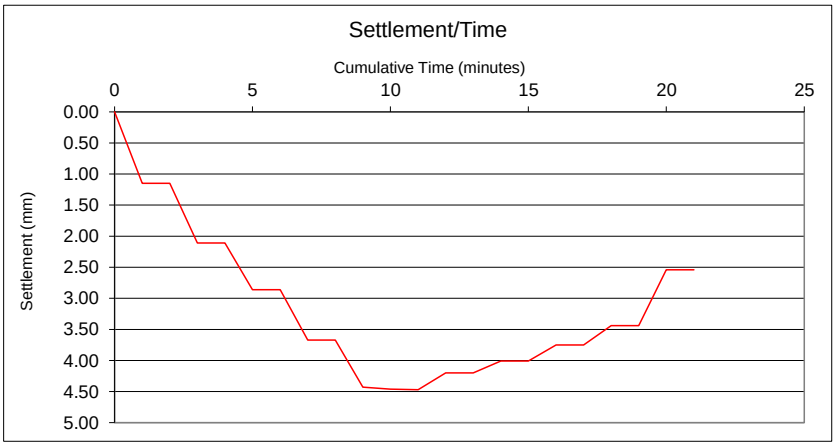

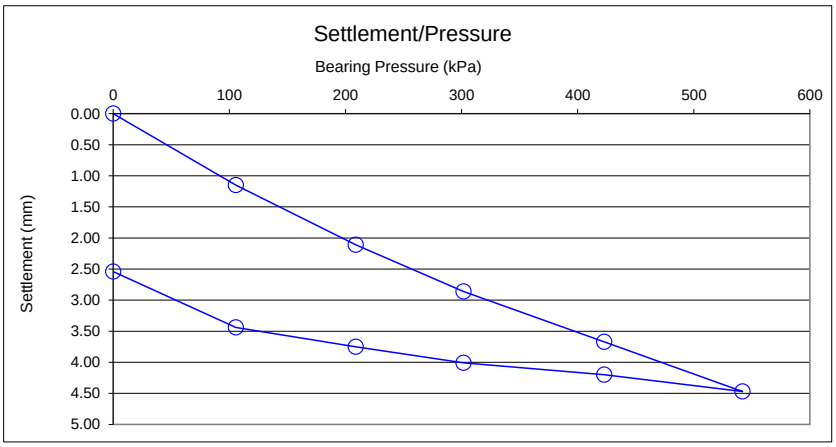


Plate Diameter	**600 mm**	Maximum Applied Pressure	**542 kPa**
Reaction Load	**Digger**	Maximum Settlement	**4.47 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4AJ
T | (01302) 353652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/14A Clients Reference: DN3046/14A	**REPORT NO:** DNR/70396A Report Date: 23/06/2021

Material Description:	Type 1	Date Tested:	22/06/2021
Test Location:	PT11	Supplier/Source:	Not Stated
Weather:	Overcast		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	105.6	1.77
4.0	210.9	4.98
6.0	301.7	7.01
8.0	423.0	9.74
11.0	542.0	11.97
13.0	423.0	11.82
15.0	301.7	11.76
17.0	208.8	11.57
19.0	105.6	10.88
21.0	0.0	8.04

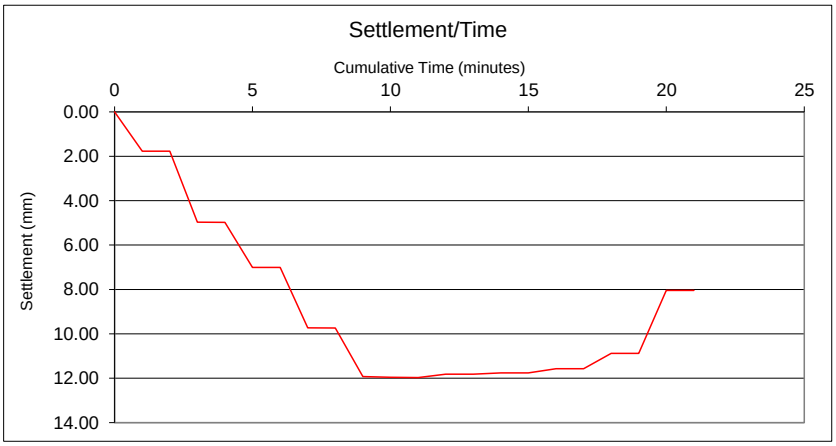

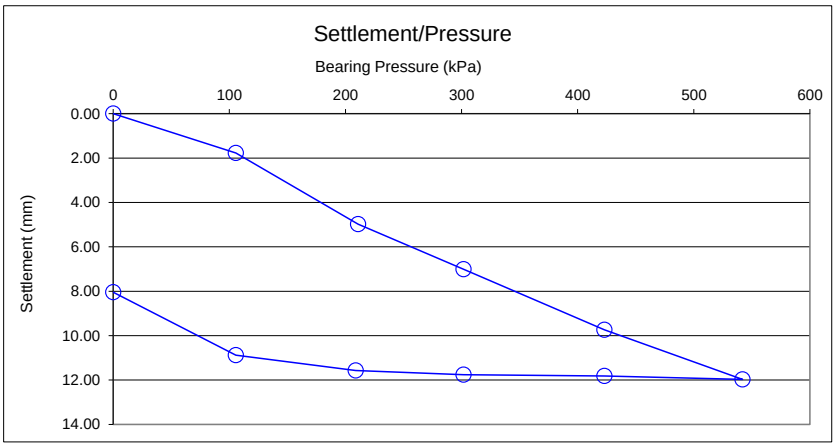


Plate Diameter	**600 mm**	Maximum Applied Pressure	**542 kPa**
Reaction Load	**Digger**	Maximum Settlement	**11.97 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/26A Clients Reference: **DN3046/26A**	**REPORT NO:** **DNR/78241A** Report Date: 27/07/2021

Material Description:	Type 1	Date Tested:	26/07/2021
Test Location:	PT 11A	Supplier/Source:	Maker/Manchester
Weather:	Dry		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	118.8	1.24
4.0	235.1	2.38
6.0	344.2	3.41
8.0	471.6	4.41
10.0	581.7	5.21
12.0	471.6	5.19
14.0	344.2	5.12
16.0	235.1	4.94
18.0	118.8	4.51
20.0	0.0	2.88

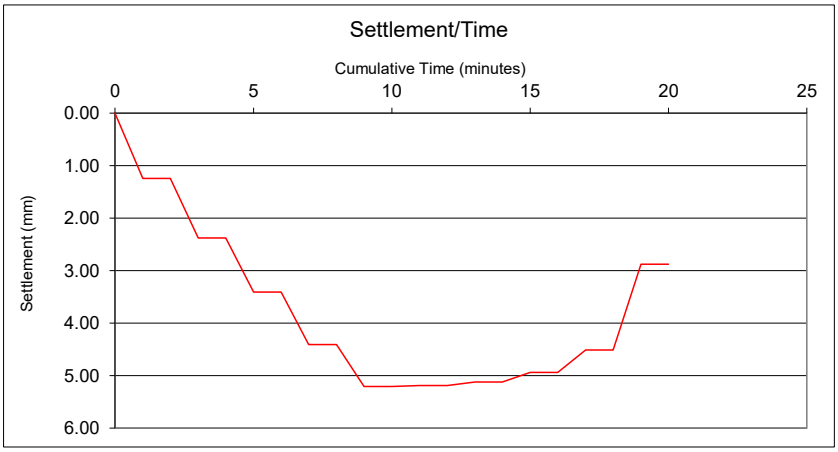

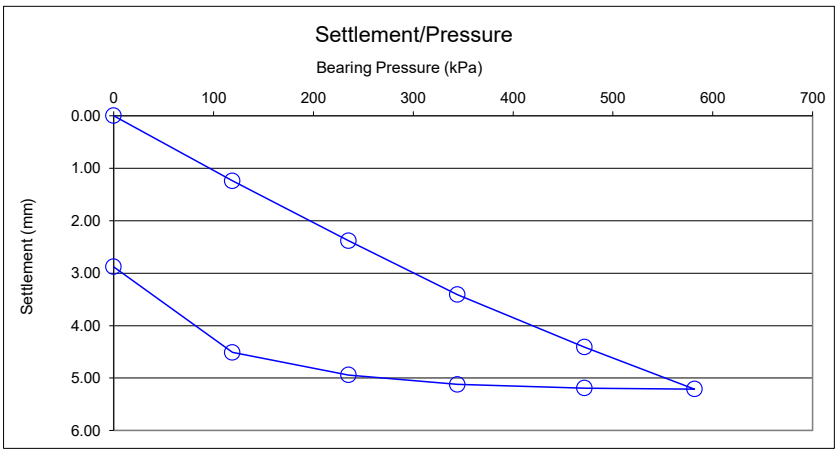


Plate Diameter	**600 mm**	Maximum Applied Pressure	**581.7 kPa**
Reaction Load	**25 Tonne**	Maximum Settlement	**5.21 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/33- Clients Reference: **DN3046-33E**	**REPORT NO: DNR/83068-B** Report Date: 13/09/2021

Material Description:	6F2	Date Tested:	10/09/2021
Test Location:	PT 12	Supplier/Source:	Manchester
Weather:	Overcast		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	104.1	0.57
4.0	207.4	0.90
6.0	313.8	1.34
8.0	419.2	1.91
10.0	523.6	2.27
12.0	419.2	2.26
14.0	313.8	2.24
16.0	207.4	2.24
18.0	104.1	1.65
20.0	0.0	0.70

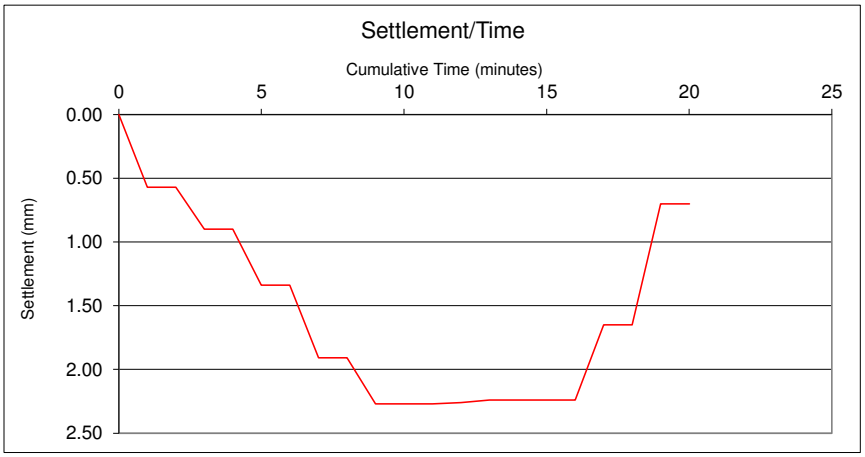

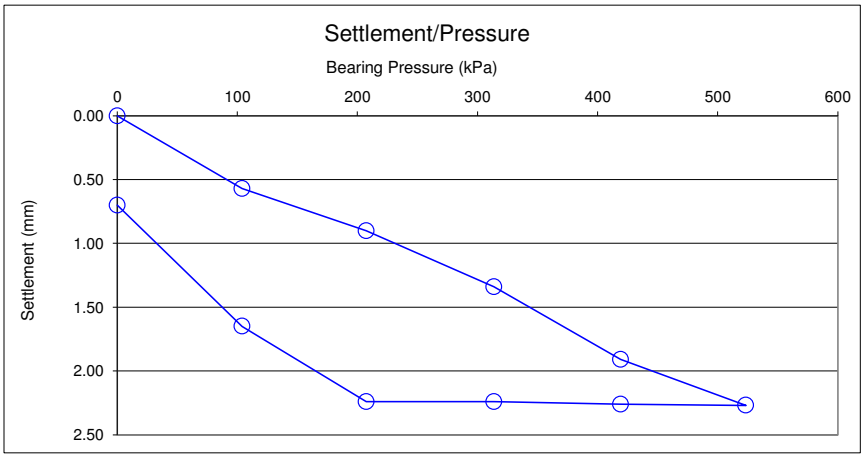


Plate Diameter	**600 mm**	Maximum Applied Pressure	**523.6 kPa**
Reaction Load	**36T**	Maximum Settlement	**2.27 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Gibbon Street, Manchester

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/25D Clients Reference: **DN3046/25D**	**REPORT NO:** **DNR/77974D** Report Date: 23/06/2021

Material Description:	Type 1	Date Tested:	21/07/2021
Test Location:	PT 13	Supplier/Source:	Not Stated
Weather:	Sunny		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
3.0	180.2	1.34
6.0	270.4	2.89
9.0	359.7	4.12
12.0	450.7	5.04
15.0	541.9	5.61
20.0	0.0	3.50

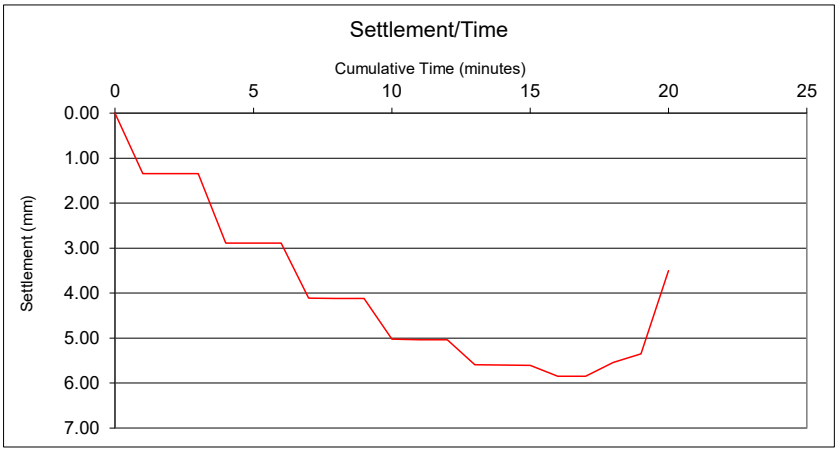

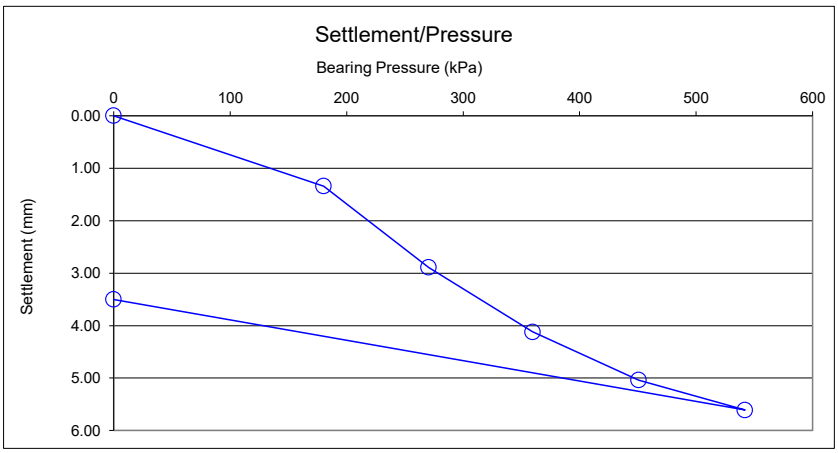


Plate Diameter	**600 mm**	Maximum Applied Pressure	**541.9 kPa**
Reaction Load	**Digger**	Maximum Settlement	**5.61 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm) **N/A**			

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Gibbon Street, Manchester

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/26A Clients Reference: **DN3046/26A**	**REPORT NO:** **DNR/78241B** Report Date: 27/07/2021

Material Description:	Type 1	**Date Tested:**	26/07/2021
Test Location:	14a	**Supplier/Source:**	Maker/Manchester
Weather:	Dry		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	118.8	0.96
4.0	235.1	1.72
6.0	344.2	2.64
8.0	471.6	3.60
10.0	581.7	4.29
12.0	471.6	4.32
14.0	344.2	4.25
16.0	235.1	4.11
18.0	118.8	3.60
20.0	0.0	1.40

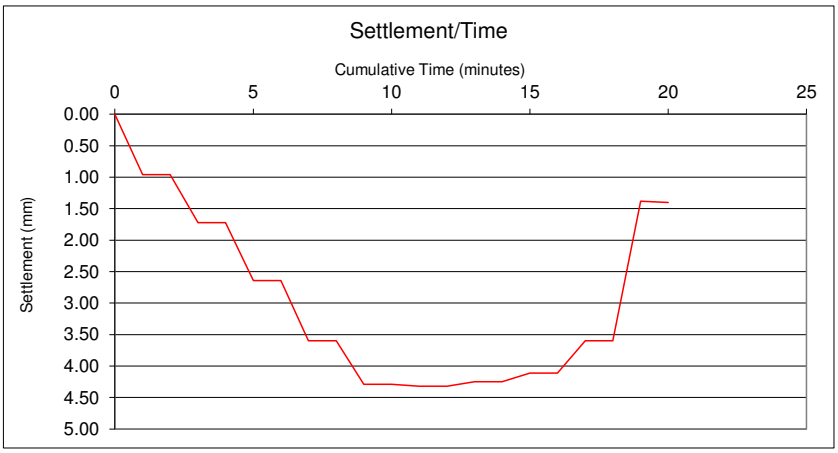

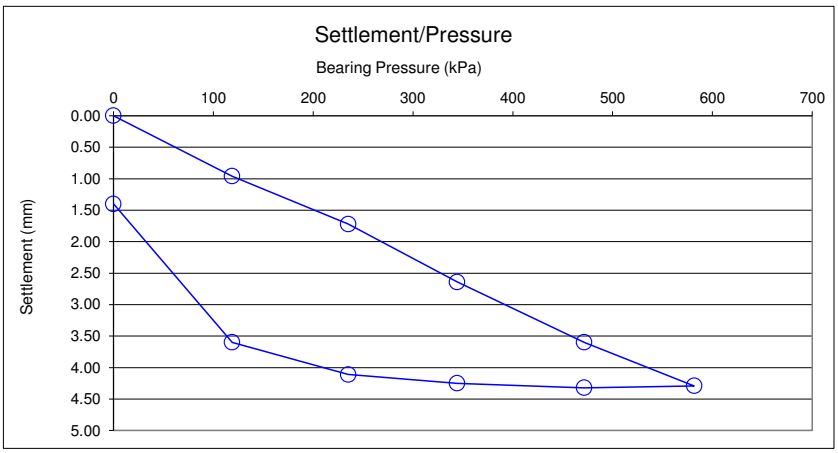


Plate Diameter	**600 mm**	Maximum Applied Pressure	**581.7 kPa**
Reaction Load	**25 Tonne**	Maximum Settlement	**4.32 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm) **N/A**			

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/1C Clients Reference: **DN3046/1C**	**REPORT NO:** **DNR/62956C** Report Date: 31/03/2021

Material Description:	Type 1	Date Tested:	29/03/2021
Test Location:	PT15	Supplier/Source:	Not Stated
Weather:	Overcast		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	104.1	1.01
4.0	207.4	1.82
6.0	313.8	2.73
8.0	419.2	3.26
10.0	495.3	3.95
12.0	0.0	2.01

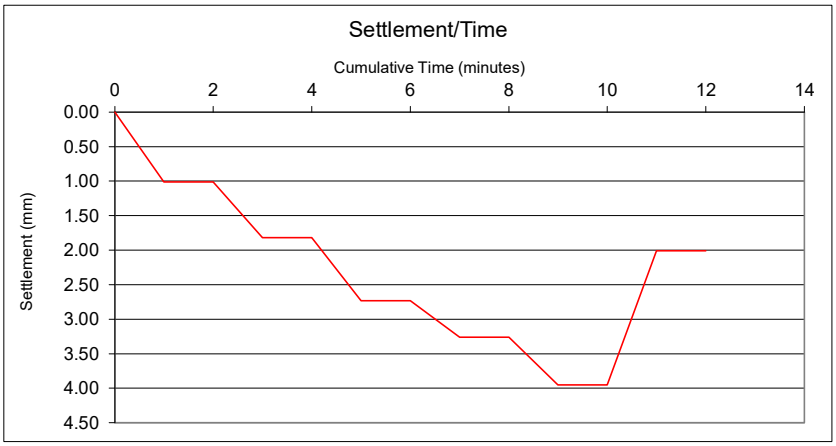

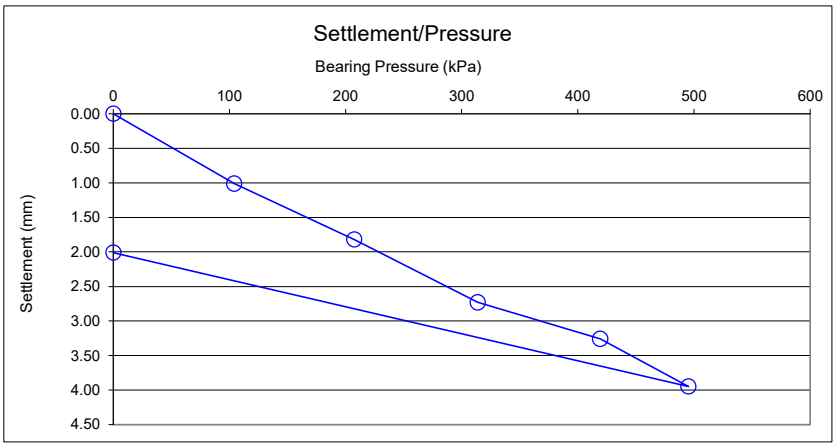


Plate Diameter	**600 mm**	Maximum Applied Pressure	**495.3 kPa**
Reaction Load	**Digger**	Maximum Settlement	**3.95 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm) **N/A**			

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/1B Clients Reference: **DN3046/1B**	**REPORT NO:** **DNR/62956B** Report Date: 31/03/2021

Material Description:	Type 1	Date Tested:	29/03/2021
Test Location:	PT16	Supplier/Source:	Not Stated
Weather:	Overcast		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	104.1	1.36
4.0	207.4	2.81
6.0	313.8	3.87
8.0	419.2	5.18
10.0	495.3	6.59
12.0	0.0	3.92

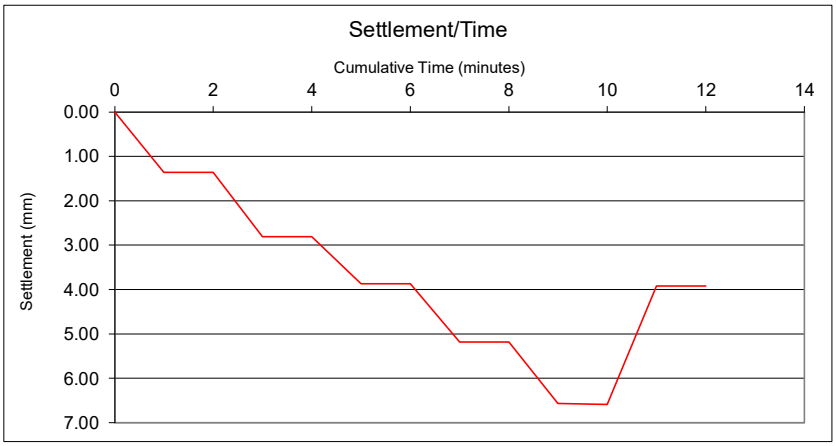

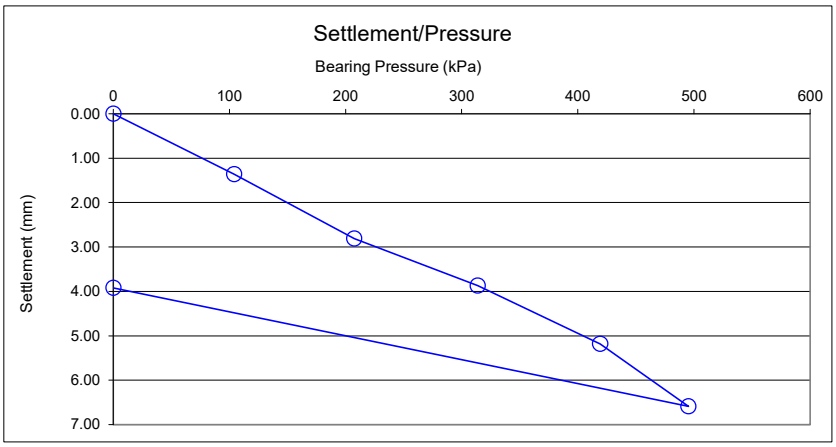


Plate Diameter	**600 mm**	Maximum Applied Pressure	**495.3 kPa**
Reaction Load	**Digger**	Maximum Settlement	**6.59 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm) **N/A**			

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4AJ
T | (01302) 353652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/14A Clients Reference: DN3046/14A	**REPORT NO:** DNR/70396B Report Date: 23/06/2021

Material Description:	Type 1	Date Tested:	22/06/2021
Test Location:	PT17	Supplier/Source:	Not Stated
Weather:	Overcast		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	105.6	0.44
4.0	210.9	0.95
6.0	301.7	1.29
8.0	423.0	1.81
11.0	542.0	2.33
12.0	0.0	1.39

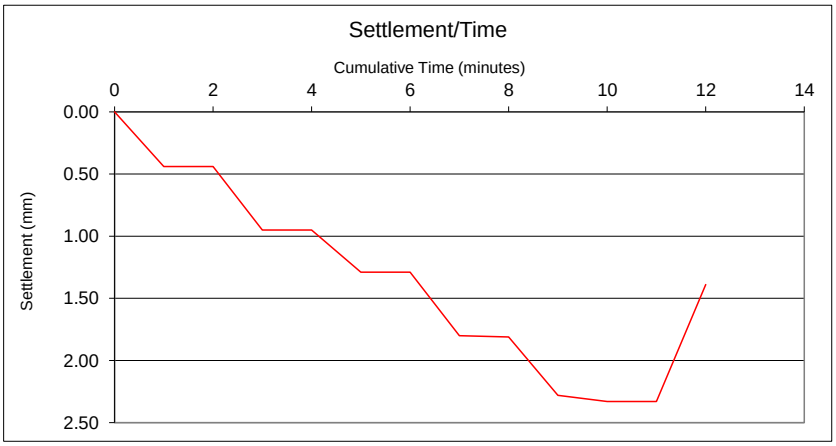

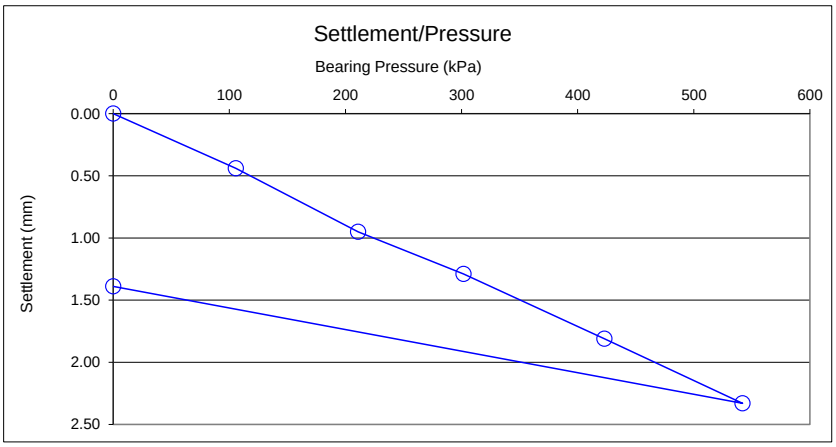


Plate Diameter	**600 mm**	Maximum Applied Pressure	**542 kPa**
Reaction Load	**Digger**	Maximum Settlement	**2.33 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/33- Clients Reference: **DN3046/33-**	**REPORT NO:** **DNR/83068-A** Report Date: 13/09/2021

Material Description:	6F2	Date Tested:	10/09/2021
Test Location:	PT 18	Supplier/Source:	Manchester
Weather:	Overcast		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	104.1	0.80
4.0	207.4	1.17
6.0	313.8	1.57
8.0	419.2	2.04
10.0	523.6	2.63
12.0	419.2	2.63
14.0	313.8	2.62
16.0	207.4	2.59
18.0	104.1	2.41
20.0	0.0	1.01

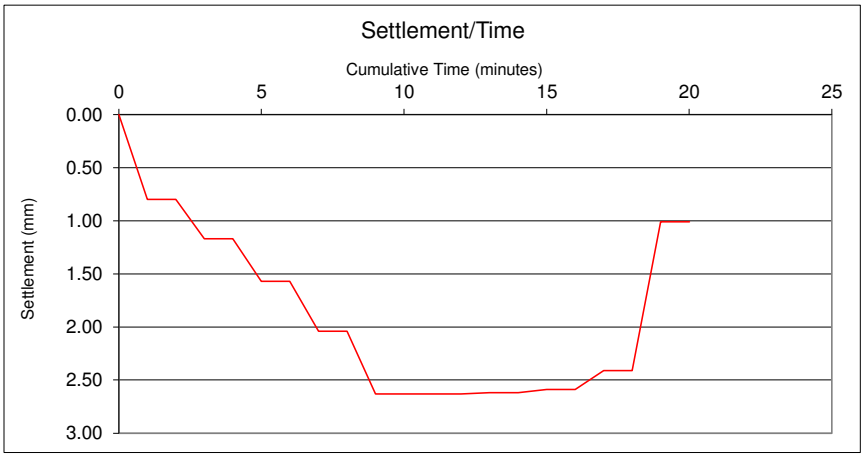

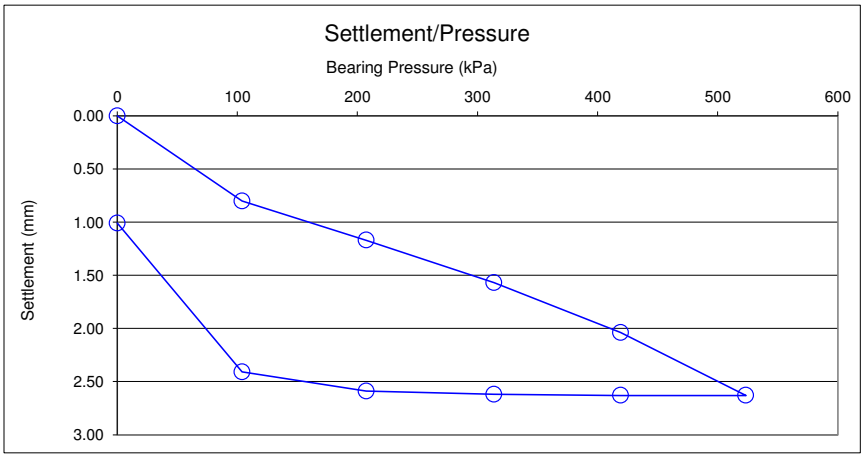


Plate Diameter	**600 mm**	Maximum Applied Pressure	**523.6 kPa**
Reaction Load	**36T**	Maximum Settlement	**2.63 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4AJ
T | (01302) 353652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/14A Clients Reference: DN3046/14A	**REPORT NO:** DNR/70396C Report Date: 23/06/2021

Material Description:	Type 1	Date Tested:	22/06/2021
Test Location:	PT18	Supplier/Source:	Not Stated
Weather:	Overcast		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	105.6	0.78
4.0	208.8	2.12
6.0	301.7	3.49
8.0	422.9	5.55
11.0	542.0	7.35
13.0	422.9	7.29
15.0	301.7	7.11
17.0	208.8	6.95
19.0	105.6	6.45
21.0	0.0	4.76

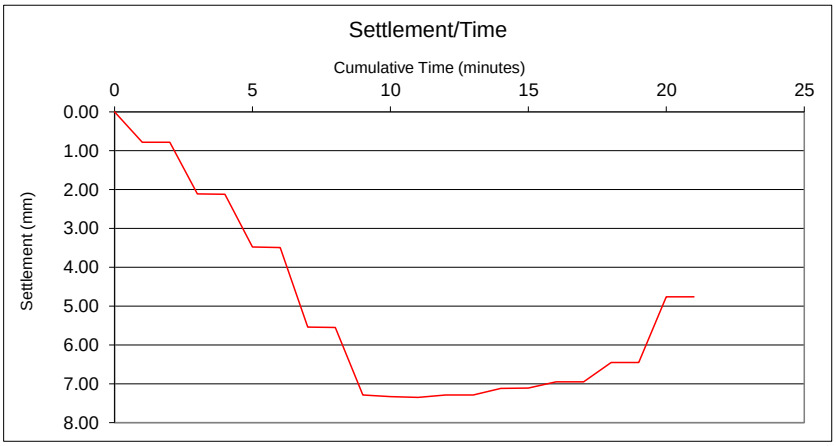

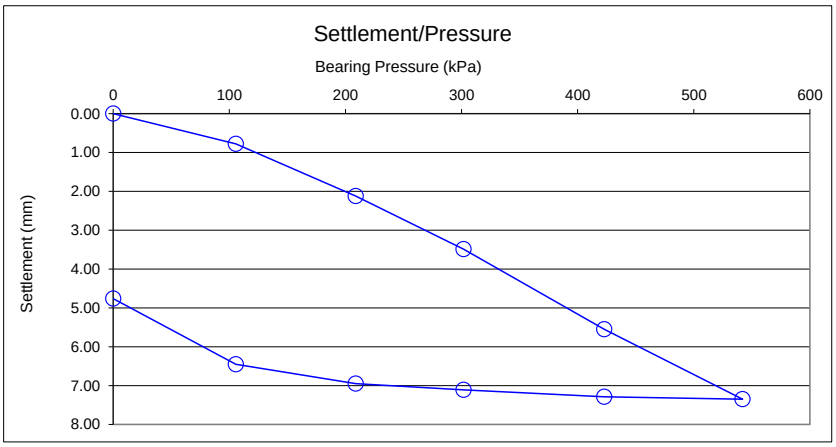


Plate Diameter	**600 mm**	Maximum Applied Pressure	**542 kPa**
Reaction Load	**Digger**	Maximum Settlement	**7.35 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/34- Clients Reference: DN3046-340	**REPORT NO:** DNR/85576-C Report Date: 20/09/2021

Material Description:	Type 1	Date Tested:	17/09/2021
Test Location:	19	Supplier/Source:	Manchester/Maker
Weather:	Sunny		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	104.1	0.45
4.0	226.4	1.08
6.0	331.3	1.66
8.0	453.7	2.09
10.0	558.3	2.18
12.0	453.7	2.18
14.0	331.2	2.17
16.0	226.4	2.15
18.0	104.1	2.01
20.0	0.0	0.45

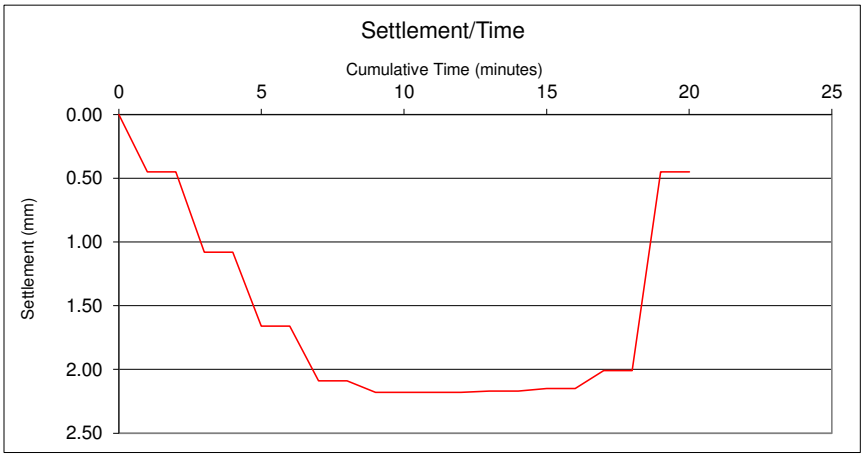

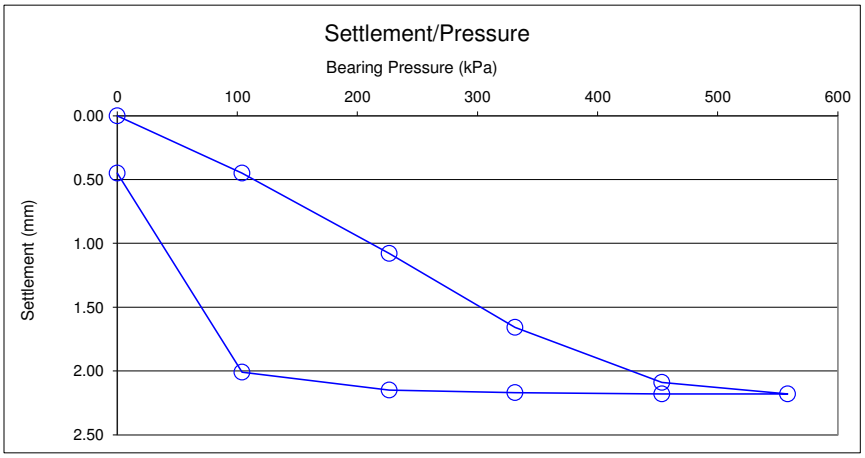


Plate Diameter	**600 mm**	Maximum Applied Pressure	**558.3 kPa**
Reaction Load	**31t**	Maximum Settlement	**2.18 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Boothams Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/34- Clients Reference: DN3046-34D	**REPORT NO:** DNR/85576-D Report Date: 20/09/2021

Material Description:	Type 1	Date Tested:	17/09/2021
Test Location:	25	Supplier/Source:	Manchester/Maker
Weather:	Sunny		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	104.1	0.37
4.0	226.4	0.77
6.0	331.3	1.08
8.0	453.7	1.52
10.0	558.3	1.90
12.0	453.7	1.90
14.0	331.2	1.90
16.0	226.4	1.84
18.0	104.1	1.74
20.0	0.0	0.59

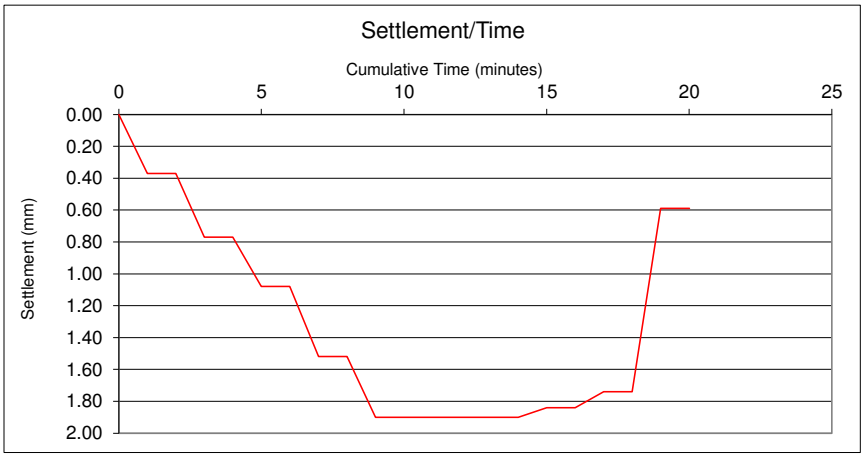

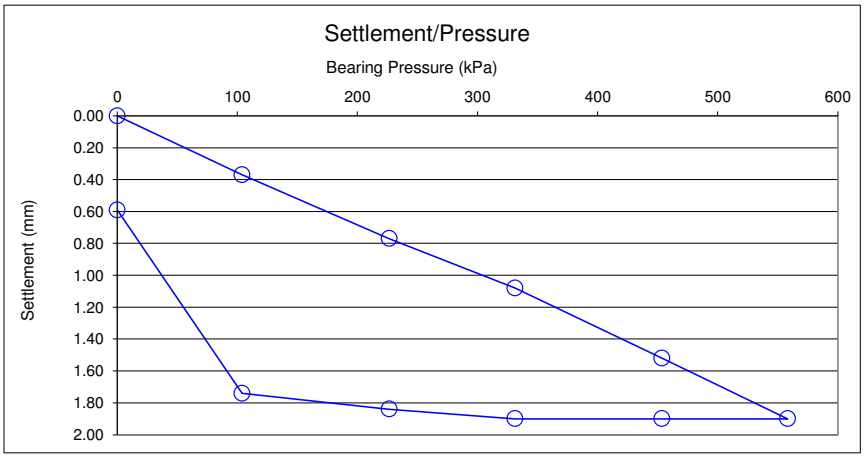


Plate Diameter	**600 mm**	Maximum Applied Pressure	**558.3 kPa**
Reaction Load	**31t**	Maximum Settlement	**1.9 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/34- Clients Reference: DN3046-34E	**REPORT NO:** DNR/85576-B Report Date: 20/09/2021

Material Description:	Type 1	Date Tested:	17/09/2021
Test Location:	26	Supplier/Source:	Manchester/Maker
Weather:	Sunny		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	104.1	0.65
4.0	226.4	1.30
6.0	331.3	2.03
8.0	453.7	2.83
10.0	558.3	3.25
12.0	453.7	3.25
14.0	331.2	3.24
16.0	226.4	3.20
18.0	104.1	3.07
20.0	0.0	1.15

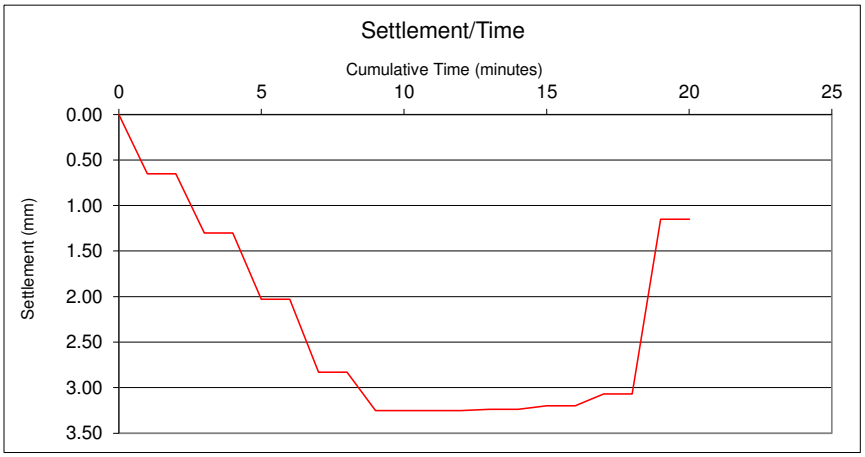

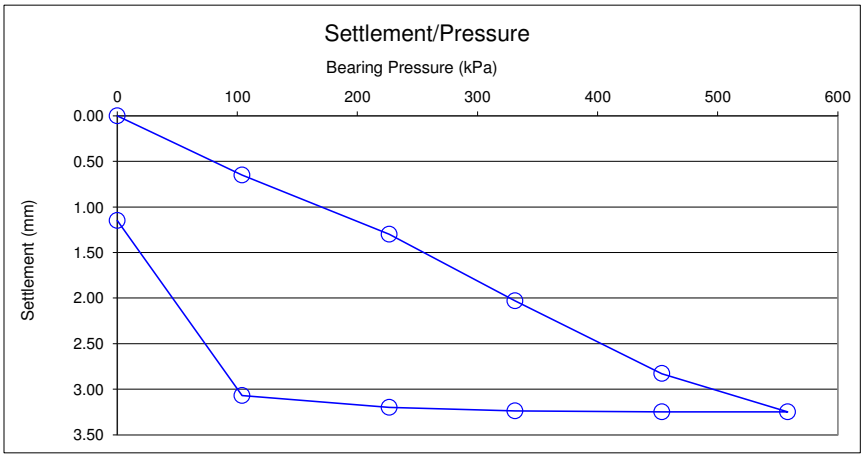


Plate Diameter	**600 mm**	Maximum Applied Pressure	**558.3 kPa**
Reaction Load	**31t**	Maximum Settlement	**3.25 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Boothams Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/29 Clients Reference: DN3046/29	**REPORT NO:** DNR/78604-D Report Date: 29/07/2021

Material Description:	Type 1	Date Tested:	28/07/2021
Test Location:	PT 27	Supplier/Source:	Maker/Manchester
Weather:	Wet		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	120.4	0.79
4.0	225.4	1.30
6.0	330.5	2.04
8.0	450.7	2.88
10.0	570.8	3.68
12.0	450.7	3.68
14.0	330.5	3.59
16.0	225.4	3.50
18.0	120.4	3.26
20.0	0.0	1.72

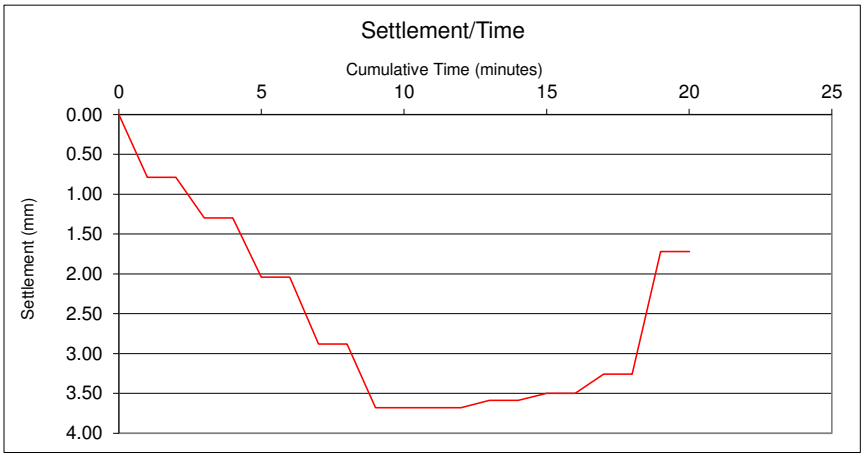

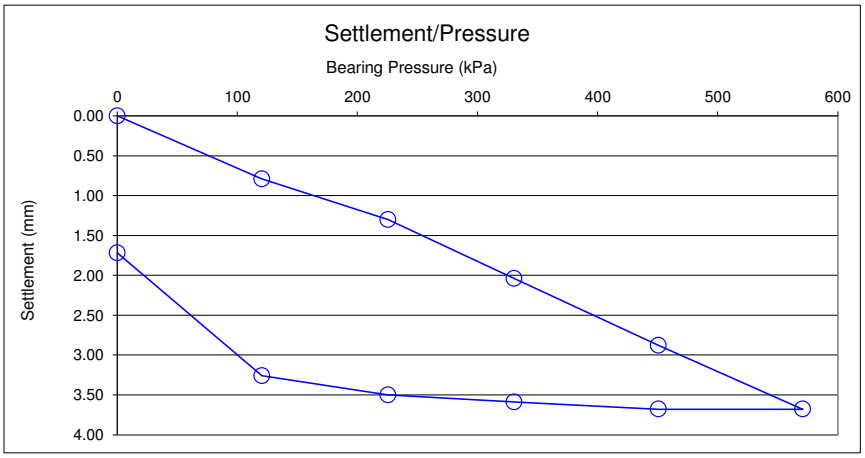


Plate Diameter	**600 mm**	Maximum Applied Pressure	**570.8 kPa**
Reaction Load	**28 T**	Maximum Settlement	**3.68 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/25E Clients Reference: **DN3046/25E**	**REPORT NO:** **DNR/77974B** Report Date: 23/06/2021

Material Description:	Type 1	Date Tested:	21/07/2021
Test Location:	PT28	Supplier/Source:	Not Stated
Weather:	Sunny		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
3.0	180.2	0.38
6.0	270.4	0.66
9.0	359.7	1.43
12.0	450.7	1.85
15.0	541.9	2.26
20.0	0.0	1.01

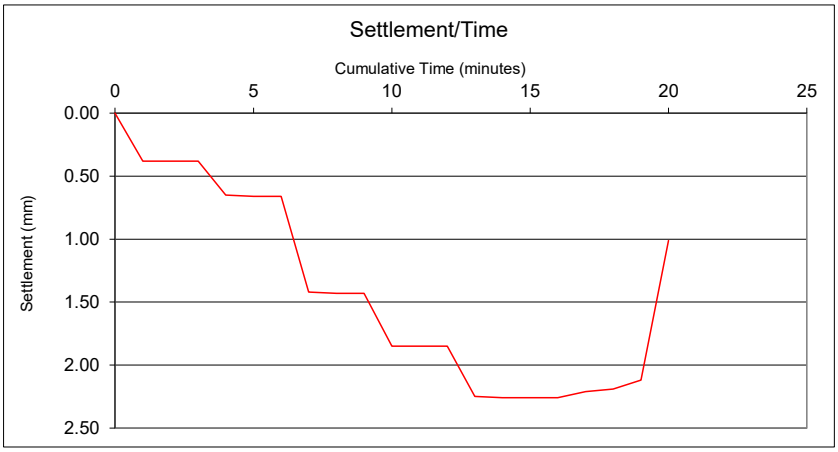

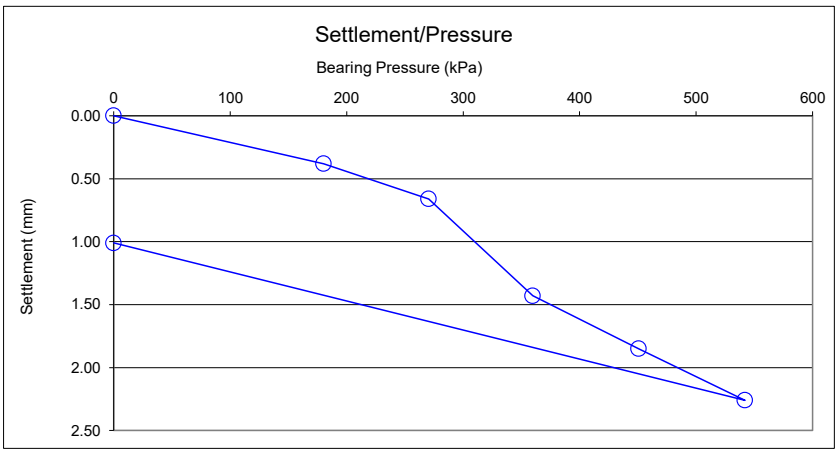


Plate Diameter	**600 mm**	Maximum Applied Pressure	**541.9 kPa**
Reaction Load	**Digger**	Maximum Settlement	**2.26 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm) **N/A**			

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4AJ
T | (01302) 353652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/11 Clients Reference: DN3046/11	**REPORT NO:** DNR/70171 Report Date: 21/06/2021

Material Description:	6F5	Date Tested:	18/06/2021
Test Location:	PT 29	Supplier/Source:	Manchester
Weather:	Clear		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	105.2	0.08
4.0	210.4	1.53
6.0	330.5	2.86
8.0	450.7	3.95
10.0	570.8	4.98
12.0	450.7	4.99
14.0	330.5	4.96
16.0	210.4	4.83
18.0	105.2	4.40
20.0	0.0	3.02

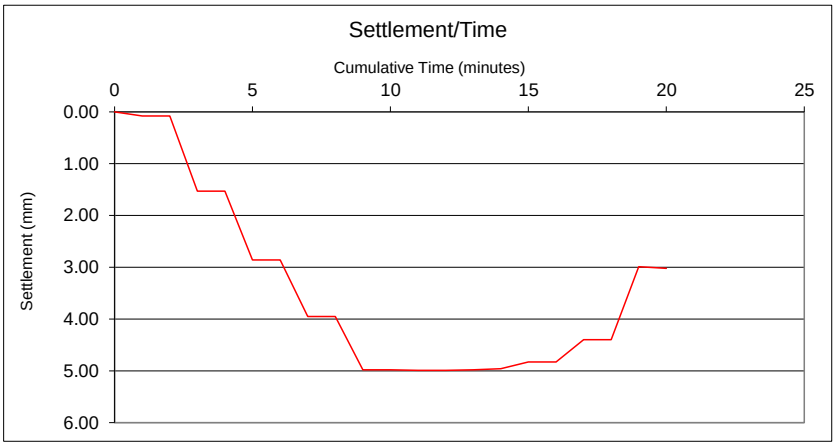

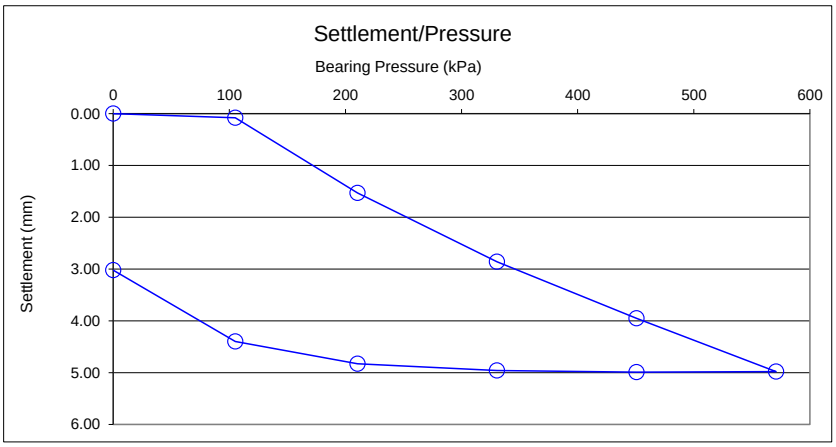


Plate Diameter	**600 mm**	Maximum Applied Pressure	**570.8 kPa**
Reaction Load	**33T**	Maximum Settlement	**4.99 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4AJ
T | (01302) 353652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/2B Clients Reference: DN3046/2B	**REPORT NO:** DNR/63774B Report Date: 08/04/2021

Material Description:	Stone	Date Tested:	07/04/2021
Test Location:	PT3	Supplier/Source:	Not Stated
Weather:	Clear		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	88.7	1.47
4.0	180.5	2.82
6.0	271.4	3.90
8.0	363.1	5.03
10.0	435.1	6.15
12.0	507.7	7.12
14.0	544.4	8.15
16.0	0.0	6.02

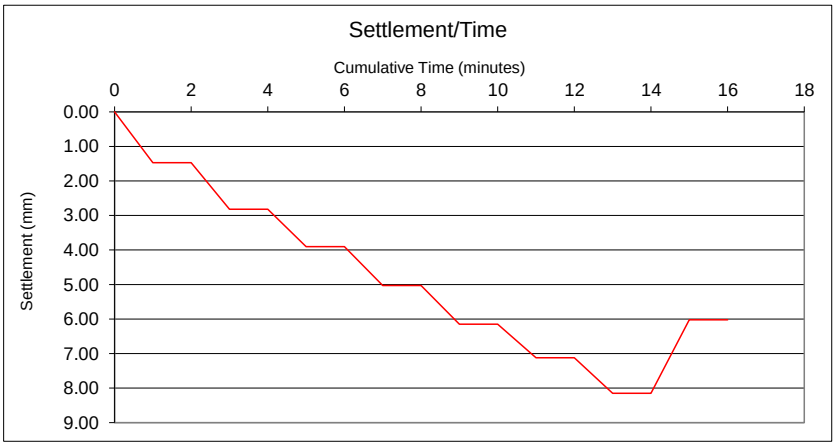

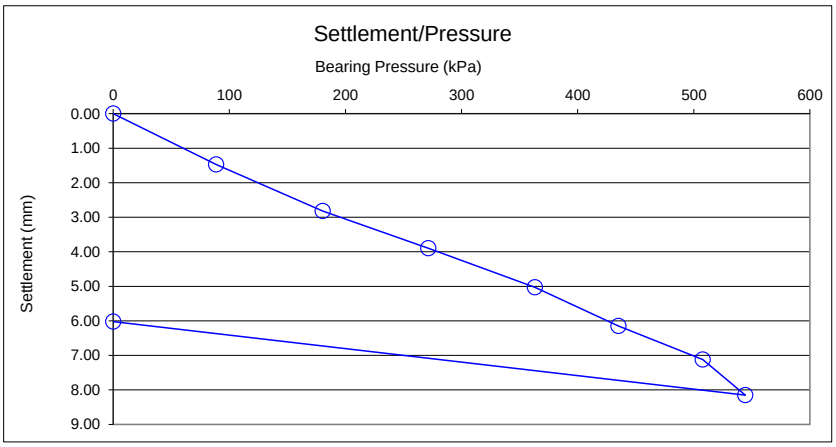


Plate Diameter	**600 mm**	Maximum Applied Pressure	**544.4 kPa**
Reaction Load	**33T**	Maximum Settlement	**8.15 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Boothams Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/34- Clients Reference: DN3046-34A	**REPORT NO:** DNR/85576-A Report Date: 20/09/2021

Material Description:	Type 1	Date Tested:	17/09/2021
Test Location:	34	Supplier/Source:	Manchester/Maker
Weather:	Sunny		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	104.1	0.39
4.0	226.4	0.84
6.0	331.3	1.51
8.0	453.7	1.74
10.0	558.3	1.92
12.0	453.7	1.92
14.0	331.2	1.89
16.0	226.4	1.88
18.0	104.1	1.74
20.0	0.0	0.72

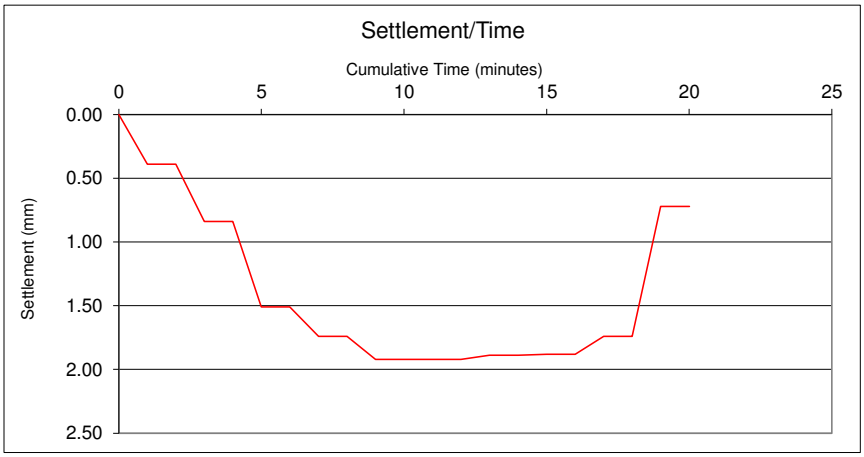

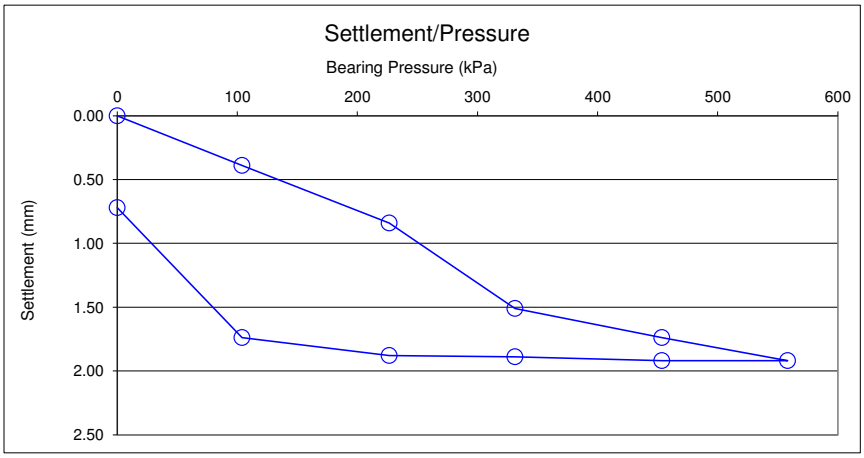


Plate Diameter	**600 mm**	Maximum Applied Pressure	**558.3 kPa**
Reaction Load	**31t**	Maximum Settlement	**1.92 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Gibbon Street, Manchester

Construction Testing Solutions

Bootham Lane Industrial Estate
Dunscroft
Doncaster
DN7 4JU


Tel: (01302) 352652
Email: enquiries@constructiontesting.co.uk
Web: www.constructiontesting.co.uk

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/36	**REPORT NO: DNR-89816**
	Clients Reference: DN3046/36	Report Date: 04/11/2021

TEST REPORT

Material Description:	Crushed Sandstone	Date Tested:	03/11/2021
Test Location:	39-A [Piling Mat]	Supplier/Source:	Not Stated
Weather:	Clear		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
3.0	123.6	5.08
6.0	240.5	8.56
11.0	362.6	13.23
16.0	478.4	15.39
21.0	596.2	11.90
24.0	468.9	10.83
27.0	240.5	9.92
32.0	123.6	6.75
35.0	0.0	6.67

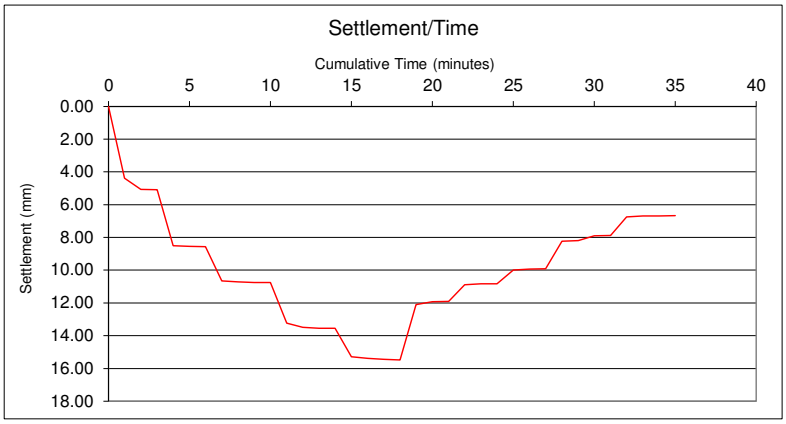

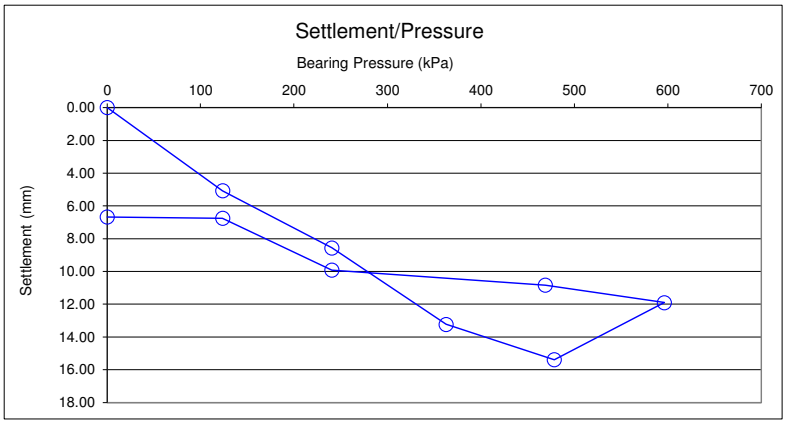


Plate Diameter	**600 mm**	Maximum Applied Pressure	**596.2 kPa**
Reaction Load	**Volvo Excavator Tp3626**	Maximum Settlement	**15.39 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Results relate only to the sample(s) as tested.
This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.
The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.
Testing carried out at client's site location.

Authorised Signatory

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4AJ
T | (01302) 353652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/2A Clients Reference: DN3046/2A	**REPORT NO:** DNR/63774A Report Date: 08/04/2021

Material Description:	Stone	Date Tested:	07/04/2021
Test Location:	PT4	Supplier/Source:	Not Stated
Weather:	Clear		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	88.7	1.44
4.0	180.5	2.70
6.0	271.4	3.83
8.0	363.1	5.25
10.0	435.1	6.07
12.0	507.7	6.87
14.0	544.4	7.56
16.0	0.0	5.81

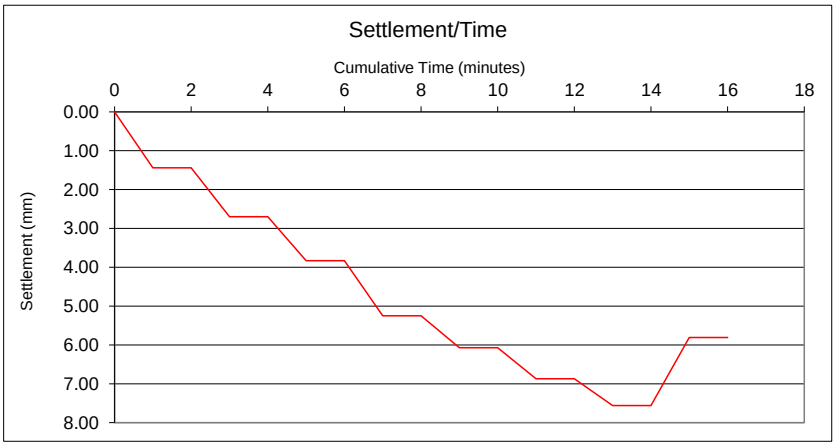

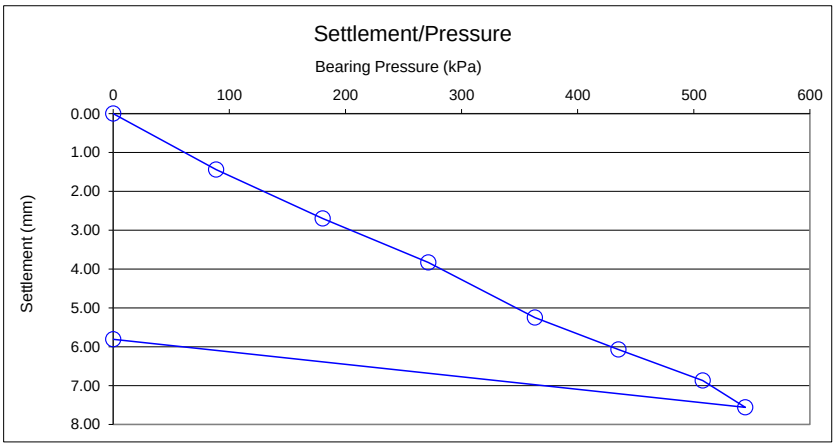


Plate Diameter	**600 mm**	Maximum Applied Pressure	**544.4 kPa**
Reaction Load	**33T**	Maximum Settlement	**7.56 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Boothams Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/29/ Clients Reference: DN3046/29A	**REPORT NO:** DNR/78604-A Report Date: 29/07/2021

Material Description:	Type 1	Date Tested:	28/07/2021
Test Location:	PT 41-A	Supplier/Source:	Maker/Manchester
Weather:	Wet		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	120.4	0.95
4.0	225.4	1.54
6.0	330.5	2.31
8.0	450.7	3.28
10.0	570.8	4.00
12.0	450.7	4.00
14.0	330.5	3.96
16.0	225.4	3.86
18.0	120.4	3.50
20.0	0.0	1.90

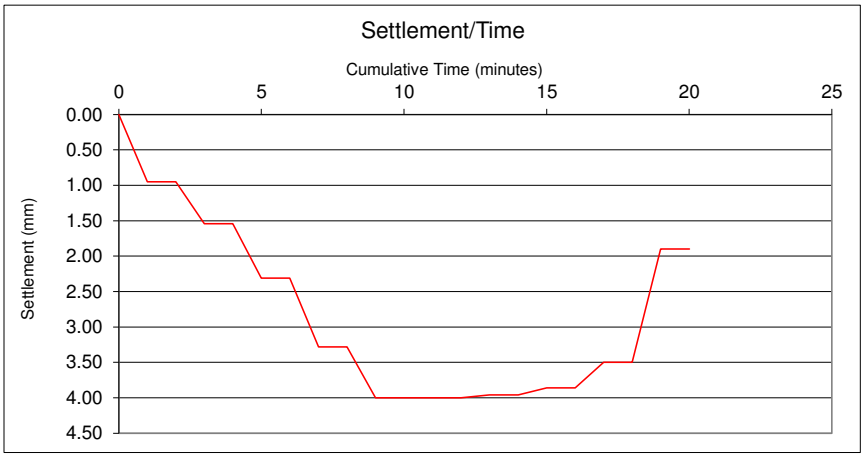

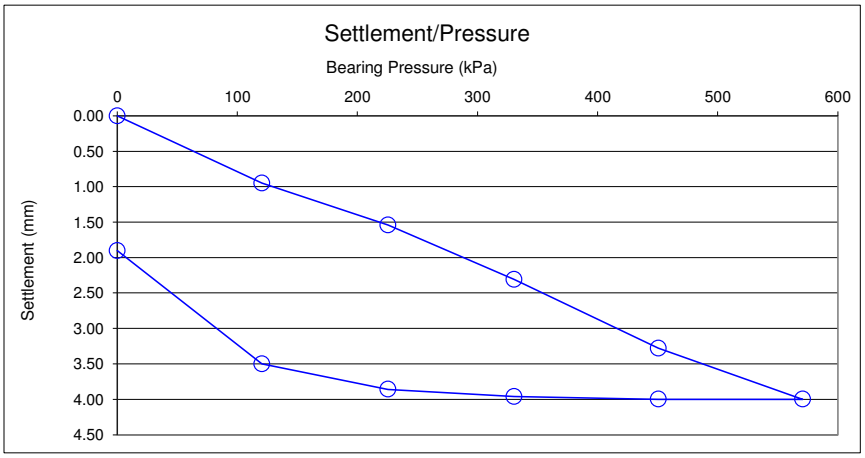


Plate Diameter	**600 mm**	Maximum Applied Pressure	**570.8 kPa**
Reaction Load	**28 T**	Maximum Settlement	**4 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk
4161

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/290 Clients Reference: DN3046/290	**REPORT NO:** DNR/78604-C Report Date: 29/07/2021

Material Description:	Type 1	Date Tested:	28/07/2021
Test Location:	PT 42	Supplier/Source:	Maker/Manchester
Weather:	Wet		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	120.4	0.30
4.0	225.4	1.16
6.0	330.5	1.76
8.0	450.7	2.49
10.0	570.8	3.18
12.0	450.7	3.20
14.0	330.5	3.20
16.0	225.4	3.20
18.0	120.4	3.15
20.0	0.0	2.11

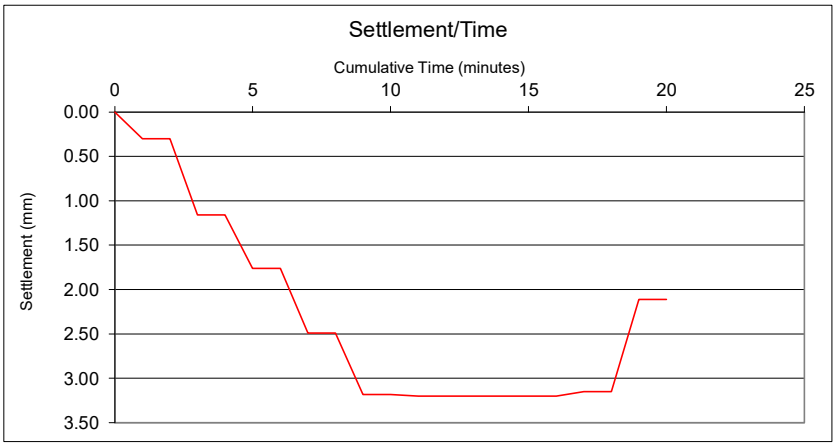

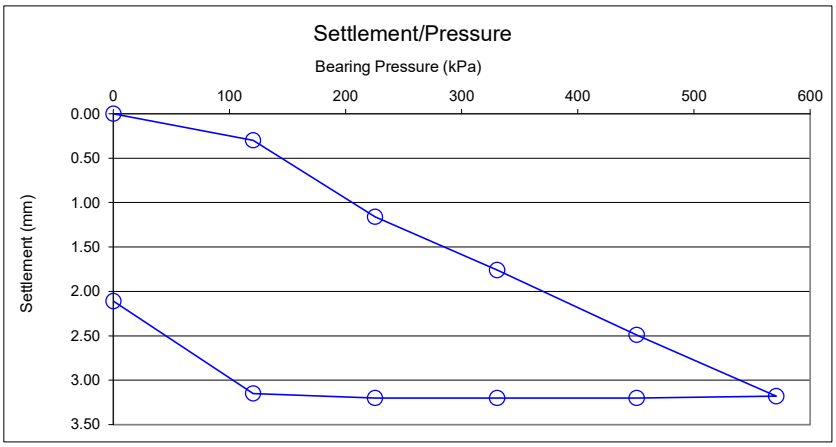


Plate Diameter	**600 mm**	Maximum Applied Pressure	**570.8 kPa**
Reaction Load	**28 T**	Maximum Settlement	**3.2 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Gibbon Street, Manchester

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Determination of Vertical Deformation - Plate Loading Test	Contract Test Reference:	DN3046/25C	**REPORT NO:**	**DNR/77974C**
BS1377: Part 9: 1990	Clients Reference:	**DN3046/25C**	Report Date:	23/06/2021

Material Description:	Type 1	Date Tested:	21/07/2021
Test Location:	PT42 B	Supplier/Source:	Not Stated
Weather:	Sunny		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
3.0	180.2	0.52
6.0	270.4	1.23
9.0	359.7	1.88
12.0	450.7	2.15
15.0	541.9	2.40
20.0	0.0	1.80

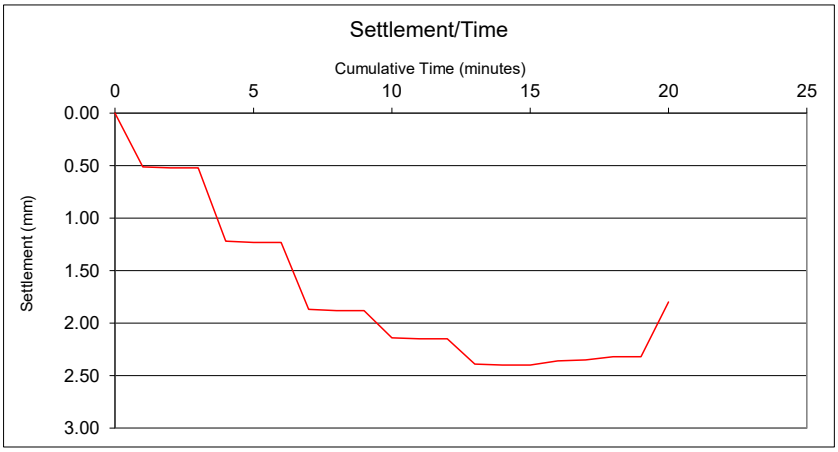

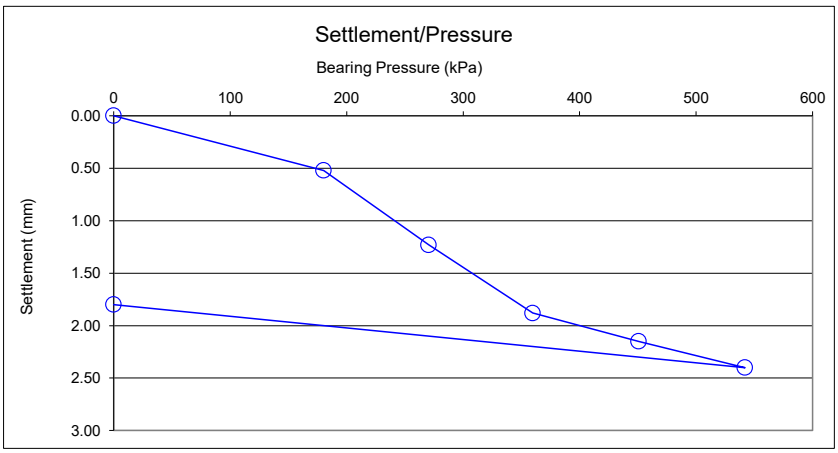


Plate Diameter	**600 mm**	Maximum Applied Pressure	**541.9 kPa**
Reaction Load	**Digger**	Maximum Settlement	**2.4 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/29 Clients Reference: DN3046/29E	**REPORT NO:** DNR/78604-B Report Date: 29/07/2021

Material Description:	Type 1	Date Tested:	28/07/2021
Test Location:	PT 43	Supplier/Source:	Maker/Manchester
Weather:	Wet		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	120.4	0.55
4.0	225.4	1.14
6.0	330.5	1.93
8.0	450.7	2.53
10.0	570.8	3.58
12.0	450.7	3.58
14.0	330.5	3.55
16.0	225.4	3.42
18.0	120.4	3.09
20.0	0.0	2.16

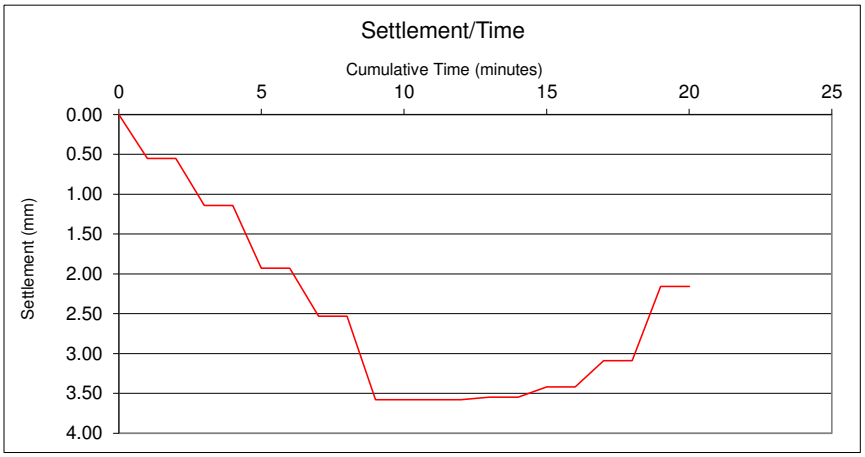

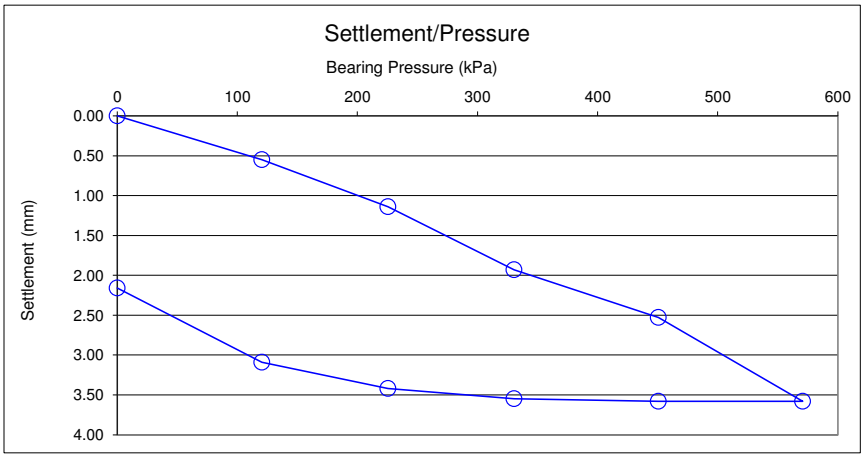


Plate Diameter	**600 mm**	Maximum Applied Pressure	**570.8 kPa**
Reaction Load	**28 T**	Maximum Settlement	**3.58 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/3C Clients Reference: **DN3046/3C**	**REPORT NO:** **DNR/64253C** Report Date: 14/04/2021

Material Description:	6F2/Mot	Date Tested:	13/04/2021
Test Location:	X7	Supplier/Source:	Not Stated
Weather:	Clear		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	36.3	1.59
4.0	142.6	2.82
6.0	326.1	3.96
8.0	435.1	5.09
10.0	544.4	6.03
12.0	435.1	5.15
14.0	326.1	4.29
16.0	142.6	2.27
18.0	36.3	1.59
20.0	0.0	1.04

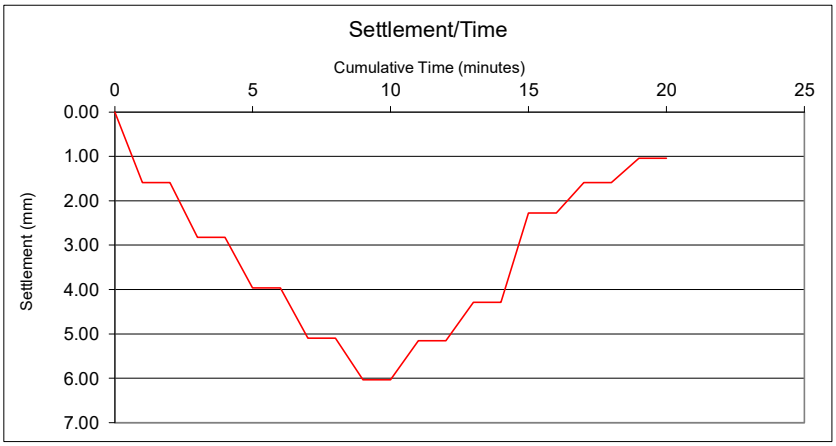

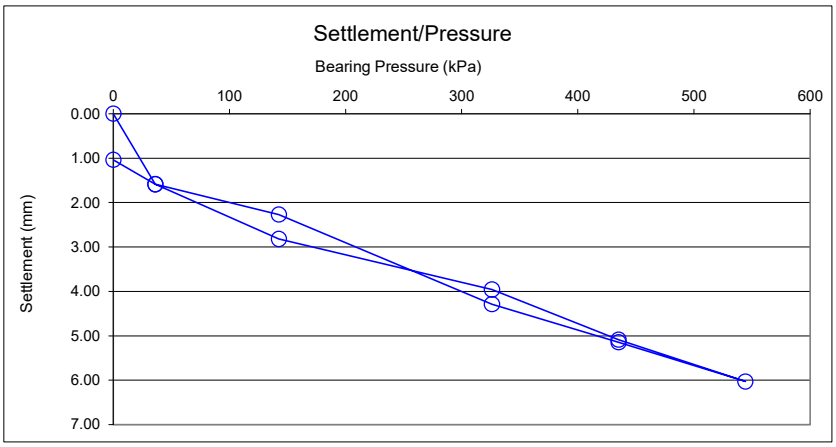


Plate Diameter	**600 mm**	Maximum Applied Pressure	**544.4 kPa**
Reaction Load	**33T**	Maximum Settlement	**6.03 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG


Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk

Gibbon Street, Manchester

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/3D Clients Reference: **DN3046/3D**	**REPORT NO:** **DNR/64253D** Report Date: 14/04/2021

Material Description:	6F2/Mot	Date Tested:	13/04/2021
Test Location:	X8	Supplier/Source:	Not Stated
Weather:	Clear		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	36.3	1.58
4.0	142.6	3.10
6.0	326.1	4.04
8.0	435.1	5.01
10.0	544.4	5.76
12.0	435.1	6.43
14.0	326.1	4.64
16.0	142.6	4.37
18.0	36.3	2.80
20.0	0.0	2.03

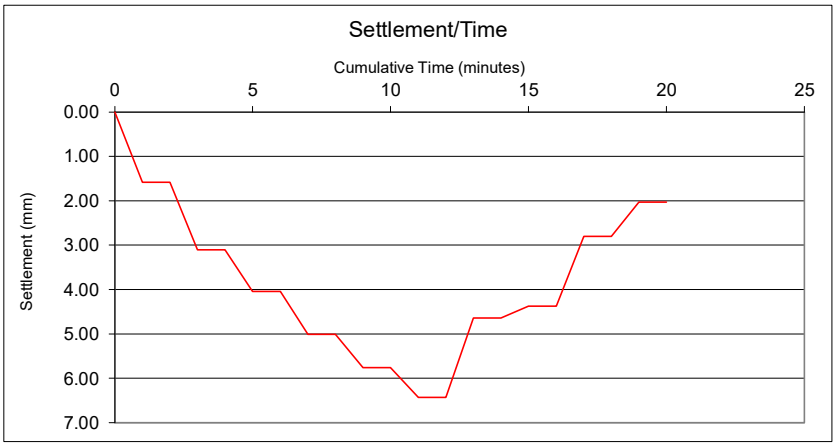

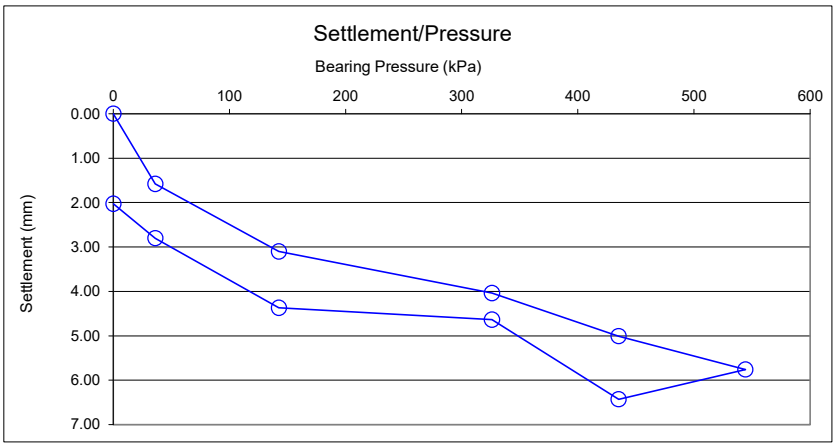


Plate Diameter	**600 mm**	Maximum Applied Pressure	**544.4 kPa**
Reaction Load	**33T**	Maximum Settlement	**6.43 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Template Version: 2.8

Authorised Signatory

J Williams - Field Services Manager

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Gibbon Street, Manchester

Construction Testing Solutions

Bootham Lane Industrial Estate
Dunscroft
Doncaster
DN7 4JU


Tel: (01302) 352652
Email: enquiries@constructiontesting.co.uk
Web: www.constructiontesting.co.uk

Determination of Vertical Deformation - Plate Loading Test BS1377: Part 9: 1990	Contract Test Reference: DN3046/41A Clients Reference: **DN3046/41A**	**REPORT NO: DNR/92374A** Report Date: 03/12/2021

TEST REPORT

Material Description:	Type 1	Date Tested:	02/12/2021
Test Location:	PLT 38	Supplier/Source:	Manchester/ Maher
Weather:	Wet		

Cumulative Time (minutes)	Mean Bearing Pressure kPa	Average Settlement (mm)
0.0	0.0	0
2.0	120.4	1.71
4.0	225.4	2.99
6.0	330.5	4.81
8.0	450.7	6.89
10.0	570.8	8.75
12.0	450.7	8.75
14.0	330.5	8.69
16.0	225.4	7.91
18.0	120.4	5.04
20.0	0.0	2.59

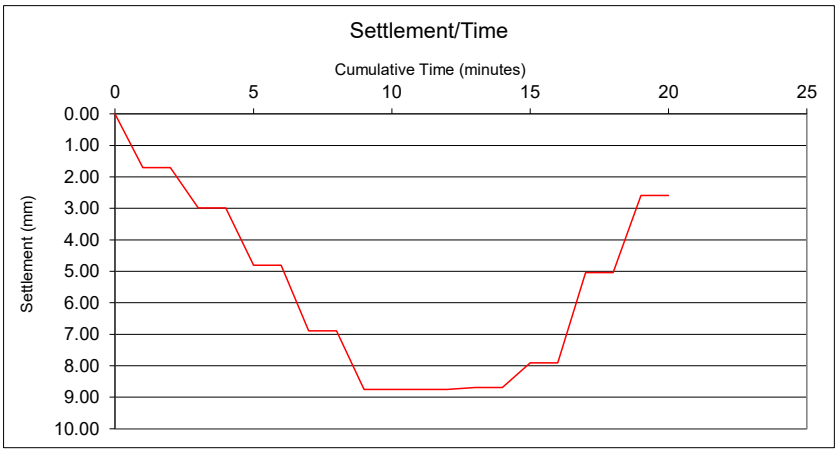

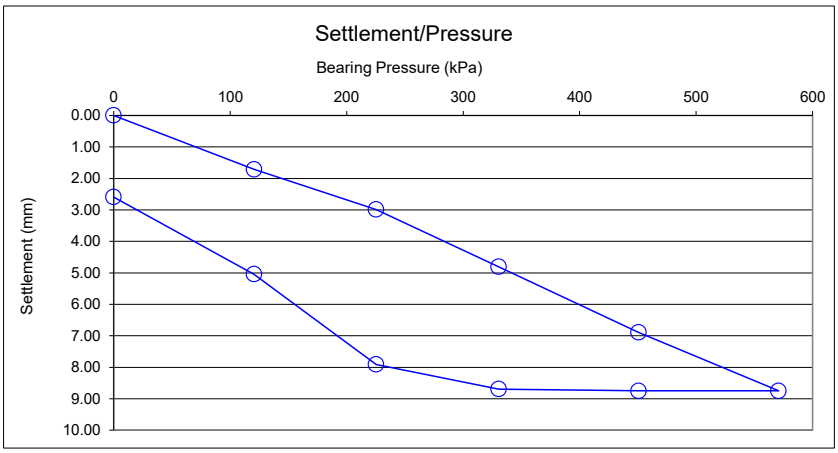


Plate Diameter	**600 mm**	Maximum Applied Pressure	**570.8 kPa**
Reaction Load	**26T**	Maximum Settlement	**8.75 mm**
Depth of Test	**Surface**	Moisture Content (BS1377: Part 2: 1990)	**Not Taken**
Distance from edge of plate to wall of excavation (mm)	**N/A**		

Results relate only to the sample(s) as tested.
This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.
The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.
Testing carried out at client's site location.

Authorised Signatory

Notes: 1 - One kPa is equivalent to One kN/m^2

Initial load applied by test equipment calculated to be less than 0.8 kN

Issue No: 3 Revision: 2	Page 1 of 4	Issue Date: May-19	Issued By: C Cowling	SAMPLE NO DN3046/25 A

TEST WORKSHEET - TEST PROCEDURE No 15

Determination Settlement of Soil Material - Incremental Plate Loading Test
BS 1377: Part 9: 1990

Construction Testing Solutions Ltd
Bentham Lane Industrial Estate
Bentham Lane, Owmersft
Doncaster, DN7 4JU

Material	TYPE 1	Client	PROVECTUS RMD CTD
Source	SITE WON	Site	GIBBON ST
Supplied		Location	PT 42
Plate Diameter	600 mm		
Test Ref	287	Date	21.7.21
Weather Conditions	SUNNY	Dipper Ref:	87
Depth of Test	N/A mm	Distance from edge of plate to wall of excavation:	N/A mm
Initial Seating Load Applied (tonne / Bar / PSI / kN):	0.27	Proctor Load:	

Note: Seating load must be the minimum detectable load given by the load measuring system

Pressure Gauge Reading Ton/PSI/Bar	Calibrated Load kN	Mean Bearing Pressure KN/m² (kPa)	Time Minutes	Dial Gauge Readings (x0.01mm) 1	2	3	Settlement (x0.01mm) 1	2	3	Mean Settlement (x0.01mm)
				202	238	249				
CYCLE 1										
3.0	25.50	90.19	1				38	52	12	
			/				38	52	12	
			/				38	52	12	34
			/							
			/							
6.0	50.95	180.20	1				45	60	16	
			/				45	60	16	
			/				45	60	16	40.3
			/							
			/							
9.0	76.46	270.44	1				71	91	23	
			/				71	92	24	
			/				71	92	24	62.3
			/							
			/							
12.0	101.71	359.74	1				108	142	43	
			/				109	143	44	
			/				109	143	45	99.0
			/							
15.0	127.43	450.68	/				140	195	63	
			1				140	196	63	
			/				141	196	63	183.3
			/							
			/							
			/							
18.0	153.23	541.96	1				176	247	88	
			/				176	248	89	
			/				176	248	89	171.0
			/							
			/							1.7
Q			15				174	245	85	168.0
										1.68
			12				172	240	80	164.0
										1.64
			9				170	240	81	163.7
										1.637
			6				167	238	79	161.3
			0				70	48	42	53.3

Tested By:		Checked By:	

Issue No: 3 Revision: 2	Page 2 of 4	Issue Date: May-19	Issued By: C Cowling	SAMPLE NO DN3046/25 (B)

TEST WORKSHEET - TEST PROCEDURE No 15

Determination Settlement of Soil Material - Incremental Plate Loading Test
BS 1377: Part 9: 1990

Construction Testing Solutions Ltd
Bootham Lane Industrial Estate
Bootham Lane, Dunsville
Doncaster, DN7 4JU

Material:	SANDY ~~BROWN CLAY~~ GRAVEL	Client:	PROVECTUS RMD LTD
Source:	SITE UNKNOWN	Site:	GIBRON ST
Supplier:	TYPE 1	Location:	PT 28
Plate Diameter:	600 mm		
Test Ref:	287	Date:	21.7.21
Weather Conditions:	SUNNY	Tyrer Ref:	87
Depth of Test:	N/A mm	Distance from edge of plate to wall of excavation:	N/A mm
Initial Seating Load Applied (Tonne / Bar / Psi /kN):	0.27	Reaction Load:	
		Note: Seating load must be the minimum detectable load given by the load measuring system	

Pressure Gauge Reading Ton/Psi/Bar	Calibrated Load kN	Mean Bearing Pressure kN/m² (kPa)	Time Minutes	Dial Gauge Readings (x0.01mm) 1	2	3	Settlement (x0.01mm) 1	2	3	Mean Settlement (x0.01mm)
				202	238	249				
CYCLE 1										
3.0	25.50	90.19	1							
			/							
			/							
			/							
			/							
6.0	50.95	180.20	1				24	39	50	
			/				25	40	50	
			/				25	40	50	38.3
			/							
			/							
9.0	76.46	270.44	1				48	64	82	
			/				49	65	83	
			/				50	65	83	66.0
			/							
			/							
12.0	101.71	359.74	1				118	168	140	
			/				120	165	140	
			/				121	168	140	143.0
			/							
15.0	127.43	450.68	/				156	217	183	
			1				155	217	183	
			/				155	218	183	185.3
			/							
			/							
			/							
			/							
18.0	153.23	541.96	1				184	264	226	
			/				186	265	228	
			/				186	265	228	226.3
			/							2.3
			/							
@	15T						~~188~~	264	228	226.7
	12T						180	262	222	221.3
	9T						180	254	222	218.7
	6T						180	238	219	212.3
	0						106	95	101	100.7

Tested By:		Checked By:	

Issue No: 3 Revision: 2	Page 3 of 4	Issue Date: May-19	Issued By: C Cowling	SAMPLE NO DN3046/25 (3)

TEST WORKSHEET - TEST PROCEDURE No 15

Determination Settlement of Soil Material - Incremental Plate Loading Test
BS 1377: Part 9: 1990

Construction Testing Solutions Ltd
Bretton Lane Industrial Estate
Bretton Lane, Dunscroft
Doncaster, DN7 4JU

TYPE 1

Material:	~~SANDY BROWN CLAY & STONE~~	Client:	PROVECTUS RMD LTD
Source:	~~SITE WON~~	Site:	GIBBON ST
Supplier:	SITE 1	Location:	PT 42 8
Plate Diameter:	600 mm		
Jack Ref:	287	Date: 21.7.21	Timer Ref: 87
Weather Conditions:		Distance from edge of plate to wall of excavation:	N/A mm
Depth of Test:	N/A mm	Reaction Load:	
Initial Seating Load Applied (Tonne / Bar / PSI /kN):	0.27	Note: Seating load must be the minimum controllable load given by the load measuring system	

Pressure Gauge Reading Ton/PSI/Bar	Calculated Load kN	Mean Bearing Pressure kN/m² (kPa)	Time Minutes	Dial Gauge Readings (x0.01mm) 1	2	3	Settlement (x0.01mm) 1	2	3	Mean Settlement (x0.01mm)
				202	238	249				
CYCLE 1										
3.0	25.50	90.19	1							
			/							
			/							
			/							
			/							
6.0	50.95	180.20	1				52	62	39	
			/				52	64	39	
			/				52	64	40	52
			/							
			/							
9.0	76.46	270.45	1				104	172	90	
			/				106	172	90	
			/				106	172	90	122.7
			/							
			/							
12.0	101.71	359.74	1				160	262	140	
			/				162	262	140	
			/				162	262	140	188.0
			/							
15.0	127.43	450.68	/				181	304	156	
			1				182	305	157	
			/				182	305	157	214.6
			/							
			/							
			/							
18.0	153.23	541.96	1				206	340	172	
			/				206	341	172	
			/				207	341	172	240.0
			/							
			/							2.4
RELEASE PRESS TO										
0	15						209	338	160	235.7
	12						208	337	160	235
	9						203	335	158	232.0
	6						203	335	158	232.0
	0						98	35	107	80.0

Tested By:		Checked By:	

Issue No: 3 Revision: 2	Page 4 of 4	Issue Date: May-19	Issued By: C Cowling	SAMPLE NO DN3046/25 (D)

TEST WORKSHEET - TEST PROCEDURE No 15

Determination Settlement of Soil Material - Incremental Plate Loading Test
BS 1377: Part 9: 1990

TYPE 1

Construction Testing Solutions Ltd
Bentham Lane Industrial Estate
Bentham Lane, Dunscroft
Doncaster, DN7 4AU

Material:	[redacted] TYPE 1	Client:	PROVECTUS RMD LTD		
Source:		Site:	GIBBON ST		
Supplier:	SITE 1	Location:	PT 13		
Plate Diameter:	600 mm				
Area Ref:	287	Date:	21.7.21	Timer Ref:	87
Weather Conditions:	SUNNY	Distance from edge of plate to wall of excavation:		N/A	mm
Depth of Test:	N/A mm	Position Load:			
Initial Seating Load Applied (Tonne / Bar / PSI / kN):	0.2T	Note: Seating load must be the minimum detectable load given by the load measuring system.			

Pressure Gauge Reading Ton/PSI/Bar	Calibrated Load kN	Mean Bearing Pressure kN/m² (kPa)	Time Minutes	Dial Gauge Readings (x0.01mm) 1	2	3	Settlement (x0.01mm) 1	2	3	Mean Settlement (x0.01mm)
				202	238	249				
CYCLE 1										
3.0	25.50	90.19	1							
			/							
			/							
			/							
			/							
6.0	50.95	180.20	1				120	148	134	
			/				120	148	134	/
			/				120	148	134	134
			/							134.0
			/							
9.0	76.46	270.44	1				248	330	288	
			/				248	330	288	
			/				250	330	288	289.3
			/							
			/							
12.0	101.71	359.74	1				356	474	402	
			/				357	474	404	
			/				357	475	404	412.0
			/							
15.0	127.43	450.68	/							
			1				435	582	490	
			/				436	583	492	
			/				437	583	493	504.3
			/							
			/							
18.0	153.23	541.96	1				502	672	502	
			/				503	674	504	
			/				504	675	505	561.3
			/							
			/							5.6
	RECOVERY PRESSURES									
0		15					508	677	569	584.7
		12					508	674	569	583.7
		9					500	659	503	554.0
		6					489	619	496	534.7
		0					330	350	370	353.3

Tested By:		Checked By:	

APPENDIX J Sample Tracker and Laboratory Test Results

Co-op Live! Sample Tracker

Suite	Date Sample Taken	No. Samples Taken	Sample ID	Sample Description
Dust	16/04/2021	4	BMP1, BMP2, BMP3, BMP4	
Soil	22/04/2021	5	SP2(6F2), B7.1, B7.2, NonHaz1, NonHaz	
Dust	14/05/2021	4	BMP1, BMP2, BMP3, BMP4	
Soil	15/06/2021	1	SP3	SP3 - Dark grey to black, loose, clayey, very sandy GRAVEL. Slight odour.
Dust	11/06/2021	4	BMP1, BMP2, BMP3, BMP4	
Soil	22/06/2021	1	HLM/A2	6F2, Loose, light brown, slightly sandy medium to corse GRAVEL
Stone re-use	05/07/2021	5	HLM/A3, HLM/A4, HLM/A5, HLM/A6, HLM/A7	HLM/A3, HLM/A4, HLM/A5- 6F5, Loose, brown, slightly sandy medium to corse GRAVEL, no odour HLM/A6, HLM/A7- 6F5, dense, dark brown, medium to corse GRAVEL, no odour, wet
Dust	09/07/2021	4	BMP1, BMP2, BMP3, BMP4	
Stone re-use	15/07/2021	1	HLM/G2	6F2, Loose, light brown, corse GRAVEL
Stone re-use	15/07/2021	1	TYPE1/A6	Type 1, Loose, brown, medium sandy GRAVEL
Water	04/08/2021	1	MTP_DIS/01	
Soil	10/08/2021	2	HLM/G2, HLM/G3	Type 1, Loose, brown, medium sandy GRAVEL
Dust	13/08/2021	4	BMP1, BMP2, BMP3, BMP4	
Stone re-use	07/09/2021	2	HLM/E7, HLM/F7	Type1/6f5
Soil	13/09/2021	1	SP7	
Stone re-use	15/09/2021	1	HLM/G7	Type1/6f5
Dust	17/09/2021	4	BMP1, BMP2, BMP3, BMP4	
Dust	15/10/2021	4	BMP1, BMP2, BMP3, BMP4	
Stone re-use	12/11/2021	2	LLMF2/01, LLMF2/02	Type1/6f5
Dust	12/11/2021	4	BMP1, BMP2, BMP3, BMP4	
Stone re-use	18/11/2021	2	SOUTHRAMP/01, SOUTHRAMP/02	6f5/type1/75mm

Co-op Live! Sample Tracker

Suite	Date Sample Taken	No. Samples Taken	Sample Descrpition
Soil	22/04/2021	2	PA1, PA2
Soil	27/04/2021	2	PA2/02, PA2/03
Soil	06/05/2021	2	PA3/01- Loose, grey, fine sandy GRAVEL, no odour PA3/02- Loose, brown, medium GRAVEL, slight hydrocarbon odour
Soil	10/05/2021	3	PA4/01- Medium dense, brown black, gravelly CLAY, no odour PA4/02- Loose, black, medium GRAVEL, slight hydrocarbon odour PA4/03- Medium dense, brown, fine sandy GRAVEL no odour
Soil	17/05/2021	2	PA5/01- Loose, light brown, fine sandy, GRAVEL, no odour PA5/02- Loose, brown grey, fine sandy GRAVEL, no odour
Soil	21/05/2021	3	PA6/01- Loose, brown, medium, GRAVEL, no odour PA6/02- Loose, brown, medium, GRAVEL, no odour PA6/03- Soft, light brown, sandy gravelly CLAY, no odour
Soil	28/05/2021	3	PA7/01- Loose, light brown, medium sandy GRAVEL, no odour PA7/02- Loose, light brown, medium sandy GRAVEL, no odour PA7/03 - Loose, light brown, medium sandy GRAVEL, no odour
Soil	02/06/2021	5	PA7/04- Loose, light brown/grey, medium SAND, no odour PA7/05- Loose, light brown, fine sandy GRAVEL, no odour PA7/06- Loose, light brown, fine sandy GRAVEL, no odour PA7/07- Loose, light brown, fine sandy GRAVEL, no odour PA7/08- Loose, brown, fine sandy GRAVEL, no odour
Soil	04/06/2021	2	PA8/01- Medium dense, light brown grey, sandy, medium GRAVEL, no odour PA8/02- Loose, brown, fine sandy GRAVEL, no odour
Soil	11/06/2021	2	PA9/01 - Greyish brown, loose, slightly gravelly, sandy CLAY. No odour. PA9/02 Brown to light brown, loose, slightly gravelly sandy CLAY. No odour.
Soil	18/06/2021	1	PA10/01- Loose, brown, sandy, medium GRAVEL, no odour
Soil	25/06/2021	1	PA11/01- Loose, brown, sandy medium GRAVEL, no odour
Soil	02/07/2021	1	PA12/01- Loose, dark brown, sandy medium GRAVEL, no odour
Soil	09/07/2021	1	PA13/01- Loose, dark brown, slightly sandy medium to corse GRAVEL, no odour.
Soil	16/07/2021	1	PA14/01- Loose, dark brown, slightly sandy, medium to corse GRAVEL, no odour
Soil	23/07/2021	2	PA15/01- Loose, light brown, slightly clayey, medium GRAVEL, no odour PA15/02- Loose, light brown, slightly clayey, medium GRAVEL, no odour
Soil	30/07/2021	2	PA16/01- Dense, brown, clayey, medium to corse GRAVEL, no odour, wet PA16/02- Dense, grey brown, clayey, medium to corse GRAVEL, no odour, wet
Soil	04/08/2021	2	PA17/01- Loose, grey, medium to corse GRAVEL, no odour PA17/02- Loose, dark brown, medium to corse, sandy GRAVEL, no odour
Soil	18/08/2021	2	PA18/01-Loose, light brown, medium to corse GRAVEL, no odour PA18/02- Loose, brown, medium to corse, slightly sandy GRAVEL, no odour
Soil	20/08/2021	2	PA19/01- Loose, light brown, fine to medium GRAVEL, no odour PA19/02- Loose, light brown, fine to medium GRAVEL, no odour, very wet
Soil	27/08/2021	2	PA20/01- Loose, grey, medium to corse GRAVEL, no odour PA20/02- Loose, grey, medium to corse GRAVEL, no odour
Soil	06/09/2021	4	PA20/03 - Loose brown, medium, slightly sandy GRAVEL, hydrocarbon odour PA21/01- Loose, dark brown, medium to corse, slightly sandy GRAVEL, no odour PA21/02 - Loose, light brown, fine to corse GRAVEL, no odour PA21/03- Loose, light brown, medium to corse GRAVEL, no odour
Soil	10/09/2021	2	PA22/01, PA22/02
Soil	17/09/2021	2	PA23/01, PA23/02
Soil	24/09/2021	2	PA24/01, PA24/02
Soil	01/10/2021	2	PA25/01, PA25/02
Soil	08/10/2021	2	PA26/01, PA26/02
Soil	15/10/2021	2	PA27/01, PA27/02
Soil	22/10/2021	2	PA28/01, PA28/02
Soil	16/11/2021	1	PA29/01
Soil	19/11/2021	1	PA30/01
Soil	26/11/2021	1	PA31/01

eurofins | Chemtest
Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

UKAS TESTING 2183

Final Report

Report No.:	21-19039-1
Initial Date of Issue:	11-Jun-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Sam Lane-Ryan
Project	101114 BAM Contruction Site
Quotation No.:	Q20-19287
Order No.:	9848
No. of Samples:	2
Turnaround (Wkdays):	5
Date Approved:	11-Jun-2021
Approved By:	
Details:	Glynn Harvey, Technical Manager

Date Received:	07-Jun-2021
Date Instructed:	07-Jun-2021
Results Due:	11-Jun-2021

Results - Soil

Project: 101114 BAM Contruction Site

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-19039	21-19039
Quotation No.: Q20-19287			**Chemtest Sample ID.:**		1215530	1215531
Order No.: 9848			Client Sample Ref.:		PA8/01	PA8/02
			Sample Location:		PA8	PA8
			Sample Type:		SOIL	SOIL
			Date Sampled:		04-Jun-2021	04-Jun-2021
			Asbestos Lab:		COVENTRY	COVENTRY
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
ACM Type	U	2192		N/A	-	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected	No Asbestos Detected
Moisture	N	2030	%	0.020	8.3	9.2
pH	U	2010		4.0	12.0	10.2
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	0.059	0.12
Sulphur (Elemental)	U	2180	mg/kg	1.0	4.9	8.8
Cyanide (Complex)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Sulphate (Total)	U	2430	%	0.010	0.61	0.16
Arsenic	U	2450	mg/kg	1.0	22	5.0
Cadmium	U	2450	mg/kg	0.10	0.58	0.18
Chromium	U	2450	mg/kg	1.0	19	15
Copper	U	2450	mg/kg	0.50	18	34
Mercury	U	2450	mg/kg	0.10	0.13	< 0.10
Nickel	U	2450	mg/kg	0.50	25	18
Lead	U	2450	mg/kg	0.50	32	30
Selenium	U	2450	mg/kg	0.20	< 0.20	< 0.20
Zinc	U	2450	mg/kg	0.50	48	58
LOI	U	2610	%	0.10	4.7	2.9
Total Organic Carbon	U	2625	%	0.20	1.4	0.74
Total TPH >C6-C40	U	2670	mg/kg	10	28	66
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0

Results - Soil

Project: 101114 BAM Contruction Site

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-19039	21-19039
Quotation No.: Q20-19287			**Chemtest Sample ID.:**		1215530	1215531
Order No.: 9848			Client Sample Ref.:		PA8/01	PA8/02
			Sample Location:		PA8	PA8
			Sample Type:		SOIL	SOIL
			Date Sampled:		04-Jun-2021	04-Jun-2021
			Asbestos Lab:		COVENTRY	COVENTRY
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	< 10	< 10
Naphthalene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Acenaphthylene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Acenaphthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Fluorene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Phenanthrene	U	2700	mg/kg	0.10	1.8	< 0.10
Anthracene	U	2700	mg/kg	0.10	0.41	< 0.10
Fluoranthene	U	2700	mg/kg	0.10	2.8	1.2
Pyrene	U	2700	mg/kg	0.10	3.1	1.3
Benzo[a]anthracene	U	2700	mg/kg	0.10	1.2	0.56
Chrysene	U	2700	mg/kg	0.10	0.94	0.50
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	1.2	< 0.10
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	0.25	< 0.10
Benzo[a]pyrene	U	2700	mg/kg	0.10	0.71	< 0.10
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Total Of 16 PAH's	U	2700	mg/kg	2.0	12	3.6
Benzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Total Phenols	U	2920	mg/kg	0.10	< 0.10	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 45 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com


Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-20183-1
Initial Date of Issue:	23-Jun-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Andy Clee Charlie Gould Jon Owens Sam Gould
Project	101114 Bam Construction Site, Sportcity Way, Manchester

Quotation No.:	Q20-19287	**Date Received:**	15-Jun-2021
Order No.:	9848	**Date Instructed:**	15-Jun-2021
No. of Samples:	2		
Turnaround (Wkdays):	5	**Results Due:**	21-Jun-2021
Date Approved:	23-Jun-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 Bam Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-20183	21-20183
Quotation No.: Q20-19287			**Chemtest Sample ID.:**		1220961	1220962
Order No.: 9848			Client Sample Ref.:		PA9/01	PA9/02
			Sample Location:		PA9	PA9
			Sample Type:		SOIL	SOIL
			Date Sampled:		11-Jun-2021	11-Jun-2021
			Asbestos Lab:		COVENTRY	COVENTRY
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
ACM Type	U	2192		N/A	-	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected	No Asbestos Detected
Moisture	N	2030	%	0.020	9.2	9.2
pH	U	2010		4.0	9.4	11.0
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	0.55	0.14
Sulphur (Elemental)	U	2180	mg/kg	1.0	42	3.4
Cyanide (Complex)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Sulphate (Total)	U	2430	%	0.010	0.23	0.13
Arsenic	U	2450	mg/kg	1.0	5.8	7.5
Cadmium	U	2450	mg/kg	0.10	0.17	0.38
Chromium	U	2450	mg/kg	1.0	20	22
Copper	U	2450	mg/kg	0.50	20	21
Mercury	U	2450	mg/kg	0.10	< 0.10	< 0.10
Nickel	U	2450	mg/kg	0.50	38	37
Lead	U	2450	mg/kg	0.50	17	13
Selenium	U	2450	mg/kg	0.20	0.45	0.24
Zinc	U	2450	mg/kg	0.50	55	78
LOI	U	2610	%	0.10	5.7	4.2
Total Organic Carbon	U	2625	%	0.20	1.8	0.86
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	4.6	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	4.3	< 1.0
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	33	< 1.0

Results - Soil

Project: 101114 Bam Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-20183	21-20183
Quotation No.: Q20-19287			**Chemtest Sample ID.:**		1220961	1220962
Order No.: 9848			Client Sample Ref.:		PA9/01	PA9/02
			Sample Location:		PA9	PA9
			Sample Type:		SOIL	SOIL
			Date Sampled:		11-Jun-2021	11-Jun-2021
			Asbestos Lab:		COVENTRY	COVENTRY
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	38	< 5.0
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	43	< 10
Naphthalene	U	2700	mg/kg	0.10	4.4	< 0.10
Acenaphthylene	U	2700	mg/kg	0.10	2.2	< 0.10
Acenaphthene	U	2700	mg/kg	0.10	1.2	< 0.10
Fluorene	U	2700	mg/kg	0.10	2.8	< 0.10
Phenanthrene	U	2700	mg/kg	0.10	23	< 0.10
Anthracene	U	2700	mg/kg	0.10	5.5	< 0.10
Fluoranthene	U	2700	mg/kg	0.10	21	0.32
Pyrene	U	2700	mg/kg	0.10	23	0.27
Benzo[a]anthracene	U	2700	mg/kg	0.10	7.9	< 0.10
Chrysene	U	2700	mg/kg	0.10	8.5	< 0.10
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	8.4	< 0.10
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	3.3	< 0.10
Benzo[a]pyrene	U	2700	mg/kg	0.10	7.1	< 0.10
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	4.8	< 0.10
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	1.3	< 0.10
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	5.3	< 0.10
Total Of 16 PAH's	U	2700	mg/kg	2.0	130	< 2.0
Benzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Total Phenols	U	2920	mg/kg	0.10	0.52	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com


Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-20573-1
Initial Date of Issue:	25-Jun-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Sam Lane-Ryan Charlotte Nicholson
Project	101114 Bam Construction Site, Sportcity Way, Manchester, M11

Quotation No.:	Q20-19287	**Date Received:**	17-Jun-2021
Order No.:	9848	**Date Instructed:**	17-Jun-2021
No. of Samples:	1		
Turnaround (Wkdays):	5	**Results Due:**	23-Jun-2021
Date Approved:	25-Jun-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 Bam Construction Site, Sportcity Way, Manchester, M11

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-20573
Quotation No.: Q20-19287			**Chemtest Sample ID.:**		1222937
Order No.: 9848			Client Sample Ref.:		SP3
			Sample Location:		SP3
			Sample Type:		SOIL
			Date Sampled:		15-Jun-2021
			Asbestos Lab:		DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**	
ACM Type	U	2192		N/A	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected
Moisture	N	2030	%	0.020	14
pH	U	2010		4.0	8.5
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	0.32
Sulphur (Elemental)	U	2180	mg/kg	1.0	40
Cyanide (Complex)	U	2300	mg/kg	0.50	0.60
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	0.60
Sulphate (Total)	U	2430	%	0.010	0.28
Arsenic	U	2450	mg/kg	1.0	31
Cadmium	U	2450	mg/kg	0.10	0.40
Chromium	U	2450	mg/kg	1.0	33
Copper	U	2450	mg/kg	0.50	110
Mercury	U	2450	mg/kg	0.10	0.53
Nickel	U	2450	mg/kg	0.50	32
Lead	U	2450	mg/kg	0.50	120
Selenium	U	2450	mg/kg	0.20	1.1
Zinc	U	2450	mg/kg	0.50	100
LOI	U	2610	%	0.10	15
Total Organic Carbon	U	2625	%	0.20	11
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	81
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0

Results - Soil

Project: 101114 Bam Construction Site, Sportcity Way, Manchester, M11

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-20573
Quotation No.: Q20-19287			**Chemtest Sample ID.:**		1222937
Order No.: 9848			Client Sample Ref.:		SP3
			Sample Location:		SP3
			Sample Type:		SOIL
			Date Sampled:		15-Jun-2021
			Asbestos Lab:		DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**	
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	81
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	81
Naphthalene	U	2700	mg/kg	0.10	2.6
Acenaphthylene	U	2700	mg/kg	0.10	1.8
Acenaphthene	U	2700	mg/kg	0.10	3.4
Fluorene	U	2700	mg/kg	0.10	3.6
Phenanthrene	U	2700	mg/kg	0.10	23
Anthracene	U	2700	mg/kg	0.10	5.8
Fluoranthene	U	2700	mg/kg	0.10	24
Pyrene	U	2700	mg/kg	0.10	28
Benzo[a]anthracene	U	2700	mg/kg	0.10	12
Chrysene	U	2700	mg/kg	0.10	15
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	13
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	5.4
Benzo[a]pyrene	U	2700	mg/kg	0.10	11
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	7.2
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	2.2
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	7.4
Total Of 16 PAH's	U	2700	mg/kg	2.0	170
Benzene	U	2760	µg/kg	1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0
Total Phenols	U	2920	mg/kg	0.10	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com


Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-13378-1
Initial Date of Issue:	30-Apr-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Sam Lane-Ryan Charlotte Nicholson
Project	101114 BAM Construction Site, Sportcity Way, Manchester

Quotation No.:		**Date Received:**	23-Apr-2021
Order No.:	9848	**Date Instructed:**	23-Apr-2021
No. of Samples:	6		
Turnaround (Wkdays):	5	**Results Due:**	29-Apr-2021
Date Approved:	30-Apr-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd				**Chemtest Job No.:**	21-13378	21-13378	21-13378	21-13378	21-13378	21-13378
Quotation No.:				**Chemtest Sample ID.:**	1186229	1186230	1186231	1186232	1186233	1186234
				Client Sample ID.:	PA1	PA2	B7.1	B7.2	NON HAZ 1	NON HAZ 2
				Sample Location:	PA1	PA2	B7.1	B7.2	NON HAZ 1	NON HAZ 2
				Sample Type:	SOIL	SOIL	SOIL	SOIL	SOIL	SOIL
				Date Sampled:	22-Apr-2021	22-Apr-2021	22-Apr-2021	22-Apr-2021	22-Apr-2021	22-Apr-2021
				Asbestos Lab:	COVENTRY	COVENTRY	COVENTRY	COVENTRY	COVENTRY	COVENTRY
Determinand	**Accred.**	**SOP**	**Units**	**LOD**						
ACM Type	U	2192		N/A	-	-	-	-	-	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected	No Asbestos Detected	No Asbestos Detected	No Asbestos Detected	No Asbestos Detected	No Asbestos Detected
ACM Detection Stage	U	2192		N/A	-	-	-	-	-	-
Moisture	N	2030	%	0.020	12	5.0	7.2	17	10	12
pH	M	2010		4.0	9.7	9.5	8.5	8.3	9.8	9.2
Sulphate (2:1 Water Soluble) as SO4	M	2120	g/l	0.010	0.079	0.035	0.11	0.061	0.025	0.057
Sulphur (Elemental)	M	2180	mg/kg	1.0	95	4.3	27	49	7.1	65
Cyanide (Complex)	M	2300	mg/kg	0.50	7.5	1.4	14	11	4.9	8.6
Cyanide (Free)	M	2300	mg/kg	0.50	< 0.50	< 0.50	< 0.50	< 0.50	< 0.50	< 0.50
Cyanide (Total)	M	2300	mg/kg	0.50	7.5	1.4	14	11	4.9	8.9
Sulphate (Total)	M	2430	%	0.010	0.52	0.24	0.31	0.47	0.24	0.67
Arsenic	M	2450	mg/kg	1.0	41	13	48	120	16	43
Cadmium	M	2450	mg/kg	0.10	0.52	0.46	0.31	0.44	0.57	0.57
Chromium	M	2450	mg/kg	1.0	23	21	24	41	35	33
Copper	M	2450	mg/kg	0.50	87	49	140	300	72	170
Mercury	M	2450	mg/kg	0.10	0.99	0.16	0.94	2.5	0.51	1.4
Nickel	M	2450	mg/kg	0.50	48	25	31	79	31	44
Lead	M	2450	mg/kg	0.50	110	59	340	800	220	380
Selenium	M	2450	mg/kg	0.20	1.1	0.22	0.56	1.1	0.26	0.66
Zinc	M	2450	mg/kg	0.50	100	91	170	340	120	210
LOI	M	2610	%	0.10	6.6	3.4	13	21	5.1	11
Total Organic Carbon	M	2625	%	0.20	7.0	1.2	9.8	17	3.0	7.8
Total TPH >C6-C40	M	2670	mg/kg	10	260	120	870	100	260	4500
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C8-C10	M	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C10-C12	M	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C12-C16	M	2680	mg/kg	1.0	< 1.0	< 1.0	9.9	< 1.0	< 1.0	7.7
Aliphatic TPH >C16-C21	M	2680	mg/kg	1.0	< 1.0	< 1.0	18	< 1.0	< 1.0	11
Aliphatic TPH >C21-C35	M	2680	mg/kg	1.0	45	38	92	< 1.0	66	63
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	45	38	120	< 5.0	66	81
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C8-C10	M	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C10-C12	M	2680	mg/kg	1.0	< 1.0	< 1.0	18	< 1.0	< 1.0	8.8
Aromatic TPH >C12-C16	M	2680	mg/kg	1.0	18	< 1.0	58	6.9	17	42

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-13378	21-13378	21-13378	21-13378	21-13378	21-13378
Quotation No.:			**Chemtest Sample ID.:**		1186229	1186230	1186231	1186232	1186233	1186234
			Client Sample ID.:		PA1	PA2	B7.1	B7.2	NON HAZ 1	NON HAZ 2
			Sample Location:		PA1	PA2	B7.1	B7.2	NON HAZ 1	NON HAZ 2
			Sample Type:		SOIL	SOIL	SOIL	SOIL	SOIL	SOIL
			Date Sampled:		22-Apr-2021	22-Apr-2021	22-Apr-2021	22-Apr-2021	22-Apr-2021	22-Apr-2021
			Asbestos Lab:		COVENTRY	COVENTRY	COVENTRY	COVENTRY	COVENTRY	COVENTRY
Determinand	**Accred.**	**SOP**	**Units**	**LOD**						
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	23	14	140	16	60	150
Aromatic TPH >C21-C35	M	2680	mg/kg	1.0	150	140	540	100	300	500
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	190	150	760	120	370	700
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	240	190	880	120	440	780
Naphthalene	M	2700	mg/kg	0.10	1.1	0.77	8.5	3.0	0.97	3.7
Acenaphthylene	M	2700	mg/kg	0.10	1.1	0.36	1.0	0.95	0.41	1.2
Acenaphthene	M	2700	mg/kg	0.10	0.95	0.62	5.2	2.9	1.1	5.0
Fluorene	M	2700	mg/kg	0.10	1.3	0.60	5.2	2.7	1.0	4.9
Phenanthrene	M	2700	mg/kg	0.10	6.7	3.7	30	15	5.9	18
Anthracene	M	2700	mg/kg	0.10	1.6	0.84	6.9	< 0.10	1.6	5.2
Fluoranthene	M	2700	mg/kg	0.10	9.0	4.4	29	16	7.7	20
Pyrene	M	2700	mg/kg	0.10	10	4.9	31	17	8.2	21
Benzo[a]anthracene	M	2700	mg/kg	0.10	4.2	1.8	11	7.3	3.1	8.9
Chrysene	M	2700	mg/kg	0.10	4.4	2.1	12	8.0	3.7	9.8
Benzo[b]fluoranthene	M	2700	mg/kg	0.10	4.8	2.6	12	8.7	4.3	8.2
Benzo[k]fluoranthene	M	2700	mg/kg	0.10	2.1	1.3	5.9	4.4	1.9	4.4
Benzo[a]pyrene	M	2700	mg/kg	0.10	4.8	2.0	11	7.0	3.3	8.2
Indeno(1,2,3-c,d)Pyrene	M	2700	mg/kg	0.10	3.9	1.4	7.6	4.4	2.5	5.7
Dibenz(a,h)Anthracene	M	2700	mg/kg	0.10	2.0	0.46	1.8	1.5	0.29	0.96
Benzo[g,h,i]perylene	M	2700	mg/kg	0.10	4.1	1.6	7.7	4.6	2.6	5.7
Total Of 16 PAH's	M	2700	mg/kg	2.0	62	30	190	100	49	130
Benzene	M	2760	µg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Toluene	M	2760	µg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Ethylbenzene	M	2760	µg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
m & p-Xylene	M	2760	µg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
o-Xylene	M	2760	µg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Total Phenols	M	2920	mg/kg	0.10	< 0.10	0.10	< 0.10	< 0.10	0.14	0.14

Results - Single Stage WAC

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

					Landfill Waste Acceptance Criteria Limits		
Chemtest Job No:	21-13378						
Chemtest Sample ID:	1186229						
Sample Ref:							
Sample ID:	PA1						
Sample Location:	PA1						
Top Depth(m):							
Bottom Depth(m):							
Sampling Date:	22-Apr-2021						
Determinand	**SOP**	**Accred.**	**Units**		**Inert Waste Landfill**	**Stable, Non-reactive hazardous waste in non-hazardous Landfill**	**Hazardous Waste Landfill**
Total Organic Carbon	2625	M	%	7.0	3	5	6
Loss On Ignition	2610	M	%	6.6	--	--	10
Total BTEX	2760	M	mg/kg	< 0.010	6	--	--
Total PCBs (7 Congeners)	2815	M	mg/kg	< 0.10	1	--	--
TPH Total WAC (Mineral Oil)	2670	M	mg/kg	260	500	--	--
Total (Of 17) PAH's	2700	N	mg/kg	62	100	--	--
pH	2010	M		9.7	--	>6	--
Acid Neutralisation Capacity	2015	N	mol/kg	0.017	--	To evaluate	To evaluate
Eluate Analysis			**10:1 Eluate mg/l**	**10:1 Eluate mg/kg**	**Limit values for compliance leaching test using BS EN 12457 at L/S 10 l/kg**		
Arsenic	1455	U	0.011	0.11	0.5	2	25
Barium	1455	U	0.011	0.11	20	100	300
Cadmium	1455	U	< 0.00012	< 0.0012	0.04	1	5
Chromium	1455	U	0.0017	0.017	0.5	10	70
Copper	1455	U	0.0043	0.043	2	50	100
Mercury	1455	U	< 0.00005	< 0.00005	0.01	0.2	2
Molybdenum	1455	U	0.068	0.68	0.5	10	30
Nickel	1455	U	0.0016	0.016	0.4	10	40
Lead	1455	U	< 0.0005	< 0.0005	0.5	10	50
Antimony	1455	U	0.0054	0.054	0.06	0.7	5
Selenium	1455	U	0.0057	0.057	0.1	0.5	7
Zinc	1455	U	< 0.003	< 0.003	4	50	200
Chloride	1220	U	5.5	55	800	15000	25000
Fluoride	1220	U	0.58	5.8	10	150	500
Sulphate	1220	U	75	750	1000	20000	50000
Total Dissolved Solids	1020	N	170	1700	4000	60000	100000
Phenol Index	1920	U	< 0.030	< 0.30	1	-	-
Dissolved Organic Carbon	1610	U	5.3	53	500	800	1000

Solid Information	
Dry mass of test portion/kg	0.090
Moisture (%)	12

Waste Acceptance Criteria

Landfill WAC analysis (specifically leaching test results) must not be used for hazardous waste classification purposes. This analysis is only applicable for hazardous waste landfill acceptance and does not give any indication as to whether a waste may be hazardous or non-hazardous.

Results - Single Stage WAC

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

					Landfill Waste Acceptance Criteria Limits		
Chemtest Job No:	21-13378						
Chemtest Sample ID:	1186230						
Sample Ref:							
Sample ID:	PA2						
Sample Location:	PA2						
Top Depth(m):							
Bottom Depth(m):							
Sampling Date:	22-Apr-2021						
Determinand	**SOP**	**Accred.**	**Units**		**Inert Waste Landfill**	**Stable, Non-reactive hazardous waste in non-hazardous Landfill**	**Hazardous Waste Landfill**
Total Organic Carbon	2625	M	%	1.2	3	5	6
Loss On Ignition	2610	M	%	3.4	--	--	10
Total BTEX	2760	M	mg/kg	< 0.010	6	--	--
Total PCBs (7 Congeners)	2815	M	mg/kg	< 0.10	1	--	--
TPH Total WAC (Mineral Oil)	2670	M	mg/kg	120	500	--	--
Total (Of 17) PAH's	2700	N	mg/kg	30	100	--	--
pH	2010	M		9.5	--	>6	--
Acid Neutralisation Capacity	2015	N	mol/kg	0.017	--	To evaluate	To evaluate
Eluate Analysis			**10:1 Eluate mg/l**	**10:1 Eluate mg/kg**	**Limit values for compliance leaching test using BS EN 12457 at L/S 10 l/kg**		
Arsenic	1455	U	0.0064	0.064	0.5	2	25
Barium	1455	U	0.011	0.11	20	100	300
Cadmium	1455	U	< 0.00012	< 0.0012	0.04	1	5
Chromium	1455	U	0.0014	0.014	0.5	10	70
Copper	1455	U	0.0034	0.034	2	50	100
Mercury	1455	U	< 0.00005	< 0.00005	0.01	0.2	2
Molybdenum	1455	U	0.011	0.11	0.5	10	30
Nickel	1455	U	0.0010	0.010	0.4	10	40
Lead	1455	U	< 0.0005	< 0.0005	0.5	10	50
Antimony	1455	U	0.0033	0.033	0.06	0.7	5
Selenium	1455	U	0.0016	0.016	0.1	0.5	7
Zinc	1455	U	< 0.003	< 0.003	4	50	200
Chloride	1220	U	3.2	32	800	15000	25000
Fluoride	1220	U	0.34	3.4	10	150	500
Sulphate	1220	U	58	580	1000	20000	50000
Total Dissolved Solids	1020	N	140	1400	4000	60000	100000
Phenol Index	1920	U	< 0.030	< 0.30	1	-	-
Dissolved Organic Carbon	1610	U	5.2	52	500	800	1000

Solid Information	
Dry mass of test portion/kg	0.090
Moisture (%)	5.0

Waste Acceptance Criteria

Landfill WAC analysis (specifically leaching test results) must not be used for hazardous waste classification purposes. This analysis is only applicable for hazardous waste landfill acceptance and does not give any indication as to whether a waste may be hazardous or non-hazardous.

Results - Single Stage WAC

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

					Landfill Waste Acceptance Criteria Limits		
Chemtest Job No:	21-13378						
Chemtest Sample ID:	1186231						
Sample Ref:							
Sample ID:	B7.1						
Sample Location:	B7.1						
Top Depth(m):							
Bottom Depth(m):							
Sampling Date:	22-Apr-2021						
Determinand	**SOP**	**Accred.**	**Units**		**Inert Waste Landfill**	**Stable, Non-reactive hazardous waste in non-hazardous Landfill**	**Hazardous Waste Landfill**
Total Organic Carbon	2625	M	%	9.8	3	5	6
Loss On Ignition	2610	M	%	13	--	--	10
Total BTEX	2760	M	mg/kg	< 0.010	6	--	--
Total PCBs (7 Congeners)	2815	M	mg/kg	< 0.10	1	--	--
TPH Total WAC (Mineral Oil)	2670	M	mg/kg	870	500	--	--
Total (Of 17) PAH's	2700	N	mg/kg	190	100	--	--
pH	2010	M		8.5	--	>6	--
Acid Neutralisation Capacity	2015	N	mol/kg	0.0070	--	To evaluate	To evaluate
Eluate Analysis			**10:1 Eluate mg/l**	**10:1 Eluate mg/kg**	**Limit values for compliance leaching test using BS EN 12457 at L/S 10 l/kg**		
Arsenic	1455	U	0.0038	0.038	0.5	2	25
Barium	1455	U	0.034	0.34	20	100	300
Cadmium	1455	U	< 0.00012	< 0.0012	0.04	1	5
Chromium	1455	U	< 0.0005	< 0.0005	0.5	10	70
Copper	1455	U	0.010	0.10	2	50	100
Mercury	1455	U	< 0.00005	< 0.00005	0.01	0.2	2
Molybdenum	1455	U	0.037	0.37	0.5	10	30
Nickel	1455	U	0.0031	0.031	0.4	10	40
Lead	1455	U	< 0.0005	< 0.0005	0.5	10	50
Antimony	1455	U	0.0073	0.073	0.06	0.7	5
Selenium	1455	U	0.0016	0.016	0.1	0.5	7
Zinc	1455	U	< 0.003	< 0.003	4	50	200
Chloride	1220	U	7.5	75	800	15000	25000
Fluoride	1220	U	0.31	3.1	10	150	500
Sulphate	1220	U	120	1200	1000	20000	50000
Total Dissolved Solids	1020	N	270	2700	4000	60000	100000
Phenol Index	1920	U	< 0.030	< 0.30	1	-	-
Dissolved Organic Carbon	1610	U	6.9	69	500	800	1000

Solid Information	
Dry mass of test portion/kg	0.090
Moisture (%)	7.2

Waste Acceptance Criteria

Landfill WAC analysis (specifically leaching test results) must not be used for hazardous waste classification purposes. This analysis is only applicable for hazardous waste landfill acceptance and does not give any indication as to whether a waste may be hazardous or non-hazardous.

Results - Single Stage WAC

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

					Landfill Waste Acceptance Criteria Limits		
Chemtest Job No:	21-13378						
Chemtest Sample ID:	1186232						
Sample Ref:							
Sample ID:	B7.2						
Sample Location:	B7.2						
Top Depth(m):							
Bottom Depth(m):							
Sampling Date:	22-Apr-2021						
Determinand	**SOP**	**Accred.**	**Units**		**Inert Waste Landfill**	**Stable, Non-reactive hazardous waste in non-hazardous Landfill**	**Hazardous Waste Landfill**
Total Organic Carbon	2625	M	%	17	3	5	6
Loss On Ignition	2610	M	%	21	--	--	10
Total BTEX	2760	M	mg/kg	< 0.010	6	--	--
Total PCBs (7 Congeners)	2815	M	mg/kg	< 0.10	1	--	--
TPH Total WAC (Mineral Oil)	2670	M	mg/kg	100	500	--	--
Total (Of 17) PAH's	2700	N	mg/kg	100	100	--	--
pH	2010	M		8.3	--	>6	--
Acid Neutralisation Capacity	2015	N	mol/kg	0.0090	--	To evaluate	To evaluate
Eluate Analysis			**10:1 Eluate mg/l**	**10:1 Eluate mg/kg**	**Limit values for compliance leaching test using BS EN 12457 at L/S 10 l/kg**		
Arsenic	1455	U	0.0023	0.023	0.5	2	25
Barium	1455	U	0.043	0.43	20	100	300
Cadmium	1455	U	< 0.00012	< 0.0012	0.04	1	5
Chromium	1455	U	< 0.0005	< 0.0005	0.5	10	70
Copper	1455	U	0.0017	0.017	2	50	100
Mercury	1455	U	< 0.00005	< 0.00005	0.01	0.2	2
Molybdenum	1455	U	0.018	0.17	0.5	10	30
Nickel	1455	U	0.0005	0.0053	0.4	10	40
Lead	1455	U	< 0.0005	< 0.0005	0.5	10	50
Antimony	1455	U	0.0031	0.031	0.06	0.7	5
Selenium	1455	U	0.0011	0.011	0.1	0.5	7
Zinc	1455	U	< 0.003	< 0.003	4	50	200
Chloride	1220	U	2.7	27	800	15000	25000
Fluoride	1220	U	0.29	2.9	10	150	500
Sulphate	1220	U	79	790	1000	20000	50000
Total Dissolved Solids	1020	N	220	2200	4000	60000	100000
Phenol Index	1920	U	< 0.030	< 0.30	1	-	-
Dissolved Organic Carbon	1610	U	2.6	< 50	500	800	1000

Solid Information	
Dry mass of test portion/kg	0.090
Moisture (%)	17

Waste Acceptance Criteria

Landfill WAC analysis (specifically leaching test results) must not be used for hazardous waste classification purposes. This analysis is only applicable for hazardous waste landfill acceptance and does not give any indication as to whether a waste may be hazardous or non-hazardous.

Results - Single Stage WAC

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

					Landfill Waste Acceptance Criteria Limits		
Chemtest Job No:	21-13378						
Chemtest Sample ID:	1186233						
Sample Ref:							
Sample ID:	NON HAZ 1						
Sample Location:	NON HAZ 1						
Top Depth(m):							
Bottom Depth(m):							
Sampling Date:	22-Apr-2021						
Determinand	**SOP**	**Accred.**	**Units**		**Inert Waste Landfill**	**Stable, Non-reactive hazardous waste in non-hazardous Landfill**	**Hazardous Waste Landfill**
Total Organic Carbon	2625	M	%	3.0	3	5	6
Loss On Ignition	2610	M	%	5.1	--	--	10
Total BTEX	2760	M	mg/kg	< 0.010	6	--	--
Total PCBs (7 Congeners)	2815	M	mg/kg	< 0.10	1	--	--
TPH Total WAC (Mineral Oil)	2670	M	mg/kg	260	500	--	--
Total (Of 17) PAH's	2700	N	mg/kg	49	100	--	--
pH	2010	M		9.8	--	>6	--
Acid Neutralisation Capacity	2015	N	mol/kg	0.025	--	To evaluate	To evaluate
Eluate Analysis			**10:1 Eluate mg/l**	**10:1 Eluate mg/kg**	**Limit values for compliance leaching test using BS EN 12457 at L/S 10 l/kg**		
Arsenic	1455	U	0.0088	0.088	0.5	2	25
Barium	1455	U	0.009	0.088	20	100	300
Cadmium	1455	U	< 0.00012	< 0.0012	0.04	1	5
Chromium	1455	U	0.0011	0.011	0.5	10	70
Copper	1455	U	0.025	0.25	2	50	100
Mercury	1455	U	< 0.00005	< 0.00005	0.01	0.2	2
Molybdenum	1455	U	0.013	0.13	0.5	10	30
Nickel	1455	U	0.013	0.13	0.4	10	40
Lead	1455	U	< 0.0005	< 0.0005	0.5	10	50
Antimony	1455	U	0.0079	0.079	0.06	0.7	5
Selenium	1455	U	0.0024	0.024	0.1	0.5	7
Zinc	1455	U	< 0.003	< 0.003	4	50	200
Chloride	1220	U	2.4	24	800	15000	25000
Fluoride	1220	U	0.33	3.3	10	150	500
Sulphate	1220	U	41	410	1000	20000	50000
Total Dissolved Solids	1020	N	170	1700	4000	60000	100000
Phenol Index	1920	U	< 0.030	< 0.30	1	-	-
Dissolved Organic Carbon	1610	U	7.6	76	500	800	1000

Solid Information	
Dry mass of test portion/kg	0.090
Moisture (%)	10

Waste Acceptance Criteria

Landfill WAC analysis (specifically leaching test results) must not be used for hazardous waste classification purposes. This analysis is only applicable for hazardous waste landfill acceptance and does not give any indication as to whether a waste may be hazardous or non-hazardous.

Results - Single Stage WAC

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

					Landfill Waste Acceptance Criteria Limits		
Chemtest Job No:	21-13378						
Chemtest Sample ID:	1186234						
Sample Ref:							
Sample ID:	NON HAZ 2						
Sample Location:	NON HAZ 2						
Top Depth(m):							
Bottom Depth(m):							
Sampling Date:	22-Apr-2021						
Determinand	**SOP**	**Accred.**	**Units**		**Inert Waste Landfill**	**Stable, Non-reactive hazardous waste in non-hazardous Landfill**	**Hazardous Waste Landfill**
Total Organic Carbon	2625	M	%	7.8	3	5	6
Loss On Ignition	2610	M	%	11	--	--	10
Total BTEX	2760	M	mg/kg	< 0.010	6	--	--
Total PCBs (7 Congeners)	2815	M	mg/kg	< 0.10	1	--	--
TPH Total WAC (Mineral Oil)	2670	M	mg/kg	4500	500	--	--
Total (Of 17) PAH's	2700	N	mg/kg	130	100	--	--
pH	2010	M		9.2	--	>6	--
Acid Neutralisation Capacity	2015	N	mol/kg	0.012	--	To evaluate	To evaluate
Eluate Analysis			**10:1 Eluate mg/l**	**10:1 Eluate mg/kg**	**Limit values for compliance leaching test using BS EN 12457 at L/S 10 l/kg**		
Arsenic	1455	U	0.018	0.18	0.5	2	25
Barium	1455	U	0.013	0.13	20	100	300
Cadmium	1455	U	< 0.00012	< 0.0012	0.04	1	5
Chromium	1455	U	0.0007	0.0072	0.5	10	70
Copper	1455	U	0.023	0.23	2	50	100
Mercury	1455	U	< 0.00005	< 0.00005	0.01	0.2	2
Molybdenum	1455	U	0.027	0.26	0.5	10	30
Nickel	1455	U	0.0085	0.085	0.4	10	40
Lead	1455	U	< 0.0005	< 0.0005	0.5	10	50
Antimony	1455	U	0.013	0.13	0.06	0.7	5
Selenium	1455	U	0.0035	0.035	0.1	0.5	7
Zinc	1455	U	< 0.003	< 0.003	4	50	200
Chloride	1220	U	5.0	50	800	15000	25000
Fluoride	1220	U	0.50	5.0	10	150	500
Sulphate	1220	U	84	840	1000	20000	50000
Total Dissolved Solids	1020	N	180	1800	4000	60000	100000
Phenol Index	1920	U	< 0.030	< 0.30	1	-	-
Dissolved Organic Carbon	1610	U	9.5	95	500	800	1000

Solid Information	
Dry mass of test portion/kg	0.090
Moisture (%)	12

Waste Acceptance Criteria

Landfill WAC analysis (specifically leaching test results) must not be used for hazardous waste classification purposes. This analysis is only applicable for hazardous waste landfill acceptance and does not give any indication as to whether a waste may be hazardous or non-hazardous.

Test Methods

SOP	Title	Parameters included	Method summary
1020	Electrical Conductivity and Total Dissolved Solids (TDS) in Waters	Electrical Conductivity and Total Dissolved Solids (TDS) in Waters	Conductivity Meter
1220	Anions, Alkalinity & Ammonium in Waters	Fluoride; Chloride; Nitrite; Nitrate; Total; Oxidisable Nitrogen (TON); Sulfate; Phosphate; Alkalinity; Ammonium	Automated colorimetric analysis using 'Aquakem 600' Discrete Analyser.
1455	Metals in Waters by ICP-MS	Metals, including: Antimony; Arsenic; Barium; Beryllium; Boron; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Tin; Vanadium; Zinc	Filtration of samples followed by direct determination by inductively coupled plasma mass spectrometry (ICP-MS).
1610	Total/Dissolved Organic Carbon in Waters	Organic Carbon	TOC Analyser using Catalytic Oxidation
1920	Phenols in Waters by HPLC	Phenolic compounds including: Phenol, Cresols, Xylenols, Trimethylphenols Note: Chlorophenols are excluded.	Determination by High Performance Liquid Chromatography (HPLC) using electrochemical detection.
2010	pH Value of Soils	pH	pH Meter
2015	Acid Neutralisation Capacity	Acid Reserve	Titration
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)

Test Methods

SOP	Title	Parameters included	Method summary
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2815	Polychlorinated Biphenyls (PCB) ICES7Congeners in Soils by GC-MS	ICES7 PCB congeners	Acetone/Hexane extraction / GC-MS
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.
640	Characterisation of Waste (Leaching C10)	Waste material including soil, sludges and granular waste	ComplianceTest for Leaching of Granular Waste Material and Sludge

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 45 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com


Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-21014-1
Initial Date of Issue:	30-Jun-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Andy Clee Charlie Gould Jon Owens Sam Gould
Project	101114 BAM Construction Site, Sport City Way

Quotation No.:		**Date Received:**	21-Jun-2021
Order No.:	9848	**Date Instructed:**	21-Jun-2021
No. of Samples:	1		
Turnaround (Wkdays):	5	**Results Due:**	25-Jun-2021
Date Approved:	30-Jun-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site, Sport City Way

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-21014
Quotation No.:			**Chemtest Sample ID.:**		1224892
Order No.: 9848			Client Sample Ref.:		PA10/01
			Sample Type:		SOIL
			Date Sampled:		18-Jun-2021
			Asbestos Lab:		NEW-ASB
Determinand	**Accred.**	**SOP**	**Units**	**LOD**	
ACM Type	U	2192		N/A	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected
Total Asbestos	U	2192	%	0.001	-
Moisture	N	2030	%	0.020	10
pH	U	2010		4.0	11.6
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	0.28
Sulphur (Elemental)	U	2180	mg/kg	1.0	2.2
Cyanide (Complex)	U	2300	mg/kg	0.50	< 0.50
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	< 0.50
Sulphate (Total)	U	2430	%	0.010	0.057
Arsenic	U	2450	mg/kg	1.0	4.2
Cadmium	U	2450	mg/kg	0.10	0.12
Chromium	U	2450	mg/kg	1.0	7.9
Copper	U	2450	mg/kg	0.50	33
Mercury	U	2450	mg/kg	0.10	< 0.10
Nickel	U	2450	mg/kg	0.50	22
Lead	U	2450	mg/kg	0.50	18
Selenium	U	2450	mg/kg	0.20	0.28
Zinc	U	2450	mg/kg	0.50	74
LOI	U	2610	%	0.10	7.4
Total Organic Carbon	U	2625	%	0.20	1.5
Total TPH >C6-C40	U	2670	mg/kg	10	< 10
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0

Results - Soil

Project: 101114 BAM Construction Site, Sport City Way

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-21014
Quotation No.:			**Chemtest Sample ID.:**		1224892
Order No.: 9848			Client Sample Ref.:		PA10/01
			Sample Type:		SOIL
			Date Sampled:		18-Jun-2021
			Asbestos Lab:		NEW-ASB
Determinand	**Accred.**	**SOP**	**Units**	**LOD**	
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	< 10
Naphthalene	U	2700	mg/kg	0.10	< 0.10
Acenaphthylene	U	2700	mg/kg	0.10	< 0.10
Acenaphthene	U	2700	mg/kg	0.10	< 0.10
Fluorene	U	2700	mg/kg	0.10	< 0.10
Phenanthrene	U	2700	mg/kg	0.10	< 0.10
Anthracene	U	2700	mg/kg	0.10	< 0.10
Fluoranthene	U	2700	mg/kg	0.10	0.43
Pyrene	U	2700	mg/kg	0.10	0.53
Benzo[a]anthracene	U	2700	mg/kg	0.10	< 0.10
Chrysene	U	2700	mg/kg	0.10	< 0.10
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	< 0.10
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	< 0.10
Benzo[a]pyrene	U	2700	mg/kg	0.10	< 0.10
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	< 0.10
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	< 0.10
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	< 0.10
Total Of 16 PAH's	U	2700	mg/kg	2.0	< 2.0
Benzene	U	2760	µg/kg	1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0
Total Phenols	U	2920	mg/kg	0.10	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com


Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-21595-1
Initial Date of Issue:	30-Jun-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Andy Clee Charlie Gould Jon Owens Sam Gould
Project	101114 BAM Construction Site

Quotation No.:	Q21-23216	**Date Received:**	24-Jun-2021
Order No.:	9746	**Date Instructed:**	24-Jun-2021
No. of Samples:	1		
Turnaround (Wkdays):	5	**Results Due:**	30-Jun-2021
Date Approved:	30-Jun-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-21595
Quotation No.: Q21-23216			**Chemtest Sample ID.:**		1227825
Order No.: 9746			Client Sample Ref.:		HLM/A2
			Sample Type:		SOIL
			Date Sampled:		22-Jun-2021
			Asbestos Lab:		COVENTRY
Determinand	**Accred.**	**SOP**	**Units**	**LOD**	
ACM Type	U	2192		N/A	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected
Moisture	N	2030	%	0.020	6.7
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50
Arsenic	U	2450	mg/kg	1.0	< 1.0
Cadmium	U	2450	mg/kg	0.10	0.19
Chromium	U	2450	mg/kg	1.0	12
Copper	U	2450	mg/kg	0.50	7.9
Mercury	U	2450	mg/kg	0.10	< 0.10
Nickel	U	2450	mg/kg	0.50	16
Lead	U	2450	mg/kg	0.50	12
Selenium	U	2450	mg/kg	0.20	< 0.20
Zinc	U	2450	mg/kg	0.50	33
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	11
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	11
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	46
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	46
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	57
Naphthalene	U	2700	mg/kg	0.10	< 0.10
Acenaphthylene	U	2700	mg/kg	0.10	< 0.10
Acenaphthene	U	2700	mg/kg	0.10	< 0.10
Fluorene	U	2700	mg/kg	0.10	< 0.10
Phenanthrene	U	2700	mg/kg	0.10	< 0.10
Anthracene	U	2700	mg/kg	0.10	< 0.10
Fluoranthene	U	2700	mg/kg	0.10	0.82

Results - Soil

Project: 101114 BAM Construction Site

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-21595
Quotation No.: Q21-23216			**Chemtest Sample ID.:**		1227825
Order No.: 9746			Client Sample Ref.:		HLM/A2
			Sample Type:		SOIL
			Date Sampled:		22-Jun-2021
			Asbestos Lab:		COVENTRY
Determinand	**Accred.**	**SOP**	**Units**	**LOD**	
Pyrene	U	2700	mg/kg	0.10	0.85
Benzo[a]anthracene	U	2700	mg/kg	0.10	< 0.10
Chrysene	U	2700	mg/kg	0.10	< 0.10
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	< 0.10
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	< 0.10
Benzo[a]pyrene	U	2700	mg/kg	0.10	< 0.10
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	< 0.10
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	< 0.10
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	< 0.10
Total Of 16 PAH's	U	2700	mg/kg	2.0	< 2.0
Benzene	U	2760	µg/kg	1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0

Test Methods

SOP	Title	Parameters included	Method summary
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com


Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-22001-1
Initial Date of Issue:	04-Jul-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Sam Lane-Ryan
Project	101114 Bam Construction Site, Sport City Way Manchester

Quotation No.:		**Date Received:**	28-Jun-2021
Order No.:	9848	**Date Instructed:**	28-Jun-2021
No. of Samples:	1		
Turnaround (Wkdays):	5	**Results Due:**	02-Jul-2021
Date Approved:	04-Jul-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 Bam Construction Site, Sport City Way Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-22001
Quotation No.:			**Chemtest Sample ID.:**		1229730
Order No.: 9848			Client Sample Ref.:		PA11/01
			Sample Location:		PA11
			Sample Type:		SOIL
			Date Sampled:		25-Jun-2021
			Asbestos Lab:		DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**	
ACM Type	U	2192		N/A	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected
Moisture	N	2030	%	0.020	10
pH	U	2010		4.0	11.5
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	0.34
Sulphur (Elemental)	U	2180	mg/kg	1.0	12
Cyanide (Complex)	U	2300	mg/kg	0.50	< 0.50
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	< 0.50
Sulphate (Total)	U	2430	%	0.010	0.24
Arsenic	U	2450	mg/kg	1.0	12
Cadmium	U	2450	mg/kg	0.10	0.15
Chromium	U	2450	mg/kg	1.0	20
Copper	U	2450	mg/kg	0.50	13
Mercury	U	2450	mg/kg	0.10	< 0.10
Nickel	U	2450	mg/kg	0.50	15
Lead	U	2450	mg/kg	0.50	27
Selenium	U	2450	mg/kg	0.20	0.20
Zinc	U	2450	mg/kg	0.50	44
LOI	U	2610	%	0.10	5.5
Total Organic Carbon	U	2625	%	0.20	0.85
Total TPH >C6-C40	U	2670	mg/kg	10	< 10
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0

Results - Soil

Project: 101114 Bam Construction Site, Sport City Way Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-22001
Quotation No.:			**Chemtest Sample ID.:**		1229730
Order No.: 9848			Client Sample Ref.:		PA11/01
			Sample Location:		PA11
			Sample Type:		SOIL
			Date Sampled:		25-Jun-2021
			Asbestos Lab:		DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**	
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	< 10
Naphthalene	U	2700	mg/kg	0.10	0.20
Acenaphthylene	U	2700	mg/kg	0.10	0.25
Acenaphthene	U	2700	mg/kg	0.10	0.39
Fluorene	U	2700	mg/kg	0.10	0.31
Phenanthrene	U	2700	mg/kg	0.10	1.4
Anthracene	U	2700	mg/kg	0.10	0.32
Fluoranthene	U	2700	mg/kg	0.10	1.6
Pyrene	U	2700	mg/kg	0.10	1.9
Benzo[a]anthracene	U	2700	mg/kg	0.10	0.62
Chrysene	U	2700	mg/kg	0.10	1.2
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	0.90
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	0.44
Benzo[a]pyrene	U	2700	mg/kg	0.10	0.58
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	0.38
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	0.45
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	0.44
Total Of 16 PAH's	U	2700	mg/kg	2.0	11
Benzene	U	2760	µg/kg	1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0
Total Phenols	U	2920	mg/kg	0.10	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com


Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-22893-1
Initial Date of Issue:	12-Jul-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Sam Lane-Ryan Charlotte Nicholson
Project	101114 BAM Construction Site, Sportcity Way, Manchester

Quotation No.:		**Date Received:**	05-Jul-2021
Order No.:	9848	**Date Instructed:**	05-Jul-2021
No. of Samples:	1		
Turnaround (Wkdays):	5	**Results Due:**	09-Jul-2021
Date Approved:	12-Jul-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-22893
Quotation No.:			**Chemtest Sample ID.:**		1233926
Order No.: 9848			Client Sample Ref.:		PA12/01
			Sample Location:		PA12
			Sample Type:		SOIL
			Date Sampled:		02-Jul-2021
			Asbestos Lab:		COVENTRY
Determinand	**Accred.**	**SOP**	**Units**	**LOD**	
ACM Type	U	2192		N/A	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected
Moisture	N	2030	%	0.020	12
pH	U	2010		4.0	8.6
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	0.046
Sulphur (Elemental)	U	2180	mg/kg	1.0	4.0
Cyanide (Complex)	U	2300	mg/kg	0.50	< 0.50
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	< 0.50
Sulphate (Total)	U	2430	%	0.010	0.22
Arsenic	U	2450	mg/kg	1.0	4.7
Cadmium	U	2450	mg/kg	0.10	0.21
Chromium	U	2450	mg/kg	1.0	18
Copper	U	2450	mg/kg	0.50	19
Mercury	U	2450	mg/kg	0.10	0.58
Nickel	U	2450	mg/kg	0.50	25
Lead	U	2450	mg/kg	0.50	14
Selenium	U	2450	mg/kg	0.20	0.26
Zinc	U	2450	mg/kg	0.50	41
LOI	U	2610	%	0.10	7.1
Total Organic Carbon	U	2625	%	0.20	1.7
Florisil Cleanup	N		-	N/A	Done
Total TPH >C6-C40	U	2670	mg/kg	10	< 10
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-22893
Quotation No.:			**Chemtest Sample ID.:**		1233926
Order No.: 9848			Client Sample Ref.:		PA12/01
			Sample Location:		PA12
			Sample Type:		SOIL
			Date Sampled:		02-Jul-2021
			Asbestos Lab:		COVENTRY
Determinand	**Accred.**	**SOP**	**Units**	**LOD**	
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	< 10
Naphthalene	U	2700	mg/kg	0.10	< 0.10
Acenaphthylene	U	2700	mg/kg	0.10	< 0.10
Acenaphthene	U	2700	mg/kg	0.10	< 0.10
Fluorene	U	2700	mg/kg	0.10	< 0.10
Phenanthrene	U	2700	mg/kg	0.10	< 0.10
Anthracene	U	2700	mg/kg	0.10	< 0.10
Fluoranthene	U	2700	mg/kg	0.10	< 0.10
Pyrene	U	2700	mg/kg	0.10	< 0.10
Benzo[a]anthracene	U	2700	mg/kg	0.10	< 0.10
Chrysene	U	2700	mg/kg	0.10	< 0.10
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	< 0.10
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	< 0.10
Benzo[a]pyrene	U	2700	mg/kg	0.10	< 0.10
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	< 0.10
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	< 0.10
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	< 0.10
Total Of 16 PAH's	U	2700	mg/kg	2.0	< 2.0
Benzene	U	2760	µg/kg	1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0
Total Phenols	U	2920	mg/kg	0.10	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage


If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com

Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-23237-1		
Initial Date of Issue:	14-Jul-2021		
Client	Provectus Group Ltd		
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE		
Contact(s):	Charlotte Nicholson Sam Lane-Ryan		
Project	101114 BAM Construction Site, Sportcity Way, Manchester		
Quotation No.:	Q21-23216	**Date Received:**	07-Jul-2021
Order No.:	9746	**Date Instructed:**	07-Jul-2021
No. of Samples:	5		
Turnaround (Wkdays):	5	**Results Due:**	13-Jul-2021
Date Approved:	14-Jul-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-23237	21-23237	21-23237	21-23237	21-23237
Quotation No.: Q21-23216			**Chemtest Sample ID.:**		1235598	1235599	1235600	1235601	1235602
Order No.: 9746			Client Sample Ref.:		HLM/A3	HLM/A4	HLM/A5	HLM/A6	HLM/A7
			Sample Location:		SP5	SP5	SP5	SP5	SP5
			Sample Type:		SOIL	SOIL	SOIL	SOIL	SOIL
			Date Sampled:		05-Jul-2021	05-Jul-2021	05-Jul-2021	05-Jul-2021	05-Jul-2021
			Asbestos Lab:		DURHAM	DURHAM	DURHAM	DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**					
ACM Type	U	2192		N/A	-	-	-	-	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected	No Asbestos Detected	No Asbestos Detected	No Asbestos Detected	No Asbestos Detected
Moisture	N	2030	%	0.020	9.9	10	14	15	13
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50	< 0.50	< 0.50	< 0.50	< 0.50
Arsenic	U	2450	mg/kg	1.0	3.5	2.4	2.9	4.1	5.1
Cadmium	U	2450	mg/kg	0.10	0.12	0.16	0.14	0.25	0.25
Chromium	U	2450	mg/kg	1.0	9.3	14	12	17	20
Copper	U	2450	mg/kg	0.50	7.5	8.1	7.8	16	25
Mercury	U	2450	mg/kg	0.10	< 0.10	< 0.10	< 0.10	< 0.10	< 0.10
Nickel	U	2450	mg/kg	0.50	11	17	14	19	23
Lead	U	2450	mg/kg	0.50	14	12	10	29	32
Selenium	U	2450	mg/kg	0.20	< 0.20	< 0.20	< 0.20	< 0.20	< 0.20
Zinc	U	2450	mg/kg	0.50	26	34	28	52	61
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	42	< 1.0	110	32	65
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	42	< 5.0	110	32	65
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	20	5.5
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	32	5.2
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0	< 5.0	52	11
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	42	< 10	110	84	76
Naphthalene	U	2700	mg/kg	0.10	0.48	< 0.10	0.39	0.94	1.0
Acenaphthylene	U	2700	mg/kg	0.10	0.56	< 0.10	0.22	0.21	0.41
Acenaphthene	U	2700	mg/kg	0.10	1.3	< 0.10	0.16	0.33	0.58
Fluorene	U	2700	mg/kg	0.10	1.1	< 0.10	0.19	0.37	0.57
Phenanthrene	U	2700	mg/kg	0.10	0.82	0.38	0.67	2.0	3.0

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-23237	21-23237	21-23237	21-23237	21-23237
Quotation No.: Q21-23216			**Chemtest Sample ID.:**		1235598	1235599	1235600	1235601	1235602
Order No.: 9746			Client Sample Ref.:		HLM/A3	HLM/A4	HLM/A5	HLM/A6	HLM/A7
			Sample Location:		SP5	SP5	SP5	SP5	SP5
			Sample Type:		SOIL	SOIL	SOIL	SOIL	SOIL
			Date Sampled:		05-Jul-2021	05-Jul-2021	05-Jul-2021	05-Jul-2021	05-Jul-2021
			Asbestos Lab:		DURHAM	DURHAM	DURHAM	DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**					
Anthracene	U	2700	mg/kg	0.10	0.16	< 0.10	0.13	0.49	0.73
Fluoranthene	U	2700	mg/kg	0.10	1.1	0.52	0.79	2.5	3.3
Pyrene	U	2700	mg/kg	0.10	1.1	0.77	0.94	2.8	3.8
Benzo[a]anthracene	U	2700	mg/kg	0.10	0.62	< 0.10	0.38	1.1	1.5
Chrysene	U	2700	mg/kg	0.10	1.0	< 0.10	0.84	1.7	2.2
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	< 0.10	< 0.10	0.55	1.4	1.7
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	< 0.10	< 0.10	0.25	0.66	1.1
Benzo[a]pyrene	U	2700	mg/kg	0.10	< 0.10	< 0.10	0.38	0.91	1.5
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	< 0.10	< 0.10	0.21	0.66	0.97
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	< 0.10	< 0.10	0.33	0.40	0.73
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	< 0.10	< 0.10	0.26	0.68	0.96
Total Of 16 PAH's	U	2700	mg/kg	2.0	8.2	< 2.0	6.7	17	24
Benzene	U	2760	µg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	1.1	< 1.0	< 1.0	< 1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0

Test Methods

SOP	Title	Parameters included	Method summary
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com


Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-23800-1
Initial Date of Issue:	16-Jul-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Sam Lane-Ryan
Project	101114 BAM Construction Site, Sportcity Way, Manchester

Quotation No.:	Q21-24773	**Date Received:**	12-Jul-2021
Order No.:	9848	**Date Instructed:**	12-Jul-2021
No. of Samples:	1		
Turnaround (Wkdays):	5	**Results Due:**	16-Jul-2021
Date Approved:	16-Jul-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-23800
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1238424
Order No.: 9848			Client Sample Ref.:		PA13/01
			Sample Location:		PA13
			Sample Type:		SOIL
			Date Sampled:		09-Jul-2021
			Asbestos Lab:		DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**	
ACM Type	U	2192		N/A	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected
Moisture	N	2030	%	0.020	8.2
pH	U	2010		4.0	11.7
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	0.38
Sulphur (Elemental)	U	2180	mg/kg	1.0	23
Cyanide (Complex)	U	2300	mg/kg	0.50	< 0.50
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	< 0.50
Sulphate (Total)	U	2430	%	0.010	0.54
Arsenic	U	2450	mg/kg	1.0	14
Cadmium	U	2450	mg/kg	0.10	0.45
Chromium	U	2450	mg/kg	1.0	17
Copper	U	2450	mg/kg	0.50	50
Mercury	U	2450	mg/kg	0.10	0.12
Nickel	U	2450	mg/kg	0.50	30
Lead	U	2450	mg/kg	0.50	47
Selenium	U	2450	mg/kg	0.20	0.50
Zinc	U	2450	mg/kg	0.50	96
LOI	U	2610	%	0.10	7.2
Total Organic Carbon	U	2625	%	0.20	1.9
Florisil Cleanup	N		-	N/A	Done
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	20
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	20
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	130

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-23800
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1238424
Order No.: 9848			Client Sample Ref.:		PA13/01
			Sample Location:		PA13
			Sample Type:		SOIL
			Date Sampled:		09-Jul-2021
			Asbestos Lab:		DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**	
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	950
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	1100
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	1100
Naphthalene	U	2700	mg/kg	0.10	0.90
Acenaphthylene	U	2700	mg/kg	0.10	0.19
Acenaphthene	U	2700	mg/kg	0.10	0.47
Fluorene	U	2700	mg/kg	0.10	0.46
Phenanthrene	U	2700	mg/kg	0.10	1.7
Anthracene	U	2700	mg/kg	0.10	0.42
Fluoranthene	U	2700	mg/kg	0.10	2.0
Pyrene	U	2700	mg/kg	0.10	2.1
Benzo[a]anthracene	U	2700	mg/kg	0.10	0.70
Chrysene	U	2700	mg/kg	0.10	0.89
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	0.57
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	1.1
Benzo[a]pyrene	U	2700	mg/kg	0.10	0.95
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	0.63
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	0.85
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	0.82
Total Of 16 PAH's	U	2700	mg/kg	2.0	15
Benzene	U	2760	µg/kg	1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0
Total Phenols	U	2920	mg/kg	0.10	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com


Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-24600-1
Initial Date of Issue:	26-Jul-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Sam Lane-Ryan
Project	101114 BAM Construction Site, Sportcity Way, Manchester, M11

Quotation No.:	Q21-23216	**Date Received:**	19-Jul-2021
Order No.:	9746	**Date Instructed:**	19-Jul-2021
No. of Samples:	2		
Turnaround (Wkdays):	6	**Results Due:**	26-Jul-2021
Date Approved:	26-Jul-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester, M11

Client: Provectus Group Ltd		**Chemtest Job No.:**		21-24600	21-24600
Quotation No.: Q21-23216		**Chemtest Sample ID.:**		1242339	1242340
Order No.: 9746		Client Sample Ref.:		HLM/G2	TYPE1/A6
		Sample Location:		SP6	A6
		Sample Type:		SOIL	SOIL
		Date Sampled:		15-Jul-2021	15-Jul-2021
		Asbestos Lab:		DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
ACM Type	U	2192		N/A	-	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected	No Asbestos Detected
Moisture	N	2030	%	0.020	3.2	3.0
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Arsenic	U	2450	mg/kg	1.0	< 1.0	< 1.0
Cadmium	U	2450	mg/kg	0.10	< 0.10	< 0.10
Chromium	U	2450	mg/kg	1.0	5.0	7.8
Copper	U	2450	mg/kg	0.50	4.4	9.4
Mercury	U	2450	mg/kg	0.10	< 0.10	< 0.10
Nickel	U	2450	mg/kg	0.50	2.1	4.2
Lead	U	2450	mg/kg	0.50	5.6	5.8
Selenium	U	2450	mg/kg	0.20	< 0.20	< 0.20
Zinc	U	2450	mg/kg	0.50	11	20
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	< 10	< 10
Naphthalene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Acenaphthylene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Acenaphthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Fluorene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Phenanthrene	U	2700	mg/kg	0.10	< 0.10	< 0.10

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester, M11

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-24600	21-24600
Quotation No.: Q21-23216			**Chemtest Sample ID.:**		1242339	1242340
Order No.: 9746			Client Sample Ref.:		HLM/G2	TYPE1/A6
			Sample Location:		SP6	A6
			Sample Type:		SOIL	SOIL
			Date Sampled:		15-Jul-2021	15-Jul-2021
			Asbestos Lab:		DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
Anthracene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Fluoranthene	U	2700	mg/kg	0.10	0.32	0.26
Pyrene	U	2700	mg/kg	0.10	0.38	0.27
Benzo[a]anthracene	U	2700	mg/kg	0.10	0.50	< 0.10
Chrysene	U	2700	mg/kg	0.10	0.44	< 0.10
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[a]pyrene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Total Of 16 PAH's	U	2700	mg/kg	2.0	< 2.0	< 2.0
Benzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0

Test Methods

SOP	Title	Parameters included	Method summary
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com


Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-13332-1
Initial Date of Issue:	30-Apr-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Sam Lane-Ryan Charlotte Nicholson
Project	101114 BAM Construction Site, Sportcity Way, Manchester

Quotation No.:	Q21-23216	**Date Received:**	23-Apr-2021
Order No.:	9746	**Date Instructed:**	23-Apr-2021
No. of Samples:	1		
Turnaround (Wkdays):	5	**Results Due:**	29-Apr-2021
Date Approved:	30-Apr-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-13332
Quotation No.: Q21-23216			**Chemtest Sample ID.:**		1186021
			Client Sample ID.:		SP2
			Sample Location:		SP2
			Sample Type:		SOIL
			Date Sampled:		22-Apr-2021
			Asbestos Lab:		NEW-ASB
Determinand	**Accred.**	**SOP**	**Units**	**LOD**	
ACM Type	U	2192		N/A	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected
ACM Detection Stage	U	2192		N/A	-
Moisture	N	2030	%	0.020	6.6
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50
Arsenic	U	2450	mg/kg	1.0	11
Cadmium	U	2450	mg/kg	0.10	0.27
Chromium	U	2450	mg/kg	1.0	19
Copper	U	2450	mg/kg	0.50	26
Mercury	U	2450	mg/kg	0.10	0.14
Nickel	U	2450	mg/kg	0.50	20
Lead	U	2450	mg/kg	0.50	53
Selenium	U	2450	mg/kg	0.20	< 0.20
Zinc	U	2450	mg/kg	0.50	77
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	46
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	46
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	16
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	220
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	240
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	280
Naphthalene	U	2700	mg/kg	0.10	< 0.10
Acenaphthylene	U	2700	mg/kg	0.10	< 0.10
Acenaphthene	U	2700	mg/kg	0.10	< 0.10
Fluorene	U	2700	mg/kg	0.10	< 0.10

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-13332
Quotation No.: Q21-23216			**Chemtest Sample ID.:**		1186021
			Client Sample ID.:		SP2
			Sample Location:		SP2
			Sample Type:		SOIL
			Date Sampled:		22-Apr-2021
			Asbestos Lab:		NEW-ASB
Determinand	**Accred.**	**SOP**	**Units**	**LOD**	
Phenanthrene	U	2700	mg/kg	0.10	4.3
Anthracene	U	2700	mg/kg	0.10	0.92
Fluoranthene	U	2700	mg/kg	0.10	6.5
Pyrene	U	2700	mg/kg	0.10	7.2
Benzo[a]anthracene	U	2700	mg/kg	0.10	3.3
Chrysene	U	2700	mg/kg	0.10	3.2
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	4.0
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	1.8
Benzo[a]pyrene	U	2700	mg/kg	0.10	3.2
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	2.4
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	0.95
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	2.7
Total Of 16 PAH's	U	2700	mg/kg	2.0	41
Benzene	U	2760	µg/kg	1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0

Test Methods

SOP	Title	Parameters included	Method summary
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 45 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com

eurofins | Chemtest
Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

UKAS TESTING 2183

Interim Report

Report No.:	21-24603-0
Initial Date of Issue:	
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Sam Lane-Ryan
Project	101114 BAM Construction Site, Sportcity Way
Quotation No.:	Q21-24773
Order No.:	9848
No. of Samples:	1
Turnaround (Wkdays):	5
Date Approved:	
Approved By:	

Date Received:	19-Jul-2021
Date Instructed:	19-Jul-2021
Results Due:	23-Jul-2021

Details:

Please note that the interim data available has passed our Quality Control Criteria but has not been verified by an approved signatory and may be subject to amendment on approval. Chemtest cannot therefore be held responsible for decisions made on interim data sets but only for the data submitted on a final report containing an approval date and signature.

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-24603
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1242346
Order No.: 9848			Client Sample Ref.:		PA14/01
			Sample Location:		SPA14
			Sample Type:		SOIL
			Date Sampled:		16-Jul-2021
			Asbestos Lab:		DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**	
ACM Type	U	2192		N/A	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected
Moisture	N	2030	%	0.020	12
pH	U	2010		4.0	9.0
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	0.19
Sulphur (Elemental)	U	2180	mg/kg	1.0	23
Cyanide (Complex)	U	2300	mg/kg	0.50	2.9
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	3.0
Sulphate (Total)	U	2430	%	0.010	0.17
Arsenic	U	2450	mg/kg	1.0	8.2
Cadmium	U	2450	mg/kg	0.10	0.43
Chromium	U	2450	mg/kg	1.0	12
Copper	U	2450	mg/kg	0.50	50
Mercury	U	2450	mg/kg	0.10	0.30
Nickel	U	2450	mg/kg	0.50	8.1
Lead	U	2450	mg/kg	0.50	150
Selenium	U	2450	mg/kg	0.20	0.22
Zinc	U	2450	mg/kg	0.50	220
LOI	U	2610	%	0.10	4.9
Total Organic Carbon	U	2625	%	0.20	1.6
Total TPH >C6-C40	U	2670	mg/kg	10	240
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	To Follow
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	To Follow
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	To Follow
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	To Follow
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	To Follow
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	To Follow
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	To Follow
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	To Follow
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	To Follow
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	To Follow
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	To Follow
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	To Follow
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	To Follow
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	To Follow
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	To Follow
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	To Follow

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-24603
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1242346
Order No.: 9848			Client Sample Ref.:		PA14/01
			Sample Location:		SPA14
			Sample Type:		SOIL
			Date Sampled:		16-Jul-2021
			Asbestos Lab:		DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**	
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	To Follow
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	To Follow
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	To Follow
Naphthalene	U	2700	mg/kg	0.10	To Follow
Acenaphthylene	U	2700	mg/kg	0.10	To Follow
Acenaphthene	U	2700	mg/kg	0.10	To Follow
Fluorene	U	2700	mg/kg	0.10	To Follow
Phenanthrene	U	2700	mg/kg	0.10	To Follow
Anthracene	U	2700	mg/kg	0.10	To Follow
Fluoranthene	U	2700	mg/kg	0.10	To Follow
Pyrene	U	2700	mg/kg	0.10	To Follow
Benzo[a]anthracene	U	2700	mg/kg	0.10	To Follow
Chrysene	U	2700	mg/kg	0.10	To Follow
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	To Follow
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	To Follow
Benzo[a]pyrene	U	2700	mg/kg	0.10	To Follow
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	To Follow
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	To Follow
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	To Follow
Total Of 16 PAH's	U	2700	mg/kg	2.0	To Follow
Benzene	U	2760	µg/kg	1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0
Total Phenols	U	2920	mg/kg	0.10	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage


If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com

Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-25513-1		
Initial Date of Issue:	30-Jul-2021		
Client	Provectus Group Ltd		
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE		
Contact(s):	Charlotte Nicholson Sam Lane-Ryan		
Project	101114 BAM Construction Site, Sportcity Way		
Quotation No.:	Q21-24773	**Date Received:**	26-Jul-2021
Order No.:	9848	**Date Instructed:**	26-Jul-2021
No. of Samples:	2		
Turnaround (Wkdays):	5	**Results Due:**	30-Jul-2021
Date Approved:	30-Jul-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-25513	21-25513
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1247177	1247178
Order No.: 9848			Client Sample Ref.:		PA15/01	PA15/02
			Sample Type:		SOIL	SOIL
			Date Sampled:		23-Mar-2021	23-Mar-2021
			Asbestos Lab:		DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
ACM Type	U	2192		N/A	-	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected	No Asbestos Detected
Moisture	N	2030	%	0.020	7.0	7.3
pH	U	2010		4.0	[B] 11.5	[B] 11.4
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	[B] 0.38	[B] 0.45
Sulphur (Elemental)	U	2180	mg/kg	1.0	[B] < 1.0	[B] < 1.0
Cyanide (Complex)	U	2300	mg/kg	0.50	[B] 0.60	[B] < 0.50
Cyanide (Free)	U	2300	mg/kg	0.50	[B] < 0.50	[B] < 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	[B] 0.70	[B] < 0.50
Sulphate (Total)	U	2430	%	0.010	[B] 0.64	[B] 0.77
Arsenic	U	2450	mg/kg	1.0	12	13
Cadmium	U	2450	mg/kg	0.10	1.5	0.88
Chromium	U	2450	mg/kg	1.0	22	21
Copper	U	2450	mg/kg	0.50	30	38
Mercury	U	2450	mg/kg	0.10	0.10	0.12
Nickel	U	2450	mg/kg	0.50	29	28
Lead	U	2450	mg/kg	0.50	27	55
Selenium	U	2450	mg/kg	0.20	0.45	0.78
Zinc	U	2450	mg/kg	0.50	83	82
LOI	U	2610	%	0.10	4.9	6.7
Total Organic Carbon	U	2625	%	0.20	[B] 1.1	[B] 1.9
Total TPH >C6-C40	U	2670	mg/kg	10	[B] 28	[B] 67
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	[B] < 1.0	[B] < 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	[B] < 1.0	[B] < 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	[B] < 1.0	[B] < 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	[B] < 1.0	[B] < 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	[B] < 1.0	[B] < 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	[B] < 1.0	[B] < 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	[B] < 1.0	[B] < 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	[B] < 1.0	[B] < 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	[B] < 5.0	[B] < 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	[B] < 1.0	[B] < 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	[B] < 1.0	[B] < 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	[B] < 1.0	[B] < 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	[B] < 1.0	[B] < 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	[B] < 1.0	[B] < 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	[B] < 1.0	[B] < 1.0
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	[B] < 1.0	[B] < 1.0
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	[B] < 1.0	[B] < 1.0

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-25513	21-25513
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1247177	1247178
Order No.: 9848			Client Sample Ref.:		PA15/01	PA15/02
			Sample Type:		SOIL	SOIL
			Date Sampled:		23-Mar-2021	23-Mar-2021
			Asbestos Lab:		DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	[B] < 5.0	[B] < 5.0
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	[B] < 10	[B] < 10
Naphthalene	U	2700	mg/kg	0.10	[B] 0.50	[B] 0.53
Acenaphthylene	U	2700	mg/kg	0.10	[B] 0.48	[B] 0.28
Acenaphthene	U	2700	mg/kg	0.10	[B] 0.25	[B] 0.25
Fluorene	U	2700	mg/kg	0.10	[B] 0.35	[B] 0.37
Phenanthrene	U	2700	mg/kg	0.10	[B] 1.6	[B] 1.5
Anthracene	U	2700	mg/kg	0.10	[B] 0.36	[B] 0.29
Fluoranthene	U	2700	mg/kg	0.10	[B] 1.6	[B] 1.8
Pyrene	U	2700	mg/kg	0.10	[B] 1.8	[B] 1.9
Benzo[a]anthracene	U	2700	mg/kg	0.10	[B] 0.71	[B] 0.88
Chrysene	U	2700	mg/kg	0.10	[B] 1.1	[B] 1.8
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	[B] 0.96	[B] 1.2
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	[B] 0.52	[B] 0.65
Benzo[a]pyrene	U	2700	mg/kg	0.10	[B] 0.65	[B] 0.81
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	[B] 0.31	[B] 0.43
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	[B] 0.23	[B] 0.26
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	[B] 0.38	[B] 0.59
Total Of 16 PAH's	U	2700	mg/kg	2.0	[B] 12	[B] 14
Benzene	U	2760	µg/kg	1.0	[B] < 1.0	[B] < 1.0
Toluene	U	2760	µg/kg	1.0	[B] < 1.0	[B] < 1.0
Ethylbenzene	U	2760	µg/kg	1.0	[B] < 1.0	[B] < 1.0
m & p-Xylene	U	2760	µg/kg	1.0	[B] < 1.0	[B] < 1.0
o-Xylene	U	2760	µg/kg	1.0	[B] < 1.0	[B] < 1.0
Total Phenols	U	2920	mg/kg	0.10	< 0.10	< 0.10

Deviations

In accordance with UKAS Policy on Deviating Samples TPS 63. Chemtest have a procedure to ensure 'upon receipt of each sample a competent laboratory shall assess whether the sample is suitable with regard to the requested test(s)'. This policy and the respective holding times applied, can be supplied upon request.The reason a sample is declared as deviating is detailed below. Where applicable the analysis remains UKAS/MCERTs accredited but the results may be compromised.

Sample:	Sample Ref:	Sample ID:	Sample Location:	Sampled Date:	Deviation Code(s):	Containers Received:
1247177	PA15/01			23-Mar-2021	B	Amber Glass 250ml
1247177	PA15/01			23-Mar-2021	B	Amber Glass 60ml
1247177	PA15/01			23-Mar-2021	B	Plastic Tub 500g
1247178	PA15/02			23-Mar-2021	B	Amber Glass 250ml
1247178	PA15/02			23-Mar-2021	B	Amber Glass 60ml
1247178	PA15/02			23-Mar-2021	B	Plastic Tub 500g

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com


Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-26391-1
Initial Date of Issue:	06-Aug-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Sam Lane-Ryan
Project	101114 BAM Construction Site, Sportcity Way, Manchester

Quotation No.:	Q21-24773	**Date Received:**	02-Aug-2021
Order No.:	9848	**Date Instructed:**	02-Aug-2021
No. of Samples:	2		
Turnaround (Wkdays):	5	**Results Due:**	06-Aug-2021
Date Approved:	06-Aug-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-26391	21-26391
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1251514	1251515
Order No.: 9848			Client Sample Ref.:		PA16/01	PA16/02
			Sample Location:		PA16	PA16
			Sample Type:		SOIL	SOIL
			Date Sampled:		30-Jul-2021	30-Jul-2021
			Asbestos Lab:		NEW-ASB	NEW-ASB
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
ACM Type	U	2192		N/A	-	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected	No Asbestos Detected
Moisture	N	2030	%	0.020	14	16
pH	U	2010		4.0	11.5	11.2
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	0.26	0.45
Sulphur (Elemental)	U	2180	mg/kg	1.0	7.6	4.3
Cyanide (Complex)	U	2300	mg/kg	0.50	1.4	< 0.50
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	1.5	< 0.50
Sulphate (Total)	U	2430	%	0.010	0.28	0.27
Arsenic	U	2450	mg/kg	1.0	6.6	7.8
Cadmium	U	2450	mg/kg	0.10	0.18	0.24
Chromium	U	2450	mg/kg	1.0	13	19
Copper	U	2450	mg/kg	0.50	41	40
Mercury	U	2450	mg/kg	0.10	< 0.10	0.13
Nickel	U	2450	mg/kg	0.50	16	22
Lead	U	2450	mg/kg	0.50	17	24
Selenium	U	2450	mg/kg	0.20	0.21	0.21
Zinc	U	2450	mg/kg	0.50	44	60
LOI	U	2610	%	0.10	3.9	5.5
Total Organic Carbon	U	2625	%	0.20	0.96	1.5
Total TPH >C6-C40	U	2670	mg/kg	10	< 10	99
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-26391	21-26391
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1251514	1251515
Order No.: 9848			Client Sample Ref.:		PA16/01	PA16/02
			Sample Location:		PA16	PA16
			Sample Type:		SOIL	SOIL
			Date Sampled:		30-Jul-2021	30-Jul-2021
			Asbestos Lab:		NEW-ASB	NEW-ASB
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	< 10	< 10
Naphthalene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Acenaphthylene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Acenaphthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Fluorene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Phenanthrene	U	2700	mg/kg	0.10	< 0.10	1.3
Anthracene	U	2700	mg/kg	0.10	< 0.10	0.36
Fluoranthene	U	2700	mg/kg	0.10	0.56	1.6
Pyrene	U	2700	mg/kg	0.10	0.58	1.8
Benzo[a]anthracene	U	2700	mg/kg	0.10	< 0.10	0.76
Chrysene	U	2700	mg/kg	0.10	< 0.10	1.1
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	< 0.10	0.95
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	< 0.10	0.21
Benzo[a]pyrene	U	2700	mg/kg	0.10	< 0.10	0.80
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	< 0.10	0.61
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	< 0.10	0.14
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	< 0.10	0.69
Total Of 16 PAH's	U	2700	mg/kg	2.0	< 2.0	10
Benzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Total Phenols	U	2920	mg/kg	0.10	< 0.10	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com

eurofins | Chemtest
Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

UKAS TESTING 2183

Final Report

Report No.:	21-27100-1
Initial Date of Issue:	12-Aug-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Sam Lane-Ryan
Project	101114
Quotation No.:	Q21-24773
Order No.:	9848
No. of Samples:	2
Turnaround (Wkdays):	5
Date Approved:	12-Aug-2021
Approved By:	
Details:	Glynn Harvey, Technical Manager

Date Received:	
Date Instructed:	06-Aug-2021
Results Due:	12-Aug-2021

Results - Soil

Project: 101114

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-27100	21-27100
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1254940	1254941
Order No.: 9848			Client Sample Ref.:		PA17/01	PA17/02
			Sample Location:		PA17	PA17
			Sample Type:		SOIL	SOIL
			Date Sampled:		04-Aug-2021	04-Aug-2021
			Asbestos Lab:		COVENTRY	COVENTRY
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
ACM Type	U	2192		N/A	-	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected	No Asbestos Detected
Moisture	N	2030	%	0.020	2.5	7.5
pH	U	2010		4.0	9.9	11.4
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	0.27	0.37
Sulphur (Elemental)	U	2180	mg/kg	1.0	9.1	3.8
Cyanide (Complex)	U	2300	mg/kg	0.50	2.8	< 0.50
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	3.0	0.70
Sulphate (Total)	U	2430	%	0.010	0.28	0.35
Arsenic	U	2450	mg/kg	1.0	6.8	12
Cadmium	U	2450	mg/kg	0.10	0.16	0.29
Chromium	U	2450	mg/kg	1.0	16	22
Copper	U	2450	mg/kg	0.50	55	28
Mercury	U	2450	mg/kg	0.10	< 0.10	0.18
Nickel	U	2450	mg/kg	0.50	24	29
Lead	U	2450	mg/kg	0.50	24	55
Selenium	U	2450	mg/kg	0.20	0.38	0.44
Zinc	U	2450	mg/kg	0.50	81	76
LOI	U	2610	%	0.10	7.7	6.6
Total Organic Carbon	U	2625	%	0.20	1.7	1.4
Total TPH >C6-C40	U	2670	mg/kg	10	32	< 10
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	11	< 1.0

Results - Soil

Project: 101114

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-27100	21-27100
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1254940	1254941
Order No.: 9848			Client Sample Ref.:		PA17/01	PA17/02
			Sample Location:		PA17	PA17
			Sample Type:		SOIL	SOIL
			Date Sampled:		04-Aug-2021	04-Aug-2021
			Asbestos Lab:		COVENTRY	COVENTRY
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	11	< 5.0
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	11	< 10
Naphthalene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Acenaphthylene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Acenaphthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Fluorene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Phenanthrene	U	2700	mg/kg	0.10	1.6	< 0.10
Anthracene	U	2700	mg/kg	0.10	0.39	< 0.10
Fluoranthene	U	2700	mg/kg	0.10	2.0	0.66
Pyrene	U	2700	mg/kg	0.10	2.1	0.70
Benzo[a]anthracene	U	2700	mg/kg	0.10	1.2	< 0.10
Chrysene	U	2700	mg/kg	0.10	1.7	< 0.10
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	0.81	< 0.10
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	0.57	< 0.10
Benzo[a]pyrene	U	2700	mg/kg	0.10	0.79	< 0.10
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Total Of 16 PAH's	U	2700	mg/kg	2.0	11	< 2.0
Benzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Total Phenols	U	2920	mg/kg	0.10	< 0.10	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com


Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-27883-1
Initial Date of Issue:	19-Aug-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Sam Lane-Ryan
Project	101114 BAM Construction site

Quotation No.:	Q21-23216	**Date Received:**	12-Aug-2021
Order No.:	9746	**Date Instructed:**	12-Aug-2021
No. of Samples:	2		
Turnaround (Wkdays):	5	**Results Due:**	18-Aug-2021

Date Approved:	19-Aug-2021
Approved By:	



Details:	Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction site

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-27883	21-27883
Quotation No.: Q21-23216			**Chemtest Sample ID.:**		1259306	1259307
Order No.: 9746			Client Sample Ref.:		HLM/G2	HLM/G3
			Sample Location:		SP7	SP7
			Sample Type:		SOIL	SOIL
			Date Sampled:		10-Aug-2021	10-Aug-2021
			Asbestos Lab:		COVENTRY	COVENTRY
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
ACM Type	U	2192		N/A	-	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected	No Asbestos Detected
Moisture	N	2030	%	0.020	8.0	8.0
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Arsenic	U	2450	mg/kg	1.0	1.2	4.1
Cadmium	U	2450	mg/kg	0.10	0.12	0.21
Chromium	U	2450	mg/kg	1.0	4.3	9.2
Copper	U	2450	mg/kg	0.50	5.2	13
Mercury	U	2450	mg/kg	0.10	< 0.10	< 0.10
Nickel	U	2450	mg/kg	0.50	7.2	15
Lead	U	2450	mg/kg	0.50	10	48
Selenium	U	2450	mg/kg	0.20	< 0.20	< 0.20
Zinc	U	2450	mg/kg	0.50	19	38
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	< 10	< 10
Naphthalene	U	2700	mg/kg	0.10	0.13	0.34
Acenaphthylene	U	2700	mg/kg	0.10	0.46	0.25
Acenaphthene	U	2700	mg/kg	0.10	0.12	0.30
Fluorene	U	2700	mg/kg	0.10	0.19	0.22
Phenanthrene	U	2700	mg/kg	0.10	0.74	1.1
Anthracene	U	2700	mg/kg	0.10	0.22	0.26

Results - Soil

Project: 101114 BAM Construction site

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-27883	21-27883
Quotation No.: Q21-23216			**Chemtest Sample ID.:**		1259306	1259307
Order No.: 9746			Client Sample Ref.:		HLM/G2	HLM/G3
			Sample Location:		SP7	SP7
			Sample Type:		SOIL	SOIL
			Date Sampled:		10-Aug-2021	10-Aug-2021
			Asbestos Lab:		COVENTRY	COVENTRY
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
Fluoranthene	U	2700	mg/kg	0.10	0.97	1.7
Pyrene	U	2700	mg/kg	0.10	0.97	1.8
Benzo[a]anthracene	U	2700	mg/kg	0.10	0.62	0.87
Chrysene	U	2700	mg/kg	0.10	0.11	0.86
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	0.47	0.88
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	0.62	0.83
Benzo[a]pyrene	U	2700	mg/kg	0.10	0.52	0.80
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	0.25	0.58
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	0.31	0.44
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	0.29	0.55
Total Of 16 PAH's	U	2700	mg/kg	2.0	7.0	12
Benzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0

Test Methods

SOP	Title	Parameters included	Method summary
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com


Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-28980-1
Initial Date of Issue:	26-Aug-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Sam Lane-Ryan
Project	101114 BAM Construction Site, Sportcity Way, Manchester

Quotation No.:	Q21-24773	**Date Received:**	20-Aug-2021
Order No.:	9848	**Date Instructed:**	20-Aug-2021
No. of Samples:	2		
Turnaround (Wkdays):	5	**Results Due:**	26-Aug-2021
Date Approved:	26-Aug-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-28980	21-28980
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1264486	1264487
			Client Sample ID.:		PA18/01	PA18/02
			Sample Location:		PA18	PA18
			Sample Type:		SOIL	SOIL
			Date Sampled:		18-Aug-2021	18-Aug-2021
			Asbestos Lab:		DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
ACM Type	U	2192		N/A	-	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected	No Asbestos Detected
Moisture	N	2030	%	0.020	12	15
pH	U	2010		4.0	11.2	10.2
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	0.41	0.61
Sulphur (Elemental)	U	2180	mg/kg	1.0	3.4	37
Cyanide (Complex)	U	2300	mg/kg	0.50	< 0.50	0.60
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	< 0.50	0.60
Sulphate (Total)	U	2430	%	0.010	0.36	0.40
Arsenic	U	2450	mg/kg	1.0	8.9	8.5
Cadmium	U	2450	mg/kg	0.10	0.27	0.22
Chromium	U	2450	mg/kg	1.0	22	45
Copper	U	2450	mg/kg	0.50	23	33
Mercury	U	2450	mg/kg	0.10	0.11	0.13
Nickel	U	2450	mg/kg	0.50	33	27
Lead	U	2450	mg/kg	0.50	19	62
Selenium	U	2450	mg/kg	0.20	0.25	0.65
Zinc	U	2450	mg/kg	0.50	77	86
LOI	U	2610	%	0.10	5.8	10
Total Organic Carbon	U	2625	%	0.20	1.6	3.6
Total TPH >C6-C40	U	2670	mg/kg	10	< 10	25
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	1.9	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	2.7	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	9.7	5.1
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	14	5.1
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-28980	21-28980
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1264486	1264487
			Client Sample ID.:		PA18/01	PA18/02
			Sample Location:		PA18	PA18
			Sample Type:		SOIL	SOIL
			Date Sampled:		18-Aug-2021	18-Aug-2021
			Asbestos Lab:		DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	55	< 1.0
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	55	< 5.0
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	69	< 10
Naphthalene	U	2700	mg/kg	0.10	< 0.10	2.6
Acenaphthylene	U	2700	mg/kg	0.10	< 0.10	0.34
Acenaphthene	U	2700	mg/kg	0.10	< 0.10	0.23
Fluorene	U	2700	mg/kg	0.10	< 0.10	0.31
Phenanthrene	U	2700	mg/kg	0.10	0.23	1.1
Anthracene	U	2700	mg/kg	0.10	< 0.10	0.33
Fluoranthene	U	2700	mg/kg	0.10	0.21	1.4
Pyrene	U	2700	mg/kg	0.10	0.28	1.7
Benzo[a]anthracene	U	2700	mg/kg	0.10	< 0.10	0.64
Chrysene	U	2700	mg/kg	0.10	< 0.10	1.0
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	< 0.10	0.59
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	< 0.10	0.19
Benzo[a]pyrene	U	2700	mg/kg	0.10	< 0.10	0.77
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	< 0.10	0.56
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	< 0.10	0.41
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	< 0.10	0.67
Total Of 16 PAH's	U	2700	mg/kg	2.0	< 2.0	13
Benzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Total Phenols	U	2920	mg/kg	0.10	< 0.10	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com

eurofins | Chemtest
Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

UKAS TESTING 2183

Final Report

Report No.:	21-29334-1
Initial Date of Issue:	02-Sep-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Sam Lane-Ryan
Project	101114 BAM Construction Site
Quotation No.:	Q21-24773
Order No.:	9848
No. of Samples:	2
Turnaround (Wkdays):	6
Date Approved:	02-Sep-2021
Approved By:	
Details:	Glynn Harvey, Technical Manager

Date Received:	24-Aug-2021
Date Instructed:	24-Aug-2021
Results Due:	01-Sep-2021

Results - Soil

Project: 101114 BAM Construction Site

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-29334	21-29334
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1266122	1266123
Order No.: 9848			Client Sample Ref.:		PA19/01	PA19/02
			Sample Location:		PA19	PA19
			Sample Type:		SOIL	SOIL
			Date Sampled:		20-Aug-2021	20-Aug-2021
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
ACM Type	U	2192		N/A	-	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected	No Asbestos Detected
Moisture	N	2030	%	0.020	7.6	13
pH	U	2010		4.0	7.7	11.5
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	0.084	0.30
Sulphur (Elemental)	U	2180	mg/kg	1.0	19	4.5
Cyanide (Complex)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Sulphate (Total)	U	2430	%	0.010	0.24	0.24
Arsenic	U	2450	mg/kg	1.0	9.4	8.5
Cadmium	U	2450	mg/kg	0.10	0.26	0.26
Chromium	U	2450	mg/kg	1.0	23	20
Copper	U	2450	mg/kg	0.50	34	19
Mercury	U	2450	mg/kg	0.10	< 0.10	< 0.10
Nickel	U	2450	mg/kg	0.50	48	29
Lead	U	2450	mg/kg	0.50	21	13
Selenium	U	2450	mg/kg	0.20	0.94	< 0.20
Zinc	U	2450	mg/kg	0.50	99	51
LOI	U	2610	%	0.10	4.8	9.0
Total Organic Carbon	U	2625	%	0.20	4.1	1.9
Total TPH >C6-C40	U	2670	mg/kg	10	< 10	< 10
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0

Results - Soil

Project: 101114 BAM Construction Site

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-29334	21-29334
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1266122	1266123
Order No.: 9848			Client Sample Ref.:		PA19/01	PA19/02
			Sample Location:		PA19	PA19
			Sample Type:		SOIL	SOIL
			Date Sampled:		20-Aug-2021	20-Aug-2021
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	< 10	< 10
Naphthalene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Acenaphthylene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Acenaphthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Fluorene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Phenanthrene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Anthracene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Fluoranthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Pyrene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[a]anthracene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Chrysene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[a]pyrene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Total Of 16 PAH's	U	2700	mg/kg	2.0	< 2.0	< 2.0
Benzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Total Phenols	U	2920	mg/kg	0.10	< 0.10	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com


Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-30019-1
Initial Date of Issue:	06-Sep-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Sam Lane-Ryan
Project	101114 Bam Construction Site, Sportcity Way, Manchester, M11

Quotation No.:	Q21-24773	**Date Received:**	31-Aug-2021
Order No.:	9848	**Date Instructed:**	31-Aug-2021
No. of Samples:	2		
Turnaround (Wkdays):	5	**Results Due:**	06-Sep-2021
Date Approved:	06-Sep-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 Bam Construction Site, Sportcity Way, Manchester, M11

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-30019	21-30019
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1268982	1268983
Order No.: 9848			Client Sample Ref.:		PA20/01	PA20/02
			Sample Location:		PA20	PA20
			Sample Type:		SOIL	SOIL
			Date Sampled:		27-Aug-2021	27-Aug-2021
			Asbestos Lab:		DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
ACM Type	U	2192		N/A	-	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected	No Asbestos Detected
Moisture	N	2030	%	0.020	4.2	87
pH	U	2010		4.0	9.1	10.5
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	0.015	0.12
Sulphur (Elemental)	U	2180	mg/kg	1.0	< 1.0	< 1.0
Cyanide (Complex)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	< 0.50	0.50
Sulphate (Total)	U	2430	%	0.010	0.28	0.19
Arsenic	U	2450	mg/kg	1.0	15	12
Cadmium	U	2450	mg/kg	0.10	0.32	0.20
Chromium	U	2450	mg/kg	1.0	25	20
Copper	U	2450	mg/kg	0.50	30	26
Mercury	U	2450	mg/kg	0.10	< 0.10	< 0.10
Nickel	U	2450	mg/kg	0.50	41	30
Lead	U	2450	mg/kg	0.50	16	15
Selenium	U	2450	mg/kg	0.20	0.44	0.22
Zinc	U	2450	mg/kg	0.50	94	63
LOI	U	2610	%	0.10	5.7	3.8
Total Organic Carbon	U	2625	%	0.20	1.5	1.2
Total TPH >C6-C40	U	2670	mg/kg	10	< 10	< 10
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0

Results - Soil

Project: 101114 Bam Construction Site, Sportcity Way, Manchester, M11

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-30019	21-30019
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1268982	1268983
Order No.: 9848			Client Sample Ref.:		PA20/01	PA20/02
			Sample Location:		PA20	PA20
			Sample Type:		SOIL	SOIL
			Date Sampled:		27-Aug-2021	27-Aug-2021
			Asbestos Lab:		DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	< 10	< 10
Naphthalene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Acenaphthylene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Acenaphthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Fluorene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Phenanthrene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Anthracene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Fluoranthene	U	2700	mg/kg	0.10	< 0.10	0.49
Pyrene	U	2700	mg/kg	0.10	< 0.10	0.43
Benzo[a]anthracene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Chrysene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[a]pyrene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Total Of 16 PAH's	U	2700	mg/kg	2.0	< 2.0	< 2.0
Benzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Total Phenols	U	2920	mg/kg	0.10	< 0.10	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com

eurofins | Chemtest
Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com


UKAS TESTING 2183

Final Report

Report No.:	21-30826-1
Initial Date of Issue:	13-Sep-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Sam Lane-Ryan
Project	101114 BAM Construction Site, Sportity Way, Manchester

Quotation No.:	Q21-24773	**Date Received:**	07-Sep-2021
Order No.:	9848	**Date Instructed:**	07-Sep-2021
No. of Samples:	4		
Turnaround (Wkdays):	5	**Results Due:**	13-Sep-2021
Date Approved:	13-Sep-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site, Sportity Way, Manchester

Client: Provectus Group Ltd		**Chemtest Job No.:**			21-30826	21-30826	21-30826	21-30826
Quotation No.: Q21-24773		**Chemtest Sample ID.:**			1273503	1273504	1273505	1273506
				Sample Location:	PA21/01	PA21/02	PA20/03	PA21/03
				Sample Type:	SOIL	SOIL	SOIL	SOIL
				Date Sampled:	06-Sep-2021	06-Sep-2021	06-Sep-2021	06-Sep-2021
				Asbestos Lab:	COVENTRY	COVENTRY	COVENTRY	COVENTRY
Determinand	**Accred.**	**SOP**	**Units**	**LOD**				
ACM Type	U	2192		N/A	-	-	-	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected	No Asbestos Detected	No Asbestos Detected	No Asbestos Detected
Moisture	N	2030	%	0.020	6.2	7.3	4.0	7.1
pH	U	2010		4.0	10.3	9.4	10.2	10.7
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	0.20	0.13	0.55	0.75
Sulphur (Elemental)	U	2180	mg/kg	1.0	25	7.4	36	45
Cyanide (Complex)	U	2300	mg/kg	0.50	1.0	0.50	3.8	6.1
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50	< 0.50	< 0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	1.2	0.50	3.8	6.2
Sulphate (Total)	U	2430	%	0.010	0.21	0.31	0.38	0.42
Arsenic	U	2450	mg/kg	1.0	5.3	5.9	9.6	13
Cadmium	U	2450	mg/kg	0.10	0.16	< 0.10	0.26	0.29
Chromium	U	2450	mg/kg	1.0	15	18	15	19
Copper	U	2450	mg/kg	0.50	24	20	24	29
Mercury	U	2450	mg/kg	0.10	< 0.10	< 0.10	0.13	0.19
Nickel	U	2450	mg/kg	0.50	24	30	27	28
Lead	U	2450	mg/kg	0.50	12	13	27	39
Selenium	U	2450	mg/kg	0.20	< 0.20	0.20	0.55	0.50
Zinc	U	2450	mg/kg	0.50	31	37	58	56
LOI	U	2610	%	0.10	5.5	4.6	7.6	7.9
Total Organic Carbon	U	2625	%	0.20	1.2	1.2	3.3	4.4
Total TPH >C6-C40	U	2670	mg/kg	10	< 10	48	61	48
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	28	< 1.0	87
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	28	< 5.0	87
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	34
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	160	< 1.0	110

Results - Soil

Project: 101114 BAM Construction Site, Sportity Way, Manchester

Client: Provectus Group Ltd		**Chemtest Job No.:**			21-30826	21-30826	21-30826	21-30826
Quotation No.: Q21-24773		**Chemtest Sample ID.:**			1273503	1273504	1273505	1273506
			Sample Location:		PA21/01	PA21/02	PA20/03	PA21/03
			Sample Type:		SOIL	SOIL	SOIL	SOIL
			Date Sampled:		06-Sep-2021	06-Sep-2021	06-Sep-2021	06-Sep-2021
			Asbestos Lab:		COVENTRY	COVENTRY	COVENTRY	COVENTRY
Determinand	**Accred.**	**SOP**	**Units**	**LOD**				
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	160	< 5.0	150
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	< 10	180	< 10	240
Naphthalene	U	2700	mg/kg	0.10	2.1	2.1	1.3	2.9
Acenaphthylene	U	2700	mg/kg	0.10	0.44	0.59	0.95	1.2
Acenaphthene	U	2700	mg/kg	0.10	0.66	0.56	0.73	0.95
Fluorene	U	2700	mg/kg	0.10	0.47	0.53	1.1	1.3
Phenanthrene	U	2700	mg/kg	0.10	1.4	1.6	6.1	6.6
Anthracene	U	2700	mg/kg	0.10	0.37	0.45	1.1	1.6
Fluoranthene	U	2700	mg/kg	0.10	1.2	1.0	5.2	5.4
Pyrene	U	2700	mg/kg	0.10	1.2	1.3	5.6	6.3
Benzo[a]anthracene	U	2700	mg/kg	0.10	0.38	0.77	2.6	2.7
Chrysene	U	2700	mg/kg	0.10	0.77	0.83	3.2	3.2
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	0.58	0.60	2.5	2.8
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	0.39	0.37	1.2	1.4
Benzo[a]pyrene	U	2700	mg/kg	0.10	0.50	0.56	2.1	2.6
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	< 0.10	0.34	1.2	1.7
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	< 0.10	0.24	0.62	0.81
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	< 0.10	0.33	1.3	1.7
Total Of 16 PAH's	U	2700	mg/kg	2.0	11	12	37	43
Benzene	U	2760	µg/kg	1.0	26	8.3	15	8.5
Toluene	U	2760	µg/kg	1.0	44	3.2	8.1	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	14	6.3	17	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	81	5.2	21	< 1.0
o-Xylene	U	2760	µg/kg	1.0	33	3.3	15	< 1.0
Total Phenols	U	2920	mg/kg	0.10	< 0.10	< 0.10	< 0.10	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com

eurofins | Chemtest
Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

UKAS TESTING 2183

Final Report

Report No.:	21-31212-1
Initial Date of Issue:	16-Sep-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Sam Lane-Ryan
Project	101114 BAM Construction Site

Quotation No.:	Q21-23216	**Date Received:**	09-Sep-2021
Order No.:	9746	**Date Instructed:**	09-Sep-2021
No. of Samples:	2		
Turnaround (Wkdays):	5	**Results Due:**	15-Sep-2021
Date Approved:	16-Sep-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-31212	21-31212
Quotation No.: Q21-23216			**Chemtest Sample ID.:**		1275438	1275439
Order No.: 9746			Client Sample Ref.:		HLM/E7	HLM/F7
			Sample Location:		E7	F7
			Sample Type:		SOIL	SOIL
			Date Sampled:		07-Sep-2021	07-Sep-2021
			Asbestos Lab:		DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
ACM Type	U	2192		N/A	-	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected	No Asbestos Detected
Moisture	N	2030	%	0.020	7.1	6.1
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Arsenic	U	2450	mg/kg	1.0	2.7	2.6
Cadmium	U	2450	mg/kg	0.10	0.26	0.14
Chromium	U	2450	mg/kg	1.0	18	13
Copper	U	2450	mg/kg	0.50	24	23
Mercury	U	2450	mg/kg	0.10	0.14	1.2
Nickel	U	2450	mg/kg	0.50	22	15
Lead	U	2450	mg/kg	0.50	28	32
Selenium	U	2450	mg/kg	0.20	< 0.20	< 0.20
Zinc	U	2450	mg/kg	0.50	65	54
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	95
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	95
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	3.8
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	32
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	36
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	< 10	130
Naphthalene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Acenaphthylene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Acenaphthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Fluorene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Phenanthrene	U	2700	mg/kg	0.10	0.80	0.13
Anthracene	U	2700	mg/kg	0.10	0.31	0.30

Results - Soil

Project: 101114 BAM Construction Site

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-31212	21-31212
Quotation No.: Q21-23216			**Chemtest Sample ID.:**		1275438	1275439
Order No.: 9746			Client Sample Ref.:		HLM/E7	HLM/F7
			Sample Location:		E7	F7
			Sample Type:		SOIL	SOIL
			Date Sampled:		07-Sep-2021	07-Sep-2021
			Asbestos Lab:		DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
Fluoranthene	U	2700	mg/kg	0.10	1.6	1.8
Pyrene	U	2700	mg/kg	0.10	1.7	2.7
Benzo[a]anthracene	U	2700	mg/kg	0.10	1.3	< 0.10
Chrysene	U	2700	mg/kg	0.10	1.4	< 0.10
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[a]pyrene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Total Of 16 PAH's	U	2700	mg/kg	2.0	7.1	4.9
Benzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0

Test Methods

SOP	Title	Parameters included	Method summary
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com


eurofins | Chemtest
Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-14028-1
Initial Date of Issue:	05-May-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Andy Clee Jon Owens Charlie Gould Sam Gould
Project	101114 Bam Construction Site, Sportcity Way, Manchester M11

Quotation No.:		**Date Received:**	29-Apr-2021
Order No.:	9848	**Date Instructed:**	29-Apr-2021
No. of Samples:	2		
Turnaround (Wkdays):	4	**Results Due:**	05-May-2021
Date Approved:	05-May-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 Bam Construction Site, Sportcity Way, Manchester M11

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-14028	21-14028
Quotation No.:			**Chemtest Sample ID.:**		1189772	1189773
			Client Sample ID.:		PA2/02	PA2/03
			Sample Location:		PA2	PA2
			Sample Type:		SOIL	SOIL
			Date Sampled:		27-Apr-2021	27-Apr-2021
			Asbestos Lab:		COVENTRY	COVENTRY
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
ACM Type	U	2192		N/A	-	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected	No Asbestos Detected
ACM Detection Stage	U	2192		N/A	-	-
Moisture	N	2030	%	0.020	7.5	3.1
pH	M	2010		4.0	9.0	8.9
Sulphate (2:1 Water Soluble) as SO4	M	2120	g/l	0.010	< 0.010	0.22
Sulphur (Elemental)	M	2180	mg/kg	1.0	33	12
Cyanide (Complex)	M	2300	mg/kg	0.50	3.4	0.80
Cyanide (Free)	M	2300	mg/kg	0.50	< 0.50	< 0.50
Cyanide (Total)	M	2300	mg/kg	0.50	3.4	0.80
Sulphate (Total)	M	2430	%	0.010	0.48	0.17
Arsenic	M	2450	mg/kg	1.0	34	9.0
Cadmium	M	2450	mg/kg	0.10	0.31	0.23
Chromium	M	2450	mg/kg	1.0	18	15
Copper	M	2450	mg/kg	0.50	42	44
Mercury	M	2450	mg/kg	0.10	0.45	1.5
Nickel	M	2450	mg/kg	0.50	27	18
Lead	M	2450	mg/kg	0.50	67	68
Selenium	M	2450	mg/kg	0.20	0.45	< 0.20
Zinc	M	2450	mg/kg	0.50	74	75
LOI	M	2610	%	0.10	5.2	3.7
Total Organic Carbon	M	2625	%	0.20	2.6	1.7
Total TPH >C6-C40	M	2670	mg/kg	10	420	1400
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C8-C10	M	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C10-C12	M	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C12-C16	M	2680	mg/kg	1.0	< 1.0	26
Aliphatic TPH >C16-C21	M	2680	mg/kg	1.0	< 1.0	39
Aliphatic TPH >C21-C35	M	2680	mg/kg	1.0	< 1.0	150
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	30
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	250
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C8-C10	M	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C10-C12	M	2680	mg/kg	1.0	< 1.0	29
Aromatic TPH >C12-C16	M	2680	mg/kg	1.0	< 1.0	330

Results - Soil

Project: 101114 Bam Construction Site, Sportcity Way, Manchester M11

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-14028	21-14028
Quotation No.:			**Chemtest Sample ID.:**		1189772	1189773
			Client Sample ID.:		PA2/02	PA2/03
			Sample Location:		PA2	PA2
			Sample Type:		SOIL	SOIL
			Date Sampled:		27-Apr-2021	27-Apr-2021
			Asbestos Lab:		COVENTRY	COVENTRY
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	74	1200
Aromatic TPH >C21-C35	M	2680	mg/kg	1.0	450	2800
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	220
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	520	4600
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	520	4800
Naphthalene	M	2700	mg/kg	0.10	1.3	3.8
Acenaphthylene	M	2700	mg/kg	0.10	1.3	1.5
Acenaphthene	M	2700	mg/kg	0.10	1.4	4.4
Fluorene	M	2700	mg/kg	0.10	2.1	5.6
Phenanthrene	M	2700	mg/kg	0.10	8.2	27
Anthracene	M	2700	mg/kg	0.10	2.4	6.6
Fluoranthene	M	2700	mg/kg	0.10	7.3	27
Pyrene	M	2700	mg/kg	0.10	8.0	28
Benzo[a]anthracene	M	2700	mg/kg	0.10	3.3	12
Chrysene	M	2700	mg/kg	0.10	3.2	11
Benzo[b]fluoranthene	M	2700	mg/kg	0.10	3.8	10
Benzo[k]fluoranthene	M	2700	mg/kg	0.10	1.7	5.3
Benzo[a]pyrene	M	2700	mg/kg	0.10	3.4	11
Indeno(1,2,3-c,d)Pyrene	M	2700	mg/kg	0.10	2.1	6.6
Dibenz(a,h)Anthracene	M	2700	mg/kg	0.10	0.76	2.6
Benzo[g,h,i]perylene	M	2700	mg/kg	0.10	2.7	6.3
Total Of 16 PAH's	M	2700	mg/kg	2.0	53	170
Benzene	M	2760	µg/kg	1.0	< 1.0	< 1.0
Toluene	M	2760	µg/kg	1.0	< 1.0	< 1.0
Ethylbenzene	M	2760	µg/kg	1.0	< 1.0	< 1.0
m & p-Xylene	M	2760	µg/kg	1.0	< 1.0	< 1.0
o-Xylene	M	2760	µg/kg	1.0	< 1.0	< 1.0
Total Phenols	M	2920	mg/kg	0.10	< 0.10	< 0.10

Results - Single Stage WAC

Project: 101114 Bam Construction Site, Sportcity Way, Manchester M11

					Landfill Waste Acceptance Criteria Limits		
Chemtest Job No:	21-14028						
Chemtest Sample ID:	1189772						
Sample Ref:							
Sample ID:	PA2/02						
Sample Location:	PA2						
Top Depth(m):							
Bottom Depth(m):							
Sampling Date:	27-Apr-2021						
Determinand	**SOP**	**Accred.**	**Units**		**Inert Waste Landfill**	**Stable, Non-reactive hazardous waste in non-hazardous Landfill**	**Hazardous Waste Landfill**
Total Organic Carbon	2625	M	%	2.6	3	5	6
Loss On Ignition	2610	M	%	5.2	--	--	10
Total BTEX	2760	M	mg/kg	< 0.010	6	--	--
Total PCBs (7 Congeners)	2815	M	mg/kg	< 0.10	1	--	--
TPH Total WAC (Mineral Oil)	2670	M	mg/kg	420	500	--	--
Total (Of 17) PAH's	2700	N	mg/kg	53	100	--	--
pH	2010	M		9.0	--	>6	--
Acid Neutralisation Capacity	2015	N	mol/kg	0.0090	--	To evaluate	To evaluate
Eluate Analysis			**10:1 Eluate mg/l**	**10:1 Eluate mg/kg**	**Limit values for compliance leaching test using BS EN 12457 at L/S 10 l/kg**		
Arsenic	1455	U	0.0080	0.080	0.5	2	25
Barium	1455	U	0.017	0.17	20	100	300
Cadmium	1455	U	< 0.00012	< 0.0012	0.04	1	5
Chromium	1455	U	< 0.0005	< 0.0005	0.5	10	70
Copper	1455	U	0.0010	0.0098	2	50	100
Mercury	1455	U	< 0.00005	< 0.00005	0.01	0.2	2
Molybdenum	1455	U	0.0058	0.058	0.5	10	30
Nickel	1455	U	< 0.0005	< 0.0005	0.4	10	40
Lead	1455	U	< 0.0005	< 0.0005	0.5	10	50
Antimony	1455	U	0.0009	0.0092	0.06	0.7	5
Selenium	1455	U	0.0008	0.0078	0.1	0.5	7
Zinc	1455	U	< 0.003	< 0.003	4	50	200
Chloride	1220	U	3.1	31	800	15000	25000
Fluoride	1220	U	0.12	1.2	10	150	500
Sulphate	1220	U	20	200	1000	20000	50000
Total Dissolved Solids	1020	N	65	650	4000	60000	100000
Phenol Index	1920	U	< 0.030	< 0.30	1	-	-
Dissolved Organic Carbon	1610	U	2.7	< 50	500	800	1000

Solid Information	
Dry mass of test portion/kg	0.090
Moisture (%)	7.5

Waste Acceptance Criteria

Landfill WAC analysis (specifically leaching test results) must not be used for hazardous waste classification purposes. This analysis is only applicable for hazardous waste landfill acceptance and does not give any indication as to whether a waste may be hazardous or non-hazardous.

Results - Single Stage WAC

Project: 101114 Bam Construction Site, Sportcity Way, Manchester M11

					Landfill Waste Acceptance Criteria Limits		
Chemtest Job No:	21-14028						
Chemtest Sample ID:	1189773						
Sample Ref:							
Sample ID:	PA2/03						
Sample Location:	PA2						
Top Depth(m):							
Bottom Depth(m):							
Sampling Date:	27-Apr-2021						
Determinand	**SOP**	**Accred.**	**Units**		**Inert Waste Landfill**	**Stable, Non-reactive hazardous waste in non-hazardous Landfill**	**Hazardous Waste Landfill**
Total Organic Carbon	2625	M	%	1.7	3	5	6
Loss On Ignition	2610	M	%	3.7	--	--	10
Total BTEX	2760	M	mg/kg	< 0.010	6	--	--
Total PCBs (7 Congeners)	2815	M	mg/kg	< 0.10	1	--	--
TPH Total WAC (Mineral Oil)	2670	M	mg/kg	1400	500	--	--
Total (Of 17) PAH's	2700	N	mg/kg	170	100	--	--
pH	2010	M		8.9	--	>6	--
Acid Neutralisation Capacity	2015	N	mol/kg	0.010	--	To evaluate	To evaluate
Eluate Analysis			**10:1 Eluate mg/l**	**10:1 Eluate mg/kg**	**Limit values for compliance leaching test using BS EN 12457 at L/S 10 l/kg**		
Arsenic	1455	U	0.0008	0.0078	0.5	2	25
Barium	1455	U	0.009	0.088	20	100	300
Cadmium	1455	U	< 0.00012	< 0.0012	0.04	1	5
Chromium	1455	U	< 0.0005	< 0.0005	0.5	10	70
Copper	1455	U	0.0007	0.0072	2	50	100
Mercury	1455	U	< 0.00005	< 0.00005	0.01	0.2	2
Molybdenum	1455	U	0.0008	0.0076	0.5	10	30
Nickel	1455	U	< 0.0005	< 0.0005	0.4	10	40
Lead	1455	U	< 0.0005	< 0.0005	0.5	10	50
Antimony	1455	U	< 0.0005	< 0.0005	0.06	0.7	5
Selenium	1455	U	< 0.0005	< 0.0005	0.1	0.5	7
Zinc	1455	U	< 0.003	< 0.003	4	50	200
Chloride	1220	U	< 1.0	< 10	800	15000	25000
Fluoride	1220	U	0.10	1.0	10	150	500
Sulphate	1220	U	15	150	1000	20000	50000
Total Dissolved Solids	1020	N	41	410	4000	60000	100000
Phenol Index	1920	U	< 0.030	< 0.30	1	-	-
Dissolved Organic Carbon	1610	U	< 2.5	< 50	500	800	1000

Solid Information	
Dry mass of test portion/kg	0.090
Moisture (%)	3.1

Waste Acceptance Criteria

Landfill WAC analysis (specifically leaching test results) must not be used for hazardous waste classification purposes. This analysis is only applicable for hazardous waste landfill acceptance and does not give any indication as to whether a waste may be hazardous or non-hazardous.

Test Methods

SOP	Title	Parameters included	Method summary
1020	Electrical Conductivity and Total Dissolved Solids (TDS) in Waters	Electrical Conductivity and Total Dissolved Solids (TDS) in Waters	Conductivity Meter
1220	Anions, Alkalinity & Ammonium in Waters	Fluoride; Chloride; Nitrite; Nitrate; Total; Oxidisable Nitrogen (TON); Sulfate; Phosphate; Alkalinity; Ammonium	Automated colorimetric analysis using 'Aquakem 600' Discrete Analyser.
1455	Metals in Waters by ICP-MS	Metals, including: Antimony; Arsenic; Barium; Beryllium; Boron; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Tin; Vanadium; Zinc	Filtration of samples followed by direct determination by inductively coupled plasma mass spectrometry (ICP-MS).
1610	Total/Dissolved Organic Carbon in Waters	Organic Carbon	TOC Analyser using Catalytic Oxidation
1920	Phenols in Waters by HPLC	Phenolic compounds including: Phenol, Cresols, Xylenols, Trimethylphenols Note: Chlorophenols are excluded.	Determination by High Performance Liquid Chromatography (HPLC) using electrochemical detection.
2010	pH Value of Soils	pH	pH Meter
2015	Acid Neutralisation Capacity	Acid Reserve	Titration
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)

Test Methods

SOP	Title	Parameters included	Method summary
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2815	Polychlorinated Biphenyls (PCB) ICES7Congeners in Soils by GC-MS	ICES7 PCB congeners	Acetone/Hexane extraction / GC-MS
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.
640	Characterisation of Waste (Leaching C10)	Waste material including soil, sludges and granular waste	ComplianceTest for Leaching of Granular Waste Material and Sludge

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 45 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com

eurofins | Chemtest
Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com


UKAS TESTING
2183

Final Report

Report No.:	21-31586-1
Initial Date of Issue:	20-Sep-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Sam Lane-Ryan
Project	101114 BAM Construction Site, Sportcity Way, Manchester

Quotation No.:	Q21-24773	**Date Received:**	13-Sep-2021
Order No.:	9848	**Date Instructed:**	13-Sep-2021
No. of Samples:	2		
Turnaround (Wkdays):	5	**Results Due:**	17-Sep-2021
Date Approved:	20-Sep-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-31586	21-31586
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1277496	1277497
Order No.: 9848			Client Sample Ref.:		PA22	PA22
			Client Sample ID.:		/01	/02
			Sample Location:		PA22	PA22
			Sample Type:		SOIL	SOIL
			Date Sampled:		10-Sep-2021	10-Sep-2021
			Asbestos Lab:		COVENTRY	COVENTRY
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
ACM Type	U	2192		N/A	-	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected	No Asbestos Detected
Moisture	N	2030	%	0.020	12	4.9
pH	U	2010		4.0	9.2	9.3
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	0.49	0.24
Sulphur (Elemental)	U	2180	mg/kg	1.0	52	5.0
Cyanide (Complex)	U	2300	mg/kg	0.50	1.1	< 0.50
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	1.3	< 0.50
Sulphate (Total)	U	2430	%	0.010	0.65	0.23
Arsenic	U	2450	mg/kg	1.0	8.2	9.0
Cadmium	U	2450	mg/kg	0.10	0.13	0.15
Chromium	U	2450	mg/kg	1.0	14	16
Copper	U	2450	mg/kg	0.50	19	20
Mercury	U	2450	mg/kg	0.10	< 0.10	< 0.10
Nickel	U	2450	mg/kg	0.50	22	23
Lead	U	2450	mg/kg	0.50	16	17
Selenium	U	2450	mg/kg	0.20	0.30	< 0.20
Zinc	U	2450	mg/kg	0.50	49	51
LOI	U	2610	%	0.10	7.8	7.1
Total Organic Carbon	U	2625	%	0.20	3.6	2.5
Total TPH >C6-C40	U	2670	mg/kg	10	< 10	< 10
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-31586	21-31586
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1277496	1277497
Order No.: 9848			Client Sample Ref.:		PA22	PA22
			Client Sample ID.:		/01	/02
			Sample Location:		PA22	PA22
			Sample Type:		SOIL	SOIL
			Date Sampled:		10-Sep-2021	10-Sep-2021
			Asbestos Lab:		COVENTRY	COVENTRY
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	< 10	< 10
Naphthalene	U	2700	mg/kg	0.10	0.62	0.46
Acenaphthylene	U	2700	mg/kg	0.10	0.88	0.26
Acenaphthene	U	2700	mg/kg	0.10	1.2	0.36
Fluorene	U	2700	mg/kg	0.10	1.4	0.46
Phenanthrene	U	2700	mg/kg	0.10	11	1.9
Anthracene	U	2700	mg/kg	0.10	3.8	0.62
Fluoranthene	U	2700	mg/kg	0.10	13	1.7
Pyrene	U	2700	mg/kg	0.10	13	1.9
Benzo[a]anthracene	U	2700	mg/kg	0.10	5.5	0.96
Chrysene	U	2700	mg/kg	0.10	7.2	1.5
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	5.7	0.96
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	2.3	0.75
Benzo[a]pyrene	U	2700	mg/kg	0.10	4.6	0.78
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	2.9	0.67
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	0.90	0.43
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	2.7	0.71
Total Of 16 PAH's	U	2700	mg/kg	2.0	77	14
Benzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Total Phenols	U	2920	mg/kg	0.10	< 0.10	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com

eurofins | Chemtest
Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com


UKAS TESTING 2183

Final Report

Report No.:	21-32256-1
Initial Date of Issue:	23-Sep-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Sam Lane-Ryan
Project	101114 BAM Construction Site, Sportcity Way, Manchester

Quotation No.:	Q21-23216	**Date Received:**	17-Sep-2021
Order No.:	9746	**Date Instructed:**	17-Sep-2021
No. of Samples:	1		
Turnaround (Wkdays):	5	**Results Due:**	23-Sep-2021
Date Approved:	23-Sep-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-32256
Quotation No.: Q21-23216			**Chemtest Sample ID.:**		1280477
Order No.: 9746			Client Sample Ref.:		HLM/G7
			Sample Type:		SOIL
			Date Sampled:		15-Sep-2021
			Asbestos Lab:		DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**	
ACM Type	U	2192		N/A	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected
Moisture	N	2030	%	0.020	6.4
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50
Arsenic	U	2450	mg/kg	1.0	5.3
Cadmium	U	2450	mg/kg	0.10	0.38
Chromium	U	2450	mg/kg	1.0	340
Copper	U	2450	mg/kg	0.50	24
Mercury	U	2450	mg/kg	0.10	0.54
Nickel	U	2450	mg/kg	0.50	25
Lead	U	2450	mg/kg	0.50	46
Selenium	U	2450	mg/kg	0.20	< 0.20
Zinc	U	2450	mg/kg	0.50	75
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	< 10
Naphthalene	U	2700	mg/kg	0.10	0.28
Acenaphthylene	U	2700	mg/kg	0.10	0.20
Acenaphthene	U	2700	mg/kg	0.10	0.21
Fluorene	U	2700	mg/kg	0.10	0.24
Phenanthrene	U	2700	mg/kg	0.10	1.2
Anthracene	U	2700	mg/kg	0.10	0.39

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-32256
Quotation No.: Q21-23216			**Chemtest Sample ID.:**		1280477
Order No.: 9746			Client Sample Ref.:		HLM/G7
			Sample Type:		SOIL
			Date Sampled:		15-Sep-2021
			Asbestos Lab:		DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**	
Fluoranthene	U	2700	mg/kg	0.10	1.5
Pyrene	U	2700	mg/kg	0.10	1.6
Benzo[a]anthracene	U	2700	mg/kg	0.10	0.94
Chrysene	U	2700	mg/kg	0.10	1.1
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	0.85
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	0.57
Benzo[a]pyrene	U	2700	mg/kg	0.10	0.76
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	0.38
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	0.23
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	0.39
Total Of 16 PAH's	U	2700	mg/kg	2.0	11
Benzene	U	2760	µg/kg	1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0

Test Methods

SOP	Title	Parameters included	Method summary
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com

eurofins | Chemtest
Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com


UKAS TESTING 2183

Final Report

Report No.:	21-32687-1
Initial Date of Issue:	27-Sep-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Sam Lane-Ryan
Project	101114 BAM Construction Site, Sportcity Way, Manchester

Quotation No.:	Q21-24773	**Date Received:**	21-Sep-2021
Order No.:	9848	**Date Instructed:**	21-Sep-2021
No. of Samples:	2		
Turnaround (Wkdays):	5	**Results Due:**	27-Sep-2021
Date Approved:	27-Sep-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-32687	21-32687
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1282985	1282986
Order No.: 9848			Client Sample Ref.:		PA23/01	PA23/01
			Sample Location:		PA23	PA23
			Sample Type:		SOIL	SOIL
			Date Sampled:		17-Sep-2021	17-Sep-2021
			Asbestos Lab:		DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
ACM Type	U	2192		N/A	-	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected	No Asbestos Detected
Moisture	N	2030	%	0.020	15	7.0
pH	U	2010		4.0	9.6	9.2
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	1.1	0.23
Sulphur (Elemental)	U	2180	mg/kg	1.0	13	23
Cyanide (Complex)	U	2300	mg/kg	0.50	7.4	1.5
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	7.5	1.5
Sulphate (Total)	U	2430	%	0.010	0.76	0.59
Arsenic	U	2450	mg/kg	1.0	74	15
Cadmium	U	2450	mg/kg	0.10	0.29	0.10
Chromium	U	2450	mg/kg	1.0	21	12
Copper	U	2450	mg/kg	0.50	160	43
Mercury	U	2450	mg/kg	0.10	0.63	< 0.10
Nickel	U	2450	mg/kg	0.50	52	35
Lead	U	2450	mg/kg	0.50	320	48
Selenium	U	2450	mg/kg	0.20	0.70	0.60
Zinc	U	2450	mg/kg	0.50	170	74
LOI	U	2610	%	0.10	14	11
Total Organic Carbon	U	2625	%	0.20	11	5.2
Total TPH >C6-C40	U	2670	mg/kg	10	91	180
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	7.7	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	17	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	25	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	59	< 1.0

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-32687	21-32687
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1282985	1282986
Order No.: 9848			Client Sample Ref.:		PA23/01	PA23/01
			Sample Location:		PA23	PA23
			Sample Type:		SOIL	SOIL
			Date Sampled:		17-Sep-2021	17-Sep-2021
			Asbestos Lab:		DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	190	< 1.0
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	250	< 5.0
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	280	< 10
Naphthalene	U	2700	mg/kg	0.10	2.4	< 0.10
Acenaphthylene	U	2700	mg/kg	0.10	0.81	< 0.10
Acenaphthene	U	2700	mg/kg	0.10	1.9	< 0.10
Fluorene	U	2700	mg/kg	0.10	1.9	< 0.10
Phenanthrene	U	2700	mg/kg	0.10	13	< 0.10
Anthracene	U	2700	mg/kg	0.10	3.7	< 0.10
Fluoranthene	U	2700	mg/kg	0.10	14	2.8
Pyrene	U	2700	mg/kg	0.10	17	7.2
Benzo[a]anthracene	U	2700	mg/kg	0.10	7.1	< 0.10
Chrysene	U	2700	mg/kg	0.10	8.5	< 0.10
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	7.7	< 0.10
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	4.2	< 0.10
Benzo[a]pyrene	U	2700	mg/kg	0.10	6.6	< 0.10
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	4.8	< 0.10
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	3.3	< 0.10
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	4.4	< 0.10
Total Of 16 PAH's	U	2700	mg/kg	2.0	100	10
Benzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Total Phenols	U	2920	mg/kg	0.10	< 0.10	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com


Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-33509-1
Initial Date of Issue:	01-Oct-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Sam Lane-Ryan
Project	101114 BAM Construction Site, Sportcity Way, Manchester

Quotation No.:	Q21-24773	**Date Received:**	27-Sep-2021
Order No.:	9848	**Date Instructed:**	27-Sep-2021
No. of Samples:	2		
Turnaround (Wkdays):	5	**Results Due:**	01-Oct-2021
Date Approved:	01-Oct-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-33509	21-33509
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1287210	1287211
Order No.: 9848			Client Sample Ref.:		PA24/01	PA24/02
			Sample Location:		PA24	PA24
			Sample Type:		SOIL	SOIL
			Date Sampled:		24-Sep-2021	24-Sep-2021
			Asbestos Lab:		DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
ACM Type	U	2192		N/A	-	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected	No Asbestos Detected
Moisture	N	2030	%	0.020	8.5	8.2
pH	U	2010		4.0	8.5	7.4
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	0.074	0.052
Sulphur (Elemental)	U	2180	mg/kg	1.0	23	17
Cyanide (Complex)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Sulphate (Total)	U	2430	%	0.010	0.21	0.26
Arsenic	U	2450	mg/kg	1.0	6.0	8.2
Cadmium	U	2450	mg/kg	0.10	< 0.10	0.15
Chromium	U	2450	mg/kg	1.0	17	17
Copper	U	2450	mg/kg	0.50	27	33
Mercury	U	2450	mg/kg	0.10	< 0.10	0.11
Nickel	U	2450	mg/kg	0.50	32	33
Lead	U	2450	mg/kg	0.50	21	23
Selenium	U	2450	mg/kg	0.20	0.42	0.60
Zinc	U	2450	mg/kg	0.50	49	53
LOI	U	2610	%	0.10	10	12
Total Organic Carbon	U	2625	%	0.20	2.7	3.6
Total TPH >C6-C40	U	2670	mg/kg	10	42	40
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-33509	21-33509
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1287210	1287211
Order No.: 9848			Client Sample Ref.:		PA24/01	PA24/02
			Sample Location:		PA24	PA24
			Sample Type:		SOIL	SOIL
			Date Sampled:		24-Sep-2021	24-Sep-2021
			Asbestos Lab:		DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	< 10	< 10
Naphthalene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Acenaphthylene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Acenaphthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Fluorene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Phenanthrene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Anthracene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Fluoranthene	U	2700	mg/kg	0.10	0.32	0.35
Pyrene	U	2700	mg/kg	0.10	0.47	0.40
Benzo[a]anthracene	U	2700	mg/kg	0.10	0.28	0.36
Chrysene	U	2700	mg/kg	0.10	0.70	0.41
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	0.17	0.17
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	0.51	0.31
Benzo[a]pyrene	U	2700	mg/kg	0.10	0.20	0.18
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Total Of 16 PAH's	U	2700	mg/kg	2.0	2.7	2.2
Benzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Total Phenols	U	2920	mg/kg	0.10	< 0.10	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com


Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-34599-1
Initial Date of Issue:	12-Oct-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Sam Lane-Ryan
Project	101114 BAM Construction Site, Sportcity Way, Manchester

Quotation No.:	Q21-24773	**Date Received:**	06-Oct-2021
Order No.:	9848	**Date Instructed:**	06-Oct-2021
No. of Samples:	2		
Turnaround (Wkdays):	5	**Results Due:**	12-Oct-2021
Date Approved:	12-Oct-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-34599	21-34599
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1292487	1292488
Order No.: 9848			Client Sample Ref.:		PA25/01	PA25/02
			Sample Location:		PA25	PA25
			Sample Type:		SOIL	SOIL
			Date Sampled:		01-Oct-2021	01-Oct-2021
			Asbestos Lab:		DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
ACM Type	U	2192		N/A	-	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected	No Asbestos Detected
Moisture	N	2030	%	0.020	15	15
pH	U	2010		4.0	10.6	10.4
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	0.46	0.38
Sulphur (Elemental)	U	2180	mg/kg	1.0	11	9.6
Cyanide (Complex)	U	2300	mg/kg	0.50	1.0	0.70
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	1.0	0.70
Sulphate (Total)	U	2430	%	0.010	0.19	0.14
Arsenic	U	2450	mg/kg	1.0	5.8	5.9
Cadmium	U	2450	mg/kg	0.10	0.29	0.33
Chromium	U	2450	mg/kg	1.0	16	12
Copper	U	2450	mg/kg	0.50	35	39
Mercury	U	2450	mg/kg	0.10	2.6	2.0
Nickel	U	2450	mg/kg	0.50	15	12
Lead	U	2450	mg/kg	0.50	130	78
Selenium	U	2450	mg/kg	0.20	< 0.20	< 0.20
Zinc	U	2450	mg/kg	0.50	85	68
LOI	U	2610	%	0.10	4.3	3.9
Total Organic Carbon	U	2625	%	0.20	2.1	3.6
Total TPH >C6-C40	U	2670	mg/kg	10	< 10	< 10
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-34599	21-34599
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1292487	1292488
Order No.: 9848			Client Sample Ref.:		PA25/01	PA25/02
			Sample Location:		PA25	PA25
			Sample Type:		SOIL	SOIL
			Date Sampled:		01-Oct-2021	01-Oct-2021
			Asbestos Lab:		DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	< 10	< 10
Naphthalene	U	2700	mg/kg	0.10	1.5	0.83
Acenaphthylene	U	2700	mg/kg	0.10	1.4	0.59
Acenaphthene	U	2700	mg/kg	0.10	2.2	0.80
Fluorene	U	2700	mg/kg	0.10	1.6	0.83
Phenanthrene	U	2700	mg/kg	0.10	11	6.0
Anthracene	U	2700	mg/kg	0.10	2.3	1.3
Fluoranthene	U	2700	mg/kg	0.10	11	7.5
Pyrene	U	2700	mg/kg	0.10	12	8.0
Benzo[a]anthracene	U	2700	mg/kg	0.10	4.8	3.6
Chrysene	U	2700	mg/kg	0.10	4.7	3.5
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	5.0	3.9
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	2.1	1.7
Benzo[a]pyrene	U	2700	mg/kg	0.10	3.9	3.1
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	2.4	1.9
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	0.94	0.77
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	2.6	2.1
Total Of 16 PAH's	U	2700	mg/kg	2.0	69	46
Benzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Total Phenols	U	2920	mg/kg	0.10	< 0.10	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com


Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-35145-1
Initial Date of Issue:	15-Oct-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Sarah Detheridge Sam Lane-Ryan
Project	101114 BAM Construction Site, Sportcity Way, Manchester

Quotation No.:	Q21-24773	**Date Received:**	11-Oct-2021
Order No.:	9848	**Date Instructed:**	11-Oct-2021
No. of Samples:	2		
Turnaround (Wkdays):	5	**Results Due:**	15-Oct-2021
Date Approved:	15-Oct-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-35145	21-35145
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1295352	1295353
Order No.: 9848			Client Sample Ref.:		PA26/	PA26/
			Client Sample ID.:		01	02
			Sample Location:		PA26	PA26
			Sample Type:		SOIL	SOIL
			Date Sampled:		08-Oct-2021	08-Oct-2021
			Asbestos Lab:		DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
ACM Type	U	2192		N/A	-	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected	No Asbestos Detected
Moisture	N	2030	%	0.020	6.3	5.8
pH	U	2010		4.0	8.6	9.5
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	0.18	0.14
Sulphur (Elemental)	U	2180	mg/kg	1.0	9.4	< 1.0
Cyanide (Complex)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Sulphate (Total)	U	2430	%	0.010	0.25	0.12
Arsenic	U	2450	mg/kg	1.0	9.6	4.7
Cadmium	U	2450	mg/kg	0.10	0.14	< 0.10
Chromium	U	2450	mg/kg	1.0	18	9.2
Copper	U	2450	mg/kg	0.50	25	16
Mercury	U	2450	mg/kg	0.10	< 0.10	< 0.10
Nickel	U	2450	mg/kg	0.50	34	17
Lead	U	2450	mg/kg	0.50	19	16
Selenium	U	2450	mg/kg	0.20	0.21	< 0.20
Zinc	U	2450	mg/kg	0.50	59	26
LOI	U	2610	%	0.10	7.4	5.4
Total Organic Carbon	U	2625	%	0.20	2.1	1.5
Total TPH >C6-C40	U	2670	mg/kg	10	< 10	< 10
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-35145	21-35145
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1295352	1295353
Order No.: 9848			Client Sample Ref.:		PA26/	PA26/
			Client Sample ID.:		01	02
			Sample Location:		PA26	PA26
			Sample Type:		SOIL	SOIL
			Date Sampled:		08-Oct-2021	08-Oct-2021
			Asbestos Lab:		DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	< 10	< 10
Naphthalene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Acenaphthylene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Acenaphthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Fluorene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Phenanthrene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Anthracene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Fluoranthene	U	2700	mg/kg	0.10	0.24	0.16
Pyrene	U	2700	mg/kg	0.10	0.38	0.24
Benzo[a]anthracene	U	2700	mg/kg	0.10	1.3	< 0.10
Chrysene	U	2700	mg/kg	0.10	0.99	< 0.10
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[a]pyrene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Total Of 16 PAH's	U	2700	mg/kg	2.0	2.9	< 2.0
Benzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Total Phenols	U	2920	mg/kg	0.10	< 0.10	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com


Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-36136-1
Initial Date of Issue:	22-Oct-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Sam Lane-Ryan
Project	101114 BAM Construction Site, Sportcity Way, Manchester

Quotation No.:	Q21-24773	**Date Received:**	18-Oct-2021
Order No.:	9848	**Date Instructed:**	18-Oct-2021
No. of Samples:	2		
Turnaround (Wkdays):	5	**Results Due:**	22-Oct-2021
Date Approved:	22-Oct-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-36136	21-36136
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1300365	1300366
Order No.: 9848			Client Sample Ref.:		PA27/01	PA27/02
			Sample Location:		PA27	PA27
			Sample Type:		SOIL	SOIL
			Date Sampled:		15-Oct-2021	15-Oct-2021
			Asbestos Lab:		DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
ACM Type	U	2192		N/A	-	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected	No Asbestos Detected
Asbestos by Gravimetry	U	2192	%	0.001	-	-
Total Asbestos	U	2192	%	0.001	-	-
Moisture	N	2030	%	0.020	6.4	5.5
pH	U	2010		4.0	10.0	11.7
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	0.12	0.47
Sulphur (Elemental)	U	2180	mg/kg	1.0	34	1.9
Cyanide (Complex)	U	2300	mg/kg	0.50	0.60	< 0.50
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	0.60	< 0.50
Sulphate (Total)	U	2430	%	0.010	0.11	0.25
Arsenic	U	2450	mg/kg	1.0	3.6	4.4
Cadmium	U	2450	mg/kg	0.10	< 0.10	0.13
Chromium	U	2450	mg/kg	1.0	12	10
Copper	U	2450	mg/kg	0.50	46	21
Mercury	U	2450	mg/kg	0.10	< 0.10	0.10
Nickel	U	2450	mg/kg	0.50	21	13
Lead	U	2450	mg/kg	0.50	13	15
Selenium	U	2450	mg/kg	0.20	< 0.20	< 0.20
Zinc	U	2450	mg/kg	0.50	51	44
LOI	U	2610	%	0.10	5.4	5.4
Total Organic Carbon	U	2625	%	0.20	1.2	1.2
Total TPH >C6-C40	U	2670	mg/kg	10	< 10	23
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-36136	21-36136
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1300365	1300366
Order No.: 9848			Client Sample Ref.:		PA27/01	PA27/02
			Sample Location:		PA27	PA27
			Sample Type:		SOIL	SOIL
			Date Sampled:		15-Oct-2021	15-Oct-2021
			Asbestos Lab:		DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	< 10	< 10
Naphthalene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Acenaphthylene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Acenaphthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Fluorene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Phenanthrene	U	2700	mg/kg	0.10	< 0.10	1.2
Anthracene	U	2700	mg/kg	0.10	< 0.10	0.24
Fluoranthene	U	2700	mg/kg	0.10	0.93	1.6
Pyrene	U	2700	mg/kg	0.10	0.82	1.4
Benzo[a]anthracene	U	2700	mg/kg	0.10	< 0.10	0.79
Chrysene	U	2700	mg/kg	0.10	< 0.10	0.84
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	< 0.10	0.64
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	< 0.10	0.57
Benzo[a]pyrene	U	2700	mg/kg	0.10	< 0.10	0.62
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	< 0.10	0.25
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	< 0.10	0.19
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	< 0.10	0.32
Total Of 16 PAH's	U	2700	mg/kg	2.0	< 2.0	8.7
Benzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Total Phenols	U	2920	mg/kg	0.10	< 0.10	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com


Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-37310-1
Initial Date of Issue:	02-Nov-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Sam Lane-Ryan
Project	101114 BAM Construction Site, Sportcity Way, Manchester

Quotation No.:	Q21-24773	**Date Received:**	26-Oct-2021
Order No.:	9848	**Date Instructed:**	26-Oct-2021
No. of Samples:	2		
Turnaround (Wkdays):	5	**Results Due:**	01-Nov-2021
Date Approved:	02-Nov-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-37310	21-37310
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1306468	1306469
Order No.: 9848			Client Sample Ref.:		PA28/01	PA28/02
			Sample Location:		PA28	PA28
			Sample Type:		SOIL	SOIL
			Date Sampled:		22-Oct-2021	22-Oct-2021
			Asbestos Lab:		DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
ACM Type	U	2192		N/A	-	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected	No Asbestos Detected
Moisture	N	2030	%	0.020	7.1	7.0
pH	U	2010		4.0	11.5	11.5
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	0.42	0.35
Sulphur (Elemental)	U	2180	mg/kg	1.0	< 1.0	< 1.0
Cyanide (Complex)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Sulphate (Total)	U	2430	%	0.010	0.48	0.49
Arsenic	U	2450	mg/kg	1.0	12	11
Cadmium	U	2450	mg/kg	0.10	0.26	0.49
Chromium	U	2450	mg/kg	1.0	22	24
Copper	U	2450	mg/kg	0.50	42	43
Mercury	U	2450	mg/kg	0.10	< 0.10	< 0.10
Nickel	U	2450	mg/kg	0.50	38	46
Lead	U	2450	mg/kg	0.50	25	28
Selenium	U	2450	mg/kg	0.20	0.30	0.46
Zinc	U	2450	mg/kg	0.50	67	80
LOI	U	2610	%	0.10	4.5	2.8
Total Organic Carbon	U	2625	%	0.20	2.3	1.1
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-37310	21-37310
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1306468	1306469
Order No.: 9848			Client Sample Ref.:		PA28/01	PA28/02
			Sample Location:		PA28	PA28
			Sample Type:		SOIL	SOIL
			Date Sampled:		22-Oct-2021	22-Oct-2021
			Asbestos Lab:		DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	< 10	< 10
Naphthalene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Acenaphthylene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Acenaphthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Fluorene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Phenanthrene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Anthracene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Fluoranthene	U	2700	mg/kg	0.10	0.18	< 0.10
Pyrene	U	2700	mg/kg	0.10	0.14	< 0.10
Benzo[a]anthracene	U	2700	mg/kg	0.10	0.11	< 0.10
Chrysene	U	2700	mg/kg	0.10	0.20	< 0.10
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[a]pyrene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Total Of 16 PAH's	U	2700	mg/kg	2.0	< 2.0	< 2.0
Benzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Total Phenols	U	2920	mg/kg	0.10	< 0.10	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com

Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

2183

Final Report

Report No.:	21-40110-1		
Initial Date of Issue:	22-Nov-2021		
Client	Provectus Group Ltd		
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE		
Contact(s):	Charlotte Nicholson		
Project	101114 BAM Construction Site, Sportcity Way		
Quotation No.:	Q21-23216	**Date Received:**	16-Nov-2021
Order No.:	9746	**Date Instructed:**	16-Nov-2021
No. of Samples:	2		
Turnaround (Wkdays):	5	**Results Due:**	22-Nov-2021
Date Approved:	22-Nov-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way

Client: Provectus Group Ltd		**Chemtest Job No.:**			21-40110	21-40110
Quotation No.: Q21-23216		**Chemtest Sample ID.:**			1320192	1320193
Order No.: 9746		Client Sample Ref.:			LLMF2/01	LLMF2/02
		Sample Location:			F2	F2
		Sample Type:			SOIL	SOIL
		Date Sampled:			12-Nov-2021	12-Nov-2021
		Asbestos Lab:			DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
ACM Type	U	2192		N/A	-	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected	No Asbestos Detected
Moisture	N	2030	%	0.020	8.5	7.0
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Arsenic	U	2450	mg/kg	1.0	1.5	< 1.0
Cadmium	U	2450	mg/kg	0.10	0.23	0.16
Chromium	U	2450	mg/kg	1.0	12	8.9
Copper	U	2450	mg/kg	0.50	8.8	3.3
Mercury	U	2450	mg/kg	0.10	< 0.10	< 0.10
Nickel	U	2450	mg/kg	0.50	23	18
Lead	U	2450	mg/kg	0.50	7.2	4.5
Selenium	U	2450	mg/kg	0.20	< 0.20	< 0.20
Zinc	U	2450	mg/kg	0.50	34	18
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	< 10	< 10
Naphthalene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Acenaphthylene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Acenaphthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Fluorene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Phenanthrene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Anthracene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Fluoranthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Pyrene	U	2700	mg/kg	0.10	< 0.10	< 0.10

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-40110	21-40110
Quotation No.: Q21-23216			**Chemtest Sample ID.:**		1320192	1320193
Order No.: 9746			Client Sample Ref.:		LLMF2/01	LLMF2/02
			Sample Location:		F2	F2
			Sample Type:		SOIL	SOIL
			Date Sampled:		12-Nov-2021	12-Nov-2021
			Asbestos Lab:		DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
Benzo[a]anthracene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Chrysene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[a]pyrene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Total Of 16 PAH's	U	2700	mg/kg	2.0	< 2.0	< 2.0
Benzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0

Test Methods

SOP	Title	Parameters included	Method summary
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com

Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

2183

Final Report

Report No.:	21-40535-1
Initial Date of Issue:	24-Nov-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Tom Harrington Charlotte Nicholson
Project	101114 BAM Construction Site, Sportcity Way

Quotation No.:	Q21-24773	**Date Received:**	18-Nov-2021
Order No.:	9848	**Date Instructed:**	18-Nov-2021
No. of Samples:	1		
Turnaround (Wkdays):	5	**Results Due:**	24-Nov-2021
Date Approved:	24-Nov-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-40535
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1322302
Order No.: 9848			Client Sample Ref.:		PA29/01
			Sample Location:		PA29
			Sample Type:		SOIL
			Date Sampled:		16-Nov-2021
			Asbestos Lab:		DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**	
ACM Type	U	2192		N/A	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected
Moisture	N	2030	%	0.020	9.7
pH	U	2010		4.0	11.7
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	0.36
Sulphur (Elemental)	U	2180	mg/kg	1.0	< 1.0
Cyanide (Complex)	U	2300	mg/kg	0.50	< 0.50
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	< 0.50
Sulphate (Total)	U	2430	%	0.010	0.26
Arsenic	U	2450	mg/kg	1.0	7.2
Cadmium	U	2450	mg/kg	0.10	0.18
Chromium	U	2450	mg/kg	1.0	13
Copper	U	2450	mg/kg	0.50	14
Mercury	U	2450	mg/kg	0.10	< 0.10
Nickel	U	2450	mg/kg	0.50	19
Lead	U	2450	mg/kg	0.50	11
Selenium	U	2450	mg/kg	0.20	0.23
Zinc	U	2450	mg/kg	0.50	39
LOI	U	2610	%	0.10	4.5
Total Organic Carbon	U	2625	%	0.20	1.7
Total TPH >C6-C40	U	2670	mg/kg	10	< 10
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	< 10

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-40535
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1322302
Order No.: 9848			Client Sample Ref.:		PA29/01
			Sample Location:		PA29
			Sample Type:		SOIL
			Date Sampled:		16-Nov-2021
			Asbestos Lab:		DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**	
Naphthalene	U	2700	mg/kg	0.10	< 0.10
Acenaphthylene	U	2700	mg/kg	0.10	< 0.10
Acenaphthene	U	2700	mg/kg	0.10	< 0.10
Fluorene	U	2700	mg/kg	0.10	< 0.10
Phenanthrene	U	2700	mg/kg	0.10	0.36
Anthracene	U	2700	mg/kg	0.10	0.10
Fluoranthene	U	2700	mg/kg	0.10	0.36
Pyrene	U	2700	mg/kg	0.10	0.51
Benzo[a]anthracene	U	2700	mg/kg	0.10	0.22
Chrysene	U	2700	mg/kg	0.10	0.33
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	< 0.10
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	< 0.10
Benzo[a]pyrene	U	2700	mg/kg	0.10	< 0.10
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	< 0.10
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	< 0.10
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	< 0.10
Total Of 16 PAH's	U	2700	mg/kg	2.0	< 2.0
Benzene	U	2760	µg/kg	1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	1.2
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0
Total Phenols	U	2920	mg/kg	0.10	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com


Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-15043-1
Initial Date of Issue:	13-May-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Sam Lane-Ryan
Project	101114 BAM Construction Site, Sportcity Way

Quotation No.:		**Date Received:**	07-May-2021
Order No.:	9848	**Date Instructed:**	07-May-2021
No. of Samples:	2		
Turnaround (Wkdays):	5	**Results Due:**	13-May-2021
Date Approved:	13-May-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-15043	21-15043
Quotation No.:			**Chemtest Sample ID.:**		1195460	1195461
			Client Sample ID.:		PA3/01	PA3/02
			Sample Location:		PA3	PA3
			Sample Type:		SOIL	SOIL
			Date Sampled:		06-May-2021	06-May-2021
			Asbestos Lab:		DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
ACM Type	U	2192		N/A	-	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected	No Asbestos Detected
ACM Detection Stage	U	2192		N/A	-	-
Moisture	N	2030	%	0.020	8.8	12
pH	U	2010		4.0	8.4	10.1
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	< 0.010	0.040
Sulphur (Elemental)	U	2180	mg/kg	1.0	< 1.0	14
Cyanide (Complex)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Sulphate (Total)	U	2430	%	0.010	0.27	0.32
Arsenic	U	2450	mg/kg	1.0	4.1	8.9
Cadmium	U	2450	mg/kg	0.10	0.16	0.22
Chromium	U	2450	mg/kg	1.0	14	17
Copper	U	2450	mg/kg	0.50	26	25
Mercury	U	2450	mg/kg	0.10	0.17	0.34
Nickel	U	2450	mg/kg	0.50	33	28
Lead	U	2450	mg/kg	0.50	24	36
Selenium	U	2450	mg/kg	0.20	0.73	0.27
Zinc	U	2450	mg/kg	0.50	64	60
LOI	U	2610	%	0.10	5.5	6.3
Total Organic Carbon	U	2625	%	0.20	0.94	2.3
Total TPH >C6-C40	U	2670	mg/kg	10	< 10	110
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-15043	21-15043
Quotation No.:			**Chemtest Sample ID.:**		1195460	1195461
			Client Sample ID.:		PA3/01	PA3/02
			Sample Location:		PA3	PA3
			Sample Type:		SOIL	SOIL
			Date Sampled:		06-May-2021	06-May-2021
			Asbestos Lab:		DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	< 10	< 10
Naphthalene	U	2700	mg/kg	0.10	< 0.10	1.5
Acenaphthylene	U	2700	mg/kg	0.10	< 0.10	0.74
Acenaphthene	U	2700	mg/kg	0.10	< 0.10	0.83
Fluorene	U	2700	mg/kg	0.10	< 0.10	1.2
Phenanthrene	U	2700	mg/kg	0.10	< 0.10	4.6
Anthracene	U	2700	mg/kg	0.10	< 0.10	0.91
Fluoranthene	U	2700	mg/kg	0.10	< 0.10	4.0
Pyrene	U	2700	mg/kg	0.10	< 0.10	4.6
Benzo[a]anthracene	U	2700	mg/kg	0.10	< 0.10	2.4
Chrysene	U	2700	mg/kg	0.10	< 0.10	2.1
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	< 0.10	2.6
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	< 0.10	1.5
Benzo[a]pyrene	U	2700	mg/kg	0.10	< 0.10	2.4
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Total Of 16 PAH's	U	2700	mg/kg	2.0	< 2.0	29
Benzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Total Phenols	U	2920	mg/kg	0.10	< 0.10	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 45 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com

Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

2183

Final Report

Report No.:	21-40841-1
Initial Date of Issue:	26-Nov-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Tom Harrington
Project	101114 BAM Construction Site, Sportcity Way, Manchester
Quotation No.:	Q21-23216
Order No.:	9746
No. of Samples:	2
Turnaround (Wkdays):	5
Date Approved:	26-Nov-2021
Approved By:	
Details:	Glynn Harvey, Technical Manager

Date Received:	22-Nov-2021
Date Instructed:	22-Nov-2021
Results Due:	26-Nov-2021

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd					Chemtest Job No.:	21-40841	21-40841
Quotation No.: Q21-23216					Chemtest Sample ID.:	1324003	1324004
Order No.: 9746					Client Sample Ref.:	SOUTH RAMP/01	SOUTH RAMP/02
					Sample Type:	SOIL	SOIL
					Date Sampled:	18-Nov-2021	18-Nov-2021
					Asbestos Lab:	DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**			
ACM Type	U	2192		N/A		-	-
Asbestos Identification	U	2192		N/A		No Asbestos Detected	No Asbestos Detected
Moisture	N	2030	%	0.020		9.2	9.7
Cyanide (Free)	U	2300	mg/kg	0.50		< 0.50	< 0.50
Arsenic	U	2450	mg/kg	1.0		4.6	5.0
Cadmium	U	2450	mg/kg	0.10		0.22	0.21
Chromium	U	2450	mg/kg	1.0		15	12
Copper	U	2450	mg/kg	0.50		21	14
Mercury	U	2450	mg/kg	0.10		< 0.10	< 0.10
Nickel	U	2450	mg/kg	0.50		20	18
Lead	U	2450	mg/kg	0.50		15	13
Selenium	U	2450	mg/kg	0.20		< 0.20	< 0.20
Zinc	U	2450	mg/kg	0.50		40	36
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0		< 1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0		< 1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0		< 1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0		< 1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0		< 1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0		< 1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0		< 1.0	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0		< 1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0		< 5.0	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0		< 1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0		< 1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0		< 1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0		< 1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0		< 1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0		< 1.0	< 1.0
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0		< 1.0	< 1.0
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0		< 1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0		< 5.0	< 5.0
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0		< 10	< 10
Naphthalene	U	2700	mg/kg	0.10		< 0.10	< 0.10
Acenaphthylene	U	2700	mg/kg	0.10		< 0.10	< 0.10
Acenaphthene	U	2700	mg/kg	0.10		< 0.10	< 0.10
Fluorene	U	2700	mg/kg	0.10		< 0.10	< 0.10
Phenanthrene	U	2700	mg/kg	0.10		0.56	0.36
Anthracene	U	2700	mg/kg	0.10		0.14	0.13
Fluoranthene	U	2700	mg/kg	0.10		0.71	0.44
Pyrene	U	2700	mg/kg	0.10		0.90	0.50

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			Chemtest Job No.:		21-40841	21-40841
Quotation No.: Q21-23216			Chemtest Sample ID.:		1324003	1324004
Order No.: 9746			Client Sample Ref.:		SOUTH RAMP/01	SOUTH RAMP/02
			Sample Type:		SOIL	SOIL
			Date Sampled:		18-Nov-2021	18-Nov-2021
			Asbestos Lab:		DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
Benzo[a]anthracene	U	2700	mg/kg	0.10	0.45	0.33
Chrysene	U	2700	mg/kg	0.10	0.55	0.36
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	0.29	0.23
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	0.14	0.13
Benzo[a]pyrene	U	2700	mg/kg	0.10	0.33	0.24
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Total Of 16 PAH's	U	2700	mg/kg	2.0	4.1	2.7
Benzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0

Test Methods

SOP	Title	Parameters included	Method summary
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com

Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

2183

Final Report

Report No.:	21-40840-1
Initial Date of Issue:	26-Nov-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Tom Harrington
Project	101114 BAM Construction Site, Sportcity Way, Manchester

Quotation No.:	Q21-24773	**Date Received:**	22-Nov-2021
Order No.:	9848	**Date Instructed:**	22-Nov-2021
No. of Samples:	1		
Turnaround (Wkdays):	5	**Results Due:**	26-Nov-2021
Date Approved:	26-Nov-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-40840
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1324002
			Client Sample ID.:		PA30/01
			Sample Type:		SOIL
			Date Sampled:		19-Nov-2021
			Asbestos Lab:		DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**	
ACM Type	U	2192		N/A	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected
Moisture	N	2030	%	0.020	10
pH	U	2010		4.0	11.1
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	0.10
Sulphur (Elemental)	U	2180	mg/kg	1.0	34
Cyanide (Complex)	U	2300	mg/kg	0.50	< 0.50
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	< 0.50
Sulphate (Total)	U	2430	%	0.010	0.27
Arsenic	U	2450	mg/kg	1.0	10
Cadmium	U	2450	mg/kg	0.10	0.18
Chromium	U	2450	mg/kg	1.0	18
Copper	U	2450	mg/kg	0.50	28
Mercury	U	2450	mg/kg	0.10	< 0.10
Nickel	U	2450	mg/kg	0.50	29
Lead	U	2450	mg/kg	0.50	13
Selenium	U	2450	mg/kg	0.20	0.26
Zinc	U	2450	mg/kg	0.50	56
LOI	U	2610	%	0.10	4.7
Total Organic Carbon	U	2625	%	0.20	1.1
Total TPH >C6-C40	U	2670	mg/kg	10	< 10
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	< 10

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-40840
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1324002
			Client Sample ID.:		PA30/01
			Sample Type:		SOIL
			Date Sampled:		19-Nov-2021
			Asbestos Lab:		DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**	
Naphthalene	U	2700	mg/kg	0.10	< 0.10
Acenaphthylene	U	2700	mg/kg	0.10	< 0.10
Acenaphthene	U	2700	mg/kg	0.10	< 0.10
Fluorene	U	2700	mg/kg	0.10	< 0.10
Phenanthrene	U	2700	mg/kg	0.10	< 0.10
Anthracene	U	2700	mg/kg	0.10	< 0.10
Fluoranthene	U	2700	mg/kg	0.10	0.13
Pyrene	U	2700	mg/kg	0.10	0.18
Benzo[a]anthracene	U	2700	mg/kg	0.10	< 0.10
Chrysene	U	2700	mg/kg	0.10	< 0.10
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	< 0.10
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	< 0.10
Benzo[a]pyrene	U	2700	mg/kg	0.10	< 0.10
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	< 0.10
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	< 0.10
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	< 0.10
Total Of 16 PAH's	U	2700	mg/kg	2.0	< 2.0
Benzene	U	2760	µg/kg	1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0
Total Phenols	U	2920	mg/kg	0.10	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com

eurofins | Chemtest
Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com


UKAS TESTING 2183

Final Report

Report No.:	21-42077-1
Initial Date of Issue:	06-Dec-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Tom Harrington
Project	101114 BAM Construction Site, Sportcity Way, Manchester

Quotation No.:	Q21-24773	**Date Received:**	30-Nov-2021
Order No.:	9848	**Date Instructed:**	30-Nov-2021
No. of Samples:	1		
Turnaround (Wkdays):	5	**Results Due:**	06-Dec-2021
Date Approved:	06-Dec-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-42077
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1330122
Order No.: 9848			Client Sample Ref.:		PA31/01
			Sample Location:		PA31
			Sample Type:		SOIL
			Date Sampled:		26-Nov-2021
			Asbestos Lab:		DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**	
ACM Type	U	2192		N/A	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected
Moisture	N	2030	%	0.020	7.7
pH	U	2010		4.0	11.5
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	0.27
Sulphur (Elemental)	U	2180	mg/kg	1.0	19
Cyanide (Complex)	U	2300	mg/kg	0.50	< 0.50
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	< 0.50
Sulphate (Total)	U	2430	%	0.010	0.36
Arsenic	U	2450	mg/kg	1.0	9.1
Cadmium	U	2450	mg/kg	0.10	0.33
Chromium	U	2450	mg/kg	1.0	25
Copper	U	2450	mg/kg	0.50	46
Mercury	U	2450	mg/kg	0.10	< 0.10
Nickel	U	2450	mg/kg	0.50	35
Lead	U	2450	mg/kg	0.50	20
Selenium	U	2450	mg/kg	0.20	0.31
Zinc	U	2450	mg/kg	0.50	81
LOI	U	2610	%	0.10	5.2
Total Organic Carbon	U	2625	%	0.20	1.5
Total TPH >C6-C40	U	2670	mg/kg	10	< 10
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-42077
Quotation No.: Q21-24773			**Chemtest Sample ID.:**		1330122
Order No.: 9848			Client Sample Ref.:		PA31/01
			Sample Location:		PA31
			Sample Type:		SOIL
			Date Sampled:		26-Nov-2021
			Asbestos Lab:		DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**	
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	< 10
Naphthalene	U	2700	mg/kg	0.10	< 0.10
Acenaphthylene	U	2700	mg/kg	0.10	< 0.10
Acenaphthene	U	2700	mg/kg	0.10	< 0.10
Fluorene	U	2700	mg/kg	0.10	< 0.10
Phenanthrene	U	2700	mg/kg	0.10	< 0.10
Anthracene	U	2700	mg/kg	0.10	< 0.10
Fluoranthene	U	2700	mg/kg	0.10	< 0.10
Pyrene	U	2700	mg/kg	0.10	< 0.10
Benzo[a]anthracene	U	2700	mg/kg	0.10	< 0.10
Chrysene	U	2700	mg/kg	0.10	< 0.10
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	< 0.10
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	< 0.10
Benzo[a]pyrene	U	2700	mg/kg	0.10	< 0.10
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	< 0.10
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	< 0.10
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	< 0.10
Total Of 16 PAH's	U	2700	mg/kg	2.0	< 2.0
Benzene	U	2760	µg/kg	1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0
Total Phenols	U	2920	mg/kg	0.10	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com

eurofins | Chemtest
Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

UKAS TESTING
2183

Final Report

Report No.:	21-15674-1
Initial Date of Issue:	18-May-2021
Client	Provectus Group Ltd
Client Address:	Regent House Bath Avenue Wolverhampton Staffordshire WV1 4EG
Contact(s):	Charlotte Nicholson Sam Lane-Ryan
Project	101114 BAM Construction Site, Sportcity Way, Manchester

Quotation No.:		**Date Received:**	12-May-2021
Order No.:	9848	**Date Instructed:**	12-May-2021
No. of Samples:	3		
Turnaround (Wkdays):	5	**Results Due:**	18-May-2021
Date Approved:	18-May-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd		Chemtest Job No.:			21-15674	21-15674	21-15674
Quotation No.:		Chemtest Sample ID.:			1198590	1198591	1198592
		Client Sample ID.:			PA4/01	PA4/02	PA4/03
		Sample Location:			PA4	PA4	PA4
		Sample Type:			SOIL	SOIL	SOIL
		Date Sampled:			10-May-2021	10-May-2021	10-May-2021
		Asbestos Lab:			COVENTRY	COVENTRY	COVENTRY
Determinand	**Accred.**	**SOP**	**Units**	**LOD**			
ACM Type	U	2192		N/A	-	-	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected	No Asbestos Detected	No Asbestos Detected
ACM Detection Stage	U	2192		N/A	-	-	-
Moisture	N	2030	%	0.020	13	14	15
pH	U	2010		4.0	8.6	10.0	10.6
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	0.010	0.64	< 0.010
Sulphur (Elemental)	U	2180	mg/kg	1.0	15	160	26
Cyanide (Complex)	U	2300	mg/kg	0.50	2.1	3.7	1.6
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50	< 0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	2.1	3.7	1.6
Sulphate (Total)	U	2430	%	0.010	0.34	1.3	0.33
Arsenic	U	2450	mg/kg	1.0	15	77	17
Cadmium	U	2450	mg/kg	0.10	0.40	0.63	0.19
Chromium	U	2450	mg/kg	1.0	23	29	20
Copper	U	2450	mg/kg	0.50	32	190	41
Mercury	U	2450	mg/kg	0.10	0.11	1.6	0.33
Nickel	U	2450	mg/kg	0.50	40	55	28
Lead	U	2450	mg/kg	0.50	26	440	70
Selenium	U	2450	mg/kg	0.20	1.2	0.58	0.21
Zinc	U	2450	mg/kg	0.50	110	240	79
LOI	U	2610	%	0.10	10	10	4.6
Total Organic Carbon	U	2625	%	0.20	2.9	7.7	1.1
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	9.6	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	9.6	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	6.0	< 1.0
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	48	< 1.0
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	54	< 5.0

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd		Chemtest Job No.:			21-15674	21-15674	21-15674
Quotation No.:		Chemtest Sample ID.:			1198590	1198591	1198592
		Client Sample ID.:			PA4/01	PA4/02	PA4/03
		Sample Location:			PA4	PA4	PA4
		Sample Type:			SOIL	SOIL	SOIL
		Date Sampled:			10-May-2021	10-May-2021	10-May-2021
		Asbestos Lab:			COVENTRY	COVENTRY	COVENTRY
Determinand	**Accred.**	**SOP**	**Units**	**LOD**			
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	< 10	63	< 10
Naphthalene	U	2700	mg/kg	0.10	< 0.10	1.6	0.73
Acenaphthylene	U	2700	mg/kg	0.10	< 0.10	0.75	0.22
Acenaphthene	U	2700	mg/kg	0.10	< 0.10	1.8	0.63
Fluorene	U	2700	mg/kg	0.10	< 0.10	1.6	0.79
Phenanthrene	U	2700	mg/kg	0.10	3.0	7.3	4.5
Anthracene	U	2700	mg/kg	0.10	0.52	1.8	1.1
Fluoranthene	U	2700	mg/kg	0.10	3.0	7.9	6.9
Pyrene	U	2700	mg/kg	0.10	3.4	8.9	7.6
Benzo[a]anthracene	U	2700	mg/kg	0.10	0.81	4.4	2.6
Chrysene	U	2700	mg/kg	0.10	1.0	5.0	3.1
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	< 0.10	5.4	2.8
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	< 0.10	2.4	1.2
Benzo[a]pyrene	U	2700	mg/kg	0.10	< 0.10	4.6	2.4
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	< 0.10	2.6	1.9
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	< 0.10	1.0	0.15
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	< 0.10	3.1	1.7
Total Of 16 PAH's	U	2700	mg/kg	2.0	12	60	38
Benzene	U	2760	µg/kg	1.0	12	3.9	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0	< 1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0	< 1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0	< 1.0
Total Phenols	U	2920	mg/kg	0.10	< 0.10	< 0.10	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 45 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com


Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-16449-1
Initial Date of Issue:	25-May-2021
Client	Provectus Group Ltd
Client Address:	Regent House Bath Avenue Wolverhampton Staffordshire WV1 4EG
Contact(s):	Andy Clee Charlie Gould Jon Owens Sam Gould
Project	101114 BAM Construction Site

Quotation No.:		**Date Received:**	18-May-2021
Order No.:	9848	**Date Instructed:**	18-May-2021
No. of Samples:	2		
Turnaround (Wkdays):	5	**Results Due:**	24-May-2021
Date Approved:	25-May-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-16449	21-16449
Quotation No.:			**Chemtest Sample ID.:**		1202382	1202383
			Client Sample ID.:		PA05/01	PA05/02
			Sample Location:		PA5	PA5
			Sample Type:		SOIL	SOIL
			Date Sampled:		17-May-2021	17-May-2021
			Asbestos Lab:		NEW-ASB	NEW-ASB
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
ACM Type	U	2192		N/A	-	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected	No Asbestos Detected
ACM Detection Stage	U	2192		N/A	-	-
Moisture	N	2030	%	0.020	17	15
pH	U	2010		4.0	> 12.0	> 12.0
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	0.18	0.20
Sulphur (Elemental)	U	2180	mg/kg	1.0	< 1.0	< 1.0
Cyanide (Complex)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	< 0.50	< 0.50
Sulphate (Total)	U	2430	%	0.010	0.43	0.60
Arsenic	U	2450	mg/kg	1.0	12	19
Cadmium	U	2450	mg/kg	0.10	0.40	0.24
Chromium	U	2450	mg/kg	1.0	18	21
Copper	U	2450	mg/kg	0.50	20	25
Mercury	U	2450	mg/kg	0.10	0.14	0.14
Nickel	U	2450	mg/kg	0.50	20	27
Lead	U	2450	mg/kg	0.50	27	44
Selenium	U	2450	mg/kg	0.20	< 0.20	< 0.20
Zinc	U	2450	mg/kg	0.50	48	59
LOI	U	2610	%	0.10	3.3	4.1
Total Organic Carbon	U	2625	%	0.20	0.60	0.95
Total TPH >C6-C40	U	2670	mg/kg	10	< 10	< 10
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0

Results - Soil

Project: 101114 BAM Construction Site

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-16449	21-16449
Quotation No.:			**Chemtest Sample ID.:**		1202382	1202383
			Client Sample ID.:		PA05/01	PA05/02
			Sample Location:		PA5	PA5
			Sample Type:		SOIL	SOIL
			Date Sampled:		17-May-2021	17-May-2021
			Asbestos Lab:		NEW-ASB	NEW-ASB
Determinand	**Accred.**	**SOP**	**Units**	**LOD**		
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	< 10	< 10
Naphthalene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Acenaphthylene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Acenaphthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Fluorene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Phenanthrene	U	2700	mg/kg	0.10	< 0.10	0.93
Anthracene	U	2700	mg/kg	0.10	< 0.10	0.14
Fluoranthene	U	2700	mg/kg	0.10	< 0.10	1.8
Pyrene	U	2700	mg/kg	0.10	< 0.10	1.4
Benzo[a]anthracene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Chrysene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[a]pyrene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	< 0.10	< 0.10
Total Of 16 PAH's	U	2700	mg/kg	2.0	< 2.0	4.3
Benzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0
Total Phenols	U	2920	mg/kg	0.10	< 0.10	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 45 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com


Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-17462-1
Initial Date of Issue:	01-Jun-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Sam Lane-Ryan Charlotte Nicholson
Project	101114 BAM Construction Site, Sportcity Way

Quotation No.:		**Date Received:**	25-May-2021
Order No.:	9848	**Date Instructed:**	25-May-2021
No. of Samples:	3		
Turnaround (Wkdays):	5	**Results Due:**	30-May-2021
Date Approved:	01-Jun-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-17462	21-17462	21-17462
Quotation No.:			**Chemtest Sample ID.:**		1207448	1207449	1207450
Order No.: 9848			Client Sample Ref.:		PA6	PA6	PA6
			Client Sample ID.:		PA6/01	PA6/02	PA6/03
			Sample Type:		SOIL	SOIL	SOIL
			Date Sampled:		21-May-2021	21-May-2021	21-May-2021
			Asbestos Lab:		DURHAM	DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**			
ACM Type	U	2192		N/A	-	-	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected	No Asbestos Detected	No Asbestos Detected
ACM Detection Stage	U	2192		N/A	-	-	-
Moisture	N	2030	%	0.020	11	12	13
pH	U	2010		4.0	11.6	10.4	11.7
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	0.098	0.082	0.16
Sulphur (Elemental)	U	2180	mg/kg	1.0	1.7	10	2.0
Cyanide (Complex)	U	2300	mg/kg	0.50	< 0.50	< 0.50	< 0.50
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50	< 0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	< 0.50	< 0.50	< 0.50
Sulphate (Total)	U	2430	%	0.010	0.23	0.26	0.27
Arsenic	U	2450	mg/kg	1.0	8.3	13	12
Cadmium	U	2450	mg/kg	0.10	0.18	0.19	0.29
Chromium	U	2450	mg/kg	1.0	22	23	21
Copper	U	2450	mg/kg	0.50	25	30	22
Mercury	U	2450	mg/kg	0.10	0.11	0.11	0.12
Nickel	U	2450	mg/kg	0.50	30	33	25
Lead	U	2450	mg/kg	0.50	28	24	40
Selenium	U	2450	mg/kg	0.20	< 0.20	0.68	0.47
Zinc	U	2450	mg/kg	0.50	74	79	64
LOI	U	2610	%	0.10	3.7	8.2	3.1
Total Organic Carbon	U	2625	%	0.20	0.57	2.3	0.39
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0	31
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0	15
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0	46
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	7.5	42
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0	15
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	140	81

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way

Client: Provectus Group Ltd		**Chemtest Job No.:**			21-17462	21-17462	21-17462
Quotation No.:		**Chemtest Sample ID.:**			1207448	1207449	1207450
Order No.: 9848		Client Sample Ref.:			PA6	PA6	PA6
		Client Sample ID.:			PA6/01	PA6/02	PA6/03
		Sample Type:			SOIL	SOIL	SOIL
		Date Sampled:			21-May-2021	21-May-2021	21-May-2021
		Asbestos Lab:			DURHAM	DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**			
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	150	140
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	< 10	150	180
Naphthalene	U	2700	mg/kg	0.10	< 0.10	1.4	< 0.10
Acenaphthylene	U	2700	mg/kg	0.10	< 0.10	0.45	< 0.10
Acenaphthene	U	2700	mg/kg	0.10	< 0.10	1.1	< 0.10
Fluorene	U	2700	mg/kg	0.10	< 0.10	1.4	< 0.10
Phenanthrene	U	2700	mg/kg	0.10	< 0.10	6.0	0.83
Anthracene	U	2700	mg/kg	0.10	< 0.10	1.3	0.19
Fluoranthene	U	2700	mg/kg	0.10	< 0.10	5.8	0.76
Pyrene	U	2700	mg/kg	0.10	< 0.10	7.1	0.85
Benzo[a]anthracene	U	2700	mg/kg	0.10	< 0.10	3.0	0.31
Chrysene	U	2700	mg/kg	0.10	< 0.10	3.5	0.64
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	< 0.10	2.7	< 0.10
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	< 0.10	1.6	< 0.10
Benzo[a]pyrene	U	2700	mg/kg	0.10	< 0.10	2.6	< 0.10
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	< 0.10	1.6	< 0.10
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	< 0.10	0.63	< 0.10
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	< 0.10	1.9	< 0.10
Total Of 16 PAH's	U	2700	mg/kg	2.0	< 2.0	42	3.6
Benzene	U	2760	µg/kg	1.0	< 1.0	< 1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0	< 1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0	< 1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0	< 1.0
Total Phenols	U	2920	mg/kg	0.10	< 0.10	< 0.10	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 45 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com


Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-18459-1
Initial Date of Issue:	04-Jun-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Andy Clee Charlie Gould Jon Owens Sam Gould
Project	101114 BAM Construction Site, Sportcity Way, Manchester, M11

Quotation No.:		**Date Received:**	02-Jun-2021
Order No.:	9848	**Date Instructed:**	02-Jun-2021
No. of Samples:	3		
Turnaround (Wkdays):	3	**Results Due:**	04-Jun-2021
Date Approved:	04-Jun-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester, M11

Client: Provectus Group Ltd		**Chemtest Job No.:**			21-18459	21-18459	21-18459
Quotation No.:		**Chemtest Sample ID.:**			1212186	1212187	1212188
Order No.: 9848		Client Sample Ref.:			PA7/01	PA7/02	PA7/03
		Sample Location:			PA7	PA7	PA7
		Sample Type:			SOIL	SOIL	SOIL
		Date Sampled:			28-May-2021	28-May-2021	28-May-2021
		Asbestos Lab:			DURHAM	DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**			
ACM Type	U	2192		N/A	-	-	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected	No Asbestos Detected	No Asbestos Detected
Moisture	N	2030	%	0.020	7.5	8.3	7.7
pH	U	2010		4.0	10.8	11.6	11.5
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	0.21	0.66	0.30
Sulphur (Elemental)	U	2180	mg/kg	1.0	4.6	3.1	4.2
Cyanide (Complex)	U	2300	mg/kg	0.50	< 0.50	< 0.50	< 0.50
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50	< 0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	< 0.50	< 0.50	< 0.50
Sulphate (Total)	U	2430	%	0.010	0.85	0.84	0.40
Arsenic	U	2450	mg/kg	1.0	29	31	19
Cadmium	U	2450	mg/kg	0.10	0.34	0.43	0.34
Chromium	U	2450	mg/kg	1.0	31	30	19
Copper	U	2450	mg/kg	0.50	52	41	39
Mercury	U	2450	mg/kg	0.10	0.23	0.20	0.37
Nickel	U	2450	mg/kg	0.50	45	35	32
Lead	U	2450	mg/kg	0.50	180	250	59
Selenium	U	2450	mg/kg	0.20	0.62	0.32	< 0.20
Zinc	U	2450	mg/kg	0.50	140	120	76
LOI	U	2610	%	0.10	5.5	5.2	5.7
Total Organic Carbon	U	2625	%	0.20	0.79	1.2	1.4
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester, M11

Client: Provectus Group Ltd		**Chemtest Job No.:**			21-18459	21-18459	21-18459
Quotation No.:		**Chemtest Sample ID.:**			1212186	1212187	1212188
Order No.: 9848		Client Sample Ref.:			PA7/01	PA7/02	PA7/03
		Sample Location:			PA7	PA7	PA7
		Sample Type:			SOIL	SOIL	SOIL
		Date Sampled:			28-May-2021	28-May-2021	28-May-2021
		Asbestos Lab:			DURHAM	DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**			
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0	< 5.0
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	< 10	< 10	< 10
Naphthalene	U	2700	mg/kg	0.10	< 0.10	< 0.10	< 0.10
Acenaphthylene	U	2700	mg/kg	0.10	< 0.10	< 0.10	< 0.10
Acenaphthene	U	2700	mg/kg	0.10	< 0.10	< 0.10	< 0.10
Fluorene	U	2700	mg/kg	0.10	< 0.10	< 0.10	< 0.10
Phenanthrene	U	2700	mg/kg	0.10	1.2	2.9	0.52
Anthracene	U	2700	mg/kg	0.10	0.17	1.1	0.21
Fluoranthene	U	2700	mg/kg	0.10	1.5	2.2	0.58
Pyrene	U	2700	mg/kg	0.10	1.9	2.5	0.64
Benzo[a]anthracene	U	2700	mg/kg	0.10	0.88	0.98	0.45
Chrysene	U	2700	mg/kg	0.10	0.84	0.92	0.47
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	0.91	1.0	< 0.10
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	0.56	0.53	< 0.10
Benzo[a]pyrene	U	2700	mg/kg	0.10	0.67	0.79	< 0.10
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	0.71	0.61	< 0.10
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	0.34	0.45	< 0.10
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	0.52	0.70	< 0.10
Total Of 16 PAH's	U	2700	mg/kg	2.0	10	15	2.9
Benzene	U	2760	µg/kg	1.0	< 1.0	< 1.0	< 1.0
Toluene	U	2760	µg/kg	1.0	< 1.0	< 1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0	< 1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0	< 1.0
Total Phenols	U	2920	mg/kg	0.10	< 0.10	< 0.10	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 45 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com

eurofins | Chemtest
Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com


UKAS TESTING 2183

Final Report

Report No.:	21-18613-1
Initial Date of Issue:	08-Jun-2021
Client	Provectus Group Ltd
Client Address:	Regent House Bath Avenue Wolverhampton Staffordshire WV1 4EG
Contact(s):	Andy Clee Charlie Gould Jon Owens Sam Gould
Project	101114 BAM Construction Site, Sportcity Way, Manchester, M11

Quotation No.:		**Date Received:**	03-Jun-2021
Order No.:	9848	**Date Instructed:**	03-Jun-2021
No. of Samples:	5		
Turnaround (Wkdays):	5	**Results Due:**	09-Jun-2021
Date Approved:	08-Jun-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester, M11

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-18613	21-18613	21-18613	21-18613	21-18613
Quotation No.:			**Chemtest Sample ID.:**		1213211	1213212	1213213	1213214	1213215
Order No.: 9848			Client Sample Ref.:		PA7/04	PA7/05	PA7/06	PA7/07	PA7/08
			Sample Location:		PA7	PA7	PA7	PA7	PA7
			Sample Type:		SOIL	SOIL	SOIL	SOIL	SOIL
			Date Sampled:		02-Jun-2021	02-Jun-2021	02-Jun-2021	02-Jun-2021	02-Jun-2021
			Asbestos Lab:		DURHAM	DURHAM	DURHAM	DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**					
ACM Type	U	2192		N/A	-	-	-	-	-
Asbestos Identification	U	2192		N/A	No Asbestos Detected	No Asbestos Detected	No Asbestos Detected	No Asbestos Detected	No Asbestos Detected
Moisture	N	2030	%	0.020	4.5	8.5	8.4	8.7	9.7
pH	U	2010		4.0	7.8	8.9	9.8	10.7	10.6
Sulphate (2:1 Water Soluble) as SO4	U	2120	g/l	0.010	0.56	0.35	0.26	0.48	0.75
Sulphur (Elemental)	U	2180	mg/kg	1.0	20	9.0	7.0	5.2	18
Cyanide (Complex)	U	2300	mg/kg	0.50	< 0.50	< 0.50	0.50	< 0.50	3.0
Cyanide (Free)	U	2300	mg/kg	0.50	< 0.50	< 0.50	< 0.50	< 0.50	< 0.50
Cyanide (Total)	U	2300	mg/kg	0.50	< 0.50	< 0.50	0.50	< 0.50	3.1
Sulphate (Total)	U	2430	%	0.010	0.95	0.59	0.43	0.97	0.93
Arsenic	U	2450	mg/kg	1.0	25	19	13	35	29
Cadmium	U	2450	mg/kg	0.10	0.91	0.40	0.29	0.44	0.37
Chromium	U	2450	mg/kg	1.0	25	23	32	44	48
Copper	U	2450	mg/kg	0.50	49	38	42	56	57
Mercury	U	2450	mg/kg	0.10	0.13	0.10	0.10	0.24	0.20
Nickel	U	2450	mg/kg	0.50	46	41	49	56	50
Lead	U	2450	mg/kg	0.50	35	29	42	480	160
Selenium	U	2450	mg/kg	0.20	2.7	1.5	0.65	0.98	0.65
Zinc	U	2450	mg/kg	0.50	90	72	110	120	120
LOI	U	2610	%	0.10	6.4	3.7	7.0	3.6	6.8
Total Organic Carbon	U	2625	%	0.20	15	9.1	1.8	2.3	1.2
Total TPH >C6-C40	U	2670	mg/kg	10	< 10	< 10	45	34	93
Aliphatic TPH >C5-C6	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C6-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aliphatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Total Aliphatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0	< 5.0	< 5.0	< 5.0
Aromatic TPH >C5-C7	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C7-C8	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C8-C10	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C10-C12	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C12-C16	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Aromatic TPH >C16-C21	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	13

Results - Soil

Project: 101114 BAM Construction Site, Sportcity Way, Manchester, M11

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-18613	21-18613	21-18613	21-18613	21-18613
Quotation No.:			**Chemtest Sample ID.:**		1213211	1213212	1213213	1213214	1213215
Order No.: 9848			Client Sample Ref.:		PA7/04	PA7/05	PA7/06	PA7/07	PA7/08
			Sample Location:		PA7	PA7	PA7	PA7	PA7
			Sample Type:		SOIL	SOIL	SOIL	SOIL	SOIL
			Date Sampled:		02-Jun-2021	02-Jun-2021	02-Jun-2021	02-Jun-2021	02-Jun-2021
			Asbestos Lab:		DURHAM	DURHAM	DURHAM	DURHAM	DURHAM
Determinand	**Accred.**	**SOP**	**Units**	**LOD**					
Aromatic TPH >C21-C35	U	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	130
Aromatic TPH >C35-C44	N	2680	mg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Total Aromatic Hydrocarbons	N	2680	mg/kg	5.0	< 5.0	< 5.0	< 5.0	< 5.0	140
Total Petroleum Hydrocarbons	N	2680	mg/kg	10.0	< 10	< 10	< 10	< 10	140
Naphthalene	U	2700	mg/kg	0.10	< 0.10	< 0.10	< 0.10	< 0.10	3.6
Acenaphthylene	U	2700	mg/kg	0.10	< 0.10	< 0.10	< 0.10	< 0.10	1.5
Acenaphthene	U	2700	mg/kg	0.10	< 0.10	< 0.10	< 0.10	< 0.10	2.4
Fluorene	U	2700	mg/kg	0.10	< 0.10	< 0.10	< 0.10	< 0.10	2.9
Phenanthrene	U	2700	mg/kg	0.10	< 0.10	< 0.10	0.91	1.6	21
Anthracene	U	2700	mg/kg	0.10	< 0.10	< 0.10	0.21	0.41	4.2
Fluoranthene	U	2700	mg/kg	0.10	0.93	< 0.10	1.4	2.1	17
Pyrene	U	2700	mg/kg	0.10	0.83	< 0.10	1.5	2.2	19
Benzo[a]anthracene	U	2700	mg/kg	0.10	< 0.10	< 0.10	0.52	0.80	7.1
Chrysene	U	2700	mg/kg	0.10	< 0.10	< 0.10	0.54	0.70	7.4
Benzo[b]fluoranthene	U	2700	mg/kg	0.10	< 0.10	< 0.10	0.53	0.86	8.0
Benzo[k]fluoranthene	U	2700	mg/kg	0.10	< 0.10	< 0.10	0.14	0.23	3.2
Benzo[a]pyrene	U	2700	mg/kg	0.10	< 0.10	< 0.10	0.49	0.78	6.6
Indeno(1,2,3-c,d)Pyrene	U	2700	mg/kg	0.10	< 0.10	< 0.10	0.41	0.61	4.8
Dibenz(a,h)Anthracene	U	2700	mg/kg	0.10	< 0.10	< 0.10	0.55	0.45	2.0
Benzo[g,h,i]perylene	U	2700	mg/kg	0.10	< 0.10	< 0.10	0.47	0.74	5.0
Total Of 16 PAH's	U	2700	mg/kg	2.0	< 2.0	< 2.0	7.7	12	120
Benzene	U	2760	µg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	20
Toluene	U	2760	µg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Ethylbenzene	U	2760	µg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
m & p-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
o-Xylene	U	2760	µg/kg	1.0	< 1.0	< 1.0	< 1.0	< 1.0	< 1.0
Total Phenols	U	2920	mg/kg	0.10	0.12	< 0.10	< 0.10	< 0.10	< 0.10

Test Methods

SOP	Title	Parameters included	Method summary
2010	pH Value of Soils	pH	pH Meter
2030	Moisture and Stone Content of Soils(Requirement of MCERTS)	Moisture content	Determination of moisture content of soil as a percentage of its as received mass obtained at <37°C.
2040	Soil Description(Requirement of MCERTS)	Soil description	As received soil is described based upon BS5930
2120	Water Soluble Boron, Sulphate, Magnesium & Chromium	Boron; Sulphate; Magnesium; Chromium	Aqueous extraction / ICP-OES
2175	Total Sulphur in Soils	Total Sulphur	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2180	Sulphur (Elemental) in Soils by HPLC	Sulphur	Dichloromethane extraction / HPLC with UV detection
2192	Asbestos	Asbestos	Polarised light microscopy / Gravimetry
2300	Cyanides & Thiocyanate in Soils	Free (or easy liberatable) Cyanide; total Cyanide; complex Cyanide; Thiocyanate	Allkaline extraction followed by colorimetric determination using Automated Flow Injection Analyser.
2430	Total Sulphate in soils	Total Sulphate	Acid digestion followed by determination of sulphate in extract by ICP-OES.
2450	Acid Soluble Metals in Soils	Metals, including: Arsenic; Barium; Beryllium; Cadmium; Chromium; Cobalt; Copper; Lead; Manganese; Mercury; Molybdenum; Nickel; Selenium; Vanadium; Zinc	Acid digestion followed by determination of metals in extract by ICP-MS.
2610	Loss on Ignition	loss on ignition (LOI)	Determination of the proportion by mass that is lost from a soil by ignition at 550°C.
2625	Total Organic Carbon in Soils	Total organic Carbon (TOC)	Determined by high temperature combustion under oxygen, using an Eltra elemental analyser.
2670	Total Petroleum Hydrocarbons (TPH) in Soils by GC-FID	TPH (C6–C40); optional carbon banding, e.g. 3-band – GRO, DRO & LRO*TPH C8–C40	Dichloromethane extraction / GC-FID
2680	TPH A/A Split	Aliphatics: >C5–C6, >C6–C8,>C8–C10, >C10–C12, >C12–C16, >C16–C21, >C21–C35, >C35– C44Aromatics: >C5–C7, >C7–C8, >C8– C10, >C10–C12, >C12–C16, >C16– C21, >C21– C35, >C35– C44	Dichloromethane extraction / GCxGC FID detection
2700	Speciated Polynuclear Aromatic Hydrocarbons (PAH) in Soil by GC-FID	Acenaphthene; Acenaphthylene; Anthracene; Benzo[a]Anthracene; Benzo[a]Pyrene; Benzo[b]Fluoranthene; Benzo[ghi]Perylene; Benzo[k]Fluoranthene; Chrysene; Dibenz[ah]Anthracene; Fluoranthene; Fluorene; Indeno[123cd]Pyrene; Naphthalene; Phenanthrene; Pyrene	Dichloromethane extraction / GC-FID (GC-FID detection is non-selective and can be subject to interference from co-eluting compounds)
2760	Volatile Organic Compounds (VOCs) in Soils by Headspace GC-MS	Volatile organic compounds, including BTEX and halogenated Aliphatic/Aromatics.(cf. USEPA Method 8260)*please refer to UKAS schedule	Automated headspace gas chromatographic (GC) analysis of a soil sample, as received, with mass spectrometric (MS) detection of volatile organic compounds.
2920	Phenols in Soils by HPLC	Phenolic compounds including Resorcinol, Phenol, Methylphenols, Dimethylphenols, 1-Naphthol and TrimethylphenolsNote: chlorophenols are excluded.	60:40 methanol/water mixture extraction, followed by HPLC determination using electrochemical detection.

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 45 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com

Laboratory Report	ARC/5978	Contract Sample No	DN3046/1
Report Date	08/04/2021	Clients Reference	DN3046/1
		Material Description	Recycled 6F2
Provectus Remediation Limited Regent House Bath Avenue Wolverhampton WV1 4EG		Source	Ex - Site
		Supplier	Ex - Site
		Date Sampled	23/03/2021
		Sampled By	CTS
		Date Received	23/03/2021
		Date Completed	07/04/2021
Gibbon Street, Manchester		Sample Location	SP1

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk
4161


Determination of moisture content - BS 1377: Part 2: 1990 Clause 3

Moisture Content	10 %

Determination of particle size distribution (wet sieving method) - BS 1377: Part 2: 1990 Clause 9.2

Sample prepared in accordance with BS 1377: Part 1: 1990 clause 7.3.4(a)

BS Sieve Size	Passing BS Sieve	Specification MCHW SHW Vol 1 Series 600 Table 6/2 Class 6F2
500 mm	100 %	
300 mm	100 %	
125 mm	100 %	100
100 mm	100 %	
90 mm	96 %	80 - 100
75 mm	88 %	65 - 100
63 mm	84 %	
50 mm	78 %	
37.5 mm	69 %	45 - 100
28 mm	62 %	
20 mm	52 %	
14 mm	46 %	
10 mm	41 %	15 - 60
6.3 mm	35 %	
5 mm	33 %	10 - 45
3.35 mm	30 %	
2 mm	27 %	
1.18 mm	24 %	
600 µm	20 %	0 - 25
425 µm	18 %	
300 µm	14 %	
150 µm	10 %	
63 µm	8 %	0 - 12

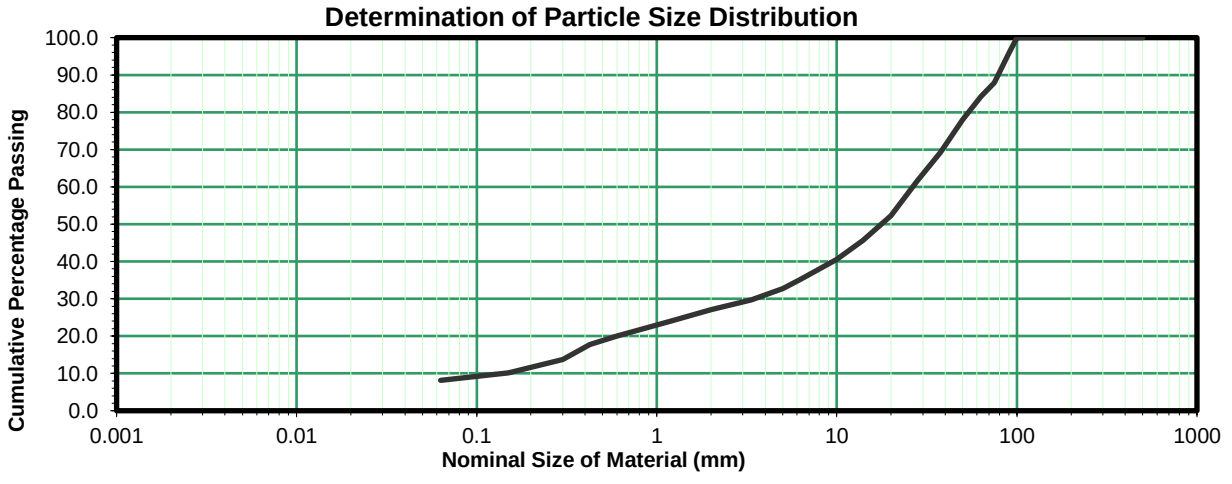

Material when tested complies with the material specification limits defined in the table above.

Template Version: 1.4

Authorised Signatory

P Nodder - Technical Director

Opinions and interpretations expressed herein are outside of the scope of the UKAS Accreditation.

This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.

The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.

Laboratory Report	ARC/5979	Contract Sample No	DN3046/2
Report Date	08/04/2021	Clients Reference	DN3046/2
		Material Description	Recycled 6F2

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Source	Ex - Site
Supplier	Ex - Site
Date Sampled	23/03/2021
Sampled By	CTS
Date Received	23/03/2021
Date Completed	07/04/2021
Sample Location	SP1

Gibbon Street, Manchester

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk
4161


Determination of moisture content - BS 1377: Part 2: 1990 Clause 3

Moisture Content	9.2 %

Determination of particle size distribution (wet sieving method) - BS 1377: Part 2: 1990 Clause 9.2

Sample prepared in accordance with BS 1377: Part 1: 1990 clause 7.3.4(a)

BS Sieve Size	Passing BS Sieve	Specification MCHW SHW Vol 1 Series 600 Table 6/2 Class 6F2
500 mm	100 %	
300 mm	100 %	
125 mm	100 %	100
100 mm	96 %	
90 mm	96 %	80 - 100
75 mm	88 %	65 - 100
63 mm	82 %	
50 mm	69 %	
37.5 mm	59 %	45 - 100
28 mm	50 %	
20 mm	40 %	
14 mm	33 %	
10 mm	30 %	15 - 60
6.3 mm	25 %	
5 mm	24 %	10 - 45
3.35 mm	21 %	
2 mm	18 %	
1.18 mm	17 %	
600 µm	14 %	0 - 25
425 µm	12 %	
300 µm	10 %	
150 µm	8 %	
63 µm	6 %	0 - 12

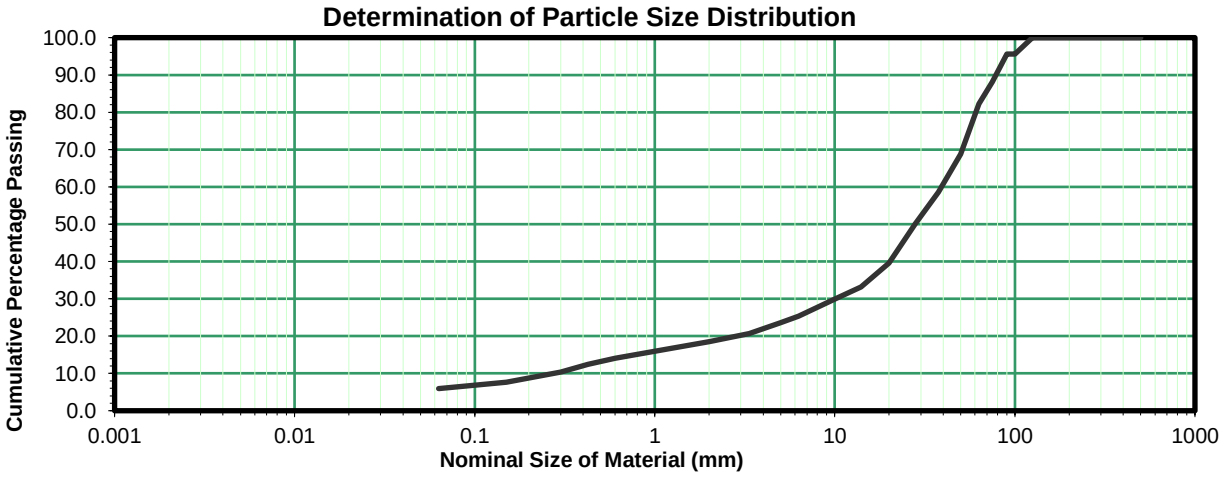

Material when tested complies with the material specification limits defined in the table above.

Template Version: 1.4

Authorised Signatory

P Nodder - Technical Director

Opinions and interpretations expressed herein are outside of the scope of the UKAS Accreditation.

This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.

The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.

Laboratory Report	ARC/5980	Contract Sample No	DN3046/3
Report Date	08/04/2021	Clients Reference	DN3046/3
		Material Description	Recycled 6F2

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Source	Ex - Site
Supplier	Ex - Site
Date Sampled	23/03/2021
Sampled By	CTS
Date Received	23/03/2021
Date Completed	07/04/2021
Sample Location	SP1

Gibbon Street, Manchester

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk
4161


Determination of moisture content - BS 1377: Part 2: 1990 Clause 3

Moisture Content	9.4 %

Determination of particle size distribution (wet sieving method) - BS 1377: Part 2: 1990 Clause 9.2

Sample prepared in accordance with BS 1377: Part 1: 1990 clause 7.3.4(a)

BS Sieve Size	Passing BS Sieve	Specification MCHW SHW Vol 1 Series 600 Table 6/2 Class 6F2
500 mm	100 %	
300 mm	100 %	
125 mm	100 %	100
100 mm	100 %	
90 mm	100 %	80 - 100
75 mm	91 %	65 - 100
63 mm	83 %	
50 mm	73 %	
37.5 mm	61 %	45 - 100
28 mm	52 %	
20 mm	43 %	
14 mm	36 %	
10 mm	30 %	15 - 60
6.3 mm	25 %	
5 mm	23 %	10 - 45
3.35 mm	21 %	
2 mm	17 %	
1.18 mm	15 %	
600 µm	11 %	0 - 25
425 µm	10 %	
300 µm	8 %	
150 µm	5 %	
63 µm	4 %	0 - 12

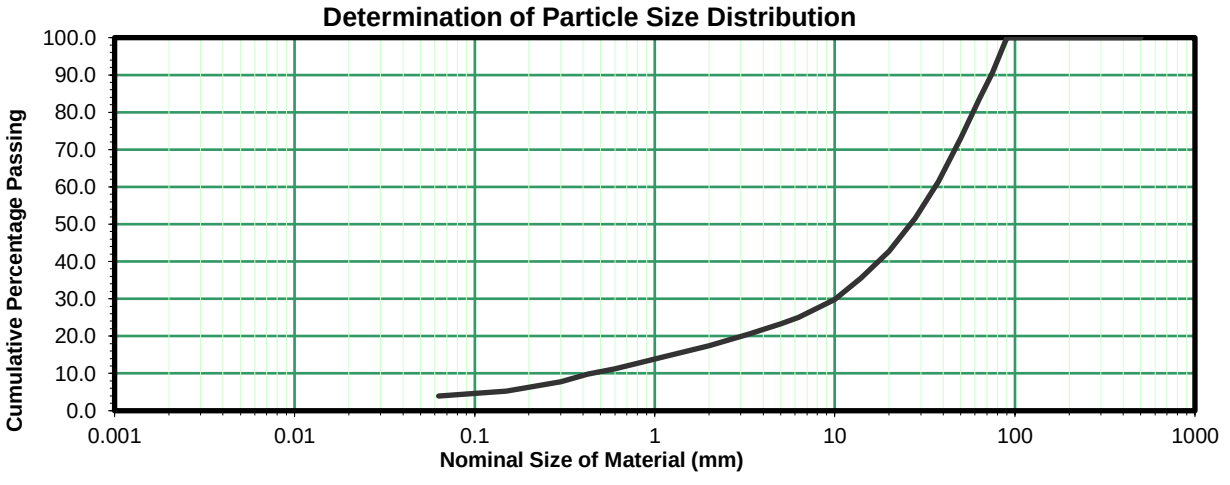

Material when tested complies with the material specification limits defined in the table above.

Template Version: 1.4

Authorised Signatory

P Nodder - Technical Director

Opinions and interpretations expressed herein are outside of the scope of the UKAS Accreditation.

This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.

The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.

Laboratory Report	ARC/5981	Contract Sample No	DN3046/4
Report Date	08/04/2021	Clients Reference	DN3046/4
		Material Description	Recycled 6F2

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Source	Ex - Site
Supplier	Ex - Site
Date Sampled	23/03/2021
Sampled By	CTS
Date Received	23/03/2021
Date Completed	07/04/2021
Sample Location	SP1

Gibbon Street, Manchester

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft | Doncaster | DN7 4JU
T | (01302) 352652
E | enquiries@constructiontesting.co.uk
W | www.constructiontesting.co.uk
4161


Determination of moisture content - BS 1377: Part 2: 1990 Clause 3

Moisture Content	8.9 %

Determination of particle size distribution (wet sieving method) - BS 1377: Part 2: 1990 Clause 9.2

Sample prepared in accordance with BS 1377: Part 1: 1990 clause 7.3.4(a)

BS Sieve Size	Passing BS Sieve	Specification MCHW SHW Vol 1 Series 600 Table 6/2 Class 6F2
500 mm	100 %	
300 mm	100 %	
125 mm	100 %	100
100 mm	93 %	
90 mm	93 %	80 - 100
75 mm	90 %	65 - 100
63 mm	85 %	
50 mm	69 %	
37.5 mm	59 %	45 - 100
28 mm	52 %	
20 mm	43 %	
14 mm	38 %	
10 mm	32 %	15 - 60
6.3 mm	27 %	
5 mm	26 %	10 - 45
3.35 mm	22 %	
2 mm	19 %	
1.18 mm	16 %	
600 µm	11 %	0 - 25
425 µm	10 %	
300 µm	8 %	
150 µm	5 %	
63 µm	4 %	0 - 12

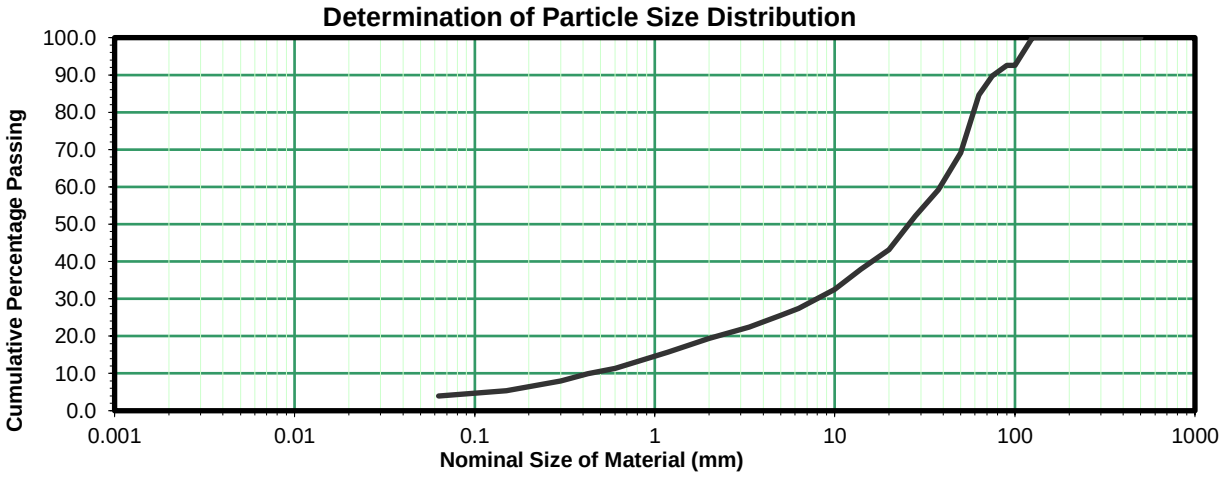

Material when tested complies with the material specification limits defined in the table above.

Template Version: 1.4

Authorised Signatory

P Nodder - Technical Director

Opinions and interpretations expressed herein are outside of the scope of the UKAS Accreditation.

This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.

The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.

Laboratory Report	DNR-70397	Contract Sample No	DN-3046/15
Report Date	18/08/2021	Clients Reference	DN-3046/15
		Material Description	6F5

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Gibbson Street Manchester

Date Sampled	22/06/2021
Sampling Plan	CTS Procedure
Source	Not Stated
Supplier	Not Stated
Sampled By	CTS
Sampling Environment	N/A
Sample Type	Bulk
Location in sample	N/A
Sample Location	Not Stated

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft
Doncaster
DN7 4JU
UKAS TESTING 4161
Tel: (01302) 352652 Web: www.constructiontesting.co.uk
Email: enquiries@constructiontesting.co.uk

Date Received	22/06/2021
Date Tests Completed	12/07/2021

TEST REPORT

Determination of Water Content by Drying in a Ventilated Oven
Tested in Accordance with BS EN 1097-5:2008


Water content of test portion *(w)* 12.8 %

Aggregate Type: Type1
Nominal Size (mm): 80

Determination of Particle Size Distribution (wet sieving method)
Tested in Accordance with BS EN 933-1: 2012

BS Sieve Size	Passing BS Sieve	Specification MCHW. SHW Vol 1, Series 800, cl 803 Table 8/5
500 mm	100 %	
300 mm	100 %	
125 mm	100 %	
80 mm	89 %	
63 mm	71 %	100
50 mm	65 %	
40 mm	63 %	
31.5 mm	57 %	75 - 99
25 mm	51 %	
20 mm	47 %	
16 mm	41 %	43 - 81*
14 mm	40 %	
12.5 mm	39 %	
10 mm	37 %	
8 mm	35 %	23 - 66*
6.3 mm	33 %	
5 mm	32 %	
4 mm	30 %	12 - 53*
2.8 mm	29 %	
2 mm	28 %	6 - 42*
1 mm	24 %	3 - 32*
500 µm	19 %	
250 µm	12 %	
125 µm	6 %	
63 µm	3.9 %	0 - 9

*Suppliers Declared Limit Not Stated

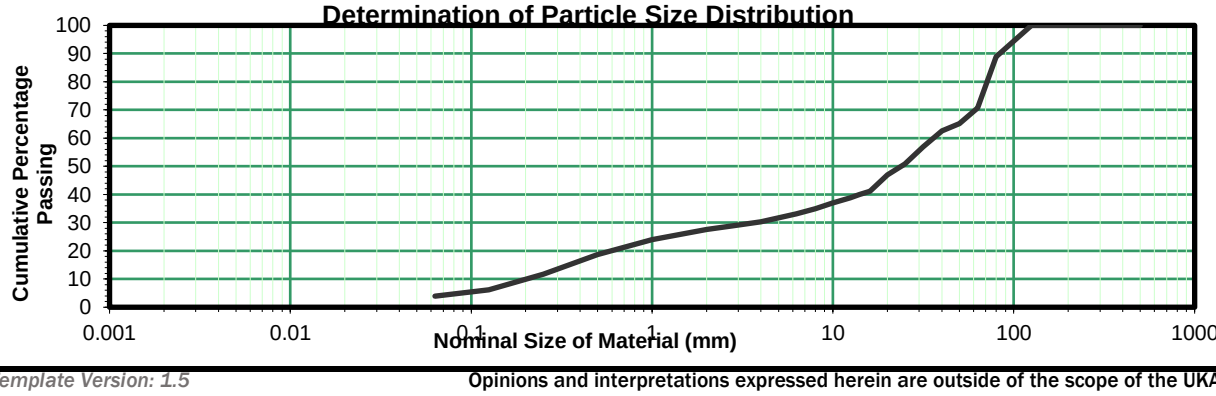

Template Version: 1.5

Opinions and interpretations expressed herein are outside of the scope of the UKAS Accreditation.
Results relate only to the sample(s) as received.
This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.
The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.

Authorised Signatory

R Walker - Senior Laboratory Technician

** END OF REPORT **

Laboratory Report	DNR-71461	Contract Sample No	DN-3046/16
Report Date	18/08/2021	Clients Reference	DN-3046/16
		Material Description	6F5

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Gibbson Street Manchester

Date Sampled	05/07/2021
Sampling Plan	CTS Procedure
Source	Not Stated
Supplier	Not Stated
Sampled By	CTS
Sampling Environment	N/A
Sample Type	Bulk
Location in sample	N/A
Sample Location	Not Stated

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft
Doncaster
DN7 4JU
UKAS TESTING 4161
Tel: (01302) 352652 Web: www.constructiontesting.co.uk
Email: enquiries@constructiontesting.co.uk

Date Received	05/07/2021
Date Tests Completed	13/08/2021

TEST REPORT

Determination of Water Content by Drying in a Ventilated Oven
Tested in Accordance with BS EN 1097-5:2008


Water content of test portion *(w)* 12.4 %

Aggregate Type: 6F5

Nominal Size (mm): 50

Determination of Particle Size Distribution (wet sieving method)
Tested in Accordance with BS EN 933-1: 2012

BS Sieve Size	Passing BS Sieve	Specification MCHW SHW Vol 1 Series 600 Table 6/5 Class 6F5
500 mm	100 %	
300 mm	100 %	
125 mm	100 %	100
80 mm	95 %	75 - 99
63 mm	91 %	
50 mm	85 %	
40 mm	81 %	50 - 90
31.5 mm	77 %	
25 mm	72 %	
20 mm	67 %	30 - 75
16 mm	63 %	
14 mm	61 %	
12.5 mm	60 %	
10 mm	57 %	15 - 60
8 mm	55 %	
6.3 mm	53 %	
5 mm	51 %	
4 mm	49 %	
2.8 mm	47 %	
2 mm	46 %	0 - 35
1 mm	42 %	
500 µm	35 %	
250 µm	26 %	
125 µm	19 %	
63 µm	15.4 %	0 - 12

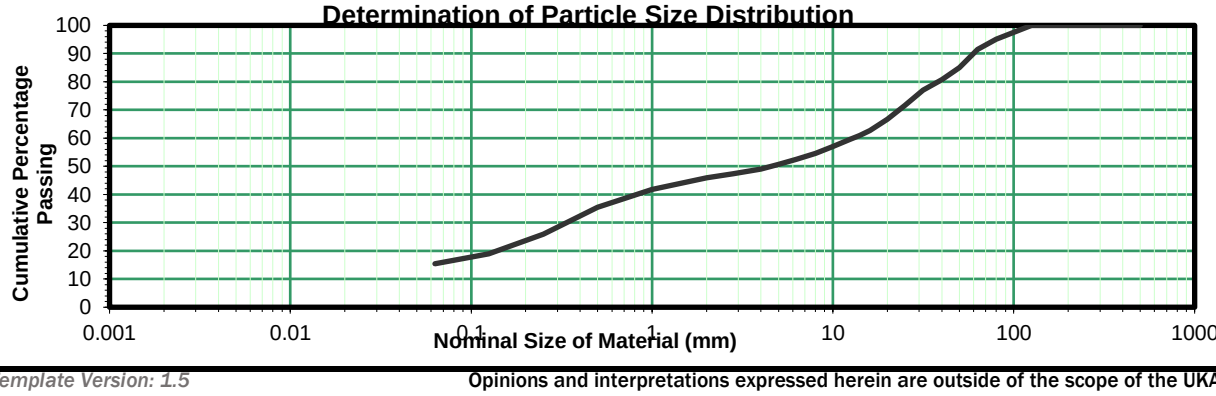

Template Version: 1.5

Authorised Signatory

R Walker - Senior Laboratory Technician

Opinions and interpretations expressed herein are outside of the scope of the UKAS Accreditation.
Results relate only to the sample(s) as received.
This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.
The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.

** END OF REPORT **

Laboratory Report	DNR-71462	Contract Sample No	DN-3046/17
Report Date	18/08/2021	Clients Reference	DN-3046/17
		Material Description	6F5

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Gibbson Street Manchester

Date Sampled	05/07/2021
Sampling Plan	Not Known
Source	Not Stated
Supplier	Not Stated
Sampled By	Not Known
Sampling Environment	N/A
Sample Type	Bulk
Location in sample	N/A
Sample Location	Not Stated

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft
Doncaster
DN7 4JU
UKAS TESTING 4161
Tel: (01302) 352652 Web: www.constructiontesting.co.uk
Email: enquiries@constructiontesting.co.uk

Date Received	05/07/2021
Date Tests Completed	13/08/2021

TEST REPORT


Determination of Water Content by Drying in a Ventilated Oven
Tested in Accordance with BS EN 1097-5:2008

Water content of test portion *(w)* 12.9 %

Aggregate Type: 6F5
Nominal Size (mm): 80

Determination of Particle Size Distribution (wet sieving method)
Tested in Accordance with BS EN 933-1: 2012

BS Sieve Size	Passing BS Sieve	Specification MCHW SHW Vol 1 Series 600 Table 6/5 Class 6F5
500 mm	100 %	
300 mm	100 %	
125 mm	100 %	100
80 mm	89 %	75 - 99
63 mm	89 %	
50 mm	89 %	
40 mm	82 %	50 - 90
31.5 mm	77 %	
25 mm	73 %	
20 mm	68 %	30 - 75
16 mm	65 %	
14 mm	63 %	
12.5 mm	61 %	
10 mm	58 %	15 - 60
8 mm	55 %	
6.3 mm	53 %	
5 mm	51 %	
4 mm	49 %	
2.8 mm	47 %	
2 mm	45 %	0 - 35
1 mm	41 %	
500 µm	35 %	
250 µm	25 %	
125 µm	19 %	
63 µm	15.3 %	0 - 12

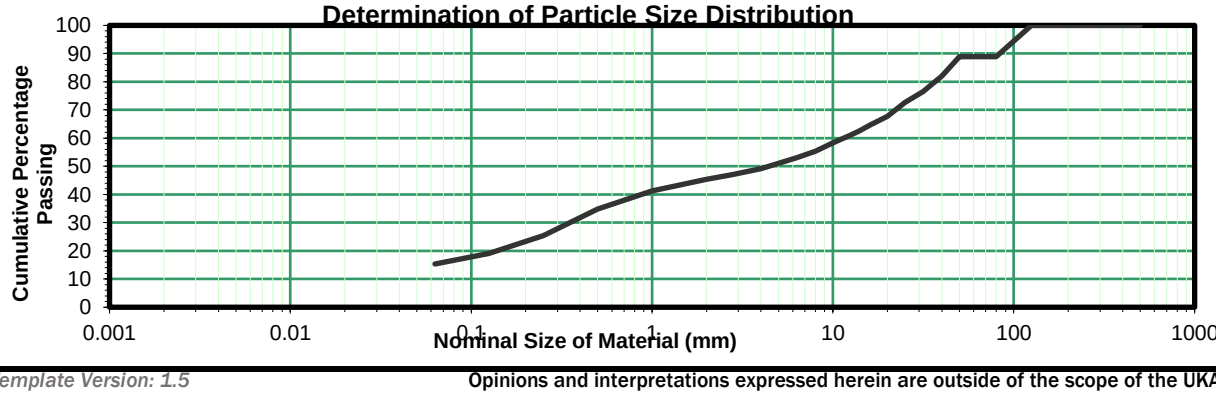

Template Version: 1.5

Opinions and interpretations expressed herein are outside of the scope of the UKAS Accreditation.
Results relate only to the sample(s) as received.
This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.
The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.

Authorised Signatory

R Walker - Senior Laboratory Technician

** END OF REPORT **

Laboratory Report	DNR-71463	Contract Sample No	DN-3046/18
Report Date	18/08/2021	Clients Reference	DN-3046/18
		Material Description	6F5

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Gibbson Street Manchester

Date Sampled	05/07/2021
Sampling Plan	CTS Procedure
Source	Not Stated
Supplier	Not Stated
Sampled By	CTS
Sampling Environment	N/A
Sample Type	Bulk
Location in sample	N/A
Sample Location	Not Stated

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft
Doncaster
DN7 4JU
UKAS TESTING 4161
Tel: (01302) 352652 Web: www.constructiontesting.co.uk
Email: enquiries@constructiontesting.co.uk

Date Received	05/07/2021
Date Tests Completed	13/08/2021

TEST REPORT


Determination of Water Content by Drying in a Ventilated Oven
Tested in Accordance with BS EN 1097-5:2008

Water content of test portion *(w)* 13.0 %

Aggregate Type: 6F5
Nominal Size (mm): 50

Determination of Particle Size Distribution (wet sieving method)
Tested in Accordance with BS EN 933-1: 2012

BS Sieve Size	Passing BS Sieve	Specification MCHW SHW Vol 1 Series 600 Table 6/5 Class 6F5
500 mm	100 %	
300 mm	100 %	
125 mm	100 %	100
80 mm	96 %	75 - 99
63 mm	91 %	
50 mm	89 %	
40 mm	83 %	50 - 90
31.5 mm	78 %	
25 mm	74 %	
20 mm	69 %	30 - 75
16 mm	65 %	
14 mm	62 %	
12.5 mm	61 %	
10 mm	58 %	15 - 60
8 mm	55 %	
6.3 mm	53 %	
5 mm	51 %	
4 mm	49 %	
2.8 mm	48 %	
2 mm	46 %	0 - 35
1 mm	42 %	
500 µm	36 %	
250 µm	25 %	
125 µm	19 %	
63 µm	15.5 %	0 - 12

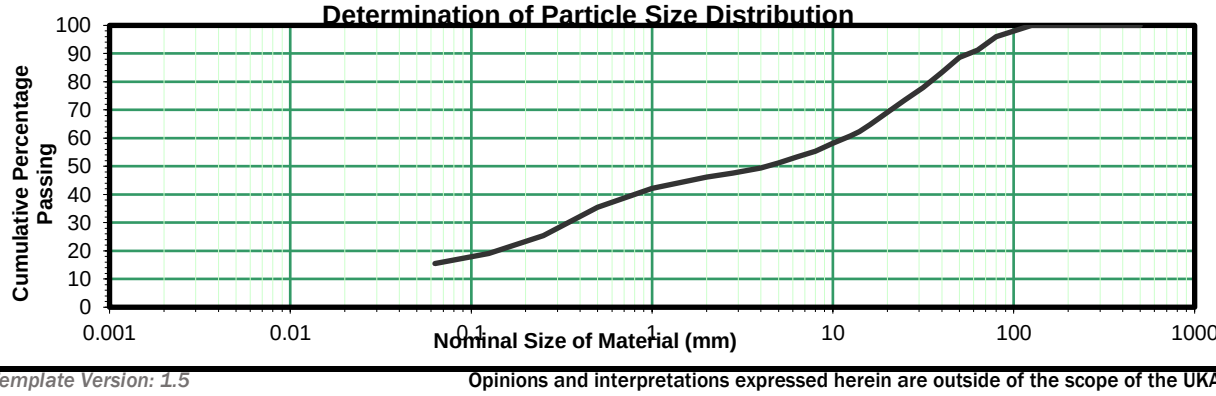

Template Version: 1.5

Opinions and interpretations expressed herein are outside of the scope of the UKAS Accreditation.
Results relate only to the sample(s) as received.
This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.
The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.

Authorised Signatory

R Walker - Senior Laboratory Technician

** END OF REPORT **

Laboratory Report	DNR-71464	Contract Sample No	DN-3046/19
Report Date	18/08/2021	Clients Reference	DN-3046/19
		Material Description	6F5

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Gibbson Street Manchester

Date Sampled	05/07/2021
Sampling Plan	CTS Procedure
Source	Not Stated
Supplier	Not Stated
Sampled By	CTS
Sampling Environment	N/A
Sample Type	Bulk
Location in sample	N/A
Sample Location	Not Stated

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft
Doncaster
DN7 4JU
UKAS TESTING 4161
Tel: (01302) 352652 Web: www.constructiontesting.co.uk
Email: enquiries@constructiontesting.co.uk

Date Received	05/07/2021
Date Tests Completed	13/08/2021

TEST REPORT


Determination of Water Content by Drying in a Ventilated Oven
Tested in Accordance with BS EN 1097-5:2008

Water content of test portion *(w)* 13.5 %

Aggregate Type: 6F5
Nominal Size (mm): 63

Determination of Particle Size Distribution (wet sieving method)
Tested in Accordance with BS EN 933-1: 2012

BS Sieve Size	Passing BS Sieve	Specification MCHW SHW Vol 1 Series 600 Table 6/5 Class 6F5
500 mm	100 %	
300 mm	100 %	
125 mm	100 %	100
80 mm	92 %	75 - 99
63 mm	83 %	
50 mm	78 %	
40 mm	76 %	50 - 90
31.5 mm	71 %	
25 mm	67 %	
20 mm	63 %	30 - 75
16 mm	60 %	
14 mm	59 %	
12.5 mm	57 %	
10 mm	55 %	15 - 60
8 mm	53 %	
6.3 mm	51 %	
5 mm	49 %	
4 mm	47 %	
2.8 mm	45 %	
2 mm	44 %	0 - 35
1 mm	40 %	
500 µm	34 %	
250 µm	25 %	
125 µm	19 %	
63 µm	15.7 %	0 - 12

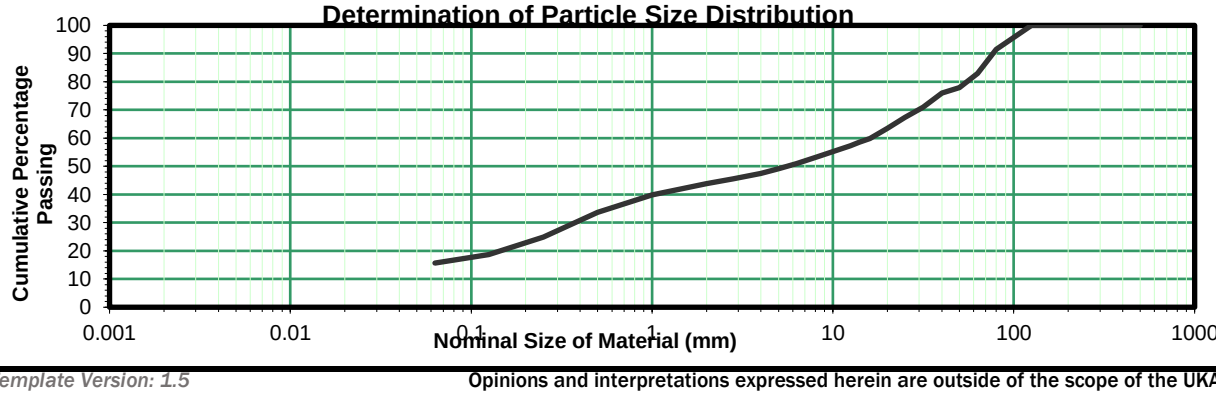

Template Version: 1.5

Opinions and interpretations expressed herein are outside of the scope of the UKAS Accreditation.
Results relate only to the sample(s) as received.
This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.
The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.

Authorised Signatory

R Walker - Senior Laboratory Technician

** END OF REPORT **

Laboratory Report	DNR-71465	Contract Sample No	DN-3046/20
Report Date	18/08/2021	Clients Reference	DN-3046/20
		Material Description	6F5

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Gibbson Street Manchester

Date Sampled	05/07/2021
Sampling Plan	CTS Procedure
Source	Not Stated
Supplier	Not Stated
Sampled By	CTS
Sampling Environment	N/A
Sample Type	Bulk
Location in sample	N/A
Sample Location	Not Stated

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft
Doncaster
DN7 4JU
UKAS TESTING 4161
Tel: (01302) 352652 Web: www.constructiontesting.co.uk
Email: enquiries@constructiontesting.co.uk

Date Received	05/07/2021
Date Tests Completed	13/08/2021

TEST REPORT


Determination of Water Content by Drying in a Ventilated Oven
Tested in Accordance with BS EN 1097-5:2008

Water content of test portion *(w)*	11.5 %

Aggregate Type
6F5
Nominal Size (mm)
80

Determination of Particle Size Distribution (wet sieving method)
Tested in Accordance with BS EN 933-1: 2012

BS Sieve Size	Passing BS Sieve	Specification MCHW SHW Vol 1 Series 600 Table 6/5 Class 6F5
500 mm	100 %	
300 mm	100 %	
125 mm	100 %	100
80 mm	87 %	75 - 99
63 mm	83 %	
50 mm	80 %	
40 mm	75 %	50 - 90
31.5 mm	71 %	
25 mm	65 %	
20 mm	61 %	30 - 75
16 mm	57 %	
14 mm	55 %	
12.5 mm	54 %	
10 mm	51 %	15 - 60
8 mm	49 %	
6.3 mm	47 %	
5 mm	46 %	
4 mm	44 %	
2.8 mm	42 %	
2 mm	41 %	0 - 35
1 mm	37 %	
500 µm	31 %	
250 µm	23 %	
125 µm	17 %	
63 µm	13.8 %	0 - 12

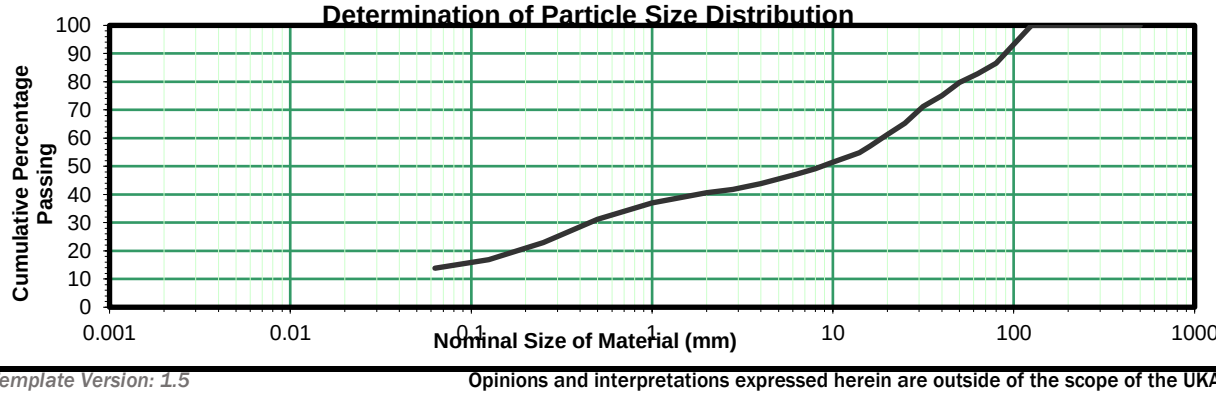

Template Version: 1.5

Opinions and interpretations expressed herein are outside of the scope of the UKAS Accreditation.
Results relate only to the sample(s) as received.
This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.
The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.

Authorised Signatory

R Walker - Senior Laboratory Technician

** END OF REPORT **

Laboratory Report	DNR-71466	Contract Sample No	DN-3046/21
Report Date	18/08/2021	Clients Reference	DN-3046/21
		Material Description	6F5

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Gibbson Street Manchester

Date Sampled	05/07/2021
Sampling Plan	CTS Procedure
Source	Not Stated
Supplier	Not Stated
Sampled By	CTS
Sampling Environment	N/A
Sample Type	Bulk
Location in sample	N/A
Sample Location	Not Stated

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft
Doncaster
DN7 4JU
UKAS TESTING 4161
Tel: (01302) 352652 Web: www.constructiontesting.co.uk
Email: enquiries@constructiontesting.co.uk

Date Received	05/07/2021
Date Tests Completed	13/08/2021

TEST REPORT

Determination of Water Content by Drying in a Ventilated Oven
Tested in Accordance with BS EN 1097-5:2008


Water content of test portion *(w)* 12.1 %

Aggregate Type: 6F5

Nominal Size (mm): 50

Determination of Particle Size Distribution (wet sieving method)
Tested in Accordance with BS EN 933-1: 2012

BS Sieve Size	Passing BS Sieve	Specification MCHW SHW Vol 1 Series 600 Table 6/5 Class 6F5
500 mm	100 %	
300 mm	100 %	
125 mm	100 %	100
80 mm	100 %	75 - 99
63 mm	95 %	
50 mm	87 %	
40 mm	80 %	50 - 90
31.5 mm	74 %	
25 mm	68 %	
20 mm	64 %	30 - 75
16 mm	60 %	
14 mm	59 %	
12.5 mm	57 %	
10 mm	55 %	15 - 60
8 mm	52 %	
6.3 mm	50 %	
5 mm	49 %	
4 mm	47 %	
2.8 mm	45 %	
2 mm	43 %	0 - 35
1 mm	40 %	
500 µm	34 %	
250 µm	25 %	
125 µm	18 %	
63 µm	14.9 %	0 - 12

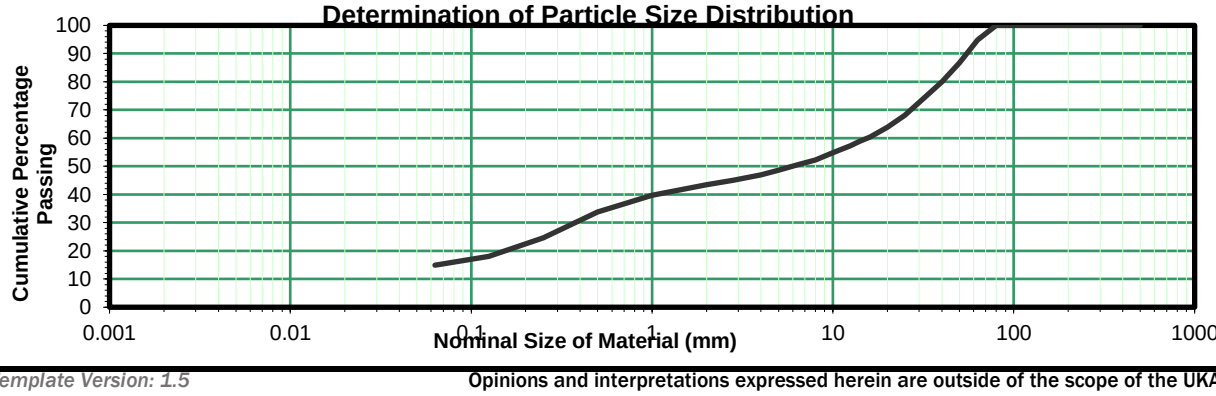

Template Version: 1.5

Opinions and interpretations expressed herein are outside of the scope of the UKAS Accreditation.
Results relate only to the sample(s) as received.
This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.
The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.

Authorised Signatory

R Walker - Senior Laboratory Technician

** END OF REPORT **

Laboratory Report	DNR-71467	Contract Sample No	DN-3046/22
Report Date	18/08/2021	Clients Reference	DN-3046/22
		Material Description	6F5

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Gibbson Street Manchester

Date Sampled	05/07/2021
Sampling Plan	CTS Procedure
Source	Not Stated
Supplier	Not Stated
Sampled By	CTS
Sampling Environment	N/A
Sample Type	Bulk
Location in sample	N/A
Sample Location	Not Stated

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft
Doncaster
DN7 4JU
UKAS TESTING 4161
Tel: (01302) 352652 Web: www.constructiontesting.co.uk
Email: enquiries@constructiontesting.co.uk

Date Received	05/07/2021
Date Tests Completed	13/08/2021

TEST REPORT

Determination of Water Content by Drying in a Ventilated Oven
Tested in Accordance with BS EN 1097-5:2008


Water content of test portion *(w)* 11.6 %

Aggregate Type: 6F5

Nominal Size (mm): 63

Determination of Particle Size Distribution (wet sieving method)
Tested in Accordance with BS EN 933-1: 2012

BS Sieve Size	Passing BS Sieve	Specification MCHW SHW Vol 1 Series 600 Table 6/5 Class 6F5
500 mm	100 %	
300 mm	100 %	
125 mm	100 %	100
80 mm	94 %	75 - 99
63 mm	86 %	
50 mm	80 %	
40 mm	76 %	50 - 90
31.5 mm	72 %	
25 mm	67 %	
20 mm	61 %	30 - 75
16 mm	57 %	
14 mm	56 %	
12.5 mm	55 %	
10 mm	53 %	15 - 60
8 mm	50 %	
6.3 mm	48 %	
5 mm	47 %	
4 mm	45 %	
2.8 mm	43 %	
2 mm	42 %	0 - 35
1 mm	38 %	
500 µm	32 %	
250 µm	23 %	
125 µm	17 %	
63 µm	13.6 %	0 - 12

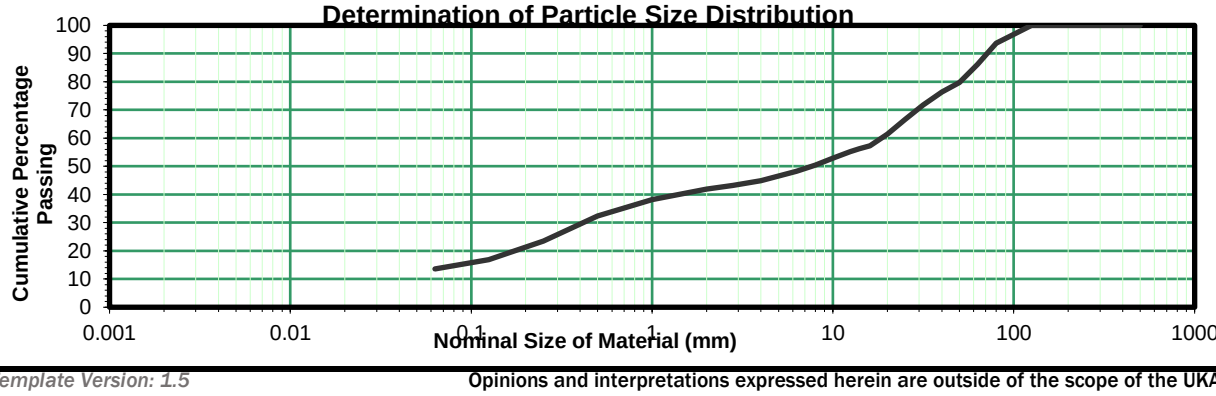

Template Version: 1.5

Authorised Signatory

R Walker - Senior Laboratory Technician

Opinions and interpretations expressed herein are outside of the scope of the UKAS Accreditation.
Results relate only to the sample(s) as received.
This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.
The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.

** END OF REPORT **

Laboratory Report	DNR-71468	Contract Sample No	DN-3046/23
Report Date	18/08/2021	Clients Reference	DN-3046/23
		Material Description	Type 1

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Gibbson Street Manchester

Date Sampled	05/07/2021
Sampling Plan	CTS Procedure
Source	Not Stated
Supplier	Not Stated
Sampled By	CTS
Sampling Environment	N/A
Sample Type	Bulk
Location in sample	N/A
Sample Location	Not Stated

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft
Doncaster
DN7 4JU
UKAS TESTING 4161
Tel: (01302) 352652 Web: www.constructiontesting.co.uk
Email: enquiries@constructiontesting.co.uk

Date Received	05/07/2021
Date Tests Completed	13/08/2021

TEST REPORT

Determination of Water Content by Drying in a Ventilated Oven
Tested in Accordance with BS EN 1097-5:2008


Water content of test portion *(w)* 8.1 %

Aggregate Type: Type1
Nominal Size (mm): 31.5

Determination of Particle Size Distribution (wet sieving method)
Tested in Accordance with BS EN 933-1: 2012

BS Sieve Size	Passing BS Sieve	Specification MCHW. SHW Vol 1, Series 800, cl 803 Table 8/5
500 mm	100 %	
300 mm	100 %	
125 mm	100 %	
80 mm	100 %	
63 mm	100 %	100
50 mm	100 %	
40 mm	100 %	
31.5 mm	86 %	75 - 99
25 mm	74 %	
20 mm	64 %	
16 mm	57 %	43 - 81*
14 mm	55 %	
12.5 mm	53 %	
10 mm	49 %	
8 mm	45 %	23 - 66*
6.3 mm	42 %	
5 mm	39 %	
4 mm	37 %	12 - 53*
2.8 mm	35 %	
2 mm	33 %	6 - 42*
1 mm	29 %	3 - 32*
500 µm	24 %	
250 µm	19 %	
125 µm	13 %	
63 µm	9.8 %	0 - 9

*Suppliers Declared Limit Not Stated

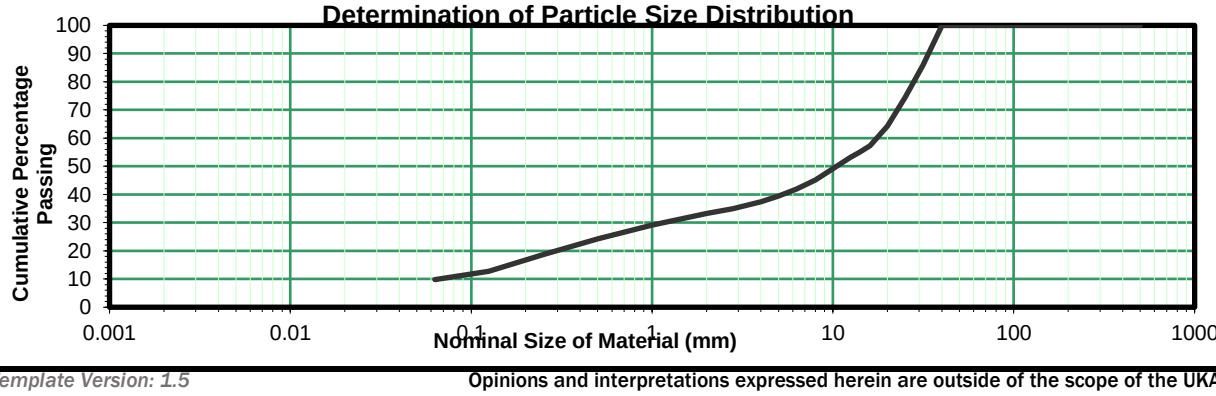

Template Version: 1.5

Opinions and interpretations expressed herein are outside of the scope of the UKAS Accreditation.
Results relate only to the sample(s) as received.
This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.
The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.

Authorised Signatory

R Walker - Senior Laboratory Technician

** END OF REPORT **

Laboratory Report	DNR-71469	Contract Sample No	DN-3046/24
Report Date	18/08/2021	Clients Reference	DN-3046/24
		Material Description	Type 1

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Gibbson Street Manchester

Date Sampled	05/07/2021
Sampling Plan	CTS Procedure
Source	Not Stated
Supplier	Not Stated
Sampled By	CTS
Sampling Environment	N/A
Sample Type	Bulk
Location in sample	N/A
Sample Location	Not Stated

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft
Doncaster
DN7 4JU
UKAS TESTING 4161
Tel: (01302) 352652 Web: www.constructiontesting.co.uk
Email: enquiries@constructiontesting.co.uk

Date Received	05/07/2021
Date Tests Completed	13/08/2021

TEST REPORT

Determination of Water Content by Drying in a Ventilated Oven
Tested in Accordance with BS EN 1097-5:2008


Water content of test portion *(w)* 8.0 %

Aggregate Type: Type1
Nominal Size (mm): 31.5

Determination of Particle Size Distribution (wet sieving method)
Tested in Accordance with BS EN 933-1: 2012

BS Sieve Size	Passing BS Sieve	Specification MCHW. SHW Vol 1, Series 800, cl 803 Table 8/5
500 mm	100 %	
300 mm	100 %	
125 mm	100 %	
80 mm	100 %	
63 mm	100 %	100
50 mm	100 %	
40 mm	100 %	
31.5 mm	88 %	75 - 99
25 mm	75 %	
20 mm	66 %	
16 mm	59 %	43 - 81*
14 mm	55 %	
12.5 mm	53 %	
10 mm	48 %	
8 mm	44 %	23 - 66*
6.3 mm	41 %	
5 mm	38 %	
4 mm	36 %	12 - 53*
2.8 mm	33 %	
2 mm	31 %	6 - 42*
1 mm	27 %	3 - 32*
500 µm	22 %	
250 µm	16 %	
125 µm	10 %	
63 µm	6.7 %	0 - 9

*Suppliers Declared Limit Not Stated

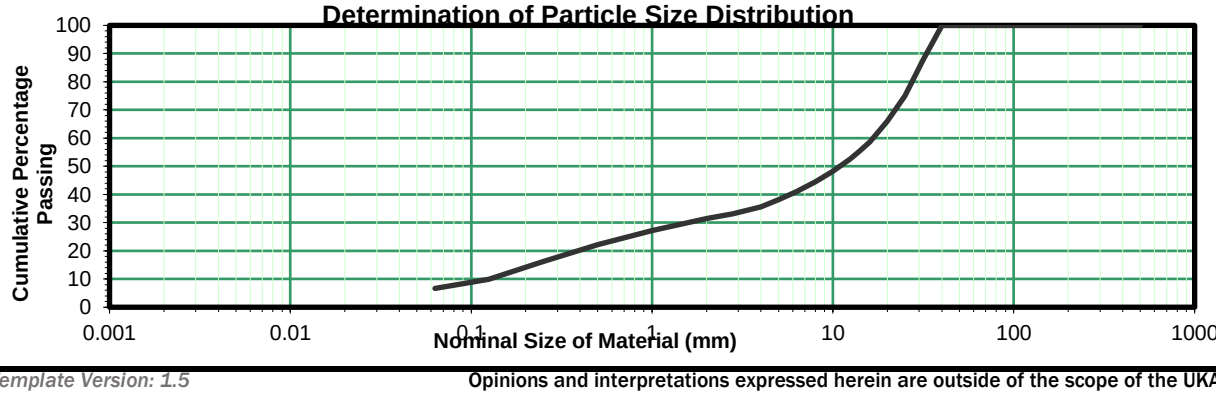

Template Version: 1.5

Opinions and interpretations expressed herein are outside of the scope of the UKAS Accreditation.
Results relate only to the sample(s) as received.
This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.
The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.

Authorised Signatory

R Walker - Senior Laboratory Technician

** END OF REPORT **

Laboratory Report	DNR/77975	Contract Sample No	DN-3046/26
Report Date	10/09/2021	Clients Reference	DN-3046/26
		Material Description	SP6/01/02 Recycled Type 1
Provectus Remediation Limited			
Regent House		Date Sampled	21/07/2021
Bath Avenue		Sampling Plan	Client Specification
Wolverhampton		Source	Ex-site
WV1 4EG		Supplier	Ex-Site
		Sampled By	CTS
		Sampling Environment	Not Stated
		Sample Type	Bulk
Gibbson Street Manchester		Location in sample	N/A
		Sample Location	Stockpile

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft
Doncaster
DN7 4JU
UKAS TESTING 4161
Tel: (01302) 352652 Web: www.constructiontesting.co.uk
Email: enquiries@constructiontesting.co.uk

Date Received	22/07/2021
Date Tests Completed	07/09/2021

TEST REPORT

Determination of Water Content by Drying in a Ventilated Oven
Tested in Accordance with BS EN 1097-5:2008

Water content of test portion *(w)* 1.9 %


Aggregate Type: Type1

Nominal Size (mm): 31.5

Determination of Particle Size Distribution (wet sieving method)
Tested in Accordance with BS EN 933-1: 2012

BS Sieve Size	Passing BS Sieve	Specification: MCHW. SHW Vol 1, Series 800, cl 803 Table 8/5
500 mm	100 %	
300 mm	100 %	
125 mm	100 %	
80 mm	100 %	
63 mm	100 %	100
50 mm	100 %	
40 mm	100 %	
31.5 mm	77 %	75 - 99
25 mm	64 %	
20 mm	57 %	
16 mm	46 %	43 - 81*
14 mm	43 %	
12.5 mm	41 %	
10 mm	38 %	
8 mm	36 %	23 - 66*
6.3 mm	34 %	
5 mm	33 %	
4 mm	32 %	12 - 53*
2.8 mm	31 %	
2 mm	30 %	6 - 42*
1 mm	27 %	3 - 32*
500 µm	22 %	
250 µm	17 %	
125 µm	10 %	
63 µm	7.3 %	0 - 9

*Suppliers Declared Limit Not Stated

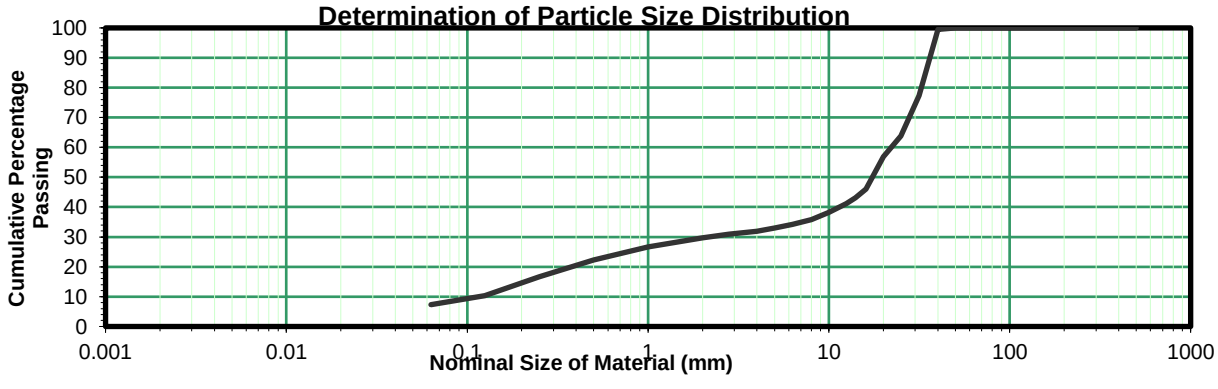

Laboratory Report	DNR/77975	Contract Sample No	DN-3046/26
Report Date	10/09/2021	Clients Reference	DN-3046/26
		Material Description	SP6/01/02 Recycled Type 1
Provectus Remediation Limited			
Regent House		Date Sampled	21/07/2021
Bath Avenue		Sampling Plan	Client Specification
Wolverhampton		Source	Ex-site
WV1 4EG		Supplier	Ex-Site
		Sampled By	CTS
		Sampling Environment	Not Stated
		Sample Type	Bulk
Gibbson Street Manchester		Location in sample	N/A
		Sample Location	Stockpile

Construction Testing Solutions

Bootham Lane Industrial Estate
Dunscroft
Doncaster
DN7 4JU

UKAS TESTING 4161

Tel: (01302) 352652 Web: www.constructiontesting.co.uk
Email: enquiries@constructiontesting.co.uk

Date Received	22/07/2021
Date Tests Completed	07/09/2021

TEST REPORT

Template Version: 1.5

Opinions and interpretations expressed herein are outside of the scope of the UKAS Accreditation.

Results relate only to the sample(s) as received.

This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.

The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.

Authorised Signatory R Walker

R Walker - Senior Laboratory Technician

** END OF REPORT **

Construction Testing Solutions is a trading division of Construction Testing Solutions Ltd - Company No. 05998333

Laboratory Report	DNR/77976	Contract Sample No	DN-3046/27
Report Date	08/09/2021	Clients Reference	DN-3046/27
		Material Description	SP6/01/01 Recycled Type 1
Provectus Remediation Limited			
Regent House		Date Sampled	21/07/2021
Bath Avenue		Sampling Plan	Client Specification
Wolverhampton		Source	Ex-site
WV1 4EG		Supplier	Ex-Site
		Sampled By	CTS
		Sampling Environment	Not Stated
		Sample Type	Bulk
Gibbson Street Manchester		Location in sample	N/A
		Sample Location	Stockpile

Construction Testing Solutions

Bootham Lane Industrial Estate
Dunscroft
Doncaster
DN7 4JU

UKAS TESTING 4161

Tel: (01302) 352652 Web: www.constructiontesting.co.uk
Email: enquiries@constructiontesting.co.uk

Date Received	22/07/2021
Date Tests Completed	07/09/2021

TEST REPORT

Determination of Water Content by Drying in a Ventilated Oven
Tested in Accordance with BS EN 1097-5:2008

Water content of test portion *(w)* 2.1 %


Aggregate Type: Type1

Nominal Size (mm): 31.5

Determination of Particle Size Distribution (wet sieving method)
Tested in Accordance with BS EN 933-1: 2012

BS Sieve Size	Passing BS Sieve	Specification MCHW. SHW Vol 1, Series 800, cl 803 Table 8/5
500 mm	100 %	
300 mm	100 %	
125 mm	100 %	
80 mm	100 %	
63 mm	100 %	100
50 mm	100 %	
40 mm	92 %	
31.5 mm	82 %	75 - 99
25 mm	68 %	
20 mm	59 %	
16 mm	52 %	43 - 81*
14 mm	48 %	
12.5 mm	46 %	
10 mm	43 %	
8 mm	40 %	23 - 66*
6.3 mm	38 %	
5 mm	36 %	
4 mm	34 %	12 - 53*
2.8 mm	32 %	
2 mm	31 %	6 - 42*
1 mm	27 %	3 - 32*
500 µm	22 %	
250 µm	16 %	
125 µm	10 %	
63 µm	6.7 %	0 - 9

*Suppliers Declared Limit Not Stated

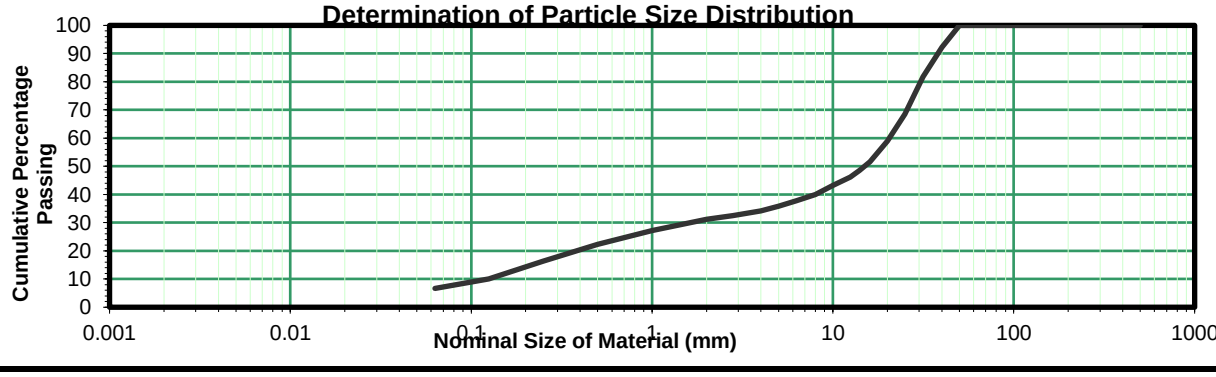

Laboratory Report	DNR/77976	Contract Sample No	DN-3046/27	Construction Testing Solutions	
Report Date	08/09/2021	Clients Reference	DN-3046/27		
		Material Description	SP6/01/01 Recycled Type 1	Bootham Lane Industrial Estate	
Provectus Remediation Limited				Dunscroft	
Regent House		Date Sampled	21/07/2021	Doncaster	
Bath Avenue		Sampling Plan	Client Specification	DN7 4JU	
Wolverhampton		Source	Ex-site		
WV1 4EG		Supplier	Ex-Site		
		Sampled By	CTS	Tel: (01302) 352652	Web: www.constructiontesting.co.uk
		Sampling Environment	Not Stated	Email: enquiries@constructiontesting.co.uk	
		Sample Type	Bulk	Date Received	22/07/2021
Gibbson Street Manchester		Location in sample	N/A	Date Tests Completed	07/09/2021
		Sample Location	Stockpile	**TEST REPORT**	

UKAS TESTING 4161

Template Version: 1.5

Opinions and interpretations expressed herein are outside of the scope of the UKAS Accreditation.

Results relate only to the sample(s) as received.

This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.

The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.

Authorised Signatory R Walker

R Walker - Senior Laboratory Technician

** END OF REPORT **

Construction Testing Solutions is a trading division of Construction Testing Solutions Ltd - Company No. 05998333

Laboratory Report	DNR/91968	Contract Sample No	DN3046/40
Report Date	07/12/2021	Clients Reference	DN3046/40
		Material Description	6F2
Provectus Remediation Limited			
Regent House		Date Sampled	Not Stated
Bath Avenue		Sampling Plan	Client Specification
Wolverhampton		Source	Not Stated
WV1 4EG		Supplier	Not Stated
		Sampled By	Not Known
		Sampling Environment	Not Stated
		Sample Type	Bulk
Gibbon Street, Manchester		Location in sample	N/A
		Sample Location	Not Stated

Construction Testing Solutions
Bootham Lane Industrial Estate
Dunscroft
Doncaster
DN7 4JU
4161
Tel: (01302) 352652 Web: www.constructiontesting.co.uk
Email: enquiries@constructiontesting.co.uk

Date Received	Not Stated
Date Tests Completed	06/12/2021

TEST REPORT

Determination of moisture content


Prepared and tested in Accordance with BS 1377: Part 2: 1990 Clause 3.2 - Oven drying

Moisture Content 8.7 %

Particle size distribution (wet sieving method) - Tested in accordance with BS 1377: Part 2: 1990 Clause 9.2

Sample prepared in Accordance with BS 1377: Part 1: 2016 clause 8.3.4(a)

BS Sieve Size (mm)	Passing BS Sieve (%)	Specification
		MCHW SHW Vol 1 Series 600 Table 6/2 Class 6F2
500	100	
300	100	
125	100	100
100	100	
90	100	80 - 100
75	96	65 - 100
63	77	
50	72	
37.5	64	45 - 100
28	53	
20	43	
14	38	
10	36	15 - 60
6.3	33	
5	32	10 - 45
3.35	28	
2	25	
1.18	21	
0.600	16	0 - 25
0.425	14	
0.300	12	
0.150	9	
0.063	8	0 - 12

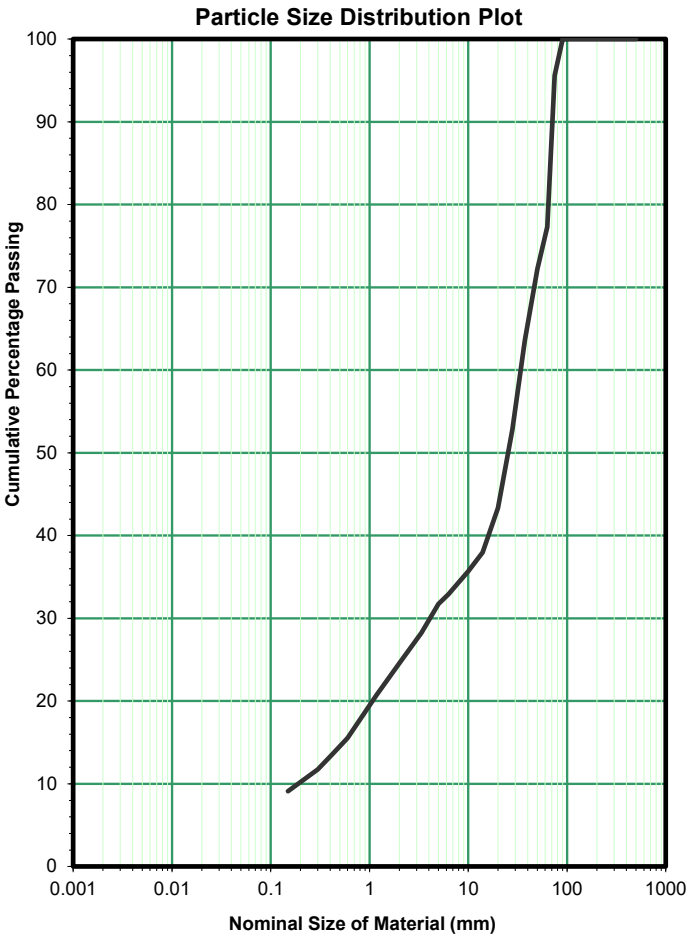

Template Version: 1.6

Authorised Signatory

Opinions and interpretations expressed herein are outside of the scope of the UKAS Accreditation.

Results relate only to the sample(s) as received.

This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.

The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.

** END OF REPORT **

Laboratory Report	DNR/91969	Contract Sample No	DN3046/41
Report Date	07/12/2021	Clients Reference	DN3046/41
		Material Description	6F2
Regent House			
Bath Avenue		Date Sampled	Not Stated
Wolverhampton		Sampling Plan	Client Specification
WV1 4EG		Source	Not Stated
		Supplier	Not Stated
Gibbon Street, Manchester		Sampled By	Not Known
		Sampling Environment	Not Stated
		Sample Type	Bulk
Gibbon Street, Manchester		Location in sample	N/A
		Sample Location	Not Stated

Construction Testing Solutions

Bootham Lane Industrial Estate
Dunscroft
Doncaster
DN7 4JU

UKAS TESTING 4161

Tel: (01302) 352652 Web: www.constructiontesting.co.uk
Email: enquiries@constructiontesting.co.uk

Date Received	Not Stated
Date Tests Completed	06/12/2021

TEST REPORT

Determination of moisture content


Prepared and tested in Accordance with BS 1377: Part 2: 1990 Clause 3.2 - Oven drying

Moisture Content 9.0 %

Particle size distribution (wet sieving method) - Tested in accordance with BS 1377: Part 2: 1990 Clause 9.2

Sample prepared in Accordance with BS 1377: Part 1: 2016 clause 8.3.4(a)

BS Sieve Size (mm)	Passing BS Sieve (%)	Specification
		MCHW SHW Vol 1 Series 600 Table 6/2 Class 6F2
500	100	
300	100	
125	100	100
100	100	
90	100	80 - 100
75	93	65 - 100
63	79	
50	72	
37.5	69	45 - 100
28	58	
20	48	
14	42	
10	39	15 - 60
6.3	35	
5	34	10 - 45
3.35	29	
2	25	
1.18	22	
0.600	17	0 - 25
0.425	15	
0.300	14	
0.150	10	
0.063	8	0 - 12

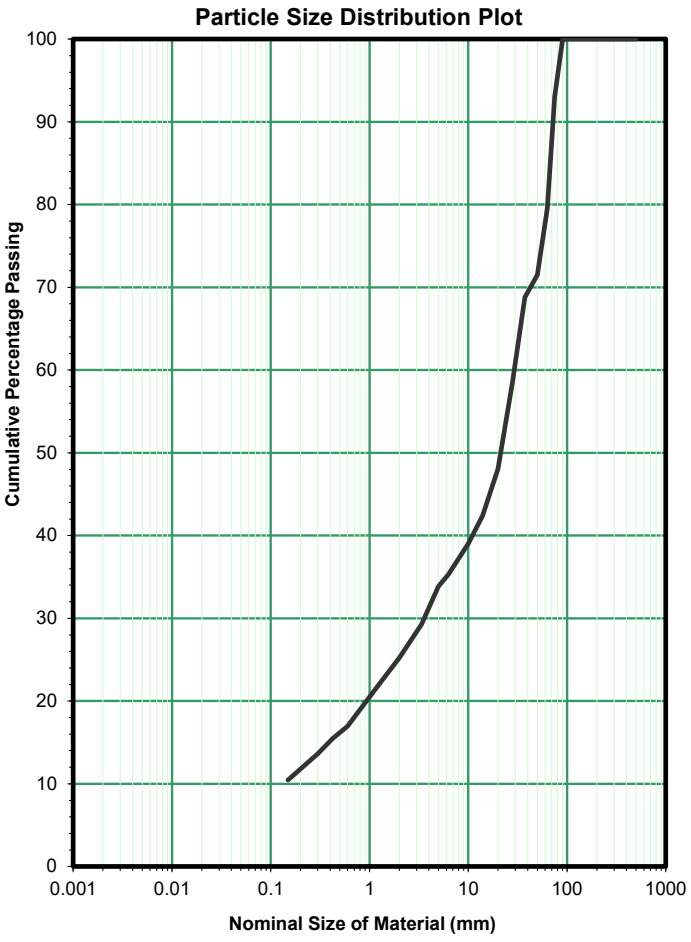

Template Version: 1.6

Authorised Signatory

Opinions and interpretations expressed herein are outside of the scope of the UKAS Accreditation.

Results relate only to the sample(s) as received.

This report may not be reproduced other than in full without the prior written approval of the issuing laboratory.

The laboratory does not apply a conformity statement to test reports as standard, unless specifically requested by the customer.

** END OF REPORT **


Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-23760-1
Initial Date of Issue:	15-Jul-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Sam Lane-Ryan
Project	101114 BAM Construction Site, Sportcity Way, Manchester

Quotation No.:	Q21-23216	**Date Received:**	12-Jul-2021
Order No.:	9746	**Date Instructed:**	12-Jul-2021
No. of Samples:	4		
Turnaround (Wkdays):	6	**Results Due:**	19-Jul-2021
Date Approved:	15-Jul-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Water

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-23760	21-23760	21-23760	21-23760
Quotation No.: Q21-23216			**Chemtest Sample ID.:**		1238194	1238195	1238196	1238197
Order No.: 9746			Client Sample Ref.:		BMP1090721	BMP2090721	BMP3090721	BMP4090721
			Client Sample ID.:		09/07/2021	09/07/2021	09/07/2021	09/07/2021
			Sample Location:		BMP1	BMP2	BMP3	BMP4
			Sample Type:		WATER	WATER	WATER	WATER
			Date Sampled:		11-Jun-2021	11-Jun-2021	11-Jun-2021	11-Jun-2021
Determinand	**Accred.**	**SOP**	**Units**	**LOD**				
Rate of Deposition	N		mg/m²/day	18	800	3800	620	360
Total Solids	N	1035	mg	5.0	900	4300	700	410

Test Methods

SOP	Title	Parameters included	Method summary
1035	Total Solids	Total Solids	Gravimetry

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com


Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-32690-1
Initial Date of Issue:	23-Sep-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Sam Lane-Ryan
Project	101114 BAM Construction Site, Sportcity Way, Manchester

Quotation No.:	Q21-23216	**Date Received:**	21-Sep-2021
Order No.:	9746	**Date Instructed:**	21-Sep-2021
No. of Samples:	4		
Turnaround (Wkdays):	5	**Results Due:**	27-Sep-2021
Date Approved:	23-Sep-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Water

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-32690	21-32690	21-32690	21-32690
Quotation No.: Q21-23216			**Chemtest Sample ID.:**		1282989	1282990	1282991	1282992
Order No.: 9746			Client Sample Ref.:		BMP1 170921	BMP2 170921	BMP3 170921	BMP4 170921
			Sample Location:		BMP1	BMP2	BMP3	BMP4
			Sample Type:		WATER	WATER	WATER	WATER
			Date Sampled:		13-Aug-2021	13-Aug-2021	13-Aug-2021	13-Aug-2021
Determinand	**Accred.**	**SOP**	**Units**	**LOD**				
Rate of Deposition	N		mg/m²/day	18	530	200	350	93
Total Solids	N	1035	mg	5.0	750	280	500	130

Test Methods

SOP	Title	Parameters included	Method summary
1035	Total Solids	Total Solids	Gravimetry

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com


Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-36102-1
Initial Date of Issue:	21-Oct-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Sam Lane-Ryan
Project	101114 Bam Construction Site, Sportcity Way, Manchester, M11

Quotation No.:	Q21-23216	**Date Received:**	18-Oct-2021
Order No.:	9746	**Date Instructed:**	18-Oct-2021
No. of Samples:	4		
Turnaround (Wkdays):	5	**Results Due:**	22-Oct-2021
Date Approved:	21-Oct-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Water

Project: 101114 Bam Construction Site, Sportcity Way, Manchester, M11

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-36102	21-36102	21-36102	21-36102
Quotation No.: Q21-23216			**Chemtest Sample ID.:**		1300236	1300237	1300238	1300239
Order No.: 9746			Client Sample Ref.:		BMP1151021	BMP2151021	BMP3151021	BMP4151021
			Client Sample ID.:		15/10/2021	15/10/2021	15/10/2021	15/10/2021
			Sample Location:		BMP1	BMP2	BMP3	BMP4
			Sample Type:		WATER	WATER	WATER	WATER
			Date Sampled:		17-Sep-2021	17-Sep-2021	17-Sep-2021	17-Sep-2021
Determinand	**Accred.**	**SOP**	**Units**	**LOD**				
Rate of Deposition	N		mg/m²/day	18	19	490	24	370
Total Solids	N	1035	mg	5.0	22	550	27	420

Test Methods

SOP	Title	Parameters included	Method summary
1035	Total Solids	Total Solids	Gravimetry

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com


Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-39860-1
Initial Date of Issue:	19-Nov-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Tom Harrington
Project	101114 BAM Construction Site, Sportcity Way, Manchester

Quotation No.:	Q21-23216	**Date Received:**	15-Nov-2021
Order No.:	9746	**Date Instructed:**	15-Nov-2021
No. of Samples:	4		
Turnaround (Wkdays):	5	**Results Due:**	19-Nov-2021
Date Approved:	19-Nov-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Water

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-39860	21-39860	21-39860	21-39860
Quotation No.: Q21-23216			**Chemtest Sample ID.:**		1319031	1319032	1319033	1319034
Order No.: 9746			Client Sample Ref.:		BMP1121121	BMP2121121	BMP3121121	BMP4121121
			Sample Location:		12/11/2021	12/11/2022	12/11/2023	12/11/2024
			Sample Type:		WATER	WATER	WATER	WATER
			Date Sampled:		15-Oct-2021	15-Oct-2021	15-Oct-2021	15-Oct-2021
Determinand	**Accred.**	**SOP**	**Units**	**LOD**				
Rate of Deposition	N		mg/m²/day	18	110	170	< 18	230
Total Solids	N	1035	mg	5.0	130	190	< 5.0	260

Test Methods

SOP	Title	Parameters included	Method summary
1035	Total Solids	Total Solids	Gravimetry

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com


Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-12579-1
Initial Date of Issue:	21-Apr-2021
Client	Provectus Group Ltd
Client Address:	Regent House Bath Avenue Wolverhampton Staffordshire WV1 4EG
Contact(s):	Charlotte Nicholson Sam Lane-Ryan
Project	101114 BAM Construction Site, Sportcity Way, Manchester

Quotation No.:	Q21-23216	**Date Received:**	20-Apr-2021
Order No.:	9746	**Date Instructed:**	20-Apr-2021
No. of Samples:	4		
Turnaround (Wkdays):	5	**Results Due:**	26-Apr-2021
Date Approved:	21-Apr-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Water

Project: 101114 BAM Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-12579	21-12579	21-12579	21-12579
Quotation No.: Q21-23216			**Chemtest Sample ID.:**		1182348	1182349	1182350	1182351
Order No.: 9746			Client Sample Ref.:		16/04/2021 BMP1160421	16/04/2021 BMP2160421	16/04/2021 BMP3160421	16/04/2021BMP4160421
			Sample Location:		BMP1	BMP2	BMP3	BMP4
			Sample Type:		WATER	WATER	WATER	WATER
			Date Sampled:		19-Mar-2021	19-Mar-2021	19-Mar-2021	19-Mar-2021
Determinand	**Accred.**	**SOP**	**Units**	**LOD**				
Rate of Deposition	N		mg/m²/day	18	< 18	< 18	24	< 18
Total Solids	N	1035	mg	5.0	13	7.9	27	18

Test Methods

SOP	Title	Parameters included	Method summary
1035	Total Solids	Total Solids	Gravimetry

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 45 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com

Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-16279-1
Initial Date of Issue:	18-May-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Charlotte Nicholson Sam Lane-Ryan
Project	101114 Bam Construction Site, Sportcity Way, Manchester, M11

Quotation No.:	Q21-23216	**Date Received:**	17-May-2021
Order No.:	9746	**Date Instructed:**	17-May-2021
No. of Samples:	4		
Turnaround (Wkdays):	5	**Results Due:**	21-May-2021
Date Approved:	18-May-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Water

Project: 101114 Bam Construction Site, Sportcity Way, Manchester, M11

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-16279	21-16279	21-16279	21-16279
Quotation No.: Q21-23216			**Chemtest Sample ID.:**		1201467	1201468	1201469	1201470
Order No.: 9746			Client Sample Ref.:		BMP1140521	BMP2140521	BMP3140521	BMP4140521
			Client Sample ID.:		14.05.2021	14.05.2021	14.05.2021	14.05.2021
			Sample Location:		BMP1	BMP2	BMP3	BMP4
			Sample Type:		WATER	WATER	WATER	WATER
			Date Sampled:		16-Apr-2021	16-Apr-2021	16-Apr-2021	16-Apr-2021
Determinand	**Accred.**	**SOP**	**Units**	**LOD**				
Rate of Deposition	N		mg/m²/day	18	26	36	< 18	37
Total Solids	N	1035	mg	5.0	29	41	20	42

Test Methods

SOP	Title	Parameters included	Method summary
1035	Total Solids	Total Solids	Gravimetry

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 45 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com


Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-20193-1
Initial Date of Issue:	21-Jun-2021
Client	Provectus Group Ltd
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE
Contact(s):	Andy Clee Charlie Gould Jon Owens Sam Gould
Project	101114 Bam Construction Site, Sportcity Way, Manchester

Quotation No.:	Q21-23216	**Date Received:**	15-Jun-2021
Order No.:	9746	**Date Instructed:**	15-Jun-2021
No. of Samples:	4		
Turnaround (Wkdays):	5	**Results Due:**	21-Jun-2021
Date Approved:	21-Jun-2021		

Approved By:



Details: Glynn Harvey, Technical Manager

Results - Water

Project: 101114 Bam Construction Site, Sportcity Way, Manchester

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-20193	21-20193	21-20193	21-20193
Quotation No.: Q21-23216			**Chemtest Sample ID.:**		1220996	1220997	1220998	1220999
Order No.: 9746			Client Sample Ref.:		BMP1110621	BMP2110621	BMP3110621	BMP4110621
			Client Sample ID.:		11/06/2021	11/06/2021	11/06/2021	11/06/2021
			Sample Location:		BMP1	BMP2	BMP3	BMP4
			Sample Type:		WATER	WATER	WATER	WATER
			Date Sampled:		14-May-2021	14-May-2021	14-May-2021	14-May-2021
Determinand	**Accred.**	**SOP**	**Units**	**LOD**				
Rate of Deposition	N		mg/m²/day	18	950	1500	1200	570
Total Solids	N	1035	mg	5.0	1100	1700	1300	640

Test Methods

SOP	Title	Parameters included	Method summary
1035	Total Solids	Total Solids	Gravimetry

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com

Eurofins Chemtest Ltd
Depot Road
Newmarket
CB8 0AL
Tel: 01638 606070
Email: info@chemtest.com

Final Report

Report No.:	21-28482-1		
Initial Date of Issue:	23-Aug-2021		
Client	Provectus Group Ltd		
Client Address:	Unit 9, Kingsdale Business Centre Regina Road Chelmsford Essex CM1 1PE		
Contact(s):	Charlotte Nicholson Sam Lane-Ryan		
Project	101114 BAM Construction Site, Sportcity Way, Manchester, M11		
Quotation No.:	Q21-23216	**Date Received:**	17-Aug-2021
Order No.:	9848	**Date Instructed:**	17-Aug-2021
No. of Samples:	4		
Turnaround (Wkdays):	5	**Results Due:**	23-Aug-2021
Date Approved:	23-Aug-2021		
Approved By:			
Details:	Glynn Harvey, Technical Manager		

Results - Water

Project: 101114 BAM Construction Site, Sportcity Way, Manchester, M11

Client: Provectus Group Ltd			**Chemtest Job No.:**		21-28482	21-28482	21-28482	21-28482
Quotation No.: Q21-23216			**Chemtest Sample ID.:**		1262089	1262090	1262091	1262092
Order No.: 9848			Client Sample Ref.:		BMP1130821	BMP2130821	BMP3130821	BMP4130821
			Client Sample ID.:		13/08/2021	13/08/2021	13/08/2021	13/08/2021
			Sample Location:		BMP1	BMP2	BMP3	BMP4
			Sample Type:		WATER	WATER	WATER	WATER
			Date Sampled:		16-Jul-2021	16-Jul-2021	16-Jul-2021	16-Jul-2021
Determinand	**Accred.**	**SOP**	**Units**	**LOD**				
Rate of Deposition	N		mg/m²/day	18	190	230	520	640
Total Solids	N	1035	mg	5.0	210	260	590	730

Test Methods

SOP	Title	Parameters included	Method summary
1035	Total Solids	Total Solids	Gravimetry

Report Information

Key

U	UKAS accredited
M	MCERTS and UKAS accredited
N	Unaccredited
S	This analysis has been subcontracted to a UKAS accredited laboratory that is accredited for this analysis
SN	This analysis has been subcontracted to a UKAS accredited laboratory that is not accredited for this analysis
T	This analysis has been subcontracted to an unaccredited laboratory
I/S	Insufficient Sample
U/S	Unsuitable Sample
N/E	not evaluated
<	"less than"
>	"greater than"
SOP	Standard operating procedure
LOD	Limit of detection

Comments or interpretations are beyond the scope of UKAS accreditation
The results relate only to the items tested
Uncertainty of measurement for the determinands tested are available upon request
None of the results in this report have been recovery corrected
All results are expressed on a dry weight basis

The following tests were analysed on samples as received and the results subsequently corrected to a dry weight basis TPH, BTEX, VOCs, SVOCs, PCBs, Phenols

For all other tests the samples were dried at < 37°C prior to analysis
All Asbestos testing is performed at the indicated laboratory
Issue numbers are sequential starting with 1 all subsequent reports are incremented by 1

Sample Deviation Codes

A - Date of sampling not supplied
B - Sample age exceeds stability time (sampling to extraction)
C - Sample not received in appropriate containers
D - Broken Container
E - Insufficient Sample (Applies to LOI in Trommel Fines Only)

Sample Retention and Disposal

All soil samples will be retained for a period of 30 days from the date of receipt
All water samples will be retained for 14 days from the date of receipt
Charges may apply to extended sample storage

If you require extended retention of samples, please email your requirements to:
customerservices@chemtest.com

APPENDIX K Material and Stockpile Tracker

Materials Tracker

PROVECTUS

Stockpile Tracker

Pile Ref	Survey Date	Location	Volume m^3	Material	Notes
SP1	06/04/2021	F6	1735	6F2/made ground	Taken off site as non-hazardous waste
SP2	13/05/2021	C1	80	6F2	Stone for re-use
SP3	25/06/2021	E4	35	Made ground	Sampled for chemical analysis- results returned non-hazardous and removed off-site
SP4	25/06/2021	C2, C3	200	6F5	Stone for re-use
SP5	02/07/2021	A2	615	6F5	Stone for re-use. Surveyed again on 09/07/21 at 635 m^3
SP6	09/07/2021	F1	289	6F5	Stone for re-use (also imported Type 1)
SP7	17/09/2021	F5	25	Made ground	Sampled for chemical analysis- Carey's backfill
SP8	19/11/2021	F6	112	6F5/Type1	Sampled for chemical analysis

APPENDIX L Mobile Treatment Licence and Discharge Consent

Provectus Remediation Ltd
9 Kingsdale Business Centre
Regina Road
Chelmsford
Essex
CM1 1PE

Our ref: EB3636AK/W0021

Date: 14/08/2020

Dear Sir/Madam

Environmental Permitting (England and Wales) Regulations 2016

Deployment ref: EB3636AK/W0021
Permit holder: Provectus Remediation Ltd
Location of the deployment: Project Bradford, Sport City Way, Manchester, M11 3DU,

Following assessment of your deployment notification reference number EB3636AK/W0021 I can confirm that we have agreed your deployment form and you may now start to operate.

This deployment lasts for one year from the date the activity starts on site. If you wish to continue beyond this one year period you must re-notify.

You must comply with your permit and carry out the activities in accordance with the requirements of the agreed deployment form and

- further information (Ref: FW: RFI Request - Deployment Application EB3636AK/W0021) received by us on 11/08/2020 at 10:45 sent by Alex Clifford.

You must seek written permission from us if any of the details provided in the deployment form change.

This approval letter is associated with the mobile plant permitting regime only. As the operator, it is your responsibility to agree other authorisations, for example, planning permission, remedial strategy, abstraction or discharge consents with the relevant regulatory authority.

Please note that operating under your Mobile Plant Permit / Mobile Treatment Licence does not imply that the remediation processes used will be suitable for meeting any remediation objectives specified. These issues must be considered separately by the developer/consultant and our local area Groundwater and Contaminated Land team. These must be defined in the site remedial strategy which sets out the remediation options to reduce or control the risks from pollution linkages associated with the site as a whole. You may need to carry out further remediation if an unacceptable risk to the environment remains at the site.

Please notify us at least seven days prior to starting the remediation activities, at psc@environment-agency.gov.uk & GMMCDeployments@environment-agency.gov.uk.

If you have any queries about this matter please contact us by telephone on 03708 506 506 or email us at enquiries@environment-agency.gov.uk quoting your deployment application reference EB3636AK/W0021.

Yours faithfully

Maria Gibbons

Team Leader,
National Permitting Service

WATER INDUSTRY ACT 1991

CONSENT TO THE DISCHARGE OF TRADE EFFLUENT

Whereas **BAM Construction Limited**

(hereinafter called "the Trader") whose Head Office or Registered Office is at

Breakspear Park Breakspear Way Hemel Hempstead Hertfordshire HP2 4FL

Is the **owner/occupier** of the trade premises at:

Land adjacent to Etihad Stadium
(Main construction site)
Gibbon Street
Manchester
M11 3DU

and by the Duly made application dated **15 January 2021**

Have applied to UNITED UTILITIES WATER LIMITED (hereinafter called "the Company") for consent to discharge trade effluent from the said trade premises into the sewers.

Under the provisions of the above mentioned Act the discharge of trade effluent in accordance with the said application form would not be lawful without the consent of the Company.

NOW THEREFORE in exercise of the powers conferred upon them by the above Act the Company HEREBY CONSENT to the discharge of trade effluent by the Trader from the said premises into their sewers SUBJECT TO THE FOLLOWING CONDITIONS:

Nature of discharge

1a) Subject to the provisions of conditions 6,7,8 and 9 below the nature or composition of the trade effluent to be discharged under this Consent shall be solely as specified in the said application form and shall consist solely of waste water derived from **pumping of groundwater and surface water from excavations.**

1b) The trader shall give to the Company prior written notice of any change in the process or the process materials or any other circumstances likely to alter the constituents of the trade effluent as set out in condition 1(a). In such circumstances, no substance of which the Company has not had previous notice, may be discharged unless and until the Company has agreed to accept the substance at a limit imposed by the Company which shall then be deemed to be incorporated in this Consent by agreement and shall not prejudice the right of the Company to serve a Direction earlier than two years from the date of such incorporation.

The Trader shall also give not less than seven days written notice to the Company of any change in the name of the occupier or owner.

Sewer affected

2. The sewer into which the trade effluent may be discharged and the point of discharge is the foul sewer situate at **MH 8908 (MH 8904)**.

Connections

3. No connections shall be made to the said sewer without the prior approval of the Company and all such connections shall be constructed and maintained to the satisfaction of the Company at the expense of the Trader.

Maximum volume of discharge

4. The maximum amount of the trade effluent discharged in any one day of twenty four hours shall not exceed **432** m^3 without prior written consent of the Company.

Maximum rate of discharge

5. The highest rate at which the trade effluent may be discharged shall not exceed **5** litre/sec.

Matters to be eliminated prior to discharge to sewers

6. The following matters shall be eliminated from the trade effluent before it is discharged into the sewers of the Company:

a) petroleum spirit;

b) calcium carbide;

c) carbon disulphide;

d) except as provided in paragraph 7 hereof, the prescribed substances listed in Schedule 1 to The Trade Effluents (Prescribed Processes and Substances) Regulations 1989, as amended from time to time, insofar as they are in concentration greater than the background concentration (as defined in the said Regulations);

e) where the trade effluent derives from a prescribed process mentioned in Schedule 2 to the said Regulations, and except as provided in paragraph 7 hereof, asbestos (as defined in the said Regulations) and chloroform in concentration greater than the background concentration (as defined in the said Regulations);

f) organo-halogen compounds including pesticide residues and degreasing agents;

g) any substances which either alone or in combination with each other or with any other matter lawfully present in the said sewers would be likely to;

i) cause a nuisance or produce flammable, harmful or toxic vapours either in the sewers or at the sewage works of the Company;

ii) injure the sewers or interfere with the free flow of their contents or affect prejudicially the treatment and disposal of their contents or have injurious effects on the sewage treatment works to which it is conveyed or upon any treatment plant there;

iii) be dangerous to or cause injury to any person working in the sewers or at the sewage treatment works;

iv) affect prejudicially any watercourse, estuary or coastal water into which the treated effluent will eventually be discharged.

Matters to be limited prior to discharge to sewer

7. The trade effluent shall not contain

a) Ammonia and its compounds as N in excess of 250 mg/l

b) Arsenic as As in excess of 50 ug/l

c) Chloroform in excess of 100 ug/l

d) Cyanides and cyanogen compounds which produce hydrogen cyanide on acidification in excess of 1 mg/l

e) Methane in solution in excess of 0.14 mg/l

f) Phenols in excess of 20 mg/l

g) Separable grease and oil in excess of 100mg/l

h) Sulphates as SO_4 in excess of 1,000 mg/l

i) Sulphides, hydrosulphides, polysulphides and substances producing hydrogen sulphide on acidification in excess of 1 mg/l

j) Total nitrogen as N in excess of 250 mg/l

k) Total suspended solids at pH 7.0 and dried at 110° C in excess of 1,000 mg/l

l) Toxic metals in excess of 10,000 ug/l either individually or in total ie Antimony, Beryllium, Chromium, Copper, Lead, Nickel, Selenium, Silver, Tin, Vanadium, Zinc;

Temperature

8. No trade effluent shall be discharged which has a temperature higher than 43.3°C (110°F).

pH value

9. No trade effluent shall be discharged having a pH of less than **6** or greater than **10**

Inspection Chamber

10. a) An inspection chamber or manhole shall be provided and maintained by the Trader in a suitable position in connection with each pipe through which the trade effluent is discharged and shall be so constructed and maintained as to enable a person readily to obtain at any time samples of the trade effluent so discharged, to the approval of the Company.

b) There shall be provided, operated and maintained in working order by the Trader a meter in such a position and of such specification as shall be approved by UUWLtd such as will measure and provide a continuous record of the quantity and rate of discharge of any trade effluent being discharged from the premises into the said sewer and following the written request of UUWLtd to have the accuracy of the meter independently tested by an agreed body.

c) If the measuring and recording apparatus as aforesaid ceases to function satisfactorily, then the Company shall have the right to make estimates of the volume and composition of the trade effluent until such time as the said apparatus is again operating to the satisfaction of the Company.

d) Records shall be kept by the Trader of the volume, rate of discharge, nature and composition of the trade effluent discharged to the sewer, together with any records required to be kept by the Trader under the provisions of any Notice of Determination issued by the Secretary of State under Sections 120 and 132 of the Water Industry Act 1991. Such records shall be kept available for inspection at all reasonable times by an authorised officer of the Company and copies shall be sent to the Company on demand.

e) The foregoing provision of this condition shall be deemed to be complied with if other methods of sampling the trade effluent, determining its nature and composition, and measuring and recording the discharge are agreed and confirmed in writing by the Company.

Dated 01st March 2021

Issuing Office Wastewater Services
Lingley Mere Business Park
Lingley Green Avenue
Great Sankey
Warrington
WA5 3LP

Signed

WASTEWATER ASSET MANAGER
WASTEWATER SERVICES
for and on behalf of United Utilities Water Limited

Your attention is drawn to Section 122 of the Water Industry Act 1991 which provides that any person aggrieved by any conditions attached to this Consent may appeal to the Director General of Water Services.

APPENDIX M Material Management Plan

Materials Management Plan (MMP) Form - October 2014

This form should be completed once the lines of evidence have been marshalled in relation to suitability for use, certainty of use and quantity required.

The answers to the questions posed within this form, together with the supporting information will constitute the MMP and must be provided to the Qualified Person.

A Qualified Person may comment on draft versions of this MMP, but will not complete the Declaration until all the relevant documents, demonstrating lines of evidence have been provided for each site.

The person / organisation who will pay the Declaration fee should confirm that they have read and understand the Terms and Conditions relating to the payment of the Declaration fee to CL:AIRE. These can be found on the CL:AIRE website.

The person / organisation agreeing to pay the Declaration Fee - Name, organisation and contact details inc. email address -	Alex Clifford Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV 1 4EG Tel: 01902 810084 alex.clifford@provectusgroup.com

✓ ☐ **I confirm I have read and understood the Terms & Conditions.**

Each question must be answered. If the question is not applicable please state this and provide a brief explanation.

1. Specify the scenario to which this MMP relates, as described in the Definition of Waste: Development Industry Code of Practice (DoW CoP) (1, 2, 3 or 4):

✓ ☐ 1. Reuse on the Site of Origin

☐ 2. Direct Transfer of clean naturally occurring soil / mineral materials

☐ 3. Cluster Project

☐ 4. Combination of any of the above

In the case of a combination of reuse scenarios, please describe it below (e.g. (i) Reuse on Site of Origin and Direct Transfer of clean naturally occurring unpolluted soils, (ii) Reuse on the Site of Origin with Direct Transfer of clean naturally occurring soil to x number of development sites etc:

(NB: A Declaration is required for reuse on the Site of Origin and for any 2 site arrangement i.e. there is no facility for a combination Declaration)

2. Organisation and name of person preparing this MMP	Sam Lane-Ryan Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton WV 1 4EG Tel: 07817 940015

Document Control

Date issued	

Revision date	
Summary of revision 1	
Summary of revision 2	

Insert additional lines to the table above for any subsequent revisions.

Note - revisions to the MMP do not trigger an additional Declaration by a Qualified Person, unless an additional site is added to the project.

Revisions to the MMP must be recorded and summarised in the Document Control box above.

Site Details

3. Site / Project name(s)	Project Bradford, Sport City Way, 101114
Reuse / receiving site name :	Project Bradford, Sport City Way, Manchester, M11 3DU
Donor site name (if Direct Transfer)	n/a

Landowners

4a. Name of Landowner(s) (full address and contact details) – where excavated materials are to be reused	OVG Europe Ltd, 55 New Bond Street, London, Greater London, England, W1S 1DG. Address of reuse site: Project Bradford, Sport City Way, Manchester, M11 3DU
4b. Name of Landowner(s) (full address and contact details) – where excavated materials are arising from	As 4a.

Summary and objectives

5a. Provide a brief description of the planned project and how excavated materials are to be reused.	Project Bradford comprises the construction of a new multipurpose event stadium on the 25,000m^2 site. Provectus Remediation Ltd are undertaking the enabling earthworks. As such this MMP application relates solely to this phase of the wider project. In order to facilitate the stadium construction existing ground levels will be reduced to circa 55m AOD. This equates to an overall cut of circa 101,000m^3 across the site. The product of the enabling earthworks phase will be a development platform comprising compacted crushed aggregate and associated supporting temporary works in the form of engineered batters where required. Therefore, while there is a requirement for suitable off-site disposal of up to 101,000m^3 of material there is an opportunity to re-use site won aggregate as part of the development platform and geotechnically suitable soils as part of the temporary works engineered fill. Previously the site has been partially capped with crushed aggregate. Site investigations to date have identified a total of circa 10,000m^3 of crushed aggregate and relict below ground structures that will be screened and crushed as required to create a suitable aggregate product meeting the site specific re-use criteria for incorporation into the development platform. Subsequent to this, as the phases of the development platform progress there will be an opportunity to re-use and addition circa 2,000m^3 of the aggregate bring the total re-used aggregate volume to circa 12,000m^3. In addition to the aggregate a further circa 12,000m^3 of geotechnically suitable soils have been identified for potential temporary re-use in development enabling works – these soils will eventually be disposed of at a suitable off-site facility but are incorporated here to recognise the re-use on-site. In summary, the works relating to the earthworks phase and this MMP will comprise: • Pre-works soils testing comprising 48 no. trial pits undertaken on a 20x25m grid, with samples taken at depths representing each metre down to the dig formation level of 55m AOD, analysed for chemical content and waste classification. This equates to a pre-validation of one sample per 500m^3.

	• Areas of previously placed crushed aggregate will be segregated, screened as required and tested in accordance with the remedial strategy for re-use in the development platform. • Relict below ground structures will be crushed, tested and if suitable added to the site-won aggregate bringing the total volume of site-won crushed aggregate to circa 12,000m^3. • Soils consigned for re-use on site are to be sampled at a frequency of 1:250m^3. Circa 12,000m^3 of material is being proposed for re-use on site. Sampling will be for both chemical and grading purposes. Soils for re-use will meet the requirements of the remediation strategy (see point below) and a suitably graded material as defined in the Specification for Highways Works Series 600. These soils will be removed from site to a suitable off-site disposal facility at the completion of the piling activities to facilitate future phases of the development. • The site re-use criteria for soils not comprising subsoil/topsoil is set out in Table 3 of Appendix A of the Buro Happold Engineering Remediation Strategy, rev. 1, dated 25 September 2020, enclosed here in Appendix 2 • Remedial works involve the screening and hand-picking of asbestos contaminated soils where visible

General Plans and Schematics

6. **Attach** a location plan for the site(s) and a plan of the site(s) which identifies where different materials are to be excavated from, stockpile locations (if applicable), where materials are to be treated (if applicable) and where materials are to be reused.	Plan Document Reference(s): Site plans are included in Appendix 1, namely: • Site Location: SK101114/01 Site Location Plan • 20 x 25m site grid for soil validation / tracking: 10811b Rev.0 Trial Pit Survey • Plans showing progress of excavation and reprofiling with stockpile and materials processing areas on weekly basis: 101114 Week1 to 101114 Week 25 • On-site re-use will be as part of, or providing temporary support to the pile mats, these are

	shown on drawing: SK101114/02 Preliminary Pile Mat Layout

7. **Attach** a schematic of proposed materials movement. Where there is only one source area and one placement area briefly describe it. For all other projects a schematic is required.	Description & Schematic Document Reference: The proposed materials movements for the duration of the project are illustrated in the plans showing progress of excavation and reprofiling with stockpile and materials processing areas on weekly basis: 101114 Week1 to 101114 Week 25 - see Appendix 1. Records of material movements will be recorded on a materials tracker – see Appendix 4. Materials will be excavated, visually checked for Asbestos Containing Materials segregated into stockpiles based on evidence of contamination and data collected from site investigation works. Soils to be retained on site as part of this MMP will be subject to chemical testing in accordance with the Table 3 of Appendix A of the Buro Happold Engineering Remediation Strategy, rev. 1, dated 25 September 2020, enclosed here prior to reuse. They will also be graded to demonstrate geotechnical suitablilty All other soils excavated including those not meeting re-use criteria will be consigned for off-site disposal as required. In order to comply with the protocol set out in the CL:AIRE Definition of Waste Code of Practice, a tracking system register needs to be compiled and adhered to. The system will include; • A unique identification number for each stockpile from the creation to the end of the stockpile; • Details relating to the date of creation, material type, contamination status, volume, proposed endues/destination and information of chemical and/or geotechnical testing; • A schematic diagram showing the location, size, movement and ultimate destination of each stockpile, to be updated as required, daily if necessary; and • Number of samples taken per stockpile and results of analysis.

	Each stockpile should be clearly labelled to allow plant drivers and other Site staff and operatives to easily identify them. Where off-site licensed disposal is required, appropriate waste classification testing has been undertaken to allow an accurate disposal route to be determined. A record of the quantities of materials disposed off-site will be kept, along with consignment notes for the materials.

Parties Involved and Consultation – if more than one party please provide additional details for them and identify the location that they will be working e.g. where a site is zoned

8a. Main earthworks contractor(s) (full address and contact details) – Where excavated materials are to be reused	Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton West Midlands WV1 4EG Alex Clifford – Tel: 01902 810085 Email: alex.clifford@provectusgroup.com
8b. Main earthworks contractor(s) (full address and contact details) - Where excavated materials are arising from	As 8a.

9. Treatment contractor(s) (full address and contact details) – for treatment on site of origin, or at a Hub site within a fixed STF / Cluster Project	Provectus Remediation Ltd Regent House Bath Avenue Wolverhampton West Midlands WV1 4EG Alex Clifford – Tel: 01902 810085 Email: alex.clifford@provectusgroup.com

10. Where wastes and materials are to be transported between sites, provide details of the transport contractor(s) (full address, contact details and waste carriers registration details (if applicable))	N/A Re-use on site of origin for materials within the scope of this MMP

11. Provide Local Authority contact details (full address and named contacts) where excavated materials are to be reused	

12a. For the site where materials are to be reused and for Hub Site locations provide Environment Agency contact details (full address and named contacts):	Andy Davies, Andy.Davies1@environment-agency.gov.uk
For all Cluster Projects: 12b. Attach any relevant documentation from the EA relating to the excavation and reuse of the materials to demonstrate no objection to the proposals (see 3.37 of DoW CoP) If the EA has not been consulted please explain why (see paragraph 3.39 of the DoW CoP).	EA references: N/A – not a cluster project

Lines of Evidence

There is no one single factor that can be used to decide that a substance or object is waste, or when it is, at what point it ceases to be waste; as complete a picture as possible has to be created.

The following sections require completion to ensure the correct decision is made.

If a requested item is not relevant it is important to clearly state why this is so (e.g. no planning permission required because permitted development status exists).

Suitable for use criteria

13. Please describe or provide copies of the required specification(s) for the materials to be reused on each site.	Document Reference(s): Any material reused on site will be compliant with the specification set out in Table 3, Appendix A of the Buro Happold Engineering Remediation Strategy, rev. 1, dated 25 September 2020 included here in Appendix 2.

Where contamination is suspected or known to be present 14a. Please provide copies of or relevant extracts from the risk assessment(s) that has been used to determine the specification for use on the site. **This must relate to the place where materials are to be used.** This must be in terms of (i) human health (ii) controlled waters and (iii) any other relevant receptors. If a risk assessment is not relevant for a particular receptor given the site setting please explain why below:	Document Reference(s): Included in Appendix 2 are the third party site investigation and interpretive risk assessment documents from which the suitable for re-use criteria has been derived and included in the remediation strategy. The documents are: • Geoenvironmental and Geotechnical Desk Study, Buro Happold Engineering, Rev.P01 dated 13/12/19 • Ground Engineering Interpretive Report, Buro Happold Engineering, Rev.P04 dated 02/03/20 • Buro Happold Engineering Remediation Strategy, rev. 1, dated 25/09/20
14b. Please attach any relevant documentation from	LA Document references:

the LA relating to the excavation and reuse of the materials to demonstrate no objection (see 3.37 of the CoP)	
14c. Please attach any relevant documentation from the EA relating to the excavation and reuse of the materials to demonstrate no objection (see 3.37 and Table 2 of the CoP)	EA Document references: Email to the EA dated 03/02/21 stating intend to re-use materials under DoW COP in Appendix 3 - no reply within statuary timeframe.
14d. Please attach any relevant documentation from any other regulators (if relevant) relating to the excavation and reuse of the materials to demonstrate no objection (see 3.37 of the CoP)	Document Reference(s):

Where contamination is not suspected 15a. Please attach copies or relevant extracts from the Desk Top Study that demonstrates that there is no suspicion of contamination.	Document Reference(s) N/A
15b. Please attach copies of or relevant extracts from the site investigation/testing reports that adequately characterise the clean materials to be used (if appropriate).	Document Reference(s) N/A
15c. Please attach copies of any other relevant information (if available) confirming that land contamination is not an issue.	Document Reference(s) N/A

NB: It is your responsibility to assess the nature of the material to be used and that it fits within the limitations of the scenario under which it is to be used

Certainty of use

Various lines of evidence are required to demonstrate that the materials are certain to be used. This includes:

- The production of this MMP
- An appropriate planning permission (or conditions that link with the reuse of the said materials)
- An agreed Remediation Strategy(ies)
- An agreed Design Statement(s)
- Details of the contractual arrangements

Please identify in the following sections what lines of evidence relate to the site(s) **where the materials are to be used**.

16a. Planning Permission(s) relating to the site where materials are to be reused Please provide a copy of the relevant planning permission	Document Reference: Planning permission has been granted under application reference: 126431/FO/2020, a copy is included in Appendix 3
16b. Explain how the reuse of the excavated materials fits within the planning permission(s) for each site.	On-site re-use fits with Conditions 2 & 3 of the planning permission by: • Increasing re-cycling • Reducing traffic impacts to the local area through reduction in required imported materials • Reducing traffic impacts to the local area through avoiding doubling of off-site disposal vehicle movements of materials temporarily re-used on site.
16c. If planning permission is not required for any one site please explain why below e.g. permitted development, clean up of a chemical spill, surrender of an Environmental Permit, re-contouring within the	N/A

existing permission.	

Where contamination is suspected or is known to be present 17. Please provide a copy of any Remediation Strategy(ies) that have been agreed with relevant regulators.	Document Reference(s): Buro Happold Engineering Remediation Strategy, rev. 1, dated 25 September 2020

Where contamination is not suspected 18. Please provide a copy of any Design Statement(s) that have been agreed (e.g. with the planning authority or in the case of permitted developments the client).	Document Reference(s): N/A

Quantity of Use

19. Please provide a breakdown of the excavated materials for each site and how much will be placed at each site or sub area of each site. Where this is not specific to a single readily identifiable source refer to an annotated plan, schematic or attach a tabulated summary.	Document Reference(s): The circa 12,000m^3 of site won aggregate is based on the available SI data including the original SI and the Provectus Waste Classification Report 101114/R002 dated 13/03/2020 attached here in Appendix 2 which shows approximately half the 25,000m^2 site to be covered in ~600mm of crushed aggregate equating to 7,500m^3. It is expected a further <2,500m^3 will be recovered from relict below ground structures after on-site crushing, of which circa 2,000m^3 will be available for further re-use as the piling phases progress giving a total of circa 12,000m^3 of site won aggregate for re-use. The circa 12,000m^3 of site won soils for use in temporary works are based on the temporary works designs as provided by BAM referenced xxxxx and shown in drawing

	SK101114/02 Preliminary Pile Mat Layout (Appendix 1)

20a. How has consolidation/compaction being considered in the above mass balance calculations?	Suitable excavated materials are to be used as a backfill material across the site. Bulking/consolidation is expected to be neutral.
20b. How has loss due to treatment being considered in the above mass balance calculations (if applicable)?	Soils for re-use may be screened for removal of oversize but this volume is factored into the aggregate re-use. Where geotechnically unsuitable soils are encountered these will form part of the overall site cut for suitable off-site disposal. The re-use figure is based on estimated volume required in the temporary works the remainder of any soils or loss of volume due to treatment / unsuitability is not considered here as it will form part of the overall site cut, required to achieve development levels
20c. How has the addition of treatment materials being considered in the above mass balance calculations (if applicable)? Note - An exact figure is not required but one that is reasonable in the circumstances and can be justified if challenged.	N/A.

Contingency arrangements

Explain what is to happen in the following situations and **identify the appropriate clauses** in the contract(s) (Such clauses must be provided to the Qualified Person, preferably as a summary document): or

21a. What is to happen to, and who is to pay for out of specification materials?	Reference: Provectus to dispose of any out of specification materials. Appendix 8.
21b. What is to happen to, and who is to pay for any excess materials?	Reference: Provectus to dispose of any surplus materials. Appendix 8.
21c. What happens if the project programme slips in	Reference: There will be no need for on-site treatment of soils for re-

relation to excavated materials or materials under -going treatment?	use, pre-validation testing shows sufficient volumes are available already meeting re-use criteria. All other excavated materials are due for off-site disposal
21d. Other identified risk scenarios for the project (relating to excavated materials)?	Reference: N/A

The Tracking System

Where contamination is suspected or known to be present, state the procedures put in place to:

22a. For all sites please describe the tracking system to be employed to monitor materials movements.	Soils will be excavated in phases from specified locations as per Appendix 1 – Figures 101114 Week1 to 101114 Week 25 and records of movements maintained on a materials tracker – Appendix 4
Where contamination is suspected or known to be present, state the procedures put in place to: 22b. Prevent contaminants not suitable for the treatment process being accepted	A watching brief will be undertaken on site during excavations. Contaminated materials will be identified visually and chemically. On-going chemical testing of soils will identify any unsuitable materials present. If un-suitable materials are identified they will be segregated and removed from site under the appropriate Duty of Care. The MMP will be updated should unsuitable materials be encountered
Where contamination is suspected or known to be present, state the procedures put in place to: 22c. Prevent cross contamination of materials not in need of treatment, wastes awaiting treatment and treated materials	Where materials exceed, or are suspected of exceeding (pending receipt of verification test data) the site re-use criteria, they will be stockpiled within a contained / bunded area to avoid cross-contamination of compliant materials. Consideration will also be given as to sheeting of stockpiles to mitigate against migration of contaminated dust or run-off onto otherwise uncontaminated areas or off the site prior to suitable off-site disposal
Where contamination is suspected or known to be present, state the procedures put in place to: 22d. Demonstrate that materials that do not require treatment and successfully treated	The materials tracking system shall ensure that only suitable materials with acceptable test data will be incorporated into the works on site. Materials will be tracked from source to stockpiles, tested and subsequently tracked to backfill destination using the Materials Tracking Form (Appendix 4) and the site grid cells as source and destination references (figure - 10811b Rev.0 Trial Pit Survey – Appendix 1).

materials reach their specific destination	
Where contamination is suspected or known to be present, state the procedures put in place to: 22e. Ensure that waste for off-site disposal or treatment is properly characterised and goes to the correct facility	All soils to be excavated as part of the project have been pre-classified on a 1/500m^3 sampling regime as documented in the Project Bradford Waste Classification Report 101114 Rev 2 included in Appendix 2. The samples were subjected to appropriate chemical analysis in accordance with WM3. Further analysis will be undertaken as required throughout the project duration. Wastes shall be consigned to a fully licensed disposal facility.

23. Please attach a copy of the tracking forms / control sheets that are to be used to monitor materials movements. To include transfer of loads on site into stockpiles prior to treatment (if applicable), stockpiled after treatment (if applicable), stockpiled awaiting use (as appropriate) and final placement.	Document reference(s) Appendix 1 - 10811b Rev.0 Trial Pit Survey Appendix 4 – Materials Tracking Form

For Hub Sites within Cluster Projects & where materials need treatment before reuse 24. Please attach a copy of the Environmental Permit covering the treatment process. Alternatively if the treatment is covered by a Mobile Plant Permit and associated Deployment Form, attach a copy of the EA agreement to the Deployment Form.	Permit reference / EA letter reference: N/A

Records

25. Where, and in what form, are records to be kept? Note – records e.g. transfer notes, delivery tickets, Desk Top Study, Site Investigation, Risk Assessment(s), Verification Report(s) need to be kept for at least 2 years after the completion of the works and production of the Verification Report	Record will be kept in an electronic format Records associated with this development – specific to the CoP – will be kept by Employer at their regional office at Unit 9, Kingsdale Business Centre, Regina Road, Chelmsford, Essex, CM1 1PE. This will be for 12 years upon the completion of the Verification Report and in line with contractual obligations.

Verification Plan

26. Provide or explain the Verification Plan which sets out how you will record the placement of materials and prove that excavated materials have been reused in the correct location and in the correct quantities within the development works (see 3.4 of the DoW CoP).	Document Reference – Appendix 2 (101101 remediation design statement). A completion (verification) report shall be prepared at the end of the earthworks phase giving details of the remediation works once all of the works have been completed. The completion report will include a clear statement regarding the adequacy of works conducted, whether any amendments were required, what these may have been, and how they were consequently implemented. The report will also detail the nature and likely extent of residual contamination at the site. The basic report will include as a minimum: Scope of works undertaken. Records of any additional remedial works. Comprehensive account of additional work and adequacy of implementation. Locations and analysis of soil samples remaining on site. Conclusions and verification that site is “suitable for use”.


	This report will be issued to the Regulatory Authorities following completion of remedial works at the site.

APPENDIX N Borehole Decommissioning Logs

Borehole Decommissioning Register


Project: Co-op Live
Ref: 101114

Borehole	Actual (m) Depth		m3	Comment
	Borehole 1	Borehole 2	Borehole Volume	
BH19/02A	49.5	17.55	Not found on arrival to site	Not found on arrival to site
BH19/03	29.71	N/A	Not found on arrival to site	Not found on arrival to site
BH19/05	20.85 50	Only 1 pipe	0.041	Decommissioned 31.03.21
BH19/07C	23.1			Decommissioned
Diameter	35mm	Only 1 pipe	0.031	30.03.21
BH19/09	42.6	14.1		Decommissioned
Diameter	35mm	35mm	0.074	29.03.21
BH19/11	24.7	14.5		Decommissioned
Diameter	35mm	50mm	0.06	31.03.21
BH19/13	8.75	26.2		Decommissioned
Diameter	35mm	35mm	0.043	29.03.21
BH19/15	41.8	12.5		Decommissioned
Diameter	35mm	50mm	0.078	07.04.21
BH19/17	15.1	25.1		Decommissioned
Diameter	35mm	35mm	0.013	07.04.21
BH19/14	28.3			Decommissioned
Diameter	35mm	Only 1 pipe	0.044	07.04.21
Total			**0.384**	

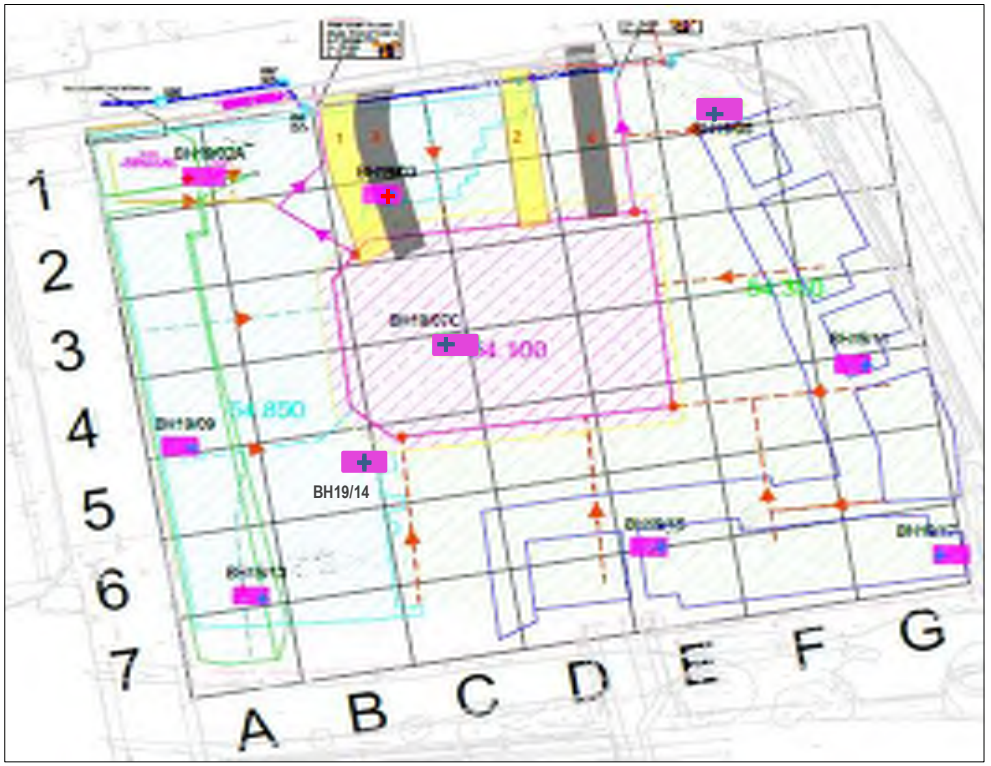

PROVECTUS	Client	BAM Construction	Well Log	
	Project	101114 Co-op Live	Well No.	BH19.05
	Address	Sports City Way, Manchester	Page	1 of 1


Decom Date	31.03.21	Well 1 Depth	20.85	Well 2 Depth	
Logged by	TH	Well 1 Diameter	50mm	Well 2 Diameter	

Depth (m)	Backfill Detail	Remarks
0		*Monitoring wells backfilled using Bentonite pellets to base of borehole in 0.20m sections up to ground level. Boreholes will be cut off following the sealing of the clay pellets, during the impending earthwork excavation works.*
1		
2		
3		
4		
5		
6		
7		
8		
9		
10		
11		**Photos**
12		 
13		
14		
15		
16		
17		
18		
19		
20		
21		
22		
23		
24		
25		
26		
27		
28		
29		
30		

PROVECTUS	Client	BAM Construction	Well Log	
	Project	101114 Co-op Live	Well No.	BH19.07C
	Address	Sports City Way, Manchester	Page	1 of 1

Decom Date	30.03.21	Well 1 Depth	23.1m	Well 2 Depth	
Logged by	TH	Well 1 Diameter	35mm	Well 2 Diameter	

Depth (m)	Backfill Detail
0	
1	
2	
3	
4	
5	
6	
7	
8	
9	
10	
11	
12	
13	
14	
15	
16	
17	
18	
19	
20	
21	
22	
23	
24	
25	
26	
27	
28	
29	
30	



Remarks

Monitoring wells backfilled using Bentonite pellets to base of borehole in 0.20m sections up to ground level. Boreholes will be cut off following the sealing of the clay pellets, during the impending earthwork excavation works.

Photos



PROVECTUS	Client	BAM Construction	Well Log
	Project	101114 Co-op Live	Well No. BH19.09
	Address	Sports City Way, Manchester	Page 1 of 1

Decom Date	29.03.21	Well 1 Depth	14.1	Well 2 Depth	42.6
Logged by	TH	Well 1 Depth	35mm	Well 2 Diameter	35mm

Depth (m)	Backfill Detail
0	
1	
2	
3	
4	
5	
6	
7	
8	
9	
10	
11	
12	
13	
14	
15	
16	
17	
18	
19	
20	
21	
22	
23	
24	
25	
26	
27	
28	
29	
30	
31	
32	
33	
34	
35	
36	
37	
38	
39	
40	
41	
42	
43	

Monitoring wells backfilled using Bentonite pellets to base of borehole in 0.20m sections up to ground level. Boreholes to be cut further to formation, as earthwrks progress.


Photos





PROVECTUS	Client	BAM Construction	Well Log	
	Project	101114 Co-op Live	Well No.	BH19.11
	Address	Sports City Way, Manchester	Page	1 of 1


Decom Date	31.03.21	Well 1 Depth	24.7	Well 2 Depth	14.5m
Logged by	TH	Well 1 Depth	35mm	Well 2 Diameter	50mm

Depth (m)	Backfill Detail
0	
1	
2	
3	
4	
5	
6	
7	
8	
9	
10	
11	
12	
13	
14	
15	
16	
17	
18	
19	
20	
21	
22	
23	
24	
25	
26	
27	
28	
29	
30	

Monitoring wells backfilled using Bentonite pellets to base of borehole in 0.20m sections up to ground level. Boreholes will be cut off following the sealing of the clay pellets, during the impending earthwork excavation works.


Photos



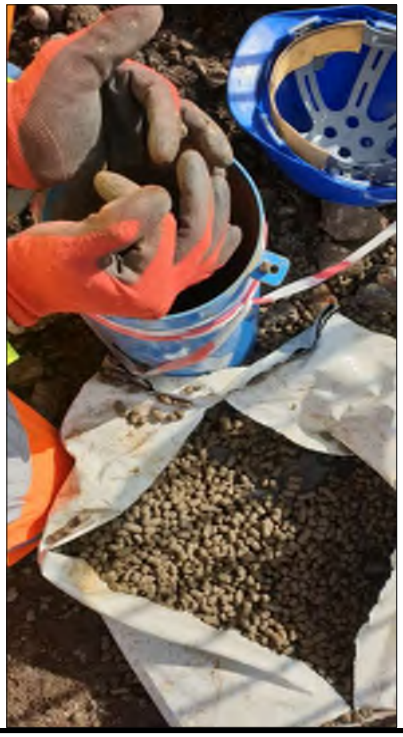

PROVECTUS	Client	BAM Construction	Well Log	
	Project	101114 Co-op Live	Well No.	BH19.13
	Address	Sports City Way, Manchester	Page	1 of 1

Decom Date	29.03.21	Well 1 Depth	8.75	Well 2 Depth	26.2
Logged by	TH	Well 1 Depth	35mm	Well 2 Diameter	35mm

Depth (m)	Backfill Detail
0	
1	
2	
3	
4	
5	
6	
7	
8	
9	
10	
11	
12	
13	
14	
15	
16	
17	
18	
19	
20	
21	
22	
23	
24	
25	
26	
27	
28	
29	
30	

Monitoring wells backfilled using Bentonite pellets to base of borehole in 0.20m sections up to ground level. Boreholes will be cut off following the sealing of the clay pellets, during the impending earthwork excavation works.

Photos






PROVECTUS	Client	BAM Construction	Well Log	
	Project	101114 Co-op Live	Well No.	BH19.14
	Address	Sports City Way, Manchester	Page	1 of 1

Decom Date	07.04.21	Well 1 Depth	28.3	Well 2 Depth	
Logged by	TH	Well 1 Diameter	35mm	Well 2 Diameter	

Depth (m)	Backfill Detail
0	
1	
2	
3	
4	
5	
6	
7	
8	
9	
10	
11	
12	
13	
14	
15	
16	
17	
18	
19	
20	
21	
22	
23	
24	
25	
26	
27	
28	
29	
30	



Remarks

Monitoring wells backfilled using Bentonite pellets to base of borehole in 0.20m sections up to ground level. Boreholes will be cut off following the sealing of the clay pellets, during the impending earthwork excavation works.


Photos



PROVECTUS	Client	BAM Construction	Well Log
	Project	101114 Co-op Live	Well No. BH19.15
	Address	Sports City Way, Manchester	Page 1 of 1

Decom Date	07.04.21	Well 1 Depth	41.8	Well 2 Depth	12.5
Logged by	TH	Well 1 Depth	35mm	Well 2 Diameter	50mm

Depth (m)	Backfill Detail
0	
1	
2	
3	
4	
5	
6	
7	
8	
9	
10	
11	
12	
13	
14	
15	
16	
17	
18	
19	
20	
21	
22	
23	
24	
25	
26	
27	
28	
29	
30	
31	
32	
33	
34	
35	
36	
37	
38	
39	
40	
41	
42	



Monitoring wells backfilled using Bentonite pellets to base of borehole in 0.20m sections up to ground level. Boreholes will be cut off following the sealing of the clay pellets, during the impending earthwork excavation works.


Photos





PROVECTUS	Client	BAM Construction	Well Log	
	Project	101114 Co-op Live	Well No.	BH19.17
	Address	Sports City Way, Manchester	Page	1 of 1

Decom Date	07.04.21	Well 1 Depth	15.1	Well 2 Depth	25.1
Logged by	TH	Well 1 Depth	35mm	Well 2 Diameter	35mm

Depth (m)	Backfill Detail
0	
1	
2	
3	
4	
5	
6	
7	
8	
9	
10	
11	
12	
13	
14	
15	
16	
17	
18	
19	
20	
21	
22	
23	
24	
25	
26	
27	
28	
29	
30	

Diameter measured to be 35mm and not 19mm as initially estimated. Monitoring wells backfilled using Bentonite pellets to base of borehole in 0.20m sections up to ground level.

Photos



APPENDIX O Temporary Works Designs











ENGINEERING CONSULTANTS

Client: Provectus

Project Number: 21228-01

Project Title: Project Bradford

Section of Work: Stockpile & Excavation

Design Risk Category: Cat 1

Reviewed by: .....

Joshua Martin

BEng(Hons) IEng MICE

05.03.21

Email: office@andun.co.uk

Registration No: 11928533

Telephone: 01245 360194

Website: www.andun.co.uk

Head Office: Monarch House, Unit 6 Drakes Lane Industrial Estate, Boreham, Chelmsford, Essex, CM3 3BE

Midlands Office: 8 Kings Street, Newcastle-Under-Lyme, ST5 1EL

Scottish Office: 7 Queens Gardens, Aberdeen, AB15 4YD

ENGINEERING CONSULTANTS

Document Revision History

REVISION	DESCRIPTION	AUTHOR	REVISION DATE	CHECKED BY
R0	Initial Issue	Richard Boyle	05.03.21	Joshua Martin

ENGINEERING CONSULTANTS

Table of Contents

Design & Check Certificate

Design Philosophy

Designers Risk Assessment

Supporting Information

ENGINEERING CONSULTANTS

Design & Check Certificate

ENGINEERING CONSULTANTS


Temporary Works Design and Check Certificate

Project: Project Bradford

Client: Provectus

Design Brief Issued:	Yes
Design Brief Reference:	Email
Does the Design Comply with the Brief?	Yes

If no, how does it differ from the design brief?

Name	Richard Boyle
Title	Temporary Works Engineer
Signature	
Date	05.03.21
To be signed by the Temporary Works Designer or other person authorised* to sign on behalf of the organisation responsible for the Design of the Temporary Works.	

*See company intranet for authority
https://sites.google.com/andun.co.uk/aecltd/home/hr-section/design-authority?authuser=0

Drawings Produced

21128-01-PRO-BRA-EXC-DRW-01

Loading Constraints
The constraints on the use of the proposed temporary works are best explained by referring to the drawings.
Please see scheme drawings.

Proposed Category of Check

Cat 1

Current Design Standards used (strike through those that do not apply)

BS5975:2019 Code of practice for temporary works procedures and the permissible stress design of falsework
~~BS 449-2:1969 The use of structural steel in building (referenced through BS5975)~~
~~BS6187:2011 Code or practice for full and partial demolition~~
~~BS5268-2 Structural Use of Timber~~
~~BS 5950-1:2000 Structural Steelwork in building. Rolled and welded sections~~
~~BS8110-1:1997 Structural Use of Concrete~~
~~BS6399-1: 1996 Loadings for buildings (dead & Imposed)~~
~~BS6399-2:1997 Code of practice for wind loads~~
~~EN1990: (Eurocode 0) Basis of structural design~~
~~EN1991: (Eurocode 1) Actions on structures~~
~~EN1992: (Eurocode 2) Design of concrete structures~~
~~EN1993: (Eurocode 3) Design of steel structures~~
~~EN1994: (Eurocode 4) Design of composite steel and concrete structures~~
~~EN1995: (Eurocode 5) Design of timber structures~~
~~EN1996: (Eurocode 6) Design of masonry structures~~
~~EN1997: (Eurocode 7) Geotechnical design~~

Historical Design Standards used (strike through those that do not apply)

~~CP110:1972~~
~~CP114:1948~~
~~BS 449-2:1969 The use of structural steel in building~~
~~BS648: 1964 Weights of building materials~~

Other literature referred to (strike through those that do not apply)

Structural Engineer's Pocket Book
~~Steel Designers Manual~~
~~Blue book (Guide to BS5950 & BS449)~~
~~Reynolds Reinforced Concrete Designers Handbook~~
~~Structural Precast Concrete (C.W. Glover 1964)~~
~~Structural Engineering Formulas (Mikhelson)~~
~~Roark's Formulas for Stress & Strain~~
~~Kempe's Engineering Year Books~~
~~Dorman Long, R.A. Skelton etc. Historical steel/iron work details~~
~~Concrete Society Note 70 on historical concrete structures~~
~~White book (British Gypsum)~~
~~Railway Engineering (Chandra/Agrawal)~~
~~Soil mechanics (Smith/Barnes/Tomlinson)~~
~~SI supplied by Site team~~
~~The Piling Handbook~~

Design Check

Checking Organisation: Andun Engineering Consultants Ltd

If other, please specify:

Design Check Undertaken: Cat 1

Does the design comply with the brief? Yes

If no, how does it differ from the design brief?


I certify that reasonable professional skill and care have been used in checking the Design of the Temporary Works identified in this certificate, with the objective of ensuring that:

1. The Design is safe;

2. The standards and codes stated are appropriate;

3. Any departures from the standards and codes are appropriate in the circumstances;

4. The Design is in accordance with the standards and codes (including any departures) stated.

Name	Joshua Martin
Title	Midlands Office Manager / Senior Engineer
Signature	
Date	05.03.21

To be signed by the Temporary Works Checker or other person authorised* to sign on behalf of the organisation responsible for the Checking of the Temporary Works.

*See company intranet for authority
https://sites.google.com/andun.co.uk/aecltd/home/hr-section/design-authority?authuser=0

ENGINEERING CONSULTANTS

Design Philosophy

ENGINEERING CONSULTANTS

Design Philosophy

Project Title:	Project Bradford
Section of Work:	Stockpile & Excavation
Calculation Reference:	21228-01-PRO-BRA-EXC-CAL-01
Client:	Provectus
Design By:	Richard Boyle
Date:	05.03.21

Documents and Drawings Utilised:

- 10811b Project Bradford Trial Pit Survey Rev0 10022020.dwg
- 10811b Project Bradford Trial Pit Survey Rev0 10022020.pdf
- 11070a Project Bradford Piling Mat Volumes Rev0 16072020.bak
- 11070a Project Bradford Piling Mat Volumes Rev0 16072020.dwg
- 11070a Project Bradford Piling Mat Volumes Rev0 16072020.pdf
- 101114 Project Bradford Waste Classification Report Rev 2.pdf
- BHE GE Interpretive Report Rev.P04 02.03.20.pdf
- CONTIG WALL- PILE MAT VOLUMES.REV 1.pdf
- MAIN AREA-PILE MAT VOLUMES.REV 1.pdf
- Project Bradford Tril Pit Survey 10022020 AJC edit 20.02.2020.xlsx
- RAMS004 Bulk Excavation Rev 0.docx
- WIP Time Slices 17-07-20 - North.pdf
- TW001 - Stockpile Design Brief Rev01.docx
- TW002 - Bulk Excavation Design Brief - 01.docx

Brief:

Produce a suitable stockpile & Excavation design in preparation for the Piling works to occur at Project Bradford.

Design Philosophy:

Methodology:

Use provided Geotechnical information to determine the safe slope angles for the stockpile at Project Bradford, in addition to this checking if the proposed plant is suitable for access to the stockpile. The stockpile is to be up to 2,000m3 and ideally a slope of between 25deg and 60 deg is desired.

To allow for varying stockpile materials, an allowable slope will be determined for each soil type based on typical angles of repose and previous site experience for the soil on this site.

The slope will be analysed in LimitState Geo. The parameters will be taken as follows:

- Ground parameters:

  Silty Made ground: Internal angle of shearing resistance: 30deg & unit weight: 18kN/m^3

  Cohesive Fill: Undrained Shear strength: 25kN/m^2: Unit weight:17kN/m^3

  Engineered Made Ground: Internal angle of shearing resistance: 36deg & unit weight: 18kN/m^3

Stockpile + excavation height must not exceed 6m, a 12m offset from the foot of the stockpile must be in place when the excavation + stockpile height is greater than 6m. The excavation will start in the north west corner of the site and progress one grid at a time across the site, the border excavation will be covered by the BAM temporary works designs.

Loads:

The loads used for the assessment will be from

- Excavator 50 t range
- A30 Dumper truck
- CAT D6T Dozer

Load Path:

The load applied from the plant will transfer through the existing ground

Stability:

The stability of the stockpile will depend on the angle of repose of the materials.

To check the stability of the ramp, a LimitState Geo model will be created and the gradient of the batter will be determined.

Design Life:

Less than two years

Assumptions:

Information provided is accurate

The ground taken for design is representative of what is found on site.

Exclusions:

Justification of long term stockpile for over 10 years.
Justification of excavations inside stockpile exclusion zones / long term excavations.

Standards Utilised:

BS5975:2019 - Code of Practice for Temporary Works.

Design Check Level:

We recommend that this design warrants a Cat 1

ENGINEERING CONSULTANTS

Designers Risk Assessment

ENGINEERING CONSULTANTS

Designers Risk Assessment

Designer: Richard Boyle	**Project: Project Bradford**
Job No: 21228-01-PRO-BRA-EXC-DRA-01	**Date: 05.03.21**

Activity Element/Potential Hazards	Infrastructure/ People at Risk	Risk Rating			Action at Design Stage/Residual Risk & Possible Control Options (Contractors)
		L	S	R	
Plant operations / Ramp maintenance	Infrastructure / Site team	L	M	M	Plant selected to suit ground conditions on site. Existing material may rut with heavy repeated use. Surface to be re-dressed and maintained regularly. The stockpile has not been designed to support plant. If plant is required to operate on top of the stockpile it should be constructed with a minimum slope gradient of 1 in 2 with plant operating at least 1m from edges with earth bund provided at edges. Areas where plant are operating frequently should be constructed in accordance with specification for highway works.
Ground Conditions	Infrastructure / Site team	M	M	M	Please ensure ground used for design is found on site. If it varies, please contact the designer.
Stockpile overload	Infrastructure / SIte team	M	M	M	Designed for a maximum stockpile height of 6m. If the contractor wishes to exceed, please contact the designer. Stockpile designed for no plant operations. If plant is expected to operate above the stockpiles, please refer to ramp restrictions.
Ground water	Infrastructure / SIte team	M	M	M	There is no groundwater interference expected. If groundwater was encountered, please contact the designer.

Excavations near stockpile destabilising stockpile	Infrastructure/ Site team	M	M	M	Provide exclusion zone. Stockpile + excavation height must not exceed 6m, a 12m offset from the foot of the stockpile must be in place when the excavation + stockpile height is greater than 6m.
Stockpile height	Infrastructure/ site team	L	H	M	The contractor must contact the designer if they wish to exceed a stockpile height of 6m. BAM excavations layout not shown in the drawing.
Long term use of stockpile	Infrastructure/ site team	L	L	L	Highlight design life on drawing. Provide inspection recommendations.

Normal Hazards:

Are hazards inherent in site work such as injury from falling, tripping, lifting materials, working at height, contact with substances hazardous to health etc. Any competent contractor will address these without a specific designers risk assessment. This is inline with HSE guidance which is to focus on the unusual hazards not obvious to a competent contractor.

Infrastructure/People at Risk Key:

ST = Site Team
NR = Network Rail
PU = Public
FI = Financial Risk
AO = Asset Owner

Risk Rating Key:

Likelihood (Low, Medium, High)
Severity (Low, Medium, High)
Risk (Likelihood x Severity)

Risk (R) Rating Matrix		Severity (S)		
		Low	Medium	High
Likelihood (L)	Low	Low	Med	Med
	Medium	Med	Med	High
	High	Med	High	High

Andun Engineering Consultants Ltd

Project Title: **Project Bradford**

Section of Work: **Stockpile & Excavation**

Calculation Reference: **21228-01-PRO-BRA-EXC-CAL-01**

Client: **Provectus**

Design By: **RPB**

Date: **05-03-21**

Documents and drawings utilised:

- 10811b Project Bradford Trial Pit Survey Rev0 10022020.dwg
- 10811b Project Bradford Trial Pit Survey Rev0 10022020.pdf
- 11070a Project Bradford Piling Mat Volumes Rev0 16072020.bak
- 11070a Project Bradford Piling Mat Volumes Rev0 16072020.dwg
- 11070a Project Bradford Piling Mat Volumes Rev0 16072020.pdf
- 101114 Project Bradford Waste Classification Report Rev 2.pdf
- BHE GE Interpretive Report Rev.P04 02.03.20.pdf
- CONTIG WALL- PILE MAT VOLUMES.REV 1.pdf
- MAIN AREA-PILE MAT VOLUMES.REV 1.pdf
- Project Bradford Tril Pit Survey 10022020 AJC edit 20.02.2020.xlsx
- RAMS004 Bulk Excavation Rev 0.docx
- WIP Time Slices 17-07-20 - North.pdf
- TW001 - Stockpile Design Brief Rev01.docx
- TW002 - Bulk Excavation Design Brief - 01.docx

www.Andun.co.uk Info@Andun.co.uk

Head Office:
Monarch House
Unit 6 Drakes Lane Industrial Estate,
Drakes Lane
Boreham
Essex
CM3 3BE
01245 360 194

Midland Office:
8 Kings Street
Newcastle Under Lyme
Staffordshire
ST5 1EL
01782 712227

Scottish Office:
7 Queens Gardens
Aberdeen
AB15 4YD

Andun Engineering Consultants Ltd

Brief:
Provide a safe an accessible access ramp from on site materials to create a 2,000M3 stockpile at Project Bradford with a height less than 6m.

Assumptions:
The ground conditions provided are accurate and representative of the soil on site
There in no expected groundwater interference

www.Andun.co.uk Info@Andun.co.uk

Head Office:
Monarch House
Unit 6 Drakes Lane Industrial Estate,
Drakes Lane
Boreham
Essex
CM3 3BE
01245 360 194

Midland Office:
8 Kings Street
Newcastle Under Lyme
Staffordshire
ST5 1EL
01782 712227

Scottish Office:
7 Queens Gardens
Aberdeen
AB15 4YD

1.0 Plant

The plant that will be accessing the ramp will be

- Excavator 30, 50 t range
- A30 Dumper truck
- CAT D6T Dozer

By inspection, the worse load case will come from the A30t Articulated dumper as the bearing pressures will be the heighest as it is on wheels.

2.0 Stockpile Design Short Term

Referencing the temporary works brief the stockpile will consist of soily, made ground with brick and aggregate or solely stone/concrete material for processing.

To allow for vaying stocklpile materials an allowable slope will be determined for each soil type based on typical angles of repose and previous site experience for the soil on site.

2.1. Allowable slope

Following review of typical angles of repose in the short term the following slope angles for each soil type has been determined.

Silty granular Made ground	$\alpha_1 := \operatorname{atan}\left(\frac{1}{1.5}\right) = 33.69 \cdot \text{deg}$	1 in 1.5
Granular Fill (Sand and gravels)	$\alpha_2 := \operatorname{atan}\left(\frac{1}{1.5}\right) = 33.69 \cdot \text{deg}$	1 in 1.5
Cohesive Fill	$\alpha_3 := \operatorname{atan}\left(\frac{1}{1}\right) = 45 \cdot \text{deg}$	1 in 1

2.2. Stockpile restrictions

To ensure the stability of the stockpile and the surrounding soil we recommend the following restrictions;

- Maximum height of 6m (if a greater height is required then the Engineer should be contacted).
- Plant to stand at least 1.0m from top of batter and gradient must be 1 in 2. (Based on angle of repose no intersecting the toe of the batter)

The stockpile should also adhere to local exclusion zones stipulated by other temporary/permanent works.

3.0 Stockpile Design Long Term

The long term design considers the self weight of the stockpile only, the plant used on site is not to be left on the stockpile long term.
Maximum height of stockpile is 6.0m

Long term ground conditions



Figure 1.1

In this instance we are only checking the stockpile for self weight as this is the long term analysis.
The analysis has been done in Limit state Geo and the ground values are shown below

Silty made ground (subgrade shown in green on figure 1.1)

Internal angle of shearing resistance $\theta_{mg} := 30deg$

Bulk unit weight $\gamma_{mg} := 18 \frac{kN}{m^3}$

Cohesive fill (stockpile material shown in pink figure 1.1)

Bulk unit weight $\gamma_{mg1} := 17 \frac{kN}{m^3}$

Undrained shear strength $C_u := 25 \frac{kN}{m^2}$



Scenario	Partial factors	Adequacy on strength
1	Unity	1.674
2	EC7 DA1/1	1.688
3	EC7 DA1/2	1.217 [more...]

Therefore slope will remain stable

4.0 Ramp Assessment

4.1 Ground conditions

The ground parameters are based on the information provided by the client.

Made ground

Internal angle of shearing resistace $\theta_{mg} := 32deg$

Bulk unit weight $\gamma_{mg} := 18 \frac{kN}{m^3}$

4.2. Loading


From CIRIA SP95 - *A minimum uniform surcharge of 10kN/m^2 should be used for plants up to 30 tonne. This can be increased to 20kN/m^2 for plants up to 60 tonne loaded weight.* Hence;

Maximum weight of Volvo AC30 dumper loaded. $q_V := 52\text{tonne}$


Therefore, take a surcharge load $q_S := 20\,\frac{\text{kN}}{\text{m}^2}$

4.3. Solution

Modelling the existing load case on LimitState Geo, the slope was failing as a minor translational surface slope failure which is not a global failure mechanism. Therefore, to simulate the most credible failure mechanism, on the edge of the slope we placed weightless concrete that would avoid the edge of the slope peeling off and wouldn't affect the credible slope failure.

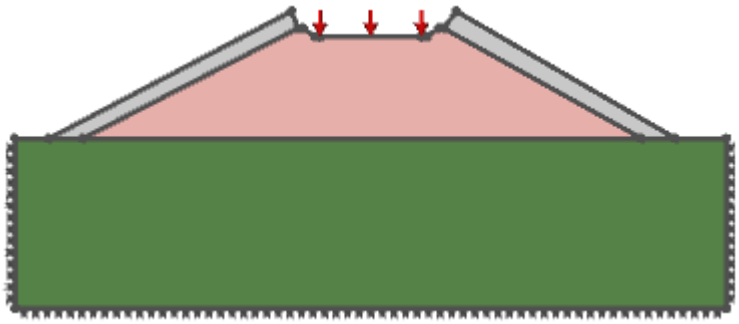

The results achieved from the slope stability Analysis are acceptable. See below failure mechanism.

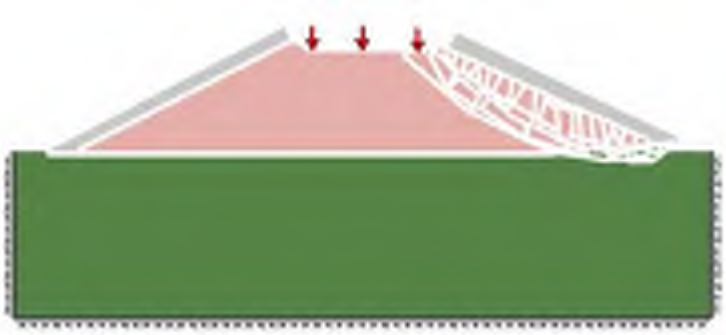


Scenario	Partial factors	Adequacy on strength
1	Unity	1.601
2	EC7 DA1/1	1.595
3	EC7 DA1/2	1.279

Therefore slope is stable

5.0 Summary

Refer to drawing 20247-01-PRO-BRA-EXC-DWG-01 for further details, stockpile does not require 12m run off area when height of stockpile + excavation does not exceed 6m.

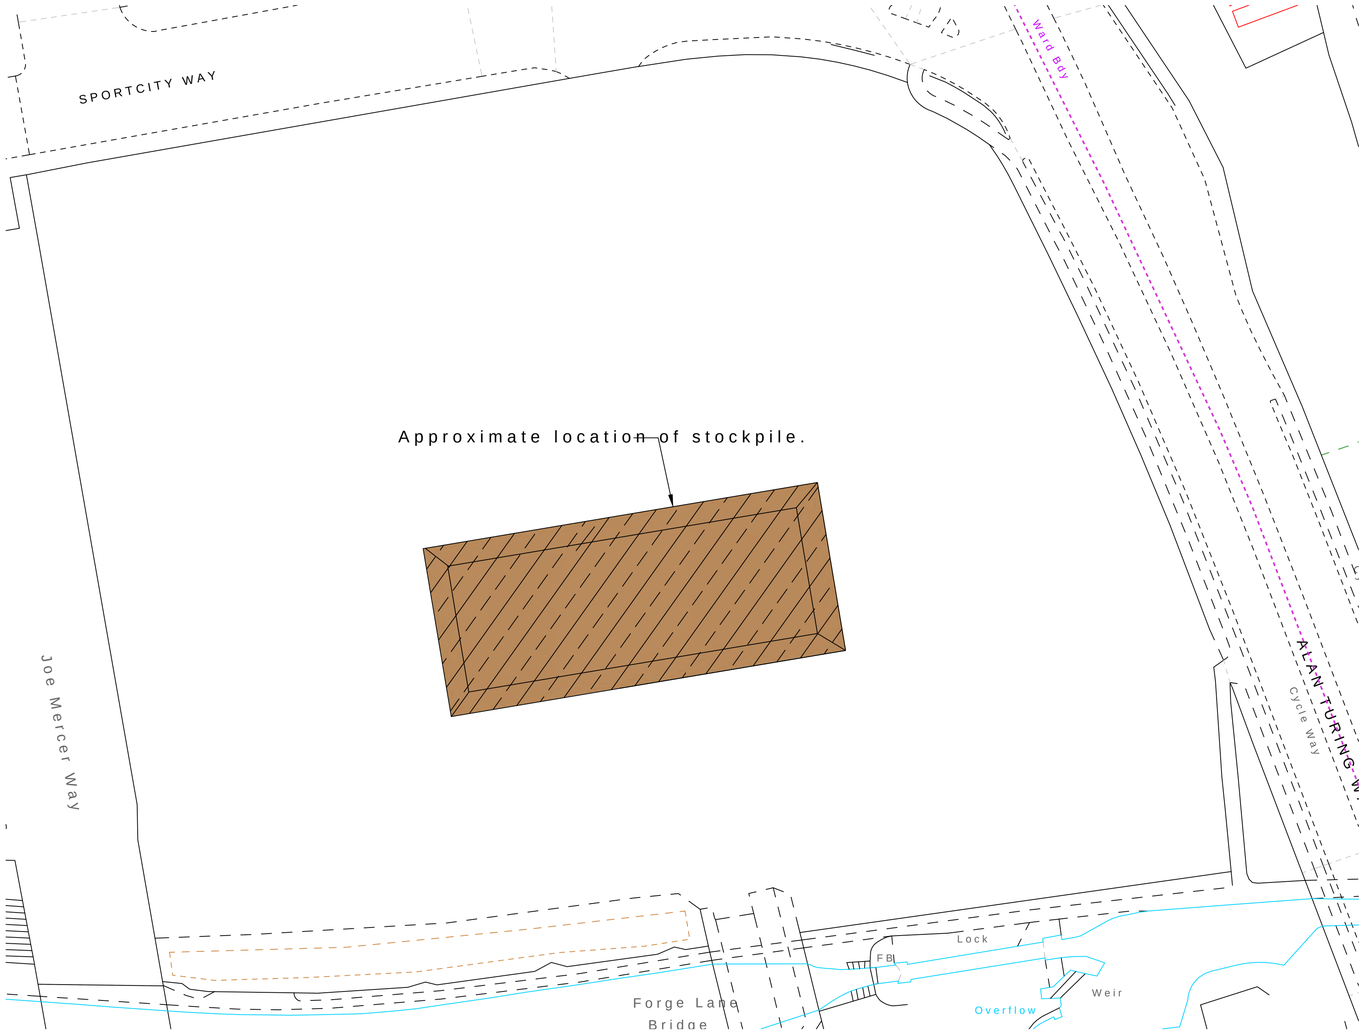

Plan
1:500

The slope should be inspected by a TWS/C at least daily while the stockpile is being constructed and weekly thereafter while operations are still ongoing on site.

The stockpile plan geometry shown is indicative. The contractor may choose a shape that suits the site.

The stockpile is to be constructed from site won material. The maximum volume of the stockpile is 2,000m3.


The plant expected on site to enable construction are;

" Excavator (up to 50te)
" A30 Dumper truck
" CAT D6T Dozer

No ground water interface is expected. If there is high ground water then contract the engineer.


The contractor must contact the designer if he wishes to exceed a stockpile height of 6m. Local site exclusion zones are not shown on this drawing.


If plant is required to operate on top of a stock pile it should be constructed with a minimum slope gradient of 1 in 2 with plant operating at least 1m from edges with an earth bund provided at edges. Areas where plant are operating frequently should be constructed in accordance with Specification for highway works.



Stockpile exclusion zone

Temporary plant loadings on top of the stockpile are pemitted providing that plant remains 1.0m from edges and an earth bund is provided as shown below.



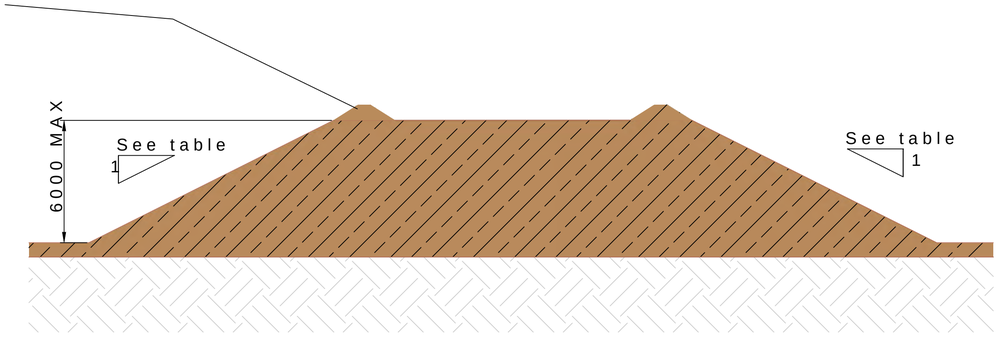

Stockpile elevation
1:100

Stockpile slope restrictions	
Soil type	Slope
Made Ground	1 in 1.5
Granular fill (sand and gravels)	1 in 1.5
Cohesive fill	1 in 1

Note: The soil type used in the stockpile is to the discretion of the contractor.

Rev	Date	Status
C2	5-Mar-21	For Construction
C1	02.03.21	For Approval

FOR CONSTRUCTION

Notes

1. If In Doubt, Ask;
2. Do Not Scale;
3. All Dimensions To Be Confirmed Ons
4. Dimensions In mm Unless Noted Othe
5. This Drawing Is To Be Read In Conju All Other Relevant Drawings;
6. Should There Be Any Conflict Betwee Indicated On This Drawing And Those On Other Drawings, The Engineer Sh Informed Prior To Construction;
7. Until Technical Approval Has Been O The Relevant Authority, It Should Be That All Drawings Issued Are Not For Construction;
8. Should The Contractor Commence Sit To Approval Being Given, It Is Entire Risk;
9. Remaining/Unusual Hazards Identified Thus:
10. Items Of Importance Highlighted Thu
11. Check Components As Supplied Matc Where Substitutions Are Made, The E (AE) MUST Be Informed Prior To Loadin
12. Where We Are Supplied With Drawing Produce Setting Out Points, The Site Check All Coordinates Prior To Cons Cannot Take Responsibility For The A The Supplied Survey/Drawings

Project Title
Project Bradfo

Client
PROVECTUS

ENGINEERING CONSULTANTS

Head Office - Monarch House, Unit 6, Drakes Lane Industrial Estate, Drakes Lane, Northern Office - 8 King Street, Newcastle under Lyme, Staffordshire, ST5 1EL
www.Andun.co.uk Tel: 01245 360 194 Info@Andun.co.uk

Designed By	Date	Checked By	Date
RPB	05.03.21	JM	05.03.21

Filename	Plot Date	Scale
21228-01	05.03.21	As Shown

Drawing Title
Stockpile

Drawing Number	Sheet	Rev
21228-01-PRO-BRA-EXC-DRW-01		C2



Plan
NTS




Rev	Date	Status
C2	5-Mar-21	For Construction
C1	23-Feb-21	For Approval

FOR CONSTRUCTION

Notes

1. If In Doubt, Ask;
2. Do Not Scale;
3. All Dimensions To Be Confirmed Ons
4. Dimensions In mm Unless Noted Othe
5. This Drawing Is To Be Read In Conju All Other Relevant Drawings;
6. Should There Be Any Conflict Betwee Indicated On This Drawing And Those On Other Drawings, The Engineer Sh Informed Prior To Construction;
7. Until Technical Approval Has Been O The Relevant Authority, It Should Be That All Drawings Issued Are Not For Construction;
8. Should The Contractor Commence Sit To Approval Being Given, It Is Entire Risk;
9. Remaining/Unusual Hazards Identified Thus:
10. Items Of Importance Highlighted Thu
11. Check Components As Supplied Matc Where Substitutions Are Made, The E (AEO) MUST Be Informed Prior To Loadin
12. Where We Are Supplied With Drawing Produce Setting Out Points, The Site Check All Coordinates Prior To Cons Cannot Take Responsibility For The A The Supplied Survey/Drawings

The border excavation designs will be covered by the BAM Temporary Works Designs.

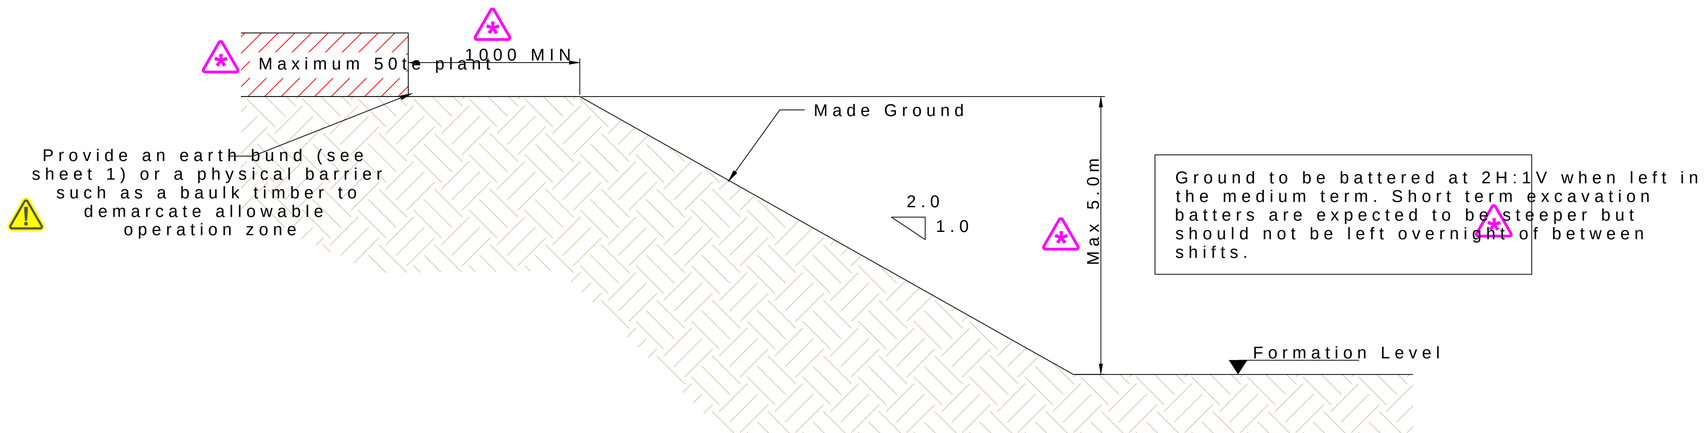

Typical Section of batter
NTS

Project Title
Project Bradfo

Client
PROVECTUS

ENGINEERING CONSULTANTS

Head Office - Monarch House, Unit 6, Drakes Lane Industrial Estate, Drakes Lane, Northern Office - 8 King Street, Newcastle under Lyme, Staffordshire, ST5 1EL
www.Andun.co.uk Tel: 01245 360 194 Info@Andun.co.uk

Designed By	Date	Checked By	Date
RPB	05.03.21	JM	05.03.21

Filename	Plot Date	Scale
21228-01	05.03.21	As Shown

Drawing Title
Excavation

Drawing Number	Sheet
21228-01-PRO-BRA-EXC-DR-CW-0001	C2

ENGINEERING CONSULTANTS

Supporting Information

FORMATION:54.630m

FORMATION:53.880m

FORMATION:54.130m

Design Used: Basement methodo
Survey Used: 19D065 A_GREY
Survey Generated From 2D Infor
All Batters 1in1.5

PRISM VOLUMES : PROJECTION TO SURVEY FROM			
Group	Volumes		
	Cut/Material	Fill/Void	Balance
PILE MAT 3	22116	0	22116
PILE MAT 1	43535	0	43535
PILE MAT 2	24650	0	24650
Total	90301	0	90301

TRIANGLE AREAS		
Group	Plan Area	Slope Area
PILE MAT 3	4425	4458
PILE MAT 1	9814	10323
PILE MAT 2	6894	7128
Total	21133	21908

stafsurv LAND SURVEYORS

www.stafsurv.com

Vernon Courtyard, Main Road, Sudbury, Der
T 01283 5848 M 0001284 5846 E44info@stafsurv.

NOTES

CLIENT

PROVECTUS

SITE

Project Bradfo
101114

PROJECT

Cut & Fill Contour
(Basement methodo

SCALE

1:500 @ A1

DATE

16/07/202

DRAWING No.

11070b Rev

5 Geotechnical Parameters

5.1 Ground Model

Table 5—1 provides the design stratigraphic sequence for the different zones of the Site, based on the zones shown in Figure 5—1.

Table 5—1: Design ground model for different zones

Strata	Zone 1 Level Top		Zone 2 Level Top		Zone 3 Level Top		Zone 4 Level Top		Zone 5 Level Top	
	mbgl	mOD	mbgl	mOD	mbgl	mOD	mbgl	mOD	mbgl	mOD
Made Ground / Fill	GL	57.7	GL	59.0	GL	59.5	GL	60.2	GL	60.0
Alluvium	10.8*	46.9*	-	-	9.0	50.5	7.4	52.8	-	-
River Terrace Deposits			-	-	10.5	49.0	-	-	-	-
Glacial Till	12.3	45.4	9.0	50.0	11.0	48.5	8.2	52.0	4.0	56.0
Coal Measures	17.7	40.0	12.5	46.5	13.5	46.0	13.0	47.2	13.0	47.0

*predominantly Alluvium. River Terrace Deposit is not always present in Zone 1. Where present, the thickness of River Terrace Deposit is thin, approx 0.6m.


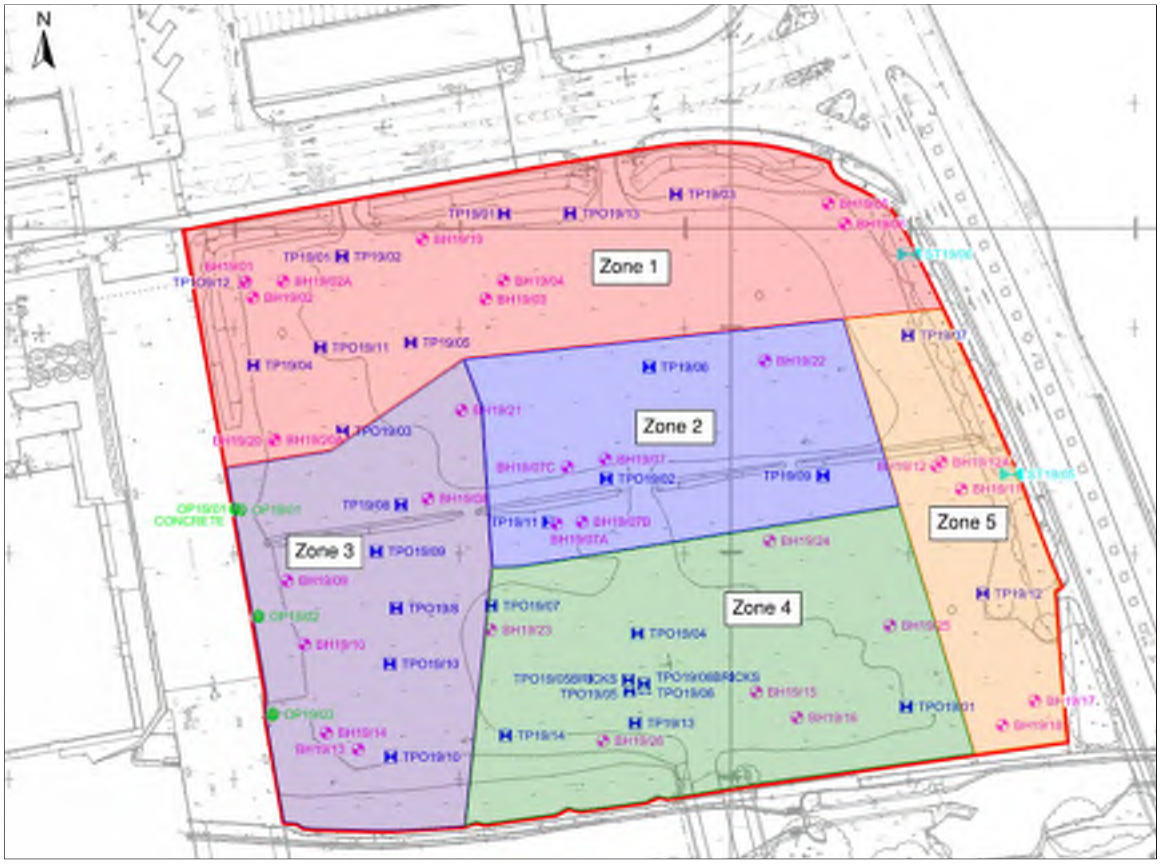


Figure 5—1: Site zone plan

Copyright © 1976 - 2020 BuroHappold Engineering. All Rights Reserved.

ENGINEERING CONSULTANTS

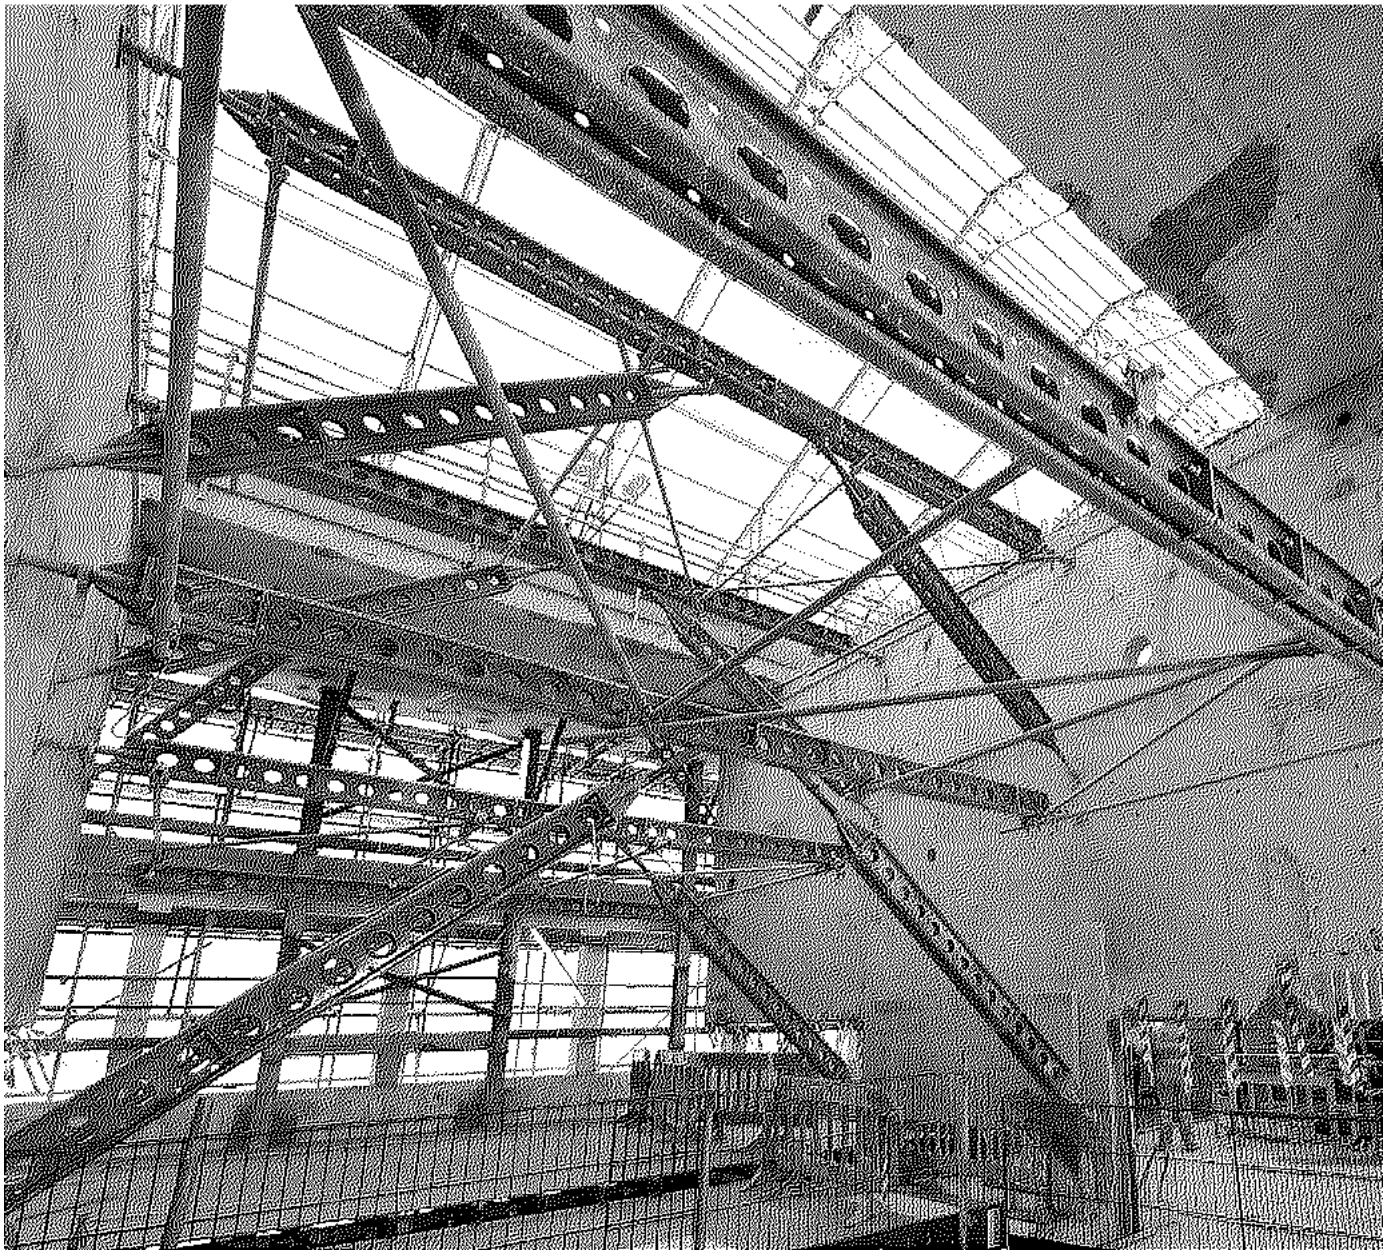

Email: office@andun.co.uk
Registration No: 11928533
Telephone: 01245 360194
Website: www.andun.co.uk
Head Office: Monarch House, Unit 6 Drakes Lane Industrial Estate, Boreham, Chelmsford, Essex, CM3 3BE
Midlands Office: 8 Kings Street, Newcastle-Under-Lyme, ST5 1EL
Scottish Office: 7 Queens Gardens, Aberdeen, AB15 4YD

Appendix P Photographs

Photo 1 – Site on Mobilisation



Photo 2 – Preliminary Excavations



Photo 3 Muckaway of Waste Material Commences



Photo 4 - Placement of Low Level Pile Mat



Photo 5 – Decommissioning of Boreholes

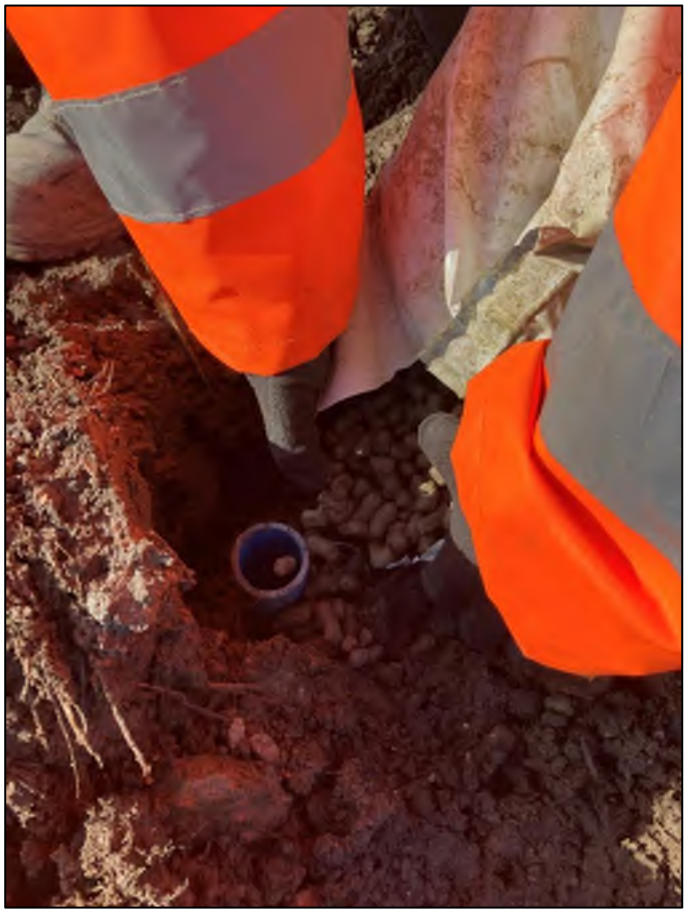


Photo 6 Placement of Upper Level Pile Mat



Photo 7 Stockpile Segregation and Dust Suppression



Photo 8 Flowmeter Reading for Groundwater Treatment System



Photo 9 - Trimming of Pile Mat Levels



Photo 10 – Tarmac Bowl Area



Photo 11 Dust Suppression and Stockpiling



Photo 12 Low Level Mat Earthworks



Photo 13 High Level and Low Level Pile Mat



Photo 14 – Surface Water Collection Sump



Photo 15 – Low Level Mat Earthworks and Screening



Photo 16 Stockpile of Concrete and Bricks



Photo 17 Installation of Temporary Surface Water Drainage



Photo 18 Groundwater Treatment System



Photo 19 Reuse of approved 6F5 Material



Photo 20 Stockpile Signing



Photo 21 – Excavation along Site Boundary



Photo 22 – Excavation to Formation



Photo 27 – Flow Meter on Demobilisation of Water Treatment System



Photo 28 – Installation of Temporary Surface Water Drainage



Photo 29 – Visible Chrysotile Fragments Observed in Cell G1



Photo 30 – Pile Mat in Southeast Corner of Site



Photo 31 – Pile Mat and Excavation in Southeast Corner of Site



Photo 32 – Stockpiling and Muckaway Point



Photo 33 – Final Pile Mat Area on South of Site



Appendix Q - Imported Stone Grading Certificates

MURRAY RIX
CONSULTANCY, SITE INVESTIGATION
CONSTRUCTION MATERIALS TESTING

TEST REPORT

Client W Maher & Sons Ltd

Address Rixton Old Hall
Manchester Road
Warrington
WA3 6EW

Contract Buckton Vale

Job Number MRN 4119/3
Date of Issue 17 March 2021
Page **1 of 2**

Approved Signatories

S J Hutchings, O P Davies

Notes

1 All remaining samples and remnants from this contract will be disposed 28 days from the date of this report unless you notify us to the contrary.

2 Result certificates, in this report, not bearing a UKAS mark, are not included in our UKAS accreditation schedule.

3 Opinions and interpretations expressed herein are outside the scope of our UKAS accreditation

4 Certified that the samples have been examined and tested in accordance with the terms of the contract/order and unless otherwise stated conform to the standards/specifications quoted. This does not, however, guarantee the balance of the materials from which the tested samples have been taken to be of equal quality.

MURRAY RIX
ANDREW HOUSE, HADFIELD STREET,
DUKINFIELD, CHESHIRE SK16 4QX
TEL 0161 475 0870

UKAS TESTING 1580

TEST CERTIFICATE

PARTICLE SIZE DISTRIBUTION

BS EN 933-1 : 2012 (Washing & Sieving Method)


Determination of water content in accordance with BS EN 1097-5:2008

CLIENT	W Maher & Sons Ltd
SITE	Buckton Vale
JOB NUMBER	MRN 4119/3

SAMPLE LABEL	6F5	DATE SAMPLED	Not advised
LAB SAMPLE No	96876	DATE RECEIVED	09-Mar-21
DATE TESTED	12-Mar-21	SAMPLED BY	Client

MATERIAL	Gritstone 6F5
ADVISED SOURCE	As client and site above

Sieve Size (mm)	% Passing (%)	Specification (%)	Sieve Size (mm)	% Passing (%)	Specification (%)
125	100	100	6.3	12	
90	94		5	12	
80	78	75-99	4	11	
75	75		2	11	0-35
63	69		1.18	10	
50	63		1	10	
40	57	50-90	0.6	8	
31.5	48		0.5	8	
28	44		0.425	8	
20	30	30-75	0.3	7	
16	24		0.25	6	
14	20		0.15	5	
10	15	15-60	0.125	5	
8	13		0.063	4.1	0-12

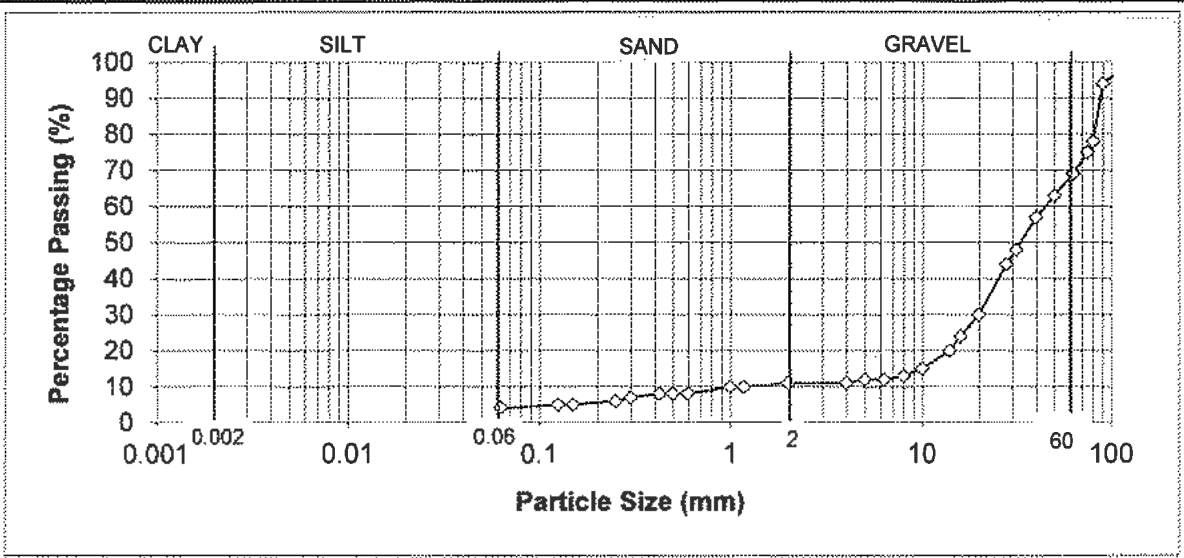

REMARKS
Sample complies with the advised grading specification 6F5 (SHW 2016)
As received moisture content = 4.1%

SIGNED

NAME O.P. Davies BA (Hons) (Laboratory Manager) DATE 17-Mar-21

MURRAY RIX

ANDREW HOUSE, HADFIELD STREET,
DUKINFIELD, CHESHIRE SK16 4QX
TEL 0161 475 0870

UKAS TESTING 1580

TEST CERTIFICATE

PARTICLE SIZE DISTRIBUTION

BS EN 933-1 : 2012 (Washing & Sieving Method)


Determination of water content in accordance with BS EN 1097-5:2008

CLIENT	W Mahers & Sons Ltd
SITE	Buckton Vale
JOB NUMBER	MRN 3818/26

SAMPLE LABEL	6F5	DATE SAMPLED	20-Nov-20
LAB SAMPLE No	93669	DATE RECEIVED	20-Nov-20
DATE TESTED	23-Nov-20	SAMPLED BY	Client

MATERIAL	Gritstone 6F5
ADVISED SOURCE	As client and site above

Sieve Size (mm)	% Passing (%)	Specification (%)	Sieve Size (mm)	% Passing (%)	Specification (%)
125	100	100	6.3	30	
90	100		5	29	
80	98	75-99	4	28	
75	96		2	24	0-35
63	92		1.18	21	
50	82		1	20	
40	79	50-90	0.6	15	
31.5	69		0.5	14	
28	63		0.425	12	
20	45	30-75	0.3	10	
16	39		0.25	9	
14	37		0.15	7	
10	34	15-60	0.125	6	
8	32		0.063	4.5	0-12

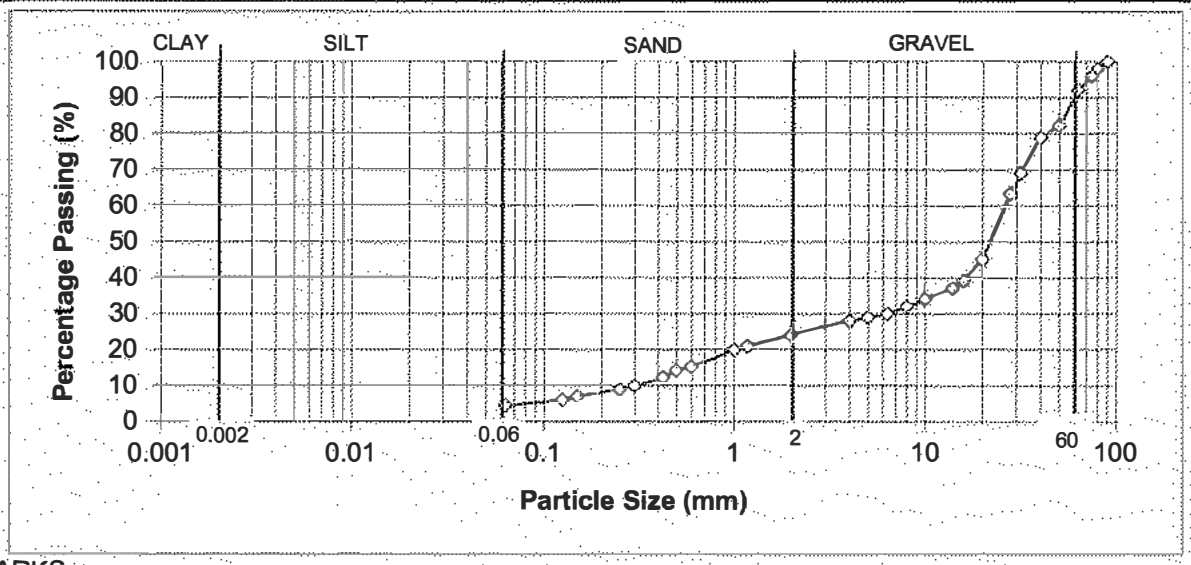

REMARKS

Sample complies with the advised grading specification 6F5 (SHW 2016)

As received moisture content = 5.3%

SIGNED

NAME O.P. Davies BA (Hons) (Laboratory Manager) DATE 07-Dec-20

MURRAY RIX
ANDREW HOUSE, HADFIELD STREET,
DUKINFIELD, CHESHIRE SK16 4QX
TEL 0161 475 0870

TEST CERTIFICATE

DETERMINATION OF THE pH VALUE
BS 1377: PART 3: 1990

CLIENT	W Maher & Sons Ltd
SITE	Buckton Vale
JOB NUMBER	MRN 3818/24

SAMPLE LABEL	Subbase, Type 1	DATE SAMPLED	30 October 2020
LAB SAMPLE No	93660	DATE RECEIVED	30 October 2020
DATE TESTED	02 November 2020	SAMPLED BY	Client

ADVISED SOURCE	Site Investigation Sample
PRE TREATMENT	Air Dried

PH Value	7.3

REMARKS

SIGNED

NAME O.P. Davies BA (Hons)
(Laboratory Manager)

DATE 10 November 2020

MURRAY RIX

33C VAUXHALL INDUSTRIAL ESTATE
GREG STREET, REDDISH, STOCKPORT SK5 7BR
TEL 0161 475 0870 FAX 0161 475 0871

UKAS TESTING 1580

TEST CERTIFICATE

PARTICLE SIZE DISTRIBUTION

BS EN 933-1 : 2012 (Washing & Sieving Method)


Determination of water content in accordance with BS EN 1097-5:2008

CLIENT	W Maher & Sons Ltd
SITE	Buckton Vale
JOB NUMBER	MRN 3818/29

SAMPLE LABEL	Subbase Type 1	DATE SAMPLED	01-Dec-20
LAB SAMPLE No	93672	DATE RECEIVED	01-Dec-20
DATE TESTED	02-Dec-20	SAMPLED BY	Client

MATERIAL	Subbase Type 1
ADVISED SOURCE	W Maher & Sons Ltd - Buckton Vale

Sieve Size (mm)	% Passing (%)	Specification (%)	Sieve Size (mm)	% Passing (%)	Specification (%)
125	100		6.3	43	
90	100		5	40	
80	100		4	36	12-53
75	100		2	30	6-42
63	100	100	1.18	25	
50	99		1	22	3-32
40	95		0.6	18	
31.5	82	75-99	0.5	16	
28	76		0.425	14	
20	67		0.3	12	
16	61	43-81	0.25	11	
14	58		0.15	10	
10	52		0.125	9	
8	47	23-66	0.063	6.8	0-9

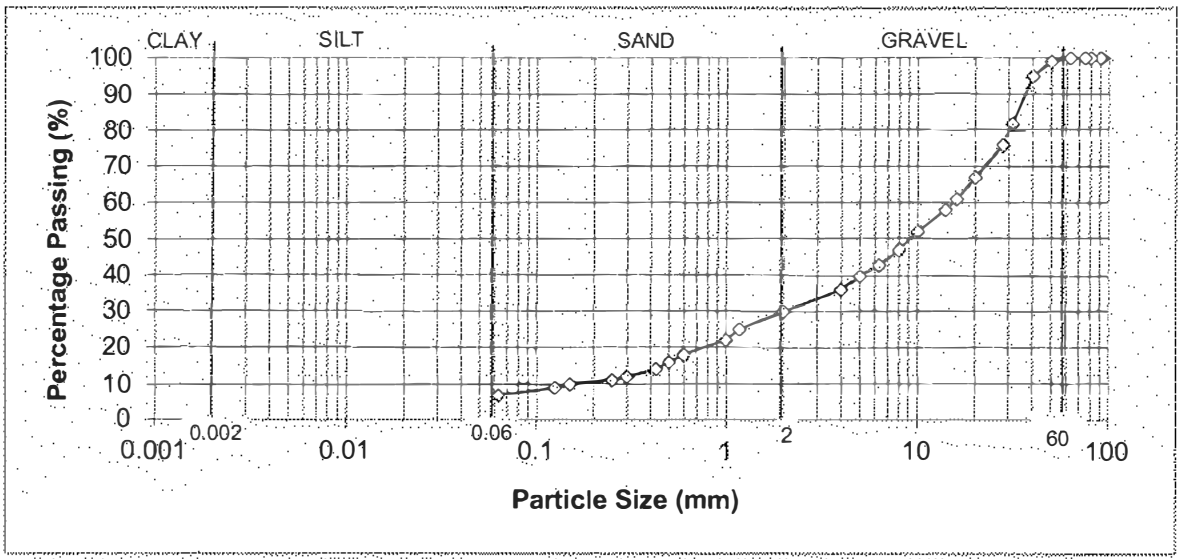

REMARKS

Sample complies with the advised grading specification, specification shown is the overall grading specification in accordance with the specification for highway works Feb 2016.

As received moisture content = 8.9%

SIGNED

NAME O.P. Davies (Deputy Laboratory Manager) DATE 04-Dec-20

MURRAY RIX
CONSULTANCY, SITE INVESTIGATION
CONSTRUCTION MATERIALS TESTING

TEST REPORT

Client W Maher & Sons Ltd

Address Rixton Old Hall
Manchester Road
Warrington
WA3 6EW

Contract Buckton Vale

Job Number MRN 4119/4
Date of Issue 18 March 2021

Approved Signatories

S J Hutchings, O P Davies

Notes

1 All remaining samples and remnants from this contract will be disposed 28 days from the date of this report unless you notify us to the contrary.

2 Result certificates, in this report, not bearing a UKAS mark, are not included in our UKAS accreditation schedule.

3 Opinions and interpretations expressed herein are outside the scope of our UKAS accreditation

4 Certified that the samples have been examined and tested in accordance with the terms of the contract/order and unless otherwise stated conform to the standards/specifications quoted. This does not, however, guarantee the balance of the materials from which the tested samples have been taken to be of equal quality.

MURRAY RIX
ANDREW HOUSE, HADFIELD STREET,
DUKINFIELD, CHESHIRE SK16 4QX
TEL 0161 475 0870

UKAS TESTING 1580

TEST CERTIFICATE

PARTICLE SIZE DISTRIBUTION

BS EN 933-1 : 2012 (Washing & Sieving Method)


Determination of water content in accordance with BS EN 1097-5:2008

CLIENT	W Maher & Sons Ltd
SITE	Buckton Vale
JOB NUMBER	MRN 4119/4

SAMPLE LABEL	Subbase, Type 1	DATE SAMPLED	Not advised
LAB SAMPLE No	96875	DATE RECEIVED	04-Mar-21
DATE TESTED	12-Mar-21	SAMPLED BY	Client

MATERIAL	Gritstone Subbase, Type 1
ADVISED SOURCE	As client and site above

Sieve Size (mm)	% Passing (%)	Specification (%)	Sieve Size (mm)	% Passing (%)	Specification (%)
125	100		6.3	26	
90	100		5	24	
80	100		4	22	12-53
75	100		2	20	6-42
63	100	100	1.18	17	
50	100		1	16	3-32
40	100		0.6	13	
31.5	91	75-99	0.5	12	
28	82		0.425	11	
20	61		0.3	9	
16	44	43-81	0.25	8	
14	40		0.15	6	
10	33		0.125	5	
8	29	23-66	0.063	3.5	0-9

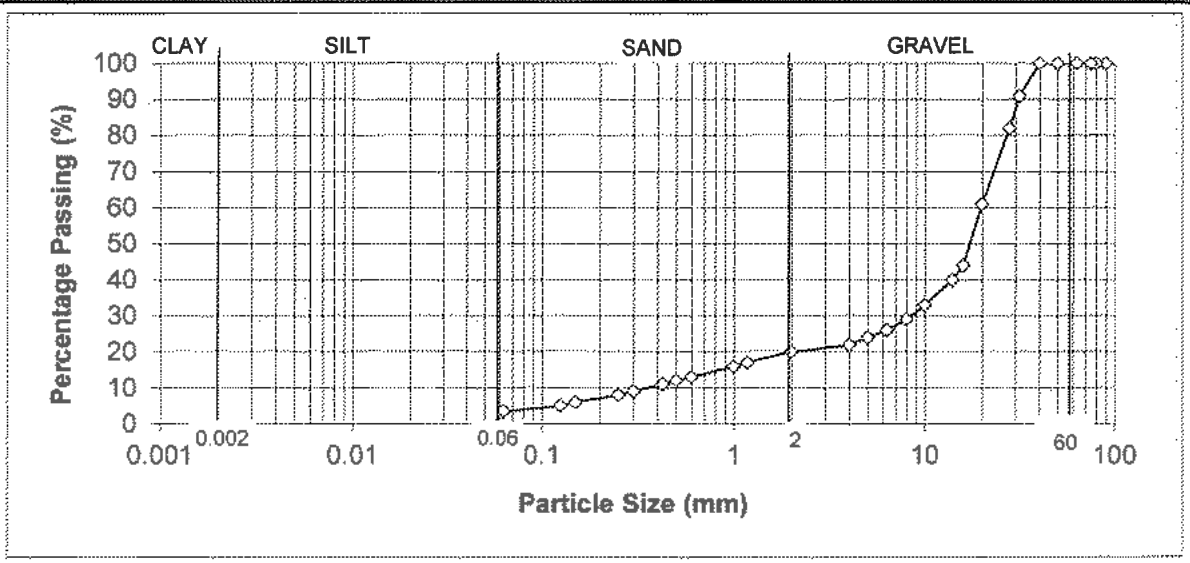

REMARKS Sample complies with the advised grading specification, specification shown is the overall grading specification in accordance with the specification for highway works Feb 2016.
Percentage of material passing 16mm and retained 8mm = 15% (Specification 7% to 30%)
Percentage of material passing 8mm and retained 4mm = 7% (Specification 7% to 30%)
As received moisture content = 2.3%

SIGNED

NAME O.P. Davies BA (Hons) (Laboratory Manager) DATE 18-Mar-21

MURRAY RIX

33C VAUXHALL INDUSTRIAL ESTATE
GREG STREET, REDDISH, STOCKPORT SK5 7BR
TEL 0161 475 0870 FAX 0161 475 0871

UKAS TESTING 1580

TEST CERTIFICATE

PARTICLE SIZE DISTRIBUTION

BS EN 933-1 : 2012 (Washing & Sieving Method)


Determination of water content in accordance with BS EN 1097-5:2008

CLIENT	W Maher & Sons Ltd
SITE	Fletcher Bank Quarry, Ramsbottom
JOB NUMBER	MRN 3818/27

SAMPLE LABEL	6F5	DATE SAMPLED	20-Nov-20
LAB SAMPLE No	93670	DATE RECEIVED	20-Nov-20
DATE TESTED	23-Nov-20	SAMPLED BY	Client

MATERIAL	Gritstone 6F5
ADVISED SOURCE	As client and site above

Sieve Size (mm)	% Passing (%)	Specification (%)	Sieve Size (mm)	% Passing (%)	Specification (%)
125	100	100	6.3	27	
90	83		5	25	
80	83	75-99	4	24	
75	77		2	21	0-35
63	74		1.18	20	
50	70		1	19	
40	64	50-90	0.6	18	
31.5	56		0.5	18	
28	52		0.425	17	
20	42	30-75	0.3	14	
16	38		0.25	12	
14	36		0.15	8	
10	32	15-60	0.125	7	
8	30		0.063	5.9	0-12

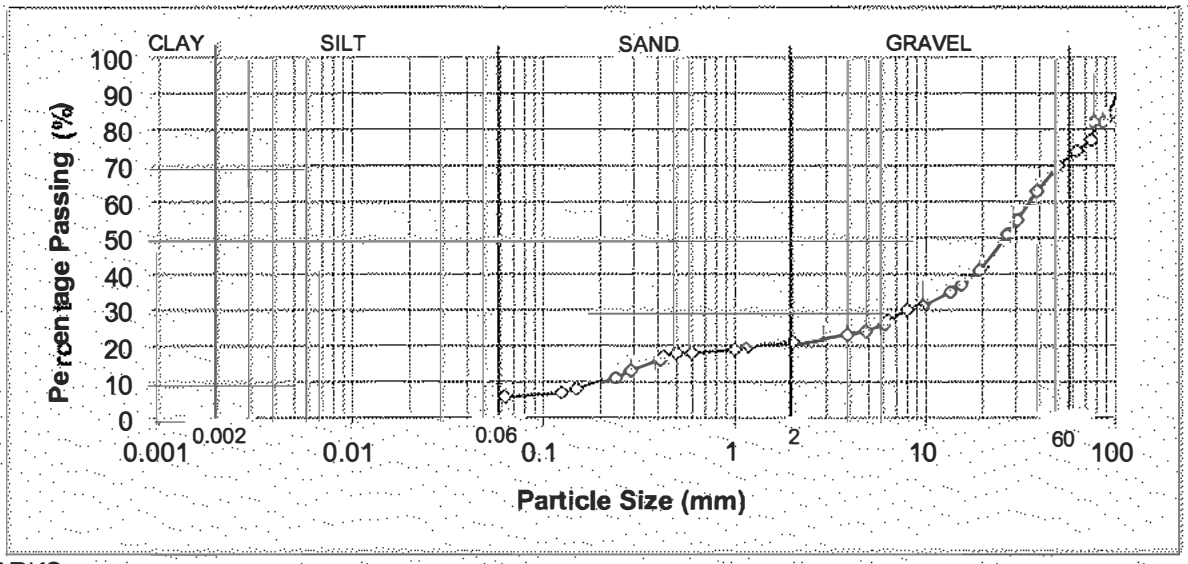

REMARKS

Sample complies with the advised grading specification 6F5 (SHW 2016)

As received moisture content = 9.3%

SIGNED

NAME O.P. Davies BA (Hons) (Laboratory Manager) DATE 07-Dec-20

MURRAY RIX
CONSULTANCY, SITE INVESTIGATION
CONSTRUCTION MATERIALS TESTING

TEST REPORT

Client W Maher & Sons Ltd

Address Rixton Old Hall
Manchester Road
Warrington
WA3 6EW

Contract Fletcher Bank Quarry, Ramsbottom

Job Number MRN 4119/7
Date of Issue 23 March 2021

Approved Signatories

S J Hutchings, O P Davies

Notes

1 All remaining samples and remnants from this contract will be disposed 28 days from the date of this report unless you notify us to the contrary.

2 Result certificates, in this report, not bearing a UKAS mark, are not included in our UKAS accreditation schedule.

3 Opinions and interpretations expressed herein are outside the scope of our UKAS accreditation

4 Certified that the samples have been examined and tested in accordance with the terms of the contract/order and unless otherwise stated conform to the standards/specifications quoted. This does not, however, guarantee the balance of the materials from which the tested samples have been taken to be of equal quality.

MURRAY RIX
ANDREW HOUSE, HADFIELD STREET,
DUKINFIELD, CHESHIRE SK16 4QX
TEL 0161 475 0870

UKAS TESTING 1560

TEST CERTIFICATE

PARTICLE SIZE DISTRIBUTION

BS EN 933-1 : 2012 (Washing & Sieving Method)


Determination of water content in accordance with BS EN 1097-5:2008

CLIENT	W Maher & Sons Ltd
SITE	Fletcher Bank Quarry, Ramsbottom
JOB NUMBER	MRN 4119/7

SAMPLE LABEL	Subbase, Type 1	DATE SAMPLED	Not advised
LAB SAMPLE No	96982	DATE RECEIVED	08-Mar-21
DATE TESTED	12-Mar-21	SAMPLED BY	Client

MATERIAL	Gritstone Subbase, Type 1
ADVISED SOURCE	As client and site above

Sieve Size (mm)	% Passing (%)	Specification (%)	Sieve Size (mm)	% Passing (%)	Specification (%)
125	100		6.3	24	
90	100		5	20	
80	100		4	18	12-53
75	100		2	14	6-42
63	100	100	1.18	12	
50	100		1	11	3-32
40	97		0.6	10	
31.5	94	75-99	0.5	8	
28	89		0.425	7	
20	69		0.3	6	
16	54	43-81	0.25	5	
14	48		0.15	4	
10	35		0.125	3	
8	30	23-66	0.063	2.8	0-9

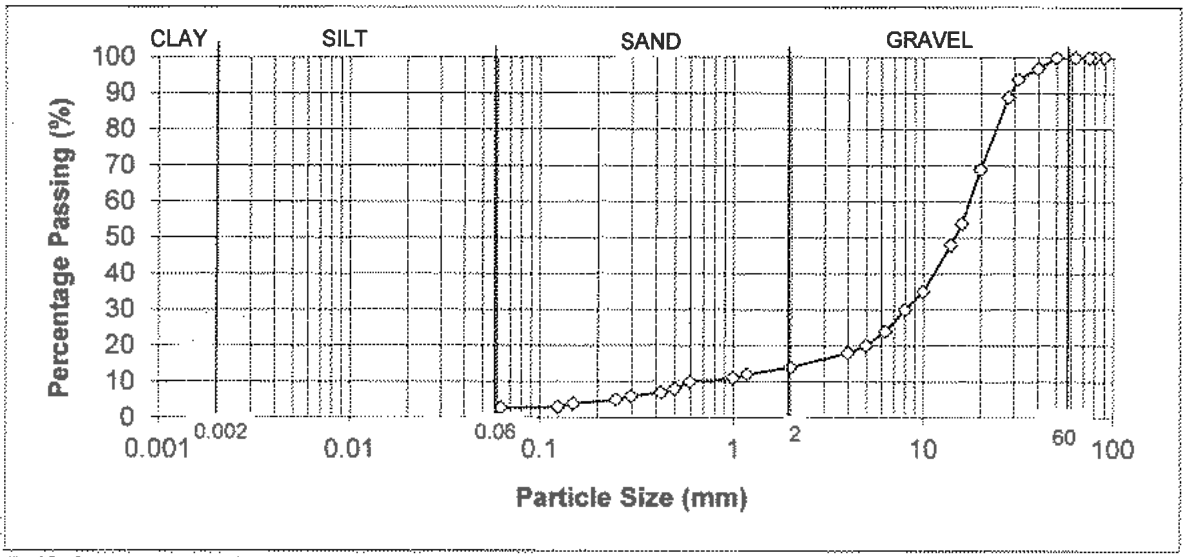

REMARKS Sample complies with the advised grading specification, specification shown is the overall grading specification in accordance with the specification for highway works Feb 2016.
Percentage of material passing 16mm and retained 8mm = 24% (Specification 7% to 30%)
Percentage of material passing 8mm and retained 4mm = 12% (Specification 7% to 30%)
As received moisture content = 6.0%

SIGNED

NAME O.P. Davies BA (Hons) (Laboratory Manager) DATE 23-Mar-21

MURRAY RIX
ANDREW HOUSE, HADFIELD STREET,
DUKINFIELD, CHESHIRE SK16 4QX
TEL 0161 475 0870

UKAS TESTING 1080

TEST CERTIFICATE

PARTICLE SIZE DISTRIBUTION

BS EN 933-1 : 2012 (Washing & Sieving Method)


Determination of water content in accordance with BS EN 1097-5:2008

CLIENT	W Maher & Sons Ltd
SITE	Fletcher Bank Quarry, Ramsbottom
JOB NUMBER	MRN 4119/7

SAMPLE LABEL	6F5	DATE SAMPLED	Not advised
LAB SAMPLE No	96983	DATE RECEIVED	08-Mar-21
DATE TESTED	12-Mar-21	SAMPLED BY	Client

MATERIAL	Gritstone 6F5
ADVISED SOURCE	As client and site above

Sieve Size (mm)	% Passing (%)	Specification (%)	Sieve Size (mm)	% Passing (%)	Specification (%)
125	100	100	6.3	25	
90	88		5	23	
80	88	75-99	4	21	
75	85		2	16	0-35
63	71		1.18	14	
50	68		1	13	
40	64	50-90	0.6	10	
31.5	61		0.5	9	
28	58		0.425	8	
20	47	30-75	0.3	7	
16	42		0.25	6	
14	39		0.15	5	
10	32	15-60	0.125	4	
8	29		0.063	3.7	0-12

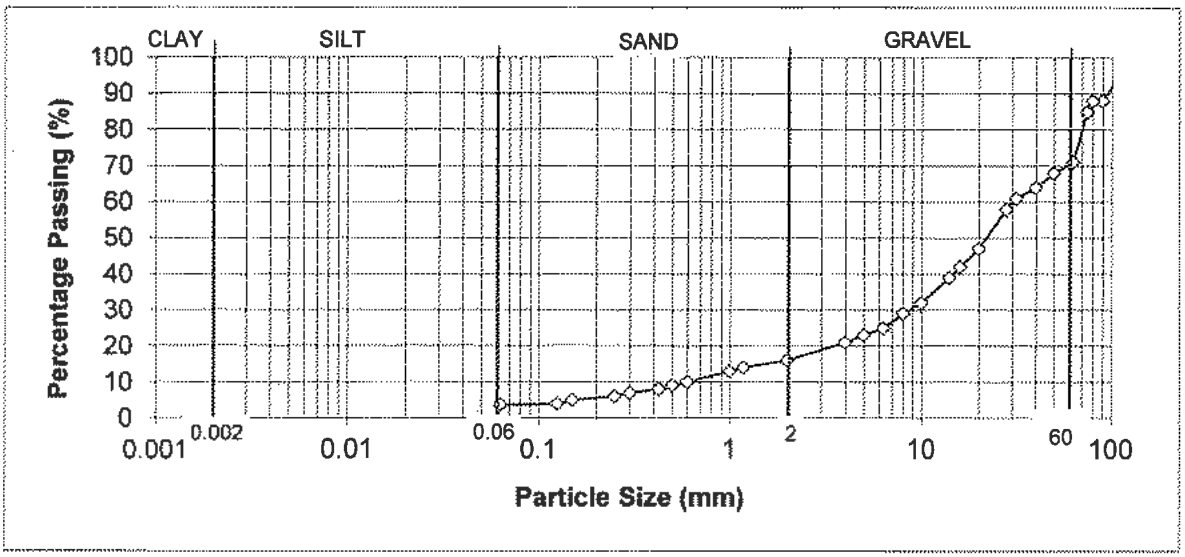

REMARKS
Sample complies with the advised grading specification 6F5 (SHW 2016)
As received moisture content = 4.8%

SIGNED

NAME O.P. Davies BA (Hons) (Laboratory Manager) DATE 23-Mar-21

MURRAY RIX

33C VAUXHALL INDUSTRIAL ESTATE
GREG STREET, REDDISH, STOCKPORT SK5 7BR
TEL 0161 475 0870 FAX 0161 475 0871

U.K.A.S TESTING 1660

TEST CERTIFICATE

PARTICLE SIZE DISTRIBUTION

BS EN 933-1 : 2012 (Washing & Sieving Method)


Determination of water content in accordance with BS EN 1097-5:2008

CLIENT	W Maher & Sons Ltd
SITE	Fletcher Bank Quarry, Ramsbottom
JOB NUMBER	MRN 3818/30

SAMPLE LABEL	Gritstone MOT Subbase Type	DATE SAMPLED	02-Dec-20
LAB SAMPLE No	93674	DATE RECEIVED	02-Dec-20
DATE TESTED	02-Dec-20	SAMPLED BY	Client

MATERIAL	Gritstone - Subbase Type 1
ADVISED SOURCE	W Maher & Sons - Fletcher Bank Quarry, Ramsbottom

Sieve Size (mm)	% Passing (%)	Specification (%)	Sieve Size (mm)	% Passing (%)	Specification (%)
125	100		6.3	38	
90	100		5	36	
80	100		4	35	12-53
75	100		2	31	6-42
63	100	100	1.18	28	
50	100		1	27	3-32
40	100		0.6	23	
31.5	93	75-99	0.5	21	
28	86		0.425	18	
20	62		0.3	14	
16	55	43-81	0.25	12	
14	50		0.15	9	
10	43		0.125	8	
8	41	23-66	0.063	6.7	0-9

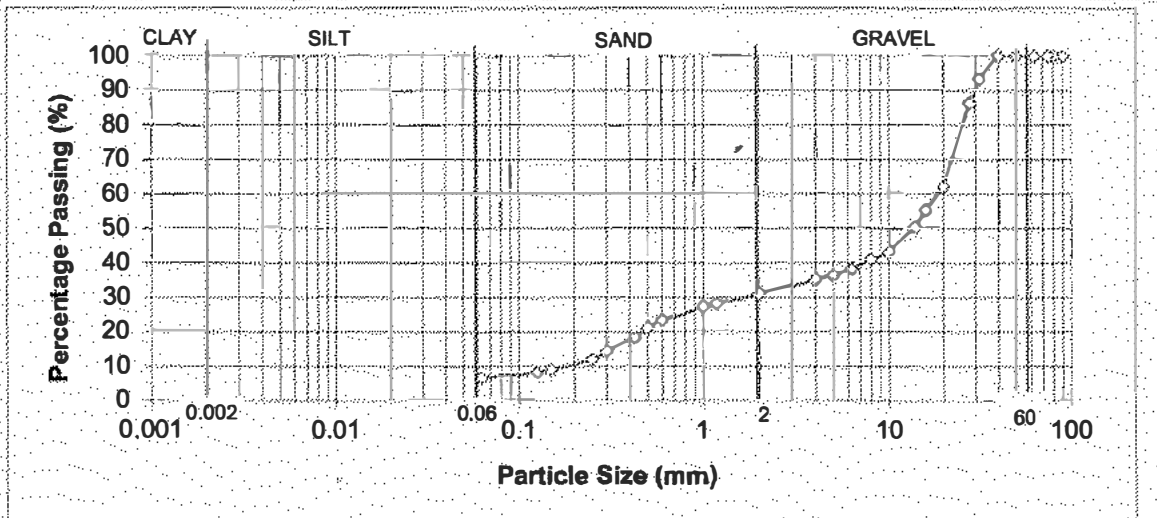

REMARKS

Sample complies with the advised grading specification, specification shown is the overall grading specification in accordance with the specification for highway works Feb 2016.
As received moisture content = 5.8%

SIGNED

NAME O.P. Davies (Deputy Laboratory Manager) DATE 04-Dec-20

Appendix B Provectus Landfill Permits

Copyright © 1976 - 2024 Buro Happold. All rights reserved

Permit

The Environmental Permitting (England & Wales) Regulations 2016

Churchill Enviro Ltd

Buckton Vale Quarry - Western Rock Trap
Carrbrook
Stalybridge
Greater Manchester
SK15 3RD

Permit number

EPR/GB3004XN

Permit

The Environmental Permitting (England and Wales) Regulations 2016

Permit number

EPR/GB3004XN

The Environment Agency hereby authorises, under regulation 13 of the Environmental Permitting (England and Wales) Regulations 2016

Churchill Enviro Ltd ("the operator"),

whose registered office is

1 Eyebrook Road
Bowdon
Altrincham
England
WA14 3LR

company registration number 05393456

to operate a waste operation described in standard rules **SR2015 No.39** at

Buckton Vale Quarry - Western Rock Trap
Carrbrook
Stalybridge
Greater Manchester
SK15 3RD

to the extent authorised by and subject to the conditions of this permit.


Under regulation 27(2) of the Regulations, standard rules **SR2015 No.39** are conditions of this permit.

Name	Date
Dominiqua Drakeford-Allen	**15/04/2019**


Authorised on behalf of the Environment Agency

Schedule 1 – Site plan

This is the plan referred to in the standard rules SR2015 No.39

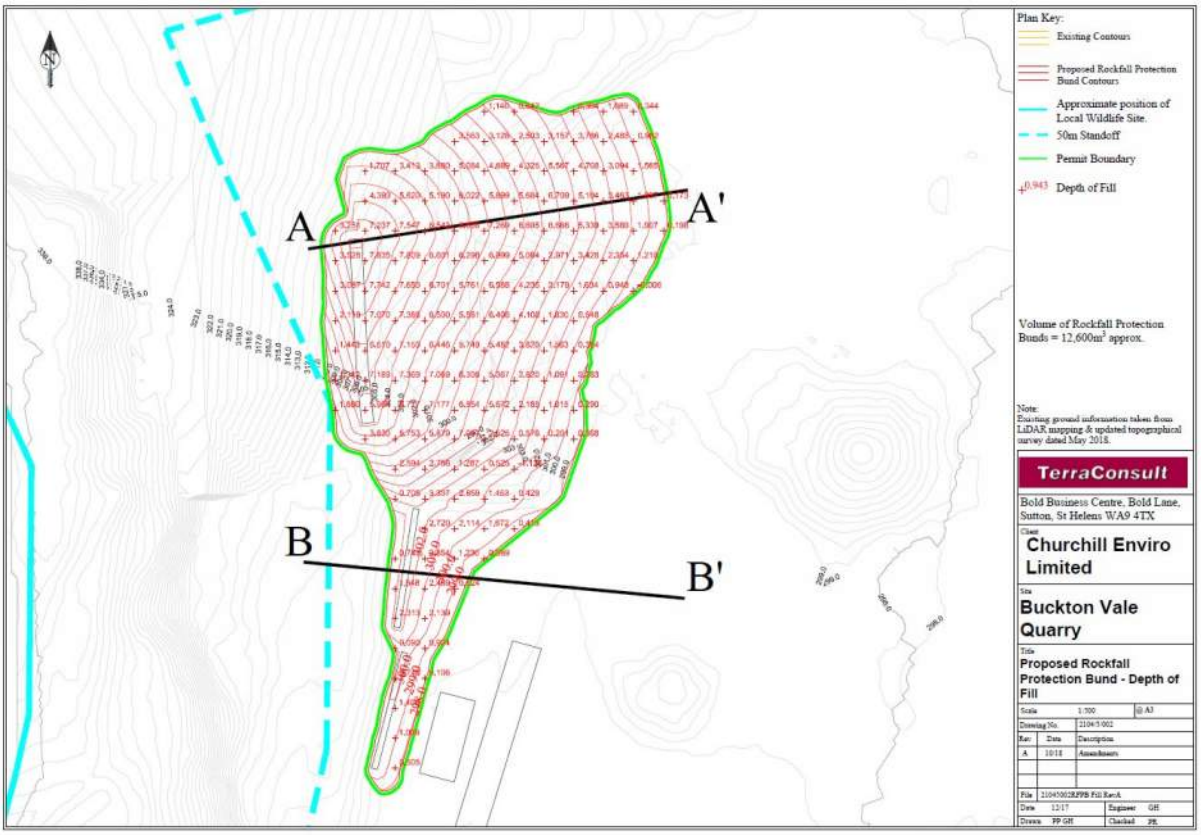

Crown Copyright. All rights reserved. Environment Agency, 100024198, 2019.

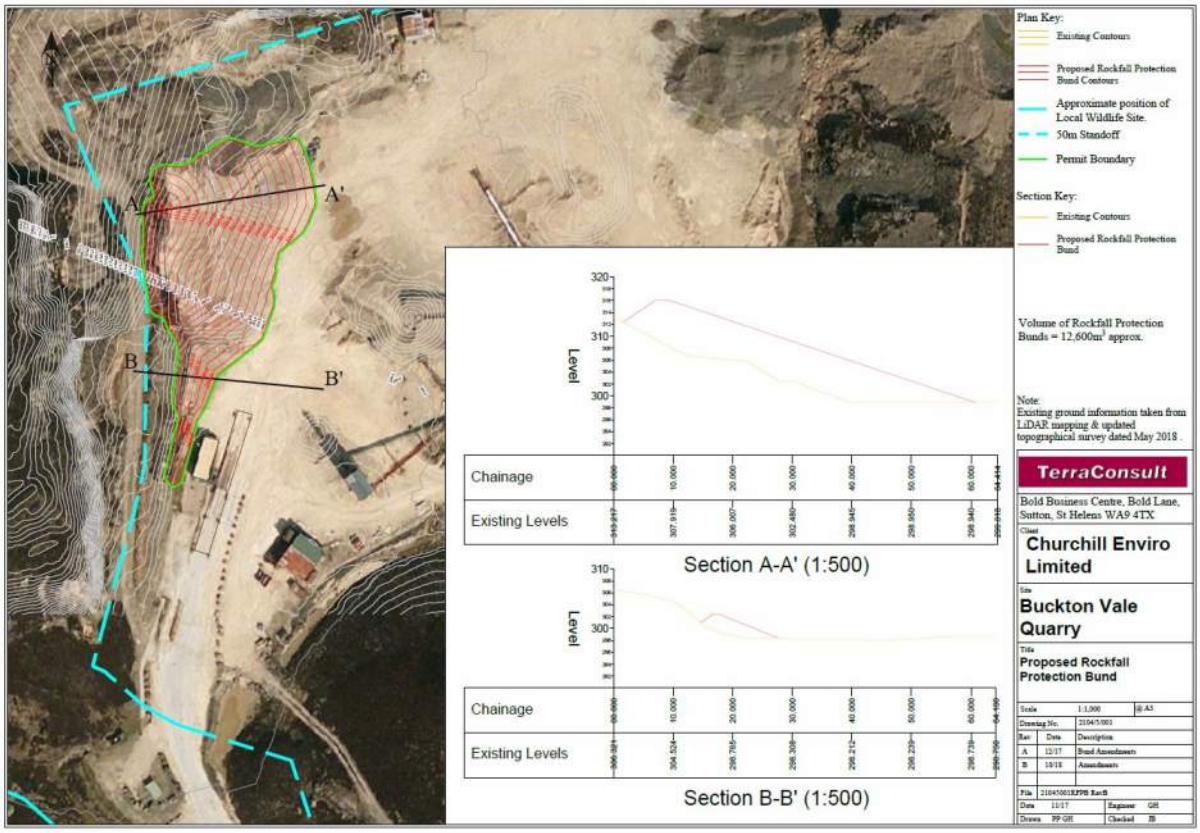
A
A'
B
B'
Plan Key:
Existing Contours
Proposed Rockfall Protection Bund Contours
Approximate position of Local Wildlife Site.
50m Standoff
Permit Boundary
Section Key:
Existing Contours
Proposed Rockfall Protection Bund
Volume of Rockfall Protection Bunds = 12,600m³ approx.
Note:
Existing ground information taken from LiDAR mapping & updated topographical survey dated May 2018 .
Level
320
310
300
Chainage
Existing Levels
Section A-A' (1:500)
Level
310
300
Chainage
Existing Levels
Section B-B' (1:500)
TerraConsult
Bold Business Centre, Bold Lane, Sutton, St Helens WA9 4TX
Client
Churchill Enviro Limited
Site
Buckton Vale Quarry
Title
Proposed Rockfall Protection Bund
Scale 1:1,000 @ A3
Drawing No. 2104/5/001
Rev Date Description
A 12/17 Bund Amendments
B 10/18 Amendments
File 2104/5001EPR Rev B
Date 11/17 Engineer GH
Drawn PP/GH Checked JB

ENVIRONMENT AGENCY

Permit with introductory note

Pollution Prevention and Control (England & Wales) Regulations 2000

Fletcher Bank Quarry Landfill Site

Marshalls Mono Limited
Fletcher Bank
Ramsbottom
Bury
Lancashire
BL0 0DD

Permit number

DP3638ST

Fletcher Bank Quarry Landfill Site
Permit Number DP3638ST

Introductory note

This introductory note does not form a part of the permit

The main features of the installation are as follows.

This is a Permit to operate a landfill located to the east of Ramsbottom, Lancashire at national grid reference SD 804 173. The Operator of this landfill is Marshalls Mono Limited. The site is surrounded by agricultural land to the north, west and east. To the south of the site is a concrete works and quarry area. The nearest residential receptors are approximately 50m from the installation boundary to the north west of the site. The boundary between Bury Metropolitan Borough Council and Lancashire County Council goes through the centre of the site.

The landfill is a waste disposal facility for non-hazardous wastes. Quarrying has taken place at the site since the 1880's and the site continues to be an operational quarry. The overall capacity of the installation is 1.6 million cubic metres. The Permit limits the disposal of waste to 150,000 tonnes per year. The site is to be operated as 6 separate cells.

The main emissions from the site are likely to be noise and vibration, dust and mud.

Due to the permitted waste types there is no active management of landfill gas. Each cell will be fitted with monitoring wells to monitor the presence of landfill gas and leachate. In addition monitoring boreholes are installed externally to the site to allow monitoring of groundwater and landfill gas migration.

Status log of the permit		
Detail	**Date**	**Response Date**
Application DP3638ST	Received 09/05/2005	
Response to Schedule 4 notice	Request dated 01/02/2006	Response dated 03/05/2006
Response to request for information	Request dated 09/05/2006	Response dated 12/05/2006 and 22/05/2006
Permit determined	08/03/2007	

End of Introductory Note

Permit

Permit number
DP3638ST

The Environment Agency (the Agency) in exercise of its powers under regulation 10 of the Pollution Prevention and Control (England and Wales) Regulations 2000 (SI 2000 No 1973) and regulation 6 of the Landfill (England and Wales) Regulations 2002 (SI 2002 No.1559) hereby authorises **Marshalls Mono Limited** ("the operator"),

whose registered office is

Birkby Grange

85 Birkby Hall Road

Birkby

Huddersfield

HD2 2YA

Company registration number **509579**

to operate an installation at
Fletcher Bank Quarry Landfill Site
Fletcher Bank
Ramsbottom
Bury
Lancashire
BL0 0DD

to the extent authorised by and subject to the conditions of this permit.

Signed	Date
Martin Jenkins	8th March 2007

Martin Jenkins, Permitting Team Leader, Warrington Strategic Permitting Group

Authorised to sign on behalf of the Agency

Conditions

1. Management

1.1 General management

1.1.1 The activities shall be managed and operated:

(a) in accordance with a management system, which identifies and minimises risks of pollution, including those arising from operations, maintenance, accidents, incidents and non-conformances and those drawn to the attention of the operator as a result of complaints; and

(b) by sufficient persons who are competent in respect of the responsibilities to be undertaken by them in connection with the operation of the activities.

1.1.2 Records demonstrating compliance with condition 1.1.1 shall be maintained.

1.1.3 Any person having duties that are or may be affected by the matters set out in this permit shall have convenient access to a copy of it kept at or near the place where those duties are carried out.

1.2 Accidents that may cause pollution

1.2.1 The operator shall:

(a) maintain and implement an accident management plan;

(b) review and record at least every 4 years or as soon as practicable after an accident, (whichever is the earlier) whether changes to the plan should be made;

(c) make any appropriate changes to the plan identified by a review.

1.3 Finance

1.3.1 No activities authorised by this permit shall be commenced unless the Operator has entered into an Agreement with the Agency to secure financial provision to meet the obligations under this Permit, and the Operator has given prior written notice to the Agency of the intention to commence operations at the site.

1.3.2 The financial provision for meeting the obligations under this permit provided under condition 1.3.1 shall thereafter be maintained by the operator throughout the subsistence of this permit and the operator shall produce evidence of such provision whenever required by the Agency.

1.3.3 The operator shall ensure that the charges it makes for the disposal of waste in the landfill cover all of the following:

(a) the costs of setting up and operating the landfill;

(b) the costs of the financial provision required by condition 1.3.1; and

(c) the estimated costs for the closure and aftercare of the landfill.

1.4 Energy efficiency

1.4.1 The operator shall:

(a) Review and record at least every 4 years whether there are suitable opportunities to improve the energy efficiency of the activities; and

(b) Implement any appropriate measures identified by a review.

1.5 Site security

1.5.1 Site security measures shall prevent unauthorised access to the site, as far as practicable.

2. Operations

2.1 Permitted activities

2.1.1 The operator is authorised to carry out the activities specified in schedule 1 table S1.1 (the "activities").

2.2 The site

2.2.1 The activities shall not extend beyond the site, being the land shown edged in red on the site plan at schedule 2 to this permit.

2.3 Operating techniques

2.3.1 The activities shall, subject to the conditions of this permit, be operated using the techniques and in the manner described in the documentation specified in schedule 1 table S1.2, unless otherwise agreed in writing by the Agency.

2.5 Improvement programme

2.5.1 The operator shall complete the improvements specified in schedule 1 table S1.3 by the date specified in that table unless otherwise agreed in writing by the Agency.

2.5.2 Except in the case of an improvement which consists only of a submission to the Agency, the operator shall notify the Agency within 14 days of completion of each improvement.

2.6 Pre-operational conditions.

2.6.1 The operations specified in schedule 1 table S1.4 shall not commence until the measures specified in that table have been completed.

2.7 Engineering

2.7.1 No construction of any new cell shall commence until the operator has submitted construction proposals and the Agency has confirmed that it is satisfied with the construction proposals.

2.7.2 The construction of a new cell shall take place only in accordance with the approved construction proposals unless:

(a) any change to the approved construction proposals would have no impact on the performance of any element of the design; or

(b) a change has otherwise been agreed in writing by the Agency.

2.7.3 No disposal of waste shall take place in a new cell until the operator has submitted a CQA Validation Report and the Agency has confirmed that it is satisfied with the CQA Validation Report.

2.7.4 No construction of landfill Infrastructure shall commence until the operator has submitted relevant construction proposals or a written request to use previous construction proposals and the Agency has confirmed that it is satisfied with the construction proposals.

2.7.5 The construction of the landfill Infrastructure shall take place only in accordance with the approved construction proposals unless:

(a) any change to the approved construction proposals would have no impact on the performance of any element of the design; or

(b) a change has otherwise been agreed in writing by the Agency.

2.7.6 The operator shall submit a CQA Validation Report as soon as practicable following the construction of the relevant landfill Infrastructure.

2.7.7 Where pollution controls are immediately necessary to prevent an incident or accident, then conditions 2.7.4 and 2.7.5 do not apply and the relevant landfill Infrastructure may be constructed, provided that the construction proposals are submitted to the Agency as soon as practicable.

2.7.8 For the purposes of conditions 2.7.1, 2.7.3 and 2.7.4, the Agency shall be deemed to be satisfied where it has not, within the period of 4 weeks from the date of receipt of the relevant construction proposals or CQA Validation Report, either:

(a) confirmed whether or not it is satisfied; or

(b) informed the operator that it requires further information.

2.8 Waste acceptance

2.8.1 Wastes shall only be accepted for disposal if:

(a) they are listed in schedule 3, and

(b) they are non- hazardous waste, and

(c) they are not whole used tyres (other than bicycle tyres and tyres with an outside diameter of more than 1400mm), and

(d) they are not shredded used tyres, and

(e) they are not liquid waste (including waste waters but excluding sludge), and

(f) they are not chemical substances from research and development or teaching activities, for example laboratory residues, which are unidentified and/or which are new and whose effects on man and/or the environment are unknown, and

(g) all the relevant waste acceptance procedures set out in schedule 1 of the Landfill Regulations have been completed, and

(h) they fulfil the relevant waste acceptance criteria, and

(i) they have not been diluted or mixed solely to meet the relevant waste acceptance criteria, and

(j) from 30th October 2007 they are wastes which have been treated, except for: inert wastes for which treatment is not technically feasible; or it is waste other than inert waste and treatment would not reduce its quantity or the hazards which it poses to human health or the environment,

(k) any code beginning with 07 05 and 16 03 shall exclude waste medicinal products and pharmaceutically active waste materials arising from their manufacture.

2.8.2 The operator shall visually inspect:

(a) without unloading it, waste that is not in an enclosed container or enclosed vehicle on arrival at the landfill; and

(b) waste at the point of deposit;

and shall satisfy itself that it conforms to the basic characterisation documentation submitted by the holder.

2.8.3 Where the operator has taken samples to establish that the waste is in conformity with the documentation submitted by the holder then the samples taken shall be retained for at least one month and results of any analysis for at least two years.

2.8.4 The operator on accepting each delivery of waste shall provide a receipt to the person delivering it.

2.8.5 The total quantity of waste that shall be deposited in the landfill shall be limited by the pre-settlement levels shown on drawing MM/FBQ/PPC-DESID 5A.

2.8.6 The quantity of waste that is deposited in the landfill in any year shall not exceed the limits in schedule 1 table S1.5.

2.8.7 The operator shall maintain and implement a system which ensures that a record is made of the quantity, characteristics, date of delivery and, where practicable, origin of any waste that is received for disposal or recovery and of the identity of the producer, or in the case of municipal waste and multiple collection vehicles, of the collector of such waste. Any information regarded by the operator as commercially confidential shall be clearly identified in the record.

2.9 Leachate levels

2.9.1 The limits for the level of leachate listed in schedule 4 table S4.1 shall not be exceeded.

2.10 Closure, aftercare and decommissioning

2.10.1 The operator shall maintain and operate the activities so as to prevent or where that is not practicable, to minimise, any pollution risk on closure and decommissioning.

3. Emissions and monitoring

3.1 Emissions to water, air or land

3.1.1 There shall be no point source emissions to water, air or land.

3.2 Emissions to groundwater

3.2.1 There shall be no emission from the activities into groundwater of any substance in List I (as defined by the Groundwater Regulations) contrary to those regulations.

3.2.2 There shall be no emission from the activities into groundwater of any substance in List II (as defined in the Groundwater Regulations) so as to cause pollution (as defined in those regulations).

3.2.3 The trigger levels for emissions into groundwater for the parameter(s) and monitoring point(s) set out in schedule 4 Table S4.1 shall not be exceeded.

3.2.4 The operator shall submit to the Agency a review of the Hydrogeological Risk Assessment:

(a) between 9 and 6 months prior to the fourth anniversary of the granting of the permit, and

(b) between 9 and 6 months prior to every subsequent 4 years after the fourth anniversary of the granting of the permit.

3.3 Fugitive emissions of substances

3.3.1 Fugitive emissions of substances (excluding odour, noise and vibration) shall not cause pollution. The operator shall not be taken to have breached this condition if appropriate measures have been taken to prevent or where that is not practicable, to minimise, those emissions.

3.3.2 Litter or mud arising from the activities shall not cause pollution. The operator shall not be taken to have breached this condition if appropriate measures have been used to prevent or where that is not practicable to minimise, the litter and mud.

3.3.3 Litter or mud arising from the activities shall be cleared from affected areas outside the site as soon as practicable.

3.3.4 All liquids, whose emission to water or land could cause pollution, shall be provided with secondary containment, unless the operator has used other appropriate measures to prevent or where that is not practicable, to minimise, leakage and spillage from the primary container.

3.4 Odour

3.4.1 Emissions from the activities shall be free from odour at levels likely to cause annoyance outside the site, as perceived by an authorised officer of the Agency, unless the operator has used appropriate measures to prevent or where that is not practicable to minimise the odour.

3.5 Noise and vibration

3.5.1 Emissions from the activities shall be free from noise and vibration at levels likely to cause annoyance outside the site, as perceived by an authorised officer of the Agency, unless the operator has used appropriate measures to prevent or where that is not practicable to minimise the noise and vibration.

3.6 Monitoring

3.6.1 The operator shall, unless otherwise agreed in writing by the Agency, undertake the monitoring specified in the following tables in schedule 4 to this permit:

(a) Leachate specified in table S4.1 and S4.4;

(b) Groundwater specified in tables S4.2 and S4.6;

(c) Landfill gas specified in tables S4.3 and;

(d) Surface water specified in table S4.5.

3.6.2 The operator shall maintain records of all monitoring required by this permit including records of the taking and analysis of samples, instrument measurements (periodic and continual), calibrations, examinations, tests and surveys and any assessment or evaluation made on the basis of such data.

3.6.3 A topographical survey of the site referenced to ordnance datum shall be carried out:

(a) annually, and

(b) prior to the disposal of waste in any new cell or new development area of the landfill, and

(c) following closure of the landfill or part of the landfill.

The topographical survey shall be used to produce a plan of a scale adequate to show the surveyed features of the site.

3.7 Transfers off-site

3.7.1 Records of all the wastes sent off site from the activities, for either disposal or recovery, shall be maintained.

4. Information

4.1 Records

4.1.1 All records required to be made by this permit shall:

(a) be legible;

(b) be made as soon as reasonably practicable;

(c) if amended, be amended in such a way that the original and any subsequent amendments remain legible, or are capable of retrieval; and

(d) be retained, unless otherwise agreed in writing by the Agency, for at least 6 years from the date when the records were made, or in the case of the following records until permit surrender:

(i) the results of groundwater monitoring;

(ii) sub-surface landfill gas monitoring;

(iii) leachate levels, quality and quantities;

(iv) waste types and quantities;

(v) the specification and as built drawings of the basal, sidewall and capping engineering systems

4.1.2. Any records required to be made by this permit shall be supplied to the Agency within 14 days where the records have been requested in writing by the Agency.

4.1.3. All records required to be held by this permit shall be available for on site and shall be available for inspection by the Agency at any reasonable time.

4.2 Reporting

4.2.1 A report or reports on the performance of the activities over the previous year shall be submitted to the Agency by 31 January (or other date agreed in writing by the Agency) each year. The report(s) shall include as a minimum:

(a) a review of the results of the monitoring and assessment carried out in accordance with this permit against the relevant assumptions, parameters and results in the risk assessments submitted in relation to this installation and any agreed amendments thereto;

(b) where the operator's management system encompasses annual improvement targets, a summary report of the previous year's progress against such targets;

(c) the energy consumed at the site, reported in the format set out in schedule 5 table S5.3

(d) the annual production/treatment set out in schedule 5 table S5.2;

(e) details of any contamination or decontamination of the site which has occurred;

(f) the topographical surveys required by condition 3.6.3 other than those submitted as part of a CQA validation report;

(g) the volumetric difference (reported in cubic metres) between the most recent topographical survey and the previous annual topographical survey i.e. the additional volume of the landfill void that is occupied by waste;

(h) an assessment of the settlement behavior of the landfill body based on the difference between the most recent topographical survey and previous annual topographical survey for the areas of the landfill which did not receive waste between the surveys;

(i) a calculation of the remaining capacity (reported in cubic metres) derived from the pre-settlement contours and the most recent topographical survey;

(j) the compliance testing undertaken in the period;

4.2.2 Within 28 days of the end of the reporting period the operator shall, unless otherwise agreed in writing by the Agency, submit reports of the monitoring and assessment carried out in accordance with the conditions of this permit, as follows:

(a) in respect of the parameters and emission points specified in schedule 5 Table S5.1;

(b) for the reporting periods specified in schedule 5 Table S5.1 and using the forms specified in schedule 5 Table S5.4; and

(c) giving the information from such results and assessments as may be required by the forms specified in those tables.

4.2.3 A summary report of the waste types and quantities accepted and removed from the site shall be made for each quarter. It shall be submitted to the Agency within one month of the end of the quarter and shall be in the format required by the Agency.

4.2.4 The operator shall, unless notice under this condition has been served within the preceding 4 years, submit to the Agency, within 6 months of receipt of a written notice, a report assessing whether there are other appropriate measures that could be taken to prevent, or where that is not practicable, to minimise pollution.

4.2.5 All reports and notifications required by the permit shall be sent to the Agency using the contact details supplied in writing by the Agency.

4.3 Notifications

4.3.1 The Agency shall be notified without delay following the detection of:

(a) any malfunction, breakdown or failure of equipment or techniques, accident, or fugitive emission which has caused, is causing or may cause significant pollution;

(b) the breach of a limit specified in the permit;

(c) any significant adverse environmental effects.

4.3.2 Any information provided under condition 4.3.1 shall be confirmed by sending the information listed in schedule 6 to this permit within the time period specified in that schedule.

4.3.3. Prior written notification shall be given to the Agency of the following events and in the specified timescales:

(a) as soon as practicable prior to the permanent cessation of any of the permitted activities;

(b) as soon as practicable prior to the cessation of the landfill disposal activities, for a period likely to exceed 1 month; and

(c) at least 7 days prior to the resumption of the landfill disposal activities after a cessation notified under (b) above.

4.3.4 Where the Agency has requested in writing that it shall be notified when the operator is to undertake monitoring and/or spot sampling, the operator shall inform the Agency when the relevant monitoring is to take place. The operator shall provide this information to the Agency at least 14 days before the date the monitoring is to be undertaken.

4.3.5 The Agency shall be notified within 7 days of any changes in technically competent management and the name of any incoming person together with evidence that such person has the required technical competence.

4.3.6 The Agency shall be provided, within 14 days of the operator or any relevant person being convicted of a relevant offence, (unless such information has already been notified to the Agency), with details of the nature of the offence, the place and date of conviction, and the sentence imposed.

4.3.8 The Agency shall be notified within 14 days of the operator and/or any relevant person lodging an appeal against a conviction for any relevant offence and of the outcome when the appeal is decided.

4.3.9 The Agency shall be notified within 14 days of the occurrence of the following matters, except where such disclosure is prohibited by Stock Exchange rules:

(a) any change in the operator's trading name, registered name or registered office address;

(b) any change to particulars of the operator's ultimate holding company (including details of an ultimate holding company where an operator has become a subsidiary); and

(c) any steps taken with a view to the operator going into administration, entering into a company voluntary arrangement or being wound up.

4.4 Interpretation

4.4.1 In this permit the expressions listed in schedule 7 shall have the meaning given in that schedule.

Schedule 1 - Operations

Table S1.1 Activities

Activity listed in Schedule 1 of the PPC Regulations	Description of specified activity	Limits of specified activity
Section 5.2 Part A(1) (a). The disposal of waste in a landfill.	Landfill for non-hazardous waste (landfill classification under the Landfill Regulations 2002)	Receipt, handling, storage and disposal of wastes, consisting of the types and quantities specified in conditions 2.8, as an integral part of landfilling.

Table S1.2 Operating techniques

Description	Parts	Date Received
Application	The response to questions 2.1, 2.2, 2.3, 2.4, 2.5, 2.6, 2.7, 2.8, 2.9 and 2.11 in part B of the Application Form. Excluding the response to questions 2.2.10, 2.2.15-2.2.21, 2.2.35-2.2.41, 2.2.42, 2.2.46, 2.2.47(part 5) 2.2.49, 2.2.58-2.2.61 (parts 1 and 2), 2.2.64-2.2.68, 2.2.72-2.2.76, 2.2.79-2.81, 2.3.4, 2.7, 2.9.1-2.9.3.	09/05/2005
Response to Schedule 4 dated 01/02/2006.	Revised drawings DESID 6B (Rev A) and DESID 7B (Rev A)	Received by email on 03/04/2006
	FBQ Landsim Report rev 1.pdf (March 2006) Fbq sch 4 response note.doc (March 2006) Fbq two phase model.pdf Fbq two phase results.pdf	Received by email on 03/04/2006
	Letter from Silkstone Environmental dated 26th March 2006 Letter from FGB dated 3rd April 2006 (Ref: JC/JKB/FletcherBank 192)	Received by email on 03/04/2006
Response to email dated 09/05/2006.	FletchBank_Liner_Workbook.pdf	Received by email on 12/05/2006
	Fbq hra landsim revea1.pdf (May 2006)	Received by email on 22/05/2006
Amendment to the installation boundary	INPUTS Update 1 Revised Source Term.pdf INPUTS Update 2 Revised Source Term.pdf INPUTS Update 3 Revised Source Term.pdf HRA Annex 1 ReportV2.doc	Received by email on 23/06/2006
	Revised Installation boundary drawings DESID2, 4, 5A, 5B, 6A, 7A and 8A.	Received by email on 23/06/2006
	Fletcher Bank Update 1_revised source_term.sim Fletcher Bank Update 1_revised source_term.rst Fletcher Bank Update 2_revised source_term.sim Fletcher Bank Update 2_revised source_term.rst Fletcher Bank Update 3_revised source_term.sim Fletcher Bank Update 3_revised source_term.rst	Received by email on 23/06/2006
	Revised Non-technical summary Revised Environmental Setting and Installation Design Report	Received by email on 06/07/2006
	Partial Revision of Part B of the application form (excluding the responses to questions 2.2.38, 2.2.18-2.2.19 and 2.2.74).	Received on 07/07/2006
	Drawing MM/FBQ/QWP0106-01 Site Layout Drawing MM/FBQ/PPC/DESID8B	Received on 31/07/2006


Table S1.3 Improvement programme requirements		
Reference	**Requirement**	**Date**
1	A revised Landfill Gas Risk Assessment shall be submitted to the Environment Agency for approval. The risk assessment shall consider the installation as identified in Schedule 2 of this permit and shall be based on the waste types listed in Schedule 3 of this permit. The report shall include a revised Gas Sim model and contain any necessary revisions to the procedures for the monitoring and management of landfill gas at the site.	01/04/2008
2	A landfill gas report shall be submitted to Environment Agency for approval. The report shall contain appropriate borehole specific background levels and compliance limits for perimeter gas monitoring boreholes BEL1, BEL2, SLR2 and SLR3 and assessment criteria for internal waste boreholes FB106 to FB111. The report shall include any necessary revisions to the landfill gas action plan as contained in Appendix 4 of the Regulatory Specification 2005.	01/11/2007
3	A Particulate Management and Monitoring Plan shall be submitted to the Environment Agency for approval. The plan shall include the measures to be taken to minimise any particulate matter escaping beyond the installation boundary and proposals for carrying out monitoring and assessment of particulate matter in accordance with the Environment Agency's Guidance on Monitoring of Particulate Matter (M17). The plan shall be implemented by the Operator from the date of approval by the Environment Agency.	01/07/2007
4	A Litter Management Plan shall be submitted to the Environment Agency for approval. The plan shall include proposals that minimise the risk of litter escaping from the Installation boundary and proposes reasonable timescales for litter collection. The plan shall be implemented by the Operator from the date of approval by the Environment Agency.	01/07/2007
5	The Operator shall submit to the Environment Agency for approval a revised Surface Water Management and Monitoring Plan that is specific to the installation as identified in schedule 2 of this permit. The plan shall take into account the requirements of the Environment Agency's Guidance on Monitoring of Landfill Leachate, Groundwater and Surface Water (LFTGN02) and include as a minimum: Relevant surface water monitoring points that will monitor any impact from the installation. The location of surface water monitoring points upstream and downstream of the installation on Crossbank Brook. Monitoring points shall be indicated on a drawing of suitable scale. The plan shall be implemented by the Operator from the date of approval by the Environment Agency.	01/07/2007

Table S1.4 Pre-operational measures for future development		
Reference	**Operation**	**Pre-operational Measures**
1	Prior to deposit of waste in any cell.	A revised Leachate Management Plan shall be submitted to the Environment Agency for approval. The plan shall include procedures for leachate extraction and collection and details of leachate disposal and discharge methods and routes. The plan shall be implemented by the Operator from the date of approval by the Environment Agency.
2	Prior to deposit of waste in cell 3	A report shall be submitted to the Environment Agency for approval that demonstrates the procedures in place to ensure that the wastes listed in Schedule 3 are only deposited within the installation boundary.
3	Capping of each cell	A report detailing a revised cap design shall be submitted to the Environment Agency for approval. The report shall include justification for the design of any surface water drainage layer required above the cap and shall include a protection layer above the cap to guarantee performance of the cap over the life of the site.

Table S1.5 Annual waste input limits	
Category	**Limit Tonnes/ Year**
Non-hazardous waste	150,000

Schedule 2 - Site plan

Extracted from plan ESID 2 (Rev A), 'Environmental Site Setting' submitted as part of the Permit Application.

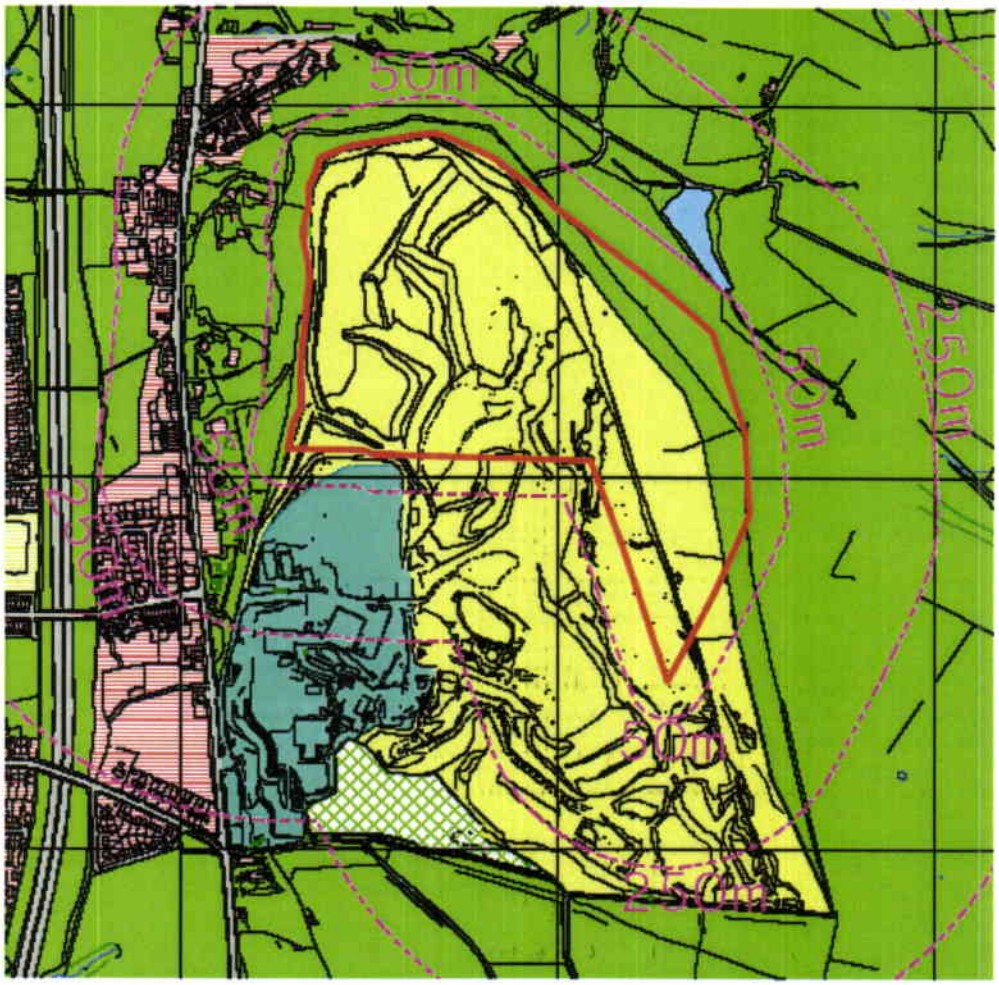

Schedule 3 - List of permitted wastes

01	**Wastes Resulting from Exploration, Mining, Quarrying, and Physical and Chemical Treatment of Minerals**
01 04	**Wastes from physical and chemical processing on non-metalliferous minerals**
01 04 99	Semi-wet cake
10	**Wastes from Thermal Processes**
10 11	**Wastes from the manufacture of glass and glass products**
10 11 03	Waste glass-based fibrous materials[1]
15	**Waste Packaging; Absorbants, wiping cloths, filter materials and protective clothing not otherwise specified**
15 01	**Packaging (including separately collected municipal packaging waste)**
15 01 01	Paper and Cardboard
15 01 02	Plastic wrap and straps
15 01 03	Wooden Pallets
15 01 07	Glass packaging
17	**Construction and Demolition Wastes (Including excavated soils from contaminated sites)**
17 01	**Concrete, bricks, tiles and ceramics**
17 01 01	Concrete
17 01 02	Bricks
17 01 03	Tiles and ceramics
17 05 04	Soil and stone
17 01 07	Mixtures of concrete, bricks, tiles and ceramics other than those mentioned in 17 01 06
17 05	**Soil (including excavated soil from contaminated sites), stones and dredging spoil)**
17 05 04	Soil and stones other than those mentioned in 17 05 03
20	**Municipal waste (household waste and similar commercial Industrial and institutional wastes) including separately collected fractions**
20 02	**Garden and park wastes (Including cemetery waste)**
20 02 02	Soil and stones

Schedule 4 – Emissions and monitoring

Table S4.1 Leachate level limits and monitoring requirements

Monitoring point reference/ Description	Limit	Monitoring frequency	Monitoring method
Leachate collection sump in each cell identified on plan MM/FBQ/PPC-DESID7A.	5m above the base of the cell.	Monthly	In accordance with Environment Agency Guidance LFTGN02 (February 2003) unless otherwise agreed in writing with the Environment Agency.

Table S4.2 Trigger levels for emissions into groundwater and monitoring requirements

Monitoring point reference	Parameter	Limit (including unit)	Reference Period	Monitoring frequency	Monitoring standard or method
BEL1, BEL2 and SLR3 as identified on drawing MMF/FBQ/PPC-DESID8A.	Ammoniacal-N	2 mg/l	Spot Sample	Monthly	In accordance with Environment Agency Guidance LFTGN02 (February 2003) unless otherwise agreed in writing with the Environment Agency.
	Chloride	250 mg/l	Spot Sample	Monthly	
	Mercury	0.0001 mg/l	Spot Sample	Quarterly	
	Cadmium	0.0001 mg/l	Spot Sample	Quarterly	

Table S4.3 Landfill gas – monitoring requirements

Emission point reference or source or description of point of measurement	Parameter	Monitoring frequency	Monitoring standard or method	Other specifications
BEL1, BEL2, SLR2 and SLR3 identified on as identified on drawing MMF/FBQ/PPC-DESID8A.	Methane Carbon Dioxide Oxygen Atmospheric pressure	Monthly	In accordance with Environment Agency Guidance LFTGN03 (September 2003) unless otherwise agreed in writing with the Environment Agency.	None
In waste monitoring boreholes FB106 to FB111 as identified on drawing as identified on drawing MMF/FBQ/PPC-DESID8A.	Methane Carbon Dioxide Oxygen Atmospheric pressure Differential pressure Meteorological Data	Monthly		None

Table S4.4 Leachate– other monitoring requirements				
Emission point reference or source or description of point of measurement	**Parameter**	**Monitoring frequency**	**Monitoring standard or method**	**Other specifications**
Leachate collection sump in each cell identified on plan MM/FBQ/PPC-DESID7A.	pH, EC, Temp	Monthly	In accordance with Environment Agency Guidance LFTGN02 (February 2003) unless otherwise agreed in writing with the Environment Agency.	None
	NH4-N, Cl, SO_4, Alk, BOD, COD, TON, TOC Filt, Na, K, Mg, Ca, Fe, Mn, Cd, Hg, Cr, Cu, Ni, Pb, Zn	Quarterly		None
	List 1 screen	Annually	In accordance with Appendix 6 of Environment Agency Guidance LFTGN01 (March 2003).	Any List I substance found above the MRV screening limits in the annual List I screening of leachate shall be incorporated into the quarterly monitoring regime unless otherwise agreed in writing with the Environment Agency.
Depth to base of monitoring well		Annually		

Table S4.5 Surface water – other monitoring requirements				
Emission point reference or source or description of point of measurement	**Parameter**	**Monitoring frequency**	**Monitoring standard or method**	**Other specifications**
Surface Water Monitoring Points as identified on plan DESID 11.	Temperature, DO, pH, EC, TSS, NH4-N, TON, TOC, BOD, COD, Cl.	Monthly	In accordance with Environment Agency Guidance LFTGN02 (February 2003) unless otherwise agreed in writing with the Environment Agency.	None

Table S4.6 Groundwater – other monitoring requirements				
Emission point reference or source or description of point of measurement	**Parameter**	**Monitoring frequency**	**Monitoring standard or method**	**Other specifications**
FB103, FB104, G, SLR2, BEL1, BEL2 and SLR3 as identified on drawing MMF/FBQ/PPC-DESID8A.	Water level, pH, EC, Temp, DO, Amm-N, Cl, COD	Monthly	In accordance with Environment Agency Guidance LFTGN02 (February 2003) unless otherwise agreed in writing with the Environment Agency.	Control levels: Amm-N 1.5mg/l Cl 150 mg/l
	Na, K, TOC FILT, Alk, Ca, Mn, Mg, Na, TON, Fe, Zn, Cd, Hg, Pb, Cr, Cu, Ni	Quarterly		Any List I substance found above the MRV screening limits in the annual List I screening of leachate required by Table S4.4 shall be incorporated into the quarterly monitoring regime for groundwater unless otherwise agreed in writing with the Environment Agency
	List I screens (PAH(EPA16); VOCs; Pesticides; Organotins).	Annually		

Schedule 5 - Reporting

Parameters, for which reports shall be made, in accordance with conditions of this permit, are listed below.

Table S5.1 Reporting of monitoring data

Parameter	Emission or monitoring point/reference	Reporting period	Period begins
Leachate levels As required by condition 3.6.1	Leachate collection sump in each cell identified on plan MM/FBQ/PPC-DESID7A.	Monthly	08/03/2007
Groundwater Parameters as required by condition 3.6.1	FB103, FB104, G, SLR2, BEL1, BEL2 and SLR3	Quarterly for all parameters monitored at a monthly or quarterly frequency. Annually for all parameters monitored at an annual frequency.	08/03/2007
Landfill gas lateral migration Parameters as required by condition 3.6.1	BEL1, BEL2, SLR2 and SLR3	Quarterly	08/03/2007
Other Landfill gas monitoring Parameters as required by condition 3.6.1	In waste monitoring boreholes FB106 to FB111	Quarterly	08/03/2007
Other leachate monitoring Parameters as required by condition 3.6.1 List 1 Screen	Leachate collection sump in each cell identified on plan MM/FBQ/PPC-DESID7A.	Quarterly for all parameters monitored at a monthly or quarterly frequency. Annually for all parameters monitored at an annual frequency.	08/03/2007
Other surface water monitoring Parameters as required by condition 3.6.1	Surface Water Monitoring Points as identified on plan DESID 11.	Quarterly	08/03/2007

Table S5.2: Annual production/treatment

Leachate: **Disposed of off site;** **Disposed of to any onsite effluent treatment plant;** **Recirculated into the waste mass.**	**Cubic metres/year**
Surface water and/ or groundwater: **Disposed of off site;** **Disposed of to any onsite effluent treatment plant.**	**Cubic metres/year**
Landfill gas: **combustion in flares;** **combustion in gas engines;** **Other methods of gas utilisation.**	**Normalised cubic metres/year**

Table S5.3 Performance Parameters			
Parameter	**Frequency of assessment**	**Annual total**	**Unit**
Energy used (including for leachate treatment)	Annually		MWh of electricity

Table S5.4 Reporting Forms		
Media/parameter	**Reporting Format**	**Date of Form**
Leachate	From leachate 1 or other reporting format to be agreed in writing with the Agency	08/03/2007
Groundwater	Form Groundwater 1 or other reporting format to be agreed in writing with the Agency	08/03/2007
Landfill gas	Form LFG 1 or other reporting format to be agreed in writing with the Agency	08/03/2007
Controlled water	Form Water 1 or other reporting format to be agreed in writing with the Agency	08/03/2007
Waste Return	Waste Return Form RATS2E	
Landfill topographical surveys and interpretation	Reporting format to be agreed in writing with the Agency	

Schedule 6 - Notification

This page outlines the information that the operator must provide.

Units of measurement used in information supplied under Part A and B requirements shall be appropriate to the circumstances of the emission. Where appropriate, a comparison should be made of actual emissions and authorised emission limits.

If any information is considered commercially confidential, it should be separated from non-confidential information, supplied on a separate sheet and accompanied by an application for commercial confidentiality under the provisions of the PPC Regulations.

Part A

Permit Number	
Name of operator	
Location of Installation	
Time and date of the detection	

(a) Notification requirements for any malfunction, breakdown or failure of equipment or techniques, accident, or fugitive emission which has caused, is causing or may cause significant pollution	
To be notified within 24 hours of detection	
Date and Time of the event	
Reference or description of the location of the event	
Description of where any release into the environment took place	
Substances(s) potentially released	
Best estimate of the quantity or rate of release of substances	
Measures taken, or intended to be taken, to stop any emission	
Description of the failure or accident.	

(b) Notification requirements for the breach of a limit	
To be notified within 24 hours of detection unless otherwise specified below	
Emission point reference/ source	
Parameter(s)	
Limit	
Measured value and uncertainty	
Date and time of monitoring	
Measures taken, or intended to be taken, to stop the emission	

(c) Notification requirements for the detection of any significant adverse environmental effect	
To be notified within 24 hours of detection	
Description of where the effect on the environment was detected	
Substances(s) detected	
Concentrations of substances detected	
Date of monitoring/sampling	

Part B to be supplied as soon as practicable

Any more accurate information on the matters for notification under Part A.	
Measures taken, or intended to be taken, to prevent a recurrence of the incident	
Measures taken, or intended to be taken, to rectify, limit or prevent any pollution of the environment which has been or may be caused by the emission	
The dates of any unauthorised emissions from the installation in the preceding 24 months.	

Name*	
Post	
Signature	
Date	

* authorised to sign on behalf of Marshalls Mono Limited.

Schedule 7 - Interpretation

"*Accident*" means an accident that may result in pollution.

"*Annually*" means once every Year.

"*Application*" means the application for this permit, together with any additional information supplied by the operator as part of the application and any response to a notice served under Schedule 4 to the PPC Regulations

"*Authorised Officer*" means any person authorised by the Agency under section 108(1) of The Environment Act 1995 to exercise, in accordance with the terms of any such authorisation, any power specified in Section 108(4) of that Act.

"*Background concentration*" means such concentration of that substance as is present in:

- For emissions to surface water, the surface water quality up-gradient of the site; or
- For emissions to sewer, the surface water quality up-gradient of the sewage treatment works discharge; or
- For emissions of landfill gas, the ground or air outside the site and not attributable to the site.

"*Construction Proposals*" means written information, at a level of detail appropriate to the complexity and pollution risk, on the design, specifications of materials selected, stability assessment (where relevant) and the construction quality assurance (CQA) programme in relation to the New Cell or Landfill Infrastructure.

"*CQA Validation Report*" means the final "as built" construction and engineering details of the New Cell or of the Landfill Infrastructure. It must provide a comprehensive record of the construction and must include, where relevant:

- The results of all testing required by the CQA programme - this must include the records of any failed tests with a written explanation, details of the remedial action taken, referenced to the appropriate secondary testing;
- Plans showing the location of all tests;
- "As-built" plans and sections of the works;
- Copies of the site engineer's daily records;
- Records of any problems or non-compliances and the solution applied;
- Any other site specific information considered relevant to proving the integrity of the New Cell or Landfill Infrastructure;
- Validation by a qualified person that all of the construction has been carried out in accordance with the Construction Proposals.

"*Fugitive emission*" means an emission to air, water or land from the activities which is not controlled by an emission or background concentration limit.

"*Groundwater Regulations*" means the Groundwater Regulations SI 1998 No. 2746, and words and expressions used in this permit which are also used in the Regulations shall have the same meanings as in those Regulations.

"*Landfill Infrastructure*" means any specified element of the:

- permanent capping;
- temporary capping (i.e. engineered temporary caps not cover materials);
- leachate abstraction systems;
- leachate transfer, treatment and storage systems;
- surface water drainage systems;
- leachate monitoring wells;
- groundwater monitoring boreholes;
- landfill gas monitoring boreholes;
- landfill gas management systems;

within the site.

"*Landfill Regulations*" means the Landfill (England and Wales) Regulations SI 2002 No. 1559, and words and expressions used in this permit which are also used in the Regulations shall have the same meanings as in those Regulations.

"*Land Protection Guidance*" means Agency guidance "H7 - Guidance on the protection of land under the PPC Regime: Application site report and site protection monitoring programme".

"*Liquids*" means any liquid other than leachate within the engineered landfill containment system.

"*LFTGN 05*" means Environment Agency Guidance for monitoring enclosed landfill gas flares, September 2004.

"*LFTGN 08*" means Environment Agency Guidance for monitoring landfill gas engines, September 2004.

"*New Cell*" means any new cell, part of a cell or other similar new area of the site where waste deposit is to commence after issue of this permit and can comprise:

- groundwater under-drainage system;
- permanent geophysical leak location system;
- leak detection layer;
- sub-grade;
- barriers;

- liners;
- leachate collection system;
- leachate abstraction system;
- separation bund/layer;
- cell or area surface water drainage system;
- side wall subgrade and containment systems;

for the New Cell.

"No impact" means that the change made to the construction process will not affect the agreed design criteria, specification or performance in a way that has a negative effect.

"notify without delay" and *"notified without delay"* means that a telephone call can be used, whereas all other reports and notifications must be supplied in writing, either electronically or on paper.

"PPC Regulations" means the Pollution, Prevention and Control (England and Wales) Regulations SI 2000 No.1973 and words and expressions used in this permit which are also used in the Regulations have the same meanings as in those Regulations.

"Quarter" means a calendar year quarter commencing on 1 January, 1 April, 1 July or 1 October.

"Relevant person" and *"relevant conviction"* shall have the meanings given to them in the Environmental Protection Act 1990

"Review of the Hydrogeological Risk Assessment" means a written review of the hydrogeological risk assessment included in the Application, together with any other parts of the Application that addressed the requirements of the Groundwater Regulations. The review shall assess whether the activities of disposal or tipping for the purpose of disposal of waste authorised by the permit continue to meet the requirements of the Groundwater Regulations

"Site Protection and Monitoring Programme" means a document which meets the requirements for Site Protection and Monitoring Programmes described in the Land Protection Guidance.

"Technically competent management" and *"technical competence"* shall have the meanings given to them in the Environmental Protection Act 1990.

"Waste code" means the six digit code referable to a type of waste in accordance with the List of Wastes (England) Regulations 2005, or List of Wastes (Wales) Regulations 2005, List of Wastes (Northern Ireland) Regulations 2005 (as amended), or The Special Waste Amendment (Scotland) Regulations 2004 as appropriate, and in relation to hazardous waste, includes the asterisk

"Year" means calendar year ending 31 December.

Where a minimum limit is set for any emission parameter, for example pH, reference to exceeding the limit shall mean that the parameter shall not be less than that limit.

Unless otherwise stated, any references in this permit to concentrations of substances in emissions into air means the standards included in Environment Agency Guidance for Monitoring Enclosed Landfill Gas Flares LFTGN 05 or Guidance for Monitoring Landfill Gas Engine Emissions LFTGN 08.

END OF PERMIT

Notice of variation and consolidation with introductory note

The Environmental Permitting (England & Wales) Regulations 2016

Waste Recycling Group (Central) Limited

Edwin Richards Quarry - Soil Treatment Centre
Portway Road
Rowley Regis
Warley
West Midlands
B65 9BT

Variation application number

EPR/HP3632RP/V002

Permit number

EPR/HP3632RP

Edwin Richards Quarry - Soil Treatment Centre
Permit number EPR/HP3632RP

Introductory note

This introductory note does not form a part of the notice

Under the Environmental Permitting (England & Wales) Regulations 2016 (schedule 5, part 1, paragraph 19) a variation may comprise a consolidated permit reflecting the variations and a notice specifying the variations included in that consolidated permit.

Schedule 1 of the notice specifies the conditions that have been varied and schedule 2 comprises a consolidated permit which reflects the variations being made. Only the variations specified in schedule 1 are subject to a right of appeal.

The operator has applied to vary the permit to add the handpicking of identifiable pieces of bonded asbestos from waste soil and to add waste code 19 12 07 (consisting only of untreated woodchip) to table S2.3 for the bioremediation process. The operator has confirmed that no crushing of hazardous waste occurs at the site and therefore crushing has been removed from table S1.1 and from the title of table S2.2. This permit authorises the storage of combustible waste and so we have varied it to include a standard condition that requires operators to take all appropriate measures to prevent fires on site and minimise the risk of pollution from them and, if required by us, to submit for approval a fire prevention plan that once approved must be implemented. We have also included improvement conditions to capture the operator's proposed works to contain drainage within the building.

The schedules specify the changes made to the permit.

The status log of a permit sets out the permitting history, including any changes to the permit reference number.

Status log of the permit		
Description	**Date**	**Comments**
Application EPR/HP3632RP/A001	Duly made 08/02/2016	Application for new permit for a waste soil treatment facility.
Additional information received response to schedule 5 notice	10/05/2016	Additional information, including; site drainage plans.
Additional information received response to schedule 5 notice and request for additional information.	23/06/2016	Additional information, including; confirmation of waste types and biopile monitoring parameters.
Additional information received response to schedule 5 notice	30/06/2016	Email confirming destination of uncontaminated surface water runoff.
Permit determined EPR/HP3632RP (PAS Billing ref. HP3632RP)	25/07/2016	Permit issued to Waste Recycling group (Central) Limited.
Application EPR/HP3632RP/V002 (variation and consolidation)	Duly made 16/11/17	Application to vary the permit to add hand picking of identifiable pieces of bonded asbestos from waste soil. Waste code 19 12 07 is also added to Table S2.3 for the bioremediation process. As part of this variation a consolidated permit has been issued.
Additional information received in response to Schedule 5 notice dated 15/01/18	29/01/18	Final Schedule 5 response received including pre-acceptance and acceptance procedures, waste receipt and depositing processes, measures in place to reduce dust and asbestos fibre emissions during

Status log of the permit		
Description	**Date**	**Comments**
		the storage and treatment process including dampening down and handling procedures, cross contamination controls, contaminant testing undertaken on the soils post-treatment, asbestos sampling procedures and locations, actions to be taken if exceedances occur, waste classification details, operating techniques document for the waste wood storage and details of further treatment proposed.
Variation determined EPR/HP3632RP (PAS Billing ref: LP3430JC)	26/02/18	Varied permit issued.

End of introductory note

Notice of variation and consolidation

The Environmental Permitting (England and Wales) Regulations 2016

The Environment Agency in exercise of its powers under regulation 20 of the Environmental Permitting (England and Wales) Regulations 2016 varies

Permit number

EPR/HP3632RP

Issued to

Waste Recycling Group (Central) Limited ("the operator")

whose registered office is

Ground Floor West
900 Pavilion Drive
Northampton Business Park
Northampton
NN4 7RG

company registration number 04000033

to operate a regulated facility at

Edwin Richards Quarry - Soil Treatment Centre
Portway Road
Rowley Regis
Warley
West Midlands
B65 9BT

to the extent set out in the schedules.

The notice shall take effect from 26/02/2018

Name	Date
Dominiqua Drakeford-Allen	**26/02/2018**

Authorised on behalf of the Environment Agency

Schedule 1

Only conditions 2.3.4, table S1.1, table S1.2, table S2.2, table S2.3, table S3.3, table S4.1, table S4.4 and Schedule 6 have been varied by the consolidated permit EPR/HP3632RP

The following conditions were varied as a result of the application made by the operator:

- Condition 2.3.4 is amended to add reference to the additional waste table S2.6.
- Table S1.1, as referenced in condition 2.1.1 is amended to remove crushing of hazardous waste from the S5.3A(1)(a)(ii) activity for the physical treatment of hazardous waste in table S2.2, each activity undertaken at the installation has been clarified in bold, the asbestos handpicking activity has been added, a restriction has been added to the bioremediation activity S5.3 A(1)(a)(i) to prevent the treatment of wastes containing hazardous levels of asbestos, the storage of asbestos contaminated soils prior to treatment has been added, a reference to table S2.3 and table S2.5 has been added and the storage of asbestos waste removed from the soil has been added as a Directly Associated Activity.
- Table S1.2, as referenced in conditions 2.3.1 and 2.3.2 is amended to add additional Operating Techniques for the asbestos handpicking activity and the quantity of waste wood added to the biopiles. The 17 06 05* waste code that was referenced in the existing Operating Techniques documents has been excluded from this document as this waste code was not permitted in the permit issued and the woody waste limit of < 1% of the biopiles volume has also been excluded to reflect the revised limit in the new Operating Techniques document.
- Table S2.2, as referenced in condition 2.1.1 is amended to remove reference to crushing activities from the table title.
- Table S2.3, as referenced in condition 2.3.4 is amended to add additional waste code 19 12 07. This table is also amended to add to an exclusion to prevent the treatment of wastes contaminated with asbestos in the bioremediation activity.
- Table S3.3, as referenced in conditions 3.5.1 and 3.5.4 is amended to add air testing for asbestos fibres during the handpicking works.
- Table S4.1, as referenced in condition 4.2.3 is amended to add a reporting requirement for the asbestos fibre air testing that is undertaken.
- Table S4.4, as referenced in conditions 4.2.2 and 4.2.3 is amended to add a reporting form for the asbestos fibre air testing reporting.
- Schedule 6, as referenced in condition 4.4.1 is amended to add the definition of “building”.

The following conditions are added as a result of an Environment Agency initiated variation:

- Condition 3.7.1 is added to include the requirements for fire prevention.
- Condition 3.7.2 is added to enable the Environment Agency to request a fire prevention plan.

The following conditions are added as a result of the application made by the operator:

- Condition 2.5.1, and Table S1.4 referenced through this condition, is added to require the improvements listed.
- Condition 2.5.1 is added to require notification to the Environment Agency on completion of each improvement.
- Table S2.6, as referenced in condition 2.3.4 is added to include the waste types and maximum quantity of waste accepted under the asbestos hand picking activity.

Schedule 2 – consolidated permit

Consolidated permit issued as a separate document.

Permit

The Environmental Permitting (England and Wales) Regulations 2016

Permit number

EPR/HP3632RP

This is the consolidated permit referred to in the variation and consolidation notice for application EPR/HP3632RP/V002 authorising,

Waste Recycling Group (Central) Limited ("the operator"),

whose registered office is

Ground Floor West
900 Pavilion Drive
Northampton Business Park
Northampton
NN4 7RG

company registration number 04000033

to operate an installation at

Edwin Richards Quarry - Soil Treatment Centre
Portway Road
Rowley Regis
Warley
West Midlands
B65 9BT

to the extent authorised by and subject to the conditions of this permit.

Name	Date
Dominiqua Drakeford-Allen	**26/02/2018**

Authorised on behalf of the Environment Agency

Conditions

1 Management

1.1 General management

1.1.1 The operator shall manage and operate the activities:

(a) in accordance with a written management system that identifies and minimises risks of pollution, including those arising from operations, maintenance, accidents, incidents, non-conformances, closure and those drawn to the attention of the operator as a result of complaints; and

(b) using sufficient competent persons and resources.

1.1.2 Records demonstrating compliance with condition 1.1.1 shall be maintained.

1.1.3 Any person having duties that are or may be affected by the matters set out in this permit shall have convenient access to a copy of it kept at or near the place where those duties are carried out.

1.1.4 The operator shall comply with the requirements of an approved competence scheme.

1.2 Energy efficiency

1.2.1 The operator shall:

(a) take appropriate measures to ensure that energy is used efficiently in the activities;

(b) review and record at least every four years whether there are suitable opportunities to improve the energy efficiency of the activities; and

(c) take any further appropriate measures identified by a review.

1.3 Efficient use of raw materials

1.3.1 The operator shall:

(a) take appropriate measures to ensure that raw materials and water are used efficiently in the activities;

(b) maintain records of raw materials and water used in the activities;

(c) review and record at least every four years whether there are suitable alternative materials that could reduce environmental impact or opportunities to improve the efficiency of raw material and water use; and

(d) take any further appropriate measures identified by a review.

1.4 Avoidance, recovery and disposal of wastes produced by the activities

1.4.1 The operator shall take appropriate measures to ensure that:

(a) the waste hierarchy referred to in Article 4 of the Waste Framework Directive is applied to the generation of waste by the activities; and

(b) any waste generated by the activities is treated in accordance with the waste hierarchy referred to in Article 4 of the Waste Framework Directive; and

(c) where disposal is necessary, this is undertaken in a manner which minimises its impact on the environment.

1.4.2 The operator shall review and record at least every four years whether changes to those measures should be made and take any further appropriate measures identified by a review.

2 Operations

2.1 Permitted activities

2.1.1 The operator is only authorised to carry out the activities specified in schedule 1 table S1.1 (the "activities").

2.1.2 Waste authorised by this permit shall be clearly distinguished from any other waste on the site.

2.2 The site

2.2.1 The activities shall not extend beyond the site, being the land shown edged in green on the site plan at schedule 7 to this permit.

2.3 Operating techniques

2.3.1 The activities shall, subject to the conditions of this permit, be operated using the techniques and in the manner described in the documentation specified in schedule 1, table S1.2, unless otherwise agreed in writing by the Environment Agency.

2.3.2 If notified by the Environment Agency that the activities are giving rise to pollution, the operator shall submit to the Environment Agency for approval within the period specified, a revision of any plan or other documentation ("plan") specified in schedule 1, table S1.2 or otherwise required under this permit which identifies and minimises the risks of pollution relevant to that plan , and shall implement the approved revised plan in place of the original from the date of approval, unless otherwise agreed in writing by the Environment Agency.

2.3.3 Any raw materials or fuels listed in schedule 2 table S2.1 shall conform to the specifications set out in that table.

2.3.4 Waste shall only be accepted if:

(a) it is of a type and quantity listed in schedule 2 tables S2.2, S2.3, S2.4, S2.5 and S2.6; and

(b) it conforms to the description in the documentation supplied by the producer and holder.

2.3.5 The operator shall ensure that where waste produced by the activities is sent to a relevant waste operation, that operation is provided with the following information, prior to the receipt of the waste:

(a) the nature of the process producing the waste;

(b) the composition of the waste;

(c) the handling requirements of the waste;

(d) the hazardous property associated with the waste, if applicable; and

(e) the waste code of the waste.

2.3.6 The operator shall ensure that where waste produced by the activities is sent to a landfill site, it meets the waste acceptance criteria for that landfill.

Hazardous waste storage and treatment

2.3.7 Hazardous waste shall not be mixed, either with a different category of hazardous waste or with other waste, substances or materials, unless it is authorised by schedule 1 table S1.1 and appropriate measures are taken.

2.4 Pre-operational conditions

2.4.1 The activities shall not be brought into operation until the measures specified in schedule 1 table S1.3 have been completed.

2.5 Improvement programme

2.5.1 The operator shall complete the improvements specified in schedule 1 table S1.4 by the date specified in that table unless otherwise agreed in writing by the Environment Agency.

2.5.2 Except in the case of an improvement which consists only of a submission to the Environment Agency, the operator shall notify the Environment Agency within 14 days of completion of each improvement.

3 Emissions and monitoring

3.1 Emissions to water, air or land

3.1.1 There shall be no point source emissions to water, air or land except from the sources and emission points listed in schedule 3 tables S3.1 and S3.2.

3.1.2 The limits given in schedule 3 shall not be exceeded.

3.1.3 Periodic monitoring shall be carried out at least once every 5 years for groundwater and 10 years for soil, unless such monitoring is based on a systematic appraisal of the risk of contamination.

3.2 Emissions of substances not controlled by emission limits

3.2.1 Emissions of substances not controlled by emission limits (excluding odour) shall not cause pollution. The operator shall not be taken to have breached this condition if appropriate measures, including, but not limited to, those specified in any approved emissions management plan, have been taken to prevent or where that is not practicable, to minimise, those emissions.

3.2.2 The operator shall:

(a) if notified by the Environment Agency that the activities are giving rise to pollution, submit to the Environment Agency for approval within the period specified, an emissions management plan which identifies and minimises the risks of pollution from emissions of substances not controlled by emission limits;

(b) implement the approved emissions management plan, from the date of approval, unless otherwise agreed in writing by the Environment Agency.

3.2.3 All liquids in containers, whose emission to water or land could cause pollution, shall be provided with secondary containment, unless the operator has used other appropriate measures to prevent or where that is not practicable, to minimise, leakage and spillage from the primary container.

3.3 Odour

3.3.1 Emissions from the activities shall be free from odour at levels likely to cause pollution outside the site, as perceived by an authorised officer of the Environment Agency, unless the operator has used appropriate measures, including, but not limited to, those specified in any approved odour management plan, to prevent or where that is not practicable to minimise the odour.

3.3.2 The operator shall:

(a) if notified by the Environment Agency that the activities are giving rise to pollution outside the site due to odour, submit to the Environment Agency for approval within the period specified, an odour management plan which identifies and minimises the risks of pollution from odour;

(b) implement the approved odour management plan, from the date of approval, unless otherwise agreed in writing by the Environment Agency.

3.4 Noise and vibration

3.4.1 Emissions from the activities shall be free from noise and vibration at levels likely to cause pollution outside the site, as perceived by an authorised officer of the Environment Agency, unless the operator has used appropriate measures, including, but not limited to, those specified in any approved noise and vibration management plan to prevent or where that is not practicable to minimise the noise and vibration.

3.4.2 The operator shall:

(a) if notified by the Environment Agency that the activities are giving rise to pollution outside the site due to noise and vibration, submit to the Environment Agency for approval within the period specified, a noise and vibration management plan which identifies and minimises the risks of pollution from noise and vibration;

(b) implement the approved noise and vibration management plan, from the date of approval, unless otherwise agreed in writing by the Environment Agency.

3.5 Monitoring

3.5.1 The operator shall, unless otherwise agreed in writing by the Environment Agency, undertake the monitoring specified in the following tables in schedule 3 to this permit:

(a) point source emissions specified in tables S3.1 and S3.2;

(b) process monitoring specified in table S3.3;

3.5.2 The operator shall maintain records of all monitoring required by this permit including records of the taking and analysis of samples, instrument measurements (periodic and continual), calibrations, examinations, tests and surveys and any assessment or evaluation made on the basis of such data.

3.5.3 Monitoring equipment, techniques, personnel and organisations employed for the emissions monitoring programme and the environmental or other monitoring specified in condition 3.5.1 shall have either MCERTS certification or MCERTS accreditation (as appropriate), where available, unless otherwise agreed in writing by the Environment Agency.

3.5.4 Permanent means of access shall be provided to enable sampling/monitoring to be carried out in relation to the emission points specified in schedule 3 tables S3.1, S3.2 and S3.3 unless otherwise agreed in writing by the Environment Agency.

3.6 Pests

3.6.1 The activities shall not give rise to the presence of pests which are likely to cause pollution, hazard or annoyance outside the boundary of the site. The operator shall not be taken to have breached this condition if appropriate measures, including, but not limited to, those specified in any approved pests management plan, have been taken to prevent or where that is not practicable, to minimise the presence of pests on the site.

3.6.2 The operator shall:

(a) if notified by the Environment Agency, submit to the Environment Agency for approval within the period specified, a pests management plan which identifies and minimises risks of pollution from pests;

(b) implement the pests management plan, from the date of approval, unless otherwise agreed in writing by the Environment Agency.

3.7 Fire prevention

3.7.1 The operator shall take all appropriate measures to prevent fires on site and minimise the risk of pollution from them including, but not limited to, those specified in any approved fire prevention plan.

3.7.2 The operator shall:

(a) if notified by the Environment Agency that the activities are giving rise to a risk of fire, submit to the Environment Agency for approval within the period specified, a fire prevention plan which prevents fires and minimises the risk of pollution from fires;

(b) implement the fire prevention plan, from the date of approval, unless otherwise agreed in writing by the Environment Agency.

4 Information

4.1 Records

4.1.1 All records required to be made by this permit shall:

(a) be legible;

(b) be made as soon as reasonably practicable;

(c) if amended, be amended in such a way that the original and any subsequent amendments remain legible, or are capable of retrieval; and

(d) be retained, unless otherwise agreed in writing by the Environment Agency, for at least 6 years from the date when the records were made, or in the case of the following records until permit surrender:

(i) off-site environmental effects; and

(ii) matters which affect the condition of the land and groundwater.

4.1.2 The operator shall keep on site all records, plans and the management system required to be maintained by this permit, unless otherwise agreed in writing by the Environment Agency.

4.2 Reporting

4.2.1 The operator shall send all reports and notifications required by the permit to the Environment Agency using the contact details supplied in writing by the Environment Agency.

4.2.2 A report or reports on the performance of the activities over the previous year shall be submitted to the Environment Agency by 31 January (or other date agreed in writing by the Environment Agency) each year. The report(s) shall include as a minimum:

(a) a review of the results of the monitoring and assessment carried out in accordance with the permit including an interpretive review of that data;

(b) the annual production/treatment data set out in schedule 4 table S4.2; and

(c) the performance parameters set out in schedule 4 table S4.3 using the forms specified in table S4.4 of that schedule.

4.2.3 Within 28 days of the end of the reporting period the operator shall, unless otherwise agreed in writing by the Environment Agency, submit reports of the monitoring and assessment carried out in accordance with the conditions of this permit, as follows:

(a) in respect of the parameters and emission points specified in schedule 4 table S4.1;

(b) for the reporting periods specified in schedule 4 table S4.1 and using the forms specified in schedule 4 table S4.4; and

(c) giving the information from such results and assessments as may be required by the forms specified in those tables.

4.2.4 The operator shall, unless notice under this condition has been served within the preceding four years, submit to the Environment Agency, within six months of receipt of a written notice, a report assessing whether there are other appropriate measures that could be taken to prevent, or where that is not practicable, to minimise pollution.

4.2.5 Within 1 month of the end of each quarter, the operator shall submit to the Environment Agency using the form made available for the purpose, the information specified on the form relating to the site and the waste accepted and removed from it during the previous quarter.

4.3 Notifications

4.3.1 In the event:

(a) that the operation of the activities gives rise to an incident or accident which significantly affects or may significantly affect the environment, the operator must immediately—

(i) inform the Environment Agency,

(ii) take the measures necessary to limit the environmental consequences of such an incident or accident, and

(iii) take the measures necessary to prevent further possible incidents or accidents;

(b) of a breach of any permit condition the operator must immediately—

(i) inform the Environment Agency, and

(ii) take the measures necessary to ensure that compliance is restored within the shortest possible time;

(c) of a breach of permit condition which poses an immediate danger to human health or threatens to cause an immediate significant adverse effect on the environment, the operator must immediately suspend the operation of the activities or the relevant part of it until compliance with the permit conditions has been restored.

4.3.2 Any information provided under condition 4.3.1(a)(i), or 4.3.1 (b)(i) where the information relates to the breach of a limit specified in the permit, shall be confirmed by sending the information listed in schedule 5 to this permit within the time period specified in that schedule.

4.3.3 Where the Environment Agency has requested in writing that it shall be notified when the operator is to undertake monitoring and/or spot sampling, the operator shall inform the Environment Agency when the relevant monitoring and/or spot sampling is to take place. The operator shall provide this information to the Environment Agency at least 14 days before the date the monitoring is to be undertaken.

4.3.4 The Environment Agency shall be notified within 14 days of the occurrence of the following matters, except where such disclosure is prohibited by Stock Exchange rules:

Where the operator is a registered company:

(a) any change in the operator's trading name, registered name or registered office address; and

(b) any steps taken with a view to the operator going into administration, entering into a company voluntary arrangement or being wound up.

Where the operator is a corporate body other than a registered company:

(a) any change in the operator's name or address; and

(b) any steps taken with a view to the dissolution of the operator.

In any other case:

(a) the death of any of the named operators (where the operator consists of more than one named individual);

(b) any change in the operator's name(s) or address(es); and

(c) any steps taken with a view to the operator, or any one of them, going into bankruptcy, entering into a composition or arrangement with creditors, or, in the case of them being in a partnership, dissolving the partnership.

4.3.5 Where the operator proposes to make a change in the nature or functioning, or an extension of the activities, which may have consequences for the environment and the change is not otherwise the subject of an application for approval under the Regulations or this permit:

(a) the Environment Agency shall be notified at least 14 days before making the change; and

(b) the notification shall contain a description of the proposed change in operation.

4.3.6 The Environment Agency shall be given at least 14 days notice before implementation of any part of the site closure plan.

4.4 Interpretation

4.4.1 In this permit the expressions listed in schedule 6 shall have the meaning given in that schedule.

4.4.2 In this permit references to reports and notifications mean written reports and notifications, except where reference is made to notification being made "immediately", in which case it may be provided by telephone.

Schedule 1 – Operations

Table S1.1 activities		
Activity listed in Schedule 1 of the EP Regulations	**Description of specified activity and WFD Annex I and II operations**	**Limits of specified activity and waste types**
S5.3A(1)(a)(ii)	**Physical treatment of hazardous waste** Disposal or recovery of hazardous waste with a capacity exceeding 10 tonnes per day involving physico-chemical treatment **D9:** Physico-chemical treatment resulting in final compounds or mixtures which are discarded by any of the operations numbered D1 to D12	From receipt of hazardous waste to despatch for other on-site operations or off-site disposal. Physical treatment consisting of sorting, separation and screening of hazardous waste. The hazardous waste specified in table S2.2
S5.3A(1)(a)(ii)	**Asbestos removal from soils** Disposal or recovery of hazardous waste with a capacity exceeding 10 tonnes per day involving physico-chemical treatment **D9:** Physico-chemical treatment resulting in final compounds or mixtures which are discarded by any of the operations numbered D1 to D12	From receipt of hazardous waste through to storage of treated waste prior to being subject to bioremediation or sent off-site for disposal. Treatment consisting only of hand picking of identifiable pieces of bonded asbestos from waste soils in a dedicated enclosed picking line. All treatment and storage shall take place on an impermeable surface with a sealed drainage system within the building (labelled as 'dust shed') as shown on drawing number 100993 – Asbestos DWG1 dated January 2018. Waste subject to this process shall only be contaminated with asbestos alone or in combination with hydrocarbons. Asbestos removed from the soil shall be double-bagged and stored in a sealed locked skip.

Table S1.1 activities		
Activity listed in Schedule 1 of the EP Regulations	**Description of specified activity and WFD Annex I and II operations**	**Limits of specified activity and waste types**
		Subject to any other requirements of this permit wastes shall be stored for no longer than 1 year prior to disposal. Waste types and quantities as specified in Table S2.6.
S5.4A(1)(a)(ii)	**Physical treatment of non-hazardous waste** Disposal of non-hazardous waste with a capacity exceeding 50 tonnes per day (or 100 tonnes per day if the only waste treatment activity is anaerobic digestion) involving physico-chemical treatment **D9**: Physico-chemical treatment resulting in final compounds or mixtures which are discarded by any of the operations numbered D1 to D12	From receipt of non-hazardous waste to despatch for other on-site operations or off-site disposal. Physical treatment consisting of sorting, separation, screening and crushing of non-hazardous waste. Temporary storage of non-hazardous waste prior to further treatment on site or off-site disposal. The non-hazardous wastes specified in table S2.2
S5.3 A(1)(a)(i)	**Bioremediation of hazardous waste** Disposal or recovery of hazardous waste with a capacity exceeding 10 tonnes per day involving biological treatment **D8:** Biological treatment resulting in final compounds or mixtures which are discarded by any of the operations numbered D1 to D12	Bioremediation process for hazardous waste. Temporary storage of hazardous waste following bioremediation, pending further treatment on-site or off-site disposal. The hazardous waste specified in table S2.3
S5.4A(1)(b)(i)	**Bioremediation of non-hazardous waste** Recovery or a mix of recovery and disposal of non-hazardous waste with a capacity exceeding 75 tonnes per day involving biological treatment **D8:** Biological treatment resulting in final compounds or mixtures which are discarded by any of the operations numbered D1 to D12	Bioremediation process for non-hazardous waste Temporary storage of non-hazardous waste following bioremediation, pending further treatment on-site or off-site disposal. The non-hazardous wastes specified in table S2.3
S5.4A(1)(a)(ii)	**De-watering of non-hazardous waste sludges and silts**	De-watering of non-hazardous waste sludges and silts

Table S1.1 activities		
Activity listed in Schedule 1 of the EP Regulations	**Description of specified activity and WFD Annex I and II operations**	**Limits of specified activity and waste types**
	Disposal of non-hazardous waste with a capacity exceeding 50 tonnes per day (or 100 tonnes per day if the only waste treatment activity is anaerobic digestion) involving physico-chemical treatment **D9:** Physico-chemical treatment resulting in final compounds or mixtures which are discarded by any of the operations numbered D1 to D12	Temporary storage of non-hazardous waste following treatment, pending further treatment or disposal. Wastes as specified in table S2.4
S5.4A(1)(a)(ii)	**Solidification process for non-hazardous sludges and silts** Disposal of non-hazardous waste with a capacity exceeding 50 tonnes per day (or 100 tonnes per day if the only waste treatment activity is anaerobic digestion) involving physico-chemical treatment **D9**: Physico-chemical treatment resulting in final compounds or mixtures which are discarded by any of the operations numbered D1 to D12	Solidification process for non-hazardous sludges and silts Temporary storage of non-hazardous waste following treatment, pending further treatment or disposal. Wastes as specified in table S2.4
S5.6 A(1)(a)	**Temporary storage of untreated hazardous waste pending further treatment or off-site disposal** The temporary storage of hazardous waste in a facility with a total capacity exceeding 50 tonnes pending any of the activities listed in sections 5.1, 5.2 and 5.3. **D15:** Storage pending any of the operations numbered D1 to D14 (excluding temporary storage, pending collection, on the site where it is produced)	Temporary storage of untreated hazardous waste pending further treatment or off-site disposal. Asbestos contaminated soil should be stored on an impermeable surface with a sealed drainage system within the building as shown on drawing number 100993 – Asbestos DWG1 dated January 2018 (labelled as 'dust shed') in a way that minimises asbestos fibre emissions. Subject to any other requirements of this permit wastes shall be stored for no longer than 1 year prior to disposal. Hazardous wastes as specified in table S2.2 table S2.3 and table S2.6.

Table S1.1 activities		
Activity listed in Schedule 1 of the EP Regulations	**Description of specified activity and WFD Annex I and II operations**	**Limits of specified activity and waste types**
Directly Associated Activity		
Fuel storage	Storage of diesel.	From receipt of fuel to use on-site for power generation
Water storage	Collection and storage of process water	From collection of process water to re-use within the facility or discharge to foul sewer.
Waste storage	Temporary storage of non-hazardous waste **D15:** Storage pending any of the operations numbered D1 to D14 (excluding temporary storage, pending collection, on the site where it is produced)	From the receipt of non-hazardous waste to despatch for on-site operations or off-site disposal. Includes temporary storage of non-hazardous wastes not requiring further treatment prior to disposal. The total amount of this waste stored at the site shall not exceed 100,000 tonnes at any one time. Wastes as specified in table S2.5.
Waste storage	**Temporary storage of asbestos waste** **D15:** Storage pending any of the operations numbered D1 to D14 (excluding temporary storage, pending collection, on the site where it is produced)	Asbestos removed from the soil shall be double-bagged and stored in a sealed locked skip. Subject to any other requirements of this permit wastes shall be stored for no longer than 1 year prior to disposal.
Raw material storage	Temporary storage of raw materials including solidifying agents such as ash prior to use in the solidification process.	From the receipt of raw materials to despatch for use within the facility.

Table S1.2 Operating techniques		
Description	**Parts**	**Date Received**
Application EPR/HP3632RP/A001	Application forms B2 and B3 and referenced supporting information. Excluding waste code 17 06 05* for the Soil Treatment Centre Waste Types in Table 3.3 (Page 36) dated 27 November 2015. Excluding the woody waste limit of < 1% of the biopiles volume.	Duly Made 08/02/2016

Table S1.2 Operating techniques		
Description	**Parts**	**Date Received**
Response to schedule 5 notice EPR/HP3632RP/A001	All parts, including; hazardous and non-hazardous waste treatment and storage procedures. Excluding waste code 17 06 05* for the Soil Treatment Centre Waste Types Accepted for Physical Treatment in Table A1 (Page 11) of the Schedule 5 Response dated 10 May 2016.	10/05/2016
Response to schedule 5 notice and request for additional information. EPR/HP3632RP/A001	All parts, including; confirmation of biopile performance parameter monitoring regime.	23/06/2016
Response to schedule 5 notice EPR/HP3632RP/A001	Confirmation of surface water drainage destination.	30/06/2016
Application EPR/HP3632RP/V002	Application form C3 section 3a – technical standards and referenced supporting information.	Duly Made 16/11/17
Response to Schedule 5 Notice dated 15/01/18	All parts document reference: 3483/L/007/05.	29/01/18

Table S1.3 Pre-operational measures	
Reference	**Pre-operational measures**
1	At least three calendar months (or any other date as agreed with the Environment Agency) before the start of commissioning the operator shall submit a written report to the Environment Agency for approval. The report shall include (but not be limited to) the following: • a detailed site drainage plan, reflecting the proposed drainage system and showing the location of all discharge points • the design specification of the containment infrastructure be installed as part of the drainage system, including all sub-surface structures and equipment • an inspection and maintenance programme for the containment infrastructure and equipment at the site • details of any abatement equipment and pollution control devices to be installed as part of the drainage system • a proposed timetable for completion of any additional improvement works No site operations shall commence or waste accepted at the facility unless the Environment Agency has given prior written permission under this condition.

Table S1.4 Improvement programme requirements		
Reference	**Requirement**	**Date**
IP1	The Operator shall complete the site drainage works within the building (labelled as 'dust shed'), as detailed in point 3 of the Schedule 5 response dated 29/01/18, to: • seal the redundant manholes; • install kerbing at both the entrance and exit; and • install a drainage sump to collect any excess runoff generated from the spraying of water used to control dust and asbestos fibres. Following completion of these works the operator shall submit a revised site drainage plan to the Environment Agency.	3 months from date of issue

Schedule 2 – Waste types, raw materials and fuels

Table S2.1 Raw materials and fuels	
Raw materials and fuel description	**Specification**
--	--

Table S2.2 Permitted waste types and quantities for physical treatment of waste	
Maximum quantity	**In total no more than 29,999 tonnes per annum of hazardous waste and no more than 150,000 tonnes per annum of non-hazardous waste will be accepted for treatment at the site.** **Waste hazardous properties HP4 to HP7, HP14**
Waste code	**Description**
01	**Wastes resulting from exploration, mining, quarrying, and physical and chemical treatment of minerals**
01 04	**wastes from physical and chemical processing of non-metalliferous minerals**
01 04 09	waste sand and clays
01 05	**drilling muds and other drilling wastes**
01 05 04	freshwater drilling muds and wastes
01 05 05*	oil-containing drilling muds and wastes
01 05 06*	drilling muds and other drilling wastes containing hazardous substances
05	**Wastes from petroleum refining, natural gas purification and pyrolytic treatment of coal**
05 01	**wastes from petroleum refining**
05 01 05*	oil spills
05 01 15*	spent filter clays
10	**Wastes from thermal processes**
10 09	**wastes from casting of ferrous pieces**
10 09 06	casting cores and moulds which have not undergone pouring other than those mentioned in 10 09 05
10 09 08	casting cores and moulds which have undergone pouring other than those mentioned in 10 09 07
10 10	**wastes from casting of non-ferrous pieces**
10 10 06	casting cores and moulds which have not undergone pouring, other than those mentioned in 10 10 05
10 10 08	casting cores and moulds which have undergone pouring, other than those mentioned in 10 10 07
13	**Oil wastes and wastes of liquid fuels (except edible oils, and those in chapters 05, 12 and 19)**
13 05	**oil/water separator contents**
13 05 01*	solids from grit chambers and oil/water separators
13 05 02*	sludges from oil/water separators
13 05 03*	interceptor sludges

Table S2.2 Permitted waste types and quantities for physical treatment of waste	
Maximum quantity	**In total no more than 29,999 tonnes per annum of hazardous waste and no more than 150,000 tonnes per annum of non-hazardous waste will be accepted for treatment at the site.** **Waste hazardous properties HP4 to HP7, HP14**
Waste code	**Description**
13 05 08*	mixtures of wastes from grit chambers and oil/water separators
17	**Construction and demolition wastes (including excavated soil from contaminated sites)**
17 02	**wood, glass and plastic**
17 02 01	wood
17 05	**soil (including excavated soil from contaminated sites), stones and dredging spoil**
17 05 03*	soil and stones containing hazardous substances
17 05 04	soil and stones other than those mentioned in 17 05 03
17 05 05*	dredging spoil containing hazardous substances
17 05 06	dredging spoil other than those mentioned in 17 05 05
17 05 07*	track ballast containing hazardous substances
17 05 08	track ballast other than those mentioned in 17 05 07
17 09	**other construction and demolition wastes**
17 09 03*	other construction and demolition wastes (including mixed wastes) containing hazardous substances
17 09 04	mixed construction and demolition wastes other than those mentioned in 17 09 01, 17 09 02 and 17 09 03
19	**Wastes from waste management facilities, off-site waste water treatment plants and the preparation of water intended for human consumption and water for industrial use**
19 02	**wastes from physico/chemical treatments of waste (including dechromatation, decyanidation, neutralisation)**
19 02 03	premixed wastes composed only of non-hazardous wastes
19 02 04*	premixed wastes composed of at least one hazardous waste – wastes suitable for biological treatment only
19 02 05*	sludges from physico/chemical treatment containing hazardous substances – wastes suitable for biological treatment only
19 02 06	sludges from physico/chemical treatment other than those mentioned in 19 02 05 – wastes suitable for biological treatment only
19 02 11*	other wastes containing hazardous substances – wastes suitable for biological treatment only
19 05	**wastes from aerobic treatment of solid wastes**
19 05 03	off-specification compost
19 08	**wastes from waste water treatment plants not otherwise specified**
19 08 01	screenings
19 08 02	waste from desanding
19 08 13*	sludges containing hazardous substances from other treatment of industrial waste water

Table S2.2 Permitted waste types and quantities for physical treatment of waste	
Maximum quantity	**In total no more than 29,999 tonnes per annum of hazardous waste and no more than 150,000 tonnes per annum of non-hazardous waste will be accepted for treatment at the site.** **Waste hazardous properties HP4 to HP7, HP14**
Waste code	**Description**
19 08 14	sludges from other treatment of industrial waste water other than those mentioned in 19 08 13
19 13	**wastes from soil and groundwater remediation**
19 13 01*	solid wastes from soil remediation containing hazardous substances
19 13 02	solid wastes from soil remediation other than those mentioned in 19 13 01
19 13 03*	sludges from soil remediation containing hazardous substances
19 13 04	sludges from soil remediation other than those mentioned in 19 13 03
20	**Municipal wastes (household waste and similar commercial, industrial and institutional wastes) including separately collected fractions**
20 01	**separately collected fractions (except 15 01)**
20 01 38	wood other than that mentioned in 20 01 37
20 02	**garden and park wastes (including cemetery waste)**
20 02 01	biodegradable waste
20 02 02	soil and stones
20 03	**other municipal wastes**
20 03 03	street-cleaning residues

Table S2.3 Permitted waste types and quantities for treatment in the bioremediation process	
Maximum quantity	**In total no more than 29,999 tonnes per annum of hazardous waste and no more than 150,000 tonnes per annum of non-hazardous waste will be accepted for treatment at the site.** **Waste hazardous properties HP4 to HP7, HP11 and HP14**
Exclusions	**Wastes having any of the following characteristics shall not be accepted:** **Waste containing asbestos**
Waste code	**Description**
01	**Wastes resulting from exploration, mining, quarrying, and physical and chemical treatment of minerals**
01 04	**wastes from physical and chemical processing of non-metalliferous minerals**
01 04 09	waste sand and clays
01 05	**drilling muds and other drilling wastes**
01 05 04	freshwater drilling muds and wastes
01 05 05*	oil-containing drilling muds and wastes
01 05 06*	drilling muds and other drilling wastes containing hazardous substances
05	**Wastes from petroleum refining, natural gas purification and pyrolytic treatment of coal**
05 01	**wastes from petroleum refining**
05 01 05*	oil spills
05 01 15*	spent filter clays

Table S2.3 Permitted waste types and quantities for treatment in the bioremediation process	
Maximum quantity	**In total no more than 29,999 tonnes per annum of hazardous waste and no more than 150,000 tonnes per annum of non-hazardous waste will be accepted for treatment at the site.** **Waste hazardous properties HP4 to HP7, HP11 and HP14**
Exclusions	**Wastes having any of the following characteristics shall not be accepted:** **Waste containing asbestos**
Waste code	**Description**
13	**Oil wastes and wastes of liquid fuels (except edible oils, and those in chapters 05, 12 and 19)**
13 05	**oil/water separator contents**
13 05 01*	solids from grit chambers and oil/water separators
13 05 02*	sludges from oil/water separators
13 05 03*	interceptor sludges
13 05 08*	mixtures of wastes from grit chambers and oil/water separators
17	**Construction and demolition wastes (including excavated soil from contaminated sites)**
17 02	**wood, glass and plastic**
17 02 01	wood
17 05	**soil (including excavated soil from contaminated sites), stones and dredging spoil**
17 05 03*	soil and stones containing hazardous substances
17 05 04	soil and stones other than those mentioned in 17 05 03
17 05 05*	dredging spoil containing hazardous substances
17 05 06	dredging spoil other than those mentioned in 17 05 05
17 05 07*	track ballast containing hazardous substances
17 05 08	track ballast other than those mentioned in 17 05 07
19	**Wastes from waste management facilities, off-site waste water treatment plants and the preparation of water intended for human consumption and water for industrial use**
19 02	**wastes from physico/chemical treatments of waste (including dechromatation, decyanidation, neutralisation)**
19 02 03	premixed wastes composed only of non-hazardous wastes
19 02 04*	premixed wastes composed of at least one hazardous waste
19 02 05*	sludges from physico/chemical treatment containing hazardous substances
19 02 06	sludges from physico/chemical treatment other than those mentioned in 19 02 05
19 02 11*	other wastes containing hazardous substances
19 05	**wastes from aerobic treatment of solid wastes**
19 05 03	off-specification compost
19 08	**wastes from waste water treatment plants not otherwise specified**
19 08 01	screenings
19 08 02	waste from desanding
19 08 13*	sludges containing hazardous substances from other treatment of industrial waste water

Table S2.3 Permitted waste types and quantities for treatment in the bioremediation process	
Maximum quantity	**In total no more than 29,999 tonnes per annum of hazardous waste and no more than 150,000 tonnes per annum of non-hazardous waste will be accepted for treatment at the site.** **Waste hazardous properties HP4 to HP7, HP11 and HP14**
Exclusions	**Wastes having any of the following characteristics shall not be accepted:** **Waste containing asbestos**
Waste code	**Description**
19 08 14	sludges from other treatment of industrial waste water other than those mentioned in 19 08 13
19 12	**wastes from the mechanical treatment of waste (for example sorting, crushing, compacting, pelletising) not otherwise specified**
19 12 07	wood other than that mentioned in 19 12 06 (consisting only of untreated woodchip)
19 13	**wastes from soil and groundwater remediation**
19 13 01*	solid wastes from soil remediation containing hazardous substances
19 13 02	solid wastes from soil remediation other than those mentioned in 19 13 01
19 13 03*	sludges from soil remediation containing hazardous substances
19 13 04	sludges from soil remediation other than those mentioned in 19 13 03
20	**Municipal wastes (household waste and similar commercial, industrial and institutional wastes) including separately collected fractions**
20 01	**separately collected fractions (except 15 01)**
20 01 38	wood other than that mentioned in 20 01 37
20 02	**garden and park wastes (including cemetery waste)**
20 02 01	biodegradable waste
20 03	**other municipal wastes**
20 03 03	street-cleaning residues

Table S2.4 Permitted waste types and quantities for treatment in the dewatering and solidification processes	
Maximum quantity	**In total no more than 150,000 tonnes per annum of non-hazardous waste will be accepted for treatment at the site.**
Exclusions	**Wastes having any of the following characteristics shall not be accepted:** **- wastes containing treated wood, wood-preserving agents or other biocides, persistent organic pollutants, Japanese Knotweed**
Waste code	**Description**
10	**Wastes from thermal processes**
10 01	**wastes from power stations and other combustion plants (except 19)**
10 01 15	bottom ash, slag and boiler dust from co-incineration other than those mentioned in 10 01 14
10 01 17	fly ash from co-incineration other than those mentioned in 10 01 16
17	**Construction and demolition wastes (including excavated soil from contaminated sites)**
17 05	**soil (including excavated soil from contaminated sites), stones and dredging spoil**

Table S2.4 Permitted waste types and quantities for treatment in the dewatering and solidification processes	
Maximum quantity	**In total no more than 150,000 tonnes per annum of non-hazardous waste will be accepted for treatment at the site.**
Exclusions	**Wastes having any of the following characteristics shall not be accepted:** **- wastes containing treated wood, wood-preserving agents or other biocides, persistent organic pollutants, Japanese Knotweed**
Waste code	**Description**
17 05 06	dredging spoil other than those mentioned in 17 05 05
19	**Wastes from waste management facilities, off-site waste water treatment plants and the preparation of water intended for human consumption and water for industrial use**
19 01	wastes from incineration or pyrolysis of waste
19 01 12	bottom ash and slag other than those mentioned in 19 01 11
19 01 14	fly ash other than those mentioned in 19 01 13
19 02	**wastes from physico/chemical treatments of waste (including dechromatation, decyanidation, neutralisation)**
19 02 06	sludges from physico/chemical treatment other than those mentioned in 19 02 05
19 08	**wastes from waste water treatment plants not otherwise specified**
19 08 14	sludges from other treatment of industrial waste water other than those mentioned in 19 08 13
19 13	**wastes from soil and groundwater remediation**
19 13 04	sludges from soil remediation other than those mentioned in 19 13 03
20	**Municipal wastes (household waste and similar commercial, industrial and institutional wastes) including separately collected fractions**
20 03	**other municipal wastes**
20 03 03	street-cleaning residues

Table S2.5 Permitted waste types and quantities for storage only (wastes not requiring treatment prior to landfill)	
Maximum quantity	**No more than 100,000 tonnes of waste to be stored at any one time.**
Exclusions	**Wastes having any of the following characteristics shall not be accepted:** **- wastes containing treated wood, wood-preserving agents or other biocides, persistent organic pollutants, Japanese Knotweed**
Waste code	**Description**
01	**Wastes resulting from exploration, mining, quarrying, and physical and chemical treatment of minerals**
01 01	**wastes from mineral excavation**
01 01 02	wastes from mineral non-metalliferous excavation
01 04	**wastes from physical and chemical processing of non-metalliferous minerals**
01 04 08	waste gravel and crushed rocks other than those mentioned in 01 04 07
01 04 09	waste sand and clays
01 04 12	tailings and other wastes from washing and cleaning of minerals other than those mentioned in 01 04 07 and 01 04 11

Table S2.5 Permitted waste types and quantities for storage only (wastes not requiring treatment prior to landfill)	
Maximum quantity	**No more than 100,000 tonnes of waste to be stored at any one time.**
Exclusions	**Wastes having any of the following characteristics shall not be accepted:** **- wastes containing treated wood, wood-preserving agents or other biocides, persistent organic pollutants, Japanese Knotweed**
Waste code	**Description**
01 04 13	wastes from stone cutting and sawing other than those mentioned in 01 04 07
10	**Wastes from thermal processes**
10 01	**wastes from power stations and other combustion plants (except 19)**
10 01 01	bottom ash and slag from power stations (Furnace Bottom Ash) (excluding boiler dust mentioned in 10 01 04)
10 01 02	PFA from Power Stations
10 08	**wastes from other non-ferrous thermal metallurgy**
10 08 09	other slags
10 11	**wastes from manufacture of glass and glass products**
10 11 12	waste glass other than those mentioned in 10 11 11
10 12	**wastes from manufacture of ceramic goods, bricks, tiles and construction products**
10 12 06	discarded moulds
10 13	**wastes from manufacture of cement, lime and plaster and articles and products made from them**
10 13 14	waste concrete and concrete sludge
15	**Waste packaging, absorbents, wiping cloths, filter materials and protective clothing not otherwise specified**
15 01	**packaging (including separately collected municipal packaging waste)**
15 01 07	glass packaging
16	**Wastes not otherwise specified in the list**
16 01	**end-of-life vehicles from different means of transport (including off-road machinery) and wastes from dismantling of end-of-life vehicles and vehicle maintenance (except 13, 14, 16 06 and 16 08)**
16 01 20	glass
17	**Construction and demolition wastes (including excavated soil from contaminated sites)**
17 01	**concrete, bricks, tiles and ceramics**
17 01 01	concrete
17 01 02	bricks
17 01 03	tiles and ceramics
17 01 07	mixtures of concrete, bricks, tiles and ceramics other than those mentioned in 17 01 06
17 02	**wood, glass and plastic**
17 02 02	glass
17 05	**soil (including excavated soil from contaminated sites), stones and dredging spoil**
17 05 04	soil and stones other than those mentioned in 17 05 03

Table S2.5 Permitted waste types and quantities for storage only (wastes not requiring treatment prior to landfill)	
Maximum quantity	**No more than 100,000 tonnes of waste to be stored at any one time.**
Exclusions	**Wastes having any of the following characteristics shall not be accepted:** **- wastes containing treated wood, wood-preserving agents or other biocides, persistent organic pollutants, Japanese Knotweed**
Waste code	**Description**
17 05 06	dredging spoil other than those mentioned in 17 05 05
17 05 08	track ballast other than those mentioned in 17 05 07
17 09	**other construction and demolition wastes**
17 09 04	mixed construction and demolition wastes other than those mentioned in 17 09 01, 17 09 02 and 17 09 03
19	**Wastes from waste management facilities, off-site waste water treatment plants and the preparation of water intended for human consumption and water for industrial use**
19 02	**wastes from physico/chemical treatments of waste (including dechromatation, decyanidation, neutralisation)**
19 02 06	sludges from physico/chemical treatment other than those mentioned in 19 02 05
19 12	**wastes from the mechanical treatment of waste (for example sorting, crushing, compacting, pelletising) not otherwise specified**
19 12 05	glass
19 12 09	minerals (for example sand, stones)
19 12 12	other wastes (including mixtures of materials) from mechanical treatment of wastes other than those mentioned in 19 12 11 (treated bottom ash including IBA and slag other than that containing hazardous substances)
19 12 12	other wastes (including mixtures of materials) from mechanical treatment of wastes other than those mentioned in 19 12 11 (qualifying fines)
19 13	**wastes from soil and groundwater remediation**
19 13 02	solid wastes from soil remediation other than those mentioned in 19 13 01
20	**Municipal wastes (household waste and similar commercial, industrial and institutional wastes) including separately collected fractions**
20 01	**separately collected fractions (except 15 01)**
20 01 02	glass
20 02	**garden and park wastes (including cemetery waste)**
20 02 02	soil and stones (excluding top soil and peat)

Table S2.6 Permitted waste types and quantities for handpicking of asbestos waste	
Maximum quantity	**In total no more than 29,999 tonnes per annum of hazardous waste and no more than 150,000 tonnes per annum of non-hazardous waste will be accepted for treatment at the site.**
Exclusions	**Wastes having any of the following characteristics shall not be accepted:** **Asbestos in unbound fibrous form (FREE CHRYSOTILE FIBROUS ASBESTOS IN THE SOIL MUST BE < 0.1% w/w. OTHER FORMS OR MIXED FORMS OF FIBROUS ASBESTOS IN THE SOIL MUST BE <0.01% w/w)** **Wastes with hazard codes HP1, HP2, HP3, HP9, HP12, HP15**
Waste code	**Description**
17	**Construction and demolition wastes (including excavated soil from contaminated sites)**
17 05	**soil (including excavated soil from contaminated sites), stones and dredging spoil**
17 05 03*	soil and stones containing hazardous substances (CONTAINS IDENTIFIABLE PIECES OF BONDED ASBESTOS (any particle of a size that can be identified as potentially being asbestos by a competent person if examined by the naked eye))
17 05 04	soil and stones other than those mentioned in 17 05 03 (CONTAINS IDENTIFIABLE PIECES OF BONDED ASBESTOS (any particle of a size that can be identified as potentially being asbestos by a competent person if examined by the naked eye))
17 06	**insulation materials and asbestos-containing construction materials**
17 06 05*	construction materials containing asbestos (DISCRETE PIECES OF BONDED ASBESTOS WITHIN THE SOIL MATRIX ONLY)

Schedule 3 – Emissions and monitoring

Table S3.1 Point source emissions to air – emission limits and monitoring requirements						
Emission point ref. & location	**Source**	**Parameter**	**Limit (including unit)**	**Reference period**	**Monitoring frequency**	**Monitoring standard or method**
A1 (biofilter on Figure 3, Site Layout dated November 2015, submitted with EPR/HP3632RP/A001)	Biofilter - Soil Treatment	Total Petroleum Hydrocarbons (TPH)	No limit set	Hourly mean	Monthly	As per M8 or other subsequent guidance as agreed in writing with the Environment Agency
		Benzene, Toluene, Ethyl Benzene and Xylenes (BTEX)	No limit set	Hourly mean	Monthly	
		Polycyclic Aromatic Hydrocarbons (PAHs)	No limit set	Hourly mean	Monthly	

Table S3.2 Point source emissions to sewer, effluent treatment plant or other transfers off-site– emission limits and monitoring requirements						
Emission point ref. & location	**Source**	**Parameter**	**Limit (incl. Unit)**	**Reference period**	**Monitoring frequency**	**Monitoring standard or method**
Emission point/s as shown on site drainage plan*	Site effluent from waste processing and storage areas	No parameter set	No limit set	--	--	--
Emission point/s as shown on site drainage plan*	Uncontaminated site source water from roofs and other non-operational areas	No parameter set	No limit set	--	--	--
*Site drainage plan to be submitted accordance with pre-operational measure 1 in table S1.3						

Table S3.3 Process monitoring requirements					
Emission point reference or source or description of point of measurement	**Parameter**	**Limit**	**Monitoring frequency**	**Monitoring standard or method**	**Other specifications**
Biofilter	Temperature	--	As required	Temperature probe	Biofilter shall be regularly checked and maintained to ensure appropriate temperature and moisture content. Equipment shall be calibrated on a 4 monthly basis or as agreed in writing by the Environment Agency.
	Moisture	--	As required	None specified	
	Thatching/ compaction	--	As required	None specified	
Internal for each biopile batch during bioremediation	Temperature	--	At least weekly	Temperature probe	Monitoring equipment shall be available on site and used as required to maintain aerobic conditions and ensure compliance with this permit. Equipment shall be calibrated on a 4 monthly basis or as agreed in writing by the Environment Agency.
	Moisture	--	As required	None specified	
	pH	--	At least fortnightly	None specified	
	Oxygen	--	At least weekly	None specified	
Air testing within the building (labelled as 'dust shed') for the duration of the asbestos hand picking works. Sampling points as detailed in Schedule 5 response dated 29/01/18 and shown on drawing 100993 – Asbestos DWG1 dated January 2018.	Asbestos fibres	0.01 fibres/ml Where total fibre concentration exceeds 0.01 fibres/ml in any sample, that sample must be submitted for electron microscopy to confirm the concentration of asbestos fibres present	During the asbestos hand picking works 1 hour at 8 l/min	In line with M17 monitoring guidance While asbestos is being treated. • Pumped sampling • 1m above ground level • Flow rate = 8 litres/ minute • Minimum sample volume = 480 litres • Filter pore size = 0.8-1.2µm Asbestos fibre limit of detection = 0.001 fibres/ml	--

Schedule 4 – Reporting

Parameters, for which reports shall be made, in accordance with conditions of this permit, are listed below.

Table S4.1 Reporting of monitoring data			
Parameter	**Emission or monitoring point/reference**	**Reporting period**	**Period begins**
Biofilter efficiency Parameters as required by condition 3.5.1	Biofilter	Every 12 months	1 January
Asbestos fibres Parameters as required by condition 3.5.1	Air testing within the building (labelled as 'dust shed') during the asbestos hand picking works Sampling points as detailed in Schedule 5 response dated 29/01/18 and shown on drawing 100993 – Asbestos DWG1 dated January 2018.	Every 3 months	1 January, 1 April, 1 July, 1 October

Table S4.2 Annual production/treatment	
Parameter	**Units**
Bioremediation Plant (treatment)	Tonnes per year
De-watering and solidification plant (treatment)	Tonnes per year
Treatment of hazardous waste (total)	Tonnes per year
Treatment of non-hazardous waste (total)	Tonnes per year

Table S4.3 Performance parameters		
Parameter	**Frequency of assessment**	**Units**
Water usage	Annually	tonnes or m^3
Energy usage	Annually	MWh

Table S4.4 Reporting forms		
Media/parameter	**Reporting format**	**Date of form**
Air	Form air 1 or other form as agreed in writing by the Environment Agency	07/04/2016
Water usage	Form water usage 1 or other form as agreed in writing by the Environment Agency	07/04/2016
Energy usage	Form energy 1 or other form as agreed in writing by the Environment Agency	07/04/2016
Other performance indicators	Form performance 1 or other form as agreed in writing by the Environment Agency	07/04/2016
Waste returns	E-Waste Return Form	--
Asbestos Fibres	Form particle 1 or other form as agreed in writing by the Environment Agency	26/02/2018

Schedule 5 – Notification

These pages outline the information that the operator must provide.

Units of measurement used in information supplied under Part A and B requirements shall be appropriate to the circumstances of the emission. Where appropriate, a comparison should be made of actual emissions and authorised emission limits.

If any information is considered commercially confidential, it should be separated from non-confidential information, supplied on a separate sheet and accompanied by an application for commercial confidentiality under the provisions of the EP Regulations.

Part A

Permit Number	
Name of operator	
Location of Facility	
Time and date of the detection	

(a) Notification requirements for any malfunction, breakdown or failure of equipment or techniques, accident, or emission of a substance not controlled by an emission limit which has caused, is causing or may cause significant pollution	
To be notified within 24 hours of detection	
Date and time of the event	
Reference or description of the location of the event	
Description of where any release into the environment took place	
Substances(s) potentially released	
Best estimate of the quantity or rate of release of substances	
Measures taken, or intended to be taken, to stop any emission	
Description of the failure or accident.	

(b) Notification requirements for the breach of a limit	
To be notified within 24 hours of detection unless otherwise specified below	
Emission point reference/ source	
Parameter(s)	
Limit	
Measured value and uncertainty	
Date and time of monitoring	
Measures taken, or intended to be taken, to stop the emission	

Time periods for notification following detection of a breach of a limit	
Parameter	**Notification period**

(c) Notification requirements for the detection of any significant adverse environmental effect	
To be notified within 24 hours of detection	
Description of where the effect on the environment was detected	
Substances(s) detected	
Concentrations of substances detected	
Date of monitoring/sampling	

Part B – to be submitted as soon as practicable

Any more accurate information on the matters for notification under Part A.	
Measures taken, or intended to be taken, to prevent a recurrence of the incident	
Measures taken, or intended to be taken, to rectify, limit or prevent any pollution of the environment which has been or may be caused by the emission	
The dates of any unauthorised emissions from the facility in the preceding 24 months.	

Name*	
Post	
Signature	
Date	

* authorised to sign on behalf of the operator

Schedule 6 – Interpretation

“accident” means an accident that may result in pollution.

“application” means the application for this permit, together with any additional information supplied by the operator as part of the application and any response to a notice served under Schedule 5 to the EP Regulations.

“authorised officer” means any person authorised by the Environment Agency under section 108(1) of The Environment Act 1995 to exercise, in accordance with the terms of any such authorisation, any power specified in section 108(4) of that Act.

“building” means a construction that has the objective of providing sheltering cover and minimising emissions of noise, particulate matter, odour and litter.

“disposal”. Means any of the operations provided for in Annex I to Directive 2008/98/EC of the European Parliament and of the Council on waste.

“emissions to land” includes emissions to groundwater.

“EP Regulations” means The Environmental Permitting (England and Wales) Regulations SI 2010 No.675 and words and expressions used in this permit which are also used in the Regulations have the same meanings as in those Regulations.

“emissions of substances not controlled by emission limits” means emissions of substances to air, water or land from the activities, either from the emission points specified in schedule 3 or from other localised or diffuse sources, which are not controlled by an emission or background concentration limit.

“groundwater” means all water, which is below the surface of the ground in the saturation zone and in direct contact with the ground or subsoil.

“hazardous property” has the meaning in Annex lll of the Waste Framework Directive.

“hazardous waste” has the meaning given in the Hazardous Waste (England and Wales) Regulations 2005 (as amended).

“Industrial Emissions Directive” means DIRECTIVE 2010/75/EU OF THE EUROPEAN PARLIAMENT AND OF THE COUNCIL of 24 November 2010 on industrial emissions

“List of Wastes” means the list of wastes established by Commission Decision 2000/532/EC replacing Decision 94/3/EC establishing a list of wastes pursuant to Article 1(a) of Council Directive 75/442/EEC on waste and Council Decision 94/904/EC establishing a list of hazardous waste pursuant to Article 1(4) of Council Directive 91/689/EEC on hazardous waste, as amended from time to time.

“MCERTS” means the Environment Agency’s Monitoring Certification Scheme.

“pests” means Birds, Vermin and Insects.

“quarter” means a calendar year quarter commencing on 1 January, 1 April, 1 July or 1 October.

“recovery” means any of the operations provided for in Annex II to Directive 2008/98/EC of the European Parliament and of the Council on waste.

“waste code” means the six digit code referable to a type of waste in accordance with the List of Wastes and in relation to hazardous waste, includes the asterisk.

“Waste Framework Directive” or “WFD” means Waste Framework Directive 2008/98/EC of the European Parliament and of the Council on waste

Where a minimum limit is set for any emission parameter, for example pH, reference to exceeding the limit shall mean that the parameter shall not be less than that limit.

Unless otherwise stated, any references in this permit to concentrations of substances in emissions into air means:

- in relation to emissions from combustion processes, the concentration in dry air at a temperature of 273K, at a pressure of 101.3 kPa and with an oxygen content of 3% dry for liquid and gaseous fuels, 6% dry for solid fuels; and/or
- in relation to emissions from non-combustion sources, the concentration at a temperature of 273K and at a pressure of 101.3 kPa, with no correction for water vapour content.

“year” means calendar year ending 31 December.

When the following terms appear in the waste code list in Schedule 2, tables S2.2 and S2.3, for that those tables, they have the meaning given below:

‘hazardous substance’ means a substance classified as hazardous as a consequence of fulfilling the criteria laid down in parts 2 to 5 of Annex I to Regulation (EC) No 1272/2008

‘heavy metal’ means any compound of antimony, arsenic, cadmium, chromium (VI), copper, lead, mercury, nickel, selenium, tellurium, thallium and tin, as well as these materials in metallic form, as far as these are classified as hazardous substances

‘PCBs’ means

- polychlorinated biphenyls
- polychlorinated terphenyls
- monomethyl-tetrachlorodiphenyl methane, Monomethyl-dichloro-diphenyl methane, Monomethyldibromo-diphenyl methane
- any mixture containing any of the above mentioned substances in a total of more than 0,005 %by weight

‘transition metals’ means any of the following metals: any compound of scandium, vanadium, manganese, cobalt, copper, yttrium, niobium, hafnium, tungsten, titanium, chromium, iron, nickel, zinc, zirconium, molybdenum and tantalum, as well as these materials in metallic form, as far as these are classified as hazardous substances

‘stabilisation’ means processes which change the hazardousness of the constituents in the waste and transform hazardous waste into non-hazardous waste

‘solidification’ means processes which only change the physical state of the waste by using additives without changing the chemical properties of the waste

‘partly stabilised wastes’ means wastes containing, after the stabilisation process, hazardous constituents which have not been changed completely into non-hazardous constituents and could be released into the environment in the short, middle or long term

Schedule 7 – Site plan



©Crown Copyright. All rights reserved. Environment Agency, 100024198, 2018.

END OF PERMIT

Standard rules

Chapter 4, The Environmental Permitting (England and Wales) Regulations 2010

Standard rules SR2010No12
Treatment of waste to produce soil, soil substitutes and aggregate

Introductory note

This introductory note does not form part of these standard rules.

When referred to in an environmental permit, these standard rules will allow the operator to store waste at a specified location and treat it to produce soil, soil substitutes and aggregate. Permitted wastes do not include hazardous wastes. The total quantity of waste that can be stored and subsequently treated at the site under these standard rules shall be no more than 75,000 tonnes per year. These standard rules do not permit the burning of any wastes, either in the open, inside buildings or in any form of incinerator.

The permitted activities shall not be carried out within 500 metres of a European Site[1], Ramsar site or a Site of Special Scientific Interest (SSSI) nor within a specified Air Quality Management Area (AQMA)[2]. The permitted activities shall not be within:

- 10 metres of any watercourse;
- 50 metres from any spring or well, or from any borehole not used to supply water for domestic or food production purposes; and
- 250 metres from any well, spring or from any borehole used to supply water for domestic or food production purposes.

These standard rules do not allow any point source emission into surface waters or groundwater. However, under the emissions of substances not controlled by emission limits rule:

- Liquids may be discharged into a foul sewer subject to a consent issued by the local water company.
- Liquids may be taken off-site in a tanker for disposal or recovery.
- Clean surface water from roofs, or from areas of the site that are not being used in connection with storing and treating waste, may be discharged directly to surface waters, or to groundwater by seepage through the soil via a soakaway.

End of introductory note

[1] A candidate or Special Area of Conservation (cSAC or SAC) and proposed or Special Protection Area (pSPA or SPA) in England and Wales.

[2] An Air Quality Management Area within the meaning of the Environment Act 1995 which has been designated due to concerns about particulate matter in the form of PM10.

Rules

1 – Management

1.1 General management

1.1.1 The operator shall manage and operate the activities:

(a) in accordance with a written management system that identifies and minimises risks of pollution, including those arising from operations, maintenance, accidents, incidents, non-conformances, closure and those drawn to the attention of the operator as a result of complaints; and

(b) using sufficient competent persons and resources.

1.1.2 Records demonstrating compliance with rule 1.1.1 shall be maintained.

1.1.3 Any person having duties that are or may be affected by the matters set out in these standard rules shall have convenient access to a copy of them kept at or near the place where those duties are carried out.

1.1.4 The operator shall comply with the requirements of an approved competence scheme.

2 – Operations

2.1 Permitted activities

2.1.1 The operator is only authorised to carry out the operations specified in table 2.1 below ("the activities").

Table 2.1 Activities

Description of activities	Limits of activities
R13: Storage of wastes pending the operations numbered R3 and R5. **R3:** recycling or reclamation of organic substances which are not used as solvents. **R5:** Recycling or reclamation of other inorganic materials.	Treatment of wastes listed in table 2.3 consisting only of sorting, separation, screening, crushing and blending of waste for recovery as a soil, soil substitute or aggregate. Secure storage of wastes listed in table 2.3 pending treatment. Storage of wastes listed in table 3.1 shall not exceed 10,000 tonnes in total at any one time. All other wastes stored shall not exceed 40,000 tonnes in total at any one time. No more than 75,000 tonnes of waste shall be treated per year.

2.2 The site

2.2.1 The activities shall not extend beyond the site, being the land shown edged in green on the site plan attached to the permit.

2.2.2 The activities shall not be carried out within:

(a) 500 metres of a European Site or Site of Special Scientific Interest (SSSI);

(b) 10 metres of any watercourse;

(c) 50 metres of any spring or well, or any borehole not used to supply water for domestic or food production purposes;

(d) 250 metres of any well, spring or borehole used to supply water for domestic or food production purposes; and / or

(e) a specified AQMA.

2.3 Waste acceptance

2.3.1 Waste shall only be accepted if:

(a) it is of a type listed in table 2.3 of these standard rules;

(b) it conforms to the description in the documentation supplied by the producer and holder;

(c) its chemical, physical and biological characteristics make it suitable for its intended treatment;

(d) any excavated soil from potentially contaminated sites has been shown by prior chemical analysis and assessment to be suitable for the intended use without significant risk of pollution; and

(e) it is visually inspected on arrival and before it enters the treatment process to ensure that it complies with these standard rules.

2.3.2. Any waste that does not comply with 2.3.1 shall be rejected and shall be;

(a) removed from the site; or

(b) moved to a designated quarantine area pending removal.

2.3.3 Records demonstrating compliance with rule 2.3 (including analysis and assessment of any excavated soil from potentially contaminated sites) shall be maintained.

Table 2.3 Waste types

Exclusions

Wastes having any of the following characteristics shall not be accepted:

- **Consisting solely or mainly of dusts, powders or loose fibres**
- **Hazardous wastes**
- **Wastes in liquid form**

Waste Code	Description
01	**WASTES RESULTING FROM EXPLORATION, MINING, QUARRYING AND PHYSICAL AND CHEMICAL TREATMENT OF MINERALS**
01 04	**wastes from physical and chemical processing of non-metalliferous minerals**
01 04 08	waste gravel and crushed rocks other than those mentioned in 01 04 07
01 04 09	waste sand and clays
02 02	**waste from preparation and processing of meat, fish and other foods of animal origin**
02 02 02	shellfish shells from which the soft tissue or flesh has been removed only

03	**WASTES FROM WOOD PROCESSING AND THE PRODUCTION OF PANELS AND FURNITURE, PULP, PAPER AND CARDBOARD**
03 01	**wastes from wood processing and the production of panels and furniture**
03 01 01	waste bark and cork
03 03	**wastes from pulp, paper and cardboard production and processing**
03 03 01	waste bark and wood
10	**WASTES FROM THERMAL PROCESSES**
10 01	**waste from power stations and other combustion plants**
10 01 01	bottom ash and slag only
10 01 02	pulverised fuel ash only
10 01 05	gypsum (solid) only
10 01 07	gypsum (sludge) only
10 01 15	bottom ash and slag only from co-incineration other than those mentioned in 10 01 14
10 11	**wastes from manufacture of glass and glass products**
10 11 12	clean glass other than those mentioned in 10 11 11
10 12	**wastes from manufacture of ceramic goods, brick, stiles and construction products**
10 12 08	waste ceramics, bricks, tiles and construction products(after thermal processing)
10 13	**wastes from manufacture of cement, lime and plaster products and articles and products made from them**
10 13 14	waste concrete only
15	**WASTE PACKAGING**
15 01	**packaging**
15 01 07	clean glass only
17	**CONSTRUCTION AND DEMOLITION WASTES (INCLUDING EXCAVATED SOIL FROM CONTAMINATED SITES)**
17 01	**concrete, bricks, tiles and ceramics**
17 01 01	concrete
17 01 02	bricks
17 01 03	tiles and ceramics
17 01 07	mixtures of concrete, bricks, tiles and ceramics other than those mentioned in 17 01 06
17 02	**wood, glass and plastic**
17 02 02	clean glass only
17 03	**bituminous mixtures, coal tar and tarred products**
17 03 02	road base and road planings (other than those containing coal tar) only
17 05	**soil (including excavated soil from contaminated sites) stones and dredging spoil**
17 05 04	soil and stones other than those mentioned in 17 05 03
17 05 06	dredging spoil other than those mentioned in 17 05 05
17 05 08	track ballast other than those mentioned in 17 05 07
17 08	**gypsum based construction material**
17 08 02	gypsum only other than that mentioned in 17 08 01
19	**WASTES FROM WASTE MANAGEMENT FACILITIES, OFF SITE WASTE WATER TREATMENT PLANTS AND PREPARATION OF WATER INTENDED FOR HUMAN CONSUMPTION / INDUSTRIAL WASTE**
19 05	**wastes from aerobic treatment of solid waste**
19 05 03	compost from source segregated biodegradable waste only
19 08	**wastes from waste water treatment plants not otherwise specified**
19 08 02	washed sewage grit (waste from desanding) free from sewage contamination only
19 08 99	stone filter media if free from sewage contamination only
19 09	**wastes from the preparation of water intended for human consumption or water for industrial use**
19 09 02	sludges from water clarification

19 12	**wastes from the mechanical treatment of wastes**
19 12 05	clean glass only
19 12 09	minerals (for example sand, stones)
19 12 12	treated bottom ash including IBA and slag other than that containing dangerous substances only
19 13	**wastes from soil and groundwater remediation**
19 13 02	solid wastes from soil remediation other than those mentioned in 19 13 01
19 13 04	sludges from soil remediation other than those mentioned in 19 13 03
20	**MUNICIPAL WASTES (HOUSEHOLD WASTE AND SIMILAR COMMERCIAL, INDUSTRIAL AND INSTITUTIONAL WASTES) INCLUDING SEPARATELY COLLECTED FRACTIONS**
20 01	**separately collected fractions**
20 01 02	clean glass only
20 02	**garden and park wastes**
20 02 02	soil and stones

3 – Emissions and monitoring

3.1 Emissions of substances not controlled by emission limits

3.1.1 Emissions of substances not controlled by emission limits (excluding odour) shall not cause pollution. The operator shall not be taken to have breached this rule if appropriate measures, including, but not limited to, those specified in Table 3.1 below and in any approved emissions management plan, have been taken to prevent or where that is not practicable, to minimise, those emissions.

Table 3.1 Appropriate measures for emissions not controlled by emission limits

When located within groundwater Source Protection Zones 1 or 2 the specified wastes below shall be stored and treated on an impermeable surface with a sealed drainage system.

When located outside groundwater Source Protection Zones 1 or 2 all permitted wastes shall be stored and treated on hard-standing or on an impermeable surface with sealed drainage system.

Waste Code	Description
03 01 01	waste bark and cork
03 03 01	waste bark and wood
10 01 01	bottom ash and slag only
10 01 05	gypsum (solid) only
10 01 07	gypsum (sludge) only
10 01 15	bottom ash and slag only from co-incineration other than those mentioned in 10 01 14
17 05 06	dredging spoil other than those mentioned in 17 05 05
17 08 02	gypsum only other than that mentioned in 17 08 01
19 05 03	compost from source segregated biodegradable waste only
19 09 02	sludges from water clarification
19 12 12	treated bottom ash including IBA and slag other than that containing dangerous substances only
19 13 02	solid wastes from soil remediation other than those mentioned in 19 13 01
19 13 04	sludges from soil remediation other than those mentioned in 19 13 03

3.1.2 The operator shall:

(a) if notified by the Environment Agency that the activities are giving rise to pollution, submit to the Environment Agency for approval within the period specified, an emissions management plan;

(b) implement the approved emissions management plan, from the date of approval, unless otherwise agreed in writing by the Environment Agency.

3.1.3 All liquids in containers, whose emission to water or land could cause pollution, shall be provided with secondary containment, unless the operator has used other appropriate measures to prevent or where that is not practicable, to minimise, leakage and spillage from the primary container

3.2 Odour

3.2.1 Emissions from the activities shall be free from odour at levels likely to cause pollution outside the site, as perceived by an authorised officer of the Environment Agency, unless the operator has used appropriate measures, including, but not limited to, those specified in any approved odour management plan, to prevent or where that is not practicable, to minimise, the odour.

3.2.2 The operator shall:

(a) if notified by the Environment Agency that the activities are giving rise to pollution outside the site due to odour, submit to the Environment Agency for approval within the period specified, an odour management plan;

(b) implement the approved odour management plan, from the date of approval, unless otherwise agreed in writing by the Environment Agency.

3.3 Noise and vibration

3.3.1 Emissions from the activities shall be free from noise and vibration at levels likely to cause pollution outside the site, as perceived by an authorised officer of the Environment Agency, unless the operator has used appropriate measures, including, but not limited to, those specified in any approved noise and vibration management plan, to prevent or where that is not practicable, to minimise, the noise and vibration.

3.3.2 The operator shall:

(a) if notified by the Environment Agency that the activities are giving rise to pollution outside the site due to noise and vibration, submit to the Environment Agency for approval within the period specified, a noise and vibration management plan;

(b) implement the approved noise and vibration management plan, from the date of approval, unless otherwise agreed in writing by the Environment Agency.

4 – Information

4.1 Records

4.1.1 All records required to be made by these standard rules shall:

(a) be legible;

(b) be made as soon as reasonably practicable;

(c) if amended, be amended in such a way that the original and any subsequent amendments remain legible or are capable of retrieval; and

(d) be retained, unless otherwise agreed by the Environment Agency, for at least 6 years from the date when the records were made, or in the case of the following records until permit surrender:

(i) off-site environmental effects; and

(ii) matters which affect the condition of land and groundwater.

4.1.2 The operator shall keep on site all records, plans and the management system required to be maintained by these standard rules, unless otherwise agreed in writing by the Environment Agency

4.2 Reporting

4.2.1 The operator shall send all reports and notifications required by these standard rules to the Environment Agency using the contact details supplied in writing by the Environment Agency.

4.2.2 Within one month of the end of each quarter, the operator shall submit to the Environment Agency using the form made available for the purpose, the information specified on the form relating to the site and the waste accepted and removed from it during the previous quarter.

4.3 Notifications

4.3.1 The Environment Agency shall be notified without delay following the detection of:

(a) any malfunction, breakdown or failure of equipment or techniques, accident or emission of a substance not controlled by an emission limit which has caused, is causing or may cause significant pollution;

(b) the breach of a limit specified in these standard rules; or

(c) any significant adverse environmental effects.

4.3.2 Written confirmation of actual or potential pollution incidents and breaches of emission limits shall be submitted within 24 hours.

4.3.3 Where the Environment Agency has requested in writing that it shall be notified when the operator is to undertake monitoring and/or spot sampling, the operator shall inform the Environment Agency when the relevant monitoring and/or spot sampling is to take place. The operator shall provide this information to the Environment Agency at least 14 days before the date the monitoring is to be undertaken.

4.3.4 The Environment Agency shall be notified within 14 days of the occurrence of the following matters except where such disclosure is prohibited by Stock Exchange rules:

a) Where the operator is a registered company:

- any change in the operator's trading name, registered name or registered office address; and
- any steps taken with a view to the operator going into administration, entering into a company voluntary arrangement or being wound up.

b) Where the operator is a corporate body other than a registered company:

- any change in the operator's name or address; and
- any steps taken with a view to the dissolution of the operator.

c) In any other case:

- the death of any of the named operators (where the operator consists of more than one named individual);
- any change in the operator's name(s) or address(es); and
- any steps taken with a view to the operator, or any one of them, going into bankruptcy, entering into a composition or arrangement with creditors, or, in the case them being in a partnership, dissolving the partnership.

4.4 Interpretation

4.4.1 In these standard rules the expressions listed below shall have the meaning given.

4.4.2 In these standard rules references to reports and notifications mean written reports and notifications, except when reference is being made to notification being made “without delay”, in which case it may be provided by telephone.

“*accident*” means an accident that may result in pollution.

“*AQMA*” means an air quality management area within the meaning of the Environment Act 1995 which has been designated due to concerns about particulate matter in the form of PM10.

“*authorised officer*” means any person authorised by the Environment Agency under section 108(1) of The Environment Act 1995 to exercise, in accordance with the terms of any such authorisation, any power specified in Section 108(4) of that Act.

“dangerous substances” means any substance that has been or will be classified as dangerous in Directive 67/548/EEC and its subsequent amendments.

“*domestic purposes*” has the same meaning as in section 218 of the Water Industry Act 1991.

“emissions of substances not controlled by emission limits” means emissions of substances to air, water or land from the activities, either from emission points specified in these standard rules or from other localised or diffuse sources, which are not controlled by an emission limit.

“European Site” means Special Area of Conservation or candidate Special Area of Conservation or Special Protection Area or proposed Special Protection Area in England and Wales, within the meaning of Council Directives 79/409/EEC on the conservation of wild birds and 92/43/EEC on the conservation of natural habitats and of wild flora and fauna and the Conservation (Natural Habitats &c) Regulations 1994. Internationally designated Ramsar sites are dealt with in the same way as European sites as a matter of government policy and for the purpose of these rules will be considered as a European Site.

“food production purposes” means the manufacturing, processing, preserving or marketing purposes with respect to food or drink for which water supplied to food production premises may be used, and for the purposes of this definition “food production purposes” means premises used for the purposes of a business of preparing food or drink for consumption otherwise than on the premises.

“groundwater” means all water, which is below the surface of the ground in the saturation zone and in direct contact with the ground or subsoil.

“impermeable surface” means a surface or pavement constructed and maintained to a standard sufficient to prevent the transmission of liquids beyond the pavement surface, and should be read in conjunction with the term “sealed drainage system” (below).

“hardstanding” is a compacted solid surface capable of withstanding the operation and the loading / unloading of wastes.

“IBA” means incinerator bottom ash derived from the incineration or pyrolosis of waste.

"pollution" means emissions as a result of human activity which may—

(a) be harmful to human health or the quality of the environment,
(b) cause offence to a human sense,
(c) result in damage to material property, or
(d) impair or interfere with amenities and other legitimate uses of the environment.

“*quarter*” means a calendar year quarter commencing on 1 January, 1 April, 1 July or 1 October.

“*R*” means a recovery operation provided for in Annex IIB to Directive 2006/12/EC of the European Parliament and of the Council of 5 April 2006 on Waste.

“sealed drainage system” in relation to an impermeable surface, means a drainage system with impermeable components which does not leak and which will ensure that:

(a) no liquid will run off the surface otherwise than via the system;
(b) except where they may lawfully be discharged to foul sewer, all liquids entering the system are collected in a sealed sump.

“secure storage” means storage where waste cannot escape and members of the public do not have access to it.

“SSSI” means Site of Special Scientific Interest within the meaning of the Wildlife and Countryside Act 1981 (as amended by the Countryside and Rights of Way Act 2000).

“waste code” means the six digit code referable to a type of waste in accordance with the List of Wastes (England) Regulations 2005, or List of Wastes (Wales) Regulations 2005, as appropriate, and in relation to hazardous waste, includes the asterisk.

"year" means calendar year commencing on 1st January.

End of standard rules

Standard rules SR2015 No.39

The Environmental Permitting (England & Wales) Regulations 2010

Use of waste in a deposit for recovery operation (Construction, reclamation, restoration or improvement of land other than by mobile plant)

Maximum volumetric capacity of recovery operation 60,000 m^3

Introductory note

This introductory note does not form part of these standard rules.

When referred to in an environmental permit, these standard rules will allow the operator to store and subsequently use waste for the purposes of a recovery activity involving the deposit of waste that is to be used in construction and/or reclamation, restoration or improvement of land. These standard rules are for the recovery of waste only and do not apply to any activities involving disposal.

You must submit a waste recovery plan with your application for these standard rules. We will only be able to issue a permit if we approve the plan and compliance with the approved plan will then be a requirement of the permit, if the application is granted. The plan must demonstrate that your proposals will meet the definition of recovery in the Waste Framework Directive 2008 as explained in relevant regulatory guidance. We recommend that you submit your plan to us so that we can advise you on whether we consider that the proposed activity would be a recovery operation before applying for these standard rules.

Permitted wastes are limited to mainly inert wastes as defined in these standard rules, with some limited uses for selected non-inert wastes. The maximum quantity of waste that can be stored and subsequently used at the site under these standard rules is 60,000m^3, although part of being a recovery operation is that the minimum amount of waste that is needed is used and therefore, where we have approved a plan proposing to use less waste, this becomes the permitted maximum.

If you need to deploy mobile plant under a mobile plant permit at a site that is subject to a site based permit to enable you to complete the recovery activity, there will be inconsistencies between the requirements of the two permits. In this situation the requirements of the site based permit prevail. Therefore you must be able to deliver the desired recovery activity through use of these standard rules alone, without relying upon the subsequent use of a separate mobile plant permit. If you need to use additional waste types or quantities to those allowed under these standard rules then you should apply to do this under a bespoke permit.

These standard rules do not allow any tipping into a water body or sub-water table.

These standard rules do not allow any point source emissions into surface waters or groundwater.

Anyone wanting to operate under these standard rules must ensure that the site location meets all the criteria set out in 2.4 of this rule set and the limits of the activity set out in Table 2.1. Definitions are given in 4.4 Interpretation.

End of introductory note

Conditions

1 Management

1.1 General management

1.1.1 The operator shall manage and operate the activities:

(a) in accordance with a written management system that identifies and minimises risks of pollution, including those arising from operations, maintenance, accidents, incidents, non-conformances and those drawn to the attention of the operator as a result of complaints; and

(b) using sufficient competent persons and resources.

1.1.2 Records demonstrating compliance with condition 1.1.1 shall be maintained.

1.1.3 Any person having duties that are or may be affected by the matters set out in these standard rules shall have convenient access to a copy of it kept at or near the place where those duties are carried out.

1.1.4 The operator shall comply with the requirements of an approved competence scheme.

1.2 Avoidance, recovery and disposal of wastes produced by the activities

1.2.1 The operator shall take appropriate measures to ensure that:

(a) the waste hierarchy referred to in Article 4 of the Waste Framework Directive is applied to the generation of waste by the activities; and

(b) any waste generated by the activities is treated in accordance with the waste hierarchy referred to in Article 4 of the Waste Framework Directive; and

(c) where disposal is necessary, this is undertaken in a manner which minimises its impact on the environment.

1.2.2 The operator shall review and record at least every four years whether changes to those measures should be made and take any further appropriate measures identified by a review.

2 Operations

2.1 Permitted activities

2.1.1 The operator is only authorised to carry out the activities specified in table 2.1 below ("Activities").

Table 2.1 Activities	
Description of activities	**Limits of activities**
R13: Storage of wastes pending any of the operations numbered R5 and R10	The use and associated secure storage of a maximum of 60,000m^3 of wastes listed in table 2.5 for the purposes of the construction work and/or restoration, reclamation or improvement of land as detailed in the

Table 2.1 Activities	
Description of activities	**Limits of activities**
R5: Recycling or reclamation of other inorganic materials **R10:** Land treatment resulting in benefit to agriculture or ecological improvement	approved waste recovery plan. In any event the total quantity of waste used shall not exceed the amount needed to complete the recovery operation to the final levels in the approved waste recovery plan. Only the waste types specified in table 2.5 that are specified in the approved waste recovery plan shall be accepted. Such wastes shall only be used as specified in the approved waste recovery plan. Restoration, reclamation and land improvement activities must only be carried out on land that has been previously subject to industrial or other man-made development. No waste shall be deposited into a water body or sub-water table. Waste types coded 17 05 04 and 20 02 02 that are top soils or peat and waste coded 02 04 01 that is soil from cleaning and washing beet shall only be used for R10 activities, subject to rule 2.3.1. Storage of waste prior to use in the recovery activity shall be limited to 12 months.

2.2 Waste recovery plan

2.2.1 The operator shall not deviate from the approved waste recovery plan without prior written approval from the Environment Agency. Submission for approval must be in a form specified by the Environment Agency.

2.2.2 A topographical survey of the site referenced to ordnance datum shall be carried out:

(a) prior to commencement of the recovery activity; and

(b) on completion of the recovery activity to show final waste levels.

2.2.3 Each topographical survey shall be used to produce a plan of a scale adequate to show the surveyed features of the site. The plan shall be produced within 1 month of the completion of the survey.

2.3 Operating techniques

2.3.1 The activities shall be operated using the techniques and in the manner described in Table 2.3 below.

Table 2.3 Operating techniques
1. Road planings (waste types coded 17 03 02) shall be: (a) limited to use for construction of hard surface infrastructure such as roads, tracks, pathways and parking; and (b) only used within 30cm of the final waste level except where they are used as temporary

Table 2.3 Operating techniques
infrastructure; and (c) removed before further waste is deposited where used as temporary infrastructure . 2. Top soils or peat (waste types coded 17 05 04 and 20 02 02) and soil from cleaning and washing beet (waste coded 02 04 01) shall be limited to use in the top 50cm of the recovery activity and shall only be used to provide a growing medium.

2.4 The site

2.4.1 The activities shall not extend beyond the site, being the land shown edged in green on the site plan attached to the permit.

2.4.2 The activities shall not be carried out:

(a) within 500 metres of a European Site or a Site of Special Scientific Interest (SSSI));

(b) within 250 metres of the presence of Great Crested Newts where the site is linked by good habitat to the breeding ponds of the newts,

(c) within 50 metres of a site that has species or habitats protected under the Biodiversity Action Plan that the Environment Agency considers is at risk from this activity,

(d) within 50 metres of a National Nature Reserve (NNR), Local Nature Reserves(LNR), Local Wildlife Site (LWS), Ancient woodland or Scheduled Ancient Monument,

(e) within groundwater Source Protection Zones 1 and 2 or if a source protection zone has not been defined then not within 250 metres of any well, spring or borehole used for the supply of water for human consumption. This includes private water supplies.

(f) on any landfill whether historical, closed, or operational,

(g) within 10 metres of a watercourse,

(h) within a specified Air Quality Management Area for particulate matter less than 10 microns (PM10).

2.5 Waste acceptance

2.5.1 Waste shall only be accepted if it is of a type listed in table 2.5 of these standard rules, it meets the additional restrictions in that table; and

(a) it is inert waste, with the exception of topsoil, peat, soil from cleaning and washing beet and road planings; and

(b) appropriate measures have been taken to ensure that the waste is free from contamination; and

(c) it has been identified as a suitable waste in the approved waste recovery plan; and

(d) its chemical, physical and biological characteristics make it suitable for its intended use on the site.

Table 2.5 Waste types				
Exclusions Wastes having any of the following characteristics shall not be accepted: • Consisting solely or mainly of dusts, powders or loose fibres • Wastes that are in a form which is either sludge or liquid				
Permitted waste types				
Source	**Sub-source**	**Waste**	**Description**	**Additional restrictions**

		code		
01 Waste resulting from exploration, mining, quarrying and physical and chemical treatment of minerals	01 01 wastes from mineral excavation	01 01 02	Wastes from mineral non-metalliferous excavation	Restricted to waste overburden and interburden only.
	01 04 wastes from physical and chemical processing of non-metalliferous minerals	01 04 08	Waste gravel and crushed rocks other than those mentioned in 01 04 06	
		01 04 09	Waste sand and clays	
02 Waste from agriculture, horticulture, aquaculture, forestry, hunting and fishing, food preparation and processing	02 04 wastes from sugar processing	02 04 01	Soil from cleaning and washing beet	
10 Wastes from thermal processes	10 12 wastes from manufacture of ceramic goods, bricks, tiles and construction products	10 12 08	Waste ceramics, bricks, tiles and construction products (after thermal processing)	
	10 13 waste from manufacture of cement, lime and plaster and articles and products made from them	10 13 14	Waste concrete	
17 Construction and demolition wastes	17 01 concrete, bricks, tiles and ceramics	17 01 01	Concrete	
		17 01 02	Bricks	
		17 01 03	Tiles and ceramics	
		17 01 07	Mixtures of concrete, bricks, tiles and ceramics other than those mentioned in 17 01 06	Metal from reinforced concrete must have been removed.
	17 03 bituminous mixtures	17 03 02	Bituminous mixtures other than those mentioned in 17 03 01	Road planings only.

	17 05 soil stones and dredging spoil	17 05 04	Soil and stones other than those mentioned in 17 05 03	Restricted to topsoil, peat, subsoil and stones only.
19 Wastes from waste management facilities	19 12 wastes from the mechanical treatment of waste (for example sorting, crushing, compacting, pelletising) not otherwise specified	19 12 09	Minerals (for example sand, stones) only	Restricted to wastes from treatment of waste aggregates that are otherwise naturally occurring minerals. Does not include fines from treatment of any non-hazardous waste or gypsum from recovered plasterboard.
		19 12 12	Other wastes (including mixtures of materials) from mechanical treatment of wastes other than those mentioned in 19 12 11	Restricted to crushed bricks, tiles, concrete and ceramics only. Metal from reinforced concrete must be removed. Does not include fines from treatment of any non-hazardous waste or gypsum from recovered plasterboard.
20 Municipal wastes (household waste and similar commercial, industrial and institutional wastes) including separately collected fractions	20 02 garden and park wastes	20 02 02	Soil and stones	Restricted to topsoil, peat, subsoil and stones only.

2.6 Waste acceptance procedures

2.6.1 The operator shall obtain, as a minimum, the following information about the characteristics of each waste stream prior to receiving the waste at the site:

(a) the full address where the waste was produced; and

(b) the identity of the producer; and

(c) all the reasonably identifiable previous uses of the producer site where the waste is excavation waste; and

(d) the process giving rise to the waste; and

(e) the physical appearance of the waste including colour and texture; and

(f) where a weighbridge isn't used a metric conversion factor for volume (cubic metres) to weight (tonnes) for each waste stream; and

(g) the quantity of waste to be imported; and

(h) evidence of compliance with condition 2.5.1.

2.6.2 The operator shall maintain records demonstrating compliance with condition 2.6.1, which shall be kept until the permit is surrendered.

2.6.3 The operator shall satisfy themselves that any waste accepted for recovery conforms to the information submitted by the holder required by condition 2.6.1 and shall visually inspect:

(a) without unloading it, waste that is in an open container or open vehicle on arrival at the site; and

(b) waste at the point of deposit;

2.6.4 Any waste that does not comply with all of the conditions of 2.5 or fit the description of the waste recorded in 2.6.1 shall be rejected and shall be:

(a) removed from the site; or

(b) moved to a designated quarantine area pending removal.

3 Emissions and monitoring

3.1 Emissions of substances not controlled by emission limits

3.1.1 Emissions of substances not controlled by emission limits (excluding odour) shall not cause pollution. The operator shall not be taken to have breached this condition if appropriate measures, including, but not limited to, those specified in any approved emissions management plan, have been taken to prevent or where that is not practicable, to minimise, those emissions.

3.1.2 The operator shall:

(a) if notified by the Environment Agency that the activities are giving rise to pollution, submit to the Environment Agency for approval within the period specified, an emissions management plan which identifies and minimises the risks of pollution from emissions of substances not controlled by emission limits;

(b) implement the approved emissions management plan, from the date of approval, unless otherwise agreed in writing by the Environment Agency.

3.1.3 All liquids in containers, whose emission to water or land could cause pollution, shall be provided with secondary containment, unless the operator has used other appropriate measures to prevent or where that is not practicable, to minimise, leakage and spillage from the primary container.

3.2 Odour

3.2.1 Emissions from the activities shall be free from odour at levels likely to cause pollution outside the site, as perceived by an authorised officer of the Environment Agency, unless the operator has used appropriate measures, including, but not limited to, those specified in any approved odour management plan, to prevent or where that is not practicable to minimise the odour.

3.2.2 The operator shall:

(a) if notified by the Environment Agency that the activities are giving rise to pollution outside the site due to odour, submit to the Environment Agency for approval within the period specified, an odour management plan which identifies and minimises the risks of pollution from odour;

(b) implement the approved odour management plan, from the date of approval, unless otherwise agreed in writing by the Environment Agency.

3.3 Noise and vibration

3.3.1 Emissions from the activities shall be free from noise and vibration at levels likely to cause pollution outside the site, as perceived by an authorised officer of the Environment Agency, unless the operator has used appropriate measures, including, but not limited to, those specified in any approved noise and vibration management plan to prevent or where that is not practicable to

3.3.2 The operator shall:

(a) if notified by the Environment Agency that the activities are giving rise to pollution outside the site due to noise and vibration, submit to the Environment Agency for approval within the period specified, a noise and vibration management plan which identifies and minimises the risks of pollution from noise and vibration;

(b) implement the approved noise and vibration management plan, from the date of approval, unless otherwise agreed in writing by the Environment Agency.

4 Information

4.1 Records

4.1.1 All records required to be made by this permit shall:

(a) be legible;

(b) be made as soon as reasonably practicable;

(c) if amended, be amended in such a way that the original and any subsequent amendments remain legible, or are capable of retrieval; and

(d) be retained, unless otherwise agreed in writing by the Environment Agency, for at least 6 years from the date when the records were made, or in the case of the following records until permit surrender:

(i) off-site environmental effects; and

(ii) matters which affect the condition of the land and groundwater.

4.1.2 The operator shall keep on site all records, plans and the management system required to be maintained by these standard rules, unless otherwise agreed in writing by the Environment Agency.

4.2 Reporting

4.2.1 The operator shall send all reports and notifications required by these standard rules to the Environment Agency using the contact details supplied in writing by the Environment Agency.

4.2.2 Within one month of the end of each quarter, the operator shall submit to the Environment Agency using the form made available for the purpose, the information specified on the form relating to each site and the waste accepted and removed from it during the previous quarter.

4.2.3 The operator shall:

(a) submit the plan required under rule 2.2.3 from the survey required by rule 2.2.2 (a) to the Environment Agency prior to commencement of operations unless otherwise agreed in writing by the Environment Agency.

(b) submit the plan required under rule 2.2.3 from the survey required by rule 2.2.2 (b) to the Environment Agency within one month of the completion of the recovery activity unless otherwise agreed in writing by the Environment Agency.

4.3 Notifications

4.3.1 The operator shall notify the Environment Agency in writing:

(a) at least 14 days before the commencement of the recovery operation; and

(b) within 14 days of completion of the recovery operation.

4.3.2 The Environment Agency shall be notified without delay following the detection of:

(a) any malfunction, breakdown or failure of equipment or techniques, accident, or emission of a substance not controlled by an emission limit which has caused, is causing or may cause significant pollution;

(b) the breach of a limit specified in the permit; or

(c) any significant adverse environmental effects.

4.3.3 Written confirmation of actual or potential pollution incidents and breaches of emissions shall be submitted within 24 hours.

4.3.4 Where the Environment Agency has requested in writing that it shall be notified when the operator is to undertake monitoring and/or spot sampling, the operator shall inform the Environment Agency when the relevant monitoring and/or spot sampling is to take place. The operator shall provide this information to the Environment Agency at least 14 days before the date the monitoring is to be undertaken.

4.3.5 The Environment Agency shall be notified within 14 days of the occurrence of the following matters, except where such disclosure is prohibited by Stock Exchange rules.

(a) Where the operator is a registered company:

- any change in the operator's trading name, registered name or registered office address; and
- any steps taken with a view to the operator going into administration, entering into a company voluntary arrangement or being wound up.

(b) Where the operator is a corporate body other than a registered company:

- any change in the operator's name or address; and
- any steps taken with a view to the dissolution of the operator.

(c) In any other case:

- the death of any of the named operators (where the operator consists of more than one named individual);
- any change in the operator's name(s) and address(es); and
- any steps taken with a view to the operator, or any one of them, going into bankruptcy, entering into a composition or arrangement with creditors, or, in the case of them being a partnership, dissolving the partnership.

4.4 Interpretation

4.4.1 In these standard rules the expressions listed below shall have the meaning given.

4.4.2 In these standard rules references to reports and notifications mean written reports and notifications, except when reference is being made to notification being made "without delay", in which case it may be provided by telephone.

"accident" means an accident that may result in pollution.

"approved waste recovery plan" means a plan that has been approved by the Environment Agency that demonstrates and gives evidence that the operation carried out under these standard rules meets the definition of waste recovery, and will continue to do so throughout the duration of the permitted operation.

“authorised officer” means any person authorised by the Environment Agency under section 108(1) of The Environment Act 1995 to exercise, in accordance with the terms of any such authorisation, any power specified in Section 108(4) of that Act.

“air quality management area” means within the meaning of the Environment Act 1995 an area which has been designated by the Local Authority where it has concerns that the Air Quality Objectives will not be met and needs to put in a Local Air Quality action plan.

“aquifer” means subsurface layer or layers of rock or other geological strata of sufficient porosity and permeability to allow either a significant flow of groundwater or the abstraction of significant quantities of groundwater.

“construction work” means the carrying out of any building, civil engineering or engineering work and includes the building, alteration, conversion, repair, upkeep or other maintenance of a structure and the preparation of a site for an intended structure. It includes drainage works.

“ecological improvement” means providing, maintaining or improving the soils ability to provide a growing medium including for growth of vegetation on landscaping and for recreational and amenity uses.

“emissions of substances” means emissions of substances to air, water or land from the activities, from localised or diffuse sources.

“European Site” means candidate or Special Area of Conservation and proposed or Special Protection Area in England and Wales, within the meaning of Council Directives 79/409/EEC on the conservation of wild birds and 92/43/EEC on the conservation of natural habitats and of wild flora and fauna and the Conservation of Habitats and Species Regulations 2010. Internationally designated Ramsar sites are dealt with in the same way as European sites as a matter of government policy and for the purpose of these rules will be considered as a European Site.

“good habitat” means rough (especially tussocky) grassland, scrub and woodland.

“groundwater” means all water, which is below the surface of the ground in the saturation zone (below the water table) and in direct contact with the ground or subsoil.

“groundwater Source Protection Zone” has the meaning given in the document titled “Groundwater Protection: Principles and Practice” published by the Environment Agency in 2013.

“historical landfill” means any area of land previously used for the disposal of waste that is no longer regulated by an environmental permit.

“inert waste” means waste that does not undergo any significant physical, chemical or biological transformations. Inert waste will not dissolve, burn or otherwise physically or chemically react, biodegrade or adversely affect other matter with which it comes into contact in a way likely to give rise to environmental pollution or harm to human health. The total leachability and pollutant content of the waste and the ecotoxicity of the leachate must be insignificant, and in particular not endanger the quality of surface water and/or groundwater.

“interburden” means material that lies between two layers of economic interest, such as the material separating coal seams within strata.

“overburden" (also called waste or spoil) is the rock and soil that typically lies above a layer of economic interest such as a coal seam or sand and gravel workings. Overburden is distinct from tailings, (the material that remains after economically valuable components have been extracted from the generally finely milled ore). Overburden is removed during surface mining, but is typically not contaminated with toxic components.

"pollution" means emissions as a result of human activity which may—

(a) be harmful to human health or the quality of the environment,

(b) cause offence to a human sense,

(c) result in damage to material property, or

(d) impair or interfere with amenities and other legitimate uses of the environment.

“quarter” means a calendar year quarter commencing on 1 January, 1 April, 1 July or 1 October.

“R” means a recovery operation provided for in Annex II of Directive 2008/98/EC of the European Parliament and the Council of 19th November 2008 on waste.

“secure storage” means storage where waste cannot escape and members of the public do not have access to it.

“SSSI” means Site of Special Scientific Interest within the meaning of the Wildlife and Countryside Act 1981 (as amended by the Countryside and Rights of Way Act 2000).

“sub-soil” means a natural soil layer extending between the topsoil and the weathered bedrock below that has no or very low organic content.

“sub-water table” is any location below the typical maximum upper level of the saturated layer of an unconfined aquifer. “Typical” in this context would employ a representative winter water table level, based on hydrogeological records and/or expert opinion, and discounting extremes in weather, or artificial suppression by engineering techniques e.g. pumping.

“topsoil” means the upper layer of an in situ soil profile, more fertile than the layer below (subsoil), and which is a product of natural chemical, physical, biological and environmental processes.

“Waste code” means the six digit code referable to a type of waste in accordance with the List of Wastes and in relation to hazardous waste, includes the asterisk. ‘List of Wastes’ means the list of wastes established by Commission Decision 2000/532/EC replacing Decision 94/3/EC establishing a list of wastes pursuant to Article 1(a) of Council Directive 75/442/EEC on waste and Council Decision 94/904/EC establishing a list of hazardous waste pursuant to Article 1(4) of Council Directive 91/689/EEC on hazardous waste, as amended from time to time.

“water body” the whole (or part) of a stream, river or canal, lake or reservoir, transitional water (estuary) or stretch of coastal water. A ‘body of groundwater’ is a distinct volume of groundwater within an aquifer or aquifers.

“watercourse” means all rivers (including underground and artificial rivers), streams, estuaries, canals, lakes, ponds, and ditches as far out as the fresh-water limit.

"year” means calendar year commencing on 1st January.

End of standard rules

Fax

ENVIRONMENT AGENCY

To	Mr Phil Roberts	From	Lorraine Matthews
Company	TerraConsult	Date	26 October 2007
Fax	01925 291191	Pages	1 of 38

Phil

Copy of Churchills licence as discussed.

Yours sincerely

LORRAINE MATTHEWS
Environment Officer

Direct dial 01925 543484

If this fax is incomplete or illegible, please contact Lorraine Matthews

Appleton House
430 Birchwood Boulevard
Birchwood
Warrington WA3 7WD

001 ENVIRONMENT AGENCY 26/10 '07 12:50 FAX

THE ENVIRONMENTAL PROTECTION ACT 1990
WASTE MANAGEMENT SITE LICENCE

Churchill Enviro Limited

Woolston Deposit Ground
Off Thelwall Lane
Thelwall
Warrington
Cheshire

NGR SJ 66972 88807

EAWML/50470

ENVIRONMENT AGENCY

ENVIRONMENTAL PROTECTION ACT 1990.
WASTE MANAGEMENT LICENCE.

LICENCE REF No :- EAWML/50470 **FACILITY TYPE :- A06**

The Environment Agency, in pursuance of Part II of the Environmental Protection Act 1990, hereby grant a waste management licence authorising the Keeping, Treatment & Recovery of controlled waste on the land specified in schedule 1 to this licence to Churchill Enviro Limited of 1 Consort Place, Off Green Walk, Bowden, Altrincham. WA14 2SH 5393456 that person being in occupation of the said land, the said licence being subject to the conditions specified in schedule 2 to this licence.

SCHEDULE 1.- SPECIFIED LAND.

The licence relates to the land at Woolston Deposit Ground, Off Thelwall Lane, Thelwall, Warrington, Cheshire (hereinafter called "the site") shown edged red on Drawing Reference Number 03/357/4/001, dated 04/06, and attached to this licence.

Signed Tracy Rimmer Name Tracy Rimmer
Environment Management Team Leader

Dated 30 April 2007

FOR ENVIRONMENT AGENCY OFFICIAL USE ONLY

YOUR ATTENTION IS DRAWN TO THE RIGHTS OF APPEAL DETAILED AT THE END OF THIS LICENCE.

Environment Agency, Appleton House, 430 Birchwood Boulevard, Birchwood, Warrington, WA3 7WD

RIGHTS OF APPEAL

Section 43(1) of the Environmental Protection Act 1990 provides that:

Where, except in pursuance of a direction given by the Secretary of State, a licence is granted subject to conditions, the applicant may appeal from the decision to the Secretary of State.

Therefore, if you feel aggrieved by the decision detailed on the attached notice, you may obtain the appropriate form on which to give written notice of an appeal from:-

The Planning Inspectorate
Environmental Appeals Team
Room 4/12 Eagle Wing
Temple Quay House
2 The Square
Temple Quay
Bristol
BS1 6PN

Tel: 0117 344 5735
Fax: 0117 344 5242

For Wales, the address is –
The Planning Inspectorate
National Assembly for Wales
Environmental Protection Division
Crown Buildings
Cardiff CF10 3NQ

Tel: 02920 823859
Fax: 02920 825150

This notice of appeal should be accompanied by the following information:

a statement of the grounds of appeal;

a copy of the licence;

a copy of any correspondence relevant to the appeal;

a copy of any other document relevant to the appeal including, in particular, any relevant consent, determination, notice, planning permission, established use certificate or certificate of lawful use or development and

a statement indicating whether you wish the appeal to be in the form of a hearing or on the basis of written representations.

You are also required to serve a copy of your notice of appeal, together with copies of any the above documents that have accompanied your notice of appeal, on the Environment Agency (at the address overleaf). You should appeal within 6 months of the date that this notice takes effect but the Secretary of State may allow notice of appeal to be given after the expiry of this time period.

SCHEDULE 2 - CONDITIONS RELATING TO THIS LICENCE

1 General considerations

1.1 Specified waste management operations

1.1.1 No waste management operations shall be authorised by this licence unless:

a specified in and undertaken in accordance with the limitations in table 1.1 below; or

b otherwise required by the conditions of this licence as being an integral part of those operations:

Table 1.1 Specified waste management operations

Specified Waste Management Operation	Permitted Waste Types which may be subject to the Specified Operation	Limits on Specified Waste Management Operations
R2: Recycling or reclamation of inorganic materials (composting area only) R3: Recycling of metals and metal compounds (Waste Recycling Centre only) R4: Recycling or reclamation of other inorganic materials. R10: Spreading of waste on land resulting in ecological improvement R11: Use of wastes obtained from any of the operations listed R13: Storage of materials for submission to reclamation of recycling operations	All	• Consisting only of deposit of waste for recovery • deposit will take place only within the area edged red as defined on drawing 03/357/4/003 • Maximum total volume to be filled 985,000m^3

Specified Waste Management Operations and Exempt Waste Management Operations

Where wastes are being brought onto the site for waste management operations which are exempt from licensing under the 1994 Regulations, then the wastes which are subject to the specified waste management operations shall be kept clearly segregated and identified from those wastes which are being kept on the site for the exempt waste management operations.

006 ENVIRONMENT AGENCY 26/10 '07 12:51 FAX

1.2 Specified surface water discharge operations

Where discharge to surface water is taking place as part of the site operations the Discharge shall consist solely of surface run off (site drainage) from all waste management activity areas within the licensed area. The discharge shall be made in the manner and at the place specified as:

a) discharging via a surface water outfall

b) discharging to the River Mersey

c) at National Grid Reference SJ 67305 89145

shown marked "Discharge Point" on Drawing Reference Number 03/357/4/003 attached to this licence.

007 ENVIRONMENT AGENCY 26/10 '07 12:51 FAX

1.3 Permitted wastes

1.3.1 *Permitted categories and types of wastes*

No wastes other than those which are categorised below in Table 1.3A, shall be deposited at the site for the purpose of the construction of the water catchment landform.

Table 1.3.A Permitted quantities of waste

Permitted Waste Categories	European Waste Catalogue Code		Maximum Permitted Quantities M^3/year
Construction, Demolition and Excavation Wastes	17 01 01	concrete	205,000m^3
	17 01 02	bricks	
	17 01 03	tiles and ceramics	
	17 01 07	mixtures of concrete, bricks, tiles and ceramics	
	17 05 04	soil and stones (excluding top soil and peat)	
	17 05 06	dredging spoil other than those mentioned in 17 05 05	
	20 02 02	soil and stones (excluding top soil and peat)	
Metal wastes			'Not Permitted'
Special Wastes			'Not Permitted'.
Degradable Household, Commercial and Industrial Wastes			'Not Permitted'.
Other wastes:			'Not Permitted'

No wastes other than those which are categorised below in Table 1.3.B, shall be accepted at the waste recycling centre.

008
ENVIRONMENT AGENCY
26/10 '07 12:51 FAX

Table 1.3.B Permitted quantities of waste

Permitted Waste Categories	European Waste Catalogue Code		Maximum Permitted Quantities m^3/year
Degradable Household, Commercial and industrial Wastes	20 02 01	Biodegradable waste	37, 500m^3
Construction, Demolition and Excavation Wastes	17 01 01	concrete	37,500m^3
	17 01 02	bricks	
	17 01 03	tiles and ceramics	
	17 01 07	mixtures of concrete, bricks, tiles and ceramics	
	17 02 02	glass	
	17 05 04	soil and stones (excluding top soil and peat)	
	17 05 06	dredging spoil other than those mentioned in 17 05 03	
	17 05 08	track ballast other than those mentioned in 17 05 07	
	19 12 09	Minerals (for example sand and stones)	
	20 02 02	soil and stones (excluding top soil and peat)	

No wastes other than those which are categorised below in Table 1.3.C, shall be accepted at the de-watering lagoons

Table 1.3.C Permitted quantities of waste

Permitted Waste Categories	European Waste Catalogue Code		Maximum Permitted Quantities M^3/year
Construction, Demolition and Excavation Wastes	17 05 08	Dredging spoil other than those mentioned in 17 05 05	80,000m^3

No waste shall be accepted at the composting facility unless Section E of the working plan has been expanded to include throughput and detailing appropriate composting risk assessments (if required) with the Environment Agency. Only wastes which are categorised below in Table 1.3.D, shall be accepted at the composting facility.

009
ENVIRONMENT AGENCY
26/10 '07 12:52 FAX

Table 1.3.D Permitted quantities of waste

Permitted Waste Categories	European Waste Catalogue Code	Maximum Permitted Quantities M³/year
Construction, Demolition and Excavation Wastes	02 01 03 plant tissue wastes 03 01 01 waste bark and wood 03 03 01 waste bark and wood	To be agreed prior to the acceptance of any waste subject to composting. See above text.
Degradable Household, Commercial and Industrial Wastes	20 01 38 wood other than that mentioned in 20 01 37 20 02 01 biodegradable wastes (gardens & parks)	

010 ENVIRONMENT AGENCY 26/10 '07 12:52 FAX

1.3.2 *Exclusion of wastes with other specified characteristics*

Notwithstanding the specification of permitted waste types under conditions 1.3.1 above, wastes shall not be accepted at the site which have any of the characteristics in Table 1.3.2.B:

Table 1.3.2.B Excluded wastes of specified form and type

Waste Characteristic	Type
Form and Type:	Powders
	Sludges
	Liquids
	Pastes
	Consisting of or containing List I substances
	Consisting of or containing List II substances

1.4 Hours of operation

The specified waste management operations authorised by this licence shall only be carried out within the times specified in the working plan.

1.5 Staffing and understanding of requirements of licence conditions and working plan

1.5.1 *Minimum staffing and supervision*

Whenever the site is open to receive or despatch waste, or is carrying out any of the specified waste management treatment or disposal operations, it shall be supervised in accordance with section A1.9 of the working plan by staff who are suitably trained and fully conversant with the requirements of the licence and the working plan regarding:

a waste acceptance and control procedures;

b operational controls and environmental monitoring;

c maintenance;

d record-keeping;

e emergency action plans;

f notifications to the Agency.

1.5.2 *Availability of licence and working plan*

A copy of this licence and the working plan shall be kept available on site for reference when required by all site staff carrying out work under the requirements of the licence.

011 ENVIRONMENT AGENCY 26/10 '07 12:52 FAX

1.5.3 *Understanding of licence and working plan*

All site staff shall be, or shall work under the direct supervision of a member of staff who is, fully conversant with those aspects of the licence conditions and working plan which are relevant to their specific duties.

1.6 Changes in technically competent persons

1.6.1 Any changes in the technically competent management of the site and the name of any incoming person [together with evidence that such person has the required technical competence] shall be submitted to the Agency in writing within 5 working days of the change in management. Technically competent management and technical competence shall be as defined under section 74 of the Environmental Protection Act 1990 and Regulations 4 and 5 of the 1994 Regulations.

1.7 Relevant convictions

1.7.1 *Notification of relevant convictions*

In the event of the Licence Holder and/or any relevant person being convicted of any relevant offence and which is in addition to any already notified to the Agency, then full details shall be provided to the Agency within 14 days following sentencing, whether or not the conviction or sentence is subsequently appealed. Such details shall include, in respect of each relevant person (as defined in section 74(7) of the Environmental Protection Act 1990 or any subsequent amendments to that section), the nature of the offence, the place and date of conviction, and any fine or other penalty imposed.

1.7.2 *Notifications of appeals against convictions*

In the event that the Licence Holder and/or any relevant person lodges an appeal against any such conviction or sentence, the Licence Holder shall notify the Agency of this within 14 days of the lodging. The Licence Holder shall notify the Agency of the results of that appeal, within 14 days of the appeal being decided.

1.8 Amendments to working plan and supporting information

1.8.1 *Amendments to working plan requiring prior consent from the Agency*

The Licence Holder shall give the Agency prior notice in writing of any proposed change to those sections of the working plan which are specified in Table 1.8 below, and to any appendices, drawings and figures which are referenced in those sections.

012 ENVIRONMENT AGENCY 26/10 '07 12:52 FAX

Table 1.8	Conditions for which changes to the working plan requiring the prior consent of the Agency	
Condition	**Subject**	**Working Plan Section**
1.1	Specified waste management operations	B1.2, C1.2, D1.2, E2
1.3	Permitted wastes	A1.5, B2, C2, D2
1.4	Hours of Operation	A1.13
1.5	Staffing and understanding of requirements of licence conditions and working plan	A1.9
2.2	Site preparation	B4.5
2.4	Site Closure	B3.2, C3.4, D3.2
4.1	Control of mud and debris	A2.3, D4.2
4.3, 4.4	Waste acceptance and control procedures	B4, C4, D4
4.6	Handling Wastes with specified hazardous characteristics or forms	C5, D5
4.7	Waste Discharge and emplacement	B4
5.1	Surface water monitoring and reporting programme	B3, C3, D3
7.1	Control, monitoring and reporting of airborne emissions of powders, dusts, fibres and particulates.	B5, C5, D5
7.2	Control of noise	B5, C5, D5
7.3	Control of Litter	B5, C5, D5

26/10 '07 12:53 FAX ENVIRONMENT AGENCY 013

1.8.2 The notice shall be accompanied by a copy of the proposed changes, and by a written assessment of the effect that implementing the proposed change to the working plan would have on the risk posed by the site to human health and the environment.

The Licence Holder shall provide up to 6 additional copies of the proposed change and supporting risk assessment to the Agency, when required by the Agency in writing.

The proposed change to the working plan shall not be implemented unless the Agency has given its written consent to it. Following consent, the Licence Holder shall give the Agency prior written notification of the implementation date of the change, and from that date the changed section shall be deemed to be incorporated in the working plan in replacement of the previous version of that section.

26/10 '07 12:53 FAX ENVIRONMENT AGENCY 014

Amendments to the working plan requiring prior notification to the Agency

1.8.3 Except where it is specified under condition 1.8.1 above that the amendment of specified sections of the working plan requires the prior consent of the Agency, the Licence Holder shall give the Agency not less than 7 days prior written notice of any change to the working plan and to any appendices, drawings and figures which are referenced from those sections.

The notice shall be accompanied by a copy of the specified changes.

The Licence Holder shall provide up to 6 additional copies of the proposed change to the Agency, when required by the Agency in writing.

Such changes to the working plan shall be deemed to be incorporated in the working plan and implemented on the date specified to the Agency in the amendment notification.

1.9 Notification of change of operator's or holder's details

The following information shall be notified in writing within 5 working days to the Agency:

i any change in the Licence Holder's trading name, registered name or registered office address;

ii any steps taken with a view to the Licence Holder going into administration, entering into a company voluntary arrangement or being wound up;

iii the operator at the time of issue of the licence and of any change in the operator or in the operator's trading name, address, registered name or registered office address (if different from the Licence Holder);

1.10 Notification of preparatory works

No preparatory works shall be undertaken until at least 7 days prior notice in writing has been given to the Agency of the intention to do so. The notification shall include details of what work is being done and when.

1.11 Notification of commencement, cessation and recommencement of waste handling operations

1.11.1 *Specified waste management operations*

No specified waste management operation shall be carried out until at least 7 days prior notice in writing has been given to the Agency of the intention to commence carrying out the specified waste management operation.

015 ENVIRONMENT AGENCY 26/10 '07 12:53 FAX

Cessation and recommencement of receiving wastes

1.11.2 In the event that the site ceases receiving wastes for longer than 1 month then within 7 days following the elapse of that time, the Licence Holder shall inform the Agency in writing of the date of cessation and of the planned date of recommencement. In the event that the site recommences receiving wastes sooner than the notified date then the Licence Holder shall give the Agency not less than 7 days prior notice in writing.

1.12 Notifications and submissions to Agency

Except where otherwise specified, all notifications and submissions to the Agency under the requirements of these licence conditions:

a shall be made in writing to the address specified by the Agency in writing at the time of issue of this licence, or as subsequently specified by written notification to the Licence Holder;

b shall quote the licence reference number and the name of the Licence Holder.

016 ENVIRONMENT AGENCY 26/10 '07 12:54 FAX

2 Site engineering for pollution prevention and control

2.1 Engineering surveys

A network of stable, permanent survey control stations [minimum four] shall be established and maintained for the control of all survey work around the site. The stations shall be referenced to Ordnance Survey National Grid co-ordinates, the grid alignment to be within +/-1 metre and Levels referenced to Ordnance Datum. The accuracy of horizontal control shall not be less than 1:20 000. The level values of adjacent stations shall agree to less than or equal to 0.005 metres. No waste shall be accepted at the site until a schedule of descriptions, co-ordinates and level values of all control stations, together with details of Bench Marks used, has been submitted in writing to the Agency.

A topographic survey shall be carried out immediately before the start of filling of each phase, at annual intervals (unless otherwise agreed in writing by the Agency), and at the completion of restoration. The scale shall adequately show surveyed features and be at least [1:1250]. The surveys shall be sufficient to produce plans that include all roads, structures, boundaries, monitoring points and all other relevant site features. The results of the survey shall be presented as a plan, including the immediate neighbouring landform or an indication of that landform. Plan positions of ground features to be shown to within 1 metre. Spot levels to 0.01m shall be shown at significant landform changes to a density to adequately indicate the true landform, no greater than 50 metre interval in open areas of even gradient, closer when indicating embankments, stockpiles, etc. A calculation of void space in cubic metres, taking account of settlement, shall be carried out at start and at each annual survey. The results of the survey and the calculation shall be submitted to the Environment Agency within 1 month of the survey being carried out.

2.2 Site preparation – Engineering Requirements

No waste shall be deposited in any phase unless:

a An engineered liner has been constructed and installed in accordance with "Guidance for landfill Sites for Inert Waste" Document 257_05, or

b a risk assessment process has been used to inform the design of the site to ensure that the potential for environmentally harmful emissions to the environment is low, and this has been agreed in writing with the Agency

c at least 5 working days notice has been given in writing to the Agency of the intention to commence waste deposits in that phase.

017 ENVIRONMENT AGENCY 26/10 '07 12:54 FAX

2.3 Site completion - final landform and engineering

In the event that the specified waste management operations on the site cease and it is confirmed to the Agency that they will not be resumed, the Licence Holder shall ensure that any uncompleted phases are provided with the protection required under the other conditions of this licence, so as to achieve a landform that meets the following standards:

a maximum gradient of [1 in 6];

b minimum gradients on Drawing No. 03/357/4/004

2.4 Site Closure - Final Landform

The Licence Holder shall, subject to the conditions of this licence, cease the deposit of waste in accordance with section B3.2 of the working plan.

26/10 '07 12:54 FAX ENVIRONMENT AGENCY 018

3 Site infrastructure

3.1 Provision of site identification board

3.1.1 No wastes shall be received at the site until an identification board has been provided at or near the site entrance.

3.1.2 The identification board shall be inspected at least once per week. In the event of damage or defect, the board shall be repaired or replaced within 7 working days.

3.1.3 The board shall be easily readable from outside the site entrance in daylight hours, and shall display the following information:

a Site name and address;

b Licence Holder name (company name, not individual name unless justified as necessary);

c Operator name (company name, not individual name unless justified as necessary);

d Licence number;

e Emergency contact name and telephone number (for security reasons, personal names and home phone numbers should not be used except where no alternative is practicable);

f Statement that the site is licensed by the Environment Agency;

g Agency national numbers: 08708 506 605 and 0800 807060;

h Days and hours site is open to receive waste.

The location of the noticeboard should be such that it is clear that it does not designate areas outside the licensed site and does not encourage illegal tipping.

3.2 Site security

Site security systems shall be provided at all times during the subsistence of this licence, the objective of which shall be to prevent access by humans and livestock which is not authorised either by the Licence Holder or under legal powers of entry. These shall be installed, operated and maintained, and shall be fully documented and recorded, in accordance with the requirements detailed in table 3.2 below:

26/10 '07 12:54 FAX ENVIRONMENT AGENCY 019

Table 3.2 Site security system standards	
Site security system	**Specified standards**
Timetable of provision	Prior to commencement of specified operations
Design standards	In accordance with A1.14 of the Working Plan
Operational standards	The site shall be kept closed and secure at all times when unattended
Maintenance standards	The site security shall be fully inspected at the commencement of each working day, and recorded in the site diary. Any defects or damage shall be made secure by the end of the working day, and shall be repaired within 7 working days of the damage being detected. All repairs shall be recorded in the site diary.

020 ENVIRONMENT AGENCY 26/10 '07 12:55 FAX

4 Site operations

4.1 Control of mud and debris

Prevention of mud and debris on road

4.1.1 Whenever the site is receiving or despatching wastes measures shall be provided, operated and maintained in accordance with section A2.3 of the working plan, with the objective of preventing the deposit or tracking of mud or debris arising from the site onto public areas outside the site, which shall include public highways and areas of public access.

4.1.2 All vehicles leaving areas of the site which are operational or upon which engineering works are being carried out shall, before leaving the site, be cleaned as necessary and shall be checked to ensure that they are clear of loose waste and that their loads are secure.

Remediation of mud and debris on road

4.1.3 In the event that mud or debris arising from the site is deposited onto public areas outside the site, remedial measures shall be implemented immediately, in accordance with section A2.3 of the working plan.

4.2 Fires on the site

Prohibition of unauthorised fires on site

4.2.1 No wastes shall be burned on the site

Actions to be taken in the event of a fire

4.2.2 In the event of a fire on the site, notwithstanding any actions taken to suppress or extinguish the fire, the following actions shall be taken immediately and recorded in the site diary:

- the Agency shall be informed of the fire;
- so far as practicable contaminated site drainage shall be prevented from entering the site surface water management system, drains, watercourses or unsurfaced ground.

021 ENVIRONMENT AGENCY 26/10 '07 12:55 FAX

4.3 Waste acceptance and control procedures

No waste shall be accepted at the site until the Waste Acceptance procedures detailed in Section B4.4 of the working plan have been justified based on the conceptual model and updated groundwater risk assessment and the results of the additional background monitoring as detailed in the 28th March 2007 letter from Terraconsult to the Agency, and this has been agreed in writing with the Agency.

Once agreed in writing with the Agency, all wastes accepted at the site shall be handled, kept and recorded in accordance with the working plan and the standards specified in Table 4.3 below.

022 ENVIRONMENT AGENCY 26/10 '07 12:55 FAX

Table 4.3 Standards for waste acceptance and control procedures

Stage of Waste Handling	Specified standards
Pre-delivery and delivery of wastes	Before or at the time of delivery, or of the first of a series of deliveries, provided that the type of waste remains unchanged, the Licence Holder shall ensure that the waste in question can be accepted at the site according to the other conditions of this licence, and that this is recorded in accordance with condition 4.3.1
Waste reception	Wastes shall only be received at the site in accordance with the working plan On acceptance of each delivery the Licence Holder shall provide a written receipt to the person delivering it. All incoming waste shall be kept in the waste reception area unless it has been confirmed for acceptance at the site or has been placed in the designated quarantine storage area pending removal from the site.
Waste inspection	All wastes received at the site shall be inspected in accordance with section B4.4 of the working plan at the point of deposit to confirm their description and composition.
Waste rejection	Wastes which are not permitted by this licence shall be rejected and the Agency must be informed as soon as possible and in any event within seven days. Quantities and types of all wastes which are not accepted at the landfill, including origin, date of delivery and non-acceptance, identity of the producer or collector in the case of municipal waste shall be recorded in a log maintained for that purpose.
Quarantine storage and rejection of wastes	i) Any wastes which are received at the site but rejected as a result of inspection or testing shall be placed in a designated quarantine storage area, and, where these are hazardous wastes, the Agency shall be informed immediately; ii) Quarantined wastes shall be kept segregated from other wastes in the quarantine area which are likely to be incompatible; iii) Quarantined wastes shall be removed from the site within 7 days; iv) The maximum quantity of waste to be kept in the quarantine storage area shall be 20 m^3 at any one time; v) A record shall be kept in the site diary of all rejected wastes; All wastes despatched from the site shall be inspected prior to dispatch to confirm their description and composition.
Identification of wastes	i) Waste reception areas, storage bays and quarantine areas shall all be clearly labelled
Incompatible wastes or other potentially polluting materials which are to be used in combination with those wastes in the specified	Incompatible wastes or other potentially polluting materials which are to be used in combination with those wastes in the specified waste management operations, which are likely, in combination with each other or with other material at the facility, to give rise to pollution of the environment or harm to human health outside the site, shall be clearly identified and kept physically separate in designated areas, as

26/10 '07 12:55 FAX ENVIRONMENT AGENCY 023

waste management operations	specified in plan 03/357/4/003

4.4 Waste sampling and testing

Incoming wastes shall be sampled and tested to confirm their composition and characteristics in accordance with the working plan.

4.5 Waste quantity measurement systems

Means of measurement

All wastes accepted at and despatched from the site shall be measured in accordance with the working plan.

4.6 Handling of wastes with specified hazardous properties or forms

a Notwithstanding the specification of permitted waste types under condition 1.2, wastes displaying any of the properties or forms specified in Table 4.6 shall not be accepted at the site unless handled in accordance with section B5.3, C5.2 & D5.2 of the working plan so as to meet the limitations specified in Table 4.6.

Table 4.6	Limitations on inert wastes with specified hazardous characteristics
a) Solid wastes which when handled are likely to generate significant quantities of dusts, fibres or particulates.	These wastes are only permitted if : • the site is provided with a permanent water supply • bowsering equipment is provided, and used at all times when significant quantities of dust, fibres or particulates are likely to be generated

b No composting activities shall be conducted on site unless a site-specific risk assessment, based on clear, independent scientific evidence which shows that the bioaerosol levels are and can be maintained at appropriate levels at the site boundary.

4.7 Waste discharge and emplacement

4.7.1 Wastes shall be emplaced in such a way as to ensure stability and to avoid slippages of the mass of waste as associated engineering and infrastructure.

024 ENVIRONMENT AGENCY 26/10 '07 12:56 FAX

Methods and procedures of waste discharge and emplacement

4.7.2 No wastes shall be deposited in any phase or cell other than in accordance with section B4.1 of the working plan

4.8 Removal of residual wastes from site

In the event that the specified waste management operations on the site cease and the Agency has reasonable grounds to believe that they will not be resumed within 2 months then, notwithstanding the operational limits on storage times of wastes specified in the other conditions of this licence, the licence holder shall ensure that all wastes remaining on the site shall be removed by the date specified by the Agency in writing. This shall not apply to any wastes which have been deposited on the site in accordance with the other conditions of this licence or prior to the issue of this licence.

026/10 '07 12:56 FAX ENVIRONMENT AGENCY 025

5 Pollution control, monitoring and reporting

5.1 Surface water quality monitoring and reporting systems

Surface water monitoring and sampling programme

5.1.1 Monitoring and sampling of surface water in the vicinity of the site shall be carried out and recorded in accordance with section 6 of this licence and section B5.2 of the working plan.

Baseline monitoring results

5.1.2 No wastes shall be deposited in a phase until the results of baseline monitoring investigation has been agreed in writing with the Agency. This shall cover a period of 2 consecutive months prior to the programmed date for commencing deposit in such phase, the results interpreted and a report compiled and submitted to the Agency and their receipt has been acknowledged in writing by the Agency.

Monitoring and sampling records

5.1.3 A record of the surface water monitoring and sampling results shall be made and submitted to the Agency in accordance with the standards specified in Table 5.1 below.

026 ENVIRONMENT AGENCY 26/10 '07 12:56 FAX

Table 5.1 Standards for surface water monitoring and sampling records

Surface water monitoring and Sampling Records	Specified standards
Making of records	i) Trigger levels for Surface water parameters shall be agreed in writing by the Agency prior to any deposit of waste ii) Records shall include details of: I. measurements/samples to support analytical and QA requirements; e.g. dates, times, locations, weather conditions; and interpretation and review of results against site II. design lifetime and projected waste stabilisation curve
Submission of records	A copy of the quality assured records of each monitoring and sampling result, with an interpretation of the results against background and trigger levels, shall be submitted to the Agency on a monthly basis, within 1 month of its being carried out, in the format to be agreed with the Agency.

Surface water monitoring action plan

5.1.4 No wastes shall be deposited at the site unless a Surface Water monitoring action plan has been agreed in writing with the Agency. In the event that any results exceed the trigger level to be agreed in accordance with condition 5.1.3

a the results shall be notified to the Agency immediately and confirmed in writing immediately;

b the surface water generation action plan specified above shall be implemented.

5.2 Groundwater Monitoring

5.2.1 No waste shall be accepted at the site unless a the updated groundwater risk assessment detailed in the 28th March 2006 letter from Terraconsult has been completed and agreed in writing with the Environment Agency.

5.2.2 No waste shall be accepted at the site unless one borehole up groundwater gradient and two boreholes down groundwater gradient has been installed in accordance with a construction quality assurance methodology agreed in writing with the Agency.

5.2.3 No wastes shall be deposited in a phase until the results of the groundwater baseline monitoring investigation has been agreed in writing with the Agency. This shall cover a period of 2 consecutive months prior to the programmed date for commencing deposit in such phase, the results interpreted and a report compiled and submitted to the Agency and their receipt has been acknowledged in writing by the Agency.

027 ENVIRONMENT AGENCY 26/10 '07 12:56 FAX

5.2.4 A record of the groundwater monitoring and sampling results shall be made and submitted to the Agency in accordance with the standards specified in Table 5.2 below.

Table 5.2 Standards for groundwater monitoring and sampling records

Groundwater monitoring and Sampling Records	Specified standards
Making of records	iii) Trigger levels for groundwater parameters shall be agreed in writing by the Agency prior to any deposit of waste iv) Records shall include details of: iii. measurements/samples to support analytical and QA requirements; e.g. dates, times, locations, weather conditions; and interpretation and review of results against site iv. design lifetime and projected waste stabilisation curve
Submission of records	A copy of the quality assured records of each monitoring and sampling result, with an interpretation of the results against background and trigger levels, shall be submitted to the Agency on a monthly basis, within 1 month of its being carried out, in the format to be agreed with the Agency.

5.2.5 No wastes shall be deposited at the site unless a groundwater monitoring action plan has been agreed in writing with the Agency. In the event that any results exceed the trigger level to be agreed in accordance with condition 5.2.4

a the results shall be notified to the Agency immediately and confirmed in writing immediately;

b the groundwater generation action plan specified above shall be implemented.

5.3 Landfill gas

5.3.1 No waste shall be accepted at the site unless a methodology has been agreed in writing with the Agency for Monitoring of Landfill gas within waste and outside the boundary of the site at specified frequencies.

5.3.2 No waste shall be accepted at the site unless trigger levels for landfill gas and a landfill gas action plan (in the event of trigger levels being exceeded) have been agreed in writing with the Agency.

028 ENVIRONMENT AGENCY 26/10 '07 12:57 FAX

6 Sampling Point

An appropriately labelled sample point shall be provided before waste is accepted and maintained at National Grid Reference SJ 67305 89145, as shown marked 'Discharge point' on the attached Plan 03/357/4/003 so that a representative sample of the Discharge may be obtained. The licence holder shall ensure that all constituents of the Discharge pass through the said sampling point at all times and in any legal proceedings it shall, for the purposes of Section 10 of the Rivers (Prevention of Pollution) Act 1961, be presumed, until the contrary is shown, that any sample of the Discharge taken at the said sampling point is a sample of what was being discharged into controlled waters.

6.1 Composition

There shall be no discharge of water from the discharge point until the composition has been agreed in writing with the Agency following the submission of the baseline monitoring investigation as required by condition 5.1.2.

As far as is reasonably practicable, the site and its facilities shall be operated so as to prevent the Discharge from containing any significant trace of visible oil or grease.

029 ENVIRONMENT AGENCY 26/10 '07 12:57 FAX

7 Amenity management and reporting

7.1 Control, monitoring and reporting of dusts, fibres and particulates

7.1.1 Throughout the operational life of the site, measures to control and minimise aerial emissions of dusts, fibres and particulates from the site shall be carried out in accordance with section B5.3, C5.2 and D5.2 of the working plan to meet the standards specified in table 7.1 below. Such measures shall be prevent releases in such quantities or concentrations that are likely to cause pollution of the environment or harm to human health or serious detriment to the amenity of the locality.

Table 7.1 Standards for monitoring and control of aerial emissions of dusts, fibres and particulates

	Specified standards
a) Monitoring	Visual monitoring of aerial emissions shall be carried out by site staff supervising waste handling operations.
b) Control: aerial emissions action plan	i) On detection or notification of visible aerial emissions that are or are likely to be transported beyond the site boundary, immediate action is to be taken to stop the waste handling operations giving rise to the emission and to suppress any aerial emission from deposited waste. ii) The incident and the remedial action shall be recorded in the site diary.

7.1.2 All emissions to air from the specified waste management operations on the site shall be free from visible concentrations of dusts, fibres or particulates as are likely to cause pollution of the environment or harm to human health or serious detriment to the amenity of the locality outside the site boundary, as perceived by an authorised officer of the Agency.

7.2 Control of noise

7.2.1 Measures shall be implemented and maintained throughout the operational life of the site, in accordance with this condition and section B5.7, C5.4, D5.6 of the working plan to control and minimise the levels of noise from operations on the site beyond the site boundary.

030 ENVIRONMENT AGENCY 26/10 '07 12:57 FAX

7.3 Monitoring and control of pest infestations

7.3.1 Throughout the operational life of the site measures to control and minimise pests on the site, shall be carried out in accordance with the standards specified in table 7.3 below. Such measures shall prevent pest infestations that are likely to cause pollution of the environment or harm to human health or serious detriment to the amenity of the locality.

Table7.3 Standards for monitoring and control of pest infestations

	Specified standards
a) Monitoring for pest infestations	i) An inspection of the site for pest infestations shall be carried at monthly intervals by the site supervisor, and shall be recorded in the site diary.
b) Control: pest control action plan	i) On detection or notification of pest infestations immediate action to be taken to secure the attendance of a professional pest control contractor to eliminate the pest infestation. ii) The incident and the remedial action shall be recorded in the site diary.

7.4 Control of litter

7.4.1 Measures shall be implemented and maintained throughout the operational life of the site, in accordance with section B5.6, D.5.5 of the working plan, to prevent the escape of litter from the confines of the site.

In the event that litter does escape from the site, it shall be retrieved as soon as practicable.

031 ENVIRONMENT AGENCY 26/10 '07 12:57 FAX

8 Site records

8.1 Security and availability of records

Security of records

8.1.1 All records which are required to be made under the other conditions of this licence and the working plan shall be maintained and kept secure from loss, damage or deterioration, and shall be kept at a location to be agreed with the Agency and in accordance with the requirements specified in Table 8.1 below.

Availability of records

8.1.2 All records which are required to be made under the other conditions of this licence and the working plan shall be made available for inspection at the place where they are kept immediately when required by an authorised officer of the Agency.

Table 8.1 Standards for keeping of site records

Site records	Specified standards
Wastes accepted at the site; Wastes rejected. And/or despatched from the site; Environmental monitoring records; Site diaries.	1. All records shall be stored either: a) on paper in a secure cabinet or cupboard; or b) on computer disc with a back up copy. 2. Records shall be kept for a minimum of two years.

8.2 Records of waste movements

Recording of wastes accepted and removed

8.2.1 A record shall be kept of each load of waste accepted and each load of waste removed from site. This record shall include the following details:

a Loads in :- Nature (solid, sludge or liquid), waste type as specified under condition 1.2, quantity (tonnes), date received, date accepted.

b Loads out :- Nature (solid, liquid or sludge), waste type as specified under condition 1.2, quantity of waste removed (tonnes), date removed.

Summary records of wastes accepted and removed

8.2.2 A summary record of the waste types accepted and removed from the site shall be made for each quarter of the financial year, and shall be submitted to the Agency within 1 month following the end of the quarter. The summary record shall be in a format agreed by the Agency in writing.

26/10 '07 12:58 FAX ENVIRONMENT AGENCY 032

8.3 Site diary

8.3.1 A site diary shall be kept secure and shall be available for inspection at the site when required by an authorised officer of the Agency. This shall include a record of the following events:

- **a.** Start and finish of site preparatory works
- **b.** Start and finish of daily waste management activies on site
- **c.** Plant maintenance and breakdown
- **d.** Emergencies and actions taken
- **e.** Problems with wastes received and actions taken
- **f.** Site inspections including environmental monitoring by the operator, their findings and remedial responses
- **g.** Despatch of records to the Agency
- **h.** Severe weather conditions.
- **i.** Technically competent management attendance on site; time onto site and time left site
- **j.** Complaints about site operations and actions taken.
- **k.** Environmental problems and remedial actions

8.3.2 Each record shall be completed within 24 hours of the relevant event.

8.4 Periodic reporting of environmental performance

8.4.1 The Licence Holder shall provide the Agency on an annual basis by 1st April each year, or such other time as is agreed in writing with the Agency, a report on the environmental performance of the site, which shall include the following information:

- **a** an analysis and review of the results of environmental monitoring required under these conditions, with an interpretation of the trend of the results against background and trigger levels;
- **b** a review of the risk assessment for the site, taking account of the findings under '**a**' above;
- **c** where changes to the risk assessment are identified under '**b**' above, a review of the risk management systems provided at the site.

26/10 '07 12:58 FAX ENVIRONMENT AGENCY 033

9 Interpretation

In these conditions and their interpretation, unless the context otherwise requires, the following terms have the specified meanings:

"accepted"
for waste being delivered to the site, shall mean accepted as waste input to the site for storage and/or processing and/or disposal under the specified waste management operations;

"authorised officer of the Agency"
means any person(s) authorised in writing by the Agency pursuant to section 108(1) of the 1995 Act to exercise any of the powers specified in subsection (4) of that section;

"clinical waste"
has the meaning as defined in regulation 1(2) of the Controlled Waste Regulations 1992 or any statutory provisions amending or replacing them;

"consequences"
for **risk assessments** carried out within these conditions, means the adverse effects of harm as a result of realising a **hazard** which cause the quality of human health (other than health and safety of site staff or visitors to the site covered under the Health and Safety at Work Act 1974) or the environment to be impaired in the short or longer term;

"engineer"
for engineering works specified in these conditions, means a person who works in the relevant branch of engineering, as a qualified professional;

"engineered"
for works specified in these conditions, means carried out and completed using the relevant engineering process specified in these conditions;

"engineered landfill containment system"
means all elements (other than leachate and landfill gas management systems, and intermediate and final caps), relating to engineered liners for final disposal to land, and incorporating liners for individual cells and the site as a whole, and including methods of liner protection and leakage detection;

"engineered site containment and drainage system"
means all elements relating to engineered containment of activities on the site, other than final disposal to land, and incorporating site surfacing, bunding and drainage systems, buildings and fixed tanks;

26/10 '07 12:58 FAX ENVIRONMENT AGENCY 034

"engineering"
for engineering works specified in these conditions, means the relevant process of design, construction or installation, quality assurance or validation or commissioning specified in these conditions;

"engineering survey"
means a survey carried out in accordance with recognised or approved standards by a suitably qualified competent person;

"environmental targets or receptors"
for **risk assessments** carried out within these conditions, shall mean identified human and environmental populations or components, as specified in these conditions or otherwise agreed by the Agency within these conditions;

"groundwater"
means any water contained in underground strata;

"hazard"
means a property or situation that in particular circumstances could lead to harm;

"immediately"
for carrying out of actions under the conditions, shall mean without delay and within a reasonable time, taking into account any more immediate direct action necessary to prevent or minimise risk to human health and the environment. For carrying out notifications to the Agency, shall also mean by the fastest effective means available (for example, telephone) and confirmed in writing within 1 working day (or such other time as may be agreed by the Agency within the conditions);

"inert waste "
means waste which when disposed of in or on land does not undergo any significant physical, chemical or biological transformation;

"landfill gas management system"
means all elements relating to landfill gas extraction from individual landfill cells and the landfill mass as a whole, and incorporating methods of landfill gas drainage, containment and the subsequent disposal system, whether it be a methane oxidation system, landfill gas flare, landfill gas engine(s) or otherwise, either on or off the site;

"leachate management system"
means all elements relating to leachate extraction from individual landfill cells and the landfill mass as a whole, and incorporating methods of leachate drainage, containment and the subsequent treatment and/or disposal system, either on or off the site;

"maintenance"
for engineering maintenance specified in these conditions, means the process of inspection, testing, repair of the relevant engineering works specified in these conditions;

"preparatory works"
means engineering works required prior to the carrying out of the activities authorised by this licence;

26/10 '07 12:59 FAX ENVIRONMENT AGENCY 035

"probability"

means the quantified expression of chance, denoted either as:

- the ratio or percentage of the occurrence of a particular event as one among a number of possible events;
- or as the frequency of occurrence of a particular event in a given period of time;

"received"

for waste being delivered to the site, shall mean delivered to the site and undergoing the waste acceptance procedures specified in the working plan, including storage of those wastes during those procedures prior to acceptance of the waste;

"release pathways"

for **risk assessments** carried out within these conditions, shall mean the routes by which defined **hazards** may potentially realise their **consequences**, defined in terms of releases or emissions from the site that go beyond the site containment or boundary via one or more of the following routes, either directly or indirectly: **Land; Groundwater; Surface water; Atmosphere;**

"relevant offences"

are offences within the meaning of regulation 3 of the Waste Management Licensing Regulations 1994 or any statutory provisions or regulations amending or replacing them;

"risk"

means a combination of the **probability** and **consequences** of occurrence of a defined **hazard;**

"risk assessment"

means the systematic identification, analysis, estimation and evaluation within a defined **scope** of the defined **risks** of a particular activity, operation, process or design, carried out and reported by suitably qualified or competent persons, using recognised quantified or semi-quantified methods and techniques.

Unless otherwise agreed by the Agency within these conditions, a risk assessment shall include and record the following:

- definition of the **hazards** associated with an activity, operation, process or design;
- assessment of the **probability** of those **hazards** occurring;
- determination of the potential **consequences** of those hazards for defined **environmental targets or receptors**, taking into account defined **release pathways** and defined protective measures;
- evaluation of the potential **magnitude** of those consequences and the **probability** of their occurrence;

"scope of risk assessment"

means the boundaries of the **risk assessment** and the **risks** to be assessed within those boundaries, as defined in the conditions or otherwise agreed by the Agency within the conditions;

036 ENVIRONMENT AGENCY 26/10 '07 12:59 FAX

"hazardous waste"
has the meaning as defined by the Hazardous Waste Regulations 2004 or any statutory provisions or regulations amending or replacing them;

"specified waste management operations"
means the waste management operations authorised by condition 1.1 of this licence;

"surface water management system"
means all elements relating to collection of rain water or surface water from individual landfill phases and the landfill site as a whole, and incorporating methods of water collection, containment and the subsequent treatment and/or disposal system, either on or off the site;

"surface water"
means any lake, pond, river or watercourse whether natural or artificial;

"the 1994 Regulations"
means the Waste Management Licensing Regulations 1994 and any statutory provisions or regulations amending or replacing them.

"the Agency"
means the Environment Agency;

"the Licence Holder"
means the Licence Holder specified in this licence or other person to whom the licence has been transferred in accordance with section 40 of the Environmental Protection Act 1990;

"the operator"
means a person who is in occupation of the site and has responsibility for carrying out day to day activities at the site;

"the site"
means the land, structures, plant and equipment to which this licence relates;

"time periods, e.g. annually, quarterly, monthly, per year, etc. "
Where periods are referred to in conditions, they shall be calculated in the following way:

- annually or per year: 1 April to 31 March;
- quarterly: 1 April to 30 June, 1 July to 30 September, 1 October to 31 December, 1 January to 31 March;
- monthly: calendar month;
- weekly: Monday to Sunday.

Where the issue of the licence does not coincide with the start of any of these periods, then any relevant limits for the first period shall apply pro rata;

"waste"
means controlled waste as defined in section 75(4) of the 1990 Act and the Controlled Waste Regulations 1992 or any statutory provisions or regulations amending or replacing them;

26/10 '07 12:59 FAX ENVIRONMENT AGENCY 037

"working plan"

means the working plan identified in writing by the Agency at the time of issue of this licence and any subsequent amendments to it made in accordance with the conditions of this licence.

038 ENVIRONMENT AGENCY 26/10 '07 13:00 FAX

Appendix C Careys Waste Transfer Tickets (attenuation tank excavation)

Copyright © 1976 - 2024 Buro Happold. All rights reserved

Maher

W.Maher & Sons Ltd.
Civil Engineering Contractors

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T : 0161 776 2200 F: 0161 848 7357
E : enquiries@wmaherandsons.com
W : www.wmaherandsons.com

Waste Transfer Note

SECTION A - DESCRIPTION OF WASTE (To be completed by Holder/Producer of the waste)

EWC Code (*Tick one box only*)

	17:01:01	Concrete	X	17:05:04	Soil and stones (excl. dangerous substances)
	17:01:02	Bricks		17:09:04	Mixed construction and demolition waste
	17:01:07	Concrete, brick and tile			Other

How is the waste Contained 17.05.04 NON HAZ SOILS + STONES

8 Wheel Tipper ☐ Other (describe) ☐

SECTION B - HOLDER / PRODUCER OF THE WASTE

SIC 4 2 9 9 0

Holder / Producer: CAREYS

Location/address of the Collection Point: Co-op Live
Alan Turing Way
M11 3DU

Declaration (by Holder)
I have fulfilled my duty to apply the waste hierarchy as required by Regulation 12 of the Waste (England & Wales) Regulations 2011.

Name: DAVID CLARK Signature: D. Clark

SECTION C - PERSON COLLECTING THE WASTE (CARRIER)

SIC 4 9 4 1 0

Carrier: W Maher & Sons Ltd

Carrier Address: Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW

Carrier Registration No.: CBDU90617 Expiry Date: 25/03/2025 Issued by: Environment Agency

Date of Transfer: 25.03.22 - 25.03.23 (for multiple consignments state duration, max 12 months)

Name: KFMcEnaney Signature: Ken Mc Enaney

SECTION D - DISPOSAL / RECOVERY FACILITY

Facility Operator: W. Maher + Sons Ltd

Facility Address: Ashton Old Road

Facility Permit No.: EPR/GB 3930 AM

Date of Transfer: 25.03.22 - 25.03.23 (for multiple consignments, state duration, max 12 months)

Name: KF McEnaney Signature: Ken Mc Enaney

IF WASTE IS SENT DIRECTLY TO LANDFILL SITE IN ENGLAND OR WALES THE FOLLOWING DECLARATION MUST BE SIGNED (BY CARRIER).

I/We confirm that the waste delivered by the above named company has been treated as highlighted below.

The material has gone through a physical, thermal, chemical or biological process including: sorting characteristics of the waste have been changed/volume has been reduced/ hazardous nature has been reduced/handling has been facilitated/recovery has been enhanced. (Delete as required)

Name: Signature:

DISTRIBUTION:	WHITE-HOLDER	YELLOW-OFFICE	BLUE-FACILITY OPERATOR

THIS DOCUMENT MUST BE RETAINED UNTIL 2 YEARS AFTER LAST TRANSFER DATE SHOWN IN SECTION D 03:25

LL

Maher 4 CT CN 307976

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer:	CARGYS	Date:	7 2 23
Loaded at:	ETIHAD		
Delivered to:	AOR		
Driver:	TONY	Veh. Reg.:	UW1
Tick ☐ 1 x 8 wh. load: Off Site		Material	MUCK
Tick ☐ 1 x 8 wh. load: Delivered		Material	SOIL

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	

Foreman or Agent's Signature	

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE | Form MAH/OD/16 V.06 04/19

Maher

CN 307974

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer:	CAREYS	Date:	4 2 23
Loaded at:	ETIHAD		
Delivered to:	AOR		
Driver:	TONY	Veh. Reg.:	LW1

Tick ☐ 1 x 8 wh. load: Off Site	Material: MUCK
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature						

CONDITIONS OF SALE. It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

Maher

CN 307972

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: CAREYS	Date: 4 7 23
Loaded at: ETIHAD	
Delivered to: AOR	
Driver: TONY	Veh. Reg.: LW71
Tick ☐ 1 x 8 wh. load: Off Site	Material: MUCK
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature	CONSTANTIN SCHIPOR					

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE

Maher CT CN 307969

W. MAHER & SONS LTD. 0023596 M0054.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW

T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: CARGYS	Date: 4 2 23
Loaded at: ETIHAD	
Delivered to: / AOR	
Driver: / TONY	Veh. Reg: UW1
Tick ☐ 1 x 8 wh. load: Off Site	Material: MUCK
Tick ☐ 1 x 8 wh. load: Delivered	Material: 2A

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature						

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE | Form MAH/OD/16 V.06 04/19

Maher

W.Maher & Sons Ltd.
Civil Engineering Contractors

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T : 0161 776 2200 F: 0161 848 7357
E : enquiries@wmaherandsons.com
W : www.wmaherandsons.com

Waste Transfer Note

SECTION A - DESCRIPTION OF WASTE (To be completed by Holder/Producer of the waste)

EWC Code (*Tick one box only*)

	17:01:01	Concrete	X	17:05:04	Soil and stones (excl. dangerous substances)
	17:01:02	Bricks		17:09:04	Mixed construction and demolition waste
	17:01:07	Concrete, brick and tile			Other

How is the waste Contained 17.05.04 NON HAZ SOILS + STONES

8 Wheel Tipper ☐ Other (describe) ☐

SECTION B - HOLDER / PRODUCER OF THE WASTE

SIC 4 2 9 9 0

Holder / Producer: CAREYS

Location/address of the Collection Point: Co-op Live
Alan Turing Way
M11 3DU

Declaration (by Holder)
I have fulfilled my duty to apply the waste hierarchy as required by Regulation 12 of the Waste (England & Wales) Regulations 2011.

Name: DAVID CLARK Signature: D. Clark

SECTION C - PERSON COLLECTING THE WASTE (CARRIER)

SIC 4 9 4 1 0

Carrier: W Maher & Sons Ltd

Carrier Address: Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW

Carrier Registration No.: CBDU90617 Expiry Date: 25/03/2025 Issued by: Environment Agency

Date of Transfer: 25.03.22 - 25.03.23 (for multiple consignments state duration, max 12 months)

Name: KF McEnaney Signature: Ken Mc Enaney

SECTION D - DISPOSAL / RECOVERY FACILITY

Facility Operator: W. Maher + Sons Ltd

Facility Address: Ashton Old Road

Facility Permit No.: EPR/GB 3930 AM

Date of Transfer: 25.03.22 - 25.03.23 (for multiple consignments, state duration, max 12 months)

Name: KF McEnaney Signature: Ken Mc Enaney

IF WASTE IS SENT DIRECTLY TO LANDFILL SITE IN ENGLAND OR WALES THE FOLLOWING DECLARATION MUST BE SIGNED (BY CARRIER).

I/We confirm that the waste delivered by the above named company has been treated as highlighted below.

The material has gone through a physical, thermal, chemical or biological process including: sorting characteristics of the waste have been changed/volume has been reduced/ hazardous nature has been reduced/handling has been facilitated/recovery has been enhanced. (Delete as required)

Name: Signature:

DISTRIBUTION:	WHITE-HOLDER	YELLOW-OFFICE	BLUE-FACILITY OPERATOR

THIS DOCUMENT MUST BE RETAINED UNTIL 2 YEARS AFTER LAST TRANSFER DATE SHOWN IN SECTION D 03:25

LL

Maher CN 307986

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: CAREYS	Date: 8 2 23
Loaded at: ETIHAD	
Delivered to: ADR	
Driver: TONY	Veh. Reg.: LW1
Tick ☑ 1 x 8 wh. load: Off Site	Material: MUCK
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature						

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE | Form MAH/OD/16 V.06 04/19

Maher

W.Maher & Sons Ltd.
Civil Engineering Contractors

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T : 0161 776 2200 F: 0161 848 7357
E : enquiries@wmaherandsons.com
W : www.wmaherandsons.com

Waste Transfer Note

SECTION A - DESCRIPTION OF WASTE (To be completed by Holder/Producer of the waste)

EWC Code (*Tick one box only*)

	17:01:01	Concrete	X	17:05:04	Soil and stones (excl. dangerous substances)
	17:01:02	Bricks		17:09:04	Mixed construction and demolition waste
	17:01:07	Concrete, brick and tile			Other

How is the waste Contained 17.05.04 NON HAZ SOILS + STONES

8 Wheel Tipper ☐ Other (describe) ☐

SECTION B - HOLDER / PRODUCER OF THE WASTE

SIC 4 2 9 9 0

Holder / Producer: CAREYS

Location/address of the Collection Point: Co-op Live
Alan Turing Way
M11 3DU

Declaration (by Holder)
I have fulfilled my duty to apply the waste hierarchy as required by Regulation 12 of the Waste (England & Wales) Regulations 2011.

Name: DAVID CLARK Signature: D. Clark

SECTION C - PERSON COLLECTING THE WASTE (CARRIER)

SIC 4 9 4 1 0

Carrier: W Maher & Sons Ltd

Carrier Address: Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW

Carrier Registration No.: CBDU90617 Expiry Date: 25/03/2025 Issued by: Environment Agency

Date of Transfer: 26.03.22 - 25.03.23 (for multiple consignments state duration, max 12 months)

Name: KFMcEnaney Signature: Ken Mc Enaney

SECTION D - DISPOSAL / RECOVERY FACILITY

Facility Operator: W. Maher + Sons Ltd

Facility Address: Ashton Old Road

Facility Permit No.: EPR/GB 3930 AM

Date of Transfer: 25.03.22 - 25.03.23 (for multiple consignments, state duration, max 12 months)

Name: KF McEnaney Signature: Ken Mc Enaney

IF WASTE IS SENT DIRECTLY TO LANDFILL SITE IN ENGLAND OR WALES THE FOLLOWING DECLARATION MUST BE SIGNED (BY CARRIER).

I/We confirm that the waste delivered by the above named company has been treated as highlighted below.

The material has gone through a physical, thermal, chemical or biological process including: sorting characteristics of the waste have been changed/volume has been reduced/ hazardous nature has been reduced/handling has been facilitated/recovery has been enhanced. (Delete as required)

Name: Signature:

DISTRIBUTION:	WHITE-HOLDER	YELLOW-OFFICE	BLUE-FACILITY OPERATOR

THIS DOCUMENT MUST BE RETAINED UNTIL 2 YEARS AFTER LAST TRANSFER DATE SHOWN IN SECTION D 03:25

Maher

CN 307997

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: CAREYS	Date: 9 2 23
Loaded at: ETIHAD	
Delivered to: HOR	
Driver: TONY	Veh. Reg. UW1
Tick ☐ 1 x 8 wh. load: ~~Off Site~~	Material: MUCK
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	

Foreman or Agent's Signature:

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE

Maher

CN 307996

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: CARGYS	Date: 9 2 23
Loaded at: ELLAND	
Delivered to: ROR	
Driver: TONY	Veh. Reg.: UW1
Tick ☐ 1 x 8 wh. load: Off Site	Material: MUCK
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	

Foreman or Agent's Signature

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE

Maher

CN 307989

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: CARGYS	Date: 9 2 23
Loaded at: ELLHAP	
Delivered to: AOR	
Driver: TONY	Veh. Reg. LW71
Tick ☐ 1 x 8 wh. load: Off Site	Material MUCK
Tick ☐ 1 x 8 wh. load: Delivered	Material

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature						

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE

Maher

CN 307995

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: CARGYS | Date: 9 2 23

Loaded at: ELLIAD

Delivered to: AOR

Driver: TONY | Veh. Reg: LW1

Tick ☐ 1 x 8 wh. load: Off Site | Material: MUCK

Tick ☐ 1 x 8 wh. load: Delivered | Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	

Foreman or Agent's Signature: CONSTANTIN SCHIPOR

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE

Form MAH/OD/16 V.06 04/19

Maher

CN 307994

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer:	CARGYS	Date:	9 23
Loaded at:	ELLAD		
Delivered to:	AOR		
Driver:	TONY	Veh. Reg.:	UW1
Tick ☐ 1 x 8 wh. load: Off Site		Material	MUCK
Tick ☐ 1 x 8 wh. load: Delivered		Material	

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	

Foreman or Agent's Signature: CONSTANTIN SCHIPOR

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE

Maher

CN 307988

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: CAREYS	Date: 9 2 23
Loaded at: ELLAND	
Delivered to: AOR	
Driver: TONY	Veh. Reg.: UW1
Tick ☐ 1 x 8 wh. load: Off Site	Material: MUCK
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature						

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE

Maher

CN 307991

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer:	CARGUS	Date:	9/23
Loaded at:	ELLAND		
Delivered to:	AOR		
Driver:	TONY	Veh. Reg.:	LW51
Tick ☐ 1 x 8 wh. load: Off Site		Material	MUCK
Tick ☐ 1 x 8 wh. load: Delivered		Material	

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature					

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE | Form MAH/OD/16 V.06 04/19

Maher

CN 307990

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: CAREYS	Date: 9 2 23
Loaded at: ETIHAD	
Delivered to: AOR	
Driver: Tony	Veh. Reg.: UW1
Tick ☐ 1 x 8 wh. load: Off Site	Material: MUCK
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature						

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE

Maher
W.Maher & Sons Ltd.
Civil Engineering Contractors

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T : 0161 776 2200
E : enquiries@wmaherandsons.com
W : www.wmaherandsons.com

Waste Transfer Note

SECTION A - DESCRIPTION OF WASTE (To be completed by Holder/Producer of the waste)

EWC Code (*Tick one box only*)

	17:01:01	Concrete	✓	17:05:04	Naturally occurring sub-soil and crushed stone
	17:01:02	Bricks		17:09:04	Mixed construction and demolition waste
	17:01:07	Concrete, brick and tile			Other: Insert EWC and describe below
				17.05.04	NON HAZ SOILS + STONES

How is the waste Contained

8 Wheel Tipper / Articulated Tipper ☑

SECTION B - HOLDER / PRODUCER OF THE WASTE

SIC 4 2 9 9 0

Holder / Producer: CAREY'S

Location/address of the Collection Point: CO-OP Live
Alan Turing Way
M11 3DU

Declaration (by Holder)
I have fulfilled my duty to apply the waste hierarchy as required by Regulation 12 of the Waste (England & Wales) Regulations 2011.

Name: THOMAS KING | Signature: T King

SECTION C - PERSON COLLECTING THE WASTE (CARRIER)

SIC 4 9 4 1 0

Carrier: W Maher & Sons Ltd

Carrier Address: Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW

Carrier Registration No.: CBDU90617 Expiry Date: 25/03/2025 Issued by: Environment Agency

Date of Transfer: 25.03.22 - 25.03.23 (for multiple consignments state duration, max 12 months)

Name: K F Mc Enaney | Signature: Ken Mc Enaney

SECTION D - DISPOSAL / RECOVERY FACILITY (Indicate facility used)

Facility Operator: Churchill Enviro Ltd

Facility Address: ☐ Jamestone Quarry, Haslingden, BB4 4AU ☒ Woolston Deposit Ground, Thelwall, WA3 6DR

Facility Permit No.: EPR/FB3805TL EAWML/50470

Date of Transfer: 25.03.22 - 25.03.23 (for multiple consignments, state duration, max 12 months)

Name: T. ANNIS | Signature: T. Annis

IF WASTE IS SENT DIRECTLY TO LANDFILL SITE IN ENGLAND OR WALES THE FOLLOWING DECLARATION MUST BE SIGNED (BY CARRIER).

I/We confirm that the waste delivered by the above named company has been treated as highlighted below.

The material has gone through a physical, thermal, chemical or biological process including: sorting characteristics of the waste have been changed/volume has been reduced/ hazardous nature has been reduced/handling has been facilitated/recovery has been enhanced. (Delete as required)

Name: | Signature:

DISTRIBUTION:	WHITE-HOLDER	YELLOW-OFFICE	BLUE-FACILITY OPERATOR

THIS DOCUMENT MUST BE RETAINED UNTIL 2 YEARS AFTER LAST TRANSFER DATE SHOWN IN SECTION D 03 : 25

Maher

CN 269048

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: Careys	Date: 18/2/23
Loaded at: Alan Turing way	
Delivered to: TW	
Driver: Ash W	Veh. Reg.: LW20
Tick ☑ 1 x 8 wh. load: Off Site	Material: Muck.
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature						

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be mace to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE

Maher

CN 269047

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: Careys	Date: 18/2/23
Loaded at: Alan Turing way	
Delivered to: TW	
Driver: Ash W	Veh. Reg.: VW00
Tick ☑ 1 x 8 wh. load: Off Site	Material: Muck
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature						

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted
All complaints whether in respect of material or circumstances of delivery must be mace to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

Maher

CN 269046

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: Careys	Date: 18/2/23
Loaded at: Alan Boring way	
Delivered to: TW	
Driver: Ash W	Veh. Reg.: W00
Tick ☑ 1 x 8 wh. load: Off Site	Material: Muck
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature						

CONDITIONS OF SALE. It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE

LL -

Maher CN 269049

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: Careys	Date: 18/2/23
Loaded at: Regent Rd	
Delivered to: TW	
Driver: Ash W	Veh. Reg.: UWO
Tick ☑ 1 x 8 wh. load: Off Site	Material: Mud.
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	

Foreman or Agent's Signature

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE | Form MAH/OD/16 V.06 04/19

Maher
W.Maher & Sons Ltd.
Civil Engineering Contractors

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T : 0161 776 2200 F: 0161 848 7357
E : enquiries@wmaherandsons.com
W : www.wmaherandsons.com

Waste Transfer Note

SECTION A - DESCRIPTION OF WASTE (To be completed by Holder/Producer of the waste)

EWC Code (*Tick one box only*)

	17:01:01	Concrete	X	17:05:04	Naturally occurring sub-soil and crushed stone
	17:01:02	Bricks		17:09:04	Mixed construction and demolition waste
	17:01:07	Concrete, brick and tile			Other: Insert EWC and describe below
				17.05.04	NON HAZ SOILS + STONES.

How is the waste Contained

8 Wheel Tipper ☐

SECTION B - HOLDER / PRODUCER OF THE WASTE

SIC 4 2 9 9 0

Holder / Producer: CAREY'S.

Location/address of the Collection Point: CO-OP Live
Alan Turing Way
M11 3DU

Declaration (by Holder)
I have fulfilled my duty to apply the waste hierarchy as required by Regulation 12 of the Waste (England & Wales) Regulations 2011.

Name: Diana MacIvison Signature:

SECTION C - PERSON COLLECTING THE WASTE (CARRIER)

SIC 4 9 4 1 0

Carrier: W Maher & Sons Ltd

Carrier Address: Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW

Carrier Registration No.: CBDU90617 Expiry Date: 25/03/2025 Issued by: Environment Agency

Date of Transfer: 25.03.22 – 25.03.23 (for multiple consignments state duration, max 12 months)

Name: K F Mc Enaney Signature: Ken Mc Enaney

SECTION D - DISPOSAL / RECOVERY FACILITY (Indicate facility used)

Facility Operator: Churchill Enviro Ltd

Facility Address: ☒ Fletcher Bank, Ramsbottom, BL0 0HD ☐ Hutchbank, Haslingden, BB4 4PB

Facility Permit No.: EPR/GP3733 FE EPR/BB 3702 HL

Date of Transfer: 25.03.22 – 25.03.23 (for multiple consignments, state duration, max 12 months)

Name: T. ANNIS Signature:

IF WASTE IS SENT DIRECTLY TO LANDFILL SITE IN ENGLAND OR WALES THE FOLLOWING DECLARATION MUST BE SIGNED (BY CARRIER).

I/We confirm that the waste delivered by the above named company has been treated as highlighted below.

The material has gone through a physical, thermal, chemical or biological process including: sorting characteristics of the waste have been changed/volume has been reduced/ hazardous nature has been reduced/handling has been facilitated/recovery has been enhanced. (Delete as required)

Name: Signature:

DISTRIBUTION:	WHITE-HOLDER	YELLOW-OFFICE	BLUE-FACILITY OPERATOR

THIS DOCUMENT MUST BE RETAINED UNTIL 2 YEARS AFTER LAST TRANSFER DATE SHOWN IN SECTION D 03:25

Maher

CN 269612

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: Careys	Date: 22.2.23
Loaded at: Etihad.	
Delivered to: TIP	
Driver: Greg	Veh. Reg.: TVU
Tick ☑ 1 x 8 wh. load: Off Site	Material: Muck
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature						

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE | Form MAH/OD/16 V.06 04/19

Maher
W.Maher & Sons Ltd.
Civil Engineering Contractors

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T : 0161 776 2200 F: 0161 848 7357
E : enquiries@wmaherandsons.com
W : www.wmaherandsons.com

Waste Transfer Note

SECTION A - DESCRIPTION OF WASTE (To be completed by Holder/Producer of the waste)

EWC Code (*Tick one box only*)

	17:01:01	Concrete	X	17:05:04	Soil and stones (excl. dangerous substances)
	17:01:02	Bricks		17:09:04	Mixed construction and demolition waste
	17:01:07	Concrete, brick and tile			Other

How is the waste Contained 17.05.04 NON HAZ SOILS + STONES

8 Wheel Tipper ☐ Other (describe) ☐

SECTION B - HOLDER / PRODUCER OF THE WASTE

SIC 4 2 9 9 0

Holder / Producer: CAREYS

Location/address of the Collection Point: Co-op Live
Alan Turing Way
M11 3DU

Declaration (by Holder)
I have fulfilled my duty to apply the waste hierarchy as required by Regulation 12 of the Waste (England & Wales) Regulations 2011.

Name: DAVID CLARK Signature: D. Clark

SECTION C - PERSON COLLECTING THE WASTE (CARRIER)

SIC 4 9 4 1 0

Carrier: W Maher & Sons Ltd

Carrier Address: Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW

Carrier Registration No.: CBDU90617 Expiry Date: 25/03/2025 Issued by: Environment Agency

Date of Transfer: 25.03.22 - 25.03.23 (for multiple consignments state duration, max 12 months)

Name: KFMcEnaney Signature: Ken Mc Enaney

SECTION D - DISPOSAL / RECOVERY FACILITY

Facility Operator: W. Maher + Sons Ltd

Facility Address: Ashton Old Road

Facility Permit No.: EPR/GB 3930 AM

Date of Transfer: 25.03.22 - 25.03.23 (for multiple consignments, state duration, max 12 months)

Name: KF McEnaney Signature: Ken Mc Enaney

IF WASTE IS SENT DIRECTLY TO LANDFILL SITE IN ENGLAND OR WALES THE FOLLOWING DECLARATION MUST BE SIGNED (BY CARRIER).

I/We confirm that the waste delivered by the above named company has been treated as highlighted below.

The material has gone through a physical, thermal, chemical or biological process including: sorting characteristics of the waste have been changed/volume has been reduced/ hazardous nature has been reduced/handling has been facilitated/recovery has been enhanced. (Delete as required)

Name: Signature:

DISTRIBUTION:	WHITE-HOLDER	YELLOW-OFFICE	BLUE-FACILITY OPERATOR

THIS DOCUMENT MUST BE RETAINED UNTIL 2 YEARS AFTER LAST TRANSFER DATE SHOWN IN SECTION D 03:25

hh -

Maher CN 312593

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: Cianet	Date: 22-2-23
Loaded at: ARENA	
Delivered to: Aon	
Driver: Andy	Veh. Reg.: BXV
Tick ☑ 1 x 8 wh. load: Off Site	Material: much
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature						

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE | Form MAH/OD/16 V.06 04/19

Maher

CN 312586

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: CIVILE7	Date: 22.2.23
Loaded at: ARENA	
Delivered to: AON	
Driver: ANDY	Veh. Reg.: BXV
Tick ☑ 1 x 8 wh. load: Off Site	Material: MUCK
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	

Foreman or Agent's Signature

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE

Maher

CN 266988

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: LARGS	Date: 22 2 23
Loaded at: E11HAD	
Delivered to: AOR	
Driver: Tony	Veh. Reg.: LW1
Tick ☐ 1 x 8 wh. load: Off Site	Material: MUCK
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature						

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE

Maher

CN 312590

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: CRANES	Date: 22.2.23
Loaded at: ARENA	
Delivered to: AON	
Driver: ANDY	Veh. Reg.: 13XV
Tick ☑ 1 x 8 wh. load: Off Site	Material: MUCK
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	

Foreman or Agent's Signature: [signature]

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE

Maher

CN 312591

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE: A 09.50

Customer: Caney	Date: 22-3-23
Loaded at: M/C Arena	
Delivered to: AOR	
Driver: Andy	Veh. Reg.: BXV
Tick ✓ 1 x 8 wh. load: Off Site	Material: MUCK
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature						

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE

Form MAH/OD/16 V.06 04/19

Maher

CN 312599

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE A14·32-L

Customer: CANET	Date: 22-2-23
Loaded at: ARENA	
Delivered to: AOR	
Driver: ANDY	Veh. Reg.: BXV
Tick ☑ 1 x 8 wh. load: Off Site	Material: MUCH
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature	CONSTANTIN					

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE

Maher

CN 312597

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: CRANEY	Date: 22.2.23
Loaded at: ARENA	
Delivered to: AON	
Driver: ANDY	Veh. Reg.: BXV
Tick ☑ 1 x 8 wh. load: Off Site	Material: MUCK
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature						

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE

Maher

CN 312588

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: CANEN	Date: 22.2.23
Loaded at: ARENAS	
Delivered to: AON	
Driver: AUON	Veh. Reg.: BXV

Tick		Material
☑	1 x 8 wh. load: Off Site	MUCK
☐	1 x 8 wh. load: Delivered	

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature						

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE | Form MAH/OD/16 V.06 04/19

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T : 0161 776 2200 F: 0161 848 7357
E : enquiries@wmaherandsons.com
W : www.wmaherandsons.com

W.Maher & Sons Ltd.
Civil Engineering Contractors

Waste Transfer Note

SECTION A - DESCRIPTION OF WASTE (To be completed by Holder/Producer of the waste)

EWC Code (*Tick one box only*)

	17:01:01	Concrete	X	17:05:04	Naturally occurring sub-soil and crushed stone
	17:01:02	Bricks		17:09:04	Mixed construction and demolition waste
	17:01:07	Concrete, brick and tile			Other: Insert EWC and describe below
				17.05.04	NON HAZ SOILS + STONES.

How is the waste Contained

8 Wheel Tipper ☐

SECTION B - HOLDER / PRODUCER OF THE WASTE

SIC 4 2 9 9 0

Holder / Producer: CAREY'S.

Location/address of the Collection Point: CO-OP Live
Alan Turing Way
M11 3DU

Declaration (by Holder)
I have fulfilled my duty to apply the waste hierarchy as required by Regulation 12 of the Waste (England & Wales) Regulations 2011.

Name: Diana MacIvisa Signature:

SECTION C - PERSON COLLECTING THE WASTE (CARRIER)

SIC 4 9 4 1 0

Carrier: W Maher & Sons Ltd

Carrier Address: Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW

Carrier Registration No.: CBDU90617 Expiry Date: 25/03/2025 Issued by: Environment Agency

Date of Transfer: 25.03.22 - 25.03.23 (for multiple consignments state duration, max 12 months)

Name: K F Mc Enaney Signature: Ken Mc Enaney

SECTION D - DISPOSAL / RECOVERY FACILITY (Indicate facility used)

Facility Operator: Churchill Enviro Ltd

Facility Address: ☒ Fletcher Bank, Ramsbottom, BL0 0HD ☐ Hutchbank, Haslingden, BB4 4PB

Facility Permit No.: EPR/GP3733 FE EPR/BB 3702 HL

Date of Transfer: 25.03.22 - 25.03.23 (for multiple consignments, state duration, max 12 months)

Name: T. ANNIS Signature: T Annis

IF WASTE IS SENT DIRECTLY TO LANDFILL SITE IN ENGLAND OR WALES THE FOLLOWING DECLARATION MUST BE SIGNED (BY CARRIER).

I/We confirm that the waste delivered by the above named company has been treated as highlighted below.

The material has gone through a physical, thermal, chemical or biological process including: sorting characteristics of the waste have been changed/volume has been reduced/ hazardous nature has been reduced/handling has been facilitated/recovery has been enhanced. (Delete as required)

Name: Signature:

DISTRIBUTION:	WHITE-HOLDER	YELLOW-OFFICE	BLUE-FACILITY OPERATOR

THIS DOCUMENT MUST BE RETAINED UNTIL 2 YEARS AFTER LAST TRANSFER DATE SHOWN IN SECTION D 03:25

Maher

CN 269613

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE 23

Customer: Careys	Date: 22.2.23
Loaded at: Etihad	
Delivered to: TIP	
Driver: Greg	Veh. Reg.: TVC
Tick ☑ 1 x 8 wh. load: Off Site	Material: Muck
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature						

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE | Form MAH/OD/16 V.06 04/19

Maher

CN 269622

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: Careys	Date: 23-2-CJ
Loaded at: Ethel	
Delivered to: TIP.	
Driver: Greg	Veh. Reg.: TVU
Tick ☑ 1 x 8 wh. load: Off Site	Material: Muck
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature						

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

Maher

CN 269623

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: Coreys	Date: 23.2.23
Loaded at: Tilled	
Delivered to: Tip.	
Driver: Greg	Veh. Reg.: TV u
Tick ☒ 1 x 8 wh. load: Off Site	Material: Muck
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	

Foreman or Agent's Signature:

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE

Maher

CN 269624

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: Careys	Date: 23.2.23
Loaded at: Ellund	
Delivered to: T.I.P.	
Driver: Greg	Veh. Reg.: JVU
Tick ☑ 1 x 8 wh. load: Off Site	Material: Mulch
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	

Foreman or Agent's Signature:

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE

Maher

CN 269629

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: Careys	Date: 23.2.23
Loaded at: STHAD	
Delivered to: TIP.	
Driver: Greg	Veh. Reg.: TVU
Tick ☑ 1 x 8 wh. load: Off Site	Material: Muck
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature						

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE

Maher

CN 269630

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: Careys	Date: 23.2.23
Loaded at: Etihad	
Delivered to: Tip.	
Driver: Greg	Veh. Reg.: TVU
Tick ☑ 1 x 8 wh. load: Off Site	Material: Mark
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	

Foreman or Agent's Signature:

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

LL -

Maher CN 269625

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: Cuerdys	Date: 23-2-23
Loaded at: ETIHAD	
Delivered to: T2P	
Driver: Greg	Veh. Reg.: TWW
Tick ☑ 1 x 8 wh. load: Off Site	Material: Muck
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature						

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE | Form MAH/OD/16 V 06 04/19

Maher
W.Maher & Sons Ltd.
Civil Engineering Contractors

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T : 0161 776 2200 F: 0161 848 7357
E : enquiries@wmaherandsons.com
W : www.wmaherandsons.com

Waste Transfer Note

SECTION A - DESCRIPTION OF WASTE (To be completed by Holder/Producer of the waste)

EWC Code (*Tick one box only*)

	17:01:01	Concrete	X	17:05:04	Soil and stones (excl. dangerous substances)
	17:01:02	Bricks		17:09:04	Mixed construction and demolition waste
	17:01:07	Concrete, brick and tile			Other

How is the waste Contained 17.05.04 NON HAZ SOILS + STONES

8 Wheel Tipper ☐ Other (describe) ☐

SECTION B - HOLDER / PRODUCER OF THE WASTE

SIC 4 2 9 9 0

Holder / Producer: CAREYS

Location/address of the Collection Point: Co-op Live
Alan Turing Way
M11 3DU

Declaration (by Holder)
I have fulfilled my duty to apply the waste hierarchy as required by Regulation 12 of the Waste (England & Wales) Regulations 2011.

Name: DAVID CLARK Signature: D. Clark

SECTION C - PERSON COLLECTING THE WASTE (CARRIER)

SIC 4 9 4 1 0

Carrier: W Maher & Sons Ltd

Carrier Address: Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW

Carrier Registration No.: CBDU90617 Expiry Date: 25/03/2025 Issued by: Environment Agency

Date of Transfer: 25.03.22 - 25.03.23 (for multiple consignments state duration, max 12 months)

Name: KFMcEnaney Signature: Ken Mc Enaney

SECTION D - DISPOSAL / RECOVERY FACILITY

Facility Operator: W. Maher + Sons Ltd

Facility Address: Ashton Old Road

Facility Permit No.: EPR/GB 3930 AM

Date of Transfer: 25.03.22 - 25.03.23 (for multiple consignments, state duration, max 12 months)

Name: KF McEnaney Signature: Ken Mc Enaney

IF WASTE IS SENT DIRECTLY TO LANDFILL SITE IN ENGLAND OR WALES THE FOLLOWING DECLARATION MUST BE SIGNED (BY CARRIER).

I/We confirm that the waste delivered by the above named company has been treated as highlighted below.

The material has gone through a physical, thermal, chemical or biological process including: sorting characteristics of the waste have been changed/volume has been reduced/ hazardous nature has been reduced/handling has been facilitated/recovery has been enhanced. (Delete as required)

Name: Signature:

DISTRIBUTION:	WHITE-HOLDER	YELLOW-OFFICE	BLUE-FACILITY OPERATOR

THIS DOCUMENT MUST BE RETAINED UNTIL 2 YEARS AFTER LAST TRANSFER DATE SHOWN IN SECTION D 03:25

Maher

CN 312600

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: CANLEY	Date 23·2·23
Loaded at: ANENA	
Delivered to: AON	
Driver: ANDY	Veh. Reg.: BXV
Tick ☑ 1 x 8 wh. load: Off Site	Material: MUCK
Tick ☐ 1 x 8 wh. load: Delivered	Material

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature						

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE

Maher

CN 312752

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: CAREY	Date: 23.2.23
Loaded at: ARLENA	
Delivered to: RON	
Driver: ANDY	Veh. Reg.: BXV
Tick ☑ 1 x 8 wh. load: Off Site	Material: MUCK
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature						

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE

Maher

CN 312754

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: CANEY	Date 23.2.23
Loaded at: ARENA	
Delivered to: ADR	
Driver: ANDY	Veh. Reg.: BXV
Tick ☑ 1 x 8 wh. load: Off Site	Material: MUCK
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature						

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE | Form MAH/OD/16 V.06 04/19

Maher

CN 312756

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: CAREY	Date: 23.2.23
Loaded at: ARENA	
Delivered to: ROK	
Driver: RUDY	Veh. Reg.: BXV
Tick ☑ 1 x 8 wh. load: Off Site	Material: MUCK
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature						

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE

Form MAH/OD/16 V.06 04/19

Maher

CN 312762

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE A 13.32-L

Customer: CANEY	Date: 23.2.23
Loaded at: ARENA	
Delivered to: AON	
Driver: ANDY	Veh. Reg.: BXV
Tick ☑ 1 x 8 wh. load: Off Site	Material: MUCK
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	

Foreman or Agent's Signature: B

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE

Maher

CN 312759

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: CARLEY	Date: 23.2.23
Loaded at: ASHENS	
Delivered to: ADR	
Driver: ANDY	Veh. Reg.: BXV
Tick ☑ 1 x 8 wh. load: Off Site	Material: MUCK
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature						

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE

Maher
W.Maher & Sons Ltd.
Civil Engineering Contractors

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T : 0161 776 2200 F: 0161 848 7357
E : enquiries@wmaherandsons.com
W : www.wmaherandsons.com

Waste Transfer Note

SECTION A - DESCRIPTION OF WASTE (To be completed by Holder/Producer of the waste)

EWC Code (*Tick one box only*)

	17:01:01	Concrete	X	17:05:04	Soil and stones (excl. dangerous substances)
	17:01:02	Bricks		17:09:04	Mixed construction and demolition waste
	17:01:07	Concrete, brick and tile			Other

How is the waste Contained 17.05.04 NON HAZ SOILS + STONES

8 Wheel Tipper ☐ Other (describe) ☐

SECTION B - HOLDER / PRODUCER OF THE WASTE

SIC 4 2 9 9 0

Holder / Producer: CAREYS

Location/address of the Collection Point: Co-op Live
Alan Turing Way
M11 3DU

Declaration (by Holder)
I have fulfilled my duty to apply the waste hierarchy as required by Regulation 12 of the Waste (England & Wales) Regulations 2011.

Name: DAVID CLARK Signature: D. Clark

SECTION C - PERSON COLLECTING THE WASTE (CARRIER)

SIC 4 9 4 1 0

Carrier: W Maher & Sons Ltd

Carrier Address: Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW

Carrier Registration No.: CBDU90617 Expiry Date: 25/03/2025 Issued by: Environment Agency

Date of Transfer: 25.03.22 - 25.03.23 (for multiple consignments state duration, max 12 months)

Name: KFMcEnaney Signature: Ken Mc Enaney

SECTION D - DISPOSAL / RECOVERY FACILITY

Facility Operator: W. Maher + Sons Ltd

Facility Address: Ashton Old Road

Facility Permit No.: EPR/GB 3930 AM

Date of Transfer: 25.03.22 - 25.03.23 (for multiple consignments, state duration, max 12 months)

Name: KF McEnaney Signature: Ken Mc Enaney

IF WASTE IS SENT DIRECTLY TO LANDFILL SITE IN ENGLAND OR WALES THE FOLLOWING DECLARATION MUST BE SIGNED (BY CARRIER).

I/We confirm that the waste delivered by the above named company has been treated as highlighted below.

The material has gone through a physical, thermal, chemical or biological process including: sorting characteristics of the waste have been changed/volume has been reduced/ hazardous nature has been reduced/handling has been facilitated/recovery has been enhanced. (Delete as required)

Name: Signature:

DISTRIBUTION:	WHITE-HOLDER	YELLOW-OFFICE	BLUE-FACILITY OPERATOR

THIS DOCUMENT MUST BE RETAINED UNTIL 2 YEARS AFTER LAST TRANSFER DATE SHOWN IN SECTION D 03:25

hh.

Maher CN 312773

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE A10·54 - L

Customer: CANETS	Date: 24·2·23
Loaded at: ANEVA	
Delivered to: AOR	
Driver: AWDY	Veh. Reg.: BxV
Tick ☑ 1 x 8 wh. load: Off Site	Material: MUCH
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature						

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE | Form MAH/OD/16 V.06 04/19

Maher

CN 312771

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: CANEY	Date: 24.2.23
Loaded at: ARENA	
Delivered to: AOR	
Driver: ANDY	Veh. Reg.: BXV
Tick [✓] 1 x 8 wh. load: Off Site	Material: MUCK
Tick [ ] 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature						

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE | Form MAH/OD/16 V.06 04/19

Maher

CN 312769

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE A850-L

Customer: CANEY	Date: 24.2.23
Loaded at: ARENA	
Delivered to: AOR	
Driver: ANDY	Veh. Reg.: BXV
Tick ☑ 1 x 8 wh. load: Off Site	Material: MUCH
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	

Foreman or Agent's Signature	

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE | Form MAH/OD/16 V.06 04/19

Maher

CN 312767

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: CANEY	Date 24.2.23
Loaded at: ARENA	
Delivered to: AOR	
Driver: ANDY	Veh. Reg.: BXV
Tick ☑ 1 x 8 wh. load: Off Site	Material: MUCK
Tick ☐ 1 x 8 wh. load: Delivered	Material:

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	

Foreman or Agent's Signature	

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

Maher

W.Maher & Sons Ltd.
Civil Engineering Contractors

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T : 0161 776 2200 F: 0161 848 7357
E : enquiries@wmaherandsons.com
W : www.wmaherandsons.com

Waste Transfer Note

SECTION A - DESCRIPTION OF WASTE (To be completed by Holder/Producer of the waste)

EWC Code (*Tick one box only*)

	17:01:01	Concrete	X	17:05:04	Naturally occurring sub-soil and crushed stone
	17:01:02	Bricks		17:09:04	Mixed construction and demolition waste
	17:01:07	Concrete, brick and tile			Other: Insert EWC and describe below
				17.05.04	NON HAZ SOILS + STONES.

How is the waste Contained

8 Wheel Tipper ☐

SECTION B - HOLDER / PRODUCER OF THE WASTE

SIC 4 2 9 9 0

Holder / Producer: CAREY'S.

Location/address of the Collection Point: CO-OP Live
Alan Turing Way
M11 3DU

Declaration (by Holder)
I have fulfilled my duty to apply the waste hierarchy as required by Regulation 12 of the Waste (England & Wales) Regulations 2011.

Name: Diane MacIvison Signature:

SECTION C - PERSON COLLECTING THE WASTE (CARRIER)

SIC 4 9 4 1 0

Carrier: W Maher & Sons Ltd

Carrier Address: Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW

Carrier Registration No.: CBDU90617 Expiry Date: 25/03/2025 Issued by: Environment Agency

Date of Transfer: 25.03.22 – 25.03.23 (for multiple consignments state duration, max 12 months)

Name: K F Mc Enaney Signature: Ken Mc Enaney

SECTION D - DISPOSAL / RECOVERY FACILITY (Indicate facility used)

Facility Operator: Churchill Enviro Ltd

Facility Address: ☒ Fletcher Bank, Ramsbottom, BL0 0HD ☐ Hutchbank, Haslingden, BB4 4PB

Facility Permit No.: EPR/GP3733 FE EPR/BB 3702 HL

Date of Transfer: 26.03.22 – 25.03.23 (for multiple consignments, state duration, max 12 months)

Name: T. ANNIS Signature:

IF WASTE IS SENT DIRECTLY TO LANDFILL SITE IN ENGLAND OR WALES THE FOLLOWING DECLARATION MUST BE SIGNED (BY CARRIER).

I/We confirm that the waste delivered by the above named company has been treated as highlighted below.

The material has gone through a physical, thermal, chemical or biological process including: sorting characteristics of the waste have been changed/volume has been reduced/ hazardous nature has been reduced/handling has been facilitated/recovery has been enhanced. (Delete as required)

Name: Signature:

DISTRIBUTION:	WHITE-HOLDER	YELLOW-OFFICE	BLUE-FACILITY OPERATOR

THIS DOCUMENT MUST BE RETAINED UNTIL 2 YEARS AFTER LAST TRANSFER DATE SHOWN IN SECTION D 03:25

LL.

Maher

CN 263267

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: CARREGS	Date: 28/02/23.
Loaded at: EDILLAR	
Delivered to: TIP.	
Driver: NOAH	Veh. Reg.: BXM.
Tick ☑ 1 x 8 wh. load: Off Site	Material: Muck
Tick ☐ 1 x 8 wh. load: Delivered	Material

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	

Foreman or Agent's Signature

CONDITIONS OF SALE: It is essential that all written particulars entered above shou'd be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE | Form MAH/OD/16 V.06 04/19

Maher

CN 268399

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: CARREYL	Date: 28/02/23
Loaded at: EDILIAD	
Delivered to: TIP	
Driver: RICK	Veh. Reg.: BXM
Tick ☑ 1 x 8 wh. load: Off Site	Material: MUCK
Tick ☐ 1 x 8 wh. load: Delivered	Material

Daywork / Sitework	Hours Worked		Travel Time		Total Hours		

Foreman or Agent's Signature

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE | Form MAH/OD/16 V.06 04/19

Maher

CN 263268

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: CARR645	Date: 28/02/23
Loaded at: ETIHAD	
Delivered to: TIP	
Driver: [illegible]	Veh. Reg.: SXM
Tick ☒ 1 x 8 wh. load: Off Site	Material: Muck
Tick ☐ 1 x 8 wh. load: Delivered	Material

Daywork / Sitework	Hours Worked		~~Travel~~ Time		Total Hours	
Foreman or Agent's Signature						

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE

Form MAH/OD/16 V 06 04/19

Maher

CN 268400

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: CARRELLS	Date: 28/02/23
Loaded at: EDILLAD	
Delivered to: TP.	
Driver: NICK	Veh. Reg.: BSXRI

Tick ☑ 1 x 8 wh. load: Off Site	Material: Muck
Tick ☐ 1 x 8 wh. load: Delivered	Material

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	

Foreman or Agent's Signature

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE | Form MAH/OD/16 V.06 04/19

Maher

CN 263266

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: CARREYS	Date: 28/02/23
Loaded at: GOLF HAUL	
Delivered to: TIP	
Driver: RICK	Veh. Reg.: BXM
Tick ☑ 1 x 8 wh. load: Off Site	Material: MUCK
Tick ☐ 1 x 8 wh. load: Delivered	Material

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature						

CONDITIONS OF SALE: It is essential that all written particulars entered above should be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE | Form MAH/OD/16 V.06 04/19

Maher

CN 263269

W. MAHER & SONS LTD.
Rixton Old Hall, Manchester Road, Rixton, Warrington WA3 6EW
T: 0161 776 2200 E: enquiries@wmaherandsons.com

Bulk Excavation & Disposal • Ground Remediation
Quarried & Recycled Aggregates • Site Preparation

CONSIGNMENT NOTE

Customer: CARNEYS	Date: 28/6/23
Loaded at: ETHAD	
Delivered to: TIP	
Driver: [illegible]	Veh. Reg.: BX71 [illegible]

Tick ☑ 1 x 8 wh. load: Off Site	Material: [illegible]
Tick ☐ 1 x 8 wh. load: Delivered	Material

Daywork / Sitework	Hours Worked		Travel Time		Total Hours	
Foreman or Agent's Signature						

CONDITIONS OF SALE: It is essential that all written particulars entered above shou'd be carefully checked by the consignee since this delivery note, once signed by the consignee, represents formal acceptance of the material in good order and condition and subsequent complaints cannot be accepted.
All complaints whether in respect of material or circumstances of delivery must be made to the driver of the vehicle and be confirmed in writing direct to the company immediately.
All materials and title to same remain the property of supplier until paid in full.

THIS IS NOT A WASTE TRANSFER NOTE | Form MAH/OD/16 V.06 04/19

Appendix D Groundwater and River Monitoring Records


(Selection of records provided)



Copyright © 1976 - 2024 Buro Happold. All rights reserved



Copyright © 1976 - 2024 Buro Happold. All rights reserved

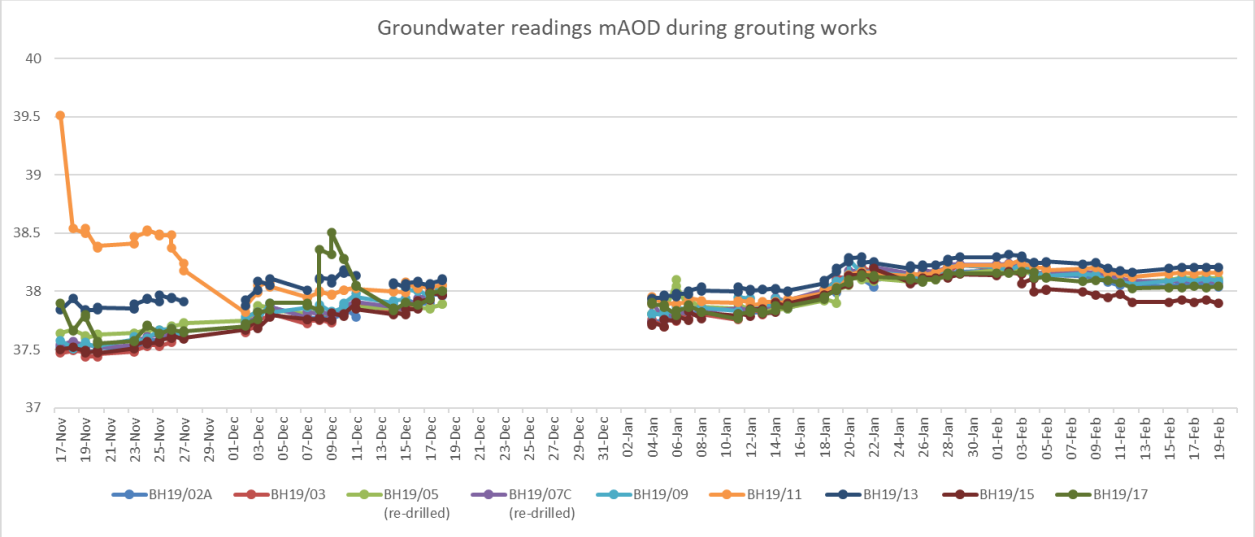

Copyright © 1976 - 2024 Buro Happold. All rights reserved

Appendix E Trade Effluent Consent

Copyright © 1976 - 2024 Buro Happold. All rights reserved

Document: Consent
WwTW: DAVYHULME
DPID: 694TLN26BAM03

Thirlmere House
Lingley Mere Business Park
Lingley Green Avenue
Great Sankey
Warrington WA5 3LP

BAM Construction Limited

Breakspear Park
Breakspear Way
Hemel Hempstead
Hertfordshire
HP2 4FL

Date: 01st March 2021

FAO The Company Secretary

Dear Sir/Madam

TRADE EFFLUENT – WATER INDUSTRY ACT 1991 - Land adjacent to Etihad Stadium (Main construction site) Gibbon Street Manchester M11 3DU

Further to your Duly made application dated 15 January 2021, I enclose your CONSENT TO THE DISCHARGE OF TRADE EFFLUENT.

This document is issued by virtue of Statutory Powers granted by the Water Industry Act 1991 and as such a "true copy" has now been placed on public record. The Consent to Discharge relates solely to the trade effluent described in your application form and you must notify United Utilities Water Limited of:

a) any proposed changes to the nature and composition of the effluent;

b) any proposed changes to the rate of discharge and/or daily volume;

c) any proposed change of name of your Company (or trading name);

d) permanent termination of the discharge

The conditions laid down in the Consent are the only conditions under which United Utilities Water Limited will undertake to receive your effluent into the foul sewer. Any failure to comply with such conditions is an offence under the Water Industry Act 1991.

In respect of clause 10a) of the Consent, I understand that representative samples of the trade effluent may be obtained from the discharge pipe after full settlement. You should note that officers designated in writing by United Utilities Water Limited shall have right of safe access at all reasonable hours without notice for the purpose of obtaining a sample of trade effluent.

The volume of trade effluent can be determined by direct measurement using the effluent meter. Until the meter is installed, the trade effluent charge will be based on 10m3. You must inform us via your retailer when the meter is installed. You will receive a separate contact with a form to complete with the meter details.

You must inform us in writing via your retailer of any changes to the volume of trade effluent. Any alteration will take effect from the date on which we are notified of such changes.

Yours sincerely

Wastewater Asset Manager

Wastewater Services

WATER INDUSTRY ACT 1991

CONSENT TO THE DISCHARGE OF TRADE EFFLUENT

Whereas **BAM Construction Limited**

(hereinafter called "the Trader") whose Head Office or Registered Office is at

Breakspear Park Breakspear Way Hemel Hempstead Hertfordshire HP2 4FL

Is the **owner/occupier** of the trade premises at:

Land adjacent to Etihad Stadium
(Main construction site)
Gibbon Street
Manchester
M11 3DU

and by the Duly made application dated **15 January 2021**

Have applied to UNITED UTILITIES WATER LIMITED (hereinafter called "the Company") for consent to discharge trade effluent from the said trade premises into the sewers.

Under the provisions of the above mentioned Act the discharge of trade effluent in accordance with the said application form would not be lawful without the consent of the Company.

NOW THEREFORE in exercise of the powers conferred upon them by the above Act the Company HEREBY CONSENT to the discharge of trade effluent by the Trader from the said premises into their sewers SUBJECT TO THE FOLLOWING CONDITIONS:

Nature of discharge

1a) Subject to the provisions of conditions 6,7,8 and 9 below the nature or composition of the trade effluent to be discharged under this Consent shall be solely as specified in the said application form and shall consist solely of waste water derived from **pumping of groundwater and surface water from excavations.**

1b) The trader shall give to the Company prior written notice of any change in the process or the process materials or any other circumstances likely to alter the constituents of the trade effluent as set out in condition 1(a). In such circumstances, no substance of which the Company has not had previous notice, may be discharged unless and until the Company has agreed to accept the substance at a limit imposed by the Company which shall then be deemed to be incorporated in this Consent by agreement and shall not prejudice the right of the Company to serve a Direction earlier than two years from the date of such incorporation.

The Trader shall also give not less than seven days written notice to the Company of any change in the name of the occupier or owner.

Sewer affected

2. The sewer into which the trade effluent may be discharged and the point of discharge is the foul sewer situate at **MH 8908 (MH 8904)**.

Connections

3. No connections shall be made to the said sewer without the prior approval of the Company and all such connections shall be constructed and maintained to the satisfaction of the Company at the expense of the Trader.

Maximum volume of discharge

4. The maximum amount of the trade effluent discharged in any one day of twenty four hours shall not exceed **432** m^3 without prior written consent of the Company.

Maximum rate of discharge

5. The highest rate at which the trade effluent may be discharged shall not exceed **5** litre/sec.

Matters to be eliminated prior to discharge to sewers

6. The following matters shall be eliminated from the trade effluent before it is discharged into the sewers of the Company:

a) petroleum spirit;

b) calcium carbide;

c) carbon disulphide;

d) except as provided in paragraph 7 hereof, the prescribed substances listed in Schedule 1 to The Trade Effluents (Prescribed Processes and Substances) Regulations 1989, as amended from time to time, insofar as they are in concentration greater than the background concentration (as defined in the said Regulations);

e) where the trade effluent derives from a prescribed process mentioned in Schedule 2 to the said Regulations, and except as provided in paragraph 7 hereof, asbestos (as defined in the said Regulations) and chloroform in concentration greater than the background concentration (as defined in the said Regulations);

f) organo-halogen compounds including pesticide residues and degreasing agents;

g) any substances which either alone or in combination with each other or with any other matter lawfully present in the said sewers would be likely to;

i) cause a nuisance or produce flammable, harmful or toxic vapours either in the sewers or at the sewage works of the Company;

ii) injure the sewers or interfere with the free flow of their contents or affect prejudicially the treatment and disposal of their contents or have injurious effects on the sewage treatment works to which it is conveyed or upon any treatment plant there;

iii) be dangerous to or cause injury to any person working in the sewers or at the sewage treatment works;

iv) affect prejudicially any watercourse, estuary or coastal water into which the treated effluent will eventually be discharged.

Matters to be limited prior to discharge to sewer

7. The trade effluent shall not contain

a) Ammonia and its compounds as N in excess of 250 mg/l

b) Arsenic as As in excess of 50 ug/l

c) Chloroform in excess of 100 ug/l

d) Cyanides and cyanogen compounds which produce hydrogen cyanide on acidification in excess of 1 mg/l

e) Methane in solution in excess of 0.14 mg/l

f) Phenols in excess of 20 mg/l

g) Separable grease and oil in excess of 100mg/l

h) Sulphates as SO_4 in excess of 1,000 mg/l

i) Sulphides, hydrosulphides, polysulphides and substances producing hydrogen sulphide on acidification in excess of 1 mg/l

j) Total nitrogen as N in excess of 250 mg/l

k) Total suspended solids at pH 7.0 and dried at 110° C in excess of 1,000 mg/l

l) Toxic metals in excess of 10,000 ug/l either individually or in total ie Antimony, Beryllium, Chromium, Copper, Lead, Nickel, Selenium, Silver, Tin, Vanadium, Zinc;

Temperature

8. No trade effluent shall be discharged which has a temperature higher than 43.3°C (110°F).

pH value

9. No trade effluent shall be discharged having a pH of less than **6** or greater than **10**

Inspection Chamber

10. a) An inspection chamber or manhole shall be provided and maintained by the Trader in a suitable position in connection with each pipe through which the trade effluent is discharged and shall be so constructed and maintained as to enable a person readily to obtain at any time samples of the trade effluent so discharged, to the approval of the Company.

b) There shall be provided, operated and maintained in working order by the Trader a meter in such a position and of such specification as shall be approved by UUWLtd such as will measure and provide a continuous record of the quantity and rate of discharge of any trade effluent being discharged from the premises into the said sewer and following the written request of UUWLtd to have the accuracy of the meter independently tested by an agreed body.

c) If the measuring and recording apparatus as aforesaid ceases to function satisfactorily, then the Company shall have the right to make estimates of the volume and composition of the trade effluent until such time as the said apparatus is again operating to the satisfaction of the Company.

d) Records shall be kept by the Trader of the volume, rate of discharge, nature and composition of the trade effluent discharged to the sewer, together with any records required to be kept by the Trader under the provisions of any Notice of Determination issued by the Secretary of State under Sections 120 and 132 of the Water Industry Act 1991. Such records shall be kept available for inspection at all reasonable times by an authorised officer of the Company and copies shall be sent to the Company on demand.

e) The foregoing provision of this condition shall be deemed to be complied with if other methods of sampling the trade effluent, determining its nature and composition, and measuring and recording the discharge are agreed and confirmed in writing by the Company.

Dated 01st March 2021

Issuing Office Wastewater Services
Lingley Mere Business Park
Lingley Green Avenue
Great Sankey
Warrington
WA5 3LP

Signed

WASTEWATER ASSET MANAGER
WASTEWATER SERVICES
for and on behalf of United Utilities Water Limited

Your attention is drawn to Section 122 of the Water Industry Act 1991 which provides that any person aggrieved by any conditions attached to this Consent may appeal to the Director General of Water Services.

Appendix F Concrete Class Certification

Copyright © 1976 - 2024 Buro Happold. All rights reserved

PJ CAREY – CO-OP LIVE MANCHESTER

DOCUMENT TYPE:	**Certificate**
DOCUMENT NUMBER:	**BRA-CCE-ZZ-ZZ-CT-Y-00001**
DOCUMENT TITLE:	**Concrete Mix Change**
STATUS:	**S3**
REVISION:	**P01**
DATE OF ISSUE:	**07/03/2022**

CONCRETE DESIGN CERTIFICATE

Mix Design Certificate **1006588545** **Quotation Number** 1006432541
Dated 23.02.2022 **Your Ref.**

Tarmac Limited
North West RMX Sales
Langley Road South
Agecroft
Salford
M6 6LQ
Tel 0161 2317111

To: **PJ CAREY (CONTRACTORS) LTD**
CAREY HOUSE
GREAT CENTRAL WAY
WEMBLEY
LONDON HA9 0HR

Site: **OVG NEW MANCHESTER ARENA M11 3FF**
ALAN TURING WAY
MANCHESTER
GREATER MANCHESTER
M11 3FF

Our Representative: Mr Ben Bland

Specification	**Our Ref.:**	
Plant	Salford	
	2	
Concrete Grade	C35/45	
Mix Type	PUMPABLE	
Cement Type	CIIIB+SR	
Maximum Aggregate Size (mm)	10	
Target Slump (mm)	S3	
Minimum Cement Content	380	
Max Water / Cement Ratio	0.45	
Chloride Class	0.40	
Maximum Alkali Content	3.50	
DC Class	DC4	
Brand	CONCRETE	
Customer's Mix Ref	MIX 3 10MM	

Mix Design: Materials & Mix Proportions: kg/m^3 at SSD unless otherwise specified

CEM I_52,5N Irish Cement, Limerick	129	
GGBS_Scun LKAB Minerals, Scunthorpe	300	
4/10mm Limestone (EN 12620) Tarmac, Tunstead	1080	
0/4mm Limestone (EN 12620) Tarmac, Tunstead	342	
0/4mm Sand MP (EN 12620) Tarmac, Crown Farm	342	
Chrysoplast RMD Chryso UK, Daventry	2.57	L
Water	193	
Aggregate/ Cement Ratio	4.11	
Water/ Cement Ratio	0.45	
Percentage Fines	38.78	
Actual Chloride Content	0.05	
Actual Alkali Content	1.00	

Please Note:

HEALTH & SAFETY

There is a real danger of contact dermatitis or serious burns if skin comes into contact with wet cement mixes such as fresh concrete, mortar or screed. Wear suitable protective clothing and eye protection. Where skin contact occurs either directly or through saturated clothing wash immediately with soap and water. For eye contact, immediately wash out the eyes thoroughly with clean water. If swallowed wash out mouth and drink plenty of water.

For and on behalf of
Tarmac Limited

Technical Services Department

This design is relevant to the above quotation of which it is a part thereof and subject to our Standard Conditions of Sale
This certificate is for illustrative purposes only, the materials and mix design(s) are those in current production, these may be changed and/or modified when material properties vary or supply sources change.

Tarmac Trading Limited
Registered in England and Wales No. 453791
Registered Office: Portland House, Bickenhill Lane, Solihull, Birmingham, B37 7BQ
Tarmac and the 'circle' logo are registered trademarks

Appendix G Provectus Environmental Monitoring (RAMS)

Copyright © 1976 - 2024 Buro Happold. All rights reserved

Project Name:	**Co-op Live**	**Project No:**	**101114**
Title:	**Environmental Monitoring Method Statement and Risk Assessment**		
Site Address:	**BAM Construction Site, Sport City Way, Manchester, M11 3DU**		
Client:	**BAM Construction Ltd**		

Prepared by:	Sam Lane-Ryan Technical Manager	Signature:	Date: 24/03/21
Approved by:	Alex Clifford Project Manager	Signature:	Date: 24/03/21
Revision:	Rev 0	Changes:	Date:
Review:	Tom Harrington Project Manager	Review Date:	24/10/21
Changes	• Addition of borehole decommissioning methodology		

1 Activities / Scope of Work:

- Monitor environmental conditions at the proposed locations within the Mobile Treatment Permit Deployment Form 101114/L101/AC (Figure 4 101114STA-1).
- Monitoring to include:
  - Noise to BS4142 standard
  - Dust – Quantifiable Frisbee Dust Sampling
  - Dust - Visible
  - Odour – Quantitative
  - Asbestos monitoring via sub-contractor- (RAMS to be provided by Sub contractor- See RAMS016)
  - Air Quality Monitoring – Gas and Vapour via Photo-Ionisation Detector (PID)
  - Weather assessment
  - Visual inspection of potential site run-off to the canal
  - Visual inspection of the Water Treatment Plant and daily flow meter reading
  - Borehole decommissioning across the site

2 Who Might be Harmed and Significant Hazards

Provectus Engineers are at risk during this activity

The main hazards associated with the above activities are:

- Construction hazards including slips, trips and falls on uneven ground, minor injuries associated with manual handling and housekeeping activities.
- Physical/strike or unsafe use hazards associated with moving plant
- Manual Handling – carrying of monitoring equipment

3 Related Documents

1. Construction Phase Health and Safety Plan 101114
2. RAMS001- COVID-19 Working Practices
3. 101114 Site Layout PRL Drawing
4. RAMS016 – Asbestos Air Monitoring
5. Provectus Environmental Monitoring Form 101114
6. Site Traffic Management Plan 101114
7. Mobile Treatment Permit Deployment Form 101114/L101/AC (Figure 4 101114STA-1)
8. Provectus Calibration of Monitoring Equipment Work Instruction PRO\WI\18 Revision 5.

4 Plant or Equipment to be Used:

- Noise meter (DBA meter)
- Photo-ionisation device (PID),
- Dust gauges and Frisbees with stands
- Deionised or distilled water
- Brush
- Asbestos Air Pumps
- Camera
- Bentonite Pellets, grout mix and powder

5 Plant / Operative Certification / Permits / Training Required

1. Site induction, Traffic Management Plan, Site Rules, Emergency Procedures
2. Engineers to be competent and hold relevant CSCS Card
3. Site manager must be first aid trained as a minimum during Monitoring Works.

6 Personal Protective Equipment

Item	Required	Item	Required
High Visibly Vest / Jacket - BS EN 471	Y	Hard Hat BS EN 397	Y
Nitrile Gloves - (During Dust Sampling)	Y	Protective Gloves BS EN 352- during Frisbee set up	Y
Protective boots steel toe and mid sole (BS EN 345	Y	Fire retardant Overalls	N
Ear Protection	N	Safety glasses BS EN 166	Y
Disposable overalls	N	Other	N

7 Method / Procedures

7.1 Ensure all monitoring equipment is within calibration date. If calibration certificate has elapsed, arrange for unit to be calibrated and obtain a new unit within calibration.

7.2 'Bump-test' PID daily, to ensure readings are within range, using 100ppm isobutylene. If out of range (+/- 10%) manually calibrate unit following the Work Instruction PRO\WI\18.

7.3 Record weather assessment on the Provectus Environmental Monitoring Form 101114

7.4 The monitoring will be undertaken at the four sampling points across the boundary of site referenced as BMP1-4 on Figure 4 101114STA-1 (Figure 1 exert below) on a daily basis.

7.5 The monitoring will occur during operational hours, not over break time to ensure monitoring data is a fair representation of site environmental emissions.

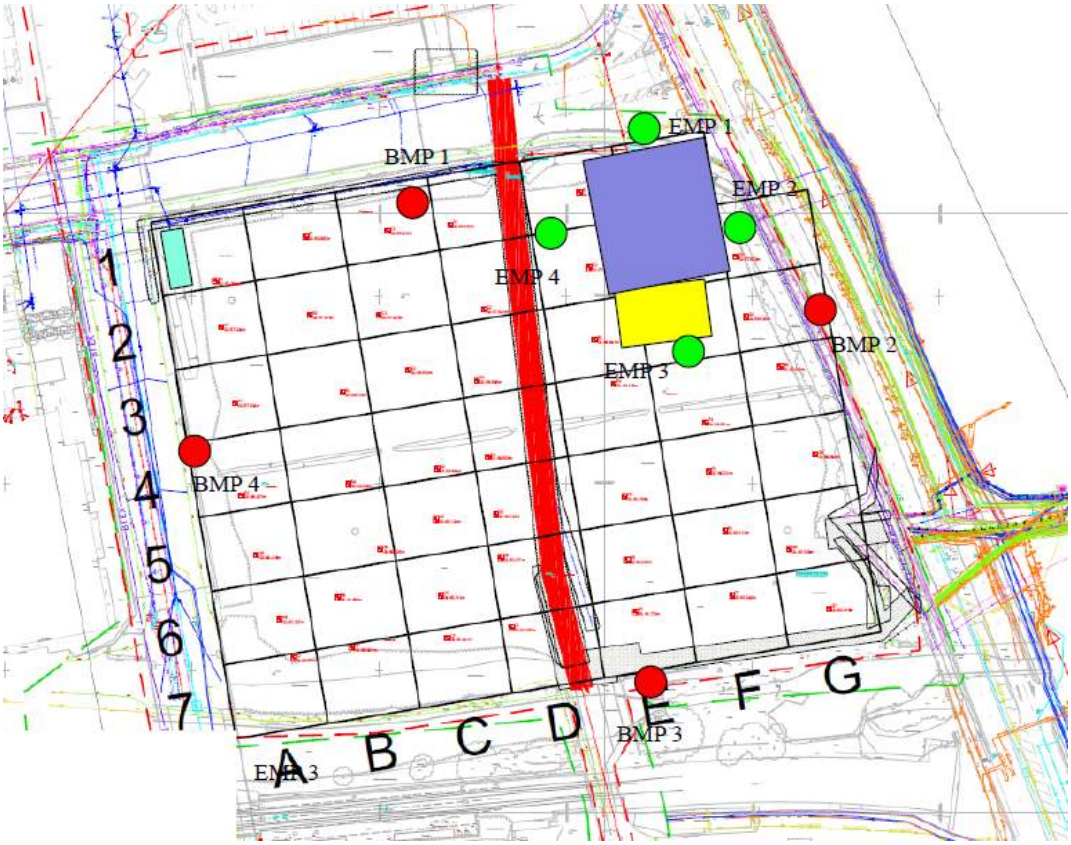


Figure 1 – Environmental Monitoring Points

7.6 The boundary monitoring points will be marked on the site boundary fencing to ensure consistency of location.

7.7 Monitoring points are set up by hand ensuring that the pedestrian routes are adhered to at all times and appropriate manual handling techniques used when lifting and transporting the Frisbee stands across site.

7.8 The agreed parameters (visual dust, noise, odour and volatile compounds) will be monitored at each of the four boundary locations for a 15 minute period noting the peak and average readings for noise and volatile compounds. Results will be recorded on the Provectus Environmental Monitoring Form 101114.

7.9 Odour monitoring will be carried out three times a day at each boundary location. Dust and noise only require one round of monitoring per day.

7.10 The Frisbee Deposition Gauges will be sampled monthly by removing the foam disc and rinsing the gauge into the sample collection bottle using 100 ml of distilled (or deionised) water and clean brush. The sample collection bottle will be labelled with site, project reference, monitoring location and date. Any leaves, bird droppings or other extraneous material should be removed with the foam disc and noted one the sample chain of custody. Nitrile gloves to be worn during Frisbee sampling works.

7.11 During excavation works further odour and PID monitoring will be conducted on an ad hoc basis by the environmental supervisor as part of the watching brief. This is covered in RAMS012

7.12 The work place monitoring points shown as EMP1-4 on Figure 1 will be monitored once a day (15 mins per location) during operational hours but only when soil treatment activities are taking place.

7.13 EMP locations will be at the boundary of the demarcated treatment area and will move if the treatment area changes size or shape significantly. These monitoring points will be located at a safe distance from moving plant. They will be recorded on the site traffic management plan and will be described in site inductions.

7.14 The canal will be monitored once a day during operational hours; this will comprise a visual assessment of potential impact from site run-off, this is a simple inspection and does not have a minimum time requirement at each location. There are three locations CMP1-3 as shown in Figure 2, below.



Figure 2 – Canal Visual Monitoring Points

7.15 The engineer undertaking the canal monitoring will inform the site supervisor when leaving site to observe the canal and when returning to site so lone working can be monitored.

7.16 A daily inspection of the Water Treatment Plant (WTP) will be carried out as part of the environmental monitoring works. This will note any leaks or over-topping of the WTP as well as the Flow Meter reading. The WTP inspection will be recorded on the Provectus Environmental Monitoring Form 101114.

7.17 Borehole decommissioning will be undertaken by Provectus across the site. This will include the complaint backfill and reinstatement of ten groundwater monitoring wells installed onsite, as part of the historical site investigation and monitoring works. All wells will be reinstated as per the EA "Good practice for decommissioning redundant boreholes and wells" document LIT

6478 / 657_12, October 2012.

7.18 The wells will be dipped and filled with Bentonite pellets/powder mix from a 25kg bag, from base, up to 1-2m from the top of ground level. Operatives must comply with the sites Manual Handling Risk Assessment and MAC Assessment. A grout mix will then be used to seal the top of the borehole to finish. Logs will be produced and kept on file, showing the makeup of each decommissioned well.

8 Site Rules and Emergency Procedures

The site rules, Traffic management Plan and emergency procedures are displayed on the site notice board and will be briefed during the site induction. Any changes to TMP to be relayed to site staff in daily briefing, prior to commencing works each day.

Risk Assessment

Activity/ Element	Hazard	Likelihood	Severity	Initial Risk	Control Measures *Using Hierarchical approach*	Likelihood	Severity	Residual Risk	Action by (Comments)
All work activities	Unawareness of clear objectives and procedures for specific tasks can lead to confusion and misunderstanding which in turn heightens the risk of an unplanned event which may lead to damage or injury	3	5	**15**	Site manager is to give an Induction into working methodology for the task being undertaken. In addition, a daily briefing to all site staff will be given clearly identifying specific tasks for the day with clear instruction as to how these are to be undertaken. Detail any updates to the traffic management plan, including changes to pedestrian routes.	1	5	**5**	Site Manager Engineer
Environmental monitoring	Plant striking operative	2	5	**10**	Operative to make contact with any driver in close proximity and inform them where you shall be working however, pedestrianised routes should be used at all times Operative to not access specifically demarked work areas (screener /crusher). Move monitoring point outside demarked area. Banksman aware of monitoring activities and communicate with engineer regarding access. If required, works will cease and monitoring will be undertaken until the engineer has left the area. Ensure operators are not tired or fatigued and have regular rest breaks. Use trained banks men where appropriate Mobile phones or personal stereos when operating plant and equipment is strictly prohibited – be alert Cab radio use should only be used when machine is inactive or on breaks.	1	5	**5**	Banksman, Engineer, Site Manager, Operators

		SEVERITY				
		1	**2**	**3**	**4**	**5**
LIKELIHOOD	**1**	**1**	**2**	**3**	**4**	**5**
	2	**2**	**4**	**6**	**8**	**10**
	3	**3**	**6**	**9**	**12**	**15**
	4	**4**	**8**	**12**	**16**	**20**
	5	**5**	**10**	**15**	**20**	**25**

***LIKELIHOOD:**				
1 =rare	**2** =unlikely	**3** =moderate	**4** =likely,	**5** = very likely
***SEVERITY:**				
1 =insignificant	**2** =minor	**3** =moderate	**4** =major	**5**=catastrophic
***RISK = LIKELIHOOD X SEVERITY:**				
1 to 4 = Acceptable	**5 to 9 = Adequate**	**10 to 16 = Tolerable,**	**17 to 25 = Unacceptable**	

Activity/ Element	Hazard	Likelihood	Severity	Initial Risk	Control Measures *Using Hierarchical approach*	Likelihood	Severity	Residual Risk	Action by (Comments)
Environmental monitoring	Injury from falling / slipping	2	5	**10**	Ensure ground is free of debris Stick to pedestrian routes Look at path you take Move monitoring point to new location if excavation within 5m. Good housekeeping along pedestrian routes.	1	5	**5**	Banksman, Engineer, Site Manager, Operators, labourers, foreman
Environmental monitoring	Manual handling	2	3	**6**	Do not overload yourself and carry a practical load ensuring visibility at all times. Lift with your knees and back straight when lifting items. Place items in bag to carry if required and ask for help where required. Refer to the Manual Handling RA and MAC Assessment Tool, kept in the site office.	1	3	**3**	Engineer
Mobile Plant General Site Operation	Lack of awareness / attention / concentration by operators. Use of mobile phones or personal stereos Loud music in cabs	3	5	**15**	Ensure operators are not tired or fatigued and have regular rest breaks. Use trained banks men where appropriate Mobile phones or personal stereos when operating plant and equipment is strictly prohibited – be alert Cab radio use should only be used when machine is inactive or on breaks.	1	5	**5**	Site Manager Operators Banksman Engineer
Canal monitoring	Falling in the canal Off-site lone working	3	5	**15**	Stick to the canal footpath. Don't take longer than needed Inform site supervisor at the start and finish (leaving site and returning to site) of the monitoring activity	1	5	**5**	Site Foreman Site Manager Operators
Borehole Backfilling	Manual Handling and exposure to grout	3	5	**15**	Do not overload yourself and carry a practical load ensuring visibility at all times. Lift with your knees and back straight when lifting grout bags. Refer to the Manual Handling RA and MAC Assessment Tool, kept in the site office.Refer to the sites COSHH Assessment when using grout mix. Use of site safety glasses and rubber A120 Gloves when handling grout mix.	1	5	**5**	Operatives/ Engineers

		SEVERITY				
		1	**2**	**3**	**4**	**5**
LIKELIHOOD	**1**	**1**	**2**	**3**	**4**	**5**
	2	**2**	**4**	**6**	**8**	**10**
	3	**3**	**6**	**9**	**12**	**15**
	4	**4**	**8**	**12**	**16**	**20**
	5	**5**	**10**	**15**	**20**	**25**

***LIKELIHOOD:**
1 =rare **2** =unlikely **3** =moderate **4** =likely, **5** = very likely

***SEVERITY:**
1 =insignificant **2** =minor **3** =moderate **4** =major **5**=catastrophic

***RISK = LIKELIHOOD X SEVERITY:**

1 to 4 = Acceptable	5 to 9 = Adequate	10 to 16 = Tolerable,	17 to 25 = Unacceptable

Person Responsible for communication of the assessment: Tom Harrington/Sam Lane-Ryan
TO BE READ TO ALL PERSONNEL RECEIVING INSTRUCTION: I acknowledge that I have received instruction in respect of the hazards and risks associated with the work activity described above. I understand the hazards and the control measures to be applied and I have had the opportunity to have any questions answered on any related matters in respect of this element of work.

No.	Print Name	Role / Occupation	Signature	Date
1				
2				
3				
4				
5				
6				
7				
8				
9				
10				

END OF DOCUMENT

		SEVERITY				
		1	**2**	**3**	**4**	**5**
LIKELIHOOD	**1**	**1**	**2**	**3**	**4**	**5**
	2	**2**	**4**	**6**	**8**	**10**
	3	**3**	**6**	**9**	**12**	**15**
	4	**4**	**8**	**12**	**16**	**20**
	5	**5**	**10**	**15**	**20**	**25**

***LIKELIHOOD:**				
1 =rare	**2** =unlikely	**3** =moderate	**4** =likely,	**5** = very likely
***SEVERITY:**				
1 =insignificant	**2** =minor	**3** =moderate	**4** =major	**5**=catastrophic
***RISK = LIKELIHOOD X SEVERITY:**				
1 to 4 = Acceptable	**5 to 9 = Adequate**	**10 to 16 = Tolerable,**	**17 to 25 = Unacceptable**	


Appendix H Borehole Decommissioning

Copyright © 1976 - 2024 Buro Happold. All rights reserved

Borehole Decommissioning Register


Project: Co-op Live
Ref: 101114

Borehole	Actual (m) Depth		m3	Comment
	Borehole 1	Borehole 2	Borehole Volume	
BH19/02A	49.5	17.55	Not found on arrival to site	Not found on arrival to site
BH19/03	29.71	N/A	Not found on arrival to site	Not found on arrival to site
	20.85			Decommissioned
BH19/05	50	Only 1 pipe	0.041	31.03.21
BH19/07C	23.1			Decommissioned
Diameter	35mm	Only 1 pipe	0.031	30.03.21
BH19/09	42.6	14.1		Decommissioned
Diameter	35mm	35mm	0.074	29.03.21
BH19/11	24.7	14.5		Decommissioned
Diameter	35mm	50mm	0.06	31.03.21
BH19/13	8.75	26.2		Decommissioned
Diameter	35mm	35mm	0.043	29.03.21
BH19/15	41.8	12.5		Decommissioned
Diameter	35mm	50mm	0.078	07.04.21
BH19/17	15.1	25.1		Decommissioned
Diameter	35mm	35mm	0.013	07.04.21
BH19/14	28.3			Decommissioned
Diameter	35mm	Only 1 pipe	0.044	07.04.21
Total			**0.384**	

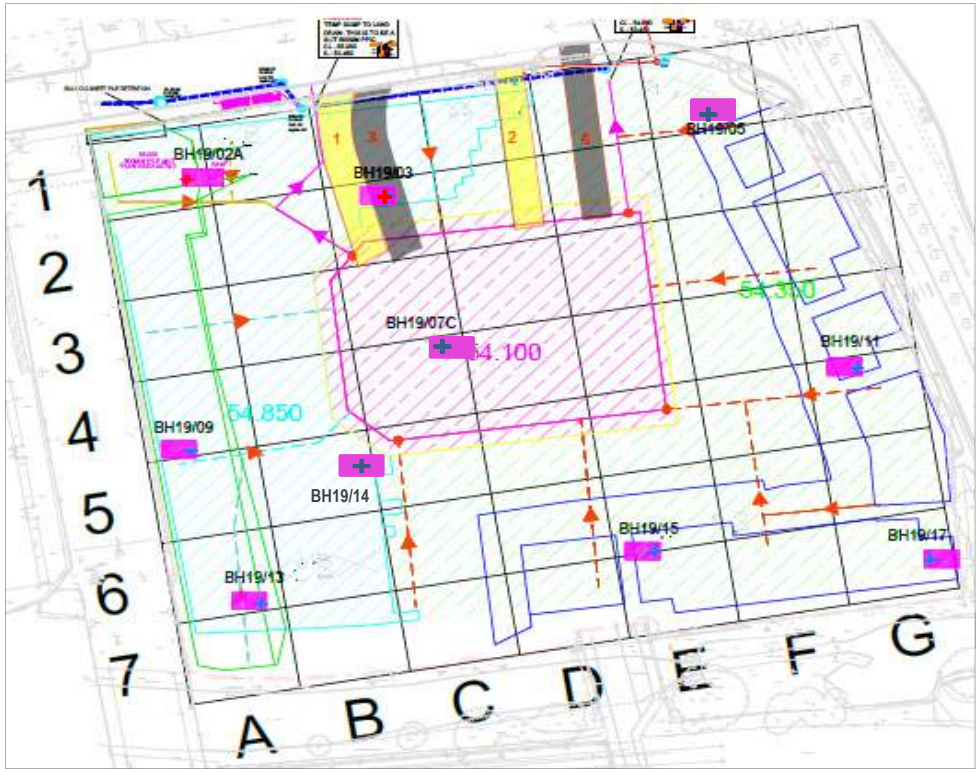

PROVECTUS	Client	BAM Construction	Well Log	
	Project	101114 Co-op Live	Well No.	BH19.05
	Address	Sports City Way, Manchester	Page	1 of 1

Decom Date	31.03.21	Well 1 Depth	20.85	Well 2 Depth	
Logged by	TH	Well 1 Diameter	50mm	Well 2 Diameter	

Depth (m)	Backfill Detail	Remarks
0		*Monitoring wells backfilled using Bentonite pellets to base of borehole in 0.20m sections up to ground level. Boreholes will be cut off following the sealing of the clay pellets, during the impending earthwork excavation works.*
1		
2		
3		
4		
5		
6		
7		
8		
9		
10		
11		**Photos**
12		 
13		
14		
15		
16		
17		
18		
19		
20		
21		
22		
23		
24		
25		
26		
27		
28		
29		
30		

PROVECTUS	Client	BAM Construction	Well Log	
	Project	101114 Co-op Live	Well No.	BH19.07C
	Address	Sports City Way, Manchester	Page	1 of 1

Decom Date	30.03.21	Well 1 Depth	23.1m	Well 2 Depth	
Logged by	TH	Well 1 Diameter	35mm	Well 2 Diameter	

Depth (m)	Backfill Detail
0	
1	
2	
3	
4	
5	
6	
7	
8	
9	
10	
11	
12	
13	
14	
15	
16	
17	
18	
19	
20	
21	
22	
23	
24	
25	
26	
27	
28	
29	
30	

Remarks

Monitoring wells backfilled using Bentonite pellets to base of borehole in 0.20m sections up to ground level. Boreholes will be cut off following the sealing of the clay pellets, during the impending earthwork excavation works.

Photos



PROVECTUS	Client	BAM Construction	**Well Log**
	Project	101114 Co-op Live	Well No. BH19.09
	Address	Sports City Way, Manchester	Page 1 of 1

Decom Date	29.03.21	**Well 1 Depth**	14.1	**Well 2 Depth**	42.6
Logged by	TH	**Well 1 Depth**	35mm	**Well 2 Diameter**	35mm

Depth (m)	Backfill Detail
0	
1	
2	
3	
4	
5	
6	
7	
8	
9	
10	
11	
12	
13	
14	
15	
16	
17	
18	
19	
20	
21	
22	
23	
24	
25	
26	
27	
28	
29	
30	
31	
32	
33	
34	
35	
36	
37	
38	
39	
40	
41	
42	
43	

Monitoring wells backfilled using Bentonite pellets to base of borehole in 0.20m sections up to ground level. Boreholes to be cut further to formation, as earthwrks progress.


Photos





PROVECTUS	Client	BAM Construction	Well Log	
	Project	101114 Co-op Live	Well No.	BH19.11
	Address	Sports City Way, Manchester	Page	1 of 1

Decom Date	31.03.21	Well 1 Depth	24.7	Well 2 Depth	14.5m
Logged by	TH	Well 1 Depth	35mm	Well 2 Diameter	50mm

Depth (m)	Backfill Detail
0	
1	
2	
3	
4	
5	
6	
7	
8	
9	
10	
11	
12	
13	
14	
15	
16	
17	
18	
19	
20	
21	
22	
23	
24	
25	
26	
27	
28	
29	
30	

Monitoring wells backfilled using Bentonite pellets to base of borehole in 0.20m sections up to ground level. Boreholes will be cut off following the sealing of the clay pellets, during the impending earthwork excavation works.

Photos






PROVECTUS	Client	BAM Construction	Well Log	
	Project	101114 Co-op Live	Well No.	BH19.13
	Address	Sports City Way, Manchester	Page	1 of 1

Decom Date	29.03.21	Well 1 Depth	8.75	Well 2 Depth	26.2
Logged by	TH	Well 1 Depth	35mm	Well 2 Diameter	35mm

Depth (m)	Backfill Detail
0	
1	
2	
3	
4	
5	
6	
7	
8	
9	
10	
11	
12	
13	
14	
15	
16	
17	
18	
19	
20	
21	
22	
23	
24	
25	
26	
27	
28	
29	
30	



Monitoring wells backfilled using Bentonite pellets to base of borehole in 0.20m sections up to ground level. Boreholes will be cut off following the sealing of the clay pellets, during the impending earthwork excavation works.

Photos






PROVECTUS	Client	BAM Construction	Well Log	
	Project	101114 Co-op Live	Well No.	BH19.14
	Address	Sports City Way, Manchester	Page	1 of 1

Decom Date	07.04.21	Well 1 Depth	28.3	Well 2 Depth	
Logged by	TH	Well 1 Diameter	35mm	Well 2 Diameter	

Depth (m)	Backfill Detail
0	
1	
2	
3	
4	
5	
6	
7	
8	
9	
10	
11	
12	
13	
14	
15	
16	
17	
18	
19	
20	
21	
22	
23	
24	
25	
26	
27	
28	
29	
30	



Remarks

Monitoring wells backfilled using Bentonite pellets to base of borehole in 0.20m sections up to ground level. Boreholes will be cut off following the sealing of the clay pellets, during the impending earthwork excavation works.


Photos



PROVECTUS	Client	BAM Construction	Well Log	
	Project	101114 Co-op Live	Well No.	BH19.15
	Address	Sports City Way, Manchester	Page	1 of 1

Decom Date	07.04.21	Well 1 Depth	41.8	Well 2 Depth	12.5
Logged by	TH	Well 1 Depth	35mm	Well 2 Diameter	50mm

Depth (m)	Backfill Detail
0	
1	
2	
3	
4	
5	
6	
7	
8	
9	
10	
11	
12	
13	
14	
15	
16	
17	
18	
19	
20	
21	
22	
23	
24	
25	
26	
27	
28	
29	
30	
31	
32	
33	
34	
35	
36	
37	
38	
39	
40	
41	
42	



Monitoring wells backfilled using Bentonite pellets to base of borehole in 0.20m sections up to ground level. Boreholes will be cut off following the sealing of the clay pellets, during the impending earthwork excavation works.


Photos





PROVECTUS	Client	BAM Construction	Well Log	
	Project	101114 Co-op Live	Well No.	BH19.17
	Address	Sports City Way, Manchester	Page	1 of 1

Decom Date	07.04.21	Well 1 Depth	15.1	Well 2 Depth	25.1
Logged by	TH	Well 1 Depth	35mm	Well 2 Diameter	35mm

Depth (m)	Backfill Detail
0	
1	
2	
3	
4	
5	
6	
7	
8	
9	
10	
11	
12	
13	
14	
15	
16	
17	
18	
19	
20	
21	
22	
23	
24	
25	
26	
27	
28	
29	
30	

Diameter measured to be 35mm and not 19mm as initially estimated. Monitoring wells backfilled using Bentonite pellets to base of borehole in 0.20m sections up to ground level.

Photos



Appendix I Ground Gas Membrane Sign Off Certification

(Selection of certificates provided)

Copyright © 1976 - 2024 Buro Happold. All rights reserved

Co-Op Live, Manchester - C777
24.1.2022

Site name: BAM Site Offices, Co-Op Live, Etihad Campus, Alan Turing Way, Manchester **Postcode: M11 3FF**	**Units / Area checked: Slab area to gridlines W07 – W08 & EW**
Installers Name: Careys Civil Engineering	
Date: 24/01/2022	
Inspection by: Barrie Ackroyd / Dan Squire	**Weather: 4ºC Dry**

Item	Comments	
Sub-floor void	N/A	
Ventilation Inlets and Outlets	N/A	
Number Of Vents	N/A	
Materials used:	Membrane – Preprufe 300R Plus Membrane	
	Self-Adhesive Membrane ☐ Yes	Preformed Top hats ☐ Yes
	Double Sided Butyl Tape ☐ Yes	Preformed Corners ☐ Yes
	Others Please List: Preprufe Tape, Bituthene LM E, Bitustik BT 240 double sided jointing tape.	
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** MTS Ltd carried out a thorough visual inspection of the membrane, the membrane had been installed to a very good standard. The membrane is lined across the main floor and tape jointed in line with GPC material specifications and industry best practices. The membrane was jointed into the perimeter liner wall membrane and all stainless steel starter bars were sealed with the Bituthene LM E trowel applied membrane. We employed seam pick probe seam integrity testing and we are pleased to advise there were no defects to report. We also noted the waterbar's had been weld jointed using the hot knife and stuck don to the 300R membrane using the Bitustik BT 240 double sided jointing tape. There were no defects to report.	

Co-Op Live, Manchester - C777
3.2.2022

Site name: BAM Construction. Co-Op Live. Manchester **Postcode: M11 3DU**	**Units/ plots checked: North west slab - Pour 2. Main floor installation Gridlines W06-W08 / NW - N01** **Core 5 - Base installation Gridlines E07-BS / N12-BE**
Installers Name: P J Carey's	
Date: 03/02/2022	
Inspection by: Dan Squire	**Weather: 9°C Dry**

Item	Comments	
Sub-floor void	N/A	
Ventilation Inlets and Outlets	N/A	
Number Of Vents	N/A	
Materials used:	Membrane – Preprufe 300R Plus	
	Self-Adhesive Membrane ☒ Yes	Preformed Top hats ☐ Yes
	Double Sided Butyl Tape ☐ Yes	Preformed Corners ☐ Yes
	Others Please List: Bituthene LM. Bituthene Liquid membrane	
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** MTS Ltd carried out a thorough visual inspection of the membrane, the membrane had been installed to a good standard. Preprufe 300R plus membrane has been lined across the pour slab areas as noted and is joined to the membrane previously installed up the liner wall to the capping beam. The membrane has a permanent back binding which is used to join the membrane together and is pressure rolled. In some areas an additional strip of Preprufe Tape LT has been added on top of the joints. A mix of Bituthene LM & Bituthene liquid membrane is applied to seal all penetrations. Patch repairs have been made to the membrane along the vertical face of the liner wall and also on the floor where a few minor damages were caused by the steel using Preprufe 300R plus membrane and strips of Preprufe LT tape.	

Installation Notes Continued	Site were carrying out their own ongoing inspections and cleaning off the membrane as the install progressed and prior to the pour. Approx 50% of the areas to inspect were restricted due to steel work on the membrane.					
Type of Joint	Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐		
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)			
Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?			☒ Yes	☐ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?			☒ Yes	☐ No	☐ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Has all other detailing work passed inspection			☒ Yes	☐ No	☐ N/A
	(List any defects to detailing work and joints): During our inspection the following defects and repairs were carried out: No recorded defects. However, holes were in the membrane in preparation for the starter bars which will then be sealed using the Bituthene LM and Liquid membrane mix once in place. Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A The Area has passed inspection ☒ The Area has failed inspection and a corrective action sheet has been left with the contractor ☐ The Area is incomplete as detailed above ☐ Signed: **Dan Squire** Date: **03/02/2022**					

Area Inspected

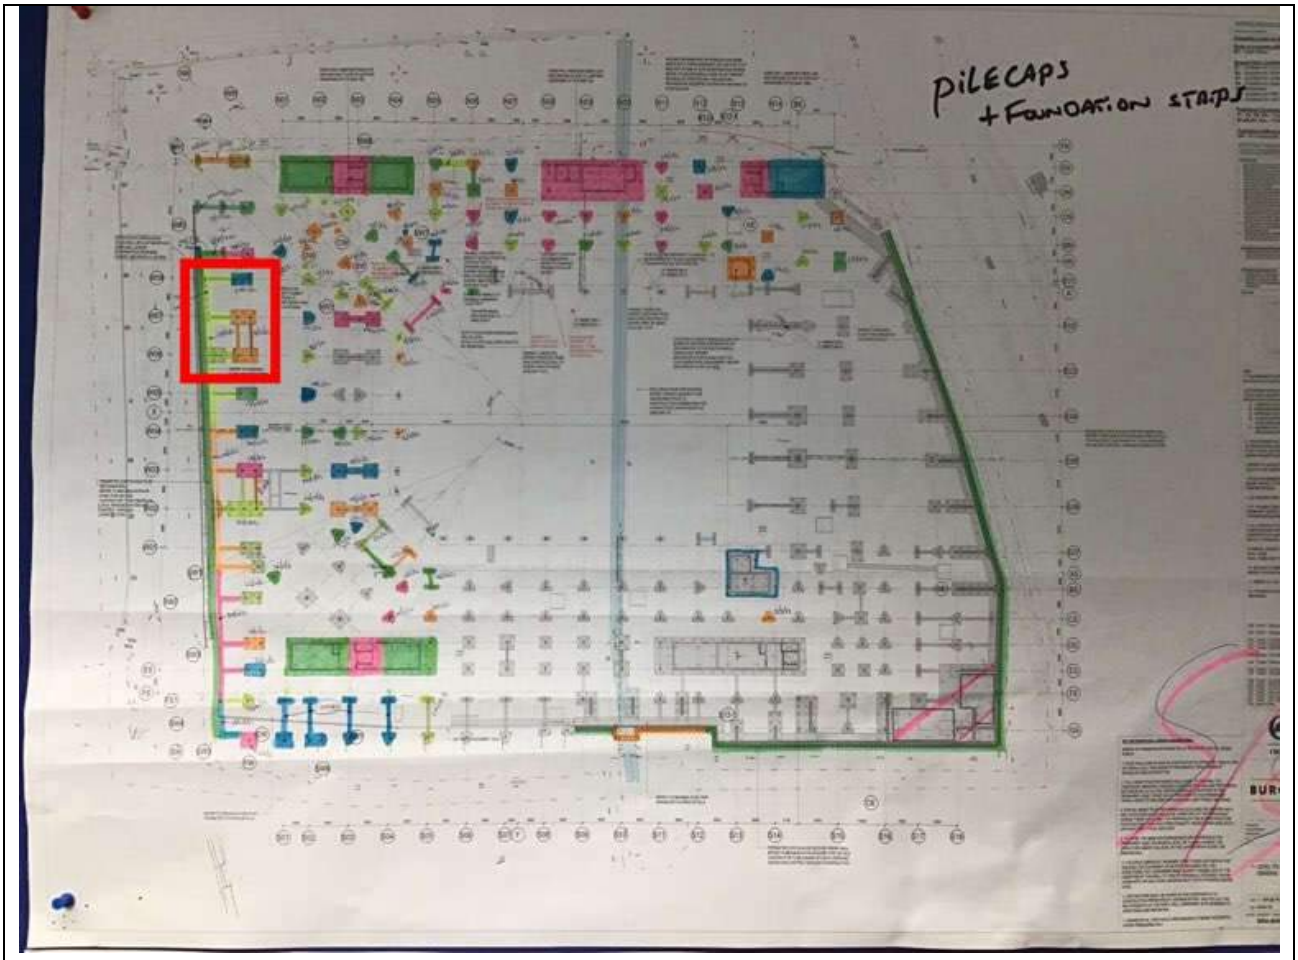


Photo **03/02/2022**



Restricted inspection area



North west pour 2 slab line out



Liner wall patch repairs



Bituthene LM and liquid membrane mix sealed penetrations



Sealed pipe penetration using Bituthene LM and liquid membrane mix



Sealed penetration using Bituthene LM and liquid membrane mix



Probe test to adhesive backing joint

Site name: BAM Construction. Co-Op Live. Manchester **Postcode: M11 3DU**	**Units/ plots checked: Core 5 - Base installation Gridlines E07-BS / N12-BE**
Installers Name: P J Carey's	
Date: 03/02/2022	
Inspection by: Dan Squire	**Weather: 9°C Dry**

	Item	**Comments**	
Sub-floor void		N/A	
Ventilation Inlets and Outlets		N/A	
Number Of Vents		N/A	
Materials used:		Membrane – Preprufe 300R Plus	
		Self-Adhesive Membrane ☒ Yes	Preformed Top hats ☐ Yes
		Double Sided Butyl Tape ☐ Yes	Preformed Corners ☐ Yes
		Others Please List: Bituthene LM. Bituthene Liquid membrane	
Installation Notes		**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** MTS Ltd carried out a thorough visual inspection of the membrane, the membrane had been installed to a good standard. Preprufe 300R plus membrane has been lined across the core base area as noted and extends up the vertical face of the core walls to be able to join membrane at a later date. The membrane has a permanent back binding which is used to join the membrane together and is pressure rolled. In some areas an additional strip of Preprufe Tape LT has been added on top of the joints. A mix of Bituthene LM & Bituthene liquid membrane is applied to seal all pile caps. Site were carrying out their own ongoing inspections and cleaning off the membrane as the install progressed. All prep work including drying off the concrete floor and smoothing of the pile caps prior to the install were carried out well. The core area base was approx 25% when the inspection took place and all works were being carried out well and sufficiently.	

Type of Joint	Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐	
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)		
Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?		☒ Yes	☐ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?		☐ Yes	☐ No	☒ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?		☐ Yes	☐ No	☒ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?		☒ Yes	☐ No	☐ N/A
	Has all other detailing work passed inspection		☐ Yes	☐ No	☒ N/A
	(List any defects to detailing work and joints): During our inspection the following defects and repairs were carried out: No recorded defects. Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A The Area has passed inspection ☒ The Area has failed inspection and a corrective action sheet has been left with the contractor ☐ The Area is incomplete as detailed above ☐ Signed: **Dan Squire** Date: **03/02/2022**				

Area Inspected

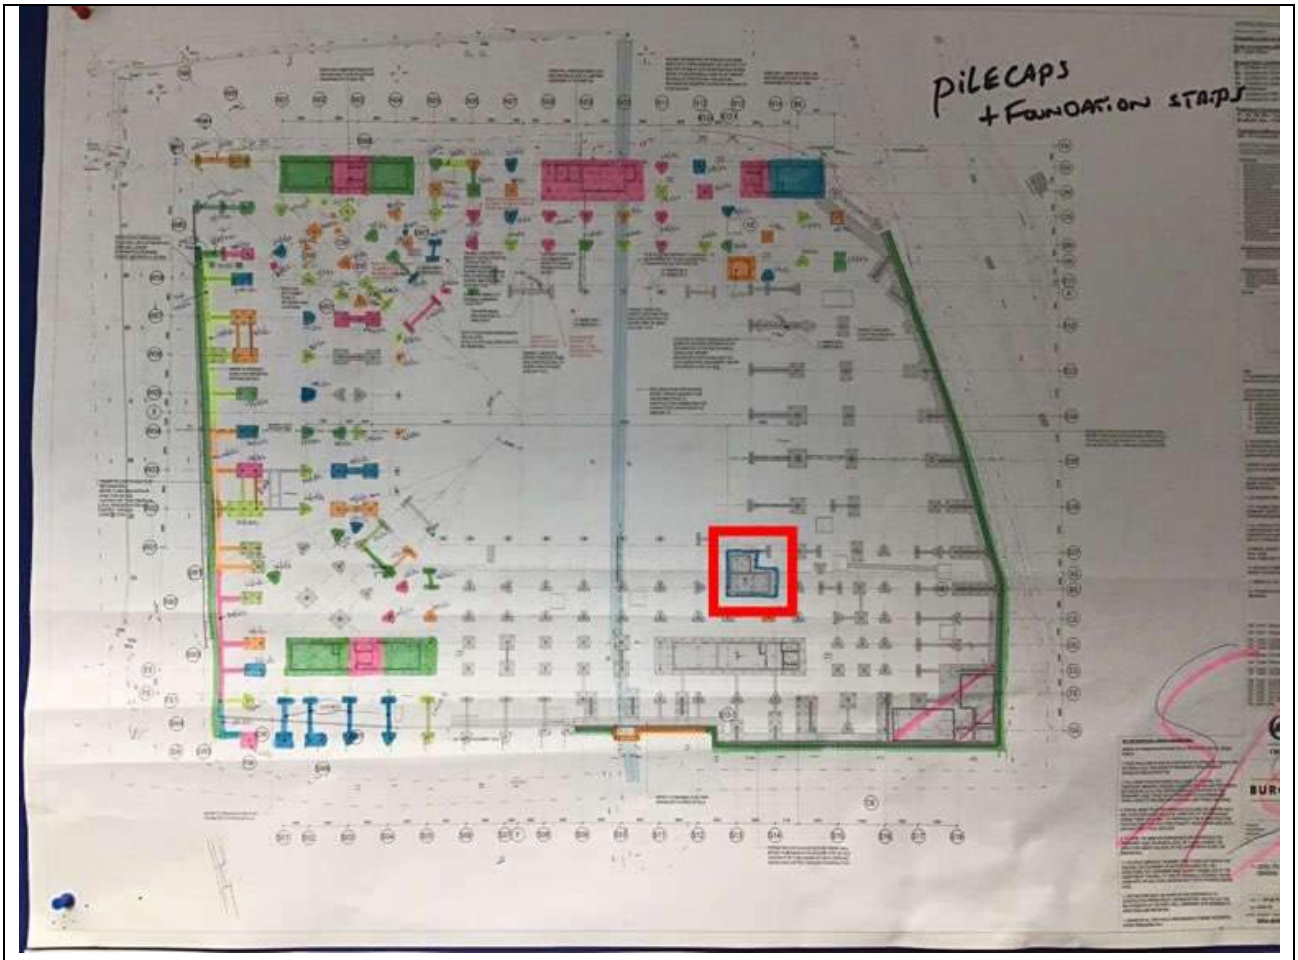


Photo **03/02/2022**



Core 5 base installation



Pile cap good prep work



Drying of the concrete prior to the install of membrane



Sealed pile cap using the Bituthene LM mixed with liquid membrane



Sealed membrane adhesive joint



Sealed and formed corner detailing using Preprufe 300R plus membrane and Preprufe tape LT

Test and Inspection Result 'PASS In FULL' to Both Areas

The areas have passed the inspection and a re-visit is not required.



Signed: Barrie Ackroyd Date: 3.2.2022


On Behalf of Membrane Testing Solutions Ltd

Co-Op Live, Manchester - C777
24.2.2022

Site name: BAM Construction. Co-Op Live. Manchester **Postcode: M11 3DU**		**Units/ plots checked: : Core 5 - Wrap installation Gridlines E07-BS / N12-BE**
Installers Name: P J Carey's		
Date: 24/02/2022		
Inspection by: Dan Squire		**Weather: 2ºC Wet**
Item		
Sub-floor void	N/A	
Ventilation Inlets and Outlets	N/A	
Number Of Vents	N/A	
Materials used:	Membrane – Preprufe 300R Plus	
	Self-Adhesive Membrane ☒ Yes	Preformed Top hats ☐ Yes
	Double Sided Butyl Tape ☐ Yes	Preformed Corners ☐ Yes
	Others Please List: Bituthene LM. GCP Bituthene primer S2. Bituthene 8000/S tanking	
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** MTS Ltd carried out a thorough visual inspection of the tanking wrap installation. Preprufe 300R plus membrane has been lined across the core base area and extends up the vertical face of the core walls. Bituthene LM mix has been applied to the membrane on show at the top of the pile cap to help adhere the Bituthene 8000/S tanking which then extends over the toe and up the pre primed vertical RC wall to the required height as per the design drawings. Overlaps have been installed to the correct measurement and all tanking thoroughly rolled and adhered well to the walls. Site were carrying out their own ongoing inspections and where areas of air were trapped under the tanking, a slit was made in these small areas and a layer of Bituthene LM was applied prior to an addition piece of Bituthene 8000/S. The tanking installation was approx 20% completed when the inspection took place and all works were being carried out to a good standard.	

Type of Joint	Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐	
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)		
Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?		☒ Yes	☐ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?		☐ Yes	☐ No	☒ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?		☐ Yes	☐ No	☒ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?		☐ Yes	☐ No	☒ N/A
	Has all other detailing work passed inspection		☐ Yes	☐ No	☒ N/A
	(List any defects to detailing work and joints): During our inspection the following defects and repairs were carried out: No recorded defects other than noted prior to our inspection in he description of installation. Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A The Area has passed inspection ☒ The Area has failed inspection and a corrective action sheet has been left with the contractor ☐ The Area is incomplete as detailed above ☐ Signed: **Dan Squire** Date: **24/02/2022**				

Area Inspected

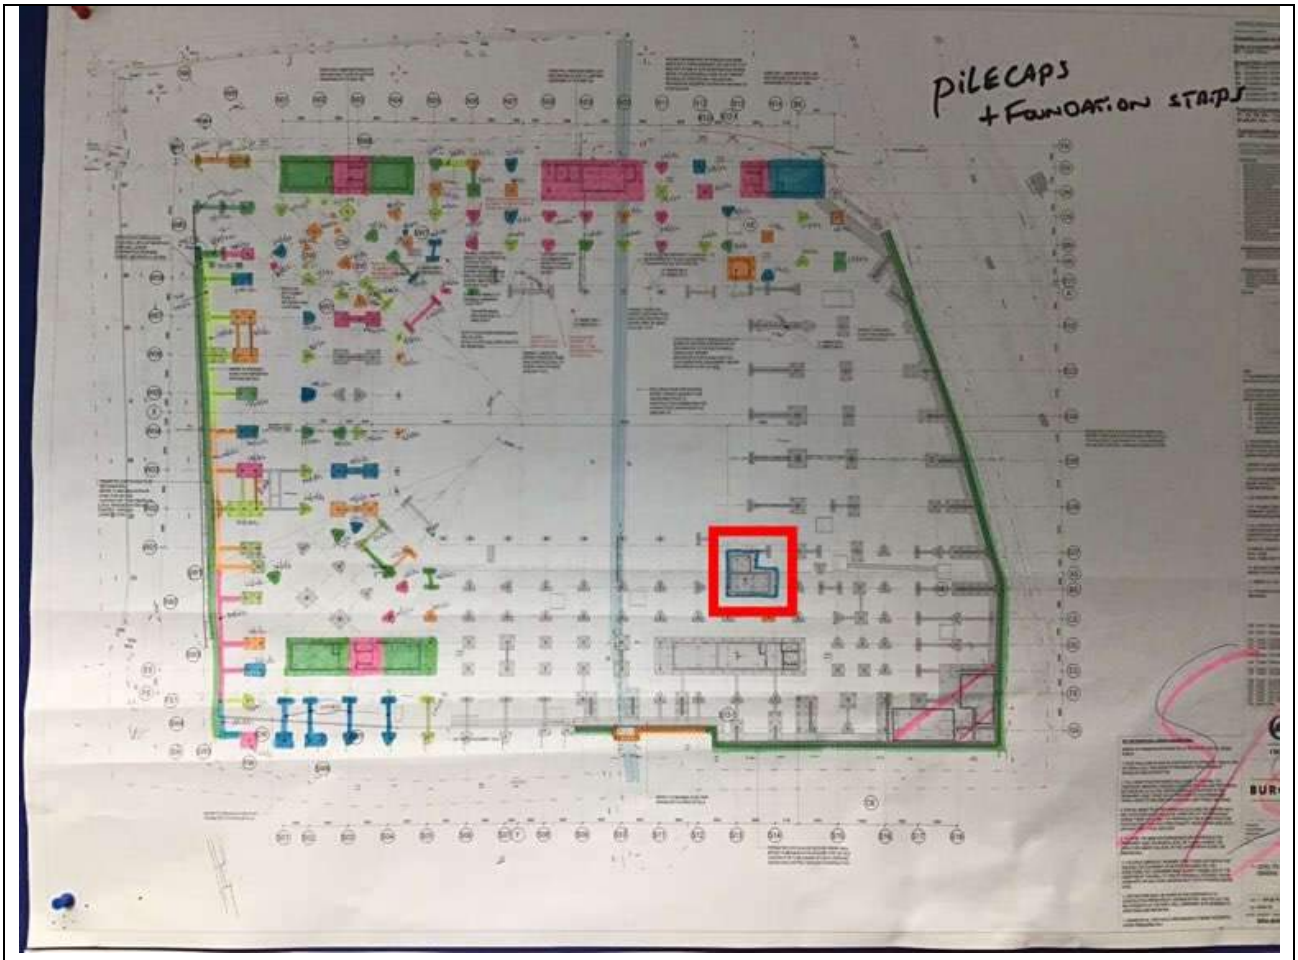

Photos **24/02/2022**



Bituthene LM installed to the top of the membrane to adhere to the tanking




Sealed repair to tanking



Core 5 tanking wrap installation



Core 5 tanking wrap installation

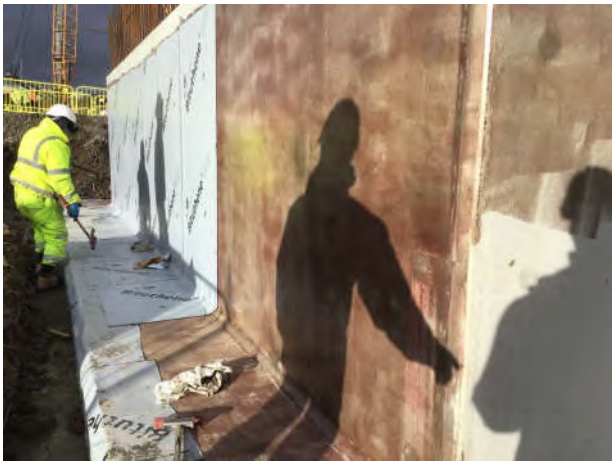

Pre primed RC walls

Test and Inspection Result 'PASS In FULL'

The areas has passed the inspection and a re-visit is not required.



Signed: Barrie Ackroyd Date: 24.2.2022

On Behalf of Membrane Testing Solutions Ltd


Co-Op Live, Manchester - C777
24.2.2022

Site name: BAM Construction. Co-Op Live. Manchester **Postcode: M11 3DU**	**Units/ plots checked: : Core 7 base Main floor installation Gridlines S11-S15 / SW3**
Installers Name: P J Carey's	
Date: 24/02/2022	
Inspection by: Dan Squire	**Weather: 2ºC Wet**

Item		
Sub-floor void	N/A	
Ventilation Inlets and Outlets	N/A	
Number Of Vents	N/A	
Materials used:	Membrane – Preprufe 300R Plus	
	Self-Adhesive Membrane ☒ Yes	Preformed Top hats ☐ Yes
	Double Sided Butyl Tape ☐ Yes	Preformed Corners ☐ Yes
	Others Please List: Bituthene LM. Bituthene Liquid membrane	
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** MTS Ltd carried out a thorough visual inspection of the membrane, the membrane had been installed to a good standard. Preprufe 300R plus membrane has been lined across the core base and is extended up the inside of the temporary shuttering which stays in place for 5 days after the pour to allow for the membrane to adhere to the concrete. The membrane has a permanent back binding which is used to join the membrane together and is pressure rolled. In some areas an additional strip of Preprufe Tape LT has been added on top of the joints. A mix of Bituthene LM & Bituthene liquid membrane is applied to seal all penetrations. Patch repairs have been made using Preprufe 300R plus membrane and strips of Preprufe LT tape. Site were carrying out their own ongoing inspections to check for any damages caused by the steelworks.	

Type of Joint	Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐		
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)			
Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?			☒ Yes	☐ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?			☒ Yes	☐ No	☐ N/A
	Has all other detailing work passed inspection			☐ Yes	☐ No	☒ N/A
	(List any defects to detailing work and joints): During our inspection the following defects and repairs were carried out: No recorded defects other than what had been previously repaired prior to the inspection as noted in the description of Installation. Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A The Area has passed inspection ☒ The Area has failed inspection and a corrective action sheet has been left with the contractor ☐ The Area is incomplete as detailed above ☐ Signed: **Dan Squire** Date: **24/02/2022**					

Area Inspected

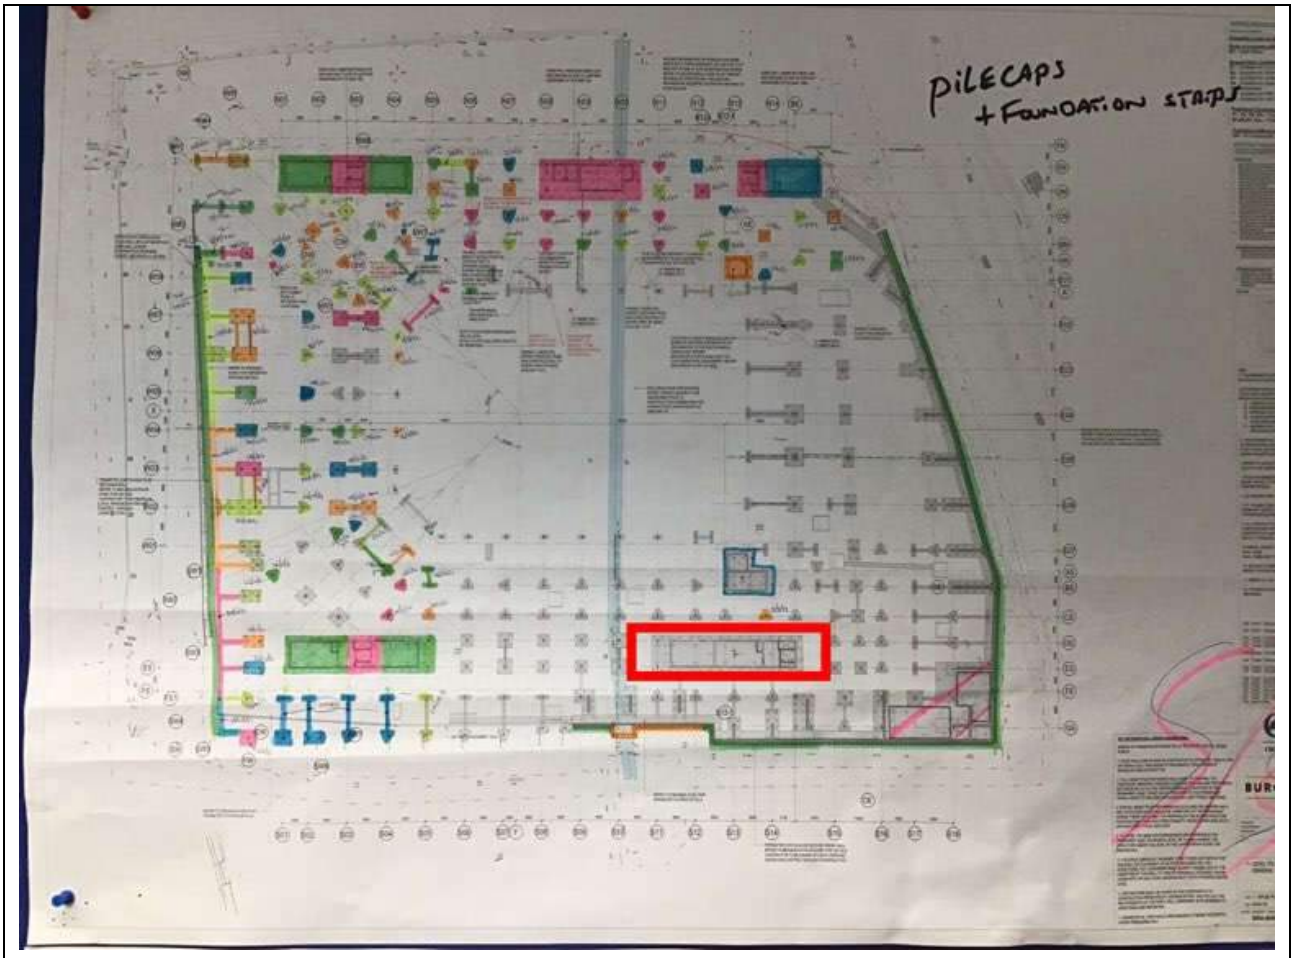

Photos **24/02/2022**



Probe test to membrane joint



Sealed pile cap using Bituthene LM



Core 7 base membrane installation




Core 7 base inspection



Sealed pile cap using Bituthene LM

Test and Inspection Result 'PASS In FULL'

The areas has passed the inspection and a re-visit is not required.



Signed: Barrie Ackroyd Date: 24.2.2022

On Behalf of Membrane Testing Solutions Ltd


Co-Op Live, Manchester - C777
24.2.2022

Site name: BAM Construction. Co-Op Live. Manchester **Postcode: M11 3DU**	**Units/ plots checked: : South west slab - Pour 9. Main floor installation - Gridlines S1-S3 / NW - N01**
Installers Name: P J Carey's	
Date: 24/02/2022	
Inspection by: Dan Squire	**Weather: 2ºC Wet**

Item		
Sub-floor void	N/A	
Ventilation Inlets and Outlets	N/A	
Number Of Vents	N/A	
Materials used:	Membrane – Preprufe 300R Plus	
	Self-Adhesive Membrane ☒ Yes	Preformed Top hats ☐ Yes
	Double Sided Butyl Tape ☐ Yes	Preformed Corners ☐ Yes
	Others Please List: Bituthene LM. Bituthene Liquid membrane	
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** MTS Ltd carried out a thorough visual inspection of the membrane, the membrane had been installed to a good standard. Preprufe 300R plus membrane has been lined across the pour slab areas as noted and is joined to the membrane previously installed up the liner wall to the capping beam. The membrane has a permanent back binding which is used to join the membrane together and is pressure rolled. In some areas an additional strip of Preprufe Tape LT has been added on top of the joints. A mix of Bituthene LM & Bituthene liquid membrane is applied to seal all penetrations. Patch repairs have been made to the membrane along the vertical face of the liner wall using Preprufe 300R plus membrane and strips of Preprufe LT tape. Site were carrying out their own ongoing inspections and cleaning off the membrane as the install progressed and prior to the pour.	

Type of Joint	Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐		
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)			
Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?			☒ Yes	☐ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?			☒ Yes	☐ No	☐ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Has all other detailing work passed inspection			☒ Yes	☐ No	☐ N/A
	(List any defects to detailing work and joints): During our inspection the following defects and repairs were carried out: No recorded defects other than what had been previously repaired prior to the inspection as noted in the description of Installation. Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A The Area has passed inspection ☒ The Area has failed inspection and a corrective action sheet has been left with the contractor ☐ The Area is incomplete as detailed above ☐ Signed: **Dan Squire** Date: **24/02/2022**					

Area Inspected

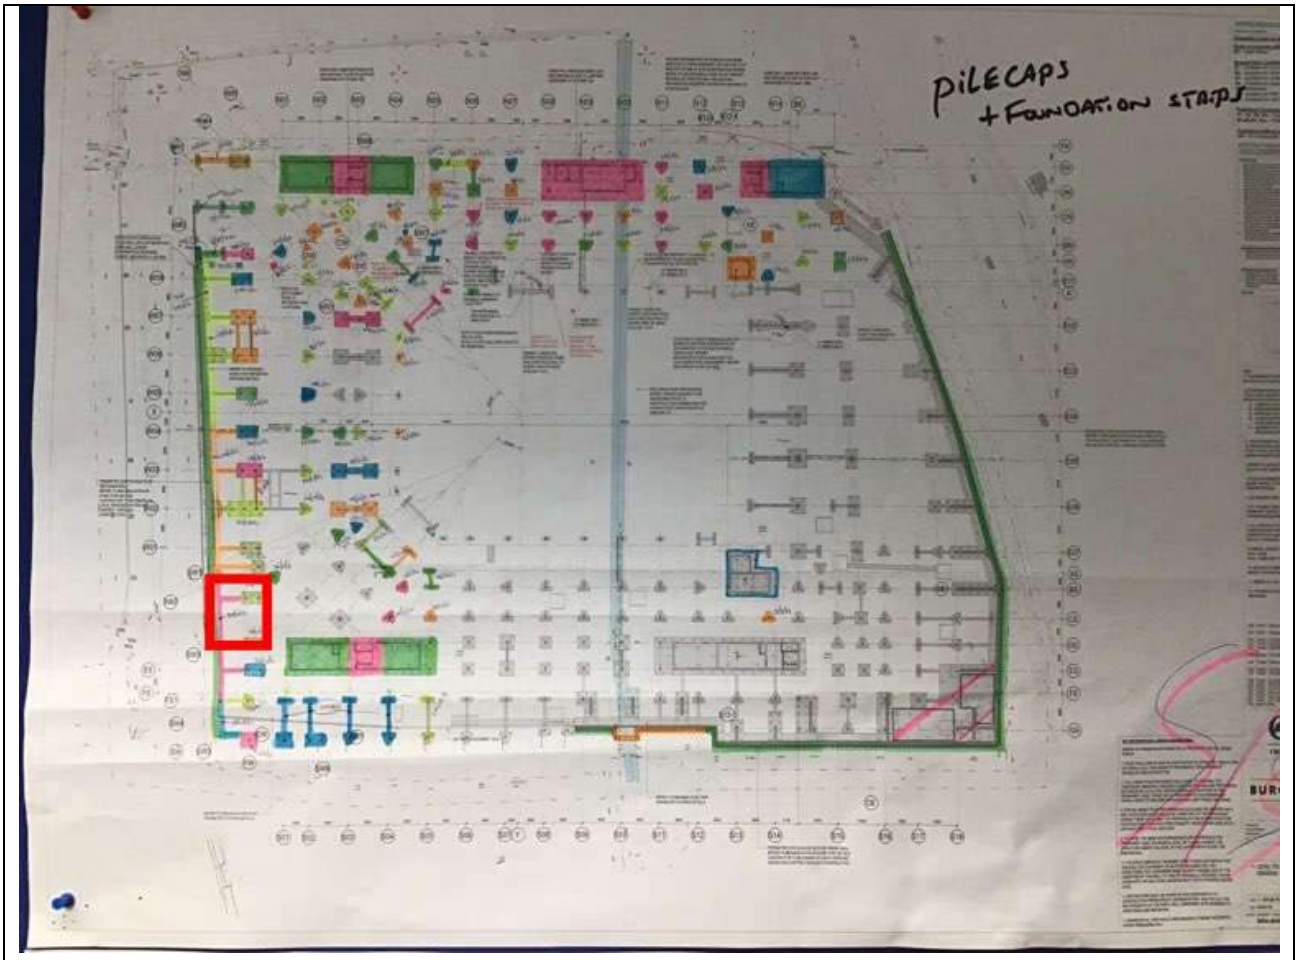

Photos **24/02/2022**



South west pour 9 line out installation



Sealed penetrations using Bituthene LM and liquid membrane mix



Sealed liner wall patch repair



Probe test inspection



Membrane sealed and joined to the liner wall



Sealed main floor patch repair



Sealed steel bars using Bituthene LM and liquid membrane mix

Test and Inspection Result 'PASS In FULL'

The areas has passed the inspection and a re-visit is not required.

Signed: Barrie Ackroyd Date: 24.2.2022

On Behalf of Membrane Testing Solutions Ltd

Co-Op Live, Manchester - C777
5.4.2022

Site name: BAM Construction, CoOp Live, Manchester. **Postcode: M11 3DU**	**Units/ plots checked: : Sprinkler room pool 2, gridlines S15.8/S17.5 - FS/GS. Buttress walls gridlines E06 - E07**
Installers Name: P J Carey	
Date: 05/04/2022	
Inspection by: Keith Barsby	**Weather: 11°C DRY**

Item	Comments	
Sub-floor void	N/A	
Ventilation Inlets and Outlets	N/A	
Number Of Vents	N/A	
Materials used:	Membrane – Preprufe 300R Plus	
	Self-Adhesive Membrane ☒ Yes	Preformed Top hats ☐ Yes
	Double Sided Butyl Tape ☐ Yes	Preformed Corners ☐ Yes
	Others Please List: Bituthene LM (Liquid Membrane)	
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** MTS carried out a thorough visual inspection of the membrane, the membrane had been installed to a good standard. Sprinkler Room: The membrane has been installed across the concrete base and turned up 90deg against the piles. The piles have been sealed to the membrane using Bituthene LM which has been applied to the pile cap and the membrane. The fixings through the membrane on the walls have been sealed using patches of Preprufe 300R Plus membrane with Preprufe LT tape.	

	Buttress walls: Preprufe 300R Plus has been installed vertically against the piles, it has been sealed at the top using Bituthene LM, which we were unable to inspect due to the height. The shuttering for the buttress walls will be installed against the Preprufe 300R Plus membrane. The fixings through the membrane have been sealed using patches of Preprufe 300R Plus membrane and Prep LT tape. The Sprinkler Room is highlighted in Red and the Buttress Walls are highlighted in Blue on the attached drawing.					
Type of Joint	Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐		
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)			
Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?			☒ Yes	☐ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?			☐ Yes	☒ No	☐ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?			☒ Yes	☐ No	☐ N/A
	Has all other detailing work passed inspection			☒ Yes	☐ No	☐ N/A
	(List any defects to detailing work and joints): During our inspection the following defects and repairs were carried out: None. Sprinkler Room: It was noted during our inspection that there has been some water ingress below the membrane in the lower floor area after it was installed, this was being pumped out during our inspection. Buttress walls: it was noted that there is to be a design change for the pipe penetrations and where the membrane joins at the base of the walls onto the concrete blinding. Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A The Area has passed inspection ☒					

	The Area has failed inspection and a corrective action sheet has been left with the contractor ☐ The Area is incomplete as detailed above ☐ Signed: **Keith Barsby** Date: **05/04/2022**

Area Inspected

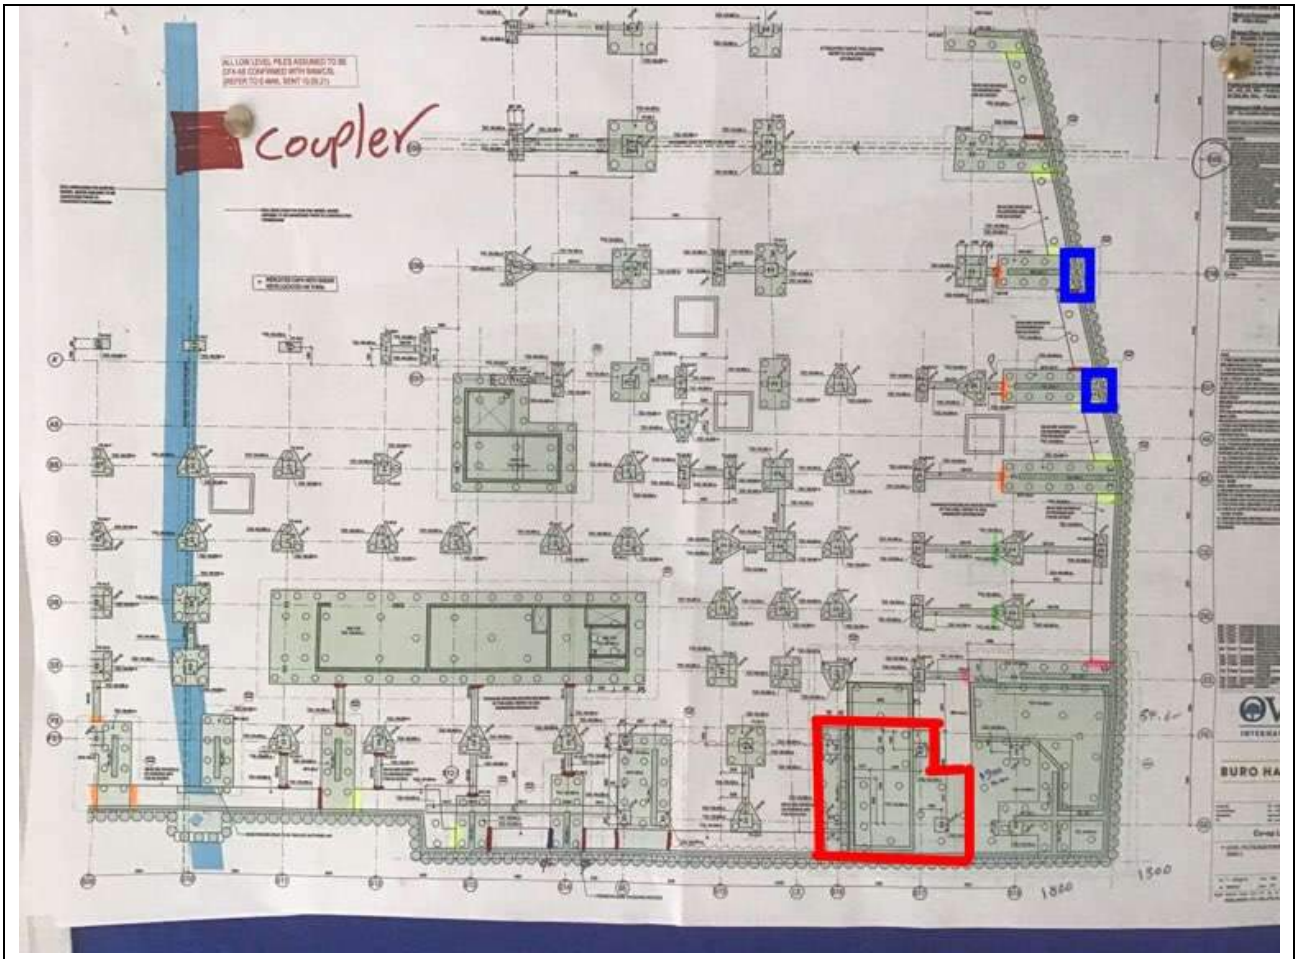


Photo **05/04/2022**



Overview of Sprinkler Room



Sprinkler Room pile cap seal



Sprinkler Room pile cap seal being pick tested



Sprinkler Room membrane joint being pick tested



Buttress walls vertical membrane being installed



Vertical membrane behind the steel cage for the buttress wall, Bituthene LM at the top edge of the membrane and movement joint



Patch using Preprufe 300R Plus and Preprufe LT tape

Test and Inspection Result 'PASS In FULL'

The areas has passed the inspection and a re-visit is not required.

Signed: Barrie Ackroyd Date: 5.4.2022

On Behalf of Membrane Testing Solutions Ltd

Co-Op Live, Manchester - C777
30.6.2022

Site name: BAM Construction, CoOp Live, Manchester. **Postcode: M11 3DU**	**Units/ plots checked: Sprinkler tank area gridlines S15.8/S17.5 south liner walls gridlines S13/S15 - Liner walls east gridlines E04/E06**
Installers Name: P J Carey	
Date: 30/06/2022	
Inspection by: Keith Barsby	**Weather: 22°C DRY**

Item	Comments	
Sub-floor void	N/A	
Ventilation Inlets and Outlets	N/A	
Number Of Vents	N/A	
Materials used:	Membrane – Preprufe 300R Plus	
	Self-Adhesive Membrane ☒ Yes	Preformed Top hats ☐ Yes
	Double Sided Butyl Tape ☐ Yes	Preformed Corners ☐ Yes
	Others Please List: Bituthene LM (Liquid Membrane)	
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** MTS carried out a thorough visual inspection of the membrane, the membrane had been installed to a good standard. Preprufe 300R Plus has been installed vertically against the piles, it has been sealed at the top using Bituthene LM, which we were unable to inspect due to the height. The reinforcement mesh for the walls will be installed against the Preprufe 300R Plus membrane. The fixings through the membrane have been sealed using patches of Preprufe 300R Plus membrane, PrepLT tape and Bituthene LM.	

Type of Joint	Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)	

Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?	☒ Yes	☐ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?	☐ Yes	☐ No	☒ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?	☐ Yes	☐ No	☒ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?	☒ Yes	☐ No	☐ N/A
	Has all other detailing work passed inspection	☒ Yes	☐ No	☐ N/A

(List any defects to detailing work and joints):

During our inspection the following defects and repairs were carried out: None.

Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A

The Area has passed inspection ☒

The Area has failed inspection and a corrective action sheet has been left with the contractor ☐

The Area is incomplete as detailed above ☐

Signed: **Keith Barsby** Date: **30/06/2022**

Area Inspected


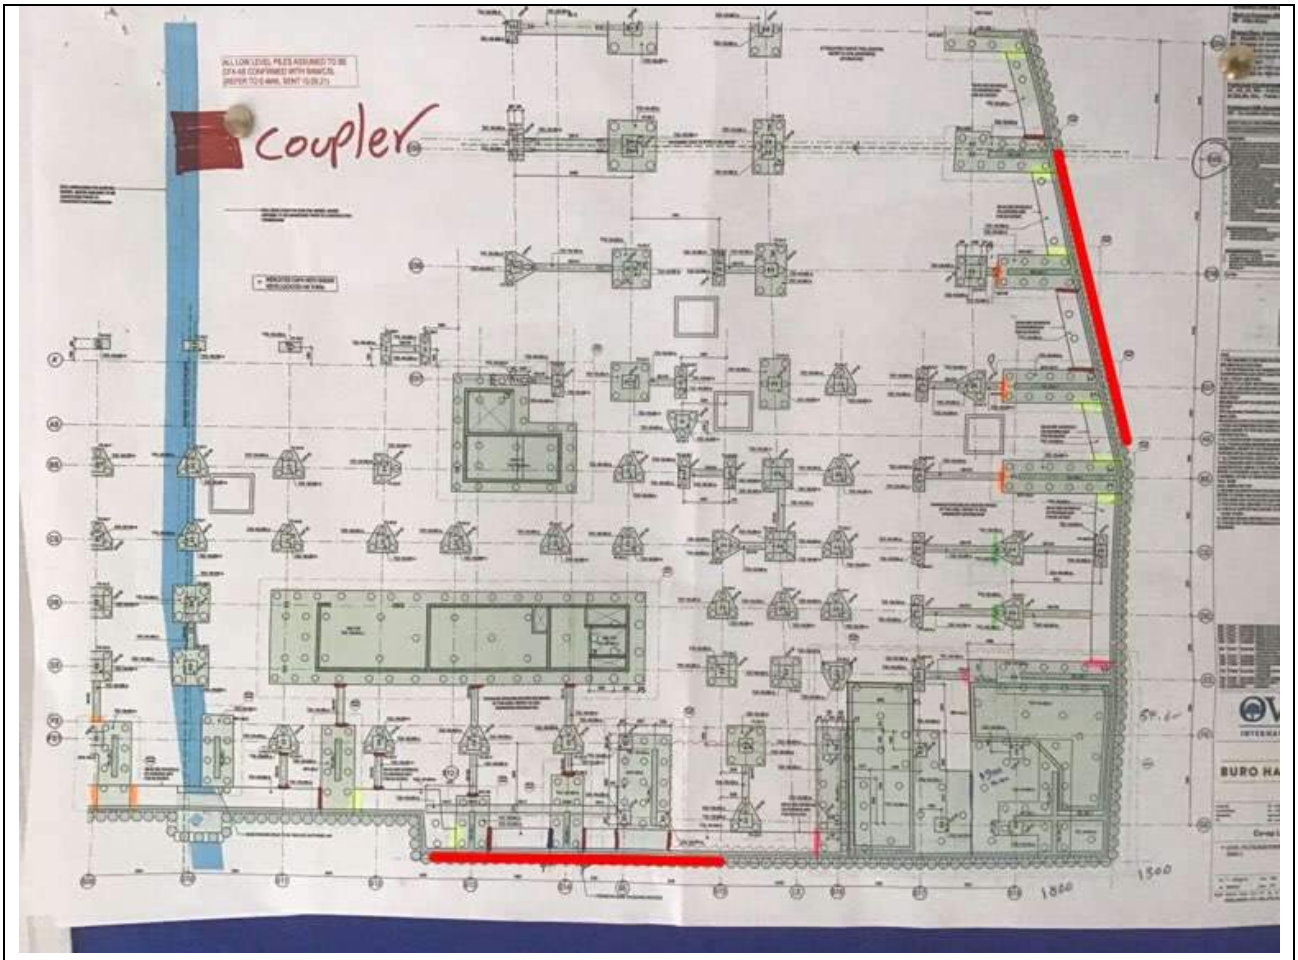


Photo **30/06/2022**



Tape joint being pick tested

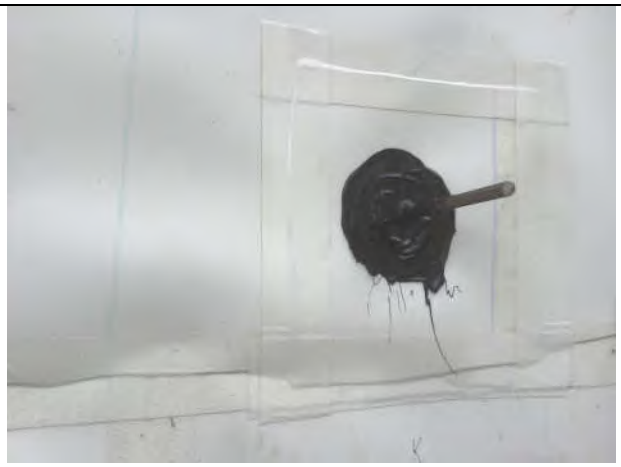

Penetration fixing sealed



Overview of wall



Overview of wall



Overview of site

Test and Inspection Result 'PASS In FULL'

The areas has passed the inspection and a re-visit is not required.



Signed: Barrie Ackroyd Date: 30.6.2022

On Behalf of Membrane Testing Solutions Ltd

Co-Op Live, Manchester - C777
23.8.2022

Site name: BAM Construction. Co-Op Live. Manchester **Postcode: M11 3DU**	**Units/ plots checked: : Core 1 Tanking to pre cast walls. Approx 12m. Gridlines N01-N04 / NW2-NW3**
Installers Name: PJ Careys	
Date: 23/08/2022	
Inspection by: Dan Squire	**Weather: 19°C Dry**

	Item		
Sub-floor void	N/A		
Ventilation Inlets and Outlets	N/A		
Number Of Vents	N/A		
Materials used:	Membrane – Preprufe 300R Plus		
	Self-Adhesive Membrane ☒ Yes	Preformed Top hats ☐ Yes	
	Double Sided Butyl Tape ☐ Yes	Preformed Corners ☐ Yes	
	Others Please List: Bituthene 8000 tanking		
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** MTS Ltd carried out a thorough visual inspection of the membrane, the membrane had been installed to a good standard. Preprufe 300R plus membrane has been previously lined across the core base and is extended up the toe and joins to the Bituthene 8000 tanking which has been adhered to the pre cast walls up to the correct height as per the design detail. Approx 12 meters of tanking has been installed at the time of the inspection to the west and south facing core walls. Site were carrying out their own ongoing inspections to check for any damages caused by the steelworks and follow-on trades. On the marked drawing the area in red is the full core area. The area in yellow is the completed tanking works.		

Type of Joint	Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐		
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)			
Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?			☒ Yes	☐ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Has all other detailing work passed inspection			☒ Yes	☐ No	☐ N/A
	(List any defects to detailing work and joints): During our inspection the following defects and repairs were carried out: No recorded defects. Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A The Area has passed inspection ☐ The Area has failed inspection and a corrective action sheet has been left with the contractor ☐ The Area is incomplete as detailed above ☒ Signed: **Dan Squire** Date: **23/08/2022**					

Area Inspected



Photo **23/08/2022**



Tanking pick testing



South side facing core tanking



South side facing core tanking



Bituthene joined to Preprufe membrane previously installed under the slab



West side facing core tanking

Test and Inspection Result 'PASS Work in Progress'

The area whilst incomplete has passed the inspection and a re-visit is not required.



Signed: Barrie Ackroyd Date: 23.8.2022

On Behalf of Membrane Testing Solutions Ltd

Co-Op Live, Manchester - C777
25.1.2023

Site name: BAM Construction. Co-Op Live. Manchester **Postcode: M11 3DU**	**Units/ plots checked: : South west slab east of core 6. See marked up plan in red**
Installers Name: PJ Carey's	
Date: 25/01/2023	
Inspection by: Dan Squire	**Weather: 7°C Light rain**

Item		
Sub-floor void	N/A	
Ventilation Inlets and Outlets	N/A	
Number Of Vents	N/A	
Materials used:	Membrane – Preprufe 300R Plus	
	Self-Adhesive Membrane ☐ Yes	Preformed Top hats ☐ Yes
	Double Sided Butyl Tape ☒ Yes	Preformed Corners ☐ Yes
	Others Please List: Preprufe Lap tape	
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** MTS Ltd carried out a thorough visual inspection of the membrane, the membrane had been installed to a good standard. Preprufe 300R membrane has been lined across footprint of the slab. Joining onto the membrane previously layed under the slab previously poured. The membrane has a permanent back binding which is used to join the membrane together and is pressure rolled. Additional Lap tap is then installed over the membrane joints.	

	At the time of our inspection the membrane works were ongoing and incomplete. The detailing areas including the pipe penetrations and stanchions were yet to be sealed using the Bituthene LM black sealant. All other works in this area were being installed to a good standard. During the inspection we were shown two other areas to the north and north east side of the building to talk through the membrane and build process. The north area needed to be cleaned and jet washed and the north east area had steel work placed over the membrane ready for the pour. These areas have not been inspected and are marked in yellow on the marked up plan. Site were carrying out there own ongoing inspections as the works progressed.					
Type of Joint	Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐		
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)			
Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?			☒ Yes	☐ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Has all other detailing work passed inspection			☐ Yes	☐ No	☒ N/A
	(List any defects to detailing work and joints): During our inspection the following defects and repairs were carried out: N/A Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A The Area has passed inspection ☐ The Area has failed inspection and a corrective action sheet has been left with the contractor ☐ The Area is incomplete as detailed above ☒ Signed: **Dan Squire** Date: **25/01/2023**					

Area Inspected

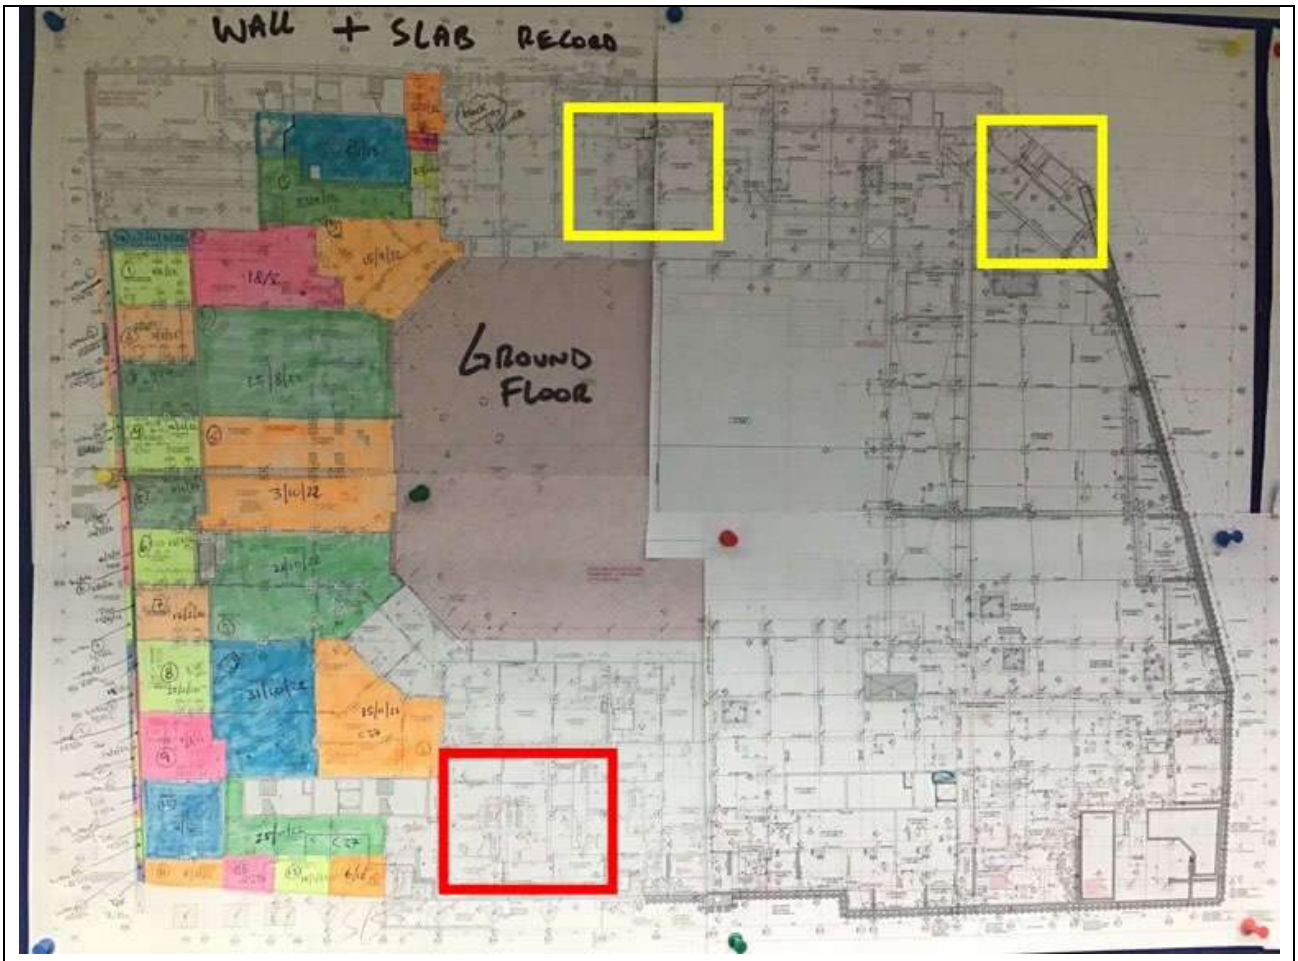


Photo **25/01/2023**



Pressure roller used to join the membrane



Membrane joining onto previously installed upper level



Stanchion detail yet to be sealed



South slab continued membrane full line out installation



Lined perimeter corner detailing



Pick testing to sealed lap joints



Sealed corner detailing



Sealed corner detail



Area unable for inspection ready for concrete



South slab continued membrane full line out installation

Test and Inspection Result 'PASS Work in Progress'

The area whilst incomplete has passed the inspection and a re-visit is not required.

Signed: Barrie Ackroyd Date: 25.1.2023

On Behalf of Membrane Testing Solutions Ltd

Co-Op Live, Manchester - C777
7.8.2023

Site name: BAM Construction. Co-Op Live. Manchester **Postcode: M11 3DU**	**Units/ plots checked:** **Bowl slab area to gridlines E01-E04 & N10-AE** **See plan mark-up in RED**
Installers Name: PJ Carey's	
Date: 07/08/2023	
Inspection by: Barrie Ackroyd	**Weather: 14°C Dry with Sunny Intervals**

Item		
Sub-floor void	N/A	
Ventilation Inlets and Outlets	N/A	
Number Of Vents	N/A	
Materials used:	Membrane – Preprufe 300R Plus	
	Self-Adhesive Membrane ☐ Yes	Preformed Top hats ☐ Yes
	Double Sided Butyl Tape ☒ Yes	Preformed Corners ☐ Yes
	Others Please List: Preprufe Lap tape	
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** Upon initial inspection we noted the majority of the Preprufe 300R Plus membrane had been covered with steel reinforcing bars meaning the majority of the membrane seams were unable to be inspected below the steel reinforcement. However, there was an area where the membrane installation was ongoing and being completed with lap tape over non-compliant membrane seams. The membrane seams in this area proved to be well sealed and fully bonded in the carried-out a thorough visual inspection of the membrane, the membrane had been installed to a good standard. We then checked down the raft slab edge which was incomplete and we noted some areas of the Waterbar was not bonded to the Preprufe 300R membrane, there were also holes drilled through the membrane which will require remedial works.	

	There were also steel stanchion depressions which are to be boxed out and repaired at a later date using the appropriate sealing detail. Our surveyor performed a detailed visual inspection of the membrane seams below the steel reinforcement and marked up two de-bonded areas with blue spray paint. There were also two additional seam debond areas adjacent to steel stanchion depressions which were also marked with blue spray paint. At the time of our inspection the membrane works were ongoing and incomplete. Site are performing their own ongoing inspections as the works progress, however MTS Ltd requested a copy of BAM's QA sign off documentation once the remedial works and BAM reinspection has been performed.					
Type of Joint	Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐		
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)			
Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?			☐ Yes	☒ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?			☐ Yes	☒ No	☐ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Has all other detailing work passed inspection			☐ Yes	☒ No	☐ N/A
	<u>(List any defects to detailing work and joints):</u> During our inspection the following defects and repairs were carried out: Repairs are to be performed to the marked-up areas. Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A The Area has passed inspection ☐ The Area has failed inspection and a corrective action sheet has been left with the contractor ☐ The Area is incomplete as detailed above ☒ Signed: **Barrie Ackroyd** Date: **07/08/2023**					

Area Inspected

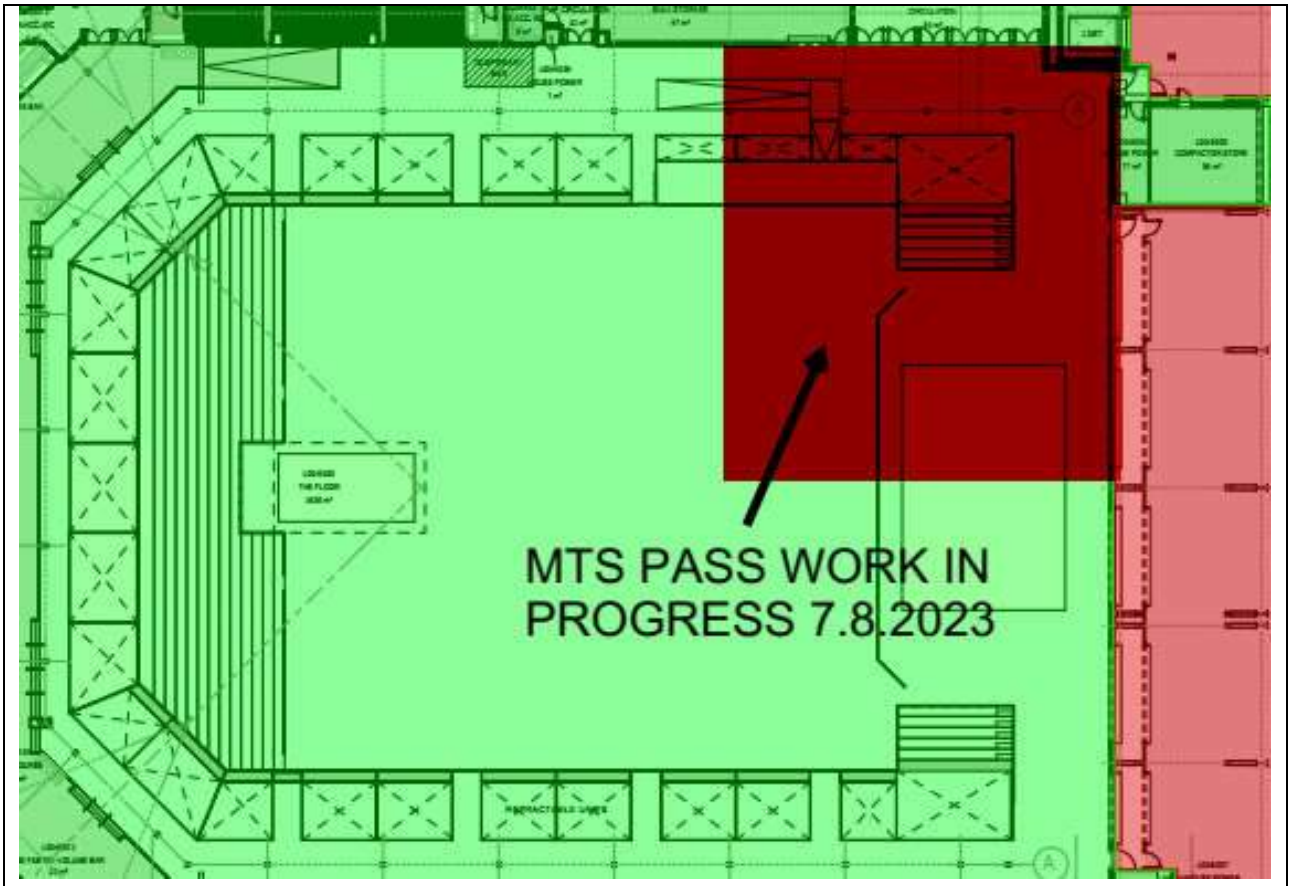


Photo **07/08/2023**




Pressure roller used to join the membrane



Ongoing membrane sealing detail



Seam pick testing performed to site seams

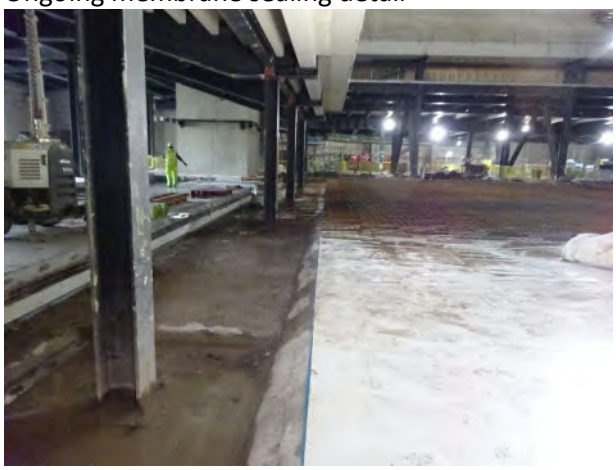

North elevation of raft slab edge with continued membrane full line out installation



Material overlap and seaming detailing (Note the blue line is visible which required overlap tape being applied above



Overlap tape applied to non-compliant seams (passed inspection)



North slab edge incomplete




Drill marks through membrane marked for repair




Defective join between Waterbar and gas membrane



Steel stanchion sealing incomplete

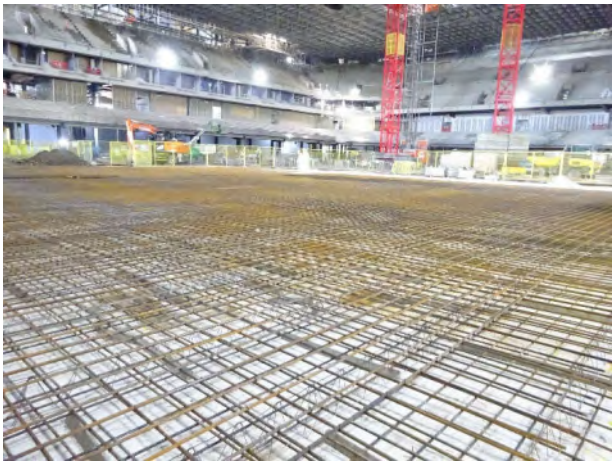

General overview of installed reinforcing bar above gas membrane

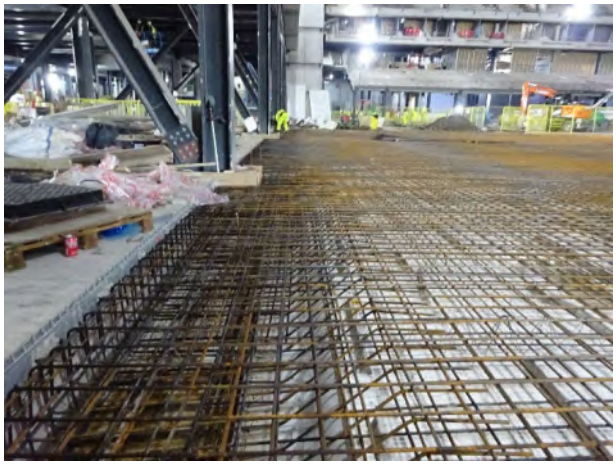

East slab edge membrane sealing detail



Seam pick testing of membrane seams, noting a seam debond defect



Lap tape debond defect marked and noted for repair




Vertical tape joint debond defect marked up and photographed



Vertical tape joint debond defect marked up and photographed



Seam bond defect marked for repair

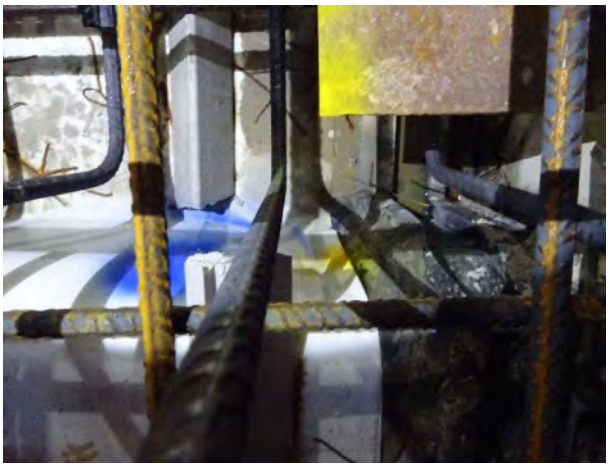

Seam lap tape bond defect marked for repair

Test and Inspection Result 'PASS Work in Progress'

The area whilst incomplete has passed the inspection and a re-visit is not required.

Bam have been requested to forward a copy of their QA sign off report as evidence of the defect repairs for inclusion within our final sign off validation report.



Signed: Barrie Ackroyd Date: 7.8.2023

On Behalf of Membrane Testing Solutions Ltd

Type of Joint	Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)	

Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?	☒ Yes	☐ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?	☒ Yes	☐ No	☐ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?	☐ Yes	☐ No	☒ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?	☐ Yes	☐ No	☒ N/A
	Has all other detailing work passed inspection	☒ Yes	☐ No	☐ N/A

(List any defects to detailing work and joints):

We are pleased to advise there were no defects to report whereby not requiring any remedial works. The works were ongoing and although practically complete the final works were being attended to. CGP were also in attendance who gave MTS a short introduction into the overall system componentry and specifications.

Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A

The Area has passed inspection ☒

The Area has failed inspection and a corrective action sheet has been left with the contractor ☐

The Area is incomplete as detailed above ☒

Signed: **Barrie Ackroyd** Date: **24/01/2022**

Area Inspected



Photo **24/01/2022**



Area installation overview



Lightning strap seal with Bituthene LM E



Typical formation preparation, with excellent laying surface



Service pipe cast into the blinding formation



Stainless steel starter bars sealed using bituthene LM E



Stainless steel starter bars sealed using bituthene LM E with Waterbar in place

Photo **24/01/2022**



Liner wall membrane installation overview



Waterbars welded together and above bitustik butyl tape ready for adhesion



Waterbars welded together and above bitustik butyl tape ready for adhesion



Bitustik butyl tape



Floor to wall junction with waterbars in place



Typical seam pick probe testing method

Test and Inspection Result 'PASS In FULL'

The areas has passed the inspection and a re-visit is not required.



Signed: Barrie Ackroyd Date: 24.1.2022

On Behalf of Membrane Testing Solutions Ltd

MembraneTestingSolutions

PHOTOGRAPHIC VALIDATION EVENT, INSPECTION CERTIFICATE OF INSTALLATION

DATE: 12.9.2023

PROJECT NAME: CO-OP LIVE, MANCHESTER

CONTRACT NO: C777 - Bowl Area to Gridlines: E01-E04 & N10-AE

PHOTOGRAPHIC INSPECTION & VALIDATION DETAILS:

MTS Ltd attended site under instruction on the 7.8.2023 to perform a detailed visual examination and seam pick testing to the above area. during our site visit there were a number of seam de-bond defects and punctures which were marked with blue paint. Unfortunately the repairs were unable to be performed at that time, therefore it was agreed MTS Ltd would accept photographic validation of the completed repairs. MTS Ltd received a completion and close out report from BAM on the 6.9.2023 which evinces the repairs have been performed using Cordeck LM material and upon a detailed visual examination we are pleased to advise all repairs have been completed and on this basis we are also pleased to close out the original pass work in progress certificate issued on the 7.8.2023. On this basis we are pleased to advise a pass in full has been acheived. A copy of the BAM close out report is appended to this certificate as evidence towards this close out photographic validation certificate.

MembraneTestingSolutions Ltd hereby confirm that the elements of the project detailed above have been photographically inspected, reviewed and validated by a suitably qualified independent consultant in accordance with industry requirements, with the test result noted below:

CONCLUSION (PASS/~~FAIL~~) PASS IN FULL

Where the conclusion above indicates a Pass, the construction activities may proceed subject to suitable protection measures of the membrane being applied in accordance with the manufacturer's recommendations.

Signed for on behalf of MembraneTestingSolutions Ltd:

Name: BARRIE ACKROYD

Dated: 12.9.2023

Membrane Testing Solutions Limited • The Studio, Parsonage House, Parsonage Street, Halstead, Essex CO9 2JR

Telephone: 0844 557 3786 • email: sales@mtsltd.net • www.mtsltd.net

Registered Office: 1, Second Avenue, Halstead, Essex. CO9 2SU • Company Registration Number: 8871015

Issue detail

#6631: Event Floor 1 - WP still not bonded in some areas

Standard fields

Status	**Closed**
Type	Quality > Quality
Description	Please see Daniel Allen this morning to close out the waterproofing issues. All holes bar one on the north side have been sealed. Some of the severseal has been sealed and blocked off but there are still some gaps on the north side, there is still one you can get you hand inside. Both column bases on east also need some repairs to vertical pieces Two snags from independents survey on pre-proof joints Need LM and blocks this morning
Assigned to	**Careys Civil Engineering**
Created by	**Daniel Allen** (BAM Construct UK)
Created on	Aug 15, 2023
Issue owner	**Daniel Allen** (BAM Construct UK)
Location	Arena
Location details	See map in blue, and yellow spray marks on site on top mat
Due date	Aug 15, 2023
Root cause	BAM Standard > Workmanship
Checklist source	3556 - 927 -CONCRETE PRE POUR INSPECTION RECORD - (CAREYS) BOWL FIRST POUR NE

Custom fields

Cost Impact	—

Severity —


Images



IMG_20230814_133818.jpg
Added on Aug 15, 2023, 6:59 AM BST
Added by Daniel Allen



IMG_20230814_135034.jpg
Added on Aug 15, 2023, 6:59 AM BST
Added by Daniel Allen

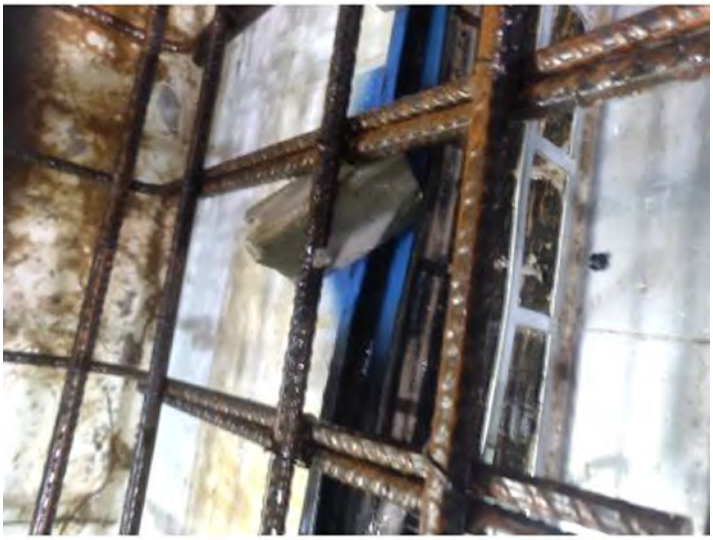

IMG_20230814_133920.jpg
Added on Aug 15, 2023, 6:59 AM BST
Added by Daniel Allen




IMG_20230814_133753.jpg
Added on Aug 15, 2023, 6:59 AM BST
Added by Daniel Allen



IMG_20230814_134847.jpg
Added on Aug 15, 2023, 6:59 AM BST
Added by Daniel Allen



IMG_20230814_135131.jpg
Added on Aug 15, 2023, 6:59 AM BST
Added by Daniel Allen

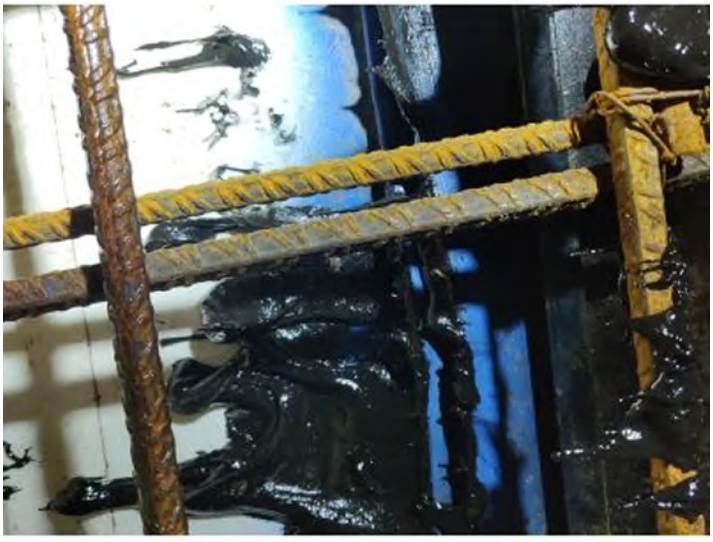

IMG_20230815_073859.jpg
Added on Sep 6, 2023, 7:56 AM BST
Added by Daniel Allen



IMG_20230815_073910.jpg
Added on Sep 6, 2023, 7:57 AM BST
Added by Daniel Allen



IMG_20230815_072715.jpg
Added on Sep 6, 2023, 7:56 AM BST
Added by Daniel Allen



IMG_20230815_073833.jpg
Added on Sep 6, 2023, 7:56 AM BST
Added by Daniel Allen



IMG_20230815_080706.jpg
Added on Sep 6, 2023, 7:56 AM BST
Added by Daniel Allen



IMG_20230815_073811.jpg
Added on Sep 6, 2023, 7:57 AM BST
Added by Daniel Allen



IMG_20230815_073838.jpg
Added on Sep 6, 2023, 7:56 AM BST
Added by Daniel Allen



IMG_20230815_080654.jpg
Added on Sep 6, 2023, 7:57 AM BST
Added by Daniel Allen



IMG_20230815_072628.jpg
Added on Sep 6, 2023, 7:56 AM BST
Added by Daniel Allen



IMG_20230815_080617.jpg
Added on Sep 6, 2023, 7:57 AM BST
Added by Daniel Allen



IMG_20230815_080651.jpg
Added on Sep 6, 2023, 7:57 AM BST
Added by Daniel Allen



IMG_20230815_073819.jpg
Added on Sep 6, 2023, 7:57 AM BST
Added by Daniel Allen



IMG_20230815_080611.jpg
Added on Sep 6, 2023, 7:57 AM BST
Added by Daniel Allen

Co-Op Live, Manchester - C777
7.8.2023

Site name: BAM Construction. Co-Op Live. Manchester **Postcode: M11 3DU**	**Units/ plots checked:** **Bowl slab area to gridlines E01-E04 & N10-AE** **See plan mark-up in RED**
Installers Name: PJ Carey's	
Date: 07/08/2023	
Inspection by: Barrie Ackroyd	**Weather: 14°C Dry with Sunny Intervals**

	Item		
Sub-floor void	N/A		
Ventilation Inlets and Outlets	N/A		
Number Of Vents	N/A		
Materials used:	Membrane – Preprufe 300R Plus		
	Self-Adhesive Membrane ☐ Yes	Preformed Top hats ☐ Yes	
	Double Sided Butyl Tape ☒ Yes	Preformed Corners ☐ Yes	
	Others Please List: Preprufe Lap tape		
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** Upon initial inspection we noted the majority of the Preprufe 300R Plus membrane had been covered with steel reinforcing bars meaning the majority of the membrane seams were unable to be inspected below the steel reinforcement. However, there was an area where the membrane installation was ongoing and being completed with lap tape over non-compliant membrane seams. The membrane seams in this area proved to be well sealed and fully bonded in the carried-out a thorough visual inspection of the membrane, the membrane had been installed to a good standard. We then checked down the raft slab edge which was incomplete and we noted some areas of the Waterbar was not bonded to the Preprufe 300R membrane, there were also holes drilled through the membrane which will require remedial works.		

	There were also steel stanchion depressions which are to be boxed out and repaired at a later date using the appropriate sealing detail. Our surveyor performed a detailed visual inspection of the membrane seams below the steel reinforcement and marked up two de-bonded areas with blue spray paint. There were also two additional seam debond areas adjacent to steel stanchion depressions which were also marked with blue spray paint. At the time of our inspection the membrane works were ongoing and incomplete. Site are performing their own ongoing inspections as the works progress, however MTS Ltd requested a copy of BAM's QA sign off documentation once the remedial works and BAM reinspection has been performed.					
Type of Joint	Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐		
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)			
Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?			☐ Yes	☒ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?			☐ Yes	☒ No	☐ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Has all other detailing work passed inspection			☐ Yes	☒ No	☐ N/A
	<u>(List any defects to detailing work and joints):</u> During our inspection the following defects and repairs were carried out: Repairs are to be performed to the marked-up areas. Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A The Area has passed inspection ☐ The Area has failed inspection and a corrective action sheet has been left with the contractor ☐ The Area is incomplete as detailed above ☒ Signed: **Barrie Ackroyd** Date: **07/08/2023**					

Area Inspected

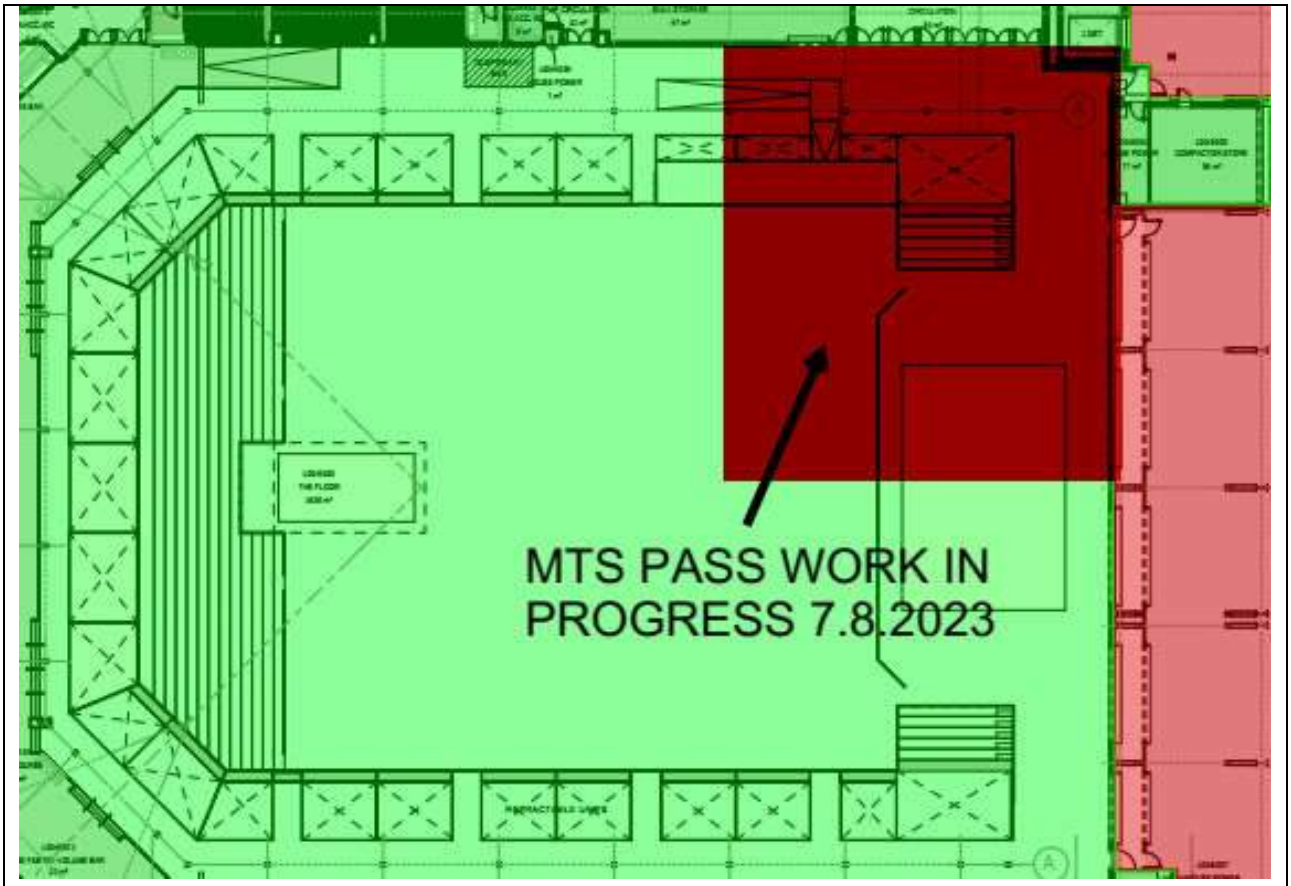


Photo **07/08/2023**




Pressure roller used to join the membrane



Ongoing membrane sealing detail



Seam pick testing performed to site seams

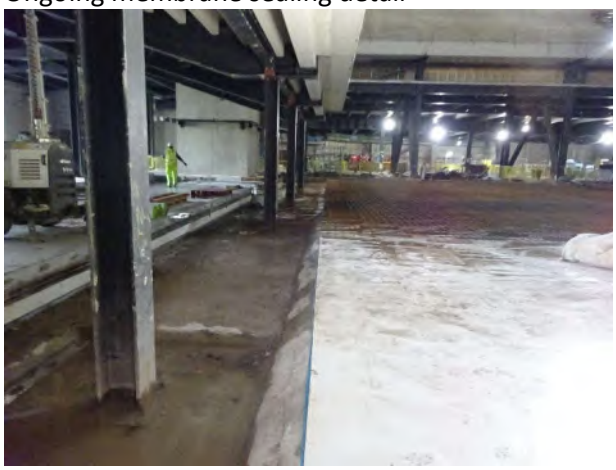

North elevation of raft slab edge with continued membrane full line out installation



Material overlap and seaming detailing (Note the blue line is visible which required overlap tape being applied above



Overlap tape applied to non-compliant seams (passed inspection)







North slab edge incomplete




Drill marks through membrane marked for repair




Defective join between Waterbar and gas membrane



Steel stanchion sealing incomplete

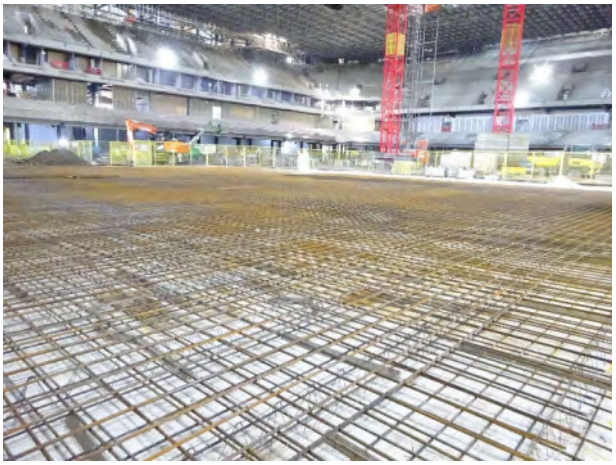

General overview of installed reinforcing bar above gas membrane

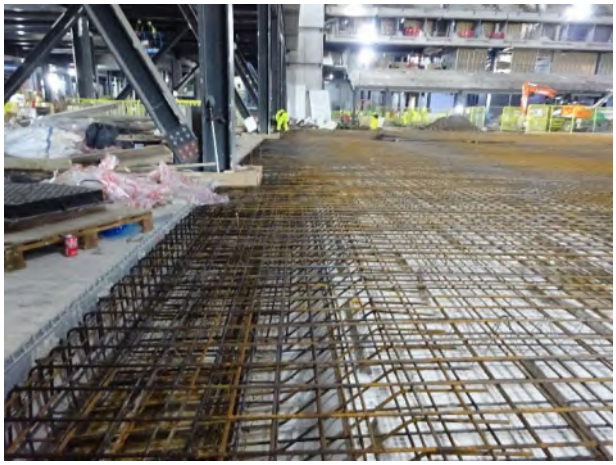

East slab edge membrane sealing detail



Seam pick testing of membrane seams, noting a seam debond defect



Lap tape debond defect marked and noted for repair



Vertical tape joint debond defect marked up and photographed



Vertical tape joint debond defect marked up and photographed



Seam bond defect marked for repair



Seam lap tape bond defect marked for repair

Test and Inspection Result 'PASS Work in Progress' REJECTED 12.9.2023

The area whilst incomplete has passed the inspection and a re-visit is not required.

Bam have been requested to forward a copy of their QA sign off report as evidence of the defect repairs for inclusion within our final sign off validation report.

Signed: Barrie Ackroyd Date: 7.8.2023

On Behalf of Membrane Testing Solutions Ltd

Co-Op Live, Manchester - C777

29.09.2023

Site name: BAM Construction. Co-Op Live. Manchester **Postcode:** M11 3DU	**Units/ plots checked:** Perimeter tanking and waterproofing detail. See marked up plan
Installers Name: P J Carey's & Waterseal	
Date: 29/09/2023	
Inspection by: Dan Squire	**Weather:** 12°C Dry

Item	Comments
Sub-floor void	N/A
Ventilation Inlets and Outlets	N/A
Number Of Vents	N/A
Materials used:	Membrane – Preprufe 300R Plus Self-Adhesive Membrane ☒ Yes — Preformed Top hats ☐ Yes Double Sided Butyl Tape ☐ Yes — Preformed Corners ☐ Yes Others Please List: Bituthene 8000. S2 Primer Bituthene. Grace Integritank waterproofing spray system
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** MTS Ltd carried out a thorough visual inspection of the waterproofing and membrane works. the works had been installed to a good standard. Bituthene 8000 has been installed by P J Carey's to the area marked in red. Sealed to the required height of the walls and joined to the Preprufe membrane previously installed under the concrete walls. An additional layer of S2 primer is installed to the walls prior to the Bituthene 8000 installation. Bituthene LM black sealant is used between the joints of the 8000 tanking and existing Preprufe membrane. Holes were being drilled through the 8000 tanking to allow for dowels to be installed. These dowels will be sealed using Bituthene LM black sealant at a later date and re inspected. On the concrete panels marked in green on the plan waterseal have installed Integritank waterproofing spray. At a later date the main concrete slab will be coated in the spray and tie in with the panels already sprayed.

Type of Joint	Tape Joint ☐	Auto Weld ☒	Hand Weld ☒	Extrusion Weld ☐		
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)			
Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?			☒ Yes	☐ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Has all other detailing work passed inspection			☒ Yes	☐ No	☐ N/A
	(List any defects to detailing work and joints): During our inspection the following defects and repairs were carried out: N/A Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A The Area has passed inspection ☒ The Area has failed inspection and a corrective action sheet has been left with the contractor ☐ The Area is incomplete as detailed above ☐ Signed: **Dan Squire** Date: **29/09/2023**					

Area Inspected



Photo 29/09/2023



Concrete panels with waterproofing spray applied



Concrete panels with waterproofing spray applied



Concrete panels with waterproofing spray applied



Bituthene 8000 installed to perimeter walls



Probe test to sealed Bituthene 8000



Bituthene 8000 sealed to Preprufe membrane using Bituthene LM Black sealant



Dowel holes cut out



Bituthene 8000 installed to perimeter walls

Membrane Testing Solutions Limited • The Studio, Parsonage House, Parsonage Street, Halstead, Essex CO9 2JR

Telephone: 0844 557 3786 • email: sales@mtsltd.net • www.mtsltd.net

Registered Office: 1, Second Avenue, Halstead, Essex. CO9 2SU • Company Registration Number: 8871015


CO-OP LIVE - C777
18.10.2023

Site name: BAM Construction, Co-OP Live, Manchester **Postcode: M11 3DU**	**Units/ plots checked: East Perimeter Tanking and Waterproof Detail. See mark-up plan**
Installers Name: Waterseal	
Date: 18/10/2023	
Inspection by: Dan Squire	**Weather: 13°C Dry**

Item	Comments	
Sub-floor void	N/A	
Ventilation Inlets and Outlets	N/A	
Number Of Vents	N/A	
Materials used:	Membrane – Bituthene 8000	
	Self-Adhesive Membrane ☒ Yes	Preformed Top hats ☐ Yes
	Double Sided Butyl Tape ☐ Yes	Preformed Corners ☐ Yes
	Others Please List: Grace Integritank Waterproofing Spray	
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** MTS Ltd carried out a thorough visual inspection of the waterproofing and membrane works. The works had been installed to a good standard. Waterseal have installed the movement joint to the east perimeter walls. Integritank waterproofing spray was then applied to the walls. Sealing the movement joint and overlapping with the Bituthene 8000 tanking to allow for dowels to be installed. These dowls are still to be sealed using bituthene LM Black sealant at a later date and re-inspected, and therefore is discounted from this cert. Some repairs were made to the Bituthene 8000 using additional layers of the Bituthene and jointing tape overlapping to reduce the risk of the Bituthene delaminating at the edges.	

Type of Joint	Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐		
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)			
Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?			☒ Yes	☐ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Has all other detailing work passed inspection			☒ Yes	☐ No	☐ N/A
	(List any defects to detailing work and joints): During our inspection the following defects and repairs were carried out: No recorded defects. Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A The Area has passed inspection ☐ The Area has failed inspection and a corrective action sheet has been left with the contractor ☐ The Area is incomplete as detailed above ☒ Signed: **Dan Squire** Date: 18**/10/2023**					

Area Inspected

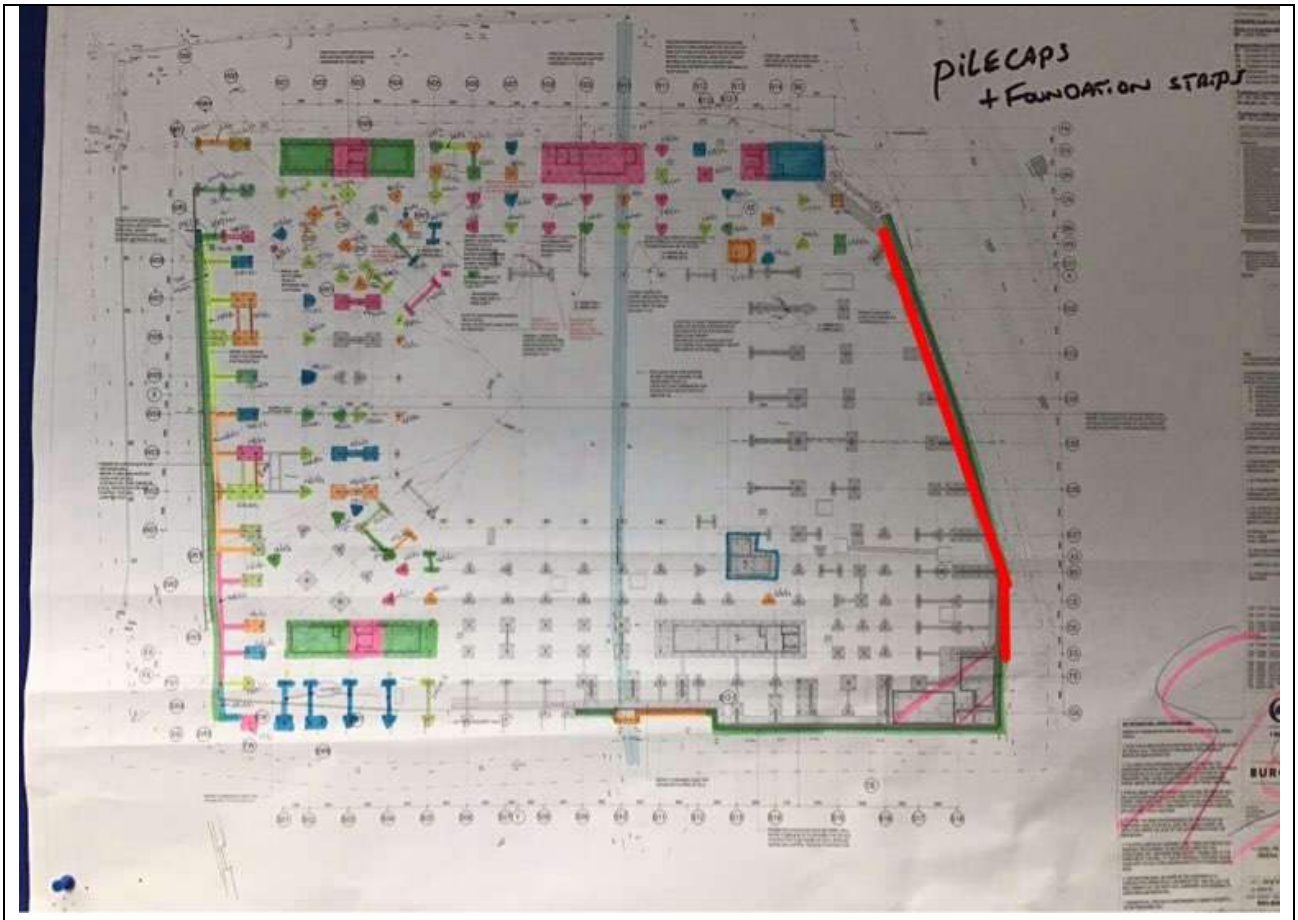



Sealed Bituthene repairs



Probe testing



East perimeter walls inspected



Areas protected prior to further installation



Movement joint installed



Integritank spray sealed movement joint and joined to Bituthene 8000



Integritank spray sealed movement joint and joined to Bituthene 8000



Dowels yet to be sealed

Test and Inspection Result 'PASS'

The area whilst incomplete has passed the inspection and a re-visit is not required.

Signed: Michael Smith Date: 18.10.2023

On Behalf of Membrane Testing Solutions Ltd

CO-Op Live, Manchester - C777
4.12.2023

Site name: BAM Construction. Co-Op Live. Manchester **Postcode: M11 3DU**	**Units/ plots checked: : South east and west Perimeter tanking and waterproofing detail. Main floor membrane installation See marked up plan**
Installers Name: Waterseal & PJ Carey's	
Date: 04/12/2023	
Inspection by: Dan Squire	**Weather: 5ºC Wet**

Item	Comments
Sub-floor void	N/A
Ventilation Inlets and Outlets	N/A
Number Of Vents	N/A
Materials used:	Membrane – Preprufe 300R Plus with Preprufe lap tape
	Self-Adhesive Membrane ☒ Yes / Preformed Top hats ☐ Yes
	Double Sided Butyl Tape ☐ Yes / Preformed Corners ☐ Yes
	Others Please List: Bituthene 8000. S2 Primer Bituthene. Grace Integritank waterproofing spray system
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** MTS Ltd carried out a thorough visual inspection of the waterproofing and membrane works. The works had been installed to a good standard. Waterseal have installed the movement joint to the south east perimeter walls and south west upper slab. Integritank waterproofing spray is installed onto the pre primed slab and walls. Sealing the movement joint and overlapping with the Bituthene 8000 which had previously been installed by P J Carey's.

(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)

MTS Ltd carried out a thorough visual inspection of the waterproofing and membrane works. The works had been installed to a good standard.

Waterseal have installed the movement joint to the south east perimeter walls and south west upper slab. Integritank waterproofing spray is installed onto the pre primed slab and walls. Sealing the movement joint and overlapping with the Bituthene 8000 which had previously been installed by P J Carey's. The Integritank spray is sealed to the required height of the walls. Some repairs have been made to the Bituthene 8000 using additional layers of the Bituthene and joining tape overlapping the joints to reduce the risk of the Bituthene peeling away at the edges.

Preprufe 300R membrane has been lined across footprint of main arena floor by PJ Carey's. Joining onto the membrane previously laid under the slab previously poured. The membrane has a permanent back binding which is used to join the membrane together and is pressure rolled. Additional Lap tap is then installed over the membrane joints.

At the time of our inspection the membrane works were ongoing and incomplete. The stanchions were yet to be sealed using the Bituthene LM black sealant and the movement joint needed additional LM Black to re seal as this was installed last year. All other works in this area were being installed to a good standard. A large section for the main floor membrane has re bar installed ready for the concrete meaning a restricted inspection in this area which seemed well cleaned off and free from any damages that we could see.

Marked up drawing key :

Area in red - waterproofing spray system works
Area in yellow - Preprufe membrane installed and inspected
Area in blue - Preprufe membrane restricted inspection.

Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐
☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)	

Have all joints passed testing prior to surveyor leaving site?	☒ Yes	☐ No	☐ N/A
Have all pipes passed testing prior to surveyor leaving site?	☐ Yes	☐ No	☒ N/A
Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?	☐ Yes	☒ No	☐ N/A
Have all piles and pile caps passed testing prior to surveyor leaving site?	☐ Yes	☐ No	☒ N/A
Has all other detailing work passed inspection	☒ Yes	☐ No	☐ N/A

	(List any defects to detailing work and joints): During our inspection the following defects and repairs were carried out: No recorded defects Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A The Area has passed inspection ☒ The Area has failed inspection and a corrective action sheet has been left with the contractor ☐ The Area is incomplete as detailed above ☐ Signed: **Dan Squire** Date: **04/12/2023**

Area Inspected

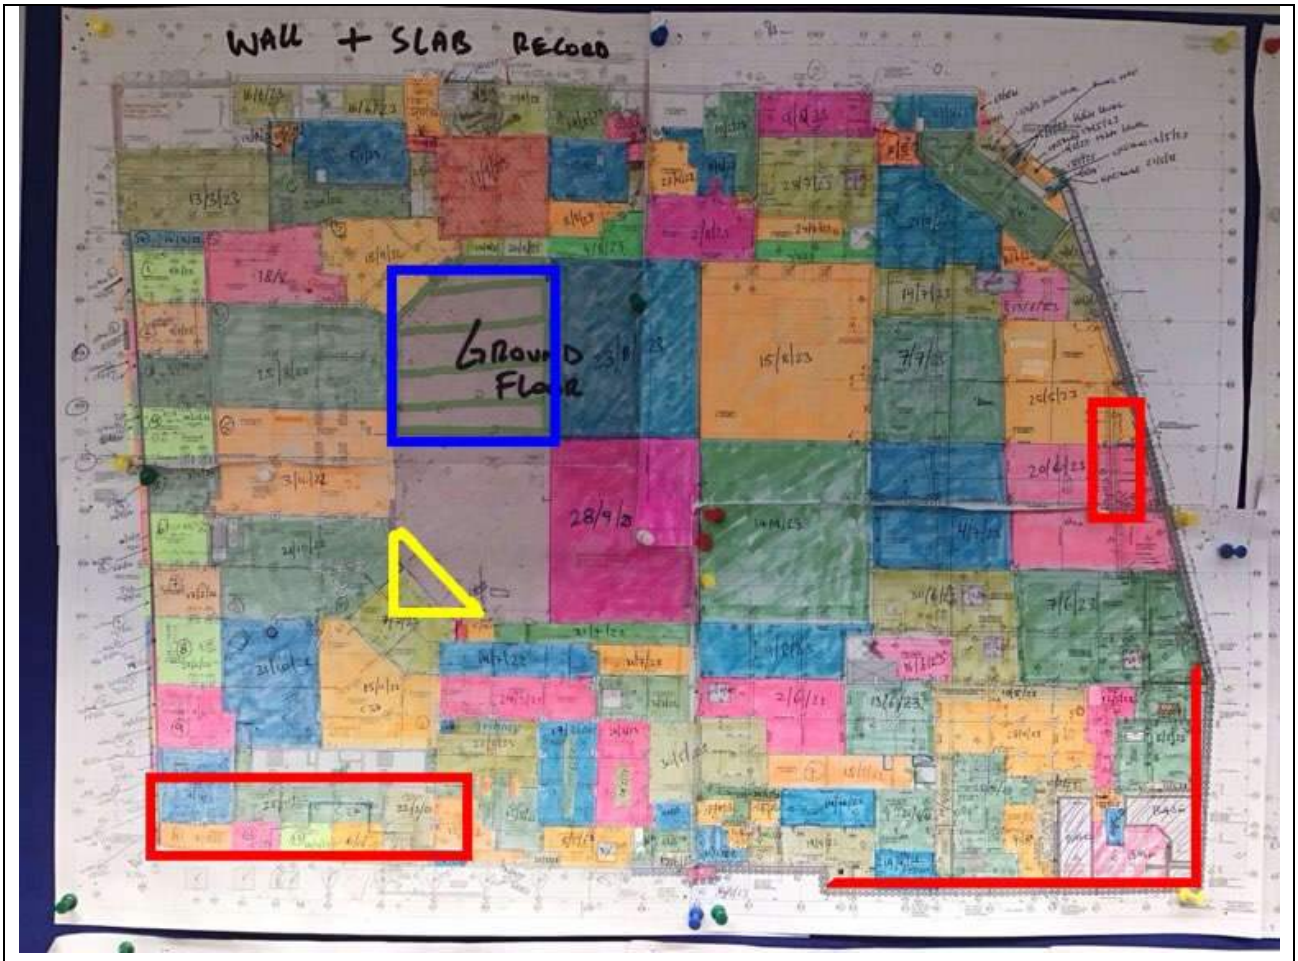


Photo **04/12/2023**



Upper slab waterproof spray system



Upper slab waterproof spray system



South east perimeter wall waterproofing system



Waterproof spray sealed to movement joint



Primer applied to perimeter walls prior to waterproofing spray




Sealed patch repairs to Bituthene tanking



South east waterproofing spray system



Pick test to sealed Preprufe membrane joint

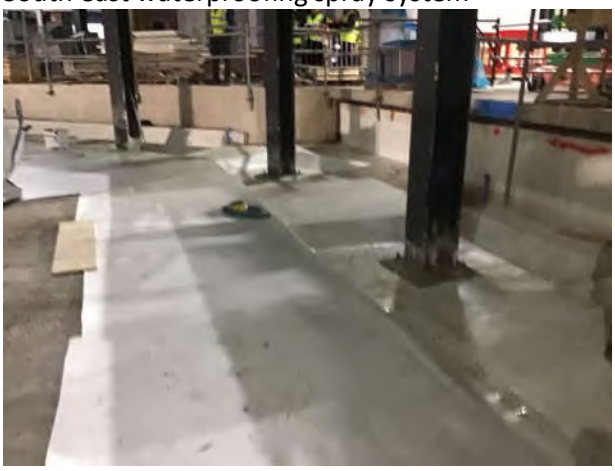

Preprufe membrane installation



Preprufe membrane installation



Stanchions yet to be sealed in the membrane section



Restricted inspection to Preprufe membrane

Test and Inspection Result 'PASS IN FULL'

The areas were incomplete but have passed the inspection performed and a re-visit is not required for these areas.



Signed: Barrie Ackroyd Date: 4.12.2023

On Behalf of Membrane Testing Solutions Ltd

Appendix J Membrane Testing Solutions Completion Report

Copyright © 1976 - 2024 Buro Happold. All rights reserved

MembraneTestingSolutions

GROUND GAS MITIGATION MEASURES, AND 3rd PARTY INDEPENDENT INSPECTION, TESTING & VALIDATION REPORT:

FOR MATERIALS INSTALLED AT:

CO-OP LIVE, ETHIAD CAMPUS, ALAN TURING WAY, MANCHESTER, M11 3DU

Document Reference No: MTS.VR.777-BA

Client: BAM Construct UK Ltd

Dated: December 2023

Membrane Testing Solutions Limited • The Studio, Parsonage House, Parsonage Street, Halstead, Essex CO9 2JR

Telephone: 0844 557 3786 • email: sales@mtsltd.net • www.mtsltd.net

Registered Office: 1, Second Avenue, Halstead, Essex. CO9 2SU • Company Registration Number: 8871015

Gas Protection Verification Declaration

Site

Site Name	CO-OP Live, Manchester
Site Address	CO-OP Live Arena, Etihad Campus, Alan Turing Way, Manchester, M11 3DU
GPVS Declaration Reference	1023-H4216

Gas Protection Verification

Brief Description of Site

This project includes the construction of a new arena complex which has a full basement on the footprint of the building. The gas/waterproofing mitigation measures were designed by GCP Ltd which were installed by PJ Carey's and Waterseal Ltd. The membranes were validated over 11no site visits and 1no photographic validation event. It was agreed MTS Ltd would only validate different areas of detailing and not 100% of the installation which was performed over 1 year 10 months. This declaration relates to the good workmanship which was regularly observed during our validation events.

Site Type	, CommercialRetail
Building Unit	The Whole Arena Complex

Document

Verification Report Title	Ground Gas Mitigation Measures, 3rd Party Independent Inspection, Testing & Validation Report
Verification Report Identifier	MTS .VR.777-BA dated 7th December 2023
Named Client	BAM Construct UK Ltd

Accredited Person Details

SGPV Name	Barrie Ackroyd
SGPV Registration No.	SGPV0002
Telephone	07884 210081
Email	sales@mtsltd.net
Organisation	Membrane Testing Solutions Ltd
Address	Parsonage House, Parsonage Street, Halstead, CO9 2JR

Declaration

I, Barrie Ackroyd, confirm that I am the person described in the Accredited Person details section and hold a current valid registration as a SGPV, Accreditation No. SGPV0002 under the Gas Protection Verification Accreditation Scheme.

I have reviewed the verification report described in the Document Details section and I am satisfied that:

1. The work has been carried out to an acceptable standard.
2. The work has been verified by suitably experienced and qualified personnel.
3. The level of verification is proportionate to the level of risk Identified in the site investigation report/Gas risk assessment.
4. The interpretations and conclusions are reasonable.
5. The verification strategy is in line with industry guidance.
6. I am competent to sign this Declaration and that
    a. I am fully aware and comply with the Scheme's Code of Conduct
    b. The work of this review and Declaration are within the limits of my knowledge, competence and professional capacity.

Note: The document that has been reviewed was prepared by the organisation named for the benefit of the named Client who has reliance upon it. Any professional liability arising from any proven negligent act or omission by the Company carrying out the work and publishing the document rests with that Company and not with the SGPV Accredited Person or the GPVS.

Signed:

Date: 7th DECEMBER 2023

Name: BARRIE ACKROYD
[Block capitals]

Gas Protection Verification

1023-H4216

Client Name: BAM Construct UK Ltd
Reference: MTS.VR.777-BA
Issue: **FINAL**
Date: 7th December 2023

Approval Status: **PASS IN FULL**

Prepared by: **Barrie Ackroyd**
Position: **Managing Director**



……

REVISIONS:

This 3rd party ground gas mitigation strategy and validation report has been prepared by MembraneTestingSolutions Ltd with all reasonable skill, care and diligence within the terms of the contract with the client, incorporation of our General Terms and Conditions of Business and considering the resources devoted to us by agreement with the client.

We disclaim any responsibility to the client and others in respect of any matters outside the scope of the above.

This 3rd party ground gas mitigation strategy and validation report is confidential to our client and we accept no responsibility of whatsoever nature to third parties to whom this report, or any part thereof, is made known. Any such party relies on this report at its own risk.

CONTENTS

EXECUTIVE SUMMARY

1. LIMITATIONS 4
2. BACKGROUND INFORMATION 5
3. GROUND GAS MONITORING 5
4. BS8485:2015+A1:2019 COMPLIANCE 6
5. DESIGN DRAWINGS 7
6. MATERIAL SPECIFICATIONS 7
7. GAS MEMBRANE INSTALLATION CONTRACTOR 7
8. INSPECTION, TESTING & VALIDATION REGIME 8
8.1 Inspection, Validation & Testing Method Statement 8
9. MTS SITE VISITS 9
10. SITE PHOTOGRAPHS 10
11. CONCLUSIONS & RECOMMENDATIONS 18
12. APPENDICES 18

Appendix A – Validation Surveyors Certificates of Competence
Mr Barrie Ackroyd (MTS Ltd)
Mr Michael Smith (MTS Ltd)
Mr Keith Barsby (MEC Ltd)
Mr Dan Squires (MEC Ltd)

Appendix B – Design Drawings

Buro Happold Drawings;

- BRA-BHE-ZC-ZZ-DR-S-3521 Level GF & GM Zone C Water Tank Sections
- BRA-BHE-XX-XX-DR-S-3501 Substructure Detail Sections Sheet 1
- BRA-BHE-XX-XX-DR-S-3504 Substructure Detail Sections Sheet 4
- BRA-BHE-ZA-GF-DR-S-1001-GF Slab Pours – 24.1.2022

GCP Applied Technologies Product Application Techniques Drawings;

- BRA-CCE-ZZ-ZZ-DR-Y-16101 Waterproofing Details
- BRA-CCE-ZZ-ZZ-DR-Y-16102 Waterproofing Details
- BRA-CCE-ZZ-ZZ-DR-Y-16104 Waterproofing Details
- BRA-CCE-ZZ-ZZ-DR-Y-16106 Waterproofing Details
- BRA-CCE-ZZ-ZZ-DR-Y-16126 Waterproofing Details
- BRA-CCE-ZZ-ZZ-DR-Y-16142 Waterproofing Details
- BRA-CCE-ZZ-ZZ-DR-Y-16144 – P02 Waterproofing Details
- BRA-CCE-ZZ-ZZ-DR-Y-16145 Waterproofing Details

Appendix C – Material Specifications

- Preprufe 300R Plus Membrane
- Preprufe Tape
- Bituthene LM Trowel Applied (Liquid) Membrane
- Bitustik BT 240 Double Sided Jointing Tape

Appendix D – Project Survey Sheets

MTS Ltd Gas Protection Inspection & Validation Record Certs

Appendix E – Copy of Validation Report and Photographs (Contained on USB Storage Device)

EXECUTIVE SUMMARY

1. LIMITATIONS

MembraneTestingSolutions Ltd (MTS Ltd) have prepared this 3rd party ground gas mitigation strategy and validation report in accordance with the instructions of BAM Construct UK Ltd (The Client) under the terms of the appointment for the 3rd party ground gas mitigation system installation inspection, testing, validation & reporting.

This 3rd party ground gas mitigation strategy and validation report is limited to the proposed ground gas protection measures installed to the new building meeting industry and current best practices. MTS Ltd have not provided any ground gas mitigation design proposals for this site, therefore professional Indemnity liability is limited to £2M for our validation works only and to ensure the specified ground gas mitigation measures meeting site specific contaminants.

This 3rd party ground gas mitigation strategy and validation report has been prepared in accordance with the information currently received, along with industry best practices and in conjunction with the relevant best practice and guidance documents listed below, of which our MD was a contributor and member of the steering committee for the Ciria C735 publication "Good practice on the testing and verification of protection systems for buildings against hazardous ground gases" (2014). MTS Ltd were also a contributor and part funder on the steering committee for the CIRIA 795 project, Retrospective Fitting of Gas Protective Measures to Existing Buildings (2020) and also the new Ciria C801 Hazardous ground gas – a site management guide, released Nov 2021.

We are pleased to advise that our Managing Director Mr Barrie Ackroyd has successfully completed the Validation & Integrity Testing Course provided by the British Geomembrane Association for validation, which is also backed by the CITB. Membrane Testing Solutions Ltd are a member of the British Geomembrane Association and are pleased to advise we are now registered with CQMS/SSIP, The Radon Council, The Property Care Association, CL:Aire and we are proud to be a founding member of the British Verification Council (BVC) of which Mr Ackroyd is a former Chairperson.

Mr Ackroyd has achieved the Level 3 Assessors Award and also the NVQ Level 4 qualification in Validation of Ground Gas Protection Systems, we are also pleased to advise he has successfully achieved CL:Aire accreditation as a Specialist in Gas Protection Verification (SGPV) and our Senior Validation Surveyor Mr Michael Anthony Smith has qualified in the NVQ Level 4 for Verification of Ground Gas Protection Systems (assessed by others) and has acheived CL:Aire TGPV accreditation.

Guidance Reference Documents:

Ground Gas Handbook "NHBC Guidance on evaluation of development proposals on sites where methane and carbon dioxide are present" (2007)
Ciria C665 "Assessing risks posed by hazardous ground gases to buildings" (2007
Ciria C716 "Remediating and mitigating risks from volatile organic compound (VOC) vapours from land affected by contamination" (2012)
Ciria C735 "Good practice on the testing and verification of protection systems for buildings against hazardous ground gases (2014)
Ciria C748 "Guidance on the use of plastic membranes as VOC vapour barriers" (2014)
BS 8485:2015+A1:2019 "Code of practice for the design of protective measures for methane and carbon dioxide ground gasses for new buildings" (2019)
Ciria C795 "Retrofitting hazardous ground gas protection measures in existing or refurbished buildings" (2020)
Ciria C801 – Hazardous ground gas – a site management guide (2021)

2. BACKGROUND INFORMATION

MembraneTestingSolutions Ltd (MTS Ltd) were initially approached by Mr Martin Werner, the Engineering Manager of BAM Construct UK Ltd (The Client) in December 2021. Mr Werner advised they were seeking to appoint a 3rd party to validate the ground gas/waterproofing mitigation measures to be installed to a development of a new multi-use indoor arena with supporting leisure & retail facilities. The development is located at the following address;

CO-OP Live, Project Bradford, Alan Turing Way, Manchester, M11 3DU

The client invited MTS Ltd to join a remote Teams meeting arranged for 4th January 2022 to discuss our potential role in the validation process on this project prior to formal appointment. Before the meeting, the client provided us with project specific documentation.

Following the remote meeting we attended site on the 5th January 2022. We noted that as the Grace Construction Products (GCP) Ltd's products currently being installed on site are being excellently executed, along with the various layers of QA processes being performed on site by numerous interested parties, we advised MTS Ltd were prepared to offer a reduced validation process. We advised we would give an overall overview of the materials installation & the quality of workmanship to allow final sign off , in line with the CIRIA C735 best practice document.

We noted there have been a number of installation processes that had already been performed on site. We were presented with the GCP & Carey's QA reports for works not witnessed by MTS Ltd. Therefore, we were able to include these areas within our validation process and final sign off validation report. On the basis of there being number of detailed items to be validated we assessed the number of validation visits which we advised will need to include upper perimeter termination details.

On the basis of the above we anticipated the validation visit numbers being approximately 20no In total with up to 20no photographic validation events to capture any unfinished areas or repairs that were unable to be completed during our site inspections.

Upon acceptance of our costs, MTS Ltd were employed by the client. We presented a verification plan for the gas mitigation measures & proposed validation processes for this project, which was submitted on the 2nd February 2022.

MTS Ltd performed 11no site validation visits throughout the project timeframe, however 1no photographic validation event was also performed.

The following information is our 3rd party independent inspection, testing and reporting for the validation works performed to this project, which we provide for approval by the local authority/project stakeholders for clearing any planning conditions pertaining to ground gas contamination.

3. GROUND GAS MONITORING

MTS Ltd received a copy of the Ground Investigation Report produced by BuroHappold Engineering for the site. The report reference is:

- Remediation Strategy Report reference: BRA-BHE-XX-XX-RP—CG-0006 Revision P02 dated 7th October 2020

Please see below excerpt regarding ground gas monitoring;

3.3 Ground gas

Ground gas monitoring was undertaken on a total of 11 locations on six different monitoring occasions following the site investigation. The monitoring data is generally consistent with the nature and extent of the source (Made Ground). The Made Ground is typically about 9m thick (varies from 1.3m to 17.2m) [Made Ground thicker within the north and west of the site]. This residual Made Ground typically contained organic material including hydrocarbons, coal and rare visual sightings of oily sheen on the perched water in the monitoring installations. The maximum concentrations of methane were recorded at 8.2%, 10.1% and 10.9%, all other recorded concentrations within these installations were also elevated above the guideline threshold (1%). The maximum concentrations of carbon dioxide (in installations with elevated concentrations) were typically in the range of 1 to 8.9% with concentrations above 2.5% recorded in 4 of the 11 installations on at least one occasion. Three installations recorded concentrations of carbon dioxide elevated above 5%.

The calculated GSV for CO_2 and CH_4 (concentrations x flow rate) have been determined as Characteristic Situation 1. However, in accordance with CIRIA C665 [15] it is recommended the Characteristic Situation is increased to Characteristic Situation 2 due to the multiple elevated concentrations of CH_4 and $C0_2$ above the typical maximum value for CS1 (1% and 5%, respectively) and the depleted oxygen concentrations (<16%). Under the worst case scenario gas flow rates only need to increase to 0.7l/hr with the methane concentration recorded for a classification of CS2 to be triggered. Such a variation in flow though not recorded is feasible and therefore it is considered appropriate for the site to be considered CS2.

End of précised text

MTS Ltd have assumed the project has been allowed to progress through to the construction stage, therefore based on the information received from the client and in line with the above MTS Ltd have employed the site Characteristic Situation 2 in accordance with the CIRIA C665.

4. BS 8485:2015+A1:2019 COMPLIANCE

Using the tabled contents of the BS 8485:2015+A1:2019 document, the gas mitigation measures installed can be calculated by the following:

Table 3, Building Type	Table 4, Gas Protection Score by CS & Type of Building	Table 5, Gas Protection Scores for the Structural Barrier	Table 6, Gas Protection Scores for Ventilation Protection Measures	Table 7, Gas Protection Score for the Gas Resistant Membrane
Type D = Commercial / Industrial	CS2 = Points required by the design = 1.5 Points	Reinforced cast in situ suspended floor slab with minimal penetration's. = 1.5 Points	No Passive Ventilation = 0 Points	Gas barrier membrane installed & validated in accordance with the CIRIA C735 =2.0 Points

Total 'MINIMUM' Points Score Achieved from the Above = (T5 = 1.5 + T7 = 2.0) = **3.5 Points Achieved** which exceeds the minimum points score requirement of the design.

5. DESIGN DRAWINGS

MTS Ltd received drawings for this project inclusive of proposed layout & ground floor details for the building, as noted below;

Buro Happold Drawings;

- BRA-BHE-ZC-ZZ-DR-S-3521 Level GF & GM Zone C Water Tank Sections
- BRA-BHE-XX-XX-DR-S-3501 Substructure Detail Sections Sheet 1
- BRA-BHE-XX-XX-DR-S-3504 Substructure Detail Sections Sheet 4
- BRA-BHE-ZA-GF-DR-S-1001-GF Slab Pours – 24.1.2022

GCP Applied Technologies Product Application Techniques Drawings;

- BRA-CCE-ZZ-ZZ-DR-Y-16101 Waterproofing Details
- BRA-CCE-ZZ-ZZ-DR-Y-16102 Waterproofing Details
- BRA-CCE-ZZ-ZZ-DR-Y-16104 Waterproofing Details
- BRA-CCE-ZZ-ZZ-DR-Y-16106 Waterproofing Details
- BRA-CCE-ZZ-ZZ-DR-Y-16126 Waterproofing Details
- BRA-CCE-ZZ-ZZ-DR-Y-16142 Waterproofing Details
- BRA-CCE-ZZ-ZZ-DR-Y-16144 – P02 Waterproofing Details
- BRA-CCE-ZZ-ZZ-DR-Y-16145 Waterproofing Details

Copies of the drawings noted above are appended in Appendix. B of this report.

6. MATERIAL SPECIFICATIONS

The ground gas mitigation measures were designed and specified by GCP Ltd. They also specified the appropriate products to be installed to mitigate against the site specific contaminates.

The material supplier was as follows;

GCP Applied Technologies (UK) Limited
487-488 Ipswich Road
Slough
Berkshire
SL1 4EP

Tel: +44 (0) 1753 490 000
Web: www.gcpat.uk/en-gb

Material Specifications

- Preprufe 300R Plus Membrane
- Preprufe Tape
- Bituthene LM Trowel Applied (Liquid) Membrane
- Bitustik BT 240 Double Sided Jointing Tape

The above Material Specifications may be found appended in Appendix. C of this report.

7. GAS MEMBRANE INSTALLATION CONTRACTOR

MTS Ltd confirm as the project was a CS2 'Low Risk'

MTS Ltd confirm as the project had been classified as a CS2 'Low Risk' (C665) the client opted to enlist their non-specialist groundworks contractor to install the GCP ground gas/waterproofing barrier materials, which was acceptable to MTS Ltd due to the low site gas risk.

The installation contractor was namely;

Carey's Civil Engineering Ltd
Carey House
Great Central Way
Wembley
HA9 0HR

Tel: 020 8900 0221

MTS Ltd have not validated this company's workmanship prior to this project however during the project duration we have regularly found them to produce a 'Good' level of workmanship, hence now having extreme faith in this company's installation methodology.

8. INSPECTION, TESTING AND VALIDATION REGIME

The installed gas protective materials were 3rd party independently inspected, tested and validated in accordance with the Ciria C735 best practice document by a competent and qualified validation surveying company, namely Membrane Testing Solutions Ltd.

Due to the perceived CS2 'Low Risk' and with a gas/waterproofing membrane being installed below the ground bearing slabs and installed by non- NVQ Level 2 qualified installation operations, MTS Ltd considered up to 20no site visits would be appropriate for validation of materials throughout the project duration.

MTS validated a number of different gas mitigation detailing areas which incorporated all GCP detailed designs, with aspects of the ground gas mitigation measures being checked and validated, inclusive of gas membrane application, sealing to service pipes, perimeter connections and the like.

The gas/waterproofing mitigation measures were installed on a piece meal basis meaning the gas mitigation measures were installed and covered post inspection, validation or various layers of QA.

MTS Ltd actually attended site on 11no occasions having been requested to attend site by the client's representatives, therefore the visit numbers were less than originally considered. However, works that were validated were well installed and in accordance with the GCP design, material specifications and industry best practices.

Due to the materials installation being of fully taped seam construction, MTS Ltd employed a detailed visual inspection and seam pick probe testing of site seams presented for validation.

No membranes were signed off by MTS Ltd until a minimum acceptable standard had been achieved, whereby ensuring the membrane installation was suitably managed to achieve maximum confidence to the suitability of the installed materials.

8.1 INSPECTION, VALIDATION & TESTING METHOD STATEMENT

1. The Validation Surveyor was suitably experienced and qualified to carry out a detailed visual inspection and seam integrity testing of the installed gas membrane system.
2. Membrane areas offered for validation were subjected to independent, inspection validation and seam integrity testing.

3. The Validation Surveyor visually inspected 100% of the gas protection measures to the areas submitted for inspection.
4. Seam pick testing was performed to 100% of site seams provided for inspection, inclusive of pipe seals and taped joints etc. ensuring all seams were suitably bonded/adhered. Seam pick testing comprises of a hand-held implement with a wooden handle and 6mm diameter x 250mm long shaft terminating in a point at 90° to the main shaft. The point of the seam pick test is drawn down the length of the seam seeking intrusion of the implement into the seam whereby indicating a defect. This testing method is also used for difficult detailing or intricate works such as around pipe sealing details etc. Seam pick testing is an approved test method in accordance with ASTM D4437 – 2018 and the CIRIA C735 best practice document.
5. There were small a number of defects to report, which were repaired and passed off after reinspection.
6. Upon completion of the test the gas membrane area was signed off and certified as integral.
7. The Validation Surveyor completed an "Independent Inspection & Validation Certificate of Conformance" at each validation visit and photographic evidence was taken. The project survey sheets and photographic logs are incorporated in this final report submission.
8. Upon completion of the validation/integrity test inspection, a validation certificate stating the outcome was issued.

The Validation Surveyor:

- Performed all visual detailed and intimate Inspections:
- Performed seam testing to 100% of site seams:
- Marked up any repairs:
- Witnessed and reinspected the repairs and passed off:
- Completed the project survey sheets:
- Took photographs for inclusion in the final validation report:
- Produced a final validation report at the end of the installation process.

9. MTS SITE VISITS

MTS Ltd attended site on 11no occasions and we performed 1no photographic validation event which were catered for.

The dates, areas validated and test results are noted in the table below;

Visit No:	DATE:	AREA & GRIDLINES:	TEST RESULT:	RE-TEST REQUIRED:	PHOTOGRAPHIC EVIDENCE RECEIVED
1	24.1.2022	Slab area to G/L W07-W08 & EW	PASS IN FULL	NO	N/A
2	3.2.2022	Pour 2 – Main floor installation to G/L's W08 / NW – N01 and Core 5 – Base Installation to G/L's E07-BS / N12-BE	PASS IN FULL TO BOTH AREAS	NO	N/A
3	24.2.2022	Core 5 Wrap to G/L's E07-BS / N12-BE + Core 7 base, Main Floor installation to G/L's S11-S15 / SW3 + Pour 9 South West Slab to G/L's S1-S3 / NW-N01	PASS IN FULL TO ALL 3NO AREAS	NO	N/A
4	5.4.2022	Sprinkler Room Pool 2 to G/L's S15.8 / S17.5 – FS/GS + Buttress Wall to G/L's e06 – E07	PASS IN FULL	NO	N/A
5	30.6.2022	Sprinkler Tank to G/L's S15.7 / S17.5 + South Liner Wall to G/L's S13/S15 + Liner Wall East to G/L's E04/E06	PASS IN FULL	NO	N/A

6	23.8.2022	Core 1 Tanking to Pre-Cast Walls to G/L's N01-N04 / NW2-NW3	PASS IN FULL	NO	N/A
7	25.1.2023	South West Slab, East of Core 6	PASS W.I.P	NO	N/A
8	7.8.2023	Bowl Slab to G/L's E01-E04 & N10-AE	PASS W.I.P	NO	YES
PV Event No.1	12.9.2023	Bowl Slab to G/L's E01-E04 & N10-AE	PASS IN FULL		
9	29.9.2023	Perimeter Tanking Detail	PASS IN FULL	NO	N/A
10	18.10.2023	East Perimeter Tanking & Waterproofing	PASS W.I.P	NO	N/A
11	4.12.2023	East and South Perimeter Tanking and internal bowl slabs	PASS IN FULL	NO	N/A

As may be noted above MTS Ltd attended site on 11no occasions and performed 1no photographic validation event, which is below the 20no originally catered for, however we have been advised by the client a small number of ongoing validation visits will be performed post provision of this verification report.

However, in line with our verification plan MTS Ltd it was agreed that we would only be providing random site visits for differing detail areas, which we have performed. As noted previously, due to the number of layers of QA being performed by GCP, Carey's the installation contractor, Waterseal Ltd and BAM, we are satisfied all parties have performed their respective duties with all visits showing 'good workmanship' therefore we have pleasure in endorsing this verification report as suitable for adoption and acceptance by the local authority.

Copies of our sign off certificate reports are appended in Appendix. D of this report.

OUTCOME – Overall PASS IN FULL

10. SITE PHOTOGRAPHS

MTS Ltd always take copious photographs during our time on site as evidence towards the installation, of which below are a small selection, however some photographs taken on site are contained within our sign off certification reports appended to Appendix. D of this report, however all photographs taken by MTS Ltd are contained on a USB Storage Device appended in Appendix. E of this report.



1



2



3



4



5



6



7



8



9



10



11



12



13



14



15



16



17



18


19


20


21


22


23



24


25


26



27

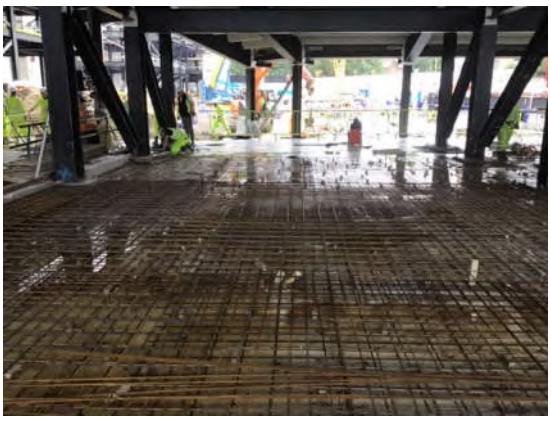

28



29



30



31



32




33



34



35

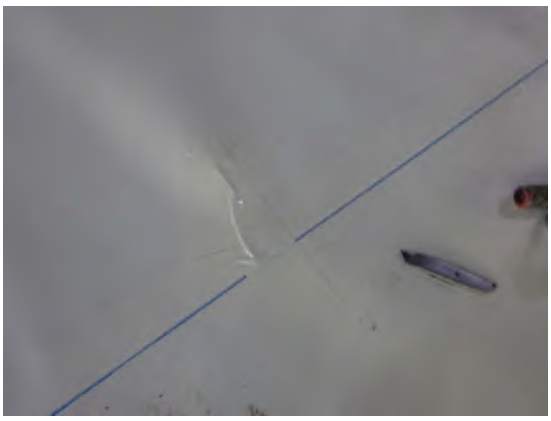


36



37



38

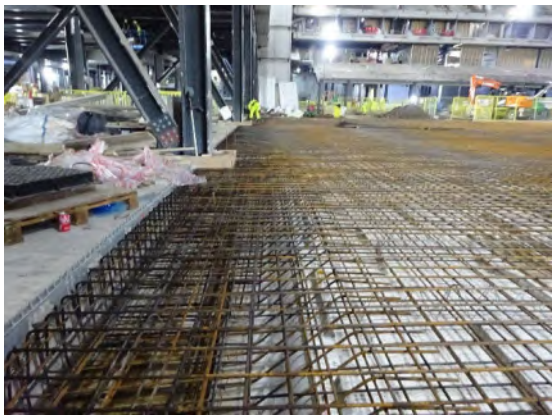

39



40



41



42



43




44



45



46

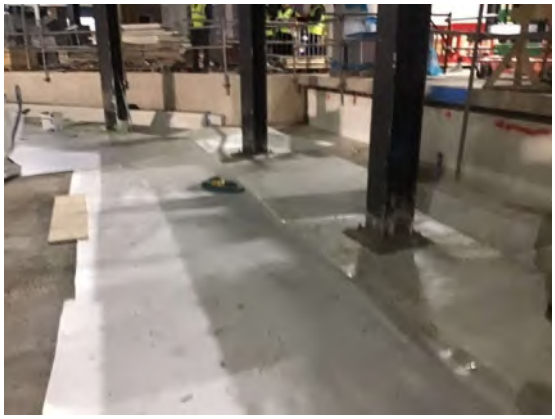

47



48



49



50

INSTALLATION & VALIDATION PHOTOGRAPHS INDEX

No.	Description	No.	Description
1	General overview of installed gas to the external perimeter walls	2	Repair patches to the perimeter vertical walls
3	General overview of installed gas to the external perimeter walls	4	General overview of installed gas to the external perimeter walls with repair patches
5	General overview of installed gas membranes to basement slab and walls	6	Basement walls starter bar installation sealed with Trowel Applied Liquid Membrane
7	Typical core perimeter sealing detail	8	Earth strap installation sealed with Trowel Applied Liquid Membrane
9	Waterbar installation at slab edge joints	10	General overview of installed gas to the basement slab and walls
11	Typical upper core membrane detail	12	Ongoing core membrane installation showing primer prior to membrane application
13	Core membrane with protection board over prior to backfilling and compaction	14	Core membrane installation with seam edge being rolled to ensure a tenacious bond is achieved
15	Typical upper core membrane detail	16	Ongoing core membrane installation detailing
17	Basement slab installation	18	Service pipe installation sealed with Trowel Applied Liquid Membrane
19	Typical manhole installation sealed with Trowel Applied Liquid Membrane	20	Basement walls starter bar installation sealed with Trowel Applied Liquid Membrane with Waterbar installation
21	Typical basement wall membrane termination detail sealed with Trowel applied liquid membrane	22	Installed membrane being overlain with steel mesh, note concrete mars bar spacers
23	Typical pile sealed with Trowel applied liquid membrane	24	Typical seam pick probe testing of site seams
25	Podium slab lined with gas membrane	26	Typical corner sealing detail
27	Typical Waterbar installation around steel stanchion movement joint	28	Ongoing steel reinforcement above membrane
29	Ongoing steel reinforcement above membrane	30	Ongoing membrane installation detailing to podium edge
31	Ongoing membrane installation detailing to podium edge	32	General overview of installed gas membranes to change in level and isolation joint around steel stanchion
33	Typical seam rolling equipment	34	Steel stanchion thickening with gas membrane applied
35	Bowl membrane installation with seam backing tape removed	36	Typical fish mouth seam repair
37	Ongoing steel reinforcement above bowl slab membrane	38	Bowl slab edge thickening including connection into previous slab edge
39	Bowl slab edge thickening including connection into previous slab edge	40	General overview of bowl slab steel reinforcement
41	Typical perimeter membrane installation with repairs	42	Typical perimeter membrane protection prior to backfill and compaction
43	Podium slab sealed with Integritank spray applied membrane	44	Perimeter expansion joint sealed with Integritank spray applied membrane
45	Podium slab edge sealed with Integritank spray applied membrane	46	Internal channel thickening lined with Pre-Prufe 300R membrane

47	Bowl slab edge lined with Pre-Prufe 300R membrane	48	Bowl slab upstand lined with Pre-Prufe 300R membrane
49	Bowl slab lined with Pre-Prufe 300R membrane, with steel reinforcing mesh above	50	General installation/pour mark-up plan

11. CONCLUSIONS AND RECOMMENDATIONS

As a result of our 3rd party ground gas mitigation independent inspection, testing & validation process, MTS Ltd conclude the ground gas mitigation measures prescribed for this site has been inspected, tested and validated in accordance with the GCP design, materials specifications and industry best practice installation requirements.

MTS Ltd confirm we have not validated every m2 of membrane installation however we believe we have captured sufficient evidence for all detailing and design elements to ensure confidence of the installation processes. The material installation proved well performed and any defects found were remediated and covered by the varying layers of contractors QA procedures.

Therefore, MTS Ltd conclude the 'CS2 Low Risk' ground gas mitigation measures installed to this project have been sufficiently managed to maintain maximum confidence to the proficiency of the installed gas mitigation system therefore, we conclude that the materials installed to this project are appropriate have been "validated in accordance with the CIRIA C735" best practice document and our accepted verification plan.

As such it is Membrane Testing Solutions Ltd recommendation to the Local Authority/project stakeholders to sign off this ground gas mitigation strategy and validation report as;

"APPROVED FOR PLANNING CONDITION SIGN OFF"

END OF REPORT

12. APPENDICES

Appendix A – Validation Surveyors Certificates of Competence

Mr Barrie Ackroyd (MTS Ltd)
Mr Michael Smith (MTS Ltd)
Mr Keith Barsby (MEC Ltd)
Mr Dan Squires (MEC Ltd)

Appendix B – Design Drawings

Buro Happold Drawings;

- BRA-BHE-ZC-ZZ-DR-S-3521 Level GF & GM Zone C Water Tank Sections
- BRA-BHE-XX-XX-DR-S-3501 Substructure Detail Sections Sheet 1
- BRA-BHE-XX-XX-DR-S-3504 Substructure Detail Sections Sheet 4
- BRA-BHE-ZA-GF-DR-S-1001-GF Slab Pours – 24.1.2022

GCP Applied Technologies Product Application Techniques Drawings;

- BRA-CCE-ZZ-ZZ-DR-Y-16101 Waterproofing Details
- BRA-CCE-ZZ-ZZ-DR-Y-16102 Waterproofing Details
- BRA-CCE-ZZ-ZZ-DR-Y-16104 Waterproofing Details

- BRA-CCE-ZZ-ZZ-DR-Y-16106 Waterproofing Details
- BRA-CCE-ZZ-ZZ-DR-Y-16126 Waterproofing Details
- BRA-CCE-ZZ-ZZ-DR-Y-16142 Waterproofing Details
- BRA-CCE-ZZ-ZZ-DR-Y-16144 – P02 Waterproofing Details
- BRA-CCE-ZZ-ZZ-DR-Y-16145 Waterproofing Details

Appendix C – Material Specifications

- Preprufe 300R Plus Membrane
- Preprufe Tape
- Bituthene LM Trowel Applied (Liquid) Membrane
- Bitustik BT 240 Double Sided Jointing Tape

Appendix D – Project Survey Sheets

MTS Ltd Gas Protection Inspection & Validation Record Certs

Appendix E – Copy of Validation Report and Photographs (Contained on USB Storage Device)

APPENDIX A

Validation Surveyors – Certificates of Competence

BGA
British Geomembrane Association

This is to certify that

Barrie Ackroyd

Has successfully attended a
Technical Course
in

Gas Membrane Installations

This in support of the Quality Controls
Of Inspection and Validation
Of Gas Membrane Installations

This certificate is awarded by: BGA British Geomembrane Association Date: 30/10/14

citb

Course content detailed overleaf

Gas Membrane Installation
Technical Course
for
Inspectors & Validators

Training Modules Attended

Practical & Knowledge

- Components of Gas Protection Systems with Venting
- Verification
- Gas Membrane Installation Techniques
- Introduction to Integrity Testing (Practical)
- Introduction to Integrity Testing (Theory)
- Risk Assessment and Validation Plan
- Site Inspections and Pro-formas
- Validation Report
- On Site Assessment

CERTIFICATE of ACCREDITATION

This is to certify that

Barrie Ackroyd

has been awarded the following accreditation

Gas Protection Verification Scheme (GPVS)

Specialist (SGPV)

Certificate No.: 435qQb4axS

Issued:19 November 2020
Valid for 4 years from the above date

Gas Protection Verification

Richard Froggatt
CL:AIRE Chairman

CL:AIRE is a Charitable Company Limited by Guarantee
Registered in England 3740059 / Entrust Enrolment No. 119820 / Registered Charity No. 1075611
Chiltern House, Haddenham Business Centre, Thame Road, Haddenham, Buckinghamshire, HP17 8BY
Telephone: +44 (0)1844 296112 | Email: enquiries@claire.co.uk | Website: www.claire.co.uk

ABBE
Quality Accredited

Certificate of Achievement

(Full Award)

This is to certify that

Barrie Anthony Ackroyd

has been assessed as meeting the required level of competence for all the units necessary to achieve the full award

ABBE Level 4 NVQ Diploma in Verification of Ground Gas Protection Systems

603/3266/9

Units achieved: Mandatory Units K/617/0687, M/617/0688, K/617/0690, M/617/0691, A/617/0693, F/617/0694, J/617/0695

ofqual
REGULATED
register.ofqual.gov.uk

Signed :

Professor Julian Beer, Chair of ABBE Board

Date: 17/01/2023

Candidate Registration No : 0000039497 Certificate Issue No : 154133

Scan code on reverse to authenticate that this is a genuine paper

ABBE
Quality Accredited

Certificate of Unit Achievement

This is to certify that

Barrie Anthony Ackroyd

has been assessed as meeting the following units of competence which form part of an accredited qualification

M/617/0688	Materials for Construction in the Built Environment
J/617/0695	Principles of Regulatory Control Procedures and Legislation
F/617/0694	Verification and Inspection of Ground Gas Protection Systems
K/617/0687	Design Principles and Application for Construction in the Built Environment
A/617/0693	Confirming Work Meets Quality Standards in the Workplace
M/617/0691	Principles of Construction and Maintenance of Buildings
K/617/0690	Health, Safety and Welfare in the Construction Environment

Signed :

Professor Julian Beer, Chair of ABBE Board

Date: 17/01/2023

Candidate Registration No : 0000039497 Certificate Issue No : 154132

Scan code on reverse to authenticate that this is a genuine paper

ABBE
Quality Accredited

Certificate of Achievement

(Full Award)

This is to certify that

Michael Anthony Smith

has been assessed as meeting the required level of competence for all the units necessary to achieve the full award

ABBE Level 4 NVQ Diploma in Verification of Ground Gas Protection Systems

603/3266/9

Units achieved: Mandatory Units K/617/0687, M/617/0688, K/617/0690, M/617/0691, A/617/0693, F/617/0694, J/617/0695

Signed :

Professor Julian Beer, Chair of ABBE Board

Date: 23/01/2020

ofqual
REGULATED
register.ofqual.gov.uk

Candidate Registration No : 0000036770 Certificate Issue No : 142188

00026189

ABBE
Quality Accredited

Certificate of Unit Achievement

This is to certify that

Michael Anthony Smith

has been assessed as meeting the following units of competence which form part of an accredited qualification

K/617/0687	Design Principles and Application for Construction in the Built Environment
M/617/0688	Materials for Construction in the Built Environment
K/617/0690	Health, Safety and Welfare in the Construction Environment
M/617/0691	Principles of Construction and Maintenance of Buildings
A/617/0693	Confirming Work Meets Quality Standards in the Workplace
F/617/0694	Verification and Inspection of Ground Gas Protection Systems
J/617/0695	Principles of Regulatory Control Procedures and Legislation

Signed :

Professor Julian Beer, Chair of ABBE Board

Date: 23/01/2020

Candidate Registration No : 0000036770 Certificate Issue No : 142185

00026186

CERTIFICATE of ACCREDITATION

This is to certify that

Michael Smith


has been awarded the following accreditation

Gas Protection Verification Scheme (GPVS)

Technician (TGPV)

Certificate No.: 2UEiQm05Uq

Issued: 8 April 2021
Valid for 4 years from the above date



Richard Froggatt
CL:AIRE Chairman



CL:AIRE is a Charitable Company Limited by Guarantee
Registered in England 3740059 / Entrust Enrolment No. 119820 / Registered Charity No. 1075611
Chiltern House, Haddenham Business Centre, Thame Road, Haddenham, Buckinghamshire, HP17 8BY
Telephone: +44 (0)1844 296112 | Email: enquiries@claire.co.uk | Website: www.claire.co.uk

ABBE
Quality Accredited

Certificate of Achievement

(Full Award)

This is to certify that

Daniel Squire

has been assessed as meeting the required level of competence for all the units necessary to achieve the full award

ABBE Level 4 NVQ Diploma in Verification of Ground Gas Protection Systems

603/3266/9

Units achieved: Mandatory Units K/617/0687, M/617/0688, K/617/0690, M/617/0691, A/617/0693, F/617/0694, J/617/0695

ofqual
REGULATED
register.ofqual.gov.uk

Signed :

Professor Julian Beer, Chair of ABBE Board

Date: 23/11/2020

Candidate Registration No : 0000037271 Certificate Issue No : 143619

00027765

ABBE
Quality Accredited

Certificate of Achievement

(Full Award)

This is to certify that

Keith Barsby

has been assessed as meeting the required level of competence for all the units necessary to achieve the full award

ABBE Level 4 NVQ Diploma in Verification of Ground Gas Protection Systems

603/3266/9

Units achieved: Mandatory Units K/617/0687, M/617/0688, K/617/0690, M/617/0691, A/617/0693, F/617/0694, J/617/0695

Signed :

Professor Julian Beer, Chair of ABBE Board


Date: 23/11/2020

ofqual
REGULATED
register.ofqual.gov.uk


Candidate Registration No : 0000037076 Certificate Issue No : 143625

APPENDIX B


Design Drawings

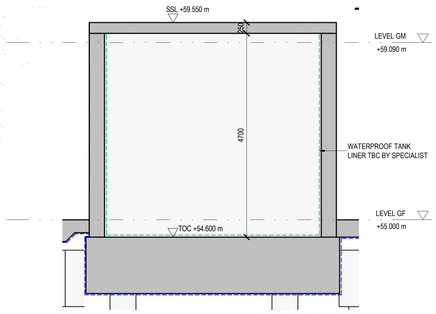


1 DET. REF. WATER TANK WALL ELEVATION 1
SCALE 1 : 50

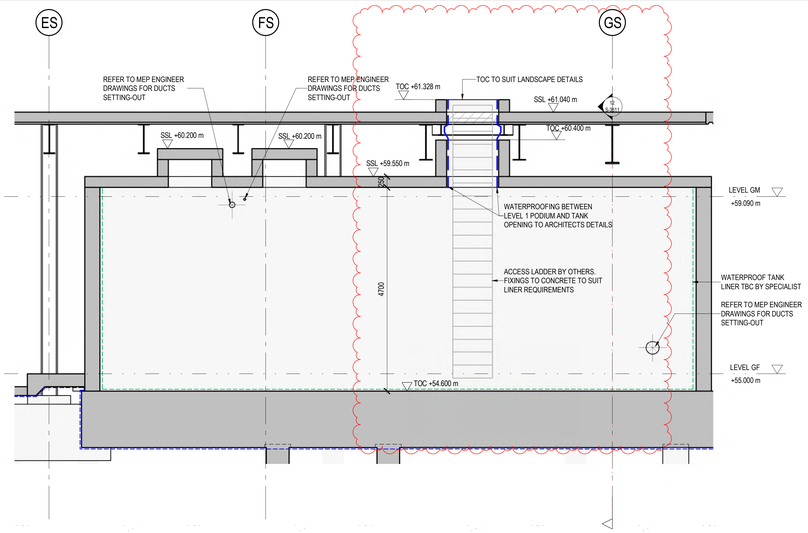

2 DET. REF. WATER TANK WALL ELEVATION 2
SCALE 1 : 50

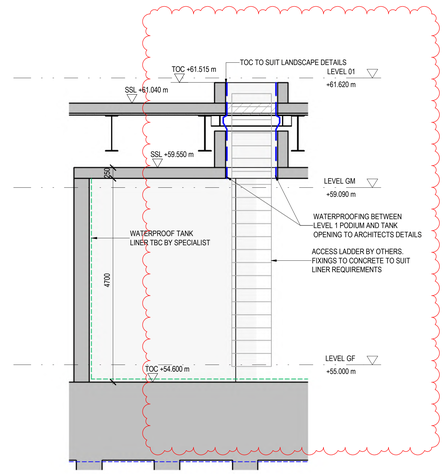


3 DET. REF. WATER TANK WALL ELEVATION 3
SCALE 1 : 50

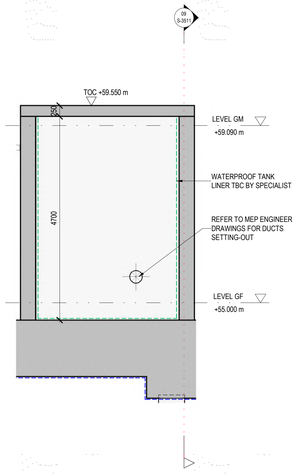


4 DET. REF. WATER TANK WALL ELEVATION 4
SCALE 1 : 50

5 DET. REF. WATER TANK WALL ELEVATION 5
SCALE 1 : 50



6 DET. REF. TYPICAL WATER TANK WALL TO LID DETAIL
SCALE 1 : 20

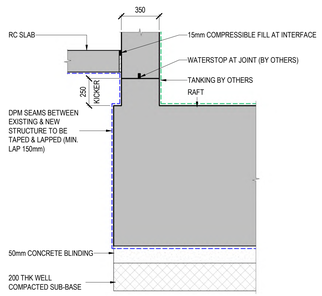

TYPICAL WATER TANK WALL AND RAFT INTERSECTION
SCALE 1 : 20

All Rights reserved. Buro Happold and its group companies assert (unless otherwise agreed in writing) their rights under s.77 & 78 of the Copyright, Designs and Patents Act 1988.

DO NOT SCALE THIS DRAWING.

Suitability Code (as defined in ISO 19650-2:2018)

Work in Progress (WIP)
S0 - Initial Status

Shared (Non- Contractual)
S1 - Suitable for co-ordination
S2 - Suitable for information
S3 - Suitable for review & comment
S4 - Suitable for stage approval
S5 - Withdrawn
S6 - Suitable for PIM authorisation
S7 - Suitable for AIM authorisation

Published (Contractual)
A1, A2, A3, Etc - Authorised and accepted
B1,B2,B3, Etc, - Partial sign-off (with comments)

Published (AIM Acceptance)
CR - As constructed record document

SAFETY HEALTH AND ENVIRONMENTAL INFORMATION
IN ADDITION TO THE HAZARDS/RISKS NORMALLY ASSOCIATED WITH THE TYPES OF WORK DETAILED ON THIS DRAWING, NOTE THE FOLLOWING


CONSTRUCTION
TANKS ARE ADJACENT TO PILED WALLS SUBJECT TO LONG TERM MOVEMENT. NO SOLID SHUTTERING OR PACKING TO BE USED TO AVOID WALL DEFLECTIONS IMPACTING WATER TANKS.

POUR SEQUENCING AND SIZES TO BE AGREED PRIOR TO CONSTRUCTION. HYDROPHILIC STRIPS TO BE USED AT ALL CONSTRUCTION JOINTS.

MAINTENANCE/CLEANING/OPERATION
SINGLE ACCESS POINT TO EACH TANK IS PROVIDED FROM PODIUM. CONFINED SPACE RESTRICTED ACCESS REQUIRED.

DECOMMISSIONING/DEMOLITION

Key Plan



Notes

1. ALL CONCRETE ASSUMED TO BE C30/37 GRADE.
2. FOR DETAILS OF PIPE SETTING OUT REFER TO MEP ENGINEER DRAWINGS.
3. ALL CONSTRUCTION JOINTS TO HAVE HYDROPHILIC STRIPS
4. BEFORE CONCRETING THE CONTRACTOR IS TO SUBMIT A LAYOUT SHOWING THE LOCATION OF ALL PROPOSED CONSTRUCTION JOINTS. THE SPACING AND SEQUENCE OF POURS SHALL NOT EXCEED THOSE GIVEN IN THE SPECIFICATION.
6. ALL TANK PENETRATIONS TO USE SUITABLE PUDDLE FLANGE CAST IN CONNECTIONS.
7. WATER TANKS TO BE LINED WITH A FULLY WATERPROOF MEMBRANE. CONCRETE IS NOT DESIGNED TO BE THE PRIMARY WATERPROOFING ELEMENT.
8. ALL CONSTRUCTION JOINTS TO HAVE HYDROPHILIC STRIP INSTALLED.

Rev	App/Chn	Date	Description
P02	TH/AT	17.12.2021	STAGE S4 APPROVAL (STEEL UPDATES)
P01	TH/AT	10.12.2021	STAGE S4 APPROVAL(WATER TANKS)

OVG INTERNATIONAL

BURO HAPPOLD

Camden Mill
Lower Bristol Road
Bath BA2 3DG
UK

Tel: +44 (0)1225 320 600
Fax: +44 (0)8707 874 146
Email: 00428H1@burohappold.com
Web: www.burohappold.com


Co-op Live

title: LEVEL GF AND GM
ZONE C
WATER TANK SECTIONS SHEET 1


purpose of issue: **STAGE APPROVAL**

scale: As indicated @ A0 | drawn: AT | job no.: 0042841 | Suitability: **S4**
date: 26/11/21 | checked: TH


reference | project code | originator | volume | level | type | role | number | rev.
BRA-BHE-ZC-ZZ-DR-S-3521 **P02**

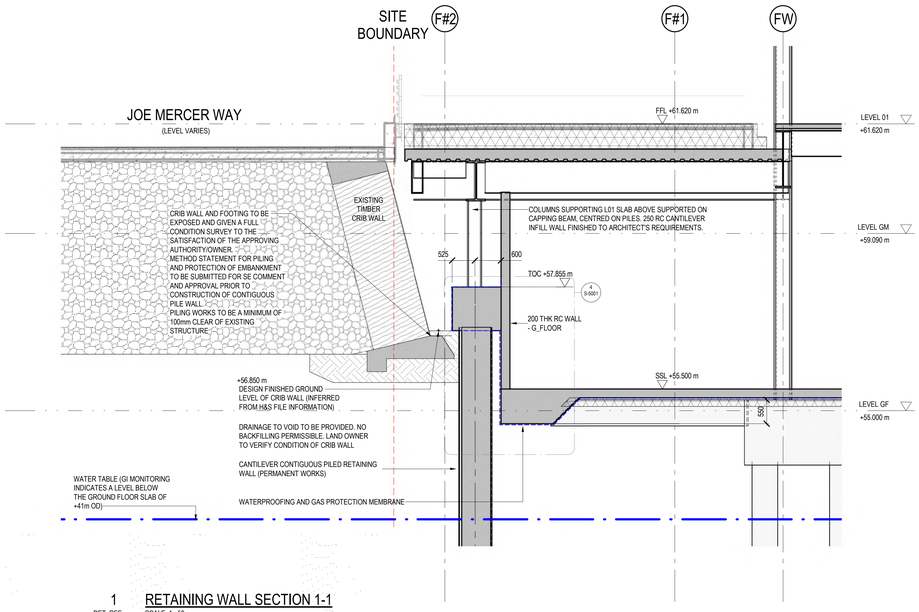


1 DET. REF. RETAINING WALL SECTION 1-1
SCALE 1 : 50

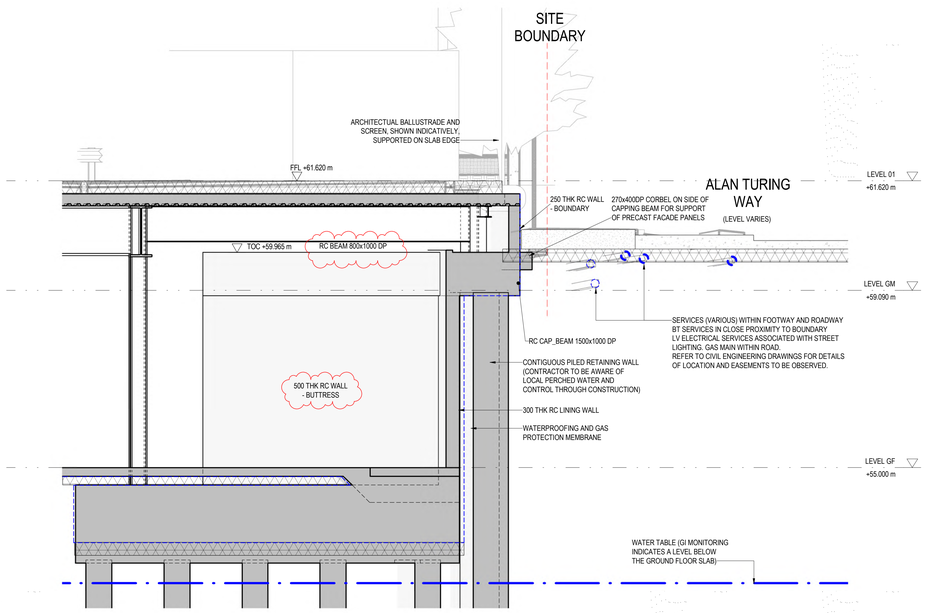

2 DET. REF. RETAINING WALL SECTION 2-2
SCALE 1 : 50

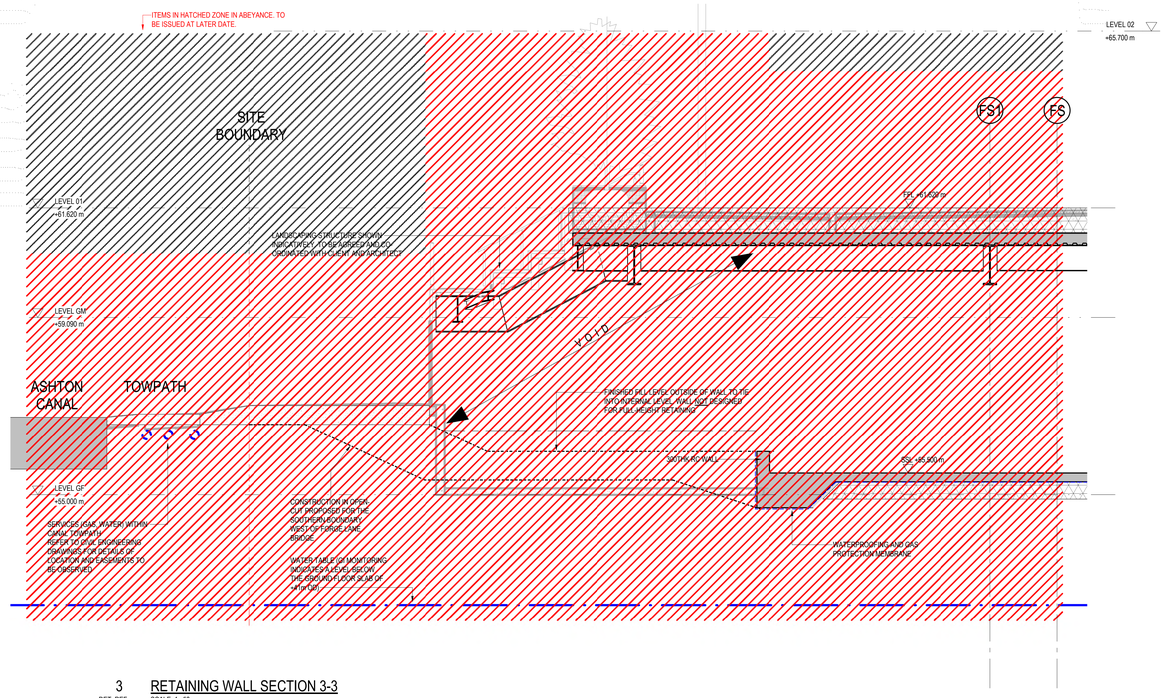

3 DET. REF. RETAINING WALL SECTION 3-3
SCALE 1 : 50

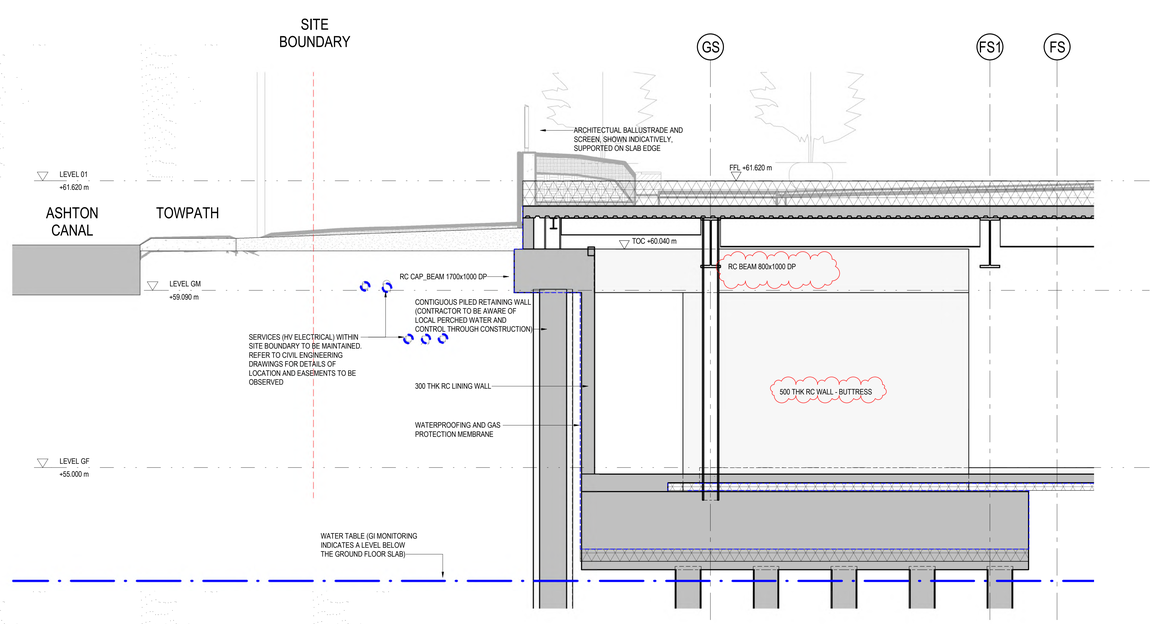

4 DET. REF. RETAINING WALL SECTION 4-4
SCALE 1 : 50

All Rights reserved. Buro Happold and its group companies assert (unless otherwise agreed in writing) their rights under s.77 & 78 of the Copyright, Designs and Patents Act 1988.

DO NOT SCALE THIS DRAWING.

Suitability Code (as defined in ISO 19650-2:2018)

Work in Progress (WIP)
S0 - Initial Status

Shared (Non- Contractual)
S1 - Suitable for co-ordination
S2 - Suitable for information
S3 - Suitable for review & comment
S4 - Suitable for stage approval
S5 - Withdrawn
S6 - Suitable for PIM authorisation
S7 - Suitable for AIM authorisation

Published (Contractual)
A1, A2, A3, Etc - Authorised and accepted
B1,B2,B3, Etc, - Partial sign-off (with comments)

Published (AIM Acceptance)
CR - As constructed record document


SAFETY HEALTH AND ENVIRONMENTAL INFORMATION
IN ADDITION TO THE HAZARDS/RISKS NORMALLY ASSOCIATED WITH THE TYPES OF WORK DETAILED ON THIS DRAWING, NOTE THE FOLLOWING

CONSTRUCTION:
1. CONSTRUCTION OF L00 INVOLVES DEEP EXCAVATIONS IN MADE GROUND.
2. MADE GROUND ON SITE IS VERY DEEP AND CONTAMINATED WITH HYDROCARBONS.
3. RECORDS INDICATE 2No. CAPPED, WORKED COAL MINING SHAFTS ON SITE – REFER TO GEO INFORMATION FOR LOCATION.
4. SITE INVESTIGATION INDICATES NUMEROUS LARGE OBSTRUCTIONS BELOW GROUND INCLUDING CONCRETE FOUNDATIONS.
5. CONTRACTOR TO ENSURE TEMPORARY STABILITY OF ALL RETAINING WALLS DURING CONSTRUCTION. RETAINING WALL DESIGN RELIES ON PROVISION OF PROPPING PRIOR TO EXCAVATION VIA THE CAPPING BEAM TO BUTTRESS WALLS OR OTHER SUITABLE PROPS.

MAINTENANCE/CLEANING/OPERATION:
1. PERIMETER RETAINING WALLS RELY ON BUTTRESS WALLS FOR STABILITY.
2. ROOF TRUSSES ARE SEATED ON BEARINGS. DESIGN AND REPLACEMENT STRATEGY TO BE DEVELOPED WITH SPECIALIST SUPPLIER.

DECOMMISSIONING/DEMOLITION:
1. DESIGN LIFE OF THE BUILDING IS 50 YEARS.

Key Plan



Notes

1. THIS DRAWING TO BE READ IN CONJUNCTION WITH GENERAL NOTES ON BRA-BHE-XX-XX-DR-S-0001.
2. REFERENCE SHOULD BE MADE TO THE BASIS OF DESIGN REPORT, INFORMATION IN SUPPORT OF COSTING REPORT AND STRUCTURAL SPECIFICATIONS FOR KEY INFORMATION INCLUDING;
   A. LOADING ALLOWANCES
   B. REINFORCEMENT RATES
   C. MATERIAL SPECIFICATIONS
   D. COSTING NOTES FOR STRUCTURAL ELEMENTS FOR CONCRETE, STEELWORK AND FOUNDATIONS
   E. INFORMATION FOR PRECAST CONCRETE ELEMENTS TO THE BOWL AND RAKER STEELWORK

3. FOR INFORMATION ON PERIMETER RETAINING STRUCTURES, BASEMENT WATERPROOFING AND SITE CONSTAINTS, REFER TO THE FOUNDATION PLAN, TYPICAL SECTIONS AND COSTING REPORT.

4. REFER TO LATEST GEOTECHNICAL INFORMATION REGARDING THE SITE GEOLOGY AND GROUND CONDITIONS INCLUDING:
BRA-BHE-XX-XX-RP-CG-0001 GEOENVIRONMENTAL AND GEOTECHNICAL DESK STUDY
BRA-BHE-XX-XX-RP-CG-0004 GROUND ENGINEERING INTERPRETIVE REPORT
OVG Manchester Factual Report on Ground Investigation Report No. 765000-1 (04) March 2020)
BRA-BHE-XX-XX-RP-CG-0006 REMEDIATION STRATEGY

5. PILES AND EMBEDDED RETAINING WALLS ARE ALL TO CONTRACTOR DESIGN. REFER TO THE PILE SCHEDULE BRA-BHE-XX-XX-SC-S-0010 FOR FURTHER DETAILS

6. ALL FOUNDATIONS TO BE CAST ON 50mm LEAN MIX BLINDING CONCRETE

7. ALL FOUNDATIONS REQUIRE BONDED WATERPROOFING AND GAS MEMBRANE. REFER TO THE WATERPROOFING SPECIFICATION FOR FURTHER DETAILS BRA-BHE-XX-XX-SP-S-0200.

8. ALL CONSTRUCTION JOINTS WITHIN THE PERIMETER CONCRETE WALLS TO BE PROVIDED WITH HYDROPHYLIC STRIPS AND WATER BARS. CONSTRUCTION JOINTS TO BE PROVIDED AT APPROX. 10m CENTRES. REFER TO DRAWING S-5001 FOR FURTHER DETAILS

9. NOMINAL COVER TO REINFORCEMENT AS FOLLOWS:
75mm - BASE
50mm - SIDES AND TOP

10. GROUND CLASSIFICATION FOR BELOW-GROUND CONCRETE IS DC-4. REFER TO PILING AND CONCRETE SPECIFICATIONS FOR FURTHER DETAILS

11. COLUMNS AND PLINTHS ARE CENTRED TO GRIDS U.N.O.

12. PILE CAPS ARE CENTRED TO COLUMNS U.N.O.

13. FOR PILE CAPS DETAILS REFER TO DRAWING BRA-BHE-XX-FN-DR-S-5020 - S-6030.

14. GROUND BEAMS CENTRED TO GRID AND PILE CAPS U.N.O.

15. FOR BELOW GROUND DRAINAGE INFORMATION REFER TO CIVILS DRAWINGS.

P05	THRM	11.06.2021	STAGE 5A APPROVAL
P04	THSO	15.03.2021	ISSUED FOR S4 SUITABLE FOR STAGE APPROVAL
P03	THSO	03.07.2020	STAGE 4A TENDER
P02	THSO	09.04.2020	STAGE 4a DRAFT
P01	THSO	20.03.2020	STAGE 3
Rev	Appr'Dm	Date	Description

OVG INTERNATIONAL

BURO HAPPOLD

Camden Mill
Lower Bristol Road
Bath BA2 3DQ
UK

Tel: +44 (0)1225 320 600
Fax: +44 (0)8707 874 148
Email: 0042841@burohappold.com
Web: www.burohappold.com

Co-op Live


title SUBSTRUCTURE DETAIL SECTIONS SHEET 1

purpose of issue: **STAGE APPROVAL**


scale	1 : 50 @ A0	drawn	SO	Job no.	Suitability
date	03/17/20	checked	TH	0042841	**S4**

reference: project code, originator, volume, level, type, role, number — rev


BRA-BHE-XX-XX-DR-S-3501 **P05**

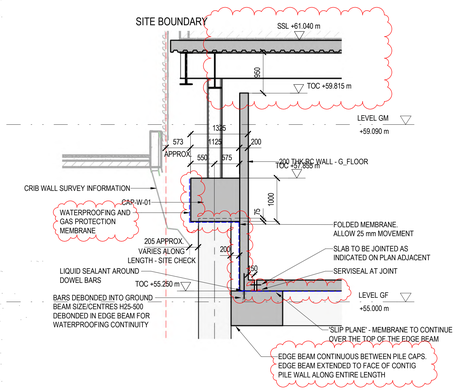


1 DET. REF. JOE MERCER WAY SECTION 1
SCALE 1 : 50

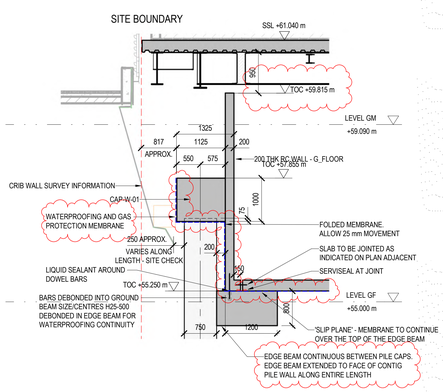


2 DET. REF. JOE MERCER WAY SECTION 2
SCALE 1 : 50

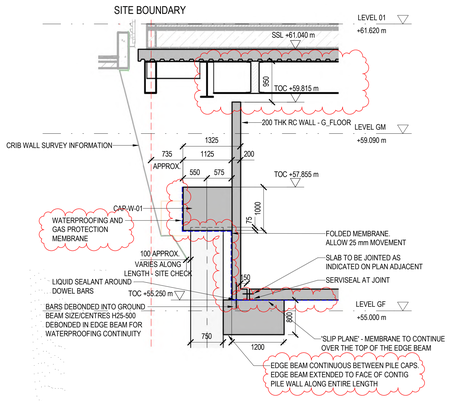


3 DET. REF. JOE MERCER WAY SECTION 3
SCALE 1 : 50

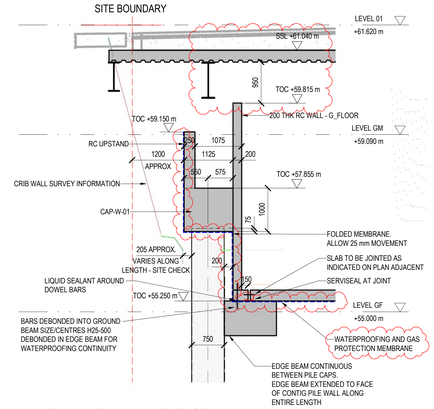

4 DET. REF. JOE MERCER WAY SECTION 4
SCALE 1 : 50

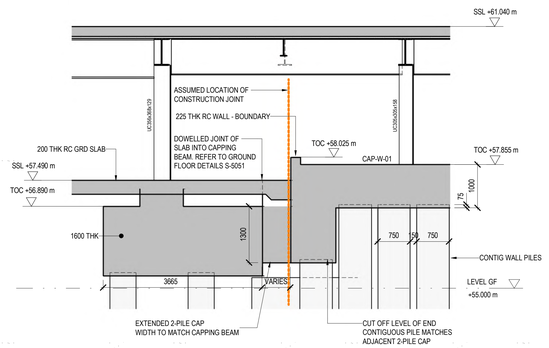

5 DET. REF. JOE MERCER WAY SECTION 5
SCALE 1 : 50

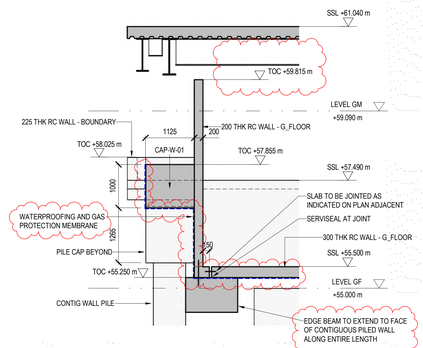

6 DET. REF. JOE MERCER WAY SECTION 6
SCALE 1 : 50

NOTE:

SECTIONS INDICATING JOE MERCER WAY EMBANKMENT ARE BASED ON BAM SURVEY INFORMATION RECEIVED 26/05/2020 WHICH COMPRISED 4No TRIAL PITS AND SURVEY OF THE EMBANKMENT PROFILE AT THESE POINTS.

FOR ACCESS AND MAINTENANCE STRATEGY FOR THE ADJACENT CRIB WALL STRUCTURE ALONG THE PROJECT WESTERN BOUNDARY, REFER TO ARCHITECTURAL DETAILS. FOR DRAINAGE DETAILS, REFER TO CIVIL ENGINEERING DRAWINGS.

A MINIMUM OFFSET FROM PILING WORKS TO THE EXISTING FOOTING OF 100mm HAS BEEN ESTABLISHED.

PILING CONTRACTOR TO EXPOSE AND IDENTIFY EXISTING STRUCTURE IN ADVANCE OF PILING AND SATISFY THEMSELVES THAT THEY CAN CARRY OUT THE WORKS WITHOUT DAMAGE TO EXISTING.

STEEL SUPERSTRUCTURE OUTSIDE OF THE BUILDING THERMAL LINE IS TO BE GALVANIZED SUITABLE FOR THE EXPOSURE CONDITIONS TO PROVIDE PROTECTION FOR THE ENTIRE LIFE OF THE BUILDING WITHOUT MAINTENANCE. REFER TO BH STEEL SPECIFICATION FOR FURTHER DETAILS.

All Rights reserved. Buro Happold and its group companies assert (unless otherwise agreed in writing) their rights under s.77 & 78 of the Copyright, Designs and Patents Act 1988.

DO NOT SCALE THIS DRAWING.

Suitability Code (as defined in ISO 19650-2:2018)

Work in Progress (WIP)
S0 - Initial Status

Shared (Non- Contractual)
S1 - Suitable for co-ordination
S2 - Suitable for information
S3 - Suitable for review & comment
S4 - Suitable for stage approval
S5 - Withdrawn
S6 - Suitable for PIM authorisation
S7 - Suitable for AIM authorisation

Published (Contractual)
A1, A2, A3, Etc - Authorised and accepted
B1,B2,B3, Etc, - Partial sign-off (with comments)

Published (AIM Acceptance)
CR - As constructed record document

SAFETY HEALTH AND ENVIRONMENTAL INFORMATION


IN ADDITION TO THE HAZARDS/RISKS NORMALLY ASSOCIATED WITH THE TYPES OF WORK DETAILED ON THIS DRAWING, NOTE THE FOLLOWING

CONSTRUCTION:
1. CONSTRUCTION OF L00 INVOLVES DEEP EXCAVATIONS IN MADE GROUND.
2. MADE GROUND ON SITE IS VERY DEEP AND CONTAMINATED WITH HYDROCARBONS.
3. RECORDS INDICATE 2No. CAPPED, WORKED COAL MINING SHAFTS ON SITE – REFER TO GEO INFORMATION FOR LOCATION.
4. SITE INVESTIGATION INDICATES NUMEROUS LARGE OBSTRUCTIONS BELOW GROUND INCLUDING CONCRETE FOUNDATIONS.
5. CONTRACTOR TO ENSURE TEMPORARY STABILITY OF ALL RETAINING WALLS DURING CONSTRUCTION. RETAINING WALL DESIGN RELIES ON PROVISION OF PROPPING PRIOR TO EXCAVATION VIA THE CAPPING BEAM TO BUTTRESS WALLS OR OTHER SUITABLE PROPS.

MAINTENANCE/CLEANING/OPERATION:
1. PERIMETER RETAINING WALLS RELY ON BUTTRESS WALLS FOR STABILITY.
2. ROOF TRUSSES ARE SEATED ON BEARINGS. DESIGN AND REPLACEMENT STRATEGY TO BE DEVELOPED WITH SPECIALIST SUPPLIER.

DECOMMISSIONING/DEMOLITION:
1. DESIGN LIFE OF THE BUILDING IS 50 YEARS.

Key Plan



Notes
1. FOR GENERAL NOTES REFER TO DRAWING BRA-BHE-XX-XX-DR-S-0001

2. THIS DRAWING IS TO BE READ IN CONJUNCTION WITH ALL RELEVANT ARCHITECTS AND ENGINEER'S DRAWINGS

3. REFERENCE SHALL BE MADE TO THE ARCHITECTS DRAWING FOR ALL SETTING OUT AND LEVEL INFORMATION.

4. CONCRETE GRADE C30/37

5. REINFORCEMENT DENOTED 'H' TO BE GRADE 500B OR 500C REINFORCING BARS IN ACCORDANCE WITH BS4449, YIELD STRENGTH = 500MPa

6. CONCRETE COVER TO ALL REINFORCEMENT
TOP = 50mm
SIDE = 50mm
BOTTOM = NOMINAL 75mm
UNLESS NOTED OTHERWISE

7. PILE EMBEDMENT INTO CAP = 75mm

8. FOR LIGHTNING PROTECTION REFER TO SUB CONTRACTOR SPECIALIST DETAILS.

9. COORDINATION WITH UPSTANDS AND LIFT DOOR THRESHOLDS, ADJACENT PITS, ADJACENT SLAB THICKENINGS/RECESSES WITH REQUIREMENTS FOR TWINWALL DETAILING ARE ALL TO BE COORDINATED BY CONTRACTOR.

11. ABBREVIATIONS
T1, T2 = TOP LAYER
B1, B2 = BOTTOM LAYER
NF = NEAR FACE
FF = FAR FACE
EF = EACH FACE
AP = ALTERNATELY PLACED

12. BAR CALL-UP: 3xBH25 - 200 - U-BARS (T1)
- MULTIPLE OF QUANTITY
- QUANTITY OF BAR
- BAR TYPE & SIZE
- SPACING
- ADDITIONAL INFO.

C04	THAT	13.08.2021	STAGE S4 APPROVAL (GROUND SLAB)
C03	THRM	17.06.2021	ISSUE FOR A4 AUTHORISED AND ACCEPTED
C02	FSiSO	26.04.2021	ISSUE FOR A4 AUTHORISED AND ACCEPTED
C01	THSO	15.03.2021	ISSUED FOR A4 AUTHORISED AND ACCEPTED
P02	THSO	15.02.2021	ISSUED FOR S3 REVIEW & COMMENT
P01	THSO	03.07.2020	STAGE 4A TENDER
Rev.	App/Chn	Date	Description

OVG INTERNATIONAL

BURO HAPPOLD

Camden Mill
Lower Bristol Road
Bath BA2 3DQ
UK

Tel: +44 (0)1225 320 600
Fax: +44 (0)8707 874 148
Email: BGEM1@burohappold.com
Web: www.burohappold.com

Co-op Live

title: SUBSTRUCTURE DETAIL SECTIONS SHEET 4

purpose of issue: **AUTHORISED & ACCEPTED**

scale 1 : 50 @ A0 | drawn SO | Job no. 0042841 | Suitability **A4**
date 04/02/20 | checked TH

reference | project code | originator | volume | level | type | role | number | rev.
BRA-BHE-XX-XX-DR-S-3504 **C04**

All Rights reserved. Buro Happold and its group companies assert (unless otherwise agreed in writing) their rights under s.77 & 83 of the Copyright, Designs and Patents Act 1988.

DO NOT SCALE THIS DRAWING.

Suitability Code (as defined in ISO 19650-2:2018)

Work in Progress (WIP)
S0 - Initial Status

Shared (Non- Contractual)
S1 - Suitable for co-ordination
S2 - Suitable for information
S3 - Suitable for review & comment
S4 - Suitable for stage approval
S5 - Withdrawn
S6 - Suitable for PIM authorisation
S7 - Suitable for AIM authorisation

Published (Contractual)
A1, A2, A3, Etc - Authorised and accepted
B1,B2,B3, Etc, - Partial sign-off (with comments)

Published (AIM Acceptance)
CR - As constructed record document

SAFETY HEALTH AND ENVIRONMENTAL INFORMATION

IN ADDITION TO THE HAZARDS/RISKS NORMALLY ASSOCIATED WITH THE TYPES OF WORK DETAILED ON THIS DRAWING, NOTE THE FOLLOWING

CONSTRUCTION:

1. CONSTRUCTION OF LSD INVOLVES DEEP EXCAVATIONS IN MADE GROUND. CONTRACTOR TO TAKE INTO ACCOUNT POTENTIAL REQUIREMENTS FOR DEWATERING OF EXCAVATIONS SHOULD PERCHED WATER BE ENCOUNTERED DURING SITE WORKS.
2. RECORDS INDICATE 2No. CAPPED, WORKED COAL MINING SHAFTS ON SITE. RECORD INFORMATION ON INVESTIGATION WORK INDICATES 1No. SHAFT LOCATED ON SITE THAT WAS NOT FOUND IN SITE INVESTIGATION WORKS. REFER TO LSD GEOMORPHOLOGY REPORT BRA-BHE-XX-XX-RP-CG-0001 AND INTERPRETATIVE REPORT BRA-BHE-XX-XX-RP-CG-0001 AND
3. CONTRACTOR TO ENSURE TEMPORARY STABILITY OF ALL RETAINING WALLS DURING CONSTRUCTION.
4. REFER TO REPORT 43X13208_R2_1.8V BAE SYSTEMS FOR RECOMMENDATIONS TO MITIGATE RISKS OF LSD. RECOMMENDATIONS INCLUDE STAFF TRAINING AND ECO ENGINEER ATTENDS SITE DURING LARGE-SCALE EXCAVATIONS IN MADE GROUND.


MAINTENANCE/CLEANING/OPERATION:

1. PERIMETER RETAINING WALLS BELOW GL ON BUTTRESS WALLS AND PERIMETER EDGE BEAMS AT GROUND LEVEL FOR STABILITY.
2. ROOF TRUSSES ARE SEATED ON BEARINGS. DESIGN AND REPLACEMENT STRATEGY TO BE DEVELOPED WITH SPECIALIST SUPPLIER.

DECOMMISSIONING/DEMOLITION:

1. DESIGN LIFE OF THE BUILDING IS 50 YEARS.
2. PILE DESIGN LIFE - 120 YEARS.
3. EXISTING LIU SEWER RUNS N-S THROUGH CENTRE OF SITE. CONTRACTOR TO ENSURE EXISTING LIU SEWER FULLY DECOMMISSIONED PRIOR TO COMMENCING WORKS ON AND SOUTH OF GRIDLINE CN.

Key Plan



Notes

1. THIS DRAWING TO BE READ IN CONJUNCTION WITH GENERAL NOTES ON BRA-BHE-XX-XX-DR-S-0001.

2. REFERENCE SHOULD BE MADE TO THE BASIS OF DESIGN REPORT, AND STRUCTURAL SPECIFICATIONS FOR KEY INFORMATION INCLUDING:
   A. LOADING ALLOWANCES
   B. REINFORCEMENT RATES
   C. MATERIAL SPECIFICATIONS
   D. COSTING NOTES FOR STRUCTURAL ELEMENTS FOR CONCRETE, STEELWORK AND FOUNDATIONS
   E. INFORMATION FOR PRECAST CONCRETE ELEMENTS TO THE BOWL AND RAKER STEELWORK

3. FOR INFORMATION ON PERIMETER RETAINING STRUCTURES, BASEMENT WATERPROOFING AND SITE CONSTAINTS, REFER TO THE FOUNDATION PLAN, TYPICAL SECTIONS AND COSTING REPORT.

4. REFER TO LATEST GEOTECHNICAL INFORMATION REGARDING THE SITE GEOLOGY AND GROUND CONDITIONS INCLUDING:
   - BRA-BHE-XX-XX-RP-CG-0001 GEOENVIRONMENTAL AND GEOTECHNICAL DESK STUDY
   - BRA-BHE-XX-XX-RP-CG-0004 GROUND ENGINEERING INTERPRETIVE REPORT
   - OVG Manchester Factual Report on Ground Investigation Report No. 765000-1 (04) March 2020)
   - BRA-BHE-XX-XX-RP-CG-0006 REMEDIATION STRATEGY

5. ALL CONSTRUCTION JOINTS WITHIN THE PERIMETER CONCRETE WALLS TO BE PROVIDED WITH HYDROPHYLIC STRIPS AND WATER BARS. CONSTRUCTION JOINTS TO BE PROVIDED AT APPROX. 10m CENTRES. REFER TO DRAWING S-5001 FOR FURTHER DETAILS

6. COLUMNS AND PLINTHS ARE CENTRED TO GRIDS U.N.O.

7. FOR BELOW GROUND DRAINAGE INFORMATION REFER TO CIVILS DRAWINGS.

8. RETRACTABLE SEATING AROUND EVENT FLOOR PERIMETER HAS VERY ONEROUS MOVEMENT LIMITS IN SERVICE. REFER TO BASIS OF DESIGN FOR THESE LIMITS. THE FINISHED SURFACE OF THE CONCRETE NEEDS TO BE PRODUCED TO SUIT THESE SPECIAL TOLERANCES.

9. SUBGRADE PREPARATION TO TRAFFICKED AREAS TO BE IN ACCORDANCE WITH THE BURO HAPPOLD EARTHWORKS AND CIVIL ENGINEERING SPECIFICATIONS. CRANE/PILING MAT TO BE RETAINED. CRANE/PILING MAT TO BE RETAINED. ALL SOFT SPOTS ARE TO BE REMOVED AND THE SUBGRADE SHALL BE COMPACTED TO SUIT THE REQUIREMENTS FOR VEHICULAR AREAS IN ACCORDANCE WITH THE BURO HAPPOLD CIVIL ENGINEERING AND EARTHWORKS SPECIFICATIONS

10. FOR EXISTING UTILITIES REFER TO RELEVANT CIVILS INFORMATION INCLUDING: BRA-BHE-XX-XX-DR-C-0020 EXISTING UTILITIES SHEET 1, BRA-BHE-XX-XX-DR-C-0021 EXISTING UTILITIES SHEET 2, BRA-BHE-XX-XX-DR-C-0022 EXISTING UTILITIES SHEET TRENCH.

P08	THAT	14.01.2022	STAGE 5A APPROVAL (PHASE 2 GF SLAB&OTHER UPDATES)
P07	THAT	10.12.2021	STAGE 5A APPROVAL (SUBSTR. UPDATES)
P06	THAT	03.12.2021	STAGE 5A APPROVAL (SUBSTRUCTURE UPDATES)
P05	THAT	26.11.2021	STAGE 5A APPROVAL (GF SLAB UPDATES)
P04	THAT	05.11.2021	STAGE 5A APPROVAL SUBSTR.UPDATES
P03	THAT	08.09.2021	STAGE 5A APPROVAL-SUBSTRUCTURE UPDATE
P02	THIRM	23.07.2021	STAGE 5A APPROVAL -FOUNDATIONS AND GENERAL UPDATES)
P01	THISO	03.07.2020	STAGE 4A TENDER
Rev	Appr/Drn	Date	Description

OVG INTERNATIONAL

BURO HAPPOLD

Camden Mill
Lower Bristol Road
Bath BA2 3DQ
UK

Tel: +44 (0)1225 320 600
Fax: +44 (0)8707 874 148
Email: 0042841@burohappold.com
Web: www.burohappold.com


Co-op Live

title LEVEL GF
ZONE A


purpose of issue
STAGE APPROVAL


scale 1 : 100 @ A0 | drawn RM | Job no. 0042841 | Suitability S4
date 10/09/19 | checked TH

reference | project code | originator | volume | level | type | role | number | rev
BRA-BHE-ZA-GF-DR-S-1001 | **P08**

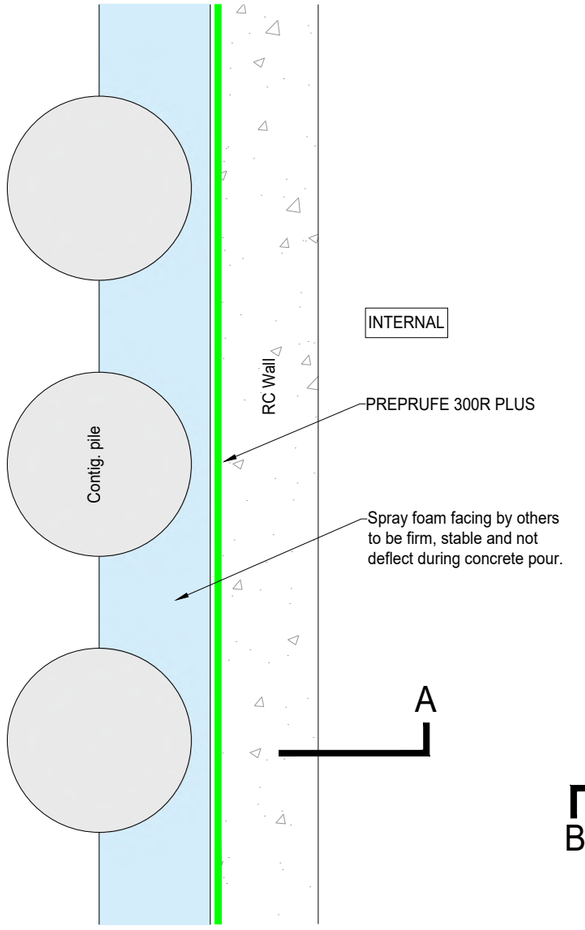


BUILD UP AT PILED WALL
Plan Section B

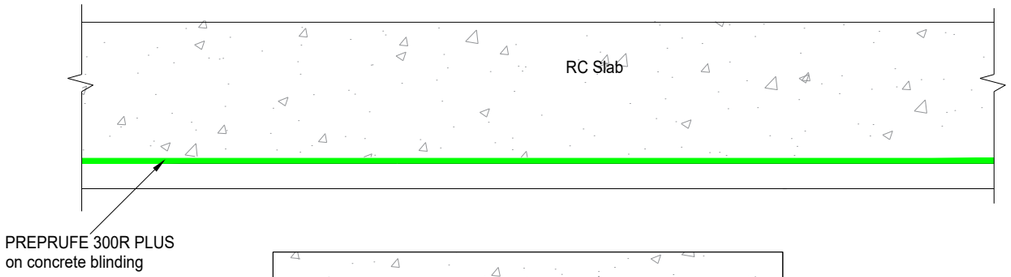



SECTION C
GROUND BEAM

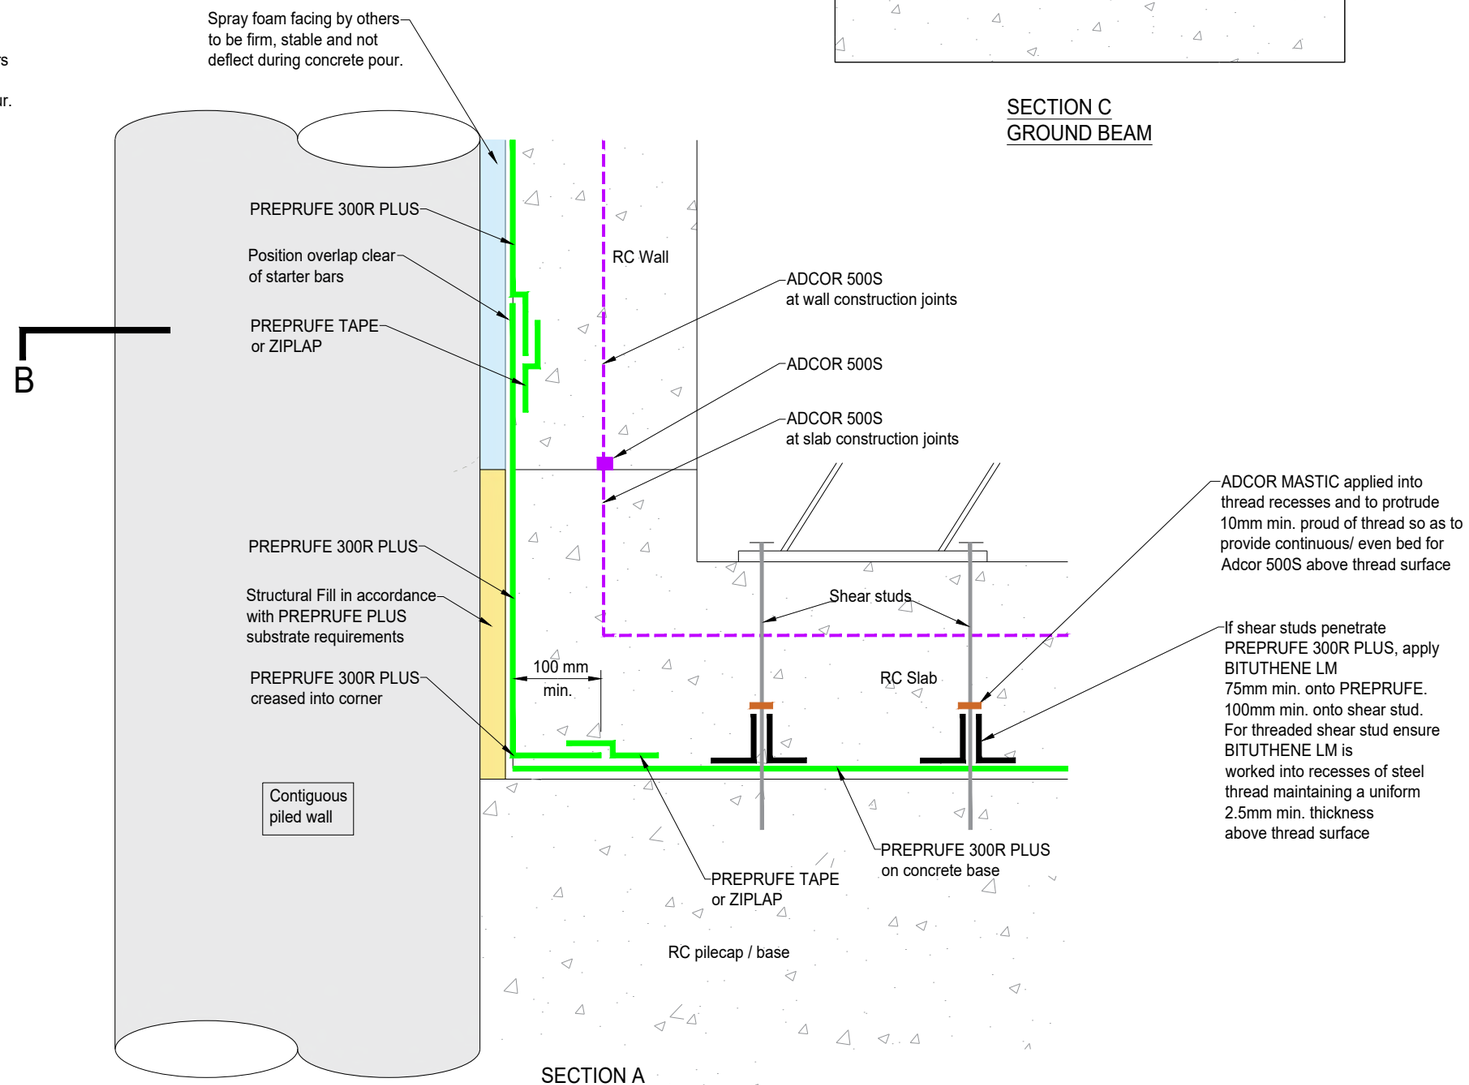

SECTION A
SLAB / WALL INTERFACE

General Notes & Guidance:

For those third parties responsible for the design of the waterproofing system, such parties must ensure the proposed system and details shown herein are brought to the attention of those responsible for the overall design of the structure, to ensure compatibility of the waterproofing system and detailing with all elements of the structural design. Final decisions, acceptance and any recommendations must be approved in writing between such responsible parties.

For product installation, this drawing is to be read in conjunction with all relevant product data sheets and application guidelines.

Drawing Notes:

Project: CO-OP LIVE

Title: WATERPROOFING DETAILS

Drawing Status: FOR CONSTRUCTION | Status: A1

gcp applied technologies

GCP APPLIED TECHNOLOGIES
487/488 Ipswich Road, Slough, Berkshire, SL1 4EP, UK

T: +44 (0)1753 490000
E: info-gb@gcpat.com
W: www.gcpat.com

ADCOR, ADPRUFE, AEROFIL, ARMOURTAPE, AQUATEK, BETEC, BENTORUB, BITUSHIELD, BITUSTIK, BITUTHENE, COLFLEX, DECSEAL, ELIMINATOR, HYDRODUCT, INTEGRITANK, METASET, MS FIXER, OMNITEK, PAK ADHESIVE, PERM-A-BARRIER, PERMARE, PREPRUFE, PREPRUFE PLUS, PVC EDGETIE, RE-INJECTO, SENTINEL, SERVIDEK, SERVIPAK, SERVIRUFE, SERVISEAL, SERVITAPE, SERVITITE, SILCOR, SLIPSTRIP, ZIPLAP and GCP APPLIED TECHNOLOGIES are trademarks which may be registered in the United States and/ or other countries, of GCP Applied Technologies Inc. This trademark list has been compiled using available published information as of the publication date and may not accurately reflect current trademark ownership or status. These products may be covered by patents or patents pending.

This drawing is Copyright 2021 of GCP Applied Technologies. Permission for copying is granted only to employees, authorised representatives, customers, and specifiers to support the sale or use of GCP Applied Technologies products. All other rights are reserved.

Project: CO-OP LIVE MANCHESTER

Client: BAM - CAREYS


Title: DETAIL DRAWING
GCP PRODUCT APPLICATION TECHNIQUES

Information Container Name: BRA-CCE-ZZ-ZZ-DR-Y-16101


Date:	Scale	Paper Size	Drawn:	Checked:
17-03-21	NTS	A3	TG	RH/LC

GCP Project Ref: D20046


Rev: C02

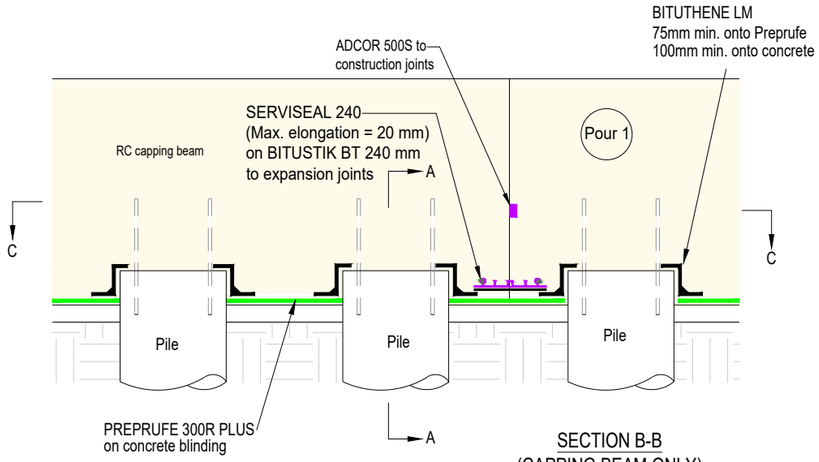


SECTION B-B
(CAPPING BEAM ONLY)

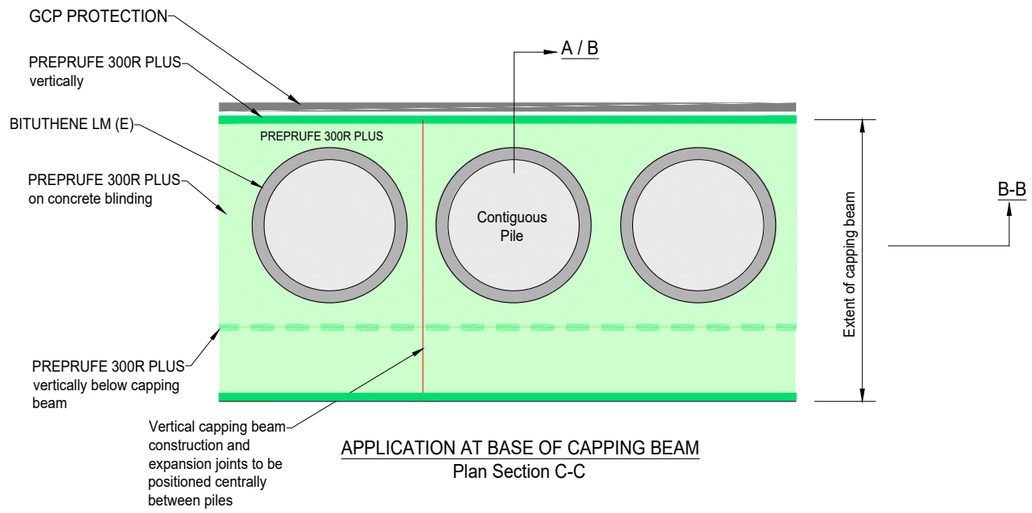

APPLICATION AT BASE OF CAPPING BEAM
Plan Section C-C

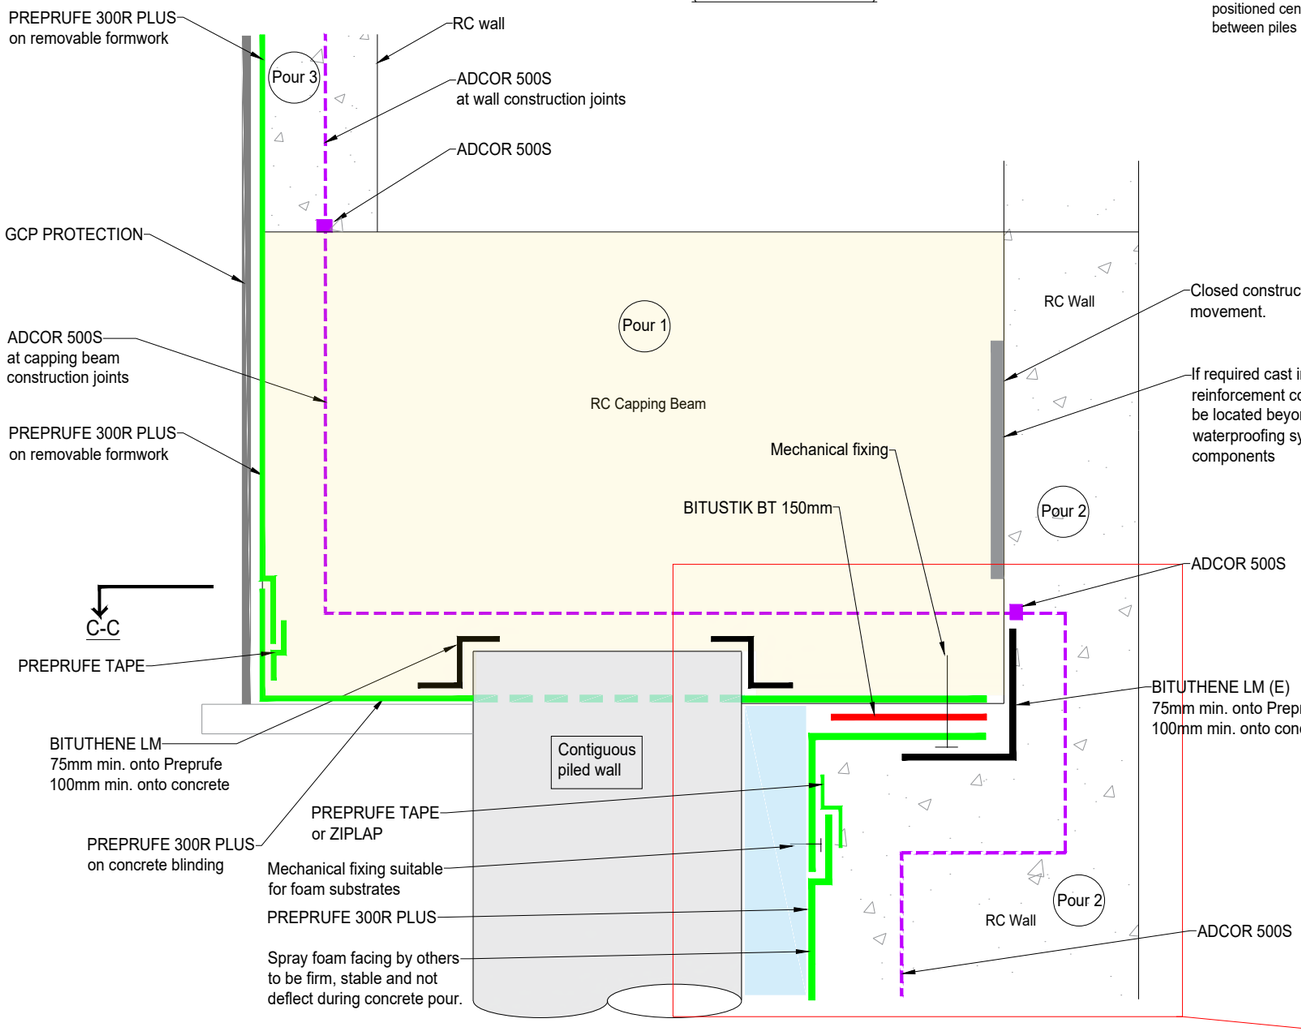

SECTION A
CAPPING BEAM AT PILE LOCATIONS
Section

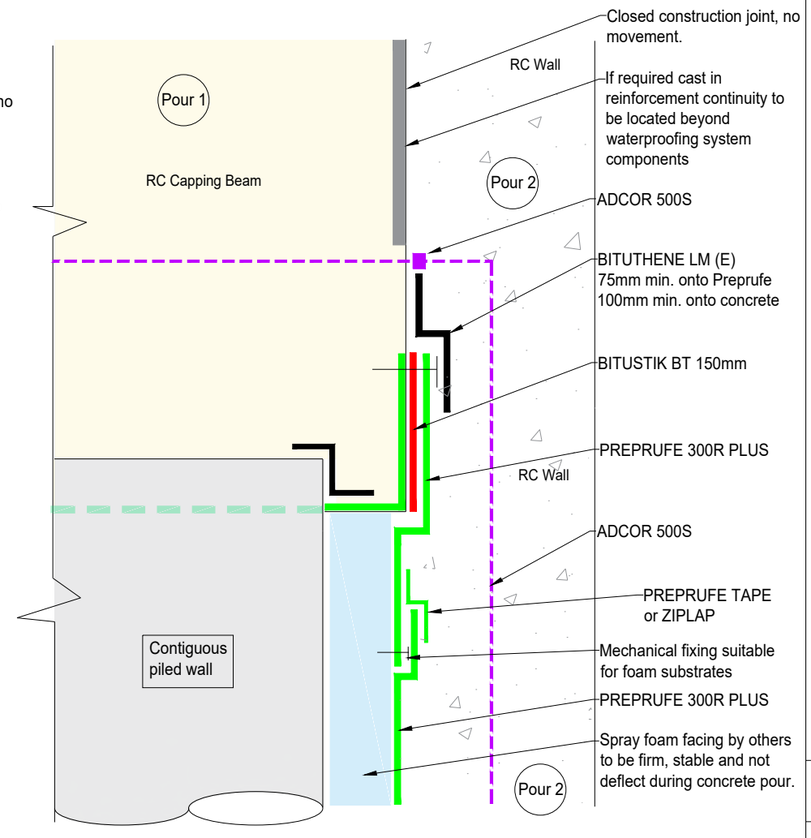

ALTERNATIVE (SECTION B)
CAPPING BEAM AT PILE LOCATIONS
Section

General Notes & Guidance:

For those third parties responsible for the design of the waterproofing system, such parties must ensure the proposed system and details shown herein are brought to the attention of those responsible for the overall design of the structure, to ensure compatibility of the waterproofing system and detailing with all elements of the structural design. Final decisions, acceptance and any recommendations must be approved in writing between such responsible parties.

For product installation, this drawing is to be read in conjunction with all relevant product data sheets and application guidelines.

Drawing Notes:

The building designer or third party responsible for the water / gas-proofing should satisfy themselves that water or gas cannot enter the protected structure by bypassing the detailed GCP system.

Project: CO-OP LIVE

Title: WATERPROOFING DETAILS

Drawing Status: FOR CONSTRUCTION | Status: A1

gcp applied technologies

GCP APPLIED TECHNOLOGIES
487/488 Ipswich Road, Slough,
Berkshire, SL1 4EP, UK

T: +44 (0)1753 490000
E: info-gb@gcpat.com
W: www.gcpat.com

ADCOR, ADPRUFE, AEROFIL, ARMOURTAPE, AQUATEK, BETEC, BENTORUB, BITUSHIELD, BITUSTIK, BITUTHENE, COLFLEX, DECSEAL, ELIMINATOR, HYDRODUCT, INTEGRITANK, METASET, MS FIXER, OMNITEK, PAK ADHESIVE, PERM-A-BARRIER, PERMARE, PREPRUFE, PREPRUFE PLUS, PVC EDGETIE, RE-INJECTO, SENTINEL, SERVIDEK, SERVIPAK, SERVIRUFE, SERVISEAL, SERVITAPE, SERVITITE, SILCOR, SLIPSTRIP, ZIPLAP and GCP APPLIED TECHNOLOGIES are trademarks which may be registered in the United States and/ or other countries, of GCP Applied Technologies Inc. This trademark list has been compiled using available published information as of the publication date and may not accurately reflect current trademark ownership or status. These products may be covered by patents or patents pending.

This drawing is Copyright 2021 of GCP Applied Technologies. Permission for copying is granted only to employees, authorised representatives, customers, and specifiers to support the sale or use of GCP Applied Technologies products. All other rights are reserved.

Project: CO-OP LIVE MANCHESTER

Client: BAM - CAREYS


Title: DETAIL DRAWING
GCP PRODUCT APPLICATION TECHNIQUES

Information Container Name: BRA-CCE-ZZ-ZZ-DR-Y-16102

Date:	Scale	Paper Size	Drawn:	Checked:
17-03-21	NTS	A3	TG	RH/LC

GCP Project Ref: D20046

Rev: C01

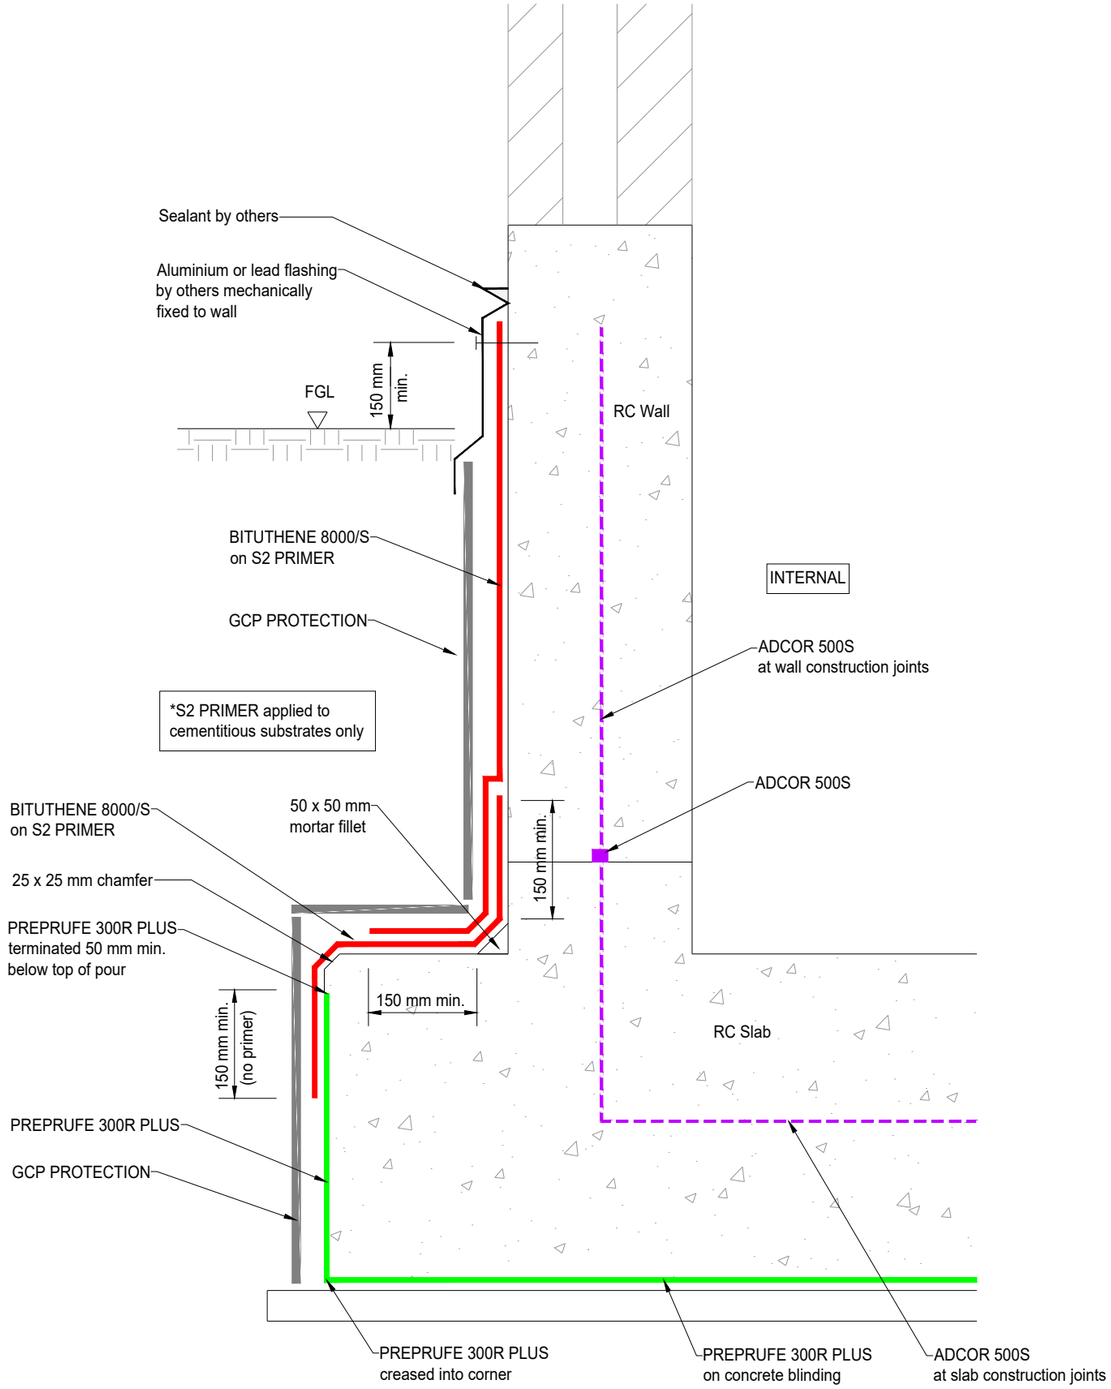

SLAB / WALL INTERFACE WITH TOE
Section

General Notes & Guidance:

For those third parties responsible for the design of the waterproofing system, such parties must ensure the proposed system and details shown herein are brought to the attention of those responsible for the overall design of the structure, to ensure compatibility of the waterproofing system and detailing with all elements of the structural design. Final decisions, acceptance and any recommendations must be approved in writing between such responsible parties.

For product installation, this drawing is to be read in conjunction with all relevant product data sheets and application guidelines.

Drawing Notes:

Project: CO-OP LIVE

Title: WATERPROOFING DETAILS

Drawing Status: FOR CONSTRUCTION | Status: A1

gcp applied technologies

GCP APPLIED TECHNOLOGIES
487/488 Ipswich Road, Slough, Berkshire, SL1 4EP, UK

T: +44 (0)1753 490000
E: info-gb@gcpat.com
W: www.gcpat.com

ADCOR, ADPRUFE, AEROFIL, ARMOURTAPE, AQUATEK, BETEC, BENTORUB, BITUSHIELD, BITUSTIK, BITUTHENE, COLFLEX, DECSEAL, ELIMINATOR, HYDRODUCT, INTEGRITANK, METASET, MS FIXER, OMNITEK, PAK ADHESIVE, PERM-A-BARRIER, PERMARE, PREPRUFE, PREPRUFE PLUS, PVC EDGETIE, RE-INJECTO, SENTINEL, SERVIDEK, SERVIPAK, SERVIRUFE, SERVISEAL, SERVITAPE, SERVITITE, SILCOR, SLIPSTRIP, ZIPLAP and GCP APPLIED TECHNOLOGIES are trademarks which may be registered in the United States and/ or other countries, of GCP Applied Technologies Inc. This trademark list has been compiled using available published information as of the publication date and may not accurately reflect current trademark ownership or status. These products may be covered by patents or patents pending.

This drawing is Copyright 2021 of GCP Applied Technologies. Permission for copying is granted only to employees, authorised representatives, customers, and specifiers to support the sale or use of GCP Applied Technologies products. All other rights are reserved.

Project: CO-OP LIVE MANCHESTER

Client: BAM - CAREYS


Title: DETAIL DRAWING
GCP PRODUCT APPLICATION TECHNIQUES

Information Container Name: BRA-CCE-ZZ-ZZ-DR-Y-16104


Date:	Scale	Paper Size	Drawn:	Checked:
17-03-21	NTS	A3	TG	RH/LC

GCP Project Ref: D20046


Rev: C01

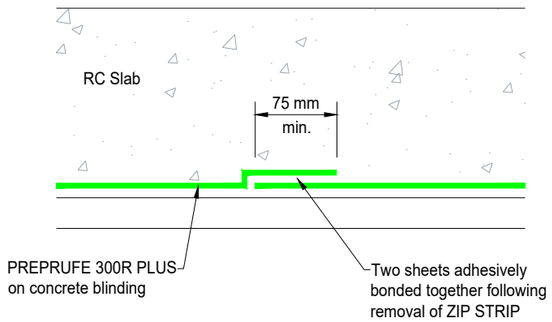


OVERLAP ALONG ZIPLAP
Horizontal Installation
Section

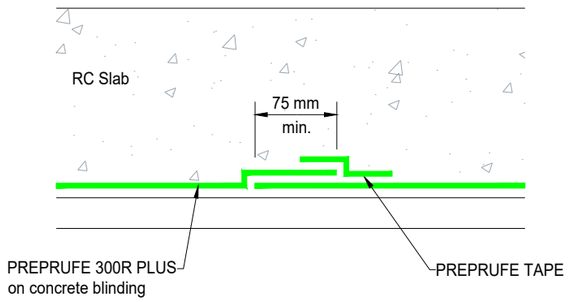


OVERLAP AT END / CUT EDGES
Horizontal Installation
Section

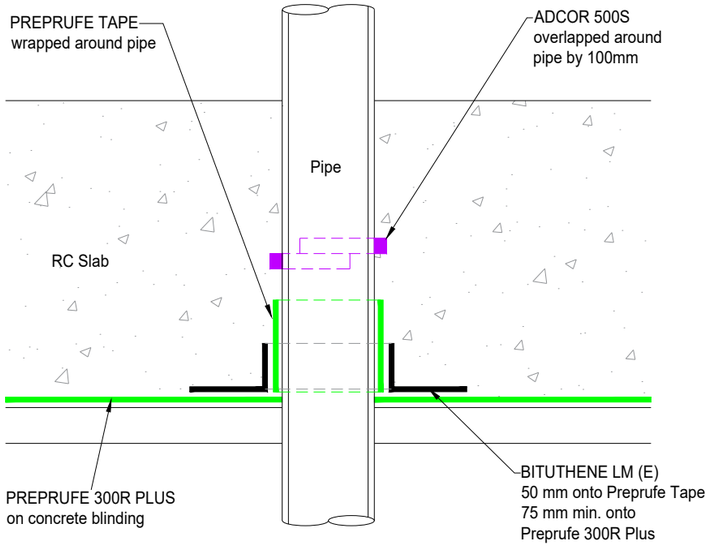


PIPE PENETRATION THROUGH SLAB
Section

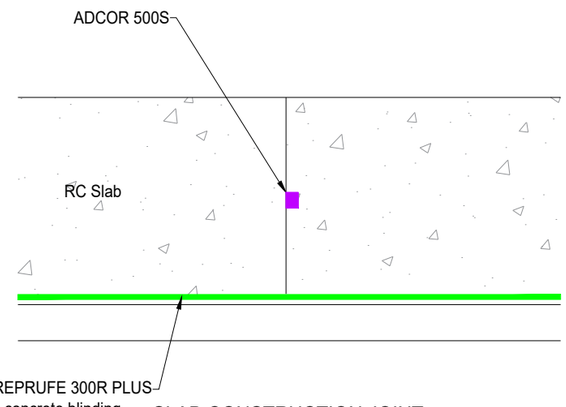


SLAB CONSTRUCTION JOINT
Section

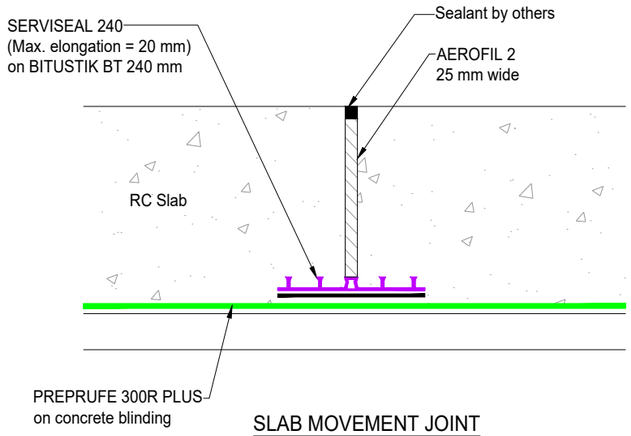


SLAB MOVEMENT JOINT
Section

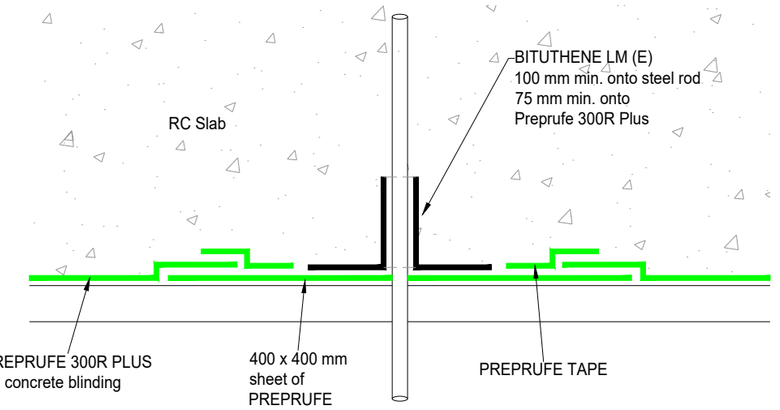

STEEL ROD PENETRATION THROUGH SLAB
Section

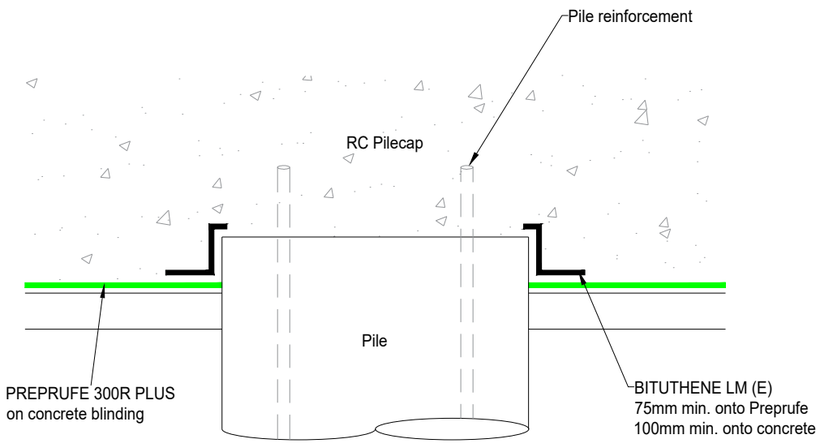

PILE HEAD
Section

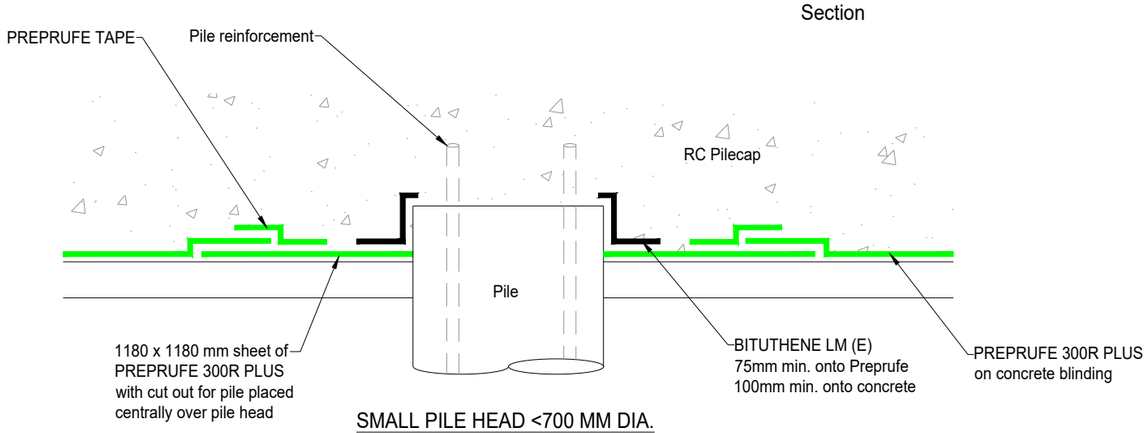

SMALL PILE HEAD <700 MM DIA.
Section

General Notes & Guidance:

For those third parties responsible for the design of the waterproofing system, such parties must ensure the proposed system and details shown herein are brought to the attention of those responsible for the overall design of the structure, to ensure compatibility of the waterproofing system and detailing with all elements of the structural design. Final decisions, acceptance and any recommendations must be approved in writing between such responsible parties.

For product installation, this drawing is to be read in conjunction with all relevant product data sheets and application guidelines.

Drawing Notes:

Project: CO-OP LIVE

Title: WATERPROOFING DETAILS

Drawing Status: FOR CONSTRUCTION | Status: A1

gcp applied technologies

GCP APPLIED TECHNOLOGIES
487/488 Ipswich Road, Slough,
Berkshire, SL1 4EP, UK

T: +44 (0)1753 490000
E: info-gb@gcpat.com
W: www.gcpat.com

ADCOR, ADPRUFE, AEROFIL, ARMOURTAPE, AQUATEK, BETEC, BENTORUB, BITUSHIELD, BITUSTIK, BITUTHENE, COLFLEX, DECSEAL, ELIMINATOR, HYDRODUCT, INTEGRITANK, METASET, MS FIXER, OMNITEK, PAK ADHESIVE, PERM-A-BARRIER, PERMARE, PREPRUFE, PREPRUFE PLUS, PVC EDGETIE, RE-INJECTO, SENTINEL, SERVIDEK, SERVIPAK, SERVIRUFE, SERVISEAL, SERVITAPE, SERVITITE, SILCOR, SLIPSTRIP, ZIPLAP and GCP APPLIED TECHNOLOGIES are trademarks which may be registered in the United States and/ or other countries, of GCP Applied Technologies Inc. This trademark list has been compiled using available published information as of the publication date and may not accurately reflect current trademark ownership or status. These products may be covered by patents or patents pending.

This drawing is Copyright 2021 of GCP Applied Technologies. Permission for copying is granted only to employees, authorised representatives, customers, and specifiers to support the sale or use of GCP Applied Technologies products. All other rights are reserved.

Project: CO-OP LIVE MANCHESTER

Client: BAM - CAREYS


Title: DETAIL DRAWING
GCP PRODUCT APPLICATION TECHNIQUES

Information Container Name: BRA-CCE-ZZ-ZZ-DR-Y-16106


Date:	Scale	Paper Size	Drawn:	Checked:
17-03-21	NTS	A3	TG	RH/LC

GCP Project Ref: D20046


Rev: C01

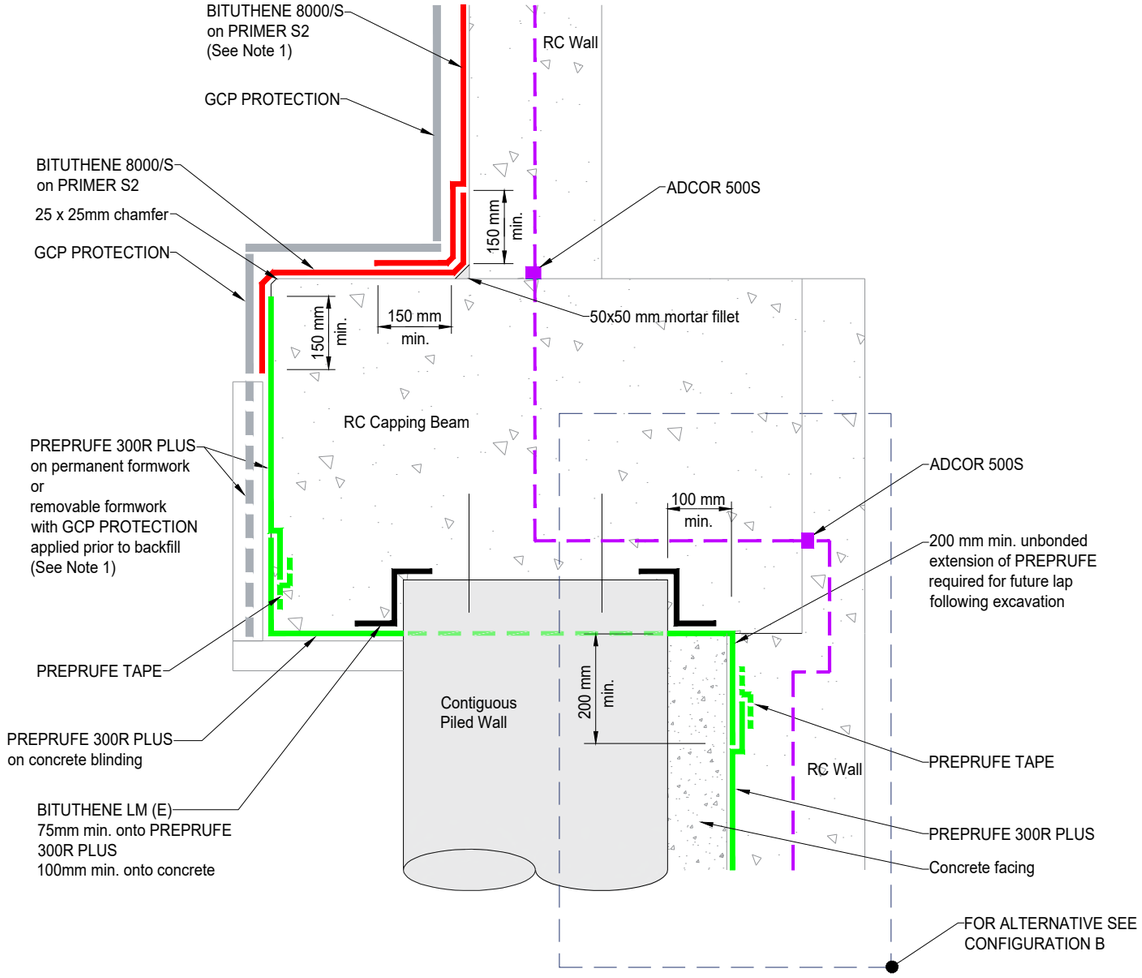

CAPPING BEAM - PREPRUFE 300R PLUS - CONFIGURATION A
Section

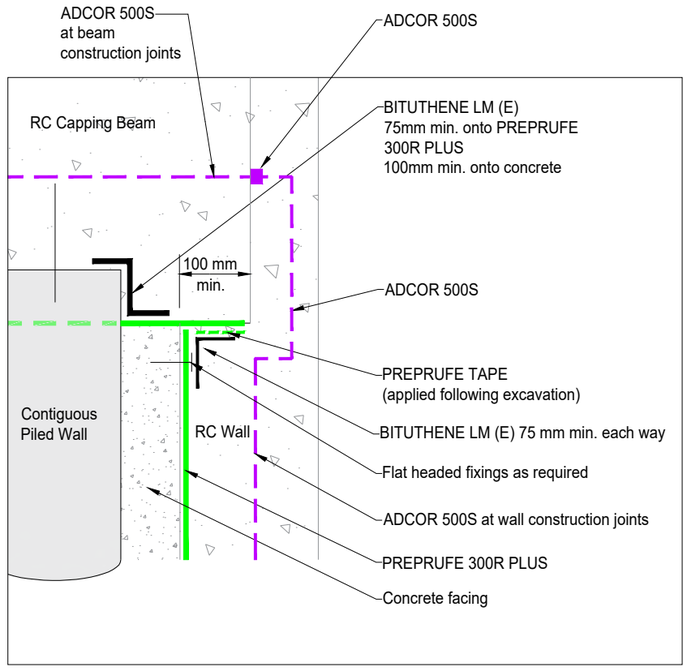

CAPPING BEAM - PREPRUFE 300R PLUS - CONFIGURATION B
Section

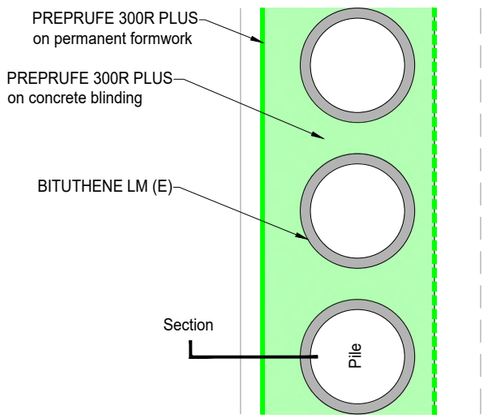

APPLICATION AROUND PILE HEADS
Plan Section

General Notes & Guidance:

For those third parties responsible for the design of the waterproofing system, such parties must ensure the proposed system and details shown herein are brought to the attention of those responsible for the overall design of the structure, to ensure compatibility of the waterproofing system and detailing with all elements of the structural design. Final decisions, acceptance and any recommendations must be approved in writing between such responsible parties.

For product installation, this drawing is to be read in conjunction with all relevant product data sheets and application guidelines.

Drawing Notes:

THIS DRAWING IS TO BE READ IN CONJUNCTION WITH ALL OTHER GCP WATERPROOFING DRAWINGS.

Details drawn for clarity - (Not To Scale)

Note 1
Bituthene 8000 to be used in below ground areas only, above ground waterproofing to be determined.

The building designer or third party responsible for the water / gas-proofing should satisfy themselves that water or gas cannot enter the protected structure by bypassing the detailed GCP system.

gcp applied technologies

GCP APPLIED TECHNOLOGIES
487/488 Ipswich Road, Slough,
Berkshire, SL1 4EP, UK

T: +44 (0)1753 490000
E: info-gb@gcpat.com
W: www.gcpat.com

ADCOR, ADPRUFE, AEROFIL, ARMOURTAPE, AQUATEK, BETEC, BENTORUB, BITUSHIELD, BITUSTIK, BITUTHENE, COLFLEX, DECSEAL, ELIMINATOR, HYDRODUCT, INTEGRITANK, METASET, MS FIXER, OMNITEK, PAK ADHESIVE, PERM-A-BARRIER, PERMARE, PREPRUFE, PREPRUFE PLUS, PVC EDGETIE, RE-INJECTO, SENTINEL, SERVIDEK, SERVIPAK, SERVIRUFE, SERVISEAL, SERVITAPE, SERVITITE, SILCOR, SLIPSTRIP, ZIPLAP and GCP APPLIED TECHNOLOGIES are trademarks which may be registered in the United States and/ or other countries, of GCP Applied Technologies Inc. This trademark list has been compiled using available published information as of the publication date and may not accurately reflect current trademark ownership or status. These products may be covered by patents or patents pending.


This drawing is Copyright 2021 of GCP Applied Technologies. Permission for copying is granted only to employees, authorised representatives, customers, and specifiers to support the sale or use of GCP Applied Technologies products. All other rights are reserved.

Project:	CO-OP LIVE MANCHESTER
Client:	BAM - CAREYS
Title:	DETAIL DRAWING GCP PRODUCT APPLICATION TECHNIQUES


Project:	CO-OP LIVE
Title:	WATERPROOFING DETAILS
Drawing Status:	FOR COMMENT / APPROVAL
Status:	S3
Information Container Name:	BRA-CCE-ZZ-ZZ-DR-Y-16126

Date:	Scale	Paper Size	Drawn:	Checked:
22-06-21	NTS	A3	TG	RH/LC

GCP Project Ref:		Rev:
D20046		P01

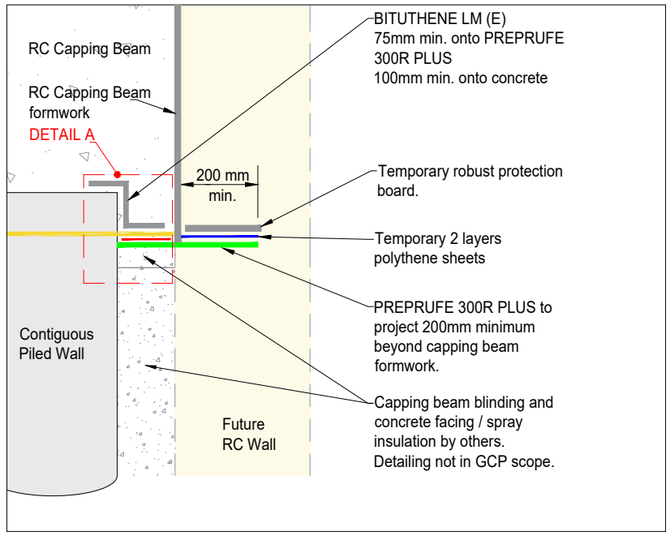


STAGE 1 - CAPPING BEAM - PREPRUFE 300R PLUS
Section

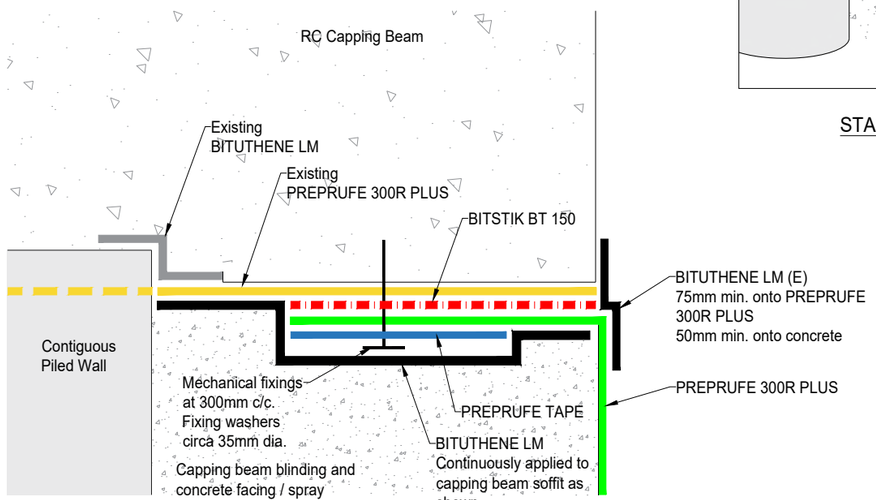


DETAIL A
Section
REMEDIAL DETAIL - PREPRUFE
WESTERN CAPPING BEAM

Best that can be achieved under the circumstances.
Building design team to determine practical installation method.

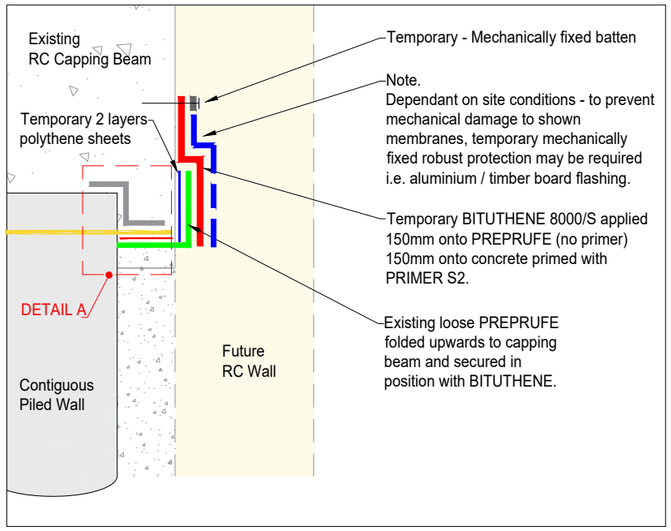


STAGE 2 - CAPPING BEAM - PREPRUFE 300R PLUS
Section

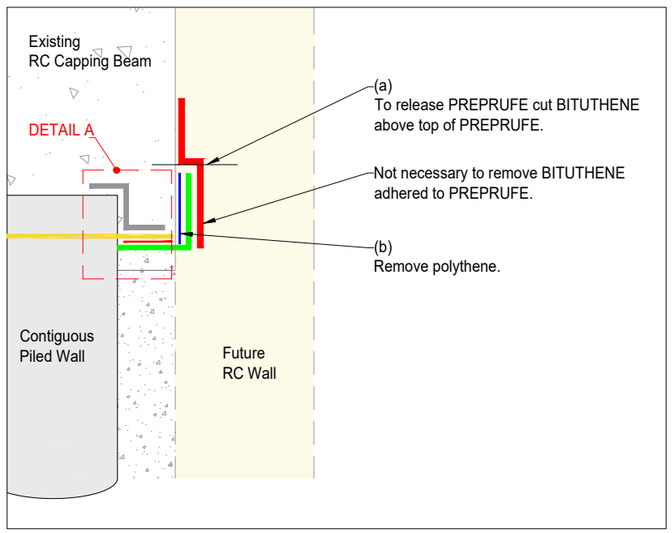

STAGE 3 - CAPPING BEAM - PREPRUFE 300R PLUS
Section

PRELIMINARY
FOR BUILDING DESIGN TEAM REVIEW

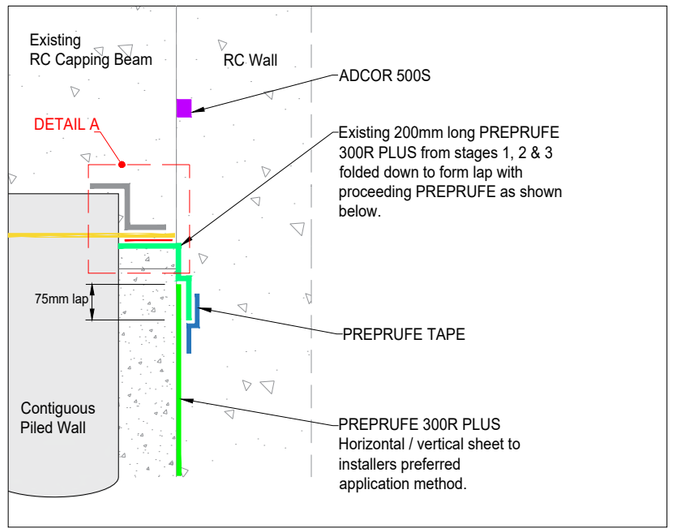

STAGE 4 - CAPPING BEAM - PREPRUFE 300R PLUS
Section

General Notes & Guidance:

For those third parties responsible for the design of the waterproofing system, such parties must ensure the proposed system and details shown herein are brought to the attention of those responsible for the overall design of the structure, to ensure compatibility of the waterproofing system and detailing with all elements of the structural design. Final decisions, acceptance and any recommendations must be approved in writing between such responsible parties.

For product installation, this drawing is to be read in conjunction with all relevant product data sheets and application guidelines.

Drawing Notes:

THIS DRAWING IS TO BE READ IN CONJUNCTION WITH ALL OTHER GCP WATERPROOFING DRAWINGS.

Details drawn for clarity - (Not To Scale).

gcp applied technologies

GCP APPLIED TECHNOLOGIES
487/488 Ipswich Road, Slough, Berkshire, SL1 4EP, UK

T: +44 (0)1753 490000
E: info-gb@gcpat.com
W: www.gcpat.com

ADCOR, ADPRUFE, AEROFIL, ARMOURTAPE, AQUATEK, BETEC, BENTORUB, BITUSHIELD, BITUSTIK, BITUTHENE, COLFLEX, DECSEAL, ELIMINATOR, HYDRODUCT, INTEGRITANK, METASET, MS FIXER, OMNITEK, PAK ADHESIVE, PERM-A-BARRIER, PERMARE, PREPRUFE, PREPRUFE PLUS, PVC EDGETIE, RE-INJECTO, SENTINEL, SERVIDEK, SERVIPAK, SERVIRUFE, SERVISEAL, SERVITAPE, SERVITITE, SILCOR, SLIPSTRIP, ZIPLAP and GCP APPLIED TECHNOLOGIES are trademarks which may be registered in the United States and/ or other countries, of GCP Applied Technologies Inc. This trademark list has been compiled using available published information as of the publication date and may not accurately reflect current trademark ownership or status. These products may be covered by patents or patents pending.


This drawing is Copyright 2021 of GCP Applied Technologies. Permission for copying is granted only to employees, authorised representatives, customers, and specifiers to support the sale or use of GCP Applied Technologies products. All other rights are reserved.

Project: CO-OP LIVE MANCHESTER
Client: BAM - CAREYS
Title: DETAIL DRAWING
GCP PRODUCT APPLICATION TECHNIQUES


Project: CO-OP LIVE
Title: WATERPROOFING DETAILS
Drawing Status: FOR COMMENT / APPROVAL
Status: S3
Information Container Name: BRA-CCE-ZZ-ZZ-DR-Y-16142

Date:	Scale	Paper Size	Drawn:	Checked:
12-10-21	NTS	A3	TG	


GCP Project Ref:	Rev:
D20046	P01

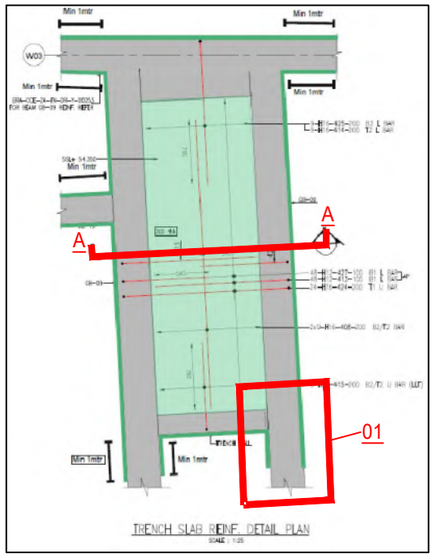

Plan structural arrangement extracted
from BRA-CCE-ZD-FN-DR-Y-00256

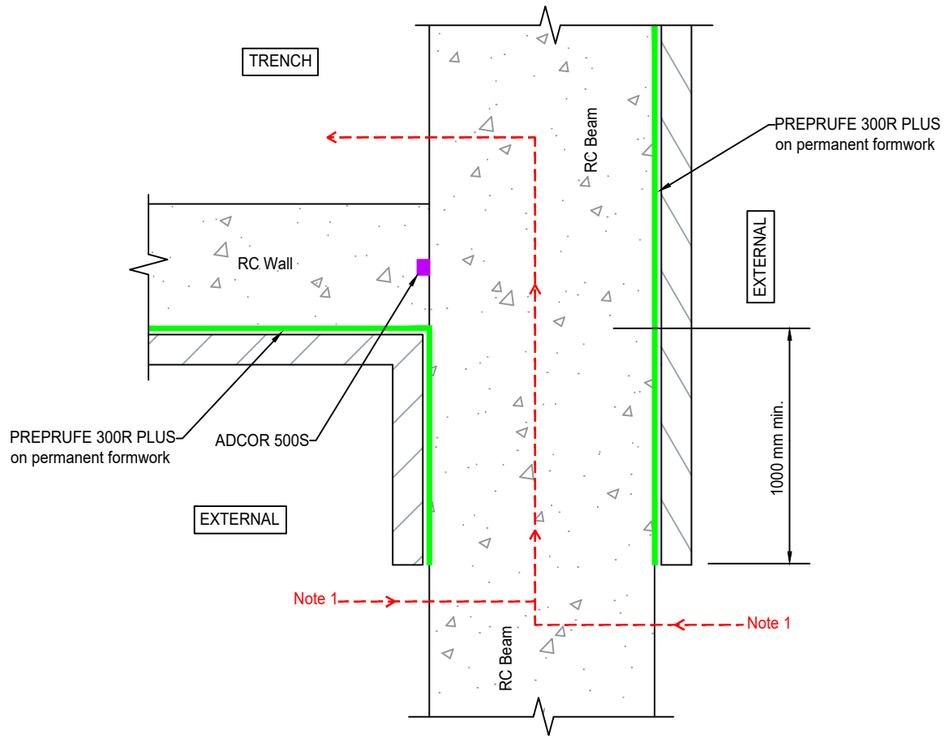

DETAIL 01
Plan Section

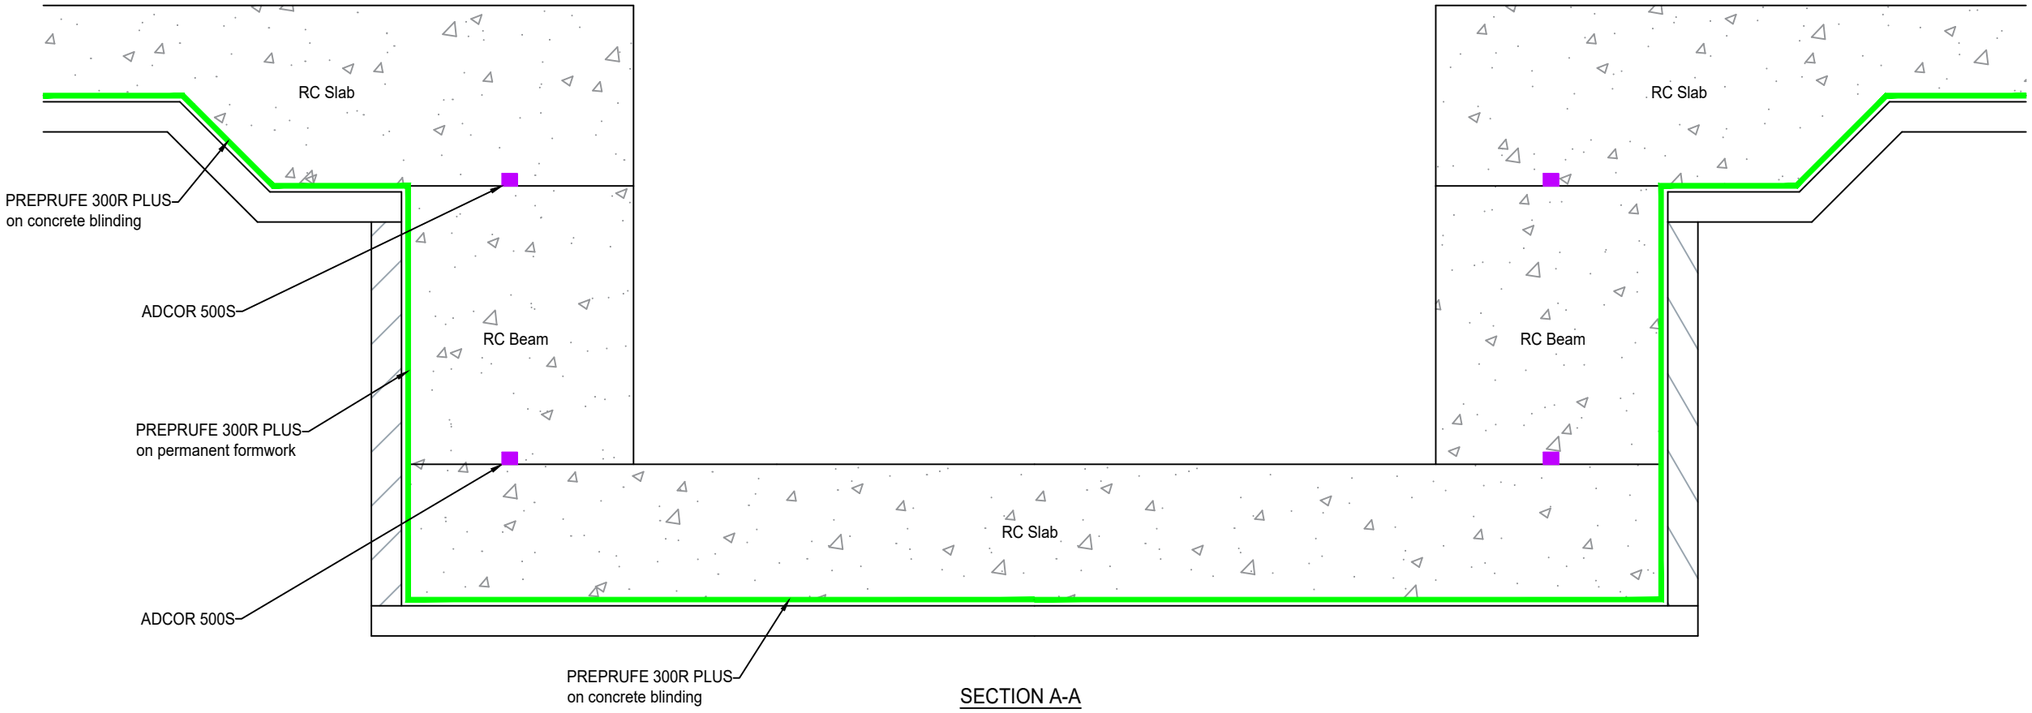

SECTION A-A

General Notes & Guidance:

For those third parties responsible for the design of the waterproofing system, such parties must ensure the proposed system and details shown herein are brought to the attention of those responsible for the overall design of the structure, to ensure compatibility of the waterproofing system and detailing with all elements of the structural design. Final decisions, acceptance and any recommendations must be approved in writing between such responsible parties.

For product installation, this drawing is to be read in conjunction with all relevant product data sheets and application guidelines.

Drawing Notes:

Note *01
Gas and water protection relies on the design and performance of the concrete and construction joints in this zone, not in GCP scope.

gcp applied technologies

GCP APPLIED TECHNOLOGIES
487/488 Ipswich Road, Slough,
Berkshire, SL1 4EP, UK

T: +44 (0)1753 490000
E: info-gb@gcpat.com
W: www.gcpat.com


ADCOR, ADPRUFE, AEROFIL, ARMOURTAPE, AQUATEK, BETEC, BENTORUB, BITUSHIELD, BITUSTIK, BITUTHENE, COLFLEX, DECSEAL, ELIMINATOR, HYDRODUCT, INTEGRITANK, METASET, MS FIXER, OMNITEK, PAK ADHESIVE, PERM-A-BARRIER, PERMARE, PREPRUFE, PREPRUFE PLUS, PVC EDGETIE, RE-INJECTO, SENTINEL, SERVIDEK, SERVIPAK, SERVIRUFE, SERVISEAL, SERVITAPE, SERVITITE, SILCOR, SLIPSTRIP, ZIPLAP and GCP APPLIED TECHNOLOGIES are trademarks which may be registered in the United States and/ or other countries, of GCP Applied Technologies Inc. This trademark list has been compiled using available published information as of the publication date and may not accurately reflect current trademark ownership or status. These products may be covered by patents or patents pending.

This drawing is Copyright 2021 of GCP Applied Technologies. Permission for copying is granted only to employees, authorised representatives, customers, and specifiers to support the sale or use of GCP Applied Technologies products. All other rights are reserved.


Project:	CO-OP LIVE MANCHESTER
Client:	BAM - CAREYS
Title:	DETAIL DRAWING GCP PRODUCT APPLICATION TECHNIQUES

Information Container Name:					
BRA-CCE-ZZ-ZZ-DR-Y-16144					
Date:	Scale	Paper Size	Drawn:	Checked:	
15-11-2021	NTS	A3	DMC	LC	
GCP Project Ref:				Rev:	
D20046				P02	

Project:	CO-OP LIVE
Title:	WATERPROOFING DETAILS
Drawing Status:	FOR COMMENT / APPROVAL
Status:	S3

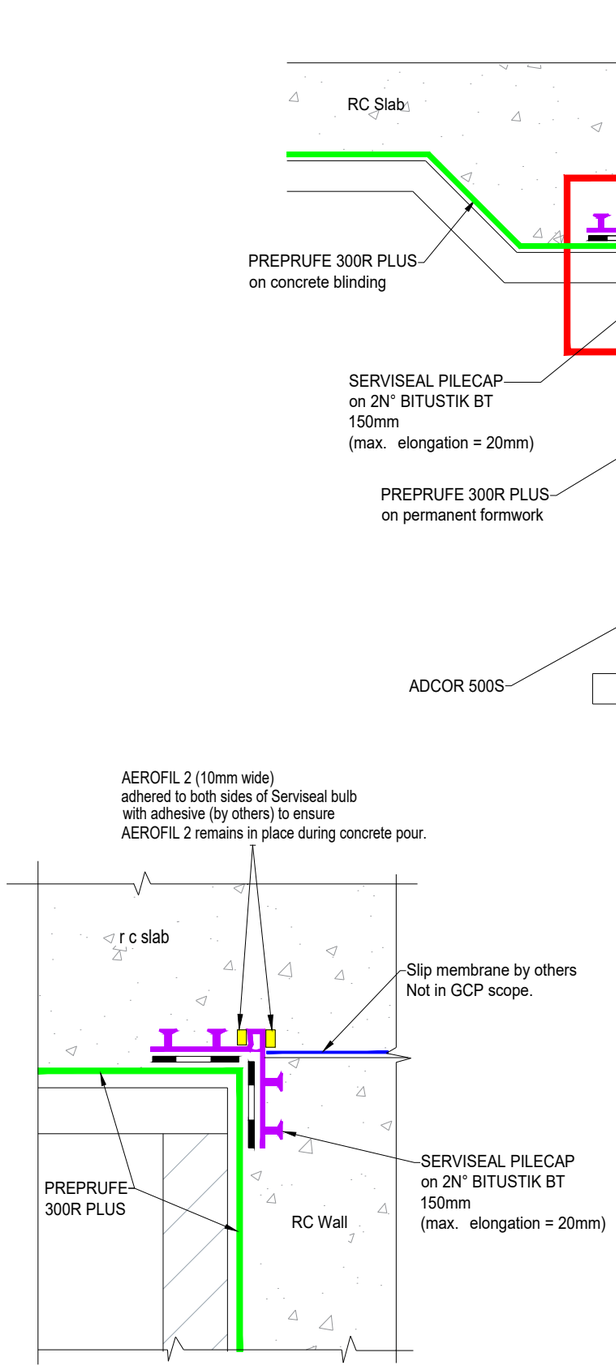

DETAIL 01
RC SLAB WALL SLIP / EXPANSION JOINT
Max. Elongation = 20 mm
Section

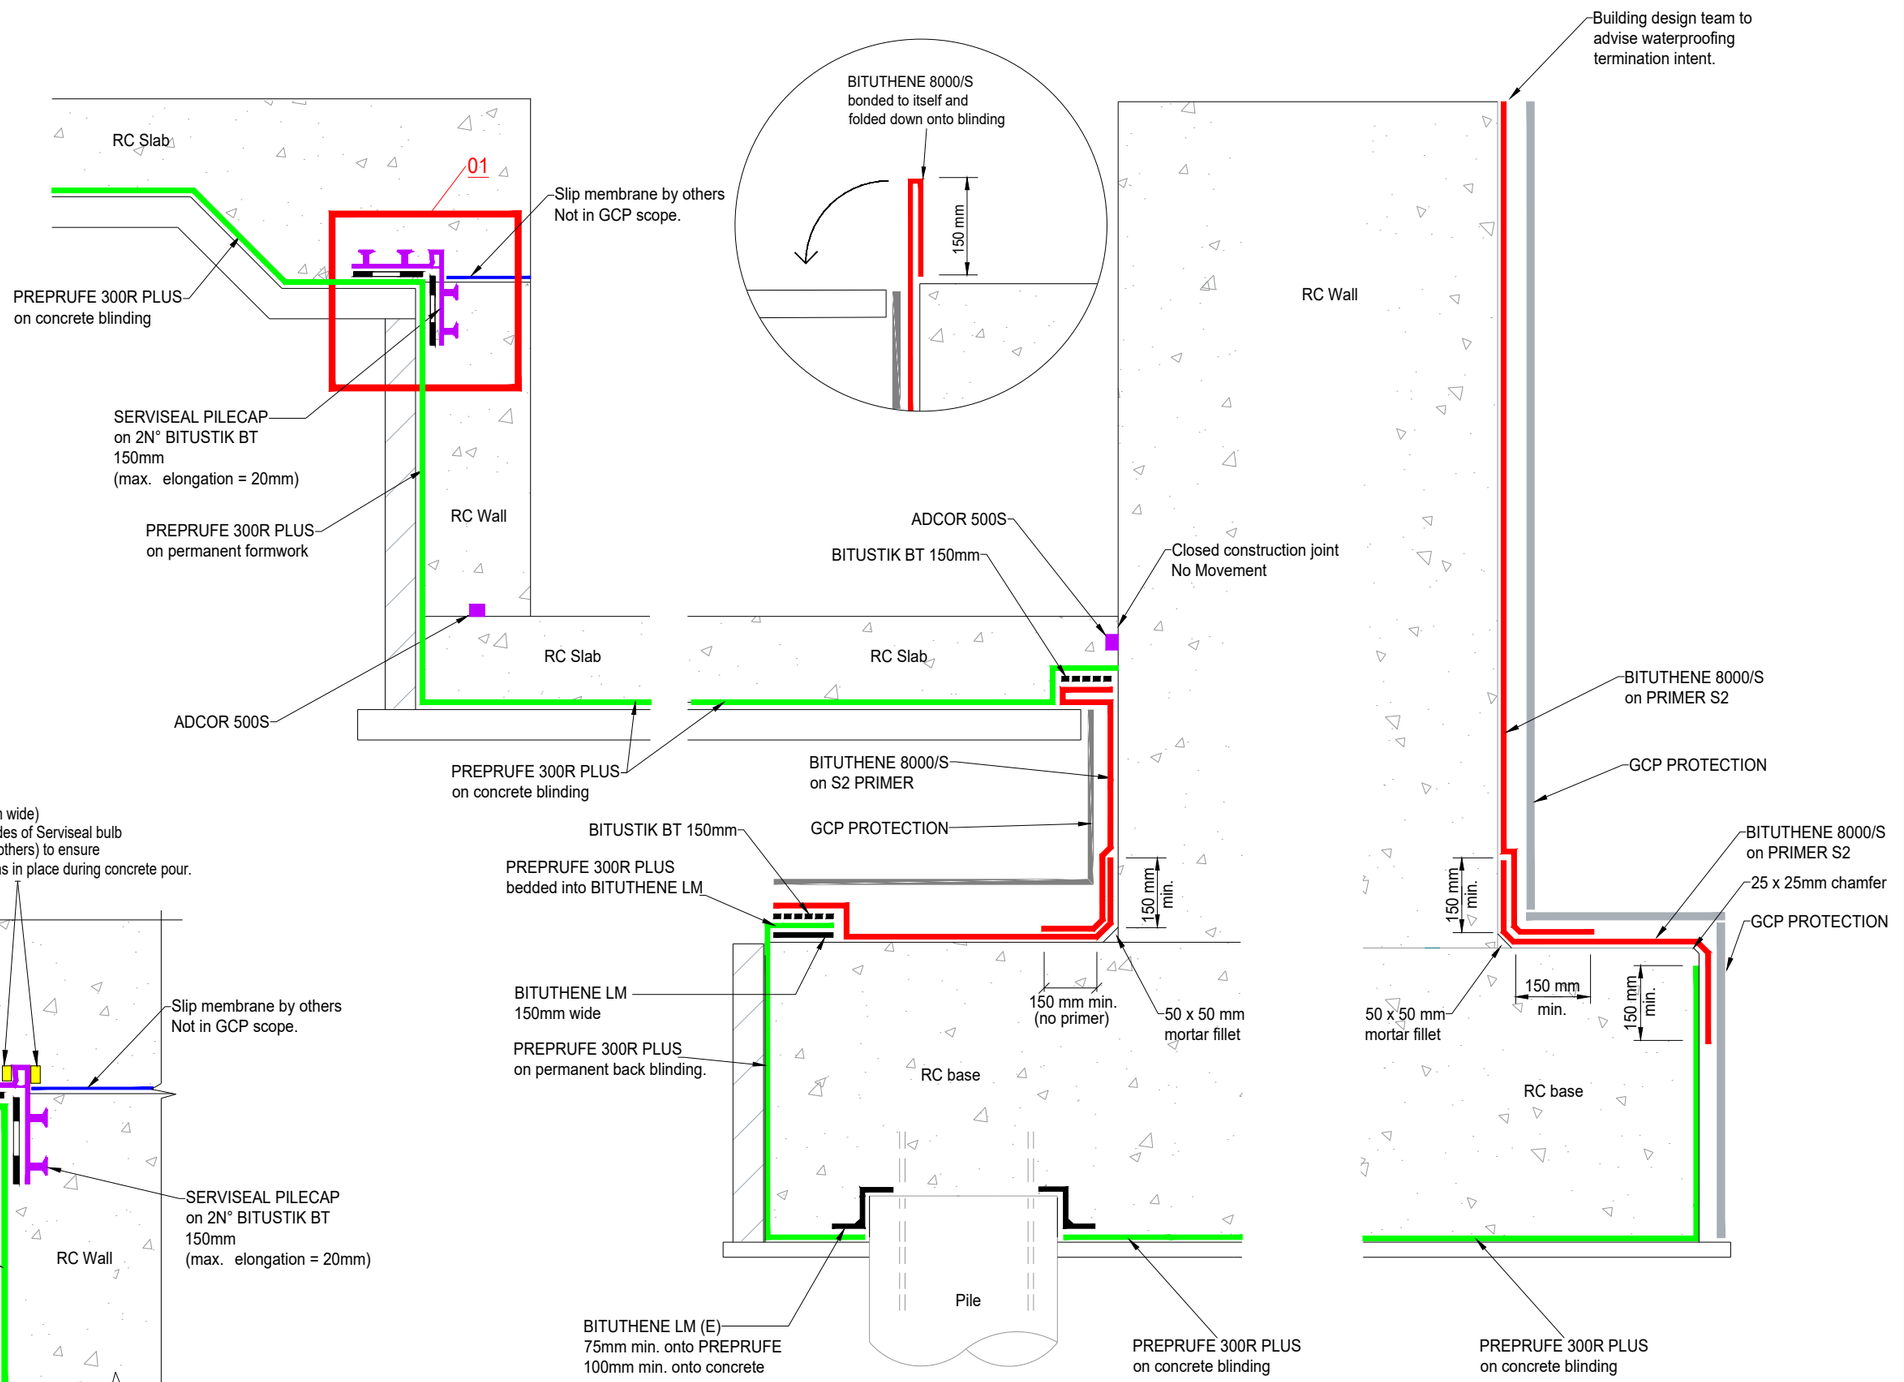

SECTION

Ref. Drg. BRA-BHE-XX-GF-DR-S-5061
GFT05 SECTION GFT05. TRENCH NEAR GLEN/N05

General Notes & Guidance:

For those third parties responsible for the design of the waterproofing system, such parties must ensure the proposed system and details shown herein are brought to the attention of those responsible for the overall design of the structure, to ensure compatibility of the waterproofing system and detailing with all elements of the structural design. Final decisions, acceptance and any recommendations must be approved in writing between such responsible parties.

For product installation, this drawing is to be read in conjunction with all relevant product data sheets and application guidelines.

Drawing Notes:

Project: CO-OP LIVE

Title: WATERPROOFING DETAILS

Drawing Status: FOR COMMENT / APPROVAL | Status: S3

gcp applied technologies

GCP APPLIED TECHNOLOGIES
487/488 Ipswich Road, Slough,
Berkshire, SL1 4EP, UK

T: +44 (0)1753 490000
E: info-gb@gcpat.com
W: www.gcpat.com

ADCOR, ADPRUFE, AEROFIL, ARMOURTAPE, AQUATEK, BETEC, BENTORUB, BITUSHIELD, BITUSTIK, BITUTHENE, COLFLEX, DECSEAL, ELIMINATOR, HYDRODUCT, INTEGRITANK, METASET, MS FIXER, OMNITEK, PAK ADHESIVE, PERM-A-BARRIER, PERMARE, PREPRUFE, PREPRUFE PLUS, PVC EDGETIE, RE-INJECTO, SENTINEL, SERVIDEK, SERVIPAK, SERVIRUFE, SERVISEAL, SERVITAPE, SERVITITE, SILCOR, SLIPSTRIP, ZIPLAP and GCP APPLIED TECHNOLOGIES are trademarks which may be registered in the United States and/ or other countries, of GCP Applied Technologies Inc. This trademark list has been compiled using available published information as of the publication date and may not accurately reflect current trademark ownership or status. These products may be covered by patents or patents pending.

This drawing is Copyright 2021 of GCP Applied Technologies. Permission for copying is granted only to employees, authorised representatives, customers, and specifiers to support the sale or use of GCP Applied Technologies products. All other rights are reserved.

Project: CO-OP LIVE MANCHESTER

Client: BAM - CAREYS

Title: DETAIL DRAWING
GCP PRODUCT APPLICATION TECHNIQUES

Information Container Name: BRA-CCE-ZZ-ZZ-DR-Y-16145

Date:	Scale	Paper Size	Drawn:	Checked:
15-11-2021	NTS	A3	TG	LC

GCP Project Ref: D20046 | Rev: P01

APPENDIX C

Material Specifications

PREPRUFE® 300R/160R membranes

Pre-applied waterproof membranes that develop an adhesive bond to poured concrete to prevent water migration. For use below slabs and on confined basement walls

Description

Preprufe® waterproof membranes are composite sheets comprising a robust HPDE backing, a pressure sensitive adhesive and a trafficable weather resistant coating. Uniquely, the membrane develops a continuous adhesive bond to concrete poured against it. This prevents water migration between the structure and the membrane, substantially reducing the risk of leaks.

Applications

- Water and vapour proofing all basement grades to BS 8102:2009
- Waterproofing civil engineering sub - structures
- Gas resistance - contributes to methane, carbon dioxide and radon gas protection according to BS 8485 (see section 7.2.4), BRE Reports 211 (radon) and 212 (methane and carbon dioxide). Independent test reports available upon request.

Independent Assessments

- BBA Certificate No. 97/3325
- Mott MacDonald Special Services Report May 2001
- International Certifications

Advantages

- **Versatile** - can be used beneath foundation slabs and with single sided formwork systems
- **Seals adhesively to concrete** - a leading technology proven to resist water migration.
- **Lightweight, flexible** - easy to handle and install without special corner pieces
- **No butt joints** - all joints have bonded 'selvedge' or Preprufe ® Tape overlaps for increased leak protection
- **Inert** - unaffected by groundwater contaminants, ponded water or wet/dry cycling
- **Remains sealed to structure** - even if ground settles
- **Smooth surface membrane** - site contamination easily removed
- **Excellent chemical resistance** - protects structure from salts and sulphate attack
- **Total system** - Full range of GCP hydrophilic and PVC waterstops available for concrete joint protection







Substrate Preparation

Suitable substrates include:

- concrete blinding
- well compacted sand on rolled crushed stone
- rigid insulation
- clay heave boards
- permanent formwork
- removable formwork
- 19 mm plywood
- Hydroduct® drainage sheets
- Adjacent sub-structures

Substrates should be uniform with no gaps or voids greater than 12 mm. Where these exist fill with a material of sufficient strength to support the membrane. All substrates must be free of loose aggregate and sharp protrusions. Where possible, avoid rounded concrete blinding.

In crushed stone applications, it is important to create a sound and solid substrate around “through slab” penetrations to eliminate movement during the concrete pour. Excessive movement may jeopardise the waterproofing integrity around the penetration. Grout around the penetration prior to installing the membrane for stabilisation.

The surface does not need to be dry, but standing water must be removed. Substrates must have sufficient rigidity not to move during the concrete pour. Boarded substrates must be close butted to provide support and not more than 12 mm out of alignment.

Installation - General

Tools /materials required:

- Heavy duty lap roller
- Stanley /Utility knives
- Tape measure
- Cotton cleaning cloths
- Plywood or similar cutting board
- Thin metal straight edge
- Chalk line
- Broom
- 2 metre long pipe or heavy broom handle
- Spiral mixing paddle for Bituthene ® LM
- Round nose trowel or spatula
- Required protection and/or drainage boards and other ancillary
- products

Preprufe® membranes are supplied in rolls 1.2m wide with a self adhesive selvedge on one edge to enable fully bonded laps between adjacent rolls. All other laps must be taped with Preprufe® Tape. Minimum application temperature +5ºC.

When installing Preprufe® membranes in cold or marginal weather conditions (<13°C) the use of Preprufe® Tape LT is recommended at all laps and detailing. Preprufe® Tape LT should be applied to clean dry surfaces and the release liner must be removed immediately after application.

Installation - Horizontal



Place the membrane with the removeable plastic release liner uppermost. End laps should be staggered to avoid a build up of layers. Leave plastic release liner in position until overlap procedure is completed. Accurately position subsequent sheets to overlap the previous sheet 75 mm along the selvedge. Ensure the underside of the succeeding sheet is clean, dry and free from contamination before attempting to overlap. Peel back the plastic release liner from between the overlaps as the two layers are bonded together. Ensure a continuous bond is achieved without creases and roll firmly. On completion of the installation, ensure complete removal of the plastic release liner from all membrane and tape.

Penetrations

To seal around penetrations such as service pipes, pile heads, lightning conductors, etc. mark and cut membrane tight to the penetration. If the membrane is not aligned within 12mm of the penetration, apply Preprufe Tape lapped onto the membrane and butted tight to the penetration. For pipe penetrations, wrap the pipe with Preprufe Tape. Mix and apply Bituthene LM around the penetrations using a fillet to provide a watertight seal between the Preprufe membrane and Tape. Refer also to Preprufe Standard Details.

Membrane Repair

Inspect the membrane for damage before installation of reinforcement steel, shuttering and final placement of concrete. Clean by jet washing if required.

Wipe the area with a damp cloth to ensure the area is clean and free from dust, and allow to dry. For minor repairs, apply Preprufe® Tape centrally over the damaged area and roll firmly. For larger repairs use a patch of Preprufe® and tape all edges with Preprufe® Tape. Remove plastic release liner from Tape.

Where exposed selvedge has lost adhesion or laps have not been sealed, ensure the area is clean and dry and overband with Preprufe® Tape and roll firmly.

Installation - Vertical

Apply the membrane with the thick white plastic face against the substrate. Mechanically fasten the membrane vertically using flat headed fixings appropriate to the substrate. The membrane may be installed in any convenient length. Secure the top of the membrane using a batten or fixing 50 mm below the top edge. Use fixings at typically 600 mm centres to secure the membrane flat against the substrate. Fixings can be made through the selvedge, this allows firmly rolled overlaps, which are covered by the subsequent strip of Preprufe® membrane. Any exposed fixings should be patched with Preprufe® Tape.

Ensure the underside of the succeeding sheet is clean, dry and free from contamination before attempting to overlap. Peel back the plastic release liner from between the overlaps as the two layers are bonded together. Ensure a continuous bond is achieved without creases and roll firmly. On completion of the installation, **completely remove the plastic release liner from all membrane and tape.**

Removal of Formwork

Preprufe® membranes can be applied to removable single sided formwork, slab perimeter formwork, pile caps, etc. Once concrete is poured the formwork must remain in place until the concrete has gained sufficient compressive strength to develop the surface bond with the Preprufe® membrane.

A minimum concrete compressive strength of 10 N/mm2 is recommended prior to stripping formwork supporting Preprufe® membranes. Premature stripping may result in loss of adhesion between the membrane and concrete.

Wall Waterproofing Options

For conventional application to walls after formwork removal use Preprufe ® 800PA - self adhesive sheet waterproofing membrane. See separate data sheet for further information.


System Components

- **Preprufe® 160R** - for use with concrete slab sections up to 500 mm thickness, or vertically with single sided formwork systems
- **Preprufe® 300R** - for use on all horizontal applications. Superior damage resistance
- **Preprufe® Tape** - incorporating Preprufe® coating for continuous concrete adhesion at taped edges and details
- **Bituthene® LM** - high performance liquid membrane for detailing terminations at pile caps and pipe penetrations
- **Adcor® 500S** - hydro-expansive waterstop for concrete construction joints
- **Adcor® 550MI** - hydro-expansive injectable waterstop for added security of concrete construction joints.

Application


Material Storage

Sequence deliveries to avoid delays, but minimise on-site storage. Select a safe, covered secure location for material storage. Store materials for each day's use in a location that won't require movement a second time. Do not double-stack pallets of waterproofing on the job site. Store protection boards flat and off the ground. Provide cover on top and all sides.

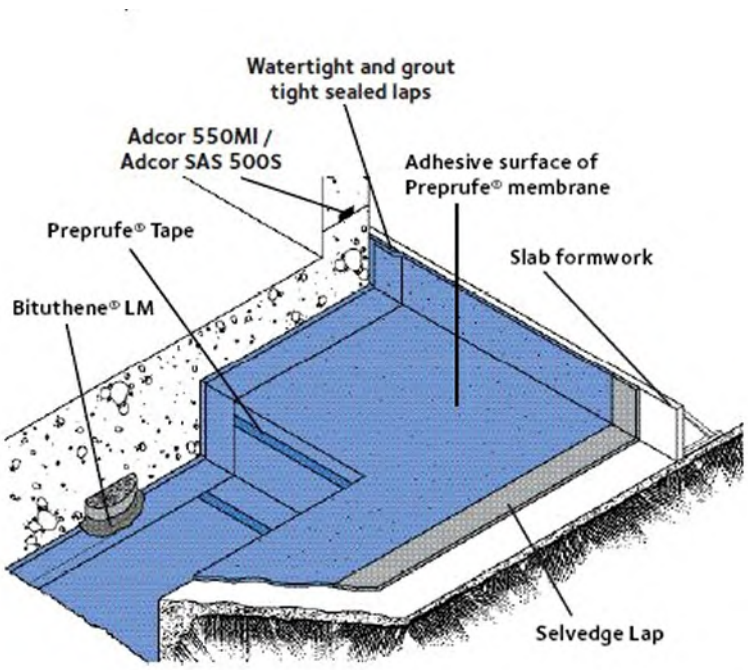

Details shown are typical illustrations only and not working drawings. For assistance with working drawings and additional technical advice please contact GCP Technical Services.

End Laps and Cut Edges

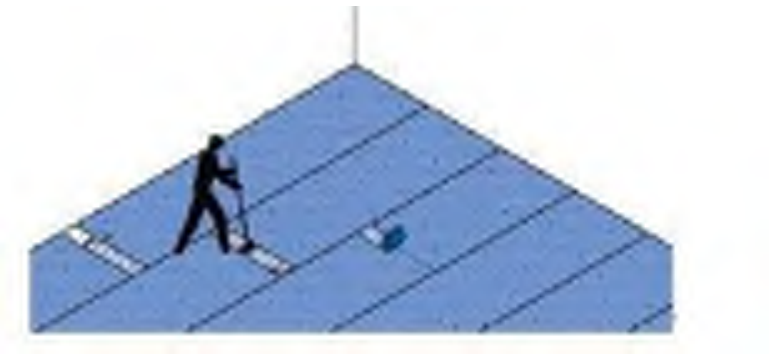


Overlap all roll ends and cut edges by a minimum 75 mm and ensure the area is clean and free from contamination, wiping with a damp cloth if necessary. Allow to dry and apply Preprufe® Tape centred over the lap and roll firmly. Refer also to Preprufe® Standard Details.


Internal & External Corners

Internal & external corners should be formed as shown in the diagrams below. Ensure that all laps are 100 mm minimum, taped with Preprufe® Tape and well rolled. Crease and fold the membrane to ensure a close fit to the substrate profile.

Corners

Internal and external corners should be formed as shown in the diagrams returning the membrane a minimum of 100 mm and sealing with Preprufe® Tape. Ensure that the apex of the corner is covered and sealed with Tape and roll firmly. Crease and fold the membrane to ensure a close fit to the substrate profile and avoid hollows.

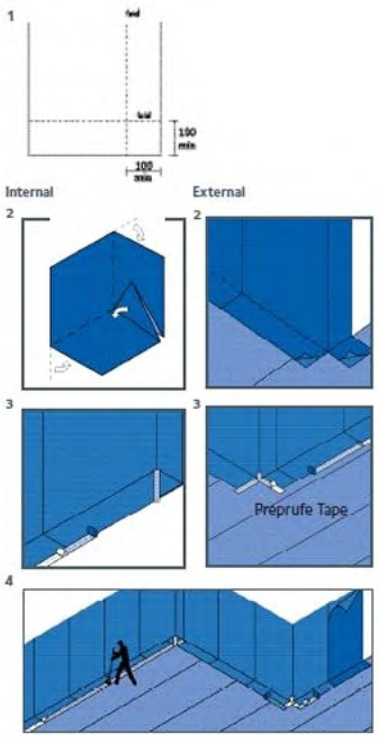

1
100
min
100
min
Internal
External
2
2
3
3
Preprufe Tape
4

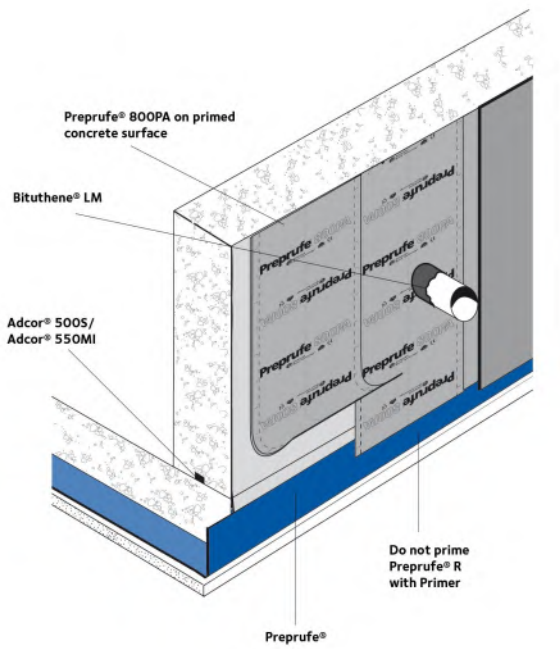
Preprufe® 800PA on primed concrete surface
Bituthene® LM
Adcor® 500S/ Adcor® 550MI
Do not prime Preprufe® R with Primer
Preprufe®

Preprufe Preparation for Preprufe ® 800PA

Inspect the Preprufe ® membrane around the perimeter edge of the concrete slab. Identify any exposed non-selvedge overlaps in the Preprufe® membrane. To ensure continuity of the fully bonded system, carefully cut and remove a 75 mm triangular piece of the top flap of Preprufe® membrane only, as shown shaded in the standard detail, Slab Perimeter Detail - non selvedge lap.

Slab Perimeter Detail

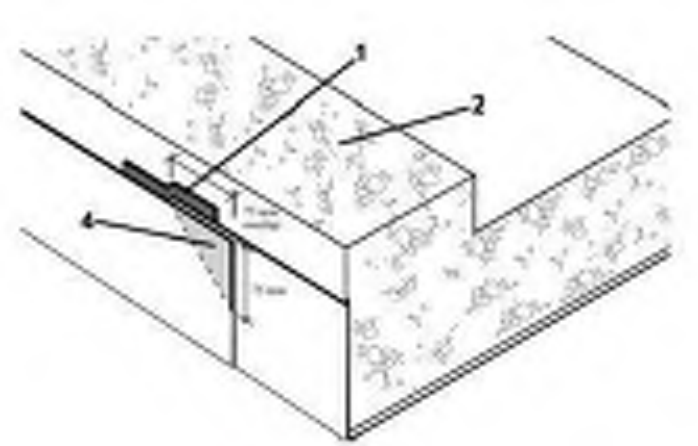

1. Taped non-selvedge lap
2. Poured Concrete
3. Remove formwork
4. Cut and remove shaded piece before applying Preprufe® post applied membrane

Ancillary Products

Adcor® 500S – Hydrophilic waterstop for construction joints and pipe entries.
AT System – Co-extruded PVC waterstops for movement joints. Bituthene ® Protection Board – protection against damage from backfill.

Limitations of Use

- Do not use Preprufe ® between concrete infilled hollow block walls
- It is recommended that concrete be poured within 56 days (42 days in hot climates) of application of the membrane.

NBS Specification

Refer to clause J40 297.

Health and Safety

There is no legal requirement for a Safety Data Sheet for Preprufe ® membrane. For health and safety questions on this product please contact GCP. For Bituthene® LM read the product carton and Safety Data Sheet (SDS) before use. Users must comply with all risk and safety phrases. SDS's can be obtained from GCP Applied Technologies.

SUPPLY			
Preprufe®	**300R**	**160R**	**Tape LT* or HC***
Thickness (nominal) (mm)	1.2	0.8	0.7
Roll size (m)	1.2 x 30	1.2 x 35	100mm x 15
Roll area (m^2)	36	42	
Roll weight (kg)	50	42	2
Minimum edge/ end laps (mm)	75	75	75

*LT denotes for temperature between -4°C and +30°C

*HC denotes for temperature between +10°C and +40°C

ANCILLARY PRODUCTS	
Adcor® 500S	6 x 5m rolls
Adcor® 550MI	8 x 5m rolls
Bituthene® LM	5.7 litre pack

TYPICAL PROPERTIES		
	300R	**160R**
Thickness of carrier sheet (mm) DIN V 20000-202	0.8 ± 0.05	0.4 ± 0.04
Adhesion to concrete (N/mm)	2.88	2.88
Shear strength of joints (N/mm) EN 12317-2	9.52	9.52
Hydrostatic head resistance (m) ASTM D 5385 mod.	> 70	> 70
Puncture resistance (N)	990	445

DECLARED VALUES ACCORDING TO EN 13967

Property	Declared Value		Test Method	Property	Declared Value		Test Method
Preprufe®	160R	300R	Method	Preprufe®	160R	300R	
Visible defects - MDV	None	None	EN 1850-2	**Joint strength** (N/50mm) - MLV	≥ 480	≥ 850	EN 12317-2
Straightness - MDV	Pass	Pass	EN 1848-2	**Water vapour transmission** (μ= sD/d) - MDV	950.000 ± 30%	950.000 ± 30%	EN 1931 Method B
Length (m) - MDV	35.15 ± 0.25	30.15 ± 0.25	EN 1848-2	**Durability of water tightness against ageing/ degradation** (at 60 kPa)	Pass	Pass	EN 1296 EN 1928 Method B
Thickness (mm) - MDV	0.8 ± 0.05	1.2 ± 0.08	EN 1849-2	**Durability of water tightness against chemicals** (at 60 kPa)	Pass	Pass	EN 1847 Method B EN 1928 Method B
Width Carrier Sheet (m) - MDV	1.206 ±0.010	1.206 ±0.010	EN 1848-2	**Compatibility with bitumen**	Pass	Pass	EN 1548
Mass per unit area (g/m²) - MDV	810 ± 50	1150 ± 70	EN 1849-2	**Resistance to static loading**	≥ 20 - Pass	≥ 20 - Pass	EN 12730
Water tightness to liquid water (at 60 kPa)	Pass	Pass	EN 1928	**Tensile properties - unreinforced sheets** (N/50mm) - MLV	Long[1] ≥ 60 Trans[2] ≥ 60	Long[1] ≥ 110 Trans[2] ≥ 120	EN 12311-2 Method A
Resistance to impact (Al-board (mm) - MLV)	≥ 250	≥ 400	EN 12691	**Tensile properties - unreinforced sheets** (Elongation %) - MLV	Long[1] ≥ 4.5 Trans[2] ≥ 4	Long[1] ≥ 4.5 Trans[2] ≥ 4	EN 12311-2 Method A

Resistance to tearing (Nail Shank)- unreinforced sheets (N) - MLV	≥ 300	≥ 450	EN 12310-1	**Reaction to fire** (Class; test conditions)	E	E	EN 13501-1

Footnotes: 1. Longitudinal - related to the roll direction 2. Transversal - related to the roll direction 3. MDV: Manufacturer Declared Value 4. MLV: Manufactured Limiting

Value 5. NPD: No Performance Declared.

All declared values shown in this data sheet are based on test results determined under laboratory conditions and with the product sample taken directly from stock in its

original packing without any alteration or modification of its component parts.

CE 0836

GCP Applied Technologies (UK) Ltd.
Ipswich Road, Slough, Berkshire, SL1 4EQ United Kingdom
06 09/FO17

EN 13967
Preprufe® 160R and 300R Flexible Sheets for Waterproofing, Type T Reaction to fire: E Watertightness: Pass at 60 kPa

We hope the information here will be helpful. It is based on data and knowledge considered to be true and accurate, and is offered for consideration, investigation and verification by the user, but we do not warrant the results to be obtained. Please read all statements, recommendations, and suggestions in conjunction with our conditions of sale, which apply to all goods supplied by us. No statement, recommendation, or suggestion is intended for any use that would infringe any patent, copyright, or other third party right.

ADCOR, BITUTHENE, and PREPRUFE are trademarks, which may be registered in the United States and/or other countries, of GCP Applied Technologies Inc. This trademark list has been compiled using available published information as of the publication date and may not accurately reflect current trademark ownership or status.

© Copyright 2018 GCP Applied Technologies Inc. All rights reserved.

GCP Applied Technologies Inc., 62 Whittemore Avenue, Cambridge, MA 02140 USA

In the UK, Ipswich Road, Slough, Berkshire, SL1 4EQ, UK

This document is only current as of the last updated date stated below and is valid only for use in the United Kingdom. It is important that you always refer to the currently available information at the URL below to provide the most current product information at the time of use. Additional literature such as Contractor Manuals, Technical Bulletins, Detail Drawings and detailing recommendations and other relevant documents are also available on www.gcpat.uk. Information found on other websites must not be relied upon, as they may not be up-to-date or applicable to the conditions in your location and we do not accept any responsibility for their content. If there are any conflicts or if you need more information, please contact GCP Customer Service.

Last Updated: 2018-08-24

gcpat.uk/solutions/products/preprufe-pre-applied-waterproofing-solutions/preprufe-300r160r-membranes

PREPRUFE® Tape

Reinforced pressure sensitive tape incorporating PREPRUFE® coating for continuous concrete adhesion at taped edges and details.

Product Description

Preprufe ® Tape is a specially formulated two sided, reinforced pressure sensitive tape. The bottom side of the tape has a highly aggressive pressure sensitive adhesive which is designed to adhere to penetrations, protrusions and GCP waterproofing membranes and accessories. The top side of the tape has a pressure sensitive adhesive, a weather resistant protective coating an a release liner. Concrete is cast directly against the top adhesive side of the tape. The specially developed Preprufe adhesive layers work together to form a continuous and integral seal to the structure.

Preprufe Tape is available in Low Temperature and Hot Climate Grades as follows:

- **Preprufe Tape LT** - for temperatures between -5°C and +30°C.
- **Preprufe Tape HC** - for use in Hot Climates minimum 10°C.

Use

Preprufe Tape is a 100 mm wide tape used in detail areas including end laps, penetrations and various tie-ins.

It is also used to patch damaged areas in the Preprufe membranes.

Supply

DIMENIONS (NOMINAL)	PREPRUFE TAPE (HC OR LT)
Roll Size	100 mm x 15 m
Roll Weight	2 kg

Application

Wipe substrates to receive Preprufe Tape clean to remove any dirt, dust or moisture. Clean the surface of penetrations or protrusions with a wire brush to remove dirt, dust, rust and loose particles.

Unroll the tape and adhere the exposed pressure sensitive adhesive surface to the membrane or penetration. The protective coating surface of the tape should face toward the concrete to be cast onto the tape.

Use heavy hand pressure or a hand roller to maximize adhesion. Remove the release liner during application. Ensure the plastic release liner is removed from all areas of Preprufe Tape. It is recommended that concrete be poured within 56 days (42 days in hot climates)

of application of the tape. Concrete must be placed carefully and consolidated properly to avoid damage to the membrane. Never use a sharp object to consolidate the concrete. Provide temporary protection from concrete over splash for areas of the tape that are adjacent to a concrete pour.

This document is only current as of the last updated date stated below and is valid only for use in the United Kingdom. It is important that you always refer to the currently available information at the URL below to provide the most current product information at the time of use. Additional literature such as Contractor Manuals, Technical Bulletins, Detail Drawings and detailing recommendations and other relevant documents are also available on www.gcpat.uk. Information found on other websites must not be relied upon, as they may not be up-to-date or applicable to the conditions in your location and we do not accept any responsibility for their content. If there are any conflicts or if you need more information, please contact GCP Customer Service.

Last Updated: 2018-08-24
gcpat.uk/solutions/products/preprufe-pre-applied-waterproofing-solutions/preprufe-tape

gcp applied technologies

BITUTHENE® LIQUID GM

Single component water based compound, formulated on styrene-butadiene co-polymer.

Product Applications

BITUTHENE® Liquid GM is a high performance elastomeric liquid rubber membrane, specifically designed for a range of vertical and horizontal surfaces, generally as follows:

- Applied to walls, floors or soffits.
- As a retro applied gas proof membrane to concrete and masonry substrates.

The product only requires stirring to form the ideal material for providing a waterproof and gas proof, methane and carbon dioxide barrier.

When designing Type A structures (as classified in BS 8102: 2009), the product applied correctly is capable of providing the levels of protection required for Grades 1, 2 & 3 basements.

Applications

- Gas proof detailing with GCP PREPRUFE® and BITUTHENE® membranes
- Suppression of methane, carbon dioxide and high density hydrocarbon vapour
- Basements and substructures

Applied To

- Concrete
- Masonry
- Steel

Advantages

- Liquid applied, methane and carbon dioxide barrier
- Excellent adhesion; fully bonds to porous and non-porous substrates
- Easily applied by brush, roller or airless spray
- Can be applied to damp substrates
- Rapid drying and easily repaired
- Non-toxic and flexible when cured
- Gas resistance - contributes to methane, carbon dioxide and radon gas protection according to BS 8485 (see section 7.2.4), BRE Reports 211 (radon) and 212 (methane and carbon dioxide). Independent test reports available upon request.

Durability


Subject to normal conditions of use, BITUTHENE® Liquid GM will provide an effective barrier to methane and carbon dioxide gases, water and water vapour for the life of the structure.


Independent Authority

Tests carried out show that BITUTHENE® Liquid GM will provide a barrier to methane, carbon dioxide and high density hydrocarbon vapour. A copy of the reports are available upon request.

Specification

J30 – Liquid Applied Tanking / Damp Proofing in accordance with NBS Clauses.
Please consult GCP for further information.

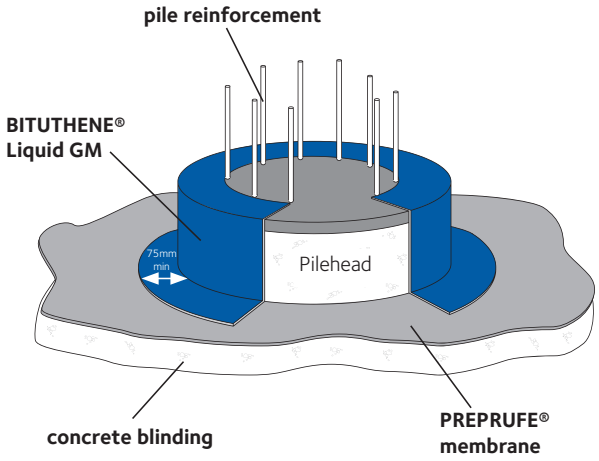

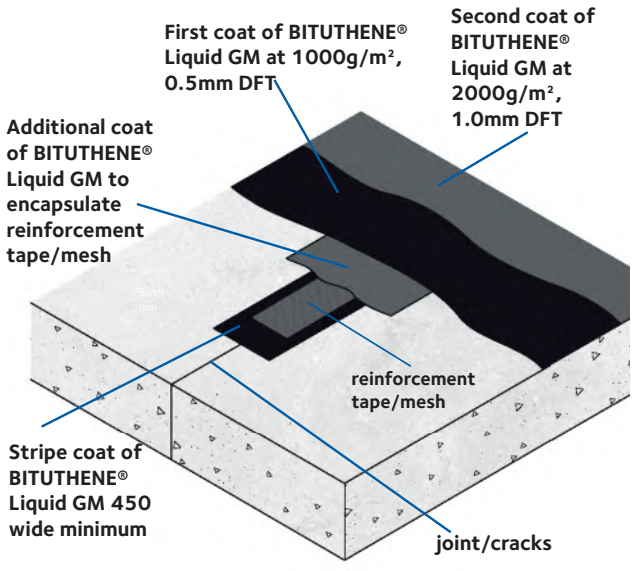

Details shown are typical illustrations only and not working drawings. For assistance with working drawings and additional technical advice please contact GCP Technical Services.

Ancillary Products

Reinforcement tape/mesh – a material for embedding in the coating, used to reinforce joints, etc.

Construction

General
All construction should conform with the Building Regulations, Codes of Practice and British Standards in current use at the time the building is constructed.

The above performance figures are typical values and should not be considered a product specification.
*Dependent upon application rate and product surface porosity.

Preparation

All surfaces: Should be clean, free from dust and loose material, oil, paint, fungal growth, etc.
Non-structural cracks, less than 0.5 mm wide, must be filled.
Structural cracks must first be repaired and filled.
The substrate must be sound and ideally present a smooth face.
Fill holes and re-point flush to the finish, using a suitable grout like OMNITEK®.

Old repairs must be inspected and re-repaired if necessary.
Remove fins and snots as necessary.

Newly laid concrete should have a clean textured surface with 45° fillets at internal angles. Use OMNITEK® to provide fillets where required.

Mixing
BITUTHENE® Liquid GM is supplied ready for use. The product requires agitation using a slow speed paddle mixer. Mix carefully for 5 minutes before use. If containers are stored for more than 2 hours after opening, re-agitate. Do not add water.

Surface Preparation
Pre-dampen (not wet) the substrate before applying the first coat.

Interface with other media
For expansion joints, ensure that BITUTHENE® Liquid GM is applied well into the rebate before the expansion media is applied.
Other gas membranes must be exposed and lapped with where present.

Dealing with cracks
Cracks must be stabilised as necessary, and filled. Apply BITUTHENE® Liquid GM along the line of the crack, at a rate of 0.3 litres/m^2, with a reinforcement tape/mesh fully embedded within it. Then apply the main coating system, as stated below.

Application Of The Main Coating System

The product can be applied by stiff brush, roller or airless spray with a minimum 17/1000 of an inch (17 thou.) nozzle. The spray method is especially suitable for less accessible locations and uneven substrates.
The first coat is to be applied at the minimum rate of 1Kg/m^2. Ensure that the coating is even and use a circular action when spraying. Allow the first coat to dry before applying the second coat.

Apply the second coat, which is to be applied at the rate of 2Kg/m^2, at right angles to the first coat using a similar application method.
Do not apply over bitumen.
The total application thickness must not exceed 4 mm if splitting or cracking is to be avoided.

Cleaning

All tools should be cleaned with water immediately after use.

Limitations

Not suitable for negative water pressure (internal tanking).
Product should be protected against site trafficking before backfilling. Rough, undulating surfaces should be 'made-good' using a suitable cementitious repair material.

Safety

Read the product carton and Safety Data Sheet (SDS) before use.
Users must comply with all risk and safety phrases. SDS's can be obtained from GCP Applied Technologies.

Supply

BITUTHENE® Liquid GM 15kg container.

Storage

BITUTHENE® Liquid GM must be stored at room temperature (minimum 10°C and max 30°C), and kept dry.
Protect from freezing and direct sunlight.

If these conditions are maintained, and the product packaging is unopened, then a shelf life of 12 months can be expected.

Properties	
Form	Thixotropic blue/grey liquid
Colour	when dry Black
Specific gravity	1.4
Number of coats	Two (2)
Coverage*	1st coat = 1 Kg/m^2 2nd coat = 2 Kg/m^2
Coverage for two coats	3 Kg/m^2
DFT of coating	1.5 mm for two coats
Curing time	Touch dry: 30–60 minutes Full cure: 24-48 hours
Overcoating time	90-120 minutes after 1st coat
Application temperature limits	5 - 35°C
Cured Properties	
Adhesion to concrete	> 1.1 N/mm²
Elongation ASTM D2370	> 100%
Hydrostatic Head Resistance, ASTM D 5385	Pass, 7 bar

All declared values are subject to a tolerance of ±10%.

All declared values shown in this data sheet are based on test results determined under laboratory conditions and with the product sample taken directly from stock in its original packing without any alteration or modification of its component parts.

Supply	
BITUTHENE® LIQUID GM	15 kg
Shelf Life	12 months (in unopened packaging and at correct storage conditions)
Storage	Must be stored at room temperature (minimum 10°C and max 30°C), and kept dry. Protect from freezing and direct sunlight.

We hope the information here will be helpful. It is based on data and knowledge considered to be true and accurate, and is offered for consideration, investigation and verification by the user, but we do not warrant the results to be obtained. Please read all statements, recommendations, and suggestions in conjunction with our conditions of sale, which apply to all goods supplied by us. No statement, recommendation, or suggestion is intended for any use that would infringe any patent, copyright, or other third party right.

BITUTHENEand OMNITEK are trademarks, which may be registered in the United States and/or other countries, of GCP Applied Technologies Inc. This trademark list has been compiled using available published information as of the publication date and may not accurately reflect current trademark ownership or status.

© Copyright 2021 GCP Applied Technologies Inc. All rights reserved.

GCP Applied Technologies Inc., 62 Whittemore Avenue, Cambridge, MA 02140 USA

In the UK, Ipswich Road, Slough, Berkshire, SL1 4EP, UK

0921 BITUTHENE-Liquid-GM_UK

gcp applied technologies

BITUSTIK™ BT

Double sided, self adhesive, cold applied, waterproofing tape for membrane detailing and sealing.

Description

BITUSTIK™ BT is a flexible self adhesive tape coated on both sides with a high adhesive butyl rubber compound reinforced with a polyester mesh, to provide excellent adhesion to most building substrates. It is fully compatible with GCP waterproofing membranes.

Applications

- General purpose, double sided waterproof sealing strip for nonexposed applications
- For use as a detailing aid with BITUTHENE® , PREPRUFE® , HYDRODUCT® and GCP Protection boards or as a bedding strip for SERVISEAL® waterstops.

Installation


Minimum application temperature +5 °C.
For application on concrete: surfaces must be smooth, clean and dry. Use BITUTHENE® Primer S2 applied evenly by roller or brush to improve adhesion, particularly on dusty substrates, and allow to dry.
For application on SERVISEAL® PVC waterstops, PREPRUFE®, BITUTHENE® membranes, HYDRODUCT® drainage or GCP Protection: wipe the area with a damp cloth to ensure the area is clean and free from dust, and allow to dry.
BITUSTIK™ BT is simply applied by peeling away the silicone release paper and applying one side of the adhesive face to the prepared substrate and roll firmly to ensure complete adhesion without creases or voids. Roll ends and cut edges should be overlapped 50 mm minimum and rolled firmly to ensure a watertight seal.
Once the first adhesive face has been applied and rolled, peel off the second release paper and apply the other material (SERVISEAL® PVC waterstops, PREPRUFE® or BITUTHENE® membranes, HYDRODUCT® drainage or GCP Protection) and roll firmly to ensure complete adhesion.
For vertical application with Serviseal®at temperatures below +10 °C, propping might be necessary every 1-2m to maintain a good bond until concrete pour.

Specification

BITUSTIK™ BT self adhesive tape to be applied in accordance with the manufacturer's instructions and supplied by GCP Applied Technologies.

Safety and Handling

Read and understand the product label and Safety Data Sheet (SDS) for each system component. All users should acquaint themselves with this information prior to working with the products and follow the precautionary statements. SDSs can be obtained by contacting your local GCP representative or office.

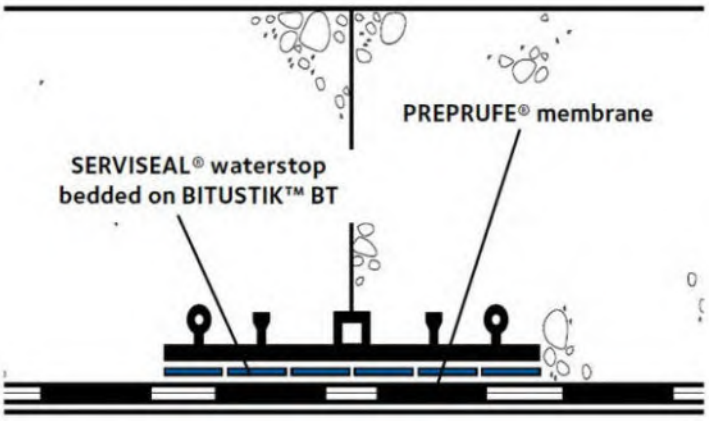

Details shown are typical illustrations only and not working drawings. For assistance with working drawings and additional technical advice please contact GCP Technical Services.

Supply

BITUSTIK™ BT		
Thickness	1.5 mm nominal	
Roll sizes[1] (m)	150 mm x 10 m long 240 mm x 10 m long	weight 3.3 kg weight 5.3 kg
Ancillary Products		
BITUTHENE® Primer S2	5, 25 ltr drums	
Coverage	9-11 m^2 per litre depending upon method of application, surface porosity and ambient temperature	
Lap Roller	Unit	
Storage	Store in original packaging in dry conditions between 5 °C & 30 °C	

Equipment by others: Stanley knife or similar, hand roller. Roller or brush for primer.

We hope the information here will be helpful. It is based on data and knowledge considered to be true and accurate, and is offered for consideration, investigation and verification by the user, but we do not warrant the results to be obtained. Please read all statements, recommendations, and suggestions in conjunction with our conditions of sale, which apply to all goods supplied by us. No statement, recommendation, or suggestion is intended for any use that would infringe any patent, copyright, or other third party right.

BITUSTIK, BITUTHENE, HYDRODUCT and PREPRUFE are trademarks, which may be registered in the United States and/or other countries, of GCP Applied Technologies Inc. This trademark list has been compiled using available published information as of the publication date and may not accurately reflect current trademark ownership or status.

© Copyright 2019 GCP Applied Technologies Inc. All rights reserved.

GCP Applied Technologies Inc., 62 Whittemore Avenue, Cambridge, MA 02140 USA

In the UK, Ipswich Road, Slough, Berkshire, SL1 4EQ, UK

GCP0082_0619 Bitustik-BT_UK

This document is only current as of the last updated date stated below and is valid only for use in the United Kingdom. It is important that you always refer to the currently available information at the URL below to provide the most current product information at the time of use. Additional literature such as Contractor Manuals, Technical Bulletins, Detail Drawings and detailing recommendations and other relevant documents are also available on www.gcpat.uk. Information found on other websites must not be relied upon, as they may not be up-to-date or applicable to the conditions in your location and we do not accept any responsibility for their content. If there are any conflicts or if you need more information, please contact GCP Customer Service.

Last Updated: 2021-02-05
gcpat.uk/solutions/products/bitustik-bt

APPENDIX D

Project Survey Sheets

Co-Op Live, Manchester - C777
24.1.2022

Site name: BAM Site Offices, Co-Op Live, Etihad Campus, Alan Turing Way, Manchester **Postcode: M11 3FF**	**Units / Area checked: Slab area to gridlines W07 – W08 & EW**
Installers Name: Careys Civil Engineering	
Date: 24/01/2022	
Inspection by: Barrie Ackroyd / Dan Squire	**Weather: 4ºC Dry**

Item	Comments	
Sub-floor void	N/A	
Ventilation Inlets and Outlets	N/A	
Number Of Vents	N/A	
Materials used:	Membrane – Preprufe 300R Plus Membrane	
	Self-Adhesive Membrane ☐ Yes	Preformed Top hats ☐ Yes
	Double Sided Butyl Tape ☐ Yes	Preformed Corners ☐ Yes
	Others Please List: Preprufe Tape, Bituthene LM E, Bitustik BT 240 double sided jointing tape.	
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** MTS Ltd carried out a thorough visual inspection of the membrane, the membrane had been installed to a very good standard. The membrane is lined across the main floor and tape jointed in line with GPC material specifications and industry best practices. The membrane was jointed into the perimeter liner wall membrane and all stainless steel starter bars were sealed with the Bituthene LM E trowel applied membrane. We employed seam pick probe seam integrity testing and we are pleased to advise there were no defects to report. We also noted the waterbar's had been weld jointed using the hot knife and stuck don to the 300R membrane using the Bitustik BT 240 double sided jointing tape. There were no defects to report.	

Type of Joint	Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)	

Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?	☒ Yes	☐ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?	☒ Yes	☐ No	☐ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?	☐ Yes	☐ No	☒ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?	☐ Yes	☐ No	☒ N/A
	Has all other detailing work passed inspection	☒ Yes	☐ No	☐ N/A

(List any defects to detailing work and joints):

We are pleased to advise there were no defects to report whereby not requiring any remedial works. The works were ongoing and although practically complete the final works were being attended to. CGP were also in attendance who gave MTS a short introduction into the overall system componentry and specifications.

Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A

The Area has passed inspection ☒

The Area has failed inspection and a corrective action sheet has been left with the contractor ☐

The Area is incomplete as detailed above ☒

Signed: **Barrie Ackroyd** Date: **24/01/2022**

Area Inspected



Photo **24/01/2022**



Area installation overview



Lightning strap seal with Bituthene LM E



Typical formation preparation, with excellent laying surface



Service pipe cast into the blinding formation



Stainless steel starter bars sealed using bituthene LM E



Stainless steel starter bars sealed using bituthene LM E with Waterbar in place

Photo **24/01/2022**



Liner wall membrane installation overview



Waterbars welded together and above bitustik butyl tape ready for adhesion



Waterbars welded together and above bitustik butyl tape ready for adhesion



Bitustik butyl tape



Floor to wall junction with waterbars in place



Typical seam pick probe testing method

Test and Inspection Result 'PASS In FULL'

The areas has passed the inspection and a re-visit is not required.



Signed: Barrie Ackroyd Date: 24.1.2022

On Behalf of Membrane Testing Solutions Ltd

Co-Op Live, Manchester - C777
3.2.2022

Site name: BAM Construction. Co-Op Live. Manchester **Postcode: M11 3DU**	**Units/ plots checked: North west slab - Pour 2. Main floor installation Gridlines W06-W08 / NW - N01** **Core 5 - Base installation Gridlines E07-BS / N12-BE**
Installers Name: P J Carey's	
Date: 03/02/2022	
Inspection by: Dan Squire	**Weather: 9°C Dry**

Item	Comments	
Sub-floor void	N/A	
Ventilation Inlets and Outlets	N/A	
Number Of Vents	N/A	
Materials used:	Membrane – Preprufe 300R Plus	
	Self-Adhesive Membrane ☒ Yes	Preformed Top hats ☐ Yes
	Double Sided Butyl Tape ☐ Yes	Preformed Corners ☐ Yes
	Others Please List: Bituthene LM. Bituthene Liquid membrane	
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** MTS Ltd carried out a thorough visual inspection of the membrane, the membrane had been installed to a good standard. Preprufe 300R plus membrane has been lined across the pour slab areas as noted and is joined to the membrane previously installed up the liner wall to the capping beam. The membrane has a permanent back binding which is used to join the membrane together and is pressure rolled. In some areas an additional strip of Preprufe Tape LT has been added on top of the joints. A mix of Bituthene LM & Bituthene liquid membrane is applied to seal all penetrations. Patch repairs have been made to the membrane along the vertical face of the liner wall and also on the floor where a few minor damages were caused by the steel using Preprufe 300R plus membrane and strips of Preprufe LT tape.	

Installation Notes Continued	Site were carrying out their own ongoing inspections and cleaning off the membrane as the install progressed and prior to the pour. Approx 50% of the areas to inspect were restricted due to steel work on the membrane.					
Type of Joint	Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐		
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)			
Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?			☒ Yes	☐ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?			☒ Yes	☐ No	☐ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Has all other detailing work passed inspection			☒ Yes	☐ No	☐ N/A
	(List any defects to detailing work and joints): During our inspection the following defects and repairs were carried out: No recorded defects. However, holes were in the membrane in preparation for the starter bars which will then be sealed using the Bituthene LM and Liquid membrane mix once in place. Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A The Area has passed inspection ☒ The Area has failed inspection and a corrective action sheet has been left with the contractor ☐ The Area is incomplete as detailed above ☐ Signed: **Dan Squire** Date: **03/02/2022**					

Area Inspected



Photo **03/02/2022**



Restricted inspection area



North west pour 2 slab line out



Liner wall patch repairs



Bituthene LM and liquid membrane mix sealed penetrations



Sealed pipe penetration using Bituthene LM and liquid membrane mix



Sealed penetration using Bituthene LM and liquid membrane mix



Probe test to adhesive backing joint

Site name: BAM Construction. Co-Op Live. Manchester **Postcode: M11 3DU**	**Units/ plots checked: Core 5 - Base installation Gridlines E07-BS / N12-BE**
Installers Name: P J Carey's	
Date: 03/02/2022	
Inspection by: Dan Squire	**Weather: 9°C Dry**

	Item	**Comments**	
Sub-floor void		N/A	
Ventilation Inlets and Outlets		N/A	
Number Of Vents		N/A	
Materials used:		Membrane – Preprufe 300R Plus	
		Self-Adhesive Membrane ☒ Yes	Preformed Top hats ☐ Yes
		Double Sided Butyl Tape ☐ Yes	Preformed Corners ☐ Yes
		Others Please List: Bituthene LM. Bituthene Liquid membrane	
Installation Notes		**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** MTS Ltd carried out a thorough visual inspection of the membrane, the membrane had been installed to a good standard. Preprufe 300R plus membrane has been lined across the core base area as noted and extends up the vertical face of the core walls to be able to join membrane at a later date. The membrane has a permanent back binding which is used to join the membrane together and is pressure rolled. In some areas an additional strip of Preprufe Tape LT has been added on top of the joints. A mix of Bituthene LM & Bituthene liquid membrane is applied to seal all pile caps. Site were carrying out their own ongoing inspections and cleaning off the membrane as the install progressed. All prep work including drying off the concrete floor and smoothing of the pile caps prior to the install were carried out well. The core area base was approx 25% when the inspection took place and all works were being carried out well and sufficiently.	

Type of Joint	Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐	
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)		
Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?		☒ Yes	☐ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?		☐ Yes	☐ No	☒ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?		☐ Yes	☐ No	☒ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?		☒ Yes	☐ No	☐ N/A
	Has all other detailing work passed inspection		☐ Yes	☐ No	☒ N/A
	(List any defects to detailing work and joints): During our inspection the following defects and repairs were carried out: No recorded defects. Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A The Area has passed inspection ☒ The Area has failed inspection and a corrective action sheet has been left with the contractor ☐ The Area is incomplete as detailed above ☐ Signed: **Dan Squire** Date: **03/02/2022**				

Area Inspected



Photo **03/02/2022**



Core 5 base installation



Pile cap good prep work



Drying of the concrete prior to the install of membrane



Sealed pile cap using the Bituthene LM mixed with liquid membrane



Sealed membrane adhesive joint



Sealed and formed corner detailing using Preprufe 300R plus membrane and Preprufe tape LT

Test and Inspection Result 'PASS In FULL' to Both Areas

The areas have passed the inspection and a re-visit is not required.



Signed: Barrie Ackroyd Date: 3.2.2022

On Behalf of Membrane Testing Solutions Ltd

Co-Op Live, Manchester - C777
24.2.2022

Site name: BAM Construction. Co-Op Live. Manchester **Postcode: M11 3DU**		**Units/ plots checked: : Core 5 - Wrap installation Gridlines E07-BS / N12-BE**
Installers Name: P J Carey's		
Date: 24/02/2022		
Inspection by: Dan Squire		**Weather: 2ºC Wet**
Item		
Sub-floor void	N/A	
Ventilation Inlets and Outlets	N/A	
Number Of Vents	N/A	
Materials used:	Membrane – Preprufe 300R Plus	
	Self-Adhesive Membrane ☒ Yes	Preformed Top hats ☐ Yes
	Double Sided Butyl Tape ☐ Yes	Preformed Corners ☐ Yes
	Others Please List: Bituthene LM. GCP Bituthene primer S2. Bituthene 8000/S tanking	
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** MTS Ltd carried out a thorough visual inspection of the tanking wrap installation. Preprufe 300R plus membrane has been lined across the core base area and extends up the vertical face of the core walls. Bituthene LM mix has been applied to the membrane on show at the top of the pile cap to help adhere the Bituthene 8000/S tanking which then extends over the toe and up the pre primed vertical RC wall to the required height as per the design drawings. Overlaps have been installed to the correct measurement and all tanking thoroughly rolled and adhered well to the walls. Site were carrying out their own ongoing inspections and where areas of air were trapped under the tanking, a slit was made in these small areas and a layer of Bituthene LM was applied prior to an addition piece of Bituthene 8000/S. The tanking installation was approx 20% completed when the inspection took place and all works were being carried out to a good standard.	

Type of Joint	Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐	
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)		
Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?		☒ Yes	☐ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?		☐ Yes	☐ No	☒ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?		☐ Yes	☐ No	☒ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?		☐ Yes	☐ No	☒ N/A
	Has all other detailing work passed inspection		☐ Yes	☐ No	☒ N/A
	(List any defects to detailing work and joints): During our inspection the following defects and repairs were carried out: No recorded defects other than noted prior to our inspection in he description of installation. Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A The Area has passed inspection ☒ The Area has failed inspection and a corrective action sheet has been left with the contractor ☐ The Area is incomplete as detailed above ☐ Signed: **Dan Squire** Date: **24/02/2022**				

Area Inspected



Photos **24/02/2022**



Bituthene LM installed to the top of the membrane to adhere to the tanking




Sealed repair to tanking



Core 5 tanking wrap installation



Core 5 tanking wrap installation

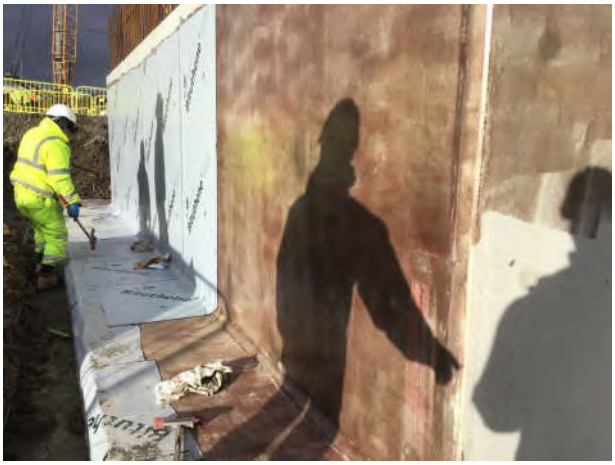

Pre primed RC walls

Test and Inspection Result 'PASS In FULL'

The areas has passed the inspection and a re-visit is not required.



Signed: Barrie Ackroyd Date: 24.2.2022

On Behalf of Membrane Testing Solutions Ltd

Co-Op Live, Manchester - C777
24.2.2022

Site name: BAM Construction. Co-Op Live. Manchester **Postcode: M11 3DU**	**Units/ plots checked: : Core 7 base Main floor installation Gridlines S11-S15 / SW3**
Installers Name: P J Carey's	
Date: 24/02/2022	
Inspection by: Dan Squire	**Weather: 2ºC Wet**

Item		
Sub-floor void	N/A	
Ventilation Inlets and Outlets	N/A	
Number Of Vents	N/A	
Materials used:	Membrane – Preprufe 300R Plus	
	Self-Adhesive Membrane ☒ Yes	Preformed Top hats ☐ Yes
	Double Sided Butyl Tape ☐ Yes	Preformed Corners ☐ Yes
	Others Please List: Bituthene LM. Bituthene Liquid membrane	
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** MTS Ltd carried out a thorough visual inspection of the membrane, the membrane had been installed to a good standard. Preprufe 300R plus membrane has been lined across the core base and is extended up the inside of the temporary shuttering which stays in place for 5 days after the pour to allow for the membrane to adhere to the concrete. The membrane has a permanent back binding which is used to join the membrane together and is pressure rolled. In some areas an additional strip of Preprufe Tape LT has been added on top of the joints. A mix of Bituthene LM & Bituthene liquid membrane is applied to seal all penetrations. Patch repairs have been made using Preprufe 300R plus membrane and strips of Preprufe LT tape. Site were carrying out their own ongoing inspections to check for any damages caused by the steelworks.	

Type of Joint	Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐		
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)			
Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?			☒ Yes	☐ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?			☒ Yes	☐ No	☐ N/A
	Has all other detailing work passed inspection			☐ Yes	☐ No	☒ N/A
	(List any defects to detailing work and joints): During our inspection the following defects and repairs were carried out: No recorded defects other than what had been previously repaired prior to the inspection as noted in the description of Installation. Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A The Area has passed inspection ☒ The Area has failed inspection and a corrective action sheet has been left with the contractor ☐ The Area is incomplete as detailed above ☐ Signed: **Dan Squire** Date: **24/02/2022**					

Area Inspected



Photos **24/02/2022**



Probe test to membrane joint



Sealed pile cap using Bituthene LM



Core 7 base membrane installation




Core 7 base inspection



Sealed pile cap using Bituthene LM

Test and Inspection Result 'PASS In FULL'

The areas has passed the inspection and a re-visit is not required.



Signed: Barrie Ackroyd Date: 24.2.2022

On Behalf of Membrane Testing Solutions Ltd

Co-Op Live, Manchester - C777
24.2.2022

Site name: BAM Construction. Co-Op Live. Manchester **Postcode: M11 3DU**	**Units/ plots checked: : Core 7 base Main floor installation Gridlines S11-S15 / SW3**
Installers Name: P J Carey's	
Date: 24/02/2022	
Inspection by: Dan Squire	**Weather: 2ºC Wet**

Item		
Sub-floor void	N/A	
Ventilation Inlets and Outlets	N/A	
Number Of Vents	N/A	
Materials used:	Membrane – Preprufe 300R Plus	
	Self-Adhesive Membrane ☒ Yes	Preformed Top hats ☐ Yes
	Double Sided Butyl Tape ☐ Yes	Preformed Corners ☐ Yes
	Others Please List: Bituthene LM. Bituthene Liquid membrane	
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** MTS Ltd carried out a thorough visual inspection of the membrane, the membrane had been installed to a good standard. Preprufe 300R plus membrane has been lined across the core base and is extended up the inside of the temporary shuttering which stays in place for 5 days after the pour to allow for the membrane to adhere to the concrete. The membrane has a permanent back binding which is used to join the membrane together and is pressure rolled. In some areas an additional strip of Preprufe Tape LT has been added on top of the joints. A mix of Bituthene LM & Bituthene liquid membrane is applied to seal all penetrations. Patch repairs have been made using Preprufe 300R plus membrane and strips of Preprufe LT tape. Site were carrying out their own ongoing inspections to check for any damages caused by the steelworks.	

Type of Joint	Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐		
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)			
Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?			☒ Yes	☐ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?			☒ Yes	☐ No	☐ N/A
	Has all other detailing work passed inspection			☐ Yes	☐ No	☒ N/A
	(List any defects to detailing work and joints): During our inspection the following defects and repairs were carried out: No recorded defects other than what had been previously repaired prior to the inspection as noted in the description of Installation. Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A The Area has passed inspection ☒ The Area has failed inspection and a corrective action sheet has been left with the contractor ☐ The Area is incomplete as detailed above ☐ Signed: **Dan Squire** Date: **24/02/2022**					

Area Inspected



Photos **24/02/2022**



Probe test to membrane joint



Sealed pile cap using Bituthene LM



Core 7 base membrane installation




Core 7 base inspection



Sealed pile cap using Bituthene LM

Test and Inspection Result 'PASS In FULL'

The areas has passed the inspection and a re-visit is not required.



Signed: Barrie Ackroyd Date: 24.2.2022

On Behalf of Membrane Testing Solutions Ltd

Co-Op Live, Manchester - C777
24.2.2022

Site name: BAM Construction. Co-Op Live. Manchester **Postcode: M11 3DU**	**Units/ plots checked: : South west slab - Pour 9. Main floor installation - Gridlines S1-S3 / NW - N01**
Installers Name: P J Carey's	
Date: 24/02/2022	
Inspection by: Dan Squire	**Weather: 2ºC Wet**

Item		
Sub-floor void	N/A	
Ventilation Inlets and Outlets	N/A	
Number Of Vents	N/A	
Materials used:	Membrane – Preprufe 300R Plus	
	Self-Adhesive Membrane ☒ Yes	Preformed Top hats ☐ Yes
	Double Sided Butyl Tape ☐ Yes	Preformed Corners ☐ Yes
	Others Please List: Bituthene LM. Bituthene Liquid membrane	
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** MTS Ltd carried out a thorough visual inspection of the membrane, the membrane had been installed to a good standard. Preprufe 300R plus membrane has been lined across the pour slab areas as noted and is joined to the membrane previously installed up the liner wall to the capping beam. The membrane has a permanent back binding which is used to join the membrane together and is pressure rolled. In some areas an additional strip of Preprufe Tape LT has been added on top of the joints. A mix of Bituthene LM & Bituthene liquid membrane is applied to seal all penetrations. Patch repairs have been made to the membrane along the vertical face of the liner wall using Preprufe 300R plus membrane and strips of Preprufe LT tape. Site were carrying out their own ongoing inspections and cleaning off the membrane as the install progressed and prior to the pour.	

Type of Joint	Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐		
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)			
Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?			☒ Yes	☐ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?			☒ Yes	☐ No	☐ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Has all other detailing work passed inspection			☒ Yes	☐ No	☐ N/A
	(List any defects to detailing work and joints): During our inspection the following defects and repairs were carried out: No recorded defects other than what had been previously repaired prior to the inspection as noted in the description of Installation. Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A The Area has passed inspection ☒ The Area has failed inspection and a corrective action sheet has been left with the contractor ☐ The Area is incomplete as detailed above ☐ Signed: **Dan Squire** Date: **24/02/2022**					

Area Inspected



Photos **24/02/2022**



South west pour 9 line out installation



Sealed penetrations using Bituthene LM and liquid membrane mix



Sealed liner wall patch repair



Probe test inspection



Membrane sealed and joined to the liner wall



Sealed main floor patch repair



Sealed steel bars using Bituthene LM and liquid membrane mix

Test and Inspection Result 'PASS In FULL'

The areas has passed the inspection and a re-visit is not required.

Signed: Barrie Ackroyd Date: 24.2.2022

On Behalf of Membrane Testing Solutions Ltd

Co-Op Live, Manchester - C777
5.4.2022

Site name: BAM Construction, CoOp Live, Manchester. **Postcode: M11 3DU**	**Units/ plots checked: : Sprinkler room pool 2, gridlines S15.8/S17.5 - FS/GS. Buttress walls gridlines E06 - E07**
Installers Name: P J Carey	
Date: 05/04/2022	
Inspection by: Keith Barsby	**Weather: 11°C DRY**

Item	Comments	
Sub-floor void	N/A	
Ventilation Inlets and Outlets	N/A	
Number Of Vents	N/A	
Materials used:	Membrane – Preprufe 300R Plus	
	Self-Adhesive Membrane ☒ Yes	Preformed Top hats ☐ Yes
	Double Sided Butyl Tape ☐ Yes	Preformed Corners ☐ Yes
	Others Please List: Bituthene LM (Liquid Membrane)	
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** MTS carried out a thorough visual inspection of the membrane, the membrane had been installed to a good standard. Sprinkler Room: The membrane has been installed across the concrete base and turned up 90deg against the piles. The piles have been sealed to the membrane using Bituthene LM which has been applied to the pile cap and the membrane. The fixings through the membrane on the walls have been sealed using patches of Preprufe 300R Plus membrane with Preprufe LT tape.	

Installation Notes	The fixings through the membrane have been sealed using patches of Preprufe 300R Plus membrane and PrepLT tape. The Sprinkler Room is highlighted in Red and the Buttress Walls are highlighted in Blue on the attached drawing.			
Type of Joint	Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)	
Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?	☒ Yes	☐ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?	☐ Yes	☒ No	☐ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?	☐ Yes	☐ No	☒ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?	☒ Yes	☐ No	☐ N/A
	Has all other detailing work passed inspection	☒ Yes	☐ No	☐ N/A
	(List any defects to detailing work and joints): During our inspection the following defects and repairs were carried out: None. Sprinkler Room: It was noted during our inspection that there has been some water ingress below the membrane in the lower floor area after it was installed, this was being pumped out during our inspection. Buttress walls: it was noted that there is to be a design change for the pipe penetrations and where the membrane joins at the base of the walls onto the concrete blinding. Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A The Area has passed inspection ☒ The Area has failed inspection and a corrective action sheet has been left with the contractor ☐ The Area is incomplete as detailed above ☐ Signed: **Keith Barsby** Date: **05/04/2022**			

Area Inspected

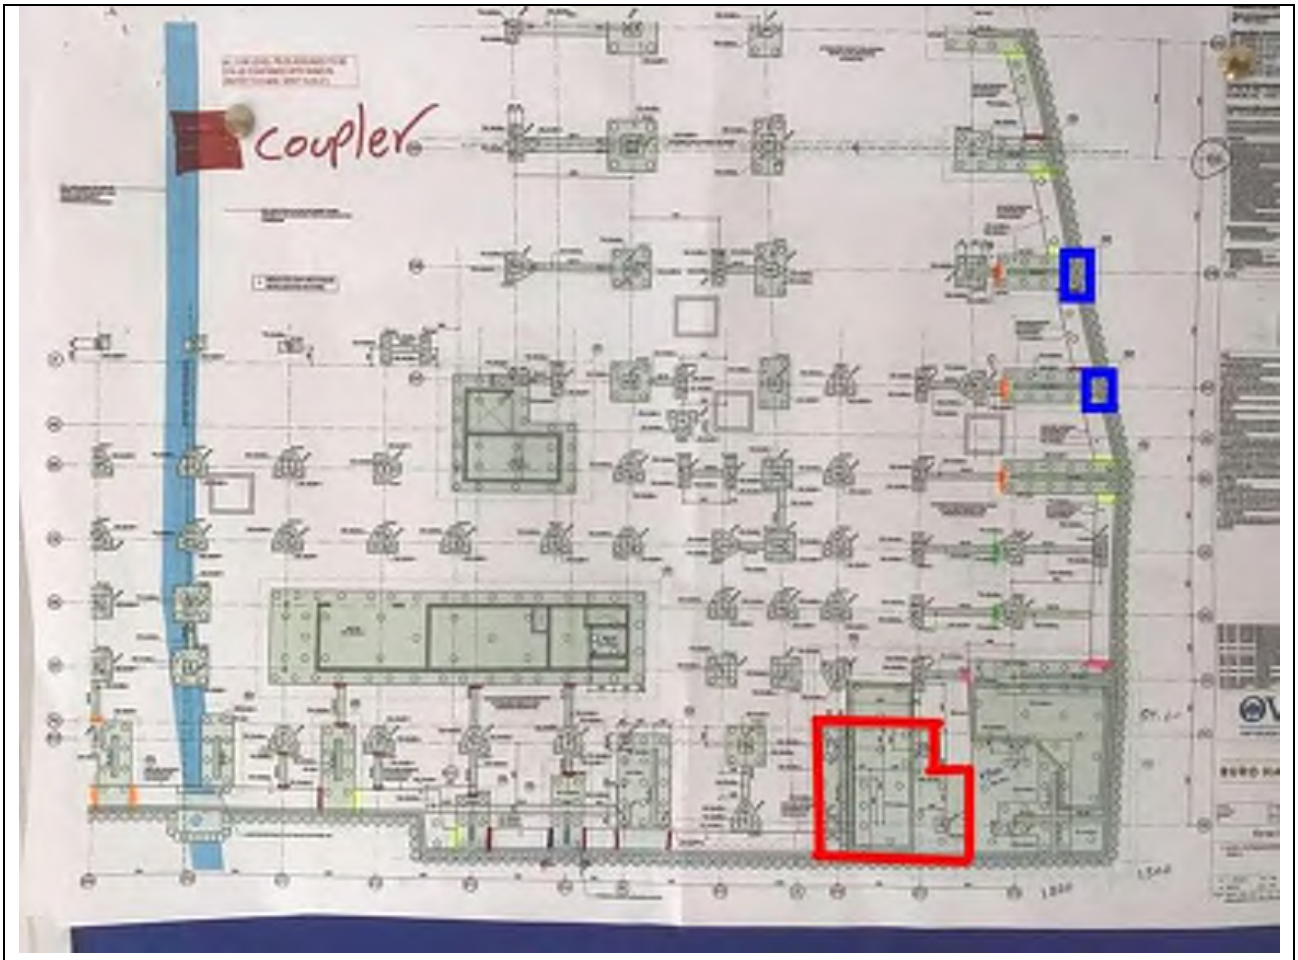


Photo **05/04/2022**



Overview of Sprinkler Room



Sprinkler Room pile cap seal



Sprinkler Room pile cap seal being pick tested



Sprinkler Room membrane joint being pick tested



Buttress walls vertical membrane being installed



Vertical membrane behind the steel cage for the buttress wall, Bituthene LM at the top edge of the membrane and movement joint



Patch using Preprufe 300R Plus and Preprufe LT tape

Test and Inspection Result 'PASS In FULL'

The areas has passed the inspection and a re-visit is not required.

Signed: Barrie Ackroyd Date: 5.4.2022

On Behalf of Membrane Testing Solutions Ltd

Co-Op Live, Manchester - C777
30.6.2022

Site name: BAM Construction, CoOp Live, Manchester. **Postcode: M11 3DU**	**Units/ plots checked: Sprinkler tank area gridlines S15.8/S17.5 south liner walls gridlines S13/S15 - Liner walls east gridlines E04/E06**
Installers Name: P J Carey	
Date: 30/06/2022	
Inspection by: Keith Barsby	**Weather: 22°C DRY**

Item	Comments	
Sub-floor void	N/A	
Ventilation Inlets and Outlets	N/A	
Number Of Vents	N/A	
Materials used:	Membrane – Preprufe 300R Plus	
	Self-Adhesive Membrane ☒ Yes	Preformed Top hats ☐ Yes
	Double Sided Butyl Tape ☐ Yes	Preformed Corners ☐ Yes
	Others Please List: Bituthene LM (Liquid Membrane)	
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** MTS carried out a thorough visual inspection of the membrane, the membrane had been installed to a good standard. Preprufe 300R Plus has been installed vertically against the piles, it has been sealed at the top using Bituthene LM, which we were unable to inspect due to the height. The reinforcement mesh for the walls will be installed against the Preprufe 300R Plus membrane. The fixings through the membrane have been sealed using patches of Preprufe 300R Plus membrane, PrepLT tape and Bituthene LM.	

Type of Joint	Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)	

Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?	☒ Yes	☐ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?	☐ Yes	☐ No	☒ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?	☐ Yes	☐ No	☒ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?	☒ Yes	☐ No	☐ N/A
	Has all other detailing work passed inspection	☒ Yes	☐ No	☐ N/A

(List any defects to detailing work and joints):

During our inspection the following defects and repairs were carried out: None.

Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A

The Area has passed inspection ☒

The Area has failed inspection and a corrective action sheet has been left with the contractor ☐

The Area is incomplete as detailed above ☐

Signed: **Keith Barsby** Date: **30/06/2022**

Area Inspected


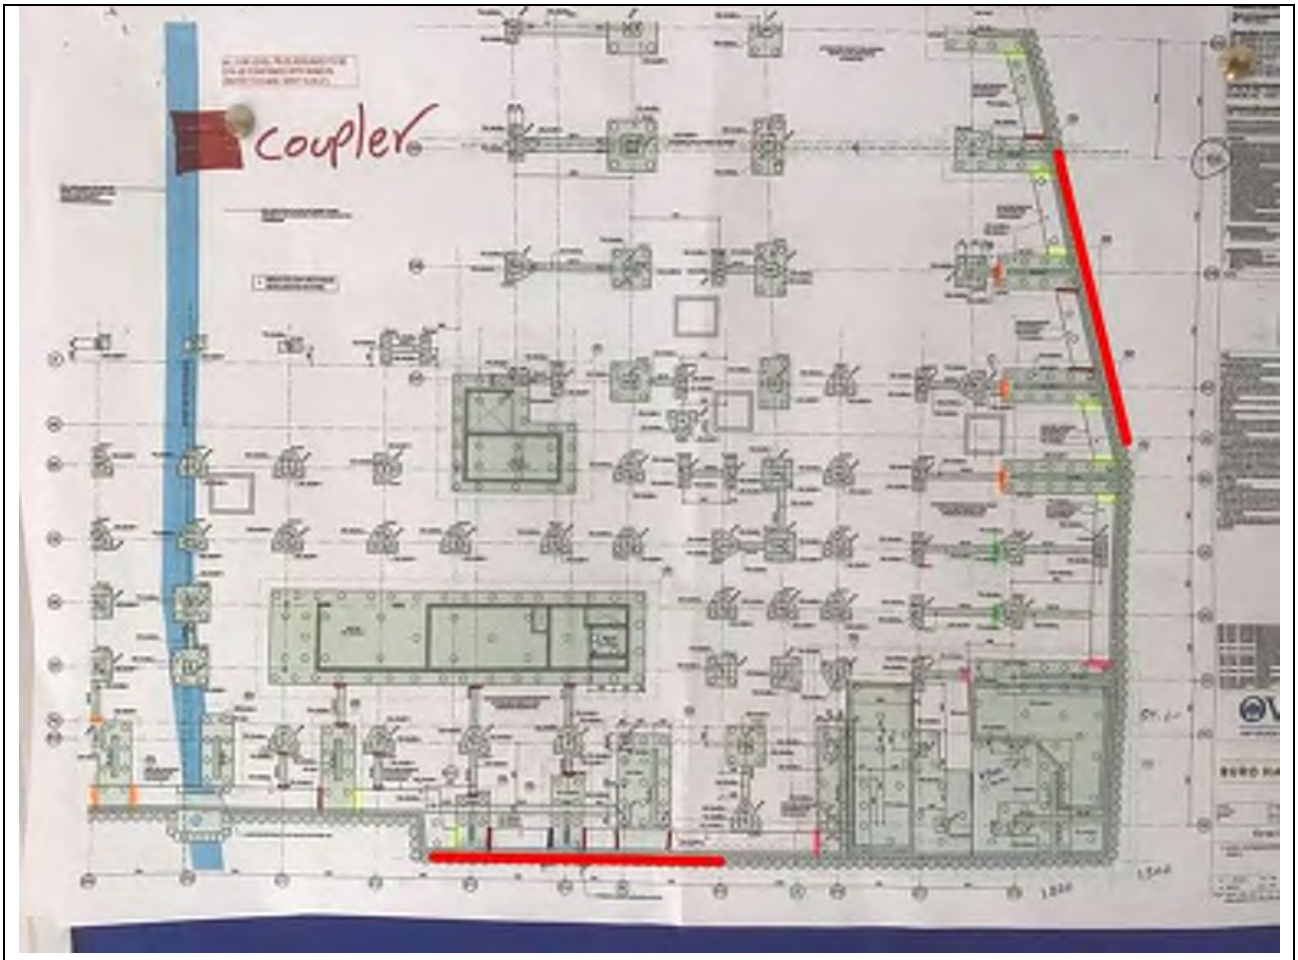


Photo **30/06/2022**



Tape joint being pick tested

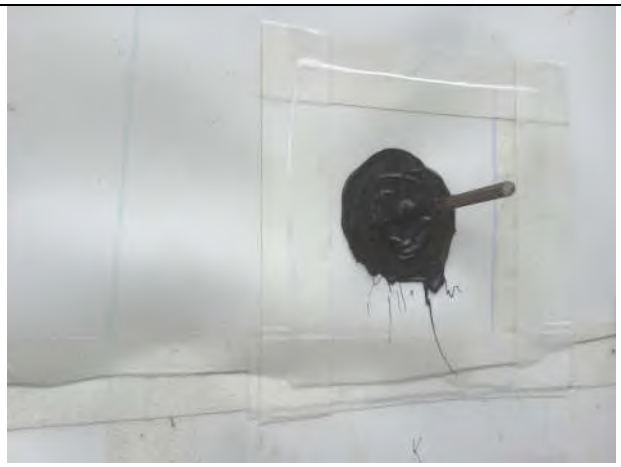

Penetration fixing sealed



Overview of wall



Overview of wall



Overview of site

Test and Inspection Result 'PASS In FULL'

The areas has passed the inspection and a re-visit is not required.



Signed: Barrie Ackroyd Date: 30.6.2022

On Behalf of Membrane Testing Solutions Ltd

Co-Op Live, Manchester - C777
23.8.2022

Site name: BAM Construction. Co-Op Live. Manchester **Postcode: M11 3DU**	**Units/ plots checked: : Core 1 Tanking to pre cast walls. Approx 12m. Gridlines N01-N04 / NW2-NW3**
Installers Name: PJ Careys	
Date: 23/08/2022	
Inspection by: Dan Squire	**Weather: 19°C Dry**

	Item		
Sub-floor void	N/A		
Ventilation Inlets and Outlets	N/A		
Number Of Vents	N/A		
Materials used:	Membrane – Preprufe 300R Plus		
	Self-Adhesive Membrane ☒ Yes	Preformed Top hats ☐ Yes	
	Double Sided Butyl Tape ☐ Yes	Preformed Corners ☐ Yes	
	Others Please List: Bituthene 8000 tanking		
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** MTS Ltd carried out a thorough visual inspection of the membrane, the membrane had been installed to a good standard. Preprufe 300R plus membrane has been previously lined across the core base and is extended up the toe and joins to the Bituthene 8000 tanking which has been adhered to the pre cast walls up to the correct height as per the design detail. Approx 12 meters of tanking has been installed at the time of the inspection to the west and south facing core walls. Site were carrying out their own ongoing inspections to check for any damages caused by the steelworks and follow-on trades. On the marked drawing the area in red is the full core area. The area in yellow is the completed tanking works.		

Type of Joint	Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐		
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)			
Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?			☒ Yes	☐ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Has all other detailing work passed inspection			☒ Yes	☐ No	☐ N/A
	(List any defects to detailing work and joints): During our inspection the following defects and repairs were carried out: No recorded defects. Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A The Area has passed inspection ☐ The Area has failed inspection and a corrective action sheet has been left with the contractor ☐ The Area is incomplete as detailed above ☒ Signed: **Dan Squire** Date: **23/08/2022**					

Area Inspected



Photo **23/08/2022**



Tanking pick testing



South side facing core tanking



South side facing core tanking



Bituthene joined to Preprufe membrane previously installed under the slab



West side facing core tanking

Test and Inspection Result 'PASS Work in Progress'

The area whilst incomplete has passed the inspection and a re-visit is not required.



Signed: Barrie Ackroyd Date: 23.8.2022

On Behalf of Membrane Testing Solutions Ltd

Co-Op Live, Manchester - C777
25.1.2023

Site name: BAM Construction. Co-Op Live. Manchester **Postcode: M11 3DU**	**Units/ plots checked: : South west slab east of core 6. See marked up plan in red**
Installers Name: PJ Carey's	
Date: 25/01/2023	
Inspection by: Dan Squire	**Weather: 7°C Light rain**

Item		
Sub-floor void	N/A	
Ventilation Inlets and Outlets	N/A	
Number Of Vents	N/A	
Materials used:	Membrane – Preprufe 300R Plus	
	Self-Adhesive Membrane ☐ Yes	Preformed Top hats ☐ Yes
	Double Sided Butyl Tape ☒ Yes	Preformed Corners ☐ Yes
	Others Please List: Preprufe Lap tape	
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** MTS Ltd carried out a thorough visual inspection of the membrane, the membrane had been installed to a good standard. Preprufe 300R membrane has been lined across footprint of the slab. Joining onto the membrane previously layed under the slab previously poured. The membrane has a permanent back binding which is used to join the membrane together and is pressure rolled. Additional Lap tap is then installed over the membrane joints.	

	At the time of our inspection the membrane works were ongoing and incomplete. The detailing areas including the pipe penetrations and stanchions were yet to be sealed using the Bituthene LM black sealant. All other works in this area were being installed to a good standard. During the inspection we were shown two other areas to the north and north east side of the building to talk through the membrane and build process. The north area needed to be cleaned and jet washed and the north east area had steel work placed over the membrane ready for the pour. These areas have not been inspected and are marked in yellow on the marked up plan. Site were carrying out there own ongoing inspections as the works progressed.					
Type of Joint	Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐		
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)			
Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?			☒ Yes	☐ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Has all other detailing work passed inspection			☐ Yes	☐ No	☒ N/A
	(List any defects to detailing work and joints): During our inspection the following defects and repairs were carried out: N/A Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A The Area has passed inspection ☐ The Area has failed inspection and a corrective action sheet has been left with the contractor ☐ The Area is incomplete as detailed above ☒ Signed: **Dan Squire** Date: **25/01/2023**					

Area Inspected

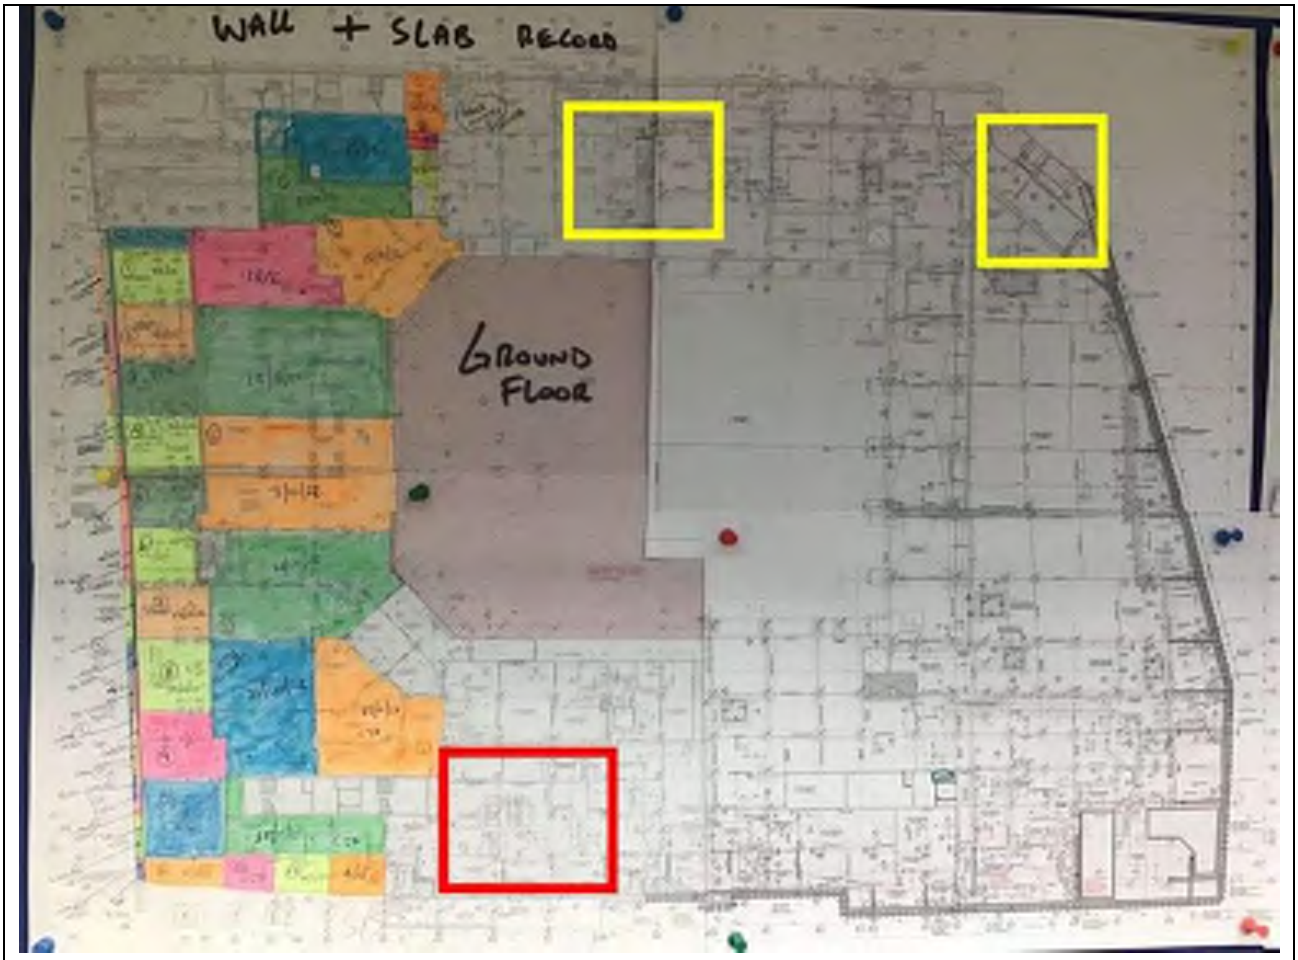


Photo **25/01/2023**



Pressure roller used to join the membrane



Membrane joining onto previously installed upper level



Stanchion detail yet to be sealed



South slab continued membrane full line out installation



Lined perimeter corner detailing



Pick testing to sealed lap joints



Sealed corner detailing



Sealed corner detail



Area unable for inspection ready for concrete



South slab continued membrane full line out installation

Test and Inspection Result 'PASS Work in Progress'

The area whilst incomplete has passed the inspection and a re-visit is not required.

Signed: Barrie Ackroyd Date: 25.1.2023

On Behalf of Membrane Testing Solutions Ltd

Co-Op Live, Manchester - C777
7.8.2023

Site name: BAM Construction. Co-Op Live. Manchester **Postcode: M11 3DU**	**Units/ plots checked:** **Bowl slab area to gridlines E01-E04 & N10-AE** **See plan mark-up in RED**
Installers Name: PJ Carey's	
Date: 07/08/2023	
Inspection by: Barrie Ackroyd	**Weather: 14°C Dry with Sunny Intervals**

Item		
Sub-floor void	N/A	
Ventilation Inlets and Outlets	N/A	
Number Of Vents	N/A	
Materials used:	Membrane – Preprufe 300R Plus	
	Self-Adhesive Membrane ☐ Yes	Preformed Top hats ☐ Yes
	Double Sided Butyl Tape ☒ Yes	Preformed Corners ☐ Yes
	Others Please List: Preprufe Lap tape	
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** Upon initial inspection we noted the majority of the Preprufe 300R Plus membrane had been covered with steel reinforcing bars meaning the majority of the membrane seams were unable to be inspected below the steel reinforcement. However, there was an area where the membrane installation was ongoing and being completed with lap tape over non-compliant membrane seams. The membrane seams in this area proved to be well sealed and fully bonded in the carried-out a thorough visual inspection of the membrane, the membrane had been installed to a good standard. We then checked down the raft slab edge which was incomplete and we noted some areas of the Waterbar was not bonded to the Preprufe 300R membrane, there were also holes drilled through the membrane which will require remedial works.	

	There were also steel stanchion depressions which are to be boxed out and repaired at a later date using the appropriate sealing detail. Our surveyor performed a detailed visual inspection of the membrane seams below the steel reinforcement and marked up two de-bonded areas with blue spray paint. There were also two additional seam debond areas adjacent to steel stanchion depressions which were also marked with blue spray paint. At the time of our inspection the membrane works were ongoing and incomplete. Site are performing their own ongoing inspections as the works progress, however MTS Ltd requested a copy of BAM's QA sign off documentation once the remedial works and BAM reinspection has been performed.					
Type of Joint	Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐		
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)			
Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?			☐ Yes	☒ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?			☐ Yes	☒ No	☐ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Has all other detailing work passed inspection			☐ Yes	☒ No	☐ N/A
	<u>(List any defects to detailing work and joints):</u> During our inspection the following defects and repairs were carried out: Repairs are to be performed to the marked-up areas. Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A The Area has passed inspection ☐ The Area has failed inspection and a corrective action sheet has been left with the contractor ☐ The Area is incomplete as detailed above ☒ Signed: **Barrie Ackroyd** Date: **07/08/2023**					

Area Inspected

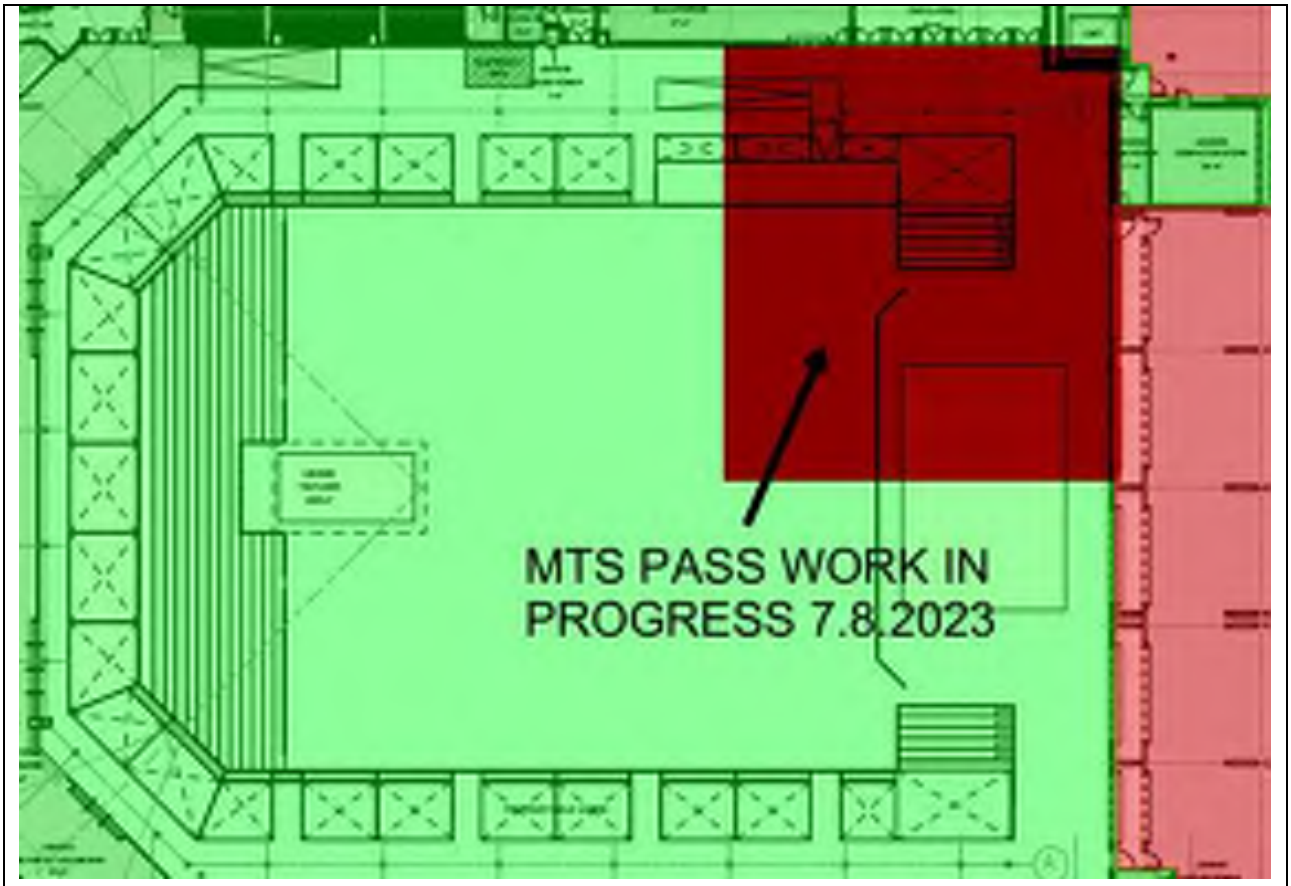


Photo **07/08/2023**




Pressure roller used to join the membrane



Ongoing membrane sealing detail



Seam pick testing performed to site seams

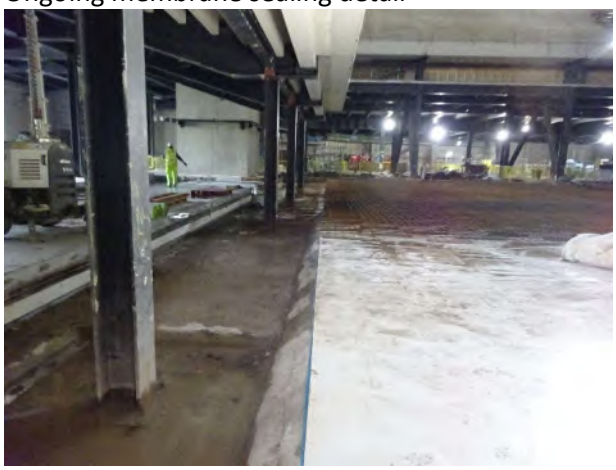

North elevation of raft slab edge with continued membrane full line out installation



Material overlap and seaming detailing (Note the blue line is visible which required overlap tape being applied above



Overlap tape applied to non-compliant seams (passed inspection)



North slab edge incomplete




Drill marks through membrane marked for repair




Defective join between Waterbar and gas membrane



Steel stanchion sealing incomplete

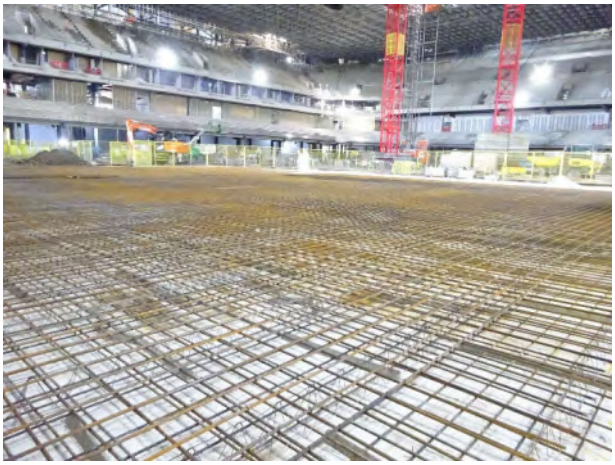

General overview of installed reinforcing bar above gas membrane

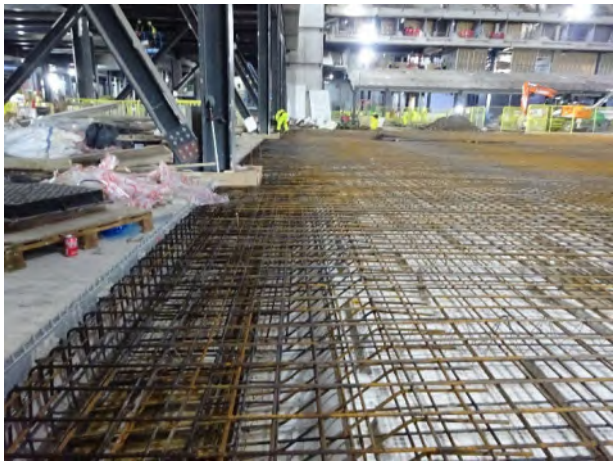

East slab edge membrane sealing detail



Seam pick testing of membrane seams, noting a seam debond defect



Lap tape debond defect marked and noted for repair




Vertical tape joint debond defect marked up and photographed



Vertical tape joint debond defect marked up and photographed



Seam bond defect marked for repair

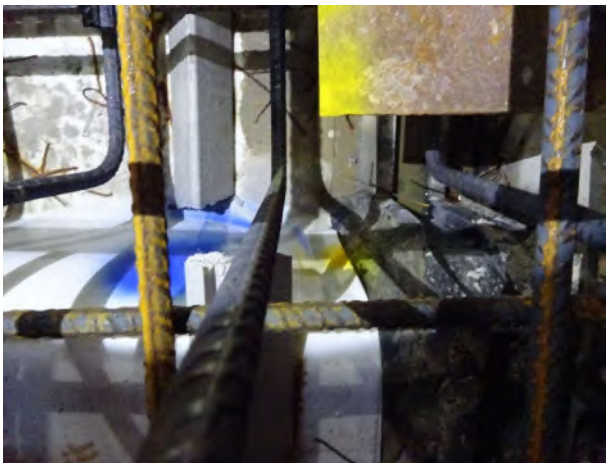

Seam lap tape bond defect marked for repair

Test and Inspection Result 'PASS Work in Progress'

The area whilst incomplete has passed the inspection and a re-visit is not required.

Bam have been requested to forward a copy of their QA sign off report as evidence of the defect repairs for inclusion within our final sign off validation report.



Signed: Barrie Ackroyd Date: 7.8.2023

On Behalf of Membrane Testing Solutions Ltd

MembraneTestingSolutions

PHOTOGRAPHIC VALIDATION EVENT, INSPECTION CERTIFICATE OF INSTALLATION

DATE: 12.9.2023

PROJECT NAME: CO-OP LIVE, MANCHESTER

CONTRACT NO: C777 - Bowl Area to Gridlines: E01-E04 & N10-AE

PHOTOGRAPHIC INSPECTION & VALIDATION DETAILS:

MTS Ltd attended site under instruction on the 7.8.2023 to perform a detailed visual examination and seam pick testing to the above area. during our site visit there were a number of seam de-bond defects and punctures which were marked with blue paint. Unfortunately the repairs were unable to be performed at that time, therefore it was agreed MTS Ltd would accept photographic validation of the completed repairs. MTS Ltd received a completion and close out report from BAM on the 6.9.2023 which evinces the repairs have been performed using Cordeck LM material and upon a detailed visual examination we are pleased to advise all repairs have been completed and on this basis we are also pleased to close out the original pass work in progress certificate issued on the 7.8.2023. On this basis we are pleased to advise a pass in full has been acheived. A copy of the BAM close out report is appended to this certificate as evidence towards this close out photographic validation certificate.

MembraneTestingSolutions Ltd hereby confirm that the elements of the project detailed above have been photographically inspected, reviewed and validated by a suitably qualified independent consultant in accordance with industry requirements, with the test result noted below:

CONCLUSION (PASS/~~FAIL~~) PASS IN FULL

Where the conclusion above indicates a Pass, the construction activities may proceed subject to suitable protection measures of the membrane being applied in accordance with the manufacturer's recommendations.

Signed for on behalf of MembraneTestingSolutions Ltd:

Name: BARRIE ACKROYD

Dated: 12.9.2023

Membrane Testing Solutions Limited • The Studio, Parsonage House, Parsonage Street, Halstead, Essex CO9 2JR

Telephone: 0844 557 3786 • email: sales@mtsltd.net • www.mtsltd.net

Registered Office: 1, Second Avenue, Halstead, Essex. CO9 2SU • Company Registration Number: 8871015

Issue detail

#6631: Event Floor 1 - WP still not bonded in some areas

Standard fields

Status	**Closed**
Type	Quality > Quality
Description	Please see Daniel Allen this morning to close out the waterproofing issues. All holes bar one on the north side have been sealed. Some of the severseal has been sealed and blocked off but there are still some gaps on the north side, there is still one you can get you hand inside. Both column bases on east also need some repairs to vertical pieces Two snags from independents survey on pre-proof joints Need LM and blocks this morning
Assigned to	**Careys Civil Engineering**
Created by	**Daniel Allen** (BAM Construct UK)
Created on	Aug 15, 2023
Issue owner	**Daniel Allen** (BAM Construct UK)
Location	Arena
Location details	See map in blue, and yellow spray marks on site on top mat
Due date	Aug 15, 2023
Root cause	BAM Standard > Workmanship
Checklist source	3556 - 927 -CONCRETE PRE POUR INSPECTION RECORD - (CAREYS) BOWL FIRST POUR NE

Custom fields

Cost Impact	—

Severity —


Images



IMG_20230814_133818.jpg
Added on Aug 15, 2023, 6:59 AM BST
Added by Daniel Allen



IMG_20230814_135034.jpg
Added on Aug 15, 2023, 6:59 AM BST
Added by Daniel Allen

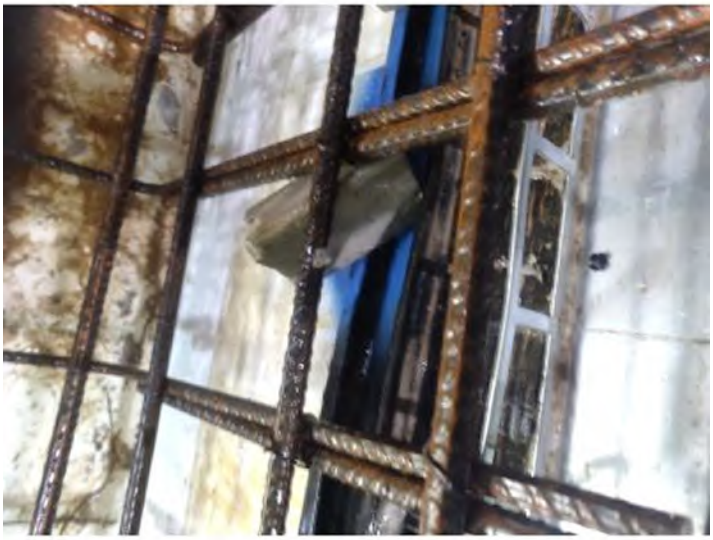

IMG_20230814_133920.jpg
Added on Aug 15, 2023, 6:59 AM BST
Added by Daniel Allen




IMG_20230814_133753.jpg
Added on Aug 15, 2023, 6:59 AM BST
Added by Daniel Allen



IMG_20230814_134847.jpg
Added on Aug 15, 2023, 6:59 AM BST
Added by Daniel Allen



IMG_20230814_135131.jpg
Added on Aug 15, 2023, 6:59 AM BST
Added by Daniel Allen

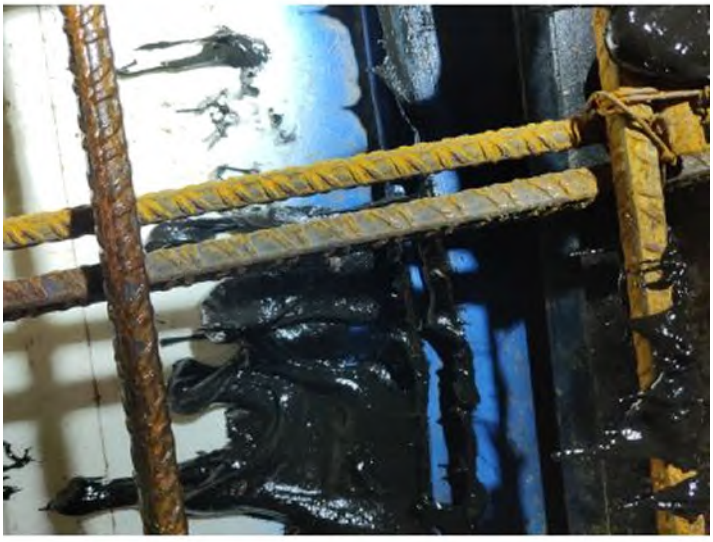

IMG_20230815_073859.jpg
Added on Sep 6, 2023, 7:56 AM BST
Added by Daniel Allen



IMG_20230815_073910.jpg
Added on Sep 6, 2023, 7:57 AM BST
Added by Daniel Allen



IMG_20230815_072715.jpg
Added on Sep 6, 2023, 7:56 AM BST
Added by Daniel Allen



IMG_20230815_073833.jpg
Added on Sep 6, 2023, 7:56 AM BST
Added by Daniel Allen



IMG_20230815_080706.jpg
Added on Sep 6, 2023, 7:56 AM BST
Added by Daniel Allen



IMG_20230815_073811.jpg
Added on Sep 6, 2023, 7:57 AM BST
Added by Daniel Allen



IMG_20230815_073838.jpg
Added on Sep 6, 2023, 7:56 AM BST
Added by Daniel Allen



IMG_20230815_080654.jpg
Added on Sep 6, 2023, 7:57 AM BST
Added by Daniel Allen



IMG_20230815_072628.jpg
Added on Sep 6, 2023, 7:56 AM BST
Added by Daniel Allen



IMG_20230815_080617.jpg
Added on Sep 6, 2023, 7:57 AM BST
Added by Daniel Allen



IMG_20230815_080651.jpg
Added on Sep 6, 2023, 7:57 AM BST
Added by Daniel Allen



IMG_20230815_073819.jpg
Added on Sep 6, 2023, 7:57 AM BST
Added by Daniel Allen



IMG_20230815_080611.jpg
Added on Sep 6, 2023, 7:57 AM BST
Added by Daniel Allen

Co-Op Live, Manchester - C777
7.8.2023

Site name: BAM Construction. Co-Op Live. Manchester **Postcode: M11 3DU**	**Units/ plots checked:** **Bowl slab area to gridlines E01-E04 & N10-AE** **See plan mark-up in RED**
Installers Name: PJ Carey's	
Date: 07/08/2023	
Inspection by: Barrie Ackroyd	**Weather: 14°C Dry with Sunny Intervals**

	Item		
Sub-floor void	N/A		
Ventilation Inlets and Outlets	N/A		
Number Of Vents	N/A		
Materials used:	Membrane – Preprufe 300R Plus		
	Self-Adhesive Membrane ☐ Yes	Preformed Top hats ☐ Yes	
	Double Sided Butyl Tape ☒ Yes	Preformed Corners ☐ Yes	
	Others Please List: Preprufe Lap tape		
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** Upon initial inspection we noted the majority of the Preprufe 300R Plus membrane had been covered with steel reinforcing bars meaning the majority of the membrane seams were unable to be inspected below the steel reinforcement. However, there was an area where the membrane installation was ongoing and being completed with lap tape over non-compliant membrane seams. The membrane seams in this area proved to be well sealed and fully bonded in the carried-out a thorough visual inspection of the membrane, the membrane had been installed to a good standard. We then checked down the raft slab edge which was incomplete and we noted some areas of the Waterbar was not bonded to the Preprufe 300R membrane, there were also holes drilled through the membrane which will require remedial works.		

	There were also steel stanchion depressions which are to be boxed out and repaired at a later date using the appropriate sealing detail. Our surveyor performed a detailed visual inspection of the membrane seams below the steel reinforcement and marked up two de-bonded areas with blue spray paint. There were also two additional seam debond areas adjacent to steel stanchion depressions which were also marked with blue spray paint. At the time of our inspection the membrane works were ongoing and incomplete. Site are performing their own ongoing inspections as the works progress, however MTS Ltd requested a copy of BAM's QA sign off documentation once the remedial works and BAM reinspection has been performed.					
Type of Joint	Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐		
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)			
Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?			☐ Yes	☒ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?			☐ Yes	☒ No	☐ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Has all other detailing work passed inspection			☐ Yes	☒ No	☐ N/A
	<u>(List any defects to detailing work and joints):</u> During our inspection the following defects and repairs were carried out: Repairs are to be performed to the marked-up areas. Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A The Area has passed inspection ☐ The Area has failed inspection and a corrective action sheet has been left with the contractor ☐ The Area is incomplete as detailed above ☒ Signed: **Barrie Ackroyd** Date: **07/08/2023**					

Area Inspected

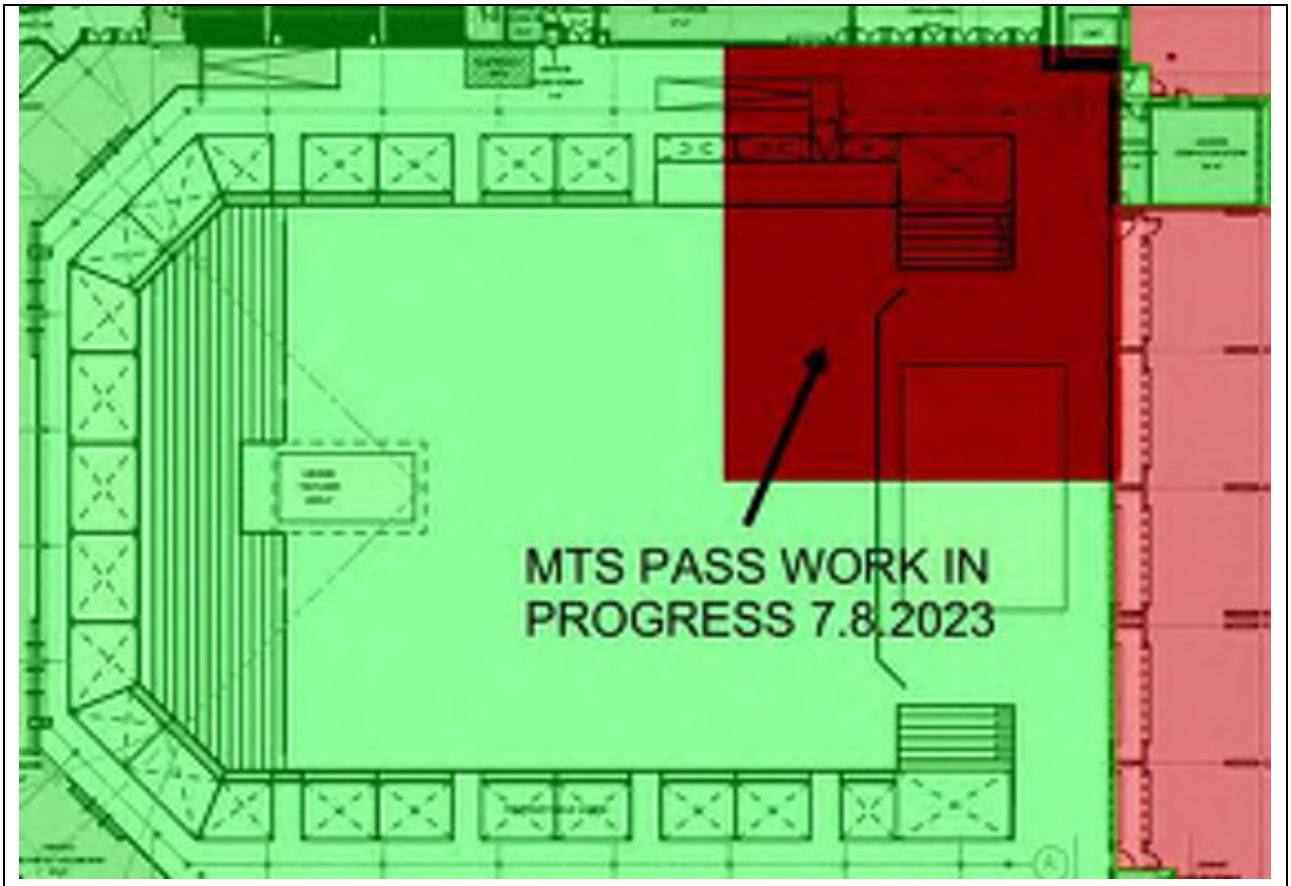


Photo **07/08/2023**




Pressure roller used to join the membrane



Ongoing membrane sealing detail



Seam pick testing performed to site seams

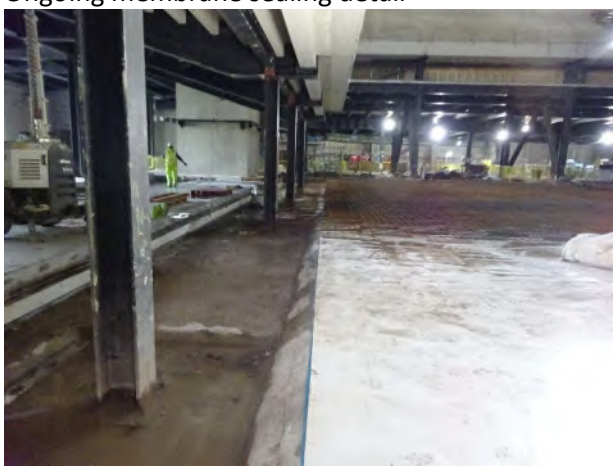

North elevation of raft slab edge with continued membrane full line out installation



Material overlap and seaming detailing (Note the blue line is visible which required overlap tape being applied above



Overlap tape applied to non-compliant seams (passed inspection)



North slab edge incomplete




Drill marks through membrane marked for repair




Defective join between Waterbar and gas membrane



Steel stanchion sealing incomplete

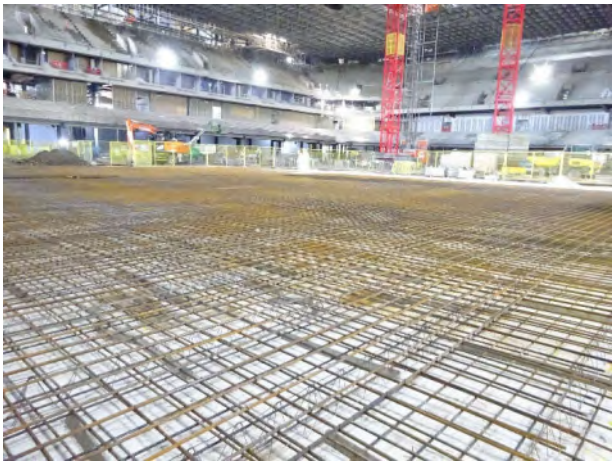

General overview of installed reinforcing bar above gas membrane

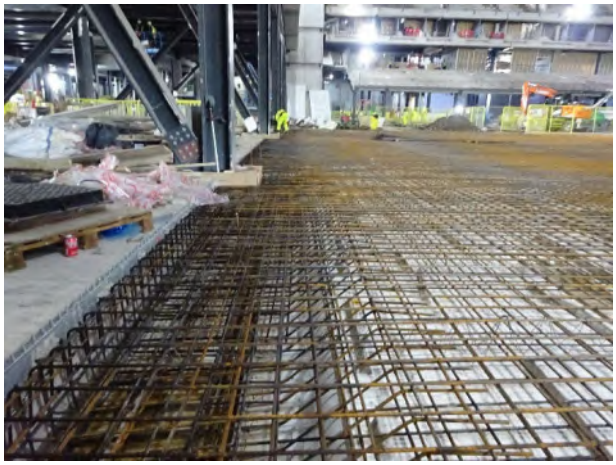

East slab edge membrane sealing detail



Seam pick testing of membrane seams, noting a seam debond defect



Lap tape debond defect marked and noted for repair



Vertical tape joint debond defect marked up and photographed



Vertical tape joint debond defect marked up and photographed



Seam bond defect marked for repair



Seam lap tape bond defect marked for repair

Test and Inspection Result 'PASS Work in Progress' REJECTED 12.9.2023

The area whilst incomplete has passed the inspection and a re-visit is not required.

Bam have been requested to forward a copy of their QA sign off report as evidence of the defect repairs for inclusion within our final sign off validation report.

Signed: Barrie Ackroyd Date: 7.8.2023

On Behalf of Membrane Testing Solutions Ltd

Co-Op Live, Manchester - C777

29.09.2023

Site name: BAM Construction. Co-Op Live. Manchester **Postcode:** M11 3DU	**Units/ plots checked:** Perimeter tanking and waterproofing detail. See marked up plan
Installers Name: P J Carey's & Waterseal	
Date: 29/09/2023	
Inspection by: Dan Squire	**Weather:** 12°C Dry


Item	Comments
Sub-floor void	N/A
Ventilation Inlets and Outlets	N/A
Number Of Vents	N/A
Materials used:	Membrane – Preprufe 300R Plus Self-Adhesive Membrane ☒ Yes — Preformed Top hats ☐ Yes Double Sided Butyl Tape ☐ Yes — Preformed Corners ☐ Yes Others Please List: Bituthene 8000. S2 Primer Bituthene. Grace Integritank waterproofing spray system
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** MTS Ltd carried out a thorough visual inspection of the waterproofing and membrane works. the works had been installed to a good standard. Bituthene 8000 has been installed by P J Carey's to the area marked in red. Sealed to the required height of the walls and joined to the Preprufe membrane previously installed under the concrete walls. An additional layer of S2 primer is installed to the walls prior to the Bituthene 8000 installation. Bituthene LM black sealant is used between the joints of the 8000 tanking and existing Preprufe membrane. Holes were being drilled through the 8000 tanking to allow for dowels to be installed. These dowels will be sealed using Bituthene LM black sealant at a later date and re inspected. On the concrete panels marked in green on the plan waterseal have installed Integritank waterproofing spray. At a later date the main concrete slab will be coated in the spray and tie in with the panels already sprayed.

Type of Joint	Tape Joint ☐	Auto Weld ☒	Hand Weld ☒	Extrusion Weld ☐		
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)			
Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?			☒ Yes	☐ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Has all other detailing work passed inspection			☒ Yes	☐ No	☐ N/A
	(List any defects to detailing work and joints): During our inspection the following defects and repairs were carried out: N/A Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A The Area has passed inspection ☒ The Area has failed inspection and a corrective action sheet has been left with the contractor ☐ The Area is incomplete as detailed above ☐ Signed: **Dan Squire** Date: **29/09/2023**					

Area Inspected



Photo 29/09/2023

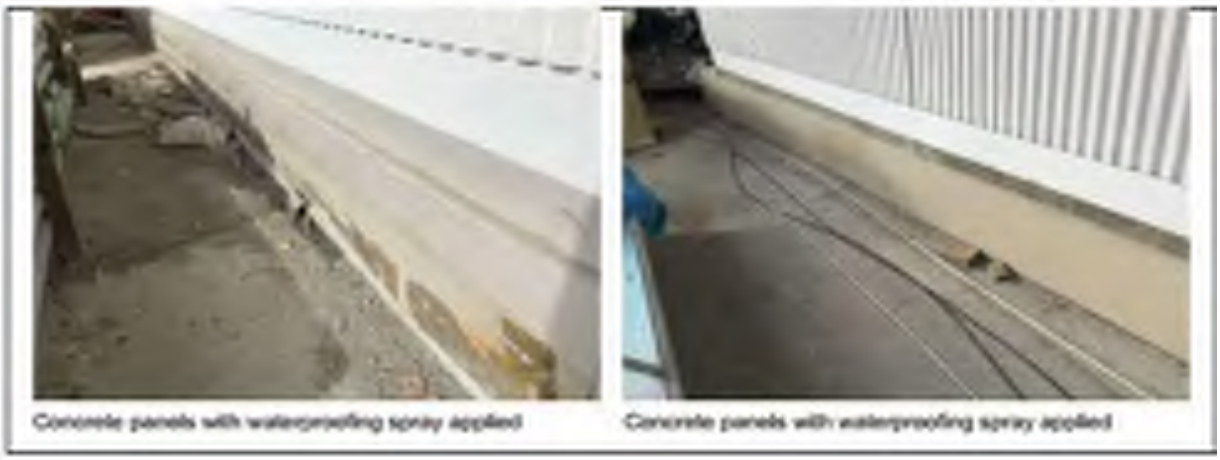


Concrete panels with waterproofing spray applied

Concrete panels with waterproofing spray applied

Membrane Testing Solutions Limited • The Studio, Parsonage House, Parsonage Street, Halstead, Essex CO9 2JR

Telephone: 0844 557 3786 • email: sales@mtsltd.net • www.mtsltd.net

Registered Office: 1, Second Avenue, Halstead, Essex. CO9 2SU • Company Registration Number: 8871015

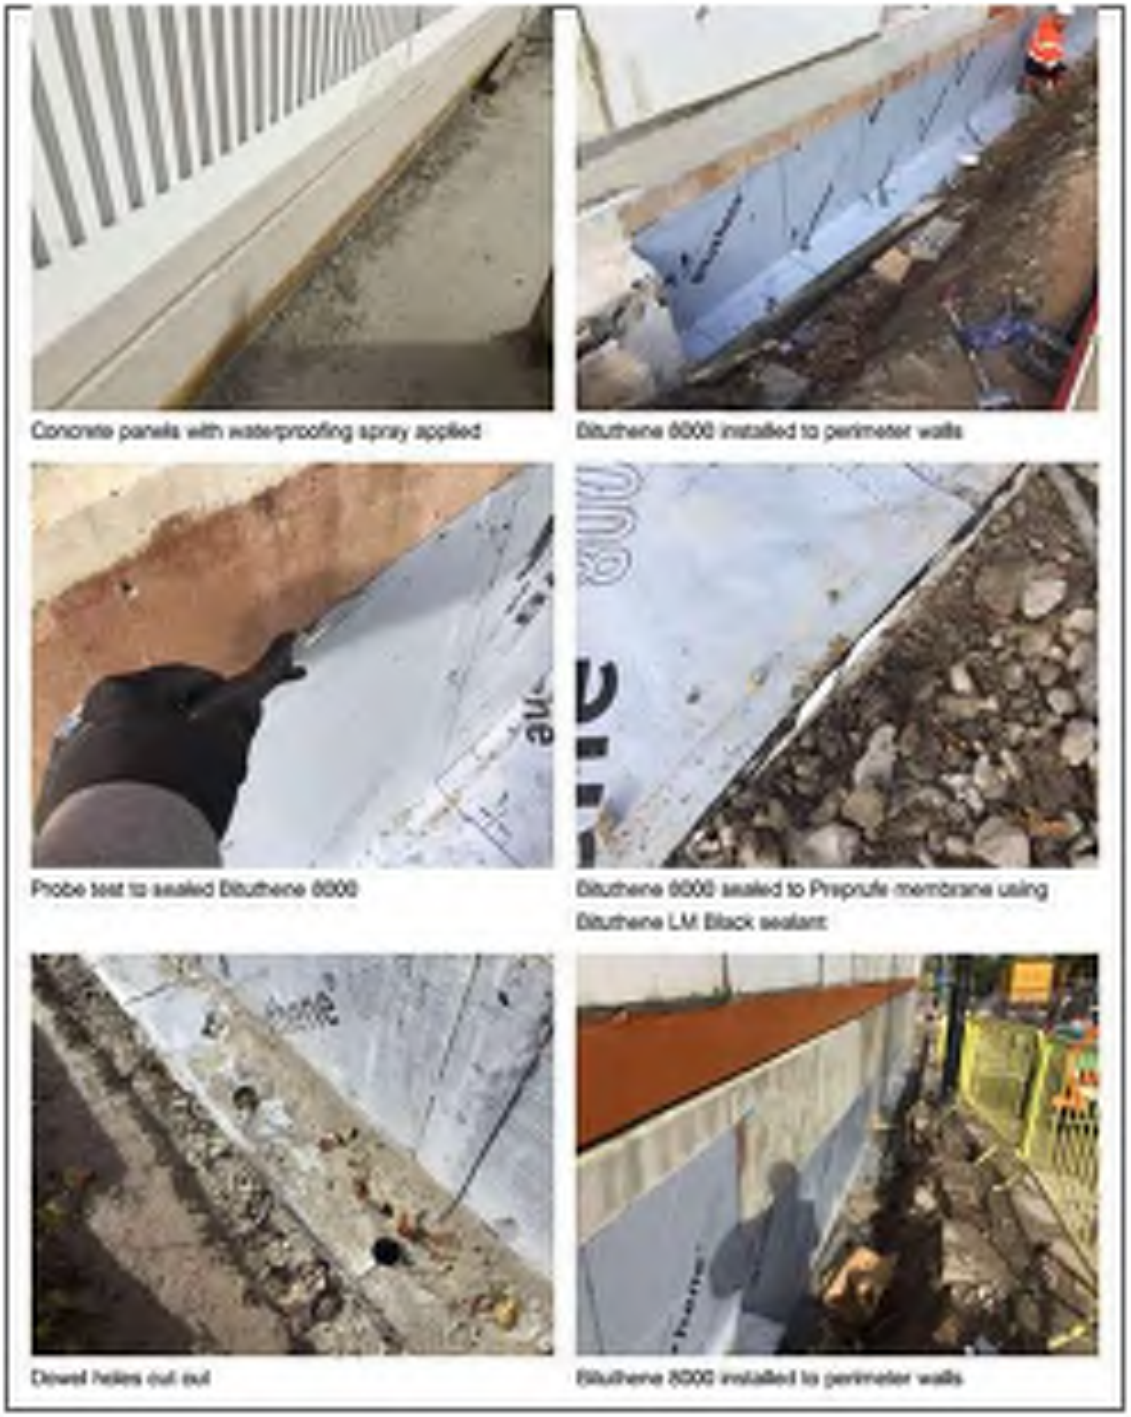

Concrete panels with waterproofing spray applied

Bituthene 8000 installed to perimeter walls

Probe test to sealed Bituthene 8000

Bituthene 8000 sealed to Preprufe membrane using Bituthene LM Black sealant

Dowel holes cut out

Bituthene 8000 installed to perimeter walls

Membrane Testing Solutions Limited • The Studio, Parsonage House, Parsonage Street, Halstead, Essex CO9 2JR

Telephone: 0844 557 3786 • email: sales@mtsltd.net • www.mtsltd.net

Registered Office: 1, Second Avenue, Halstead, Essex. CO9 2SU • Company Registration Number: 8871015

CO-OP LIVE - C777
18.10.2023

Site name: BAM Construction, Co-OP Live, Manchester **Postcode: M11 3DU**	**Units/ plots checked: East Perimeter Tanking and Waterproof Detail. See mark-up plan**
Installers Name: Waterseal	
Date: 18/10/2023	
Inspection by: Dan Squire	**Weather: 13°C Dry**

Item	Comments	
Sub-floor void	N/A	
Ventilation Inlets and Outlets	N/A	
Number Of Vents	N/A	
Materials used:	Membrane – Bituthene 8000	
	Self-Adhesive Membrane ☒ Yes	Preformed Top hats ☐ Yes
	Double Sided Butyl Tape ☐ Yes	Preformed Corners ☐ Yes
	Others Please List: Grace Integritank Waterproofing Spray	
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** MTS Ltd carried out a thorough visual inspection of the waterproofing and membrane works. The works had been installed to a good standard. Waterseal have installed the movement joint to the east perimeter walls. Integritank waterproofing spray was then applied to the walls. Sealing the movement joint and overlapping with the Bituthene 8000 tanking to allow for dowels to be installed. These dowls are still to be sealed using bituthene LM Black sealant at a later date and re-inspected, and therefore is discounted from this cert. Some repairs were made to the Bituthene 8000 using additional layers of the Bituthene and jointing tape overlapping to reduce the risk of the Bituthene delaminating at the edges.	

Type of Joint	Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐		
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)			
Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?			☒ Yes	☐ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Has all other detailing work passed inspection			☒ Yes	☐ No	☐ N/A
	(List any defects to detailing work and joints): During our inspection the following defects and repairs were carried out: No recorded defects. Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A The Area has passed inspection ☐ The Area has failed inspection and a corrective action sheet has been left with the contractor ☐ The Area is incomplete as detailed above ☒ Signed: **Dan Squire** Date: 18**/10/2023**					

Area Inspected





Sealed Bituthene repairs



Probe testing



East perimeter walls inspected



Areas protected prior to further installation



Movement joint installed



Integritank spray sealed movement joint and joined to Bituthene 8000



Integritank spray sealed movement joint and joined to Bituthene 8000



Dowels yet to be sealed

Test and Inspection Result 'PASS'

The area whilst incomplete has passed the inspection and a re-visit is not required.

Signed: Michael Smith Date: 18.10.2023

On Behalf of Membrane Testing Solutions Ltd

CO-Op Live, Manchester - C777
4.12.2023

Site name: BAM Construction. Co-Op Live. Manchester **Postcode: M11 3DU**	**Units/ plots checked: : South east and west Perimeter tanking and waterproofing detail. Main floor membrane installation See marked up plan**
Installers Name: Waterseal & PJ Carey's	
Date: 04/12/2023	
Inspection by: Dan Squire	**Weather: 5ºC Wet**

Item	Comments
Sub-floor void	N/A
Ventilation Inlets and Outlets	N/A
Number Of Vents	N/A
Materials used:	Membrane – Preprufe 300R Plus with Preprufe lap tape
	Self-Adhesive Membrane ☒ Yes / Preformed Top hats ☐ Yes
	Double Sided Butyl Tape ☐ Yes / Preformed Corners ☐ Yes
	Others Please List: Bituthene 8000. S2 Primer Bituthene. Grace Integritank waterproofing spray system
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** MTS Ltd carried out a thorough visual inspection of the waterproofing and membrane works. The works had been installed to a good standard. Waterseal have installed the movement joint to the south east perimeter walls and south west upper slab. Integritank waterproofing spray is installed onto the pre primed slab and walls. Sealing the movement joint and overlapping with the Bituthene 8000 which had previously been installed by P J Carey's.

(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)

MTS Ltd carried out a thorough visual inspection of the waterproofing and membrane works. The works had been installed to a good standard.

Waterseal have installed the movement joint to the south east perimeter walls and south west upper slab. Integritank waterproofing spray is installed onto the pre primed slab and walls. Sealing the movement joint and overlapping with the Bituthene 8000 which had previously been installed by P J Carey's. The Integritank spray is sealed to the required height of the walls. Some repairs have been made to the Bituthene 8000 using additional layers of the Bituthene and joining tape overlapping the joints to reduce the risk of the Bituthene peeling away at the edges.

Preprufe 300R membrane has been lined across footprint of main arena floor by PJ Carey's. Joining onto the membrane previously laid under the slab previously poured. The membrane has a permanent back binding which is used to join the membrane together and is pressure rolled. Additional Lap tap is then installed over the membrane joints.

At the time of our inspection the membrane works were ongoing and incomplete. The stanchions were yet to be sealed using the Bituthene LM black sealant and the movement joint needed additional LM Black to re seal as this was installed last year. All other works in this area were being installed to a good standard. A large section for the main floor membrane has re bar installed ready for the concrete meaning a restricted inspection in this area which seemed well cleaned off and free from any damages that we could see.

Marked up drawing key :

Area in red - waterproofing spray system works
Area in yellow - Preprufe membrane installed and inspected
Area in blue - Preprufe membrane restricted inspection.

Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐
☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)	

Have all joints passed testing prior to surveyor leaving site?	☒ Yes	☐ No	☐ N/A
Have all pipes passed testing prior to surveyor leaving site?	☐ Yes	☐ No	☒ N/A
Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?	☐ Yes	☒ No	☐ N/A
Have all piles and pile caps passed testing prior to surveyor leaving site?	☐ Yes	☐ No	☒ N/A
Has all other detailing work passed inspection	☒ Yes	☐ No	☐ N/A

	(List any defects to detailing work and joints): During our inspection the following defects and repairs were carried out: No recorded defects Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A The Area has passed inspection ☒ The Area has failed inspection and a corrective action sheet has been left with the contractor ☐ The Area is incomplete as detailed above ☐ Signed: **Dan Squire** Date: **04/12/2023**

Area Inspected

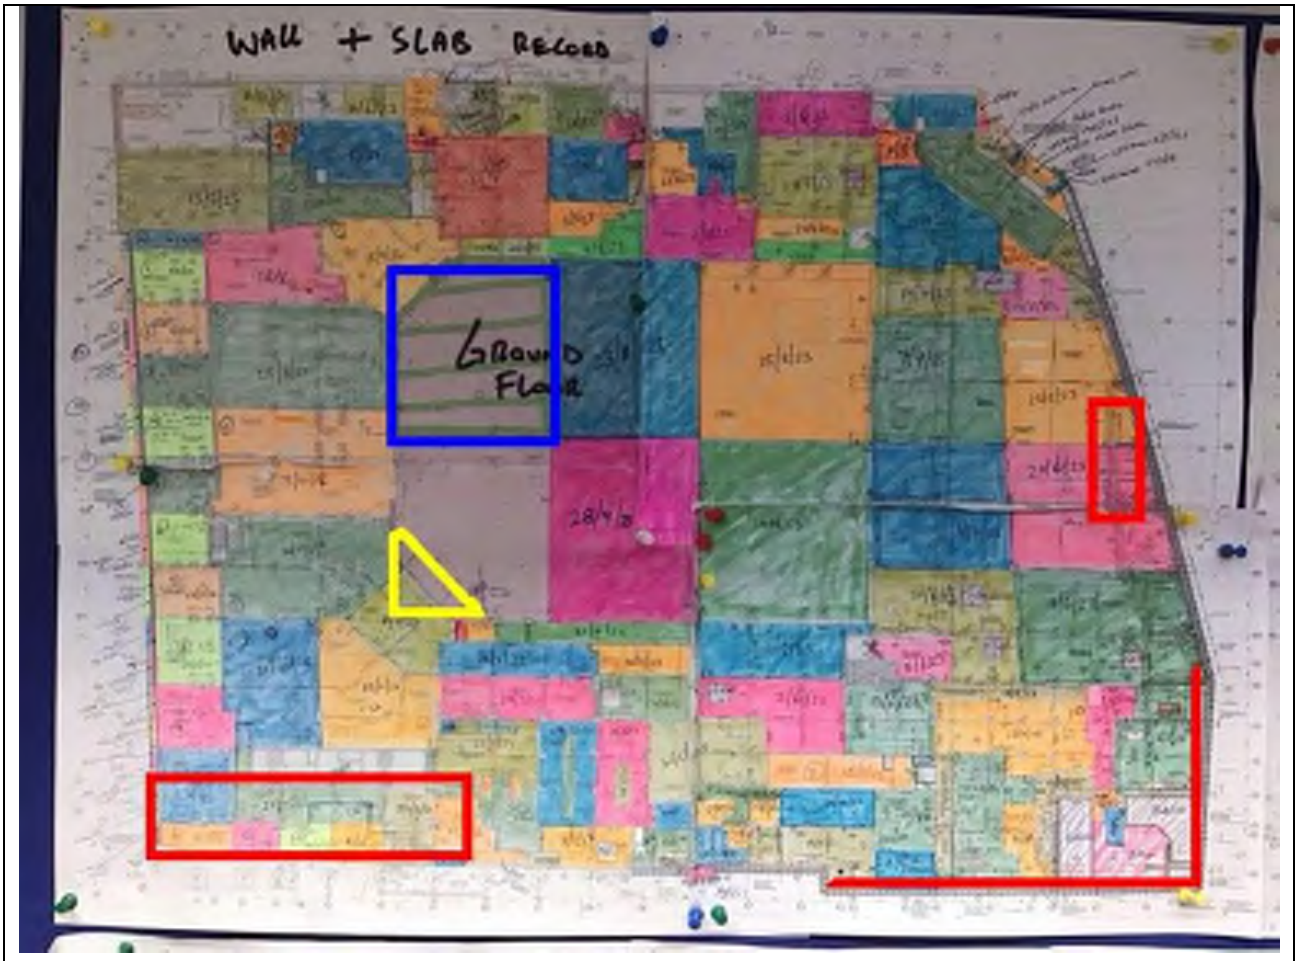


Photo **04/12/2023**



Upper slab waterproof spray system



Upper slab waterproof spray system



South east perimeter wall waterproofing system



Waterproof spray sealed to movement joint



Primer applied to perimeter walls prior to waterproofing spray




Sealed patch repairs to Bituthene tanking



South east waterproofing spray system



Pick test to sealed Preprufe membrane joint

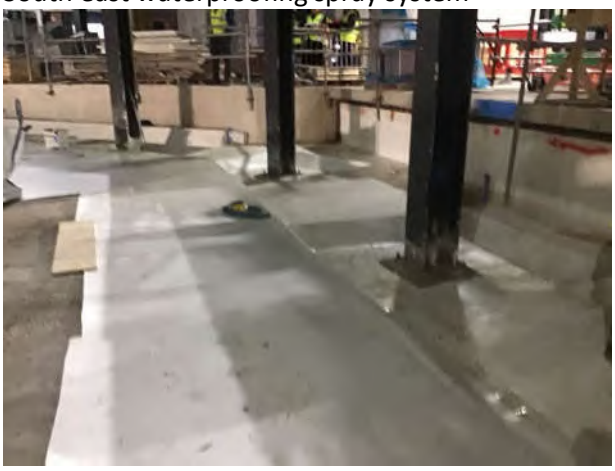

Preprufe membrane installation



Preprufe membrane installation



Stanchions yet to be sealed in the membrane section



Restricted inspection to Preprufe membrane

Test and Inspection Result 'PASS IN FULL'

The areas were incomplete but have passed the inspection performed and a re-visit is not required for these areas.



Signed: Barrie Ackroyd Date: 4.12.2023

On Behalf of Membrane Testing Solutions Ltd

APPENDIX E

Copy of Validation Report and Photographs

(Contained on USB Storage Device)

Appendix K Buro Happold Periodic Inspection Records

(Selection of records provided)

Copyright © 1976 - 2024 Buro Happold. All rights reserved

Co-op Live
Site visit record form

BUROHAPPOLD ENGINEERING

Name	Justin Hobkirk	**Date and time**	17/03/21 – 0830am to 1700pm
Project No	042841	**Visit Ref No**	Visit 002
Weather	Cloudy, 11°C, dry, ground is damp/wet.		

WORKS ON SITE

Personnel / Contractors involved

BAM: Paul Clements – looking after the earthworks package / Martin Werner / Phil London / Nick Wild

Provectus – Sam Lane-Ryan / Tom / Alex

Description of works / activities ***[Inc. any work outside / contravening Method Statements]***

Pile arising material is to be reused where possible across the site (generally clean) – testing?

Piling mats starting to be laid where possible.

"Slop" (surface trimmings) material is being removed offsite to non-hazardous landfill by BAM.

Trench is being dug for the sewer diversion.

HV cables are disconnected and waiting to be removed/realigned ahead of the piling works.

Excavation to formation level (reduced level dig) is being carried out as part of the Provectus work.

Location: Brief description (mark on plan as appropriate)

Excavation to formation level has started in the northwest corner (see attached plan).

Stockpiled surface trimmings/arisings pile is located in the southwest area.

Stockpiled material for reuse as the piling mat is in the southeast area.

Location, volume and nature of excavation / soils encountered/ removed

Provectus to provide daily volumes of material going off/onsite – to be provided by them on a weekly basis – see records for date 17/03/2021.

Arctic lorry = 15m³

Dump truck = 9m³

So, total material exported off site is 1284m² = approximately 105 wagons.

Destination of soils removed from site ***[Inc. comment on WTNs]***

Hazardous disposal will be to: Maw Green and/or Rowley Regis (Ref: EPR/BS7722ID).

Non-hazardous will be to: Buckton Vale, Fletcher Bank Quarry, and Woolston (Ref: EPR/GB3004XN).

Recycling will be to: Ashton Old Road (Ref: EPR/GB3930AM).

All tickets are being captured digitally and issued daily and submitted on a weekly basis (typically a Monday for the previous week) first week will likely be issued on Monday 22nd March 2021 (issued on 26/03/21). Tracker will also be issued on a weekly basis with the tickets (tickets will take time to come through). This will be for material moving offsite / onsite.

A survey carried out by Provectus of material will be carried out in addition to the tracker.

Location volume of reused materials (as per MMP)

MMP – written by Provectus to be issued today.

Mark on plan and request volumes.

Location, volume and nature of imported soil materials

Imported material will be used for the upper layers of the piling mat. The lower layer of the piling mat will be used from the stockpiled material on site (SP1) which will be tested as per the BH RMS and has a membrane in the stockpile to separate the material.

Tracker to be issued weekly with all of the volumes.

Notable/ unexpected contamination encountered

Area B1 has been classified has hazardous material at level. Asbestos identified in grid square A4 (see plan). Air monitoring to take place and separate methodology for the removal of material (~1m) – asbestos being tested and a watching briefing is in place.

Stockpiles of hazardous and non hazardous will be located on site and signed accordingly (see photos).

Analytical data ***[in-situ / imported / exported soils]***

Testing results for the imported material which will be part/form the ITP. Provectus to provide these to BH.

Provectus are booking testing to be carried out tomorrow.

Groundwater ***[Encountered / condition / control / disposal]***

Bunds are in place around the site (particularly in the south) with the sewer diversion taking place in the north.

Groundwater monitoring is ongoing in boreholes and visual inspection as usual.

Boreholes to be decommissioned when EA have advised this is okay and no longer required. BH need to confirm this will be acceptable to use bentonite.

Dave Hanlon to advise on the water treatment plant location – TBC

Below ground infrastructure ***[Concrete/ pipework etc.]***

Where below ground pipework is being installed, check how the trenches are being infilled (e.g. sand)

Sewer diversion trench is being installed and will be filled with 6F2 material (imported) or similar (site won).

Old manhole on site was broken down and rebuilt and a concrete slab over the top. The manhole will eventually be grouted up.

Environmental issues (e.g. dust, groundwater etc.)

They will have dust monitors in place, we should request the data weekly / monthly.

4 No. Noise monitoring in place. Dust. Odour and volatiles. Adhoc vibration monitoring. Asbestos.

Additional Information / Comments ***[Continued overleaf as appropriate]***

UXB engineer (1st line defence) on site carrying out a watching brief.

Provectus to issue RAMS

T5 mobile licence covers treatment of hazardous and non hazardous waste.

Piling mat = dig to excavation level then fill with clean material and build up

Provectus to provide drivers with tickets and information needed for when removing material from site.

Provectus to potentially decommission wells –BH suggest backfill with bentonite.


2000m³ imported stone for pile mats – this potentially to be used in the RAMS as baseline.

CCG carrying out testing on formation level. Plate load testing on stone. Prepare formation, build up and then test.

Material can be run offsite but no hard material can be dug and no reprofiling can take place (reused of material) until the MMP is in place – waiting for the LPA to sign off on the RMS and Verification report. The LPA signed off the RMS on the 23/03/21 – we are currently awaiting the Provectus MMP.

Asphalt to be imported to site

Site hours for Provectus - 0730 to 1800hrs

Name: Justin Hobkirk	**Signature** 	**Date: 17/03/21**

Photos



Surface arisings southwest area – to be exported. Left of this material is the bund to stop water running into Ashton Canal.



Provectus onsite cabin – where testing and monitoring equipment is kept.



Main haul road through the centre of the site



Main excavation area – grid square B2 completed (see plan).



Concrete slab covering the reconstructed manhole.




Imported material – use for piling platform and mat.



Noted standing water on site which is due to rainfall and depression in the ground.

Enclosure 1 Site Plan – Remediation works

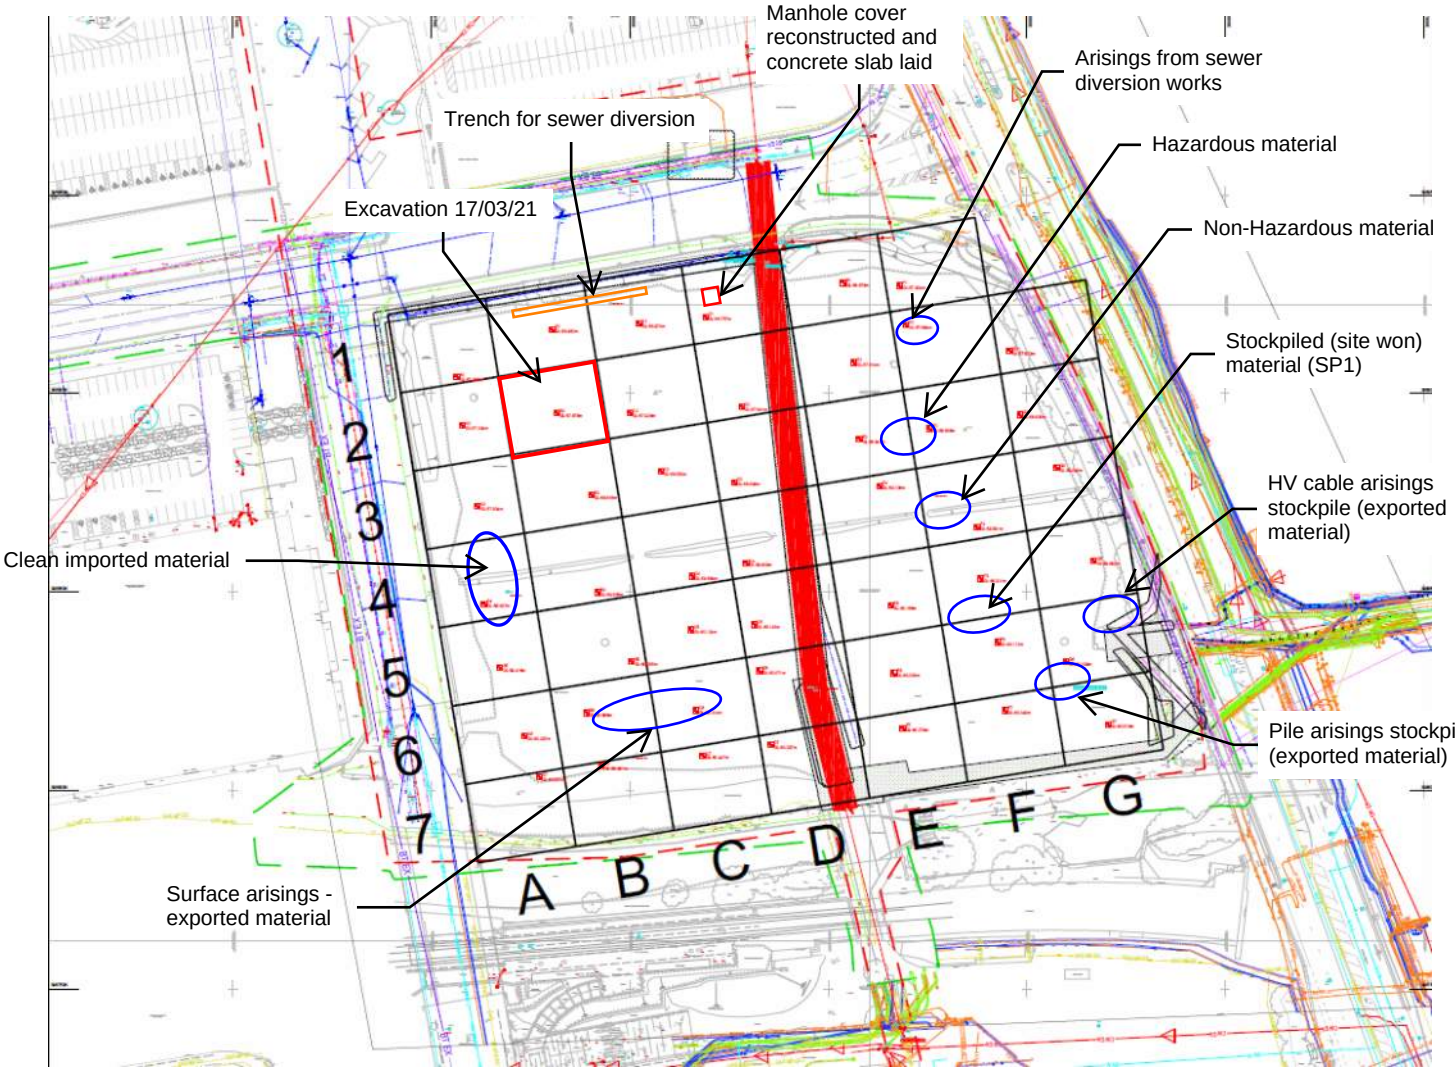

BURO HAPPOLD

Ground Engineering.

Job Title:
Co-op Live

Job Number:
0042841

Sketch Title/Number:
Site Plan - Remediation Works

Document Number:
Site Visit Record 002

Rev.	Date	Initials
000	17/03/2021	JH

PROVECTUS

Provectus Remediation Limited
Regent House
Bath Avenue
Wolverhampton
WV1 4EG

Tel. 0118 988 0200
www.provectusgroup.com

Client: BAM Construction

Project: Project Bradford

Job No.: 101114

Title: Remediation Works – Soil Validation/Tracking Grid 25m x 20m

Scale: NTS

Date Drawn: July 2020

Drawing No.: 101114 Figure 2

Co-op Live
Site visit record form

Name	Justin Hobkirk	**Date and time**	25/05/21 1345 to 1700
Project No	0042841	**Visit Ref No**	Visit 009
Weather	Overcast, wet, occasional rain, 12°C		

WORKS ON SITE

Personnel / Contractors involved

BAM – Paul Clements, Phil London and Arooj Ali

Provectus – Alex Clifford and Tom Harrington

Cementation Skanska Limited (CSL) – Gavin Clifford and Oliver Pilkington

Description of works / activities ***[Inc. any work outside / contravening Method Statements]***

Provectus working in the centre and moving east of the site – the "bowl" is almost complete in the middle of the site see photos. However southeast area is a bit difficult to excavate due to piling and storage of haz and non haz and clean material stockpiled in these areas.

Earthworks had stopped at 1100am due to heavy rain in the previous days.

PMP to include CEMP – BAM (PL) to issue to Buro Happold. Received.

Suitable gated and pathed walkways present on site.

CSL on site piling in the northwest corner on both levels, in the east and south on the higher levels.

Location: Brief description (mark on plan as appropriate)

Non-hazardous material stockpiled in the east, Hazardous material in the south. Wagons have stopped removing material temporarily due to weather however import material still being brought to site.

All stockpiles sign-posted (see photos)

KILO working in the northwest (associated with services on site) and area adjacent to the site cabins.

CSL piling in the northwest corner, the east and south east corner.

Location, volume and nature of excavation / soils encountered/ removed

Provectus to provide daily volumes of material going off/onsite within the tracker spreadsheet – issued weekly. Weekly material volumes have been provided within the meeting minutes – see attached.

Plan showing hazardous waste Vs Non-Hazardous waste to be provided. Still outstanding.

Quarried aggregate stockpiled to the west of the site (see photographs). As quarried natural material, not sampled. However, material is tested (PLT) following compaction for piling mat. Test results have now been provided see meeting minutes.

Co-op Live
Site visit record form

Destination of soils removed from site ***[Inc. comment on WTNs]***

Hazardous material to Crewe treatment facility.

Non-Hazardous material destinations logged on digital tracker held by Provectus. To be issued to Buro Happold in due course. Total volume of Non-Hazardous off site, up to and including 21/05/2021 are provided in the meeting minutes attached.

From quick check of tracker shown in the meeting minutes, typical wagon loads are 9m3 and 14m3. Tracker shows wagon reg, end destination, load (volume), classification (Haz/Non-Haz). Provectus scan tickets on exit from site and again at entrance to disposal location, complete tickets when received are documented on the Provectus digital tracker. Paper copies are available on site. BAM (Ruth and Phil) will be checking if digital tracker is compatible with their systems and whether the WTN paper copies can be digitally transferred. Requested digital version via BIM360 on 20/04/2021. – still outstanding and requested again on 11/05/2021. These are now uploaded onto BIM360.

Location volume of reused materials (as per MMP)

MMP – written by Provectus – requested copy 24/03/2021 (see email from FG to PL and AC). Still waiting for this to be sent through. Requested again on 12/05/2021. This has now been provided by BAM on 14/05/2021.

MMP has been signed off by Provectus QP. Material is not available for reuse on site as the QP is required to sign off on the MMP.

Volumes of material have been provided in the meeting minutes – see attached.

Location, volume and nature of imported soil materials

Imported quarried aggregate being used, no samples as quarried stone. (see meeting minutes).

Notable/ unexpected contamination encountered

No significant visual or olfactory contamination observed.

Analytical data ***[in-situ / imported / exported soils]***

No samples to date. Sampling not required for natural quarried aggregate. See meeting minutes regarding material reuse.

Groundwater ***[Encountered / condition / control / disposal]***

Bunds present in the south of the site to prevent surface water run-off into Canal, no surface water was observed on site. Levels reduced in the south west with a batter going up to the level of the canal (see photos) a footpath is waiting to be installed along this edge to allow safe walking around site.

Sump is present in the northwest corner on the upper level of the piling platform for any water arising during the pile installation. Method of water treatment TBC by BAM/Provectus.

Below ground infrastructure ***[Concrete/ pipework etc.]***

Land drain excavation completed. Water treatment works constructed (piles) in northeast of site.

Trenches completed for the guide wall for the piling in the southeast area.

Capping beam being formed in the northwest corner. However, a number (~3) pile reinforcements have been placed -250mm and will require remediation subject to review of the pile design and the effect from shear loading.

Co-op Live
Site visit record form

Environmental issues (e.g. dust, groundwater etc.)

No wheel wash to be installed at exit, tarmac haul road now constructed in the middle northwest site (Grid Squares B3 to D3 – see attached plan and photos). Monitoring taking place, see below and meeting minutes.

Dust was observed when on site, it had been a dry for a few weeks. Four dust monitors in place (frisbee gauges), results to be issued to BAM and then Buro Happold (see photographs). Asbestos monitoring ongoing. Noise and vibration monitors also being carried out. Data requested 23/03/2021, PL at BAM to provide. BH have requested this information again on the 12/05/2021. Still awaiting data.

BIM360 Transmittal #1137 – states vibration issues due to piling next to the monitor. This is not perceived as an issue as due to the proximity of the piling and piling rig to the monitor and steps have been carried out to reduce this. See Transmittal #1137. Ongoing.

Co-op Live
Site visit record form

Additional Information / Comments ***[Continued overleaf as appropriate]***

Buro Happold issued a request for information via email dated 12/05/2021 at 16:03pm – requesting the following information:

"The items that Buro Happold require are as follows:

- *PMP to include CEMP.*
- *MMP.*
- *Materials Tracker - either spreadsheet or PDF is fine.*
- *Noise, dust and asbestos monitoring results.*
- *Plate Load test results.*

Please could you also send through a selection (~10no.) of haz and non haz tickets for our records to form part of our evidence of the verification report?"

Above information has now been received with the exception of the environmental monitoring however, this is on BIM360.

Meeting notes during the 3pm meeting:

11am Provectus stopped works due to limited material to export and weather is poor (very wet) pile mat has stopped.

2 stockpiles of haz and non haz waste which will have additional signs put up by COB.

Groundwater from piles in the northwest corner going into the sump. Provectus to provide a rate/proposal for water removal whereby there are two options:

- Potential to use land drains but treatment would be required as the cement may block the drains. Costing between silt buster or treating the water before pushing to land drain.

- Removal of water offsite but will require treating.

Ruth will continue to upload waste transfer tickets onto BIM360 (BH can access).

Provectus ongoing with issue of tickets and of volumes of material on/offsite.

Monthly environmental report to be issued on the 28/05/2021

Small volume of hazardous material was identified and excavated on site and dealt with in accordance with the RMS.

Asbestos cell as identified at the start of the works in the lower centre level (in the 'Bowl') was excavated and removed from site. Refer to plan.

In week 20/21 total volume to excavate is circa 19,000m³ therefore, looking to start slowing works on site.

BAM/Provectus looking to excavate a land drain approx. 1m x 0.60m to assist with drainage on site on the piling mat at 20m centres.

Phasing plans will be developed – access ramp in the southwest area for piling rigs to move off/on site however, this will be subject to the weather (dry ideally).

Name	**Signature**	**Date**
Justin Hobkirk	**JJH**	**25/05/2021**

Co-op Live
Site visit record form

Photos



Piling in the south area – cement being poured into pile. Looking northwest.



New walkway installed and constructed to allow ease of access around site.

Co-op Live
Site visit record form



Lower level piling mat installation put on hold due to poor weather.



Installation of piles on upper level in the northwest corner ongoing.

Co-op Live
Site visit record form



Installation of capping beam in the northwest corner. NOTE: some reinforcement installed at -250mm.



Installation of piling mat halted due to weather. Looking southeast.

Co-op Live
Site visit record form



Stockpile of non-hazardous and hazardous material onsite.

Co-op Live
Site visit record form

BURO HAPPOLD

Name	Justin Hobkirk	**Date and time**	03/02/22 1230 to 1600
Project No	0042841	**Visit Ref No**	Visit 020
Weather	Sunny, wet, 8°C		

WORKS ON SITE

Personnel / Contractors involved

BAM – Paul Clements, Martin Werner

Buro Happold – Justin Hobkirk

Outstanding actions

Complete actions

Description of works / activities ***[Inc. any work outside / contravening Method Statements]***

Provectus have finished on site with the main bulk excavation and have demobilised from site except for 1No. lorry to remove the remaining pile arisings from site.

CSL have finished on site. Issue last week with obstruction in the ground installing the last pile.

NCRs are ongoing however, CSL have proposed remedial action on these piles which is being carried out and the NCRs being closed out. BH have reviewed the NCRs and provided comment where required.

Environmental monitoring by Provectus has ceased due to them finishing on site. BAM to confirm if environmental monitoring is still taking place on site?

Pile tests ongoing with circa 3 No. remaining to be carried out. Still waiting pile test reports and other piling record information to be issued on BIM360 and assigned to BH – ongoing process.

Careys working in various areas across the site. Construction of all Cores ongoing.

Suitable gated and pathed walkways present on site.

Waterproof membrane being installed throughout the site with multiple verification and checking of the installation of the membrane taking place.

Waterproofing is taking place on site along the west and east walls and verification is being carried out on site by a third party (GCP) – refer to BIM360 for reports. Where remedial work is required on the waterproofing or gas membrane, Careys have been undertaking the remedial work with a report to record/document the action taken. A 3rd party verifier (MTS) is attending site to inspect the membrane prior to pouring of concrete.

Pile caps are being formed, placed and poured on site.

Monitoring of the walls is ongoing but has been reduced to once a week due to limited movements.

Co-op Live
Site visit record form

BURO HAPPOLD

Location: Brief description (mark on plan as appropriate)

Careys excavation material noted to be placed next to the excavations and potentially reused. BH sent email on 26/08/21 requesting the Careys protocols with regards to excavated material on site and stockpiling etc. Received a response from BAM on the 01/09/21 with waste transfer tickets however still require further information as follows:

- which CEMP/MMP Careys are following on site (likely to be in conjunction with BH Remediation Strategy (RS));
- Waste tracker of material including: location, volumes and reuse of material;
- Evidence to show Careys are carrying out these procedures e.g. completion report or monthly reports;

A further email has been issued (08/09/21) to address the Careys earthworks reuse on site under an MMP – as per the BH remediation strategy. Still awaiting a response on this – BH to send follow up email in a week if still no response.

BH have been notified that a Careys MMP is in place work is being carried out in accordance with the Plan however, BH have requested a copy of the MMP for BH records on 24/11/21. BH waiting response – MMP still not been provided to BH.

Location, volume and nature of excavation / soils encountered/ removed

Provectus removing piling arisings and being taken off site – volumes will vary week upon week. Provectus will provide the final volumes within the waste tracker and a summary within their completion report.

Careys stockpiling material on site and being taken offsite. Careys required to provide this information as per the above section. Still waiting for confirmation of the MMP.

Destination of soils removed from site *[Inc. comment on WTNs]*

Non-Hazardous material destinations logged on digital tracker held by Provectus. This was issued and access provided.

From quick check of tracker shown in the meeting minutes, typical wagon loads are 9m3 and 14m3.

Waste transfer tickets have been provided from Careys for the excavation material that is being removed offsite. These are the same treatment facilities/landfills as Provectus.

Careys required to provide this information as per the above section. Still waiting for confirmation of the MMP.

Location volume of reused materials (as per MMP)

MMP – written by Provectus which was issued on the 14/05/21.

BAM site wide CEMP being used for works on site – dated July 2021.

Volumes of material have been provided in the meeting minutes by Provectus – see enclosure 3.

Careys to provide information as requested (above) regarding earthworks material onsite. Still waiting for confirmation of their MMP.

Location, volume and nature of imported soil materials

Provectus are offsite and only removing pile arisings from site.

Careys are stockpiling material on site in various areas across site. Careys to confirm if any additional material is being imported to site? Careys to provide information regarding material use onsite. Still waiting for confirmation of their MMP.

Co-op Live
Site visit record form

BURO HAPPOLD

Notable/ unexpected contamination encountered

No significant visual or olfactory contamination observed – noted in Provectus records.

Careys to provide details of any contamination encountered.

BAM to confirm if monitoring is ongoing?

Analytical data ***[in-situ / imported / exported soils]***

Sampling not required for natural quarried aggregate.

Careys to provide information regarding earthworks material use. Still waiting for confirmation of their MMP.

Groundwater ***[Encountered / condition / control / disposal]***

Pooling of water present on site in the southeast corner – precautionary measures should be carried out to protect excavations etc.

BAM confirmed limited rainfall however, this area on site is pooling with water – potential of water table being present due to the decrease in level on site or caused by Minewater due to the drilling and grouting for treatment of mine works/piling on site.

Water Monitoring of the canal ongoing by BAM.

Below ground infrastructure ***[Concrete/ pipework etc.]***

Waterproofing is ongoing across site. Pile caps and beams are being excavated and reinforcement is being placed with pouring of caps and beams taking place on site.

Drainage is being installed across the site. Construction of the Caisson is due to commence within the next few weeks.

Environmental issues (e.g. dust, groundwater etc.)

Minimal dust being generated due to wet weather – seasonal rainfall.

BAM to confirm if monitoring is ongoing?

Additional Information / Comments [Continued overleaf as appropriate]

Piling completed – all piling records to be issued ASAP and including the remaining static load tests to be completed – there are still 3No. outstanding however piling has finished onsite.

BH emailed BAM on 26/05/21 and 08/09/21 requesting Careys protocols for excavation/removal/reuse of material on site. Still waiting confirmation on MMP to be addressed or MMP to be issued via email.

BH emailed BAM/CSL on the 17/09/21 regarding the monitoring of the contig wall during excavation to ensure there was limited movement of the wall during this process. The email was requesting details of the wall monitoring protocols. BAM issued their wall monitoring protocol on the 20/09/21. Monitoring ongoing however, reduced to once a week.

BAM issuing NCRs to BH which are being review and comments made where required – NCRs provide a solution which is generally acceptable – ongoing.

Additional Plate Load Tests are being carried out in the southeast corner due to previous poor results which will be used to measure the subgrade of the ground is sufficient prior to the construction phase of the ground bearing slab. Testing and data TBC.

MTS attending site to verify the waterproof/gas membrane on site – envisaged 20No. visits to be carried out until November. Site visit included within Enclosure 1.

Name	**Signature**	**Date**
Justin Hobkirk	**JJH**	**03/02/2022**

Photos




Looking East. Pooling of water in the southeast corner.



Northwest area. 3rd party verification of the water/gas membrane installation.



Southeast area. 3rd party verification of the water/gas membrane installation.

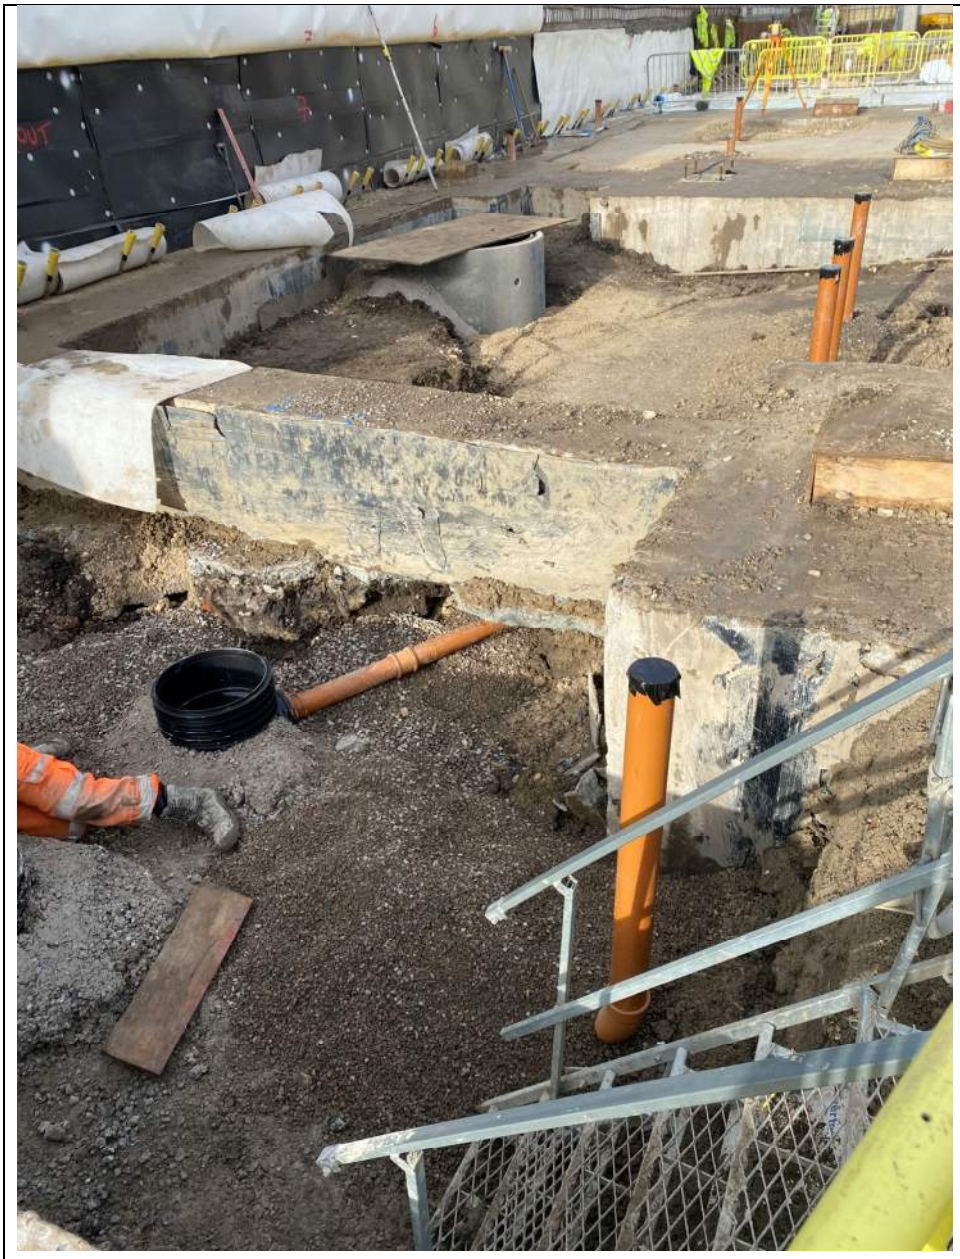

West area. Drainage installation.

BURO HAPPOLD

Enclosure 1 – MTS Verification Report

Co-Op Live, Manchester - C777
3.2.2022

Site name: BAM Construction. Co-Op Live. Manchester **Postcode: M11 3DU**	**Units/ plots checked: North west slab - Pour 2. Main floor installation Gridlines W06-W08 / NW - N01** **Core 5 - Base installation Gridlines E07-BS / N12-BE**
Installers Name: P J Carey's	
Date: 03/02/2022	
Inspection by: Dan Squire	**Weather: 9°C Dry**

Item	Comments	
Sub-floor void	N/A	
Ventilation Inlets and Outlets	N/A	
Number Of Vents	N/A	
Materials used:	Membrane – Preprufe 300R Plus	
	Self-Adhesive Membrane ☒ Yes	Preformed Top hats ☐ Yes
	Double Sided Butyl Tape ☐ Yes	Preformed Corners ☐ Yes
	Others Please List: Bituthene LM. Bituthene Liquid membrane	
Installation Notes	**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** MTS Ltd carried out a thorough visual inspection of the membrane, the membrane had been installed to a good standard. Preprufe 300R plus membrane has been lined across the pour slab areas as noted and is joined to the membrane previously installed up the liner wall to the capping beam. The membrane has a permanent back binding which is used to join the membrane together and is pressure rolled. In some areas an additional strip of Preprufe Tape LT has been added on top of the joints. A mix of Bituthene LM & Bituthene liquid membrane is applied to seal all penetrations. Patch repairs have been made to the membrane along the vertical face of the liner wall and also on the floor where a few minor damages were caused by the steel using Preprufe 300R plus membrane and strips of Preprufe LT tape.	

Installation Notes Continued	Site were carrying out their own ongoing inspections and cleaning off the membrane as the install progressed and prior to the pour. Approx 50% of the areas to inspect were restricted due to steel work on the membrane.					
Type of Joint	Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐		
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)			
Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?			☒ Yes	☐ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?			☒ Yes	☐ No	☐ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?			☐ Yes	☐ No	☒ N/A
	Has all other detailing work passed inspection			☒ Yes	☐ No	☐ N/A
	(List any defects to detailing work and joints): During our inspection the following defects and repairs were carried out: No recorded defects. However, holes were in the membrane in preparation for the starter bars which will then be sealed using the Bituthene LM and Liquid membrane mix once in place. Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A The Area has passed inspection ☒ The Area has failed inspection and a corrective action sheet has been left with the contractor ☐ The Area is incomplete as detailed above ☐ Signed: **Dan Squire** Date: **03/02/2022**					

Area Inspected

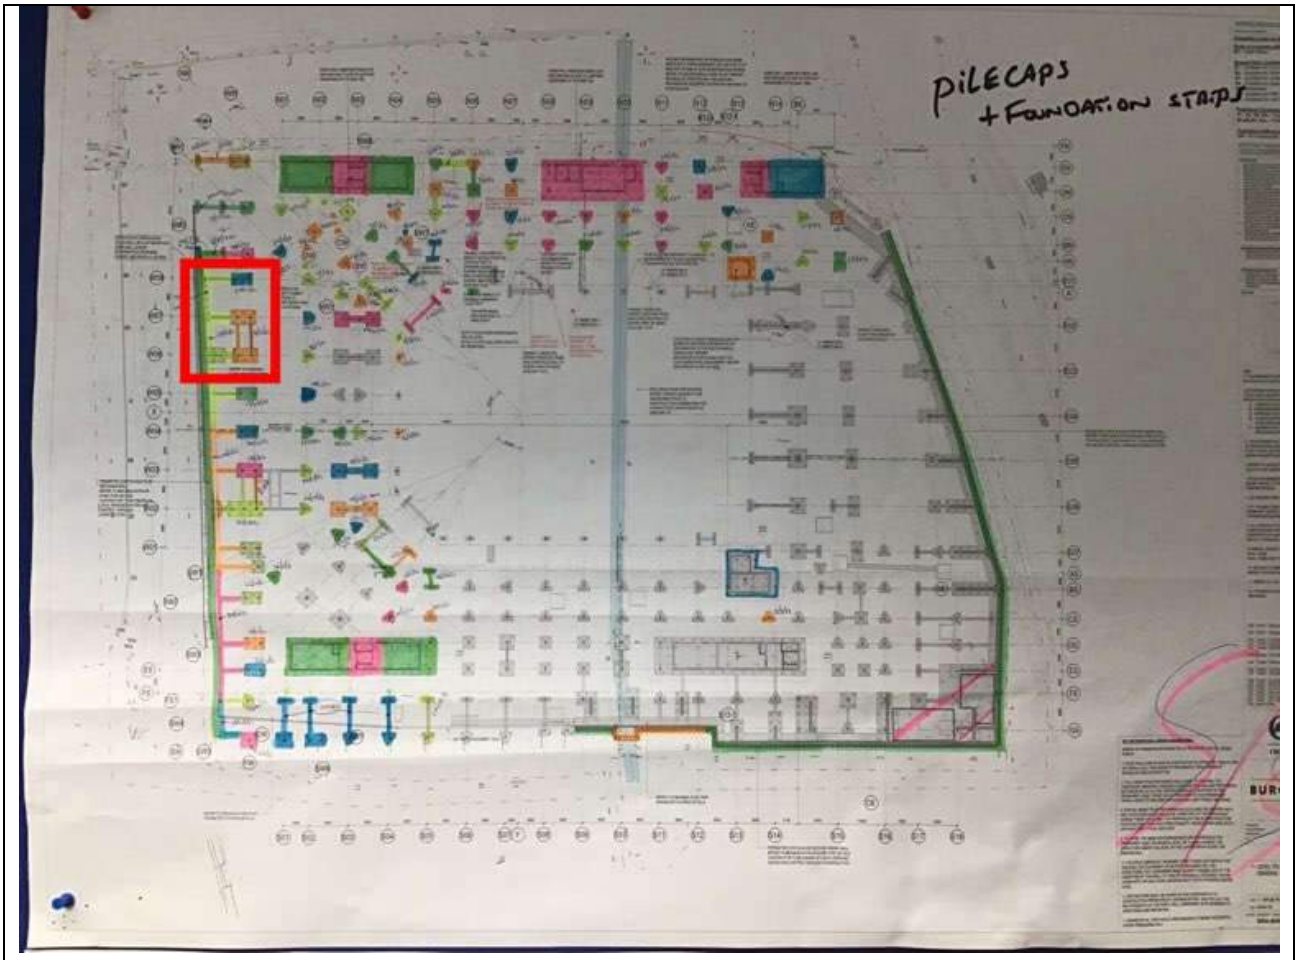


Photo **03/02/2022**



Restricted inspection area



North west pour 2 slab line out



Liner wall patch repairs



Bituthene LM and liquid membrane mix sealed penetrations



Sealed pipe penetration using Bituthene LM and liquid membrane mix



Sealed penetration using Bituthene LM and liquid membrane mix



Probe test to adhesive backing joint

Site name: BAM Construction. Co-Op Live. Manchester **Postcode: M11 3DU**	**Units/ plots checked: Core 5 - Base installation Gridlines E07-BS / N12-BE**
Installers Name: P J Carey's	
Date: 03/02/2022	
Inspection by: Dan Squire	**Weather: 9°C Dry**

	Item	**Comments**	
Sub-floor void		N/A	
Ventilation Inlets and Outlets		N/A	
Number Of Vents		N/A	
Materials used:		Membrane – Preprufe 300R Plus	
		Self-Adhesive Membrane ☒ Yes	Preformed Top hats ☐ Yes
		Double Sided Butyl Tape ☐ Yes	Preformed Corners ☐ Yes
		Others Please List: Bituthene LM. Bituthene Liquid membrane	
Installation Notes		**(brief description of area/plots and list of defects/repairs identified to the main membrane sheet, excluding detailing and joints)** MTS Ltd carried out a thorough visual inspection of the membrane, the membrane had been installed to a good standard. Preprufe 300R plus membrane has been lined across the core base area as noted and extends up the vertical face of the core walls to be able to join membrane at a later date. The membrane has a permanent back binding which is used to join the membrane together and is pressure rolled. In some areas an additional strip of Preprufe Tape LT has been added on top of the joints. A mix of Bituthene LM & Bituthene liquid membrane is applied to seal all pile caps. Site were carrying out their own ongoing inspections and cleaning off the membrane as the install progressed. All prep work including drying off the concrete floor and smoothing of the pile caps prior to the install were carried out well. The core area base was approx 25% when the inspection took place and all works were being carried out well and sufficiently.	

Type of Joint	Tape Joint ☒	Auto Weld ☐	Hand Weld ☐	Extrusion Weld ☐	
Jointing/Detailing Testing	☐ Air Lance (ASTM D4437)		☒ Probe Test (ASTM D4437)		
Laps, welds and detailing Ventilation Inlets & Outlets	Have all joints passed testing prior to surveyor leaving site?		☒ Yes	☐ No	☐ N/A
	Have all pipes passed testing prior to surveyor leaving site?		☐ Yes	☐ No	☒ N/A
	Have all stanchions/wind braces/columns passed testing prior to surveyor leaving site?		☐ Yes	☐ No	☒ N/A
	Have all piles and pile caps passed testing prior to surveyor leaving site?		☒ Yes	☐ No	☐ N/A
	Has all other detailing work passed inspection		☐ Yes	☐ No	☒ N/A
	(List any defects to detailing work and joints): During our inspection the following defects and repairs were carried out: No recorded defects. Have any defects identified above been satisfactorily rectified ☐ Yes ☐ No ☒ N/A The Area has passed inspection ☒ The Area has failed inspection and a corrective action sheet has been left with the contractor ☐ The Area is incomplete as detailed above ☐ Signed: **Dan Squire** Date: **03/02/2022**				

Area Inspected

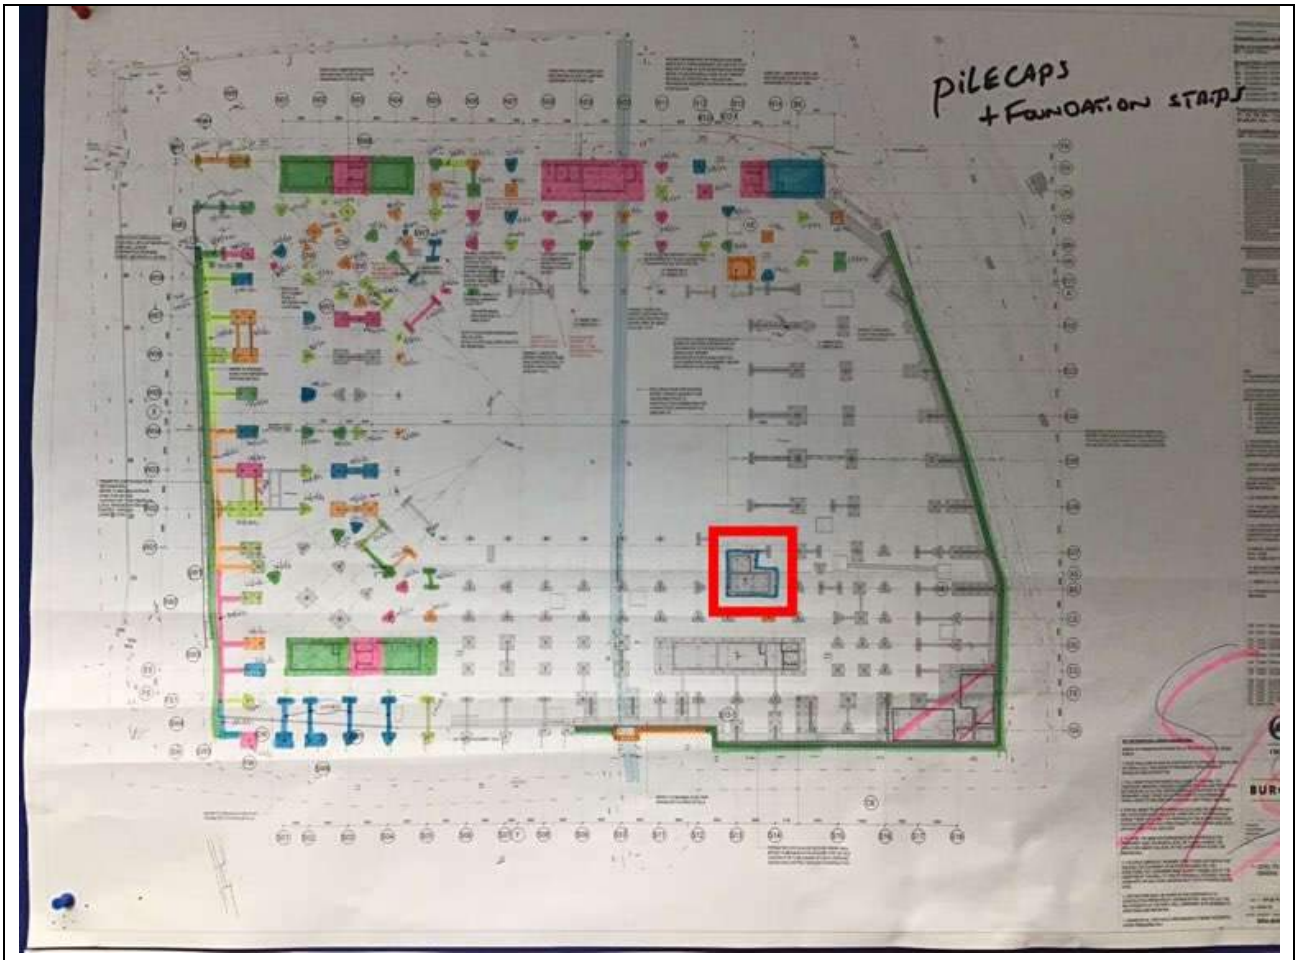


Photo **03/02/2022**



Core 5 base installation



Pile cap good prep work



Drying of the concrete prior to the install of membrane



Sealed pile cap using the Bituthene LM mixed with liquid membrane



Sealed membrane adhesive joint



Sealed and formed corner detailing using Preprufe 300R plus membrane and Preprufe tape LT

Test and Inspection Result 'PASS In FULL' to Both Areas

The areas have passed the inspection and a re-visit is not required.



Signed: Barrie Ackroyd Date: 3.2.2022

On Behalf of Membrane Testing Solutions Ltd

Francesca Gould / James Young
Buro Happold Limited
Camden Mill
Lower Bristol Road
Bath
BA2 3DQ
UK

T: +44 (0)1225 320 600
F: +44 (0)870 787 4148
Email: francesca.gould@burohappold.com
