
PCSA Programme

Etihad North Stand Development

	Line	Name	Start	Duration	Finish
+	1	**North Stand Development**	**16 Jan 23**	**180w 2d**	**30 Jun 26**
+	4	**North Stand Construction Programme**	**23 Oct 23**	**107w 1d**	**10 Nov 25**
+	8	**Steelwork Phase 1 New Core/Existing Mast Backstay F**	**22 Jan 24**	**11w 3d**	**12 Apr 24**
+	10	**Steelwork Phase 2**	**15 Apr 24**	**21w 1d**	**12 Sep 24**
+	23	**Main Cladding**	**25 Oct 24**	**25w**	**06 May 25**
+	33	**Commercial Building Construction Programme**	**19 Feb 24**	**95w 3d**	**18 Dec 25**
+	37	**Superstructure**	**30 Apr 24**	**36w**	**23 Jan 25**
+	38	**Envelope**	**04 Sep 24**	**49w**	**02 Sep 25**
+	45	**Hotel & City Square Construction Programme**	**11 Dec 23**	**133w 2d**	**30 Jun 26**
+	50	**Superstructure**	**21 Mar 24**	**84w 1d**	**27 Nov 25**
+	51	**Envelope**	**22 Aug 24**	**71w**	**05 Feb 26**
+	136	**Facade Mock-up Programme**	**29 Aug 23**	**46w**	**02 Aug 24**
+	137	Sub-contract pricing	29 Aug 23	2w	11 Sep 23
+	138	Prepare and isssue instruction / Order	12 Sep 23	2w	25 Sep 23
+	139	Desigm	26 Sep 23	4w	23 Oct 23
+	140	Design review	24 Oct 23	2w	06 Nov 23
+	141	Design ready for Material order for Sample Panel	07 Nov 23		07 Nov 23
+	142	Design ready for Suport Steel Structure	07 Nov 23		07 Nov 23
+	143	Provision of Materials Schedule to MCC LPA	07 Nov 23		07 Nov 23
+	144	**Material Procurement**	**07 Nov 23**	**14w**	**26 Feb 24**
+	145	Support structure (steel)	07 Nov 23	12w	12 Feb 24
+	146	Curtain Wall Galzing	07 Nov 23	12w	12 Feb 24
+	147	Precast Elelement - Brickwork & pier	07 Nov 23	14w	26 Feb 24
+	148	Spandrel panel	07 Nov 23	12w	12 Feb 24
+	149	Louvers	07 Nov 23	12w	12 Feb 24
+	150	**Construction**	**13 Feb 24**	**7w**	**04 Apr 24**
+	151	Erection of Support structure (steel)	13 Feb 24	1w 2d	21 Feb 24
+	152	**Sample panel**	**27 Feb 24**	**5w**	**04 Apr 24**
+	153	Precast Pier and brickwork installation	27 Feb 24	3d	29 Feb 24
+	154	Curtain wall installatin LOW	01 Mar 24	1w	07 Mar 24
+	155	Curtain wall installatin HIGH	08 Mar 24	1w	14 Mar 24
+	156	Spandrel panel instalaltion	15 Mar 24	3d	19 Mar 24
+	157	Louver installation	20 Mar 24	2d	21 Mar 24
+	158	Fins installation	22 Mar 24	2d	25 Mar 24
+	159	Soffit Installation	26 Mar 24	1w	03 Apr 24
+	160	Completion of sample panel	04 Apr 24		04 Apr 24
+	161	**Inspections**	**04 Apr 24**	**17w**	**02 Aug 24**
+	162	MCC LPA inspection of Sample panel	04 Apr 24	2w	17 Apr 24
+	163	Mock-up panel retained	18 Apr 24	15w	02 Aug 24

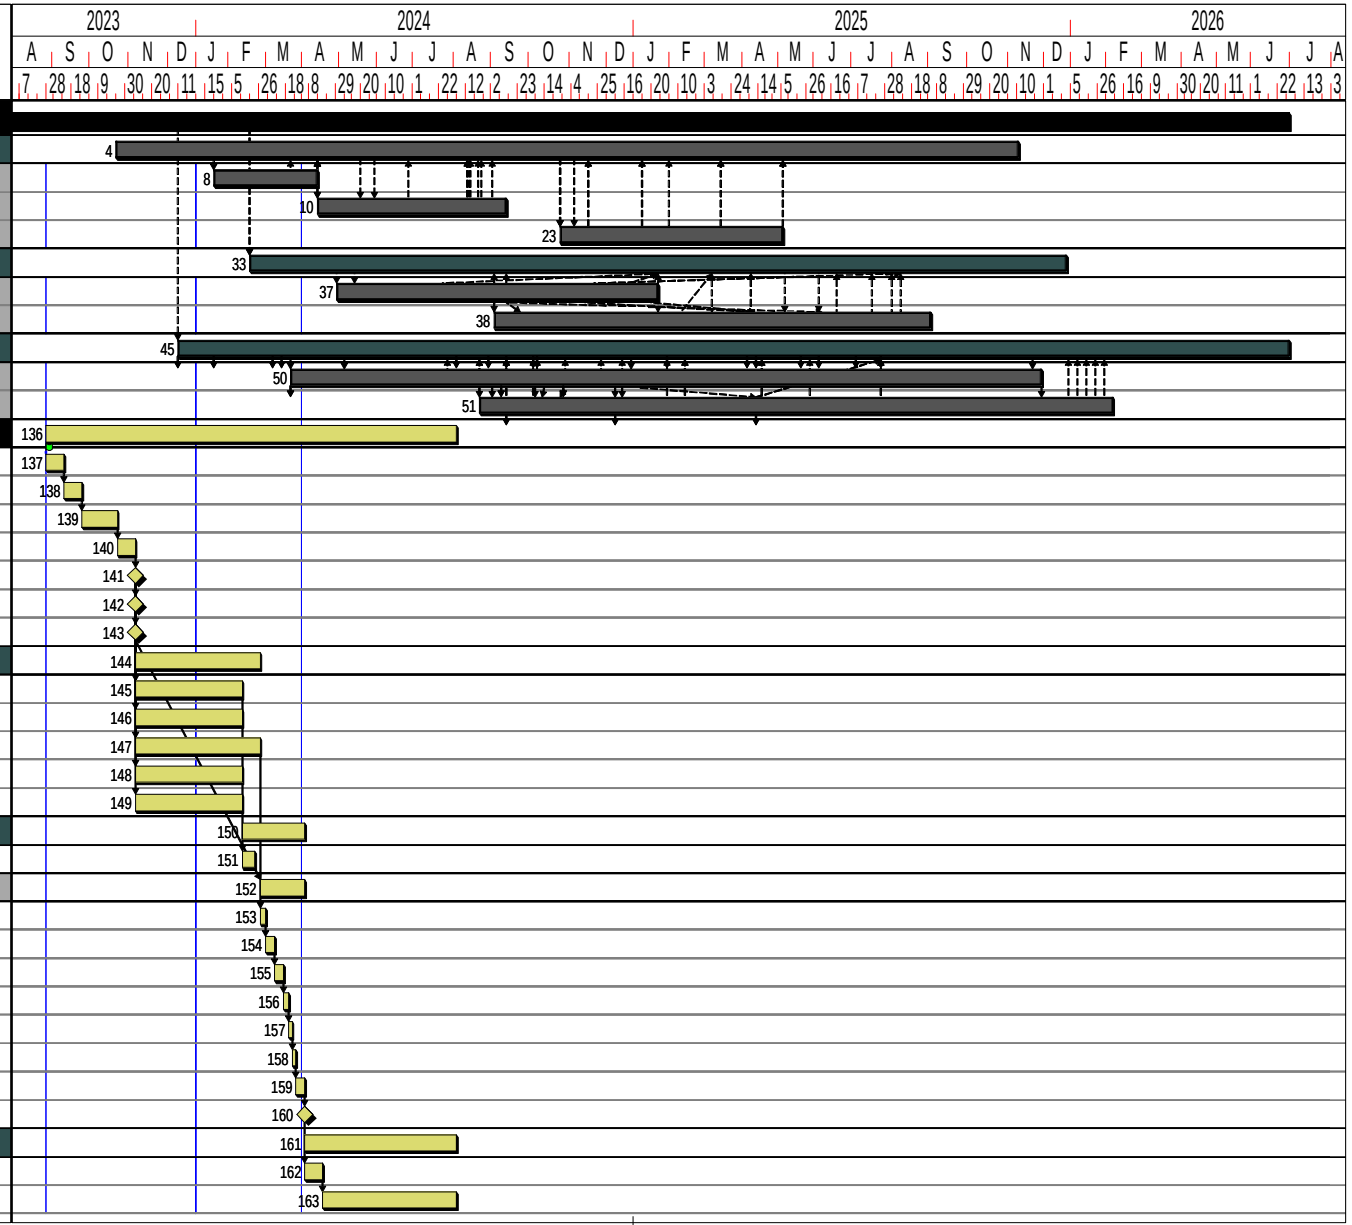

Drawn by: Sachin Varghese | Prog No: JSSL-NSH-TP-01 | Notes:

Checked by: | Revision/Status: 00

Date Issued: 25/08/2023 | Date Revised:

Facade Mock-up Programme

File Name: C:\Users\vargheses\OneDrive - John Sisk and Son (Holdings) Ltd\Desktop\SISK Projects\North Stand\Tidy\NS Development - Tender Programme (01.08.23) UPDATED PCSA progress 22.08.23.pp

John Sisk & Son Ltd.
Unit 4, Ibis Court, Centre Park,
Warrington, WA1 1RL
Tel: 0161 888 3400 Fax: 0161 888 3401
