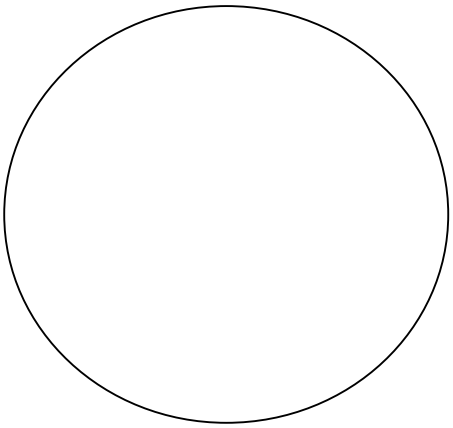
QA Form - Manholes

Installation of Manhole			Sheet No:	
Project	C376 WITHINGTON CDC		**Date:**	28/04/2025
Location: **As built coordinates:** **Cover Level:**	SW5 383789.086 391995.088 31.610	**Drawing No:**	22182-CCS-WCH006-XX-DR-S-93000	
Manhole No: **Invert:**	SWMH – S5 31.610	**Type:** **(circle as appropriate)**	FOUL/SURFACE WATER/COMBINED	
Inverts and Diameter of pipes: **Chamber Details:**	Upstream: attenuation tank – 31.625 Dia: NA Downstream: existing outfall 31.560 Dia: Inlet 1: Dia: Inlet 2: Dia: Inlet 3: Dia: Inlet 4: Dia: Inlet 5: Dia: Dia. Size: 1500mm Overall depth: 1.140mm Cover Depth: 100mm Biscuit Depth: 150mm Reducing Slab:	**Sketch:**  Position of step irons/fittings, orientation of cover/slab and branches (including backdrops) to be detailed.		

WORK TO BE INSPECTED	Accepted Yes/ No or N/a	Comments	MW Construction Eng/QA Signed as Checked:-
Setting out to drawing	Yes		[redacted]
Trench excavation supported	Yes	Stepped as required	
Installation of concrete to channel	NA	Hydro break manhole	

MURRAYWOOD CONSTRUCTION LTD	**QA Form - Manholes**

Installation of drainage channel/first manhole ring	Yes	Hydro break manhole	[redacted]	
MWC Signature confirming invert/positioning check	[redacted]		**Date**	
Client Signature confirming invert/positioning check			**Date**	

WORK TO BE INSPECTED	**Accepted Yes/ No or N/A**	**Comments**	**MW Construction Eng/QA Signed as Checked:-**
Installation of manhole rings to required levels	YES	Depths and No's of rings: 1x 500x1500, 1 x 750x1500	[redacted]
Installation of dropshafts/inlets above manhole invert	YES		
Manhole Surround	YES	Details: Concrete	
Backfilling to manhole to required level and layers as instructed in spec	YES		
Biscuit Installation	YES	Type: PCC	
Benching/Water proofing to Manhole	YES		
Installation of Step Irons	YES	Type & Numbers: Plastic 5 no	
Brickwork		No of courses: 3 course	
Lid and Frame	YES	Cover Type: D400	
Client Signature confirming Handover of Manhole:-			**Date**

QA Form - Manholes

MWC Signature confirming Handover of Manhole:-	[redacted]	**Date**	25/06/2025

Photographs.

