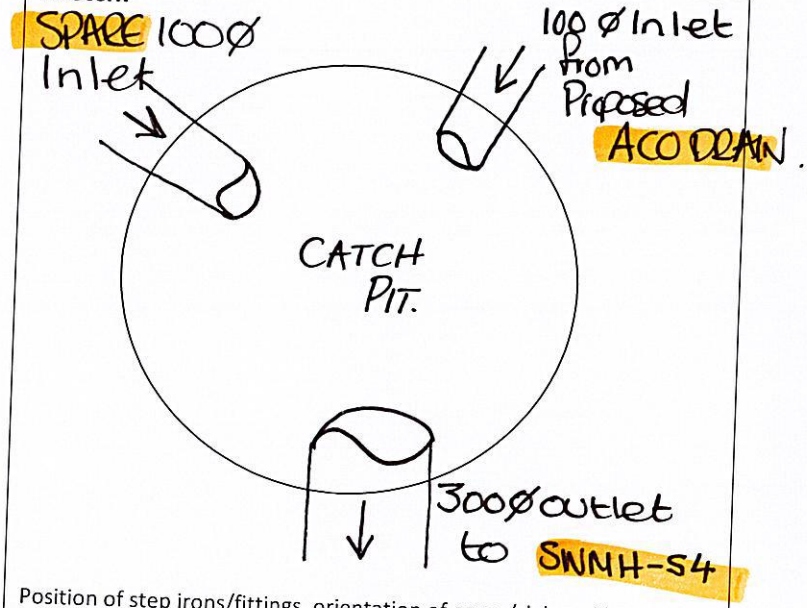
MURRAYWOOD CONSTRUCTION LTD

QA Form - Manholes

Installation of Manhole

Project	C376 WITHINGTON CDC	**Sheet No:**	7.
		Date:	28/04/2025
Location: **As built coordinates:** **Cover Level:**	SW2 383759.959 391986.989 32.830	**Drawing No:**	22182-CCS-WCH006-XX-DR-S-93000
Manhole No: **Invert:**	SW2 31.766 BAM 81.779. 500 MM SUMP = 31.266	**Type: (circle as appropriate)**	FOUL/SURFACE WATER/COMBINED
Inverts and Diameter of pipes:	Upstream: END OF RUN Dia: NA Downstream: 31.766 Dia: 300mm Inlet 1: 31.966 Dia: 100mm Inlet 2: 31.966 Dia: 100mm Inlet 3: Dia: Inlet 4: Dia: Inlet 5: Dia:	**Sketch:**	 Position of step irons/fittings, orientation of cover/slab and branches (including backdrops) to be detailed.
Chamber Details:	Dia. Size: 1500mm Overall depth: 1566mm Cover Depth: 100mm Biscuit Depth: 150mm Reducing Slab:		

WORK TO BE INSPECTED	Accepted Yes/ No or N/a	Comments	MW Construction Eng/QA Signed as Checked:-
Setting out to drawing	Yes	Chamber relocated. SWMH S3 cancelled. IL on drawing incorrect. Pipe laid to grade.	[redacted]
Trench excavation supported	Yes	Stepped as required	
Installation of concrete to channel	NA	Catch Pit	
Installation of drainage channel/first manhole ring	Yes	Catch Pit	

MURRAYWOOD CONSTRUCTION LTD

QA Form - Manholes

MWC Signature confirming invert/positioning check	[redacted]	**Date**	
Client Signature confirming invert/positioning check		**Date**	26/6/25

WORK TO BE INSPECTED	**Accepted Yes/ No or N/A**	**Comments**	**MW Construction Eng/QA Signed as Checked:-**
Installation of manhole rings to required levels	YES	Depths and No's of rings: 2x 500x1500, 1 x 230x1500	[redacted]
Installation of dropshafts/inlets above manhole invert	YES		
Manhole Surround	YES	Details: Concrete	
Backfilling to manhole to required level and layers as instructed in spec	YES		
Biscuit Installation	YES	Type: PCC	
Benching/Water proofing to Manhole	YES		
Installation of Step Irons	YES	Type & Numbers:	
Brickwork		No of courses:	
Lid and Frame	YES	Cover Type: D400 VENTED 600X1200	
Client Signature confirming Handover of Manhole:-		**Date**	

MURRAYWOOD CONSTRUCTION LTD	QA Form - Manholes

MWC Signature confirming Handover of Manhole:-	[redacted]	Date	25/06/2025


MURRAYWOOD CONSTRUCTION LTD

QA Form - Manholes



MURRAYWOOD CONSTRUCTION LTD

QA Form - Manholes

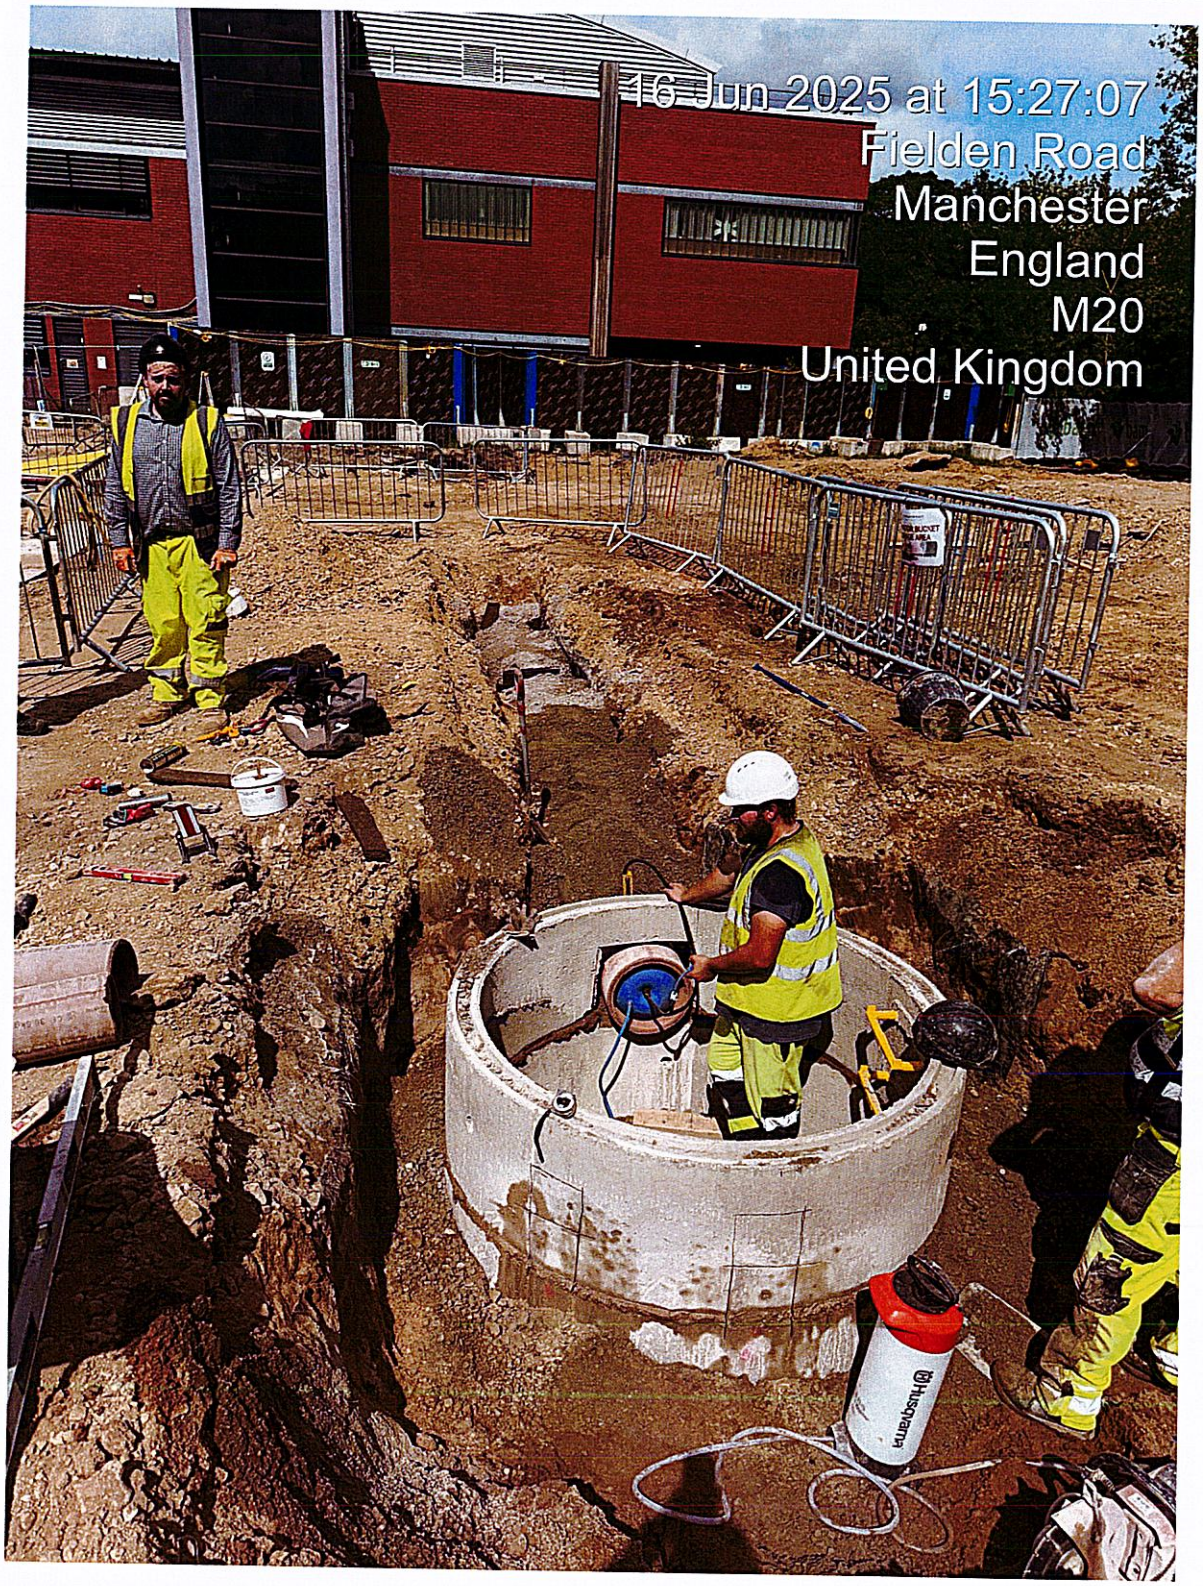

MURRAYWOOD CONSTRUCTION LTD	**QA Form - Manholes**

