
Bayerische Versorgungskammer

Hines

Manchester Royal Exchange Facade Restoration Works

TanRo MULTIBUILD

Line	Name	Duration	Start	Finish
1	**Pre-Construction Elements**	24w	06/07/2026	04/01/2027
2	**Construction Activities**	76w 4d	01/09/2026	24/03/2028
3	**MCC Highways 2026 Embargo Dates**	7w	10/11/2026	11/01/2027
4	2026 Christmas Market	7w	10/11/2026	11/01/2027
5	2026 MCC Highways Embargo	7w	10/11/2026	11/01/2027
6	**MCC Highways 2027 Embargo Dates**	7w	09/11/2027	10/01/2028
7	2027 Christmas Market	7w	09/11/2027	10/01/2028
8	2027 MCC Highways Embargo	7w	09/11/2027	10/01/2028
9	**Street Level Scaffold Amendments**	10w 4d	01/09/2026	13/11/2026
10	Scaffolder Mobilisation	4d	01/09/2026	04/09/2026
11	Implement Loading Bay Barriers / Exclusion	1w 2d	01/09/2026	09/09/2026
12	Exchange Street	4w	07/09/2026	02/10/2026
13	Market Street	4w	21/09/2026	16/10/2026
14	Cross Street	4w	05/10/2026	30/10/2026
15	**Low Level Wrap - Ribbon**	6w	05/10/2026	13/11/2026
16	Exchange Street	2w	05/10/2026	16/10/2026
17	Market Street	2w	19/10/2026	30/10/2026
18	Cross St	2w	02/11/2026	13/11/2026
19	**Scaffolding**	70w	19/10/2026	24/03/2028
20	**Cross St**	51w	19/10/2026	29/10/2027
21	Implement Street Level Loading Arrangements	2w	19/10/2026	30/10/2026
22	Erection of Main Scaffold	13w 2.5d	26/10/2026	10/02/2027
23	Scaffold Wrap	2w	08/02/2027	19/02/2027
24	HL Amendments for Leadwork	1w	14/06/2027	18/06/2027
25	Remove Wrap	2w	19/07/2027	30/07/2027
26	Main Scaffold Dismantle	6w	02/08/2027	13/09/2027
27	Low Level adjustments for Roof Work	1w	06/09/2027	10/09/2027
28	Street Level Mewp Access	7w	13/09/2027	29/10/2027
29	**Market Street**	69w	26/10/2026	24/03/2028
30	Implement Street Level Loading Arrangements	2w	26/10/2026	06/11/2026
31	Erection of Main Scaffold	7w 2.5d	02/11/2026	06/01/2027
32	Scaffold Wrap	2w	04/01/2027	15/01/2027
33	HL Amendments for Leadwork	1w	22/03/2027	26/03/2027
34	Remove Wrap	1w 4d	31/08/2027	10/09/2027
35	Main Scaffold Dismantle	6w	13/09/2027	22/10/2027
36	Low Level adjustments for Roof Work	1w	25/10/2027	29/10/2027
37	Dismantle Scaffold Gantry	2w	28/02/2028	10/03/2028
38	Street Level Access	4w	28/02/2028	24/03/2028
39	**Exchange Street**	56w	04/01/2027	18/02/2028
40	Implement Street Level Loading Arrangements	1w	04/01/2027	08/01/2027
41	Erection of Main Scaffold	13w 2.5d	04/01/2027	07/04/2027
42	Scaffold Wrap	1w 4d	05/04/2027	15/04/2027
43	HL Amendments for Leadwork	1w	27/08/2027	03/09/2027
44	Remove Wrap	2w	13/09/2027	24/09/2027
45	Dismantle Scaffold	6w	20/09/2027	29/10/2027
46	Low Level adjustments for Roof Work	1w	25/10/2027	29/10/2027
47	Dismantle Scaffold Gantry	2w	10/01/2028	21/01/2028
48	Street Level Access	4w	24/01/2028	18/02/2028
49	**Tower**	24w 1d	29/03/2027	20/09/2027
50	Erection of Main Scaffold	6w	29/03/2027	12/05/2027
51	Scaffold Wrap	2w	10/05/2027	21/05/2027
52	Remove Wrap	2w	26/07/2027	06/08/2027
53	Main Scaffold Dismantle	7w	02/08/2027	20/09/2027
54	**Old Bank St**	36w	15/02/2027	29/10/2027
55	Erection of Main Scaffold inc Monarflex	6w	15/02/2027	26/03/2027
56	HL Amendments for Leadwork	1w	07/06/2027	11/06/2027
57	Main Scaffold Dismantle	5w	14/06/2027	16/07/2027
58	Low Level adjustments for Roof Work	1w	16/08/2027	20/08/2027
59	Street Level Access	4w	04/10/2027	29/10/2027
60	**Banner Durations**	37w	04/01/2027	24/09/2027
61	Market St	35w	04/01/2027	10/09/2027
62	Cross St	24w 1d	08/02/2027	30/07/2027
63	Exchange St	23w	12/04/2027	24/09/2027
64	Tower	12w 4d	10/05/2027	06/08/2027
65	**Main Elevation Works**	69w	26/10/2026	24/03/2028

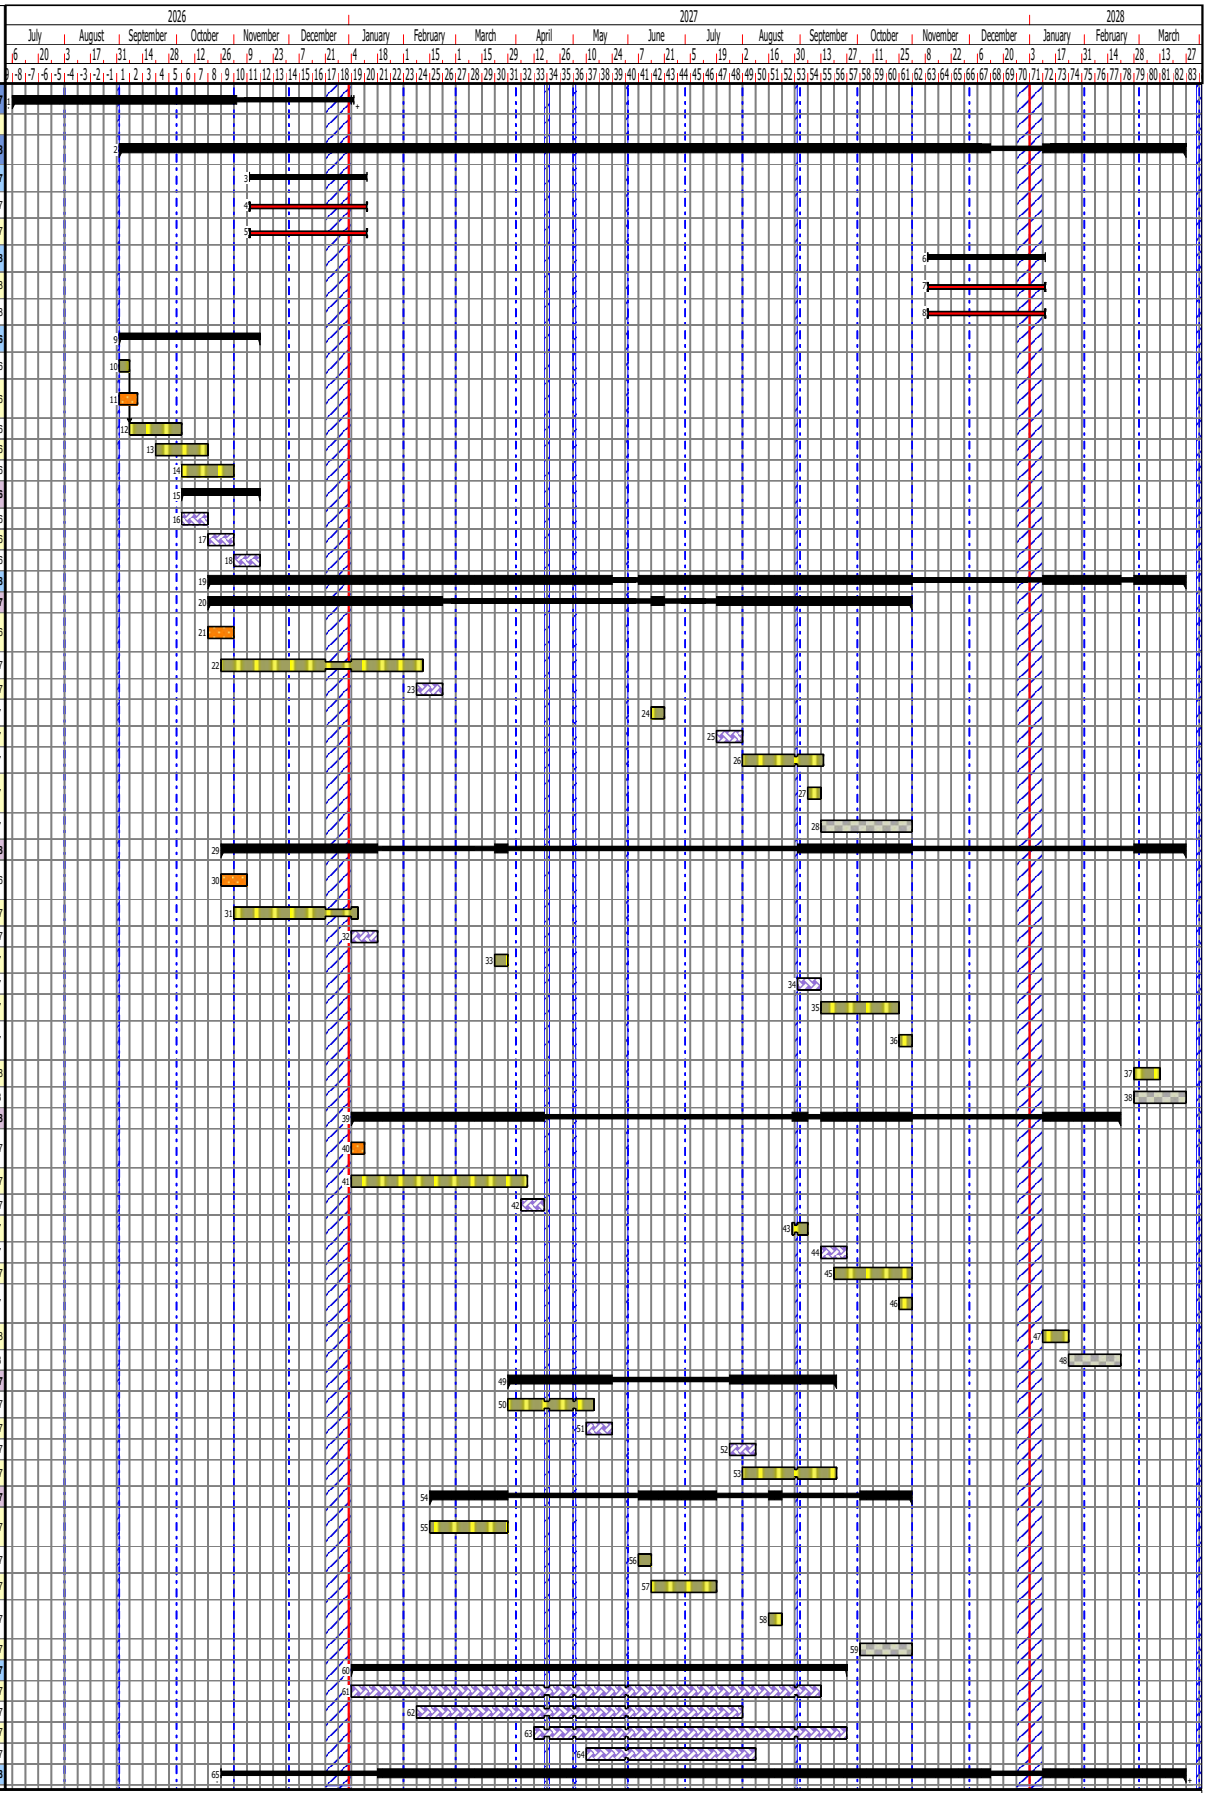

Trades Contractor,Procurement Stages,Design Discipline

MEWP Access | Design Info | TanRo | Craven Scaffolding | Arts & Banners - Scaffold Wrap

Drawn by: Mike Quinn	Prog Ref: Draft Tender Program in development	Revision No. Rev 1A	Date: 27.07.2026
