Kestrel Thermal Frame Single AFT Commercial Door
1no Required - Viewed Externally
Not PAS 24 / SBD
U Value: 1.8W/m2K

Opens Inwards - 1000mm Clear Opening
Left Hand Hung

Weather Bar To Head As Per Kestrel Manual

Concealed in Head Hold Open Door Closer
SSS 32mm Diameter Cranked D Handles @ 300mm Centres Both Sides (Contrasting Colour)
Hook Lock c/w Euro Profile Key / Key Cylinder & SAA Escutcheons


Colour is Ral 9005 Matt - Jet Black


Glazing:
6.8mm Laminated
16mm Black Thermal Spacer Bar, 90% Argon Filled Cavity
6mm Soft Coat 1.0 Toughened
2no Rows of 50mm Opaque Manifestation Circles @ 100mm Centres

Manufacture Size: 1215mm x 2100mm
Structural Opening Size: 1230mm x 2110mm


Required For Supply & Install:

A-A

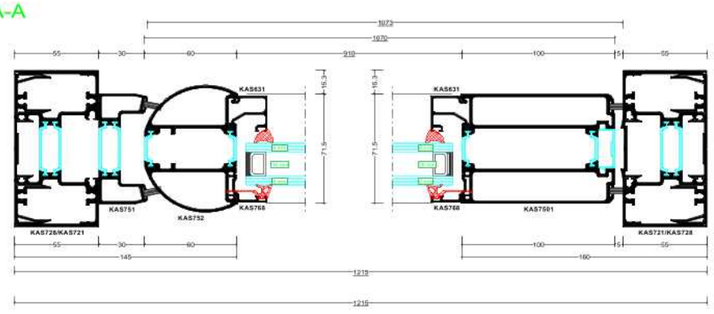

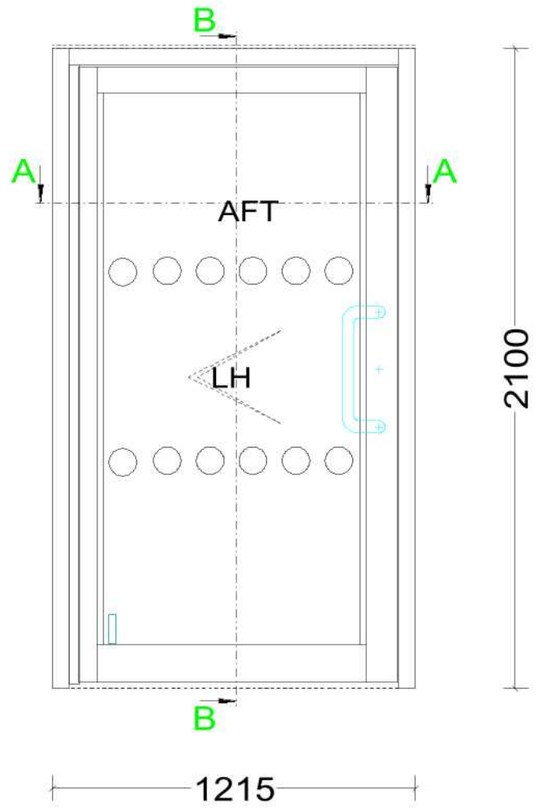

B-B

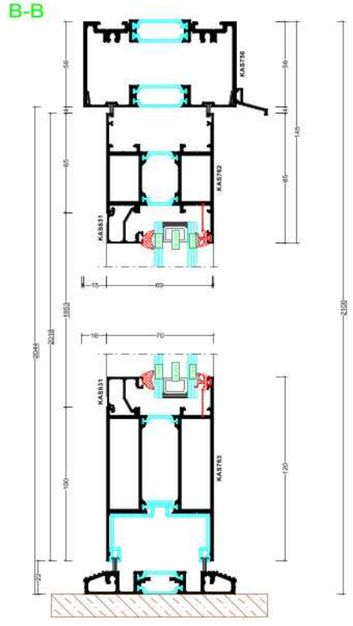

PLEASE NOTE STANDARD LEAD TIME IS 6-8 WEEKS FROM FINAL APPROVAL OF DRAWINGS (STANDARD PRODUCTS)

PLEASE NOTE UNTIL WE RECEIVE FINAL APPROVAL OF DRAWINGS WE ARE UNABLE TO PROCURE ANY MATERIALS

THIS DRAWING IS COPYRIGHT OF CB SOLUTIONS & MUST NOT BE COPIED OR REPRODUCED WITHOUT WRITTEN PERMISSION

CBSolutions

Halifax Approach
Eastfield Park New Cut
Lissett
YO25 8PT

Tel: 01262 469130
Email: info@cbsol.co.uk

APPROVAL STATUS :-
[X] STATUS A' DRAWING/DESIGN APPROVED WITH NO FURTHER COMMENTS PROCEED WITH PROCESSING & MANUFACTURE
[ ] STATUS B' DRAWING/DESIGN APPROVED SUBJECT TO COMMENTS AMEND TO COMMENTS, PROCEED WITH MANUFACTURE
[ ] STATUS C' DRAWING/DESIGN NOT APPROVED AMEND TO COMMENTS, RE-SUBMIT FOR APPROVAL

AMENDMENTS

REV	DATE	AMENDMENTS	INTL
P02	02-03-2026	Amended Sizes	CIP

STATUS: Construction
A1

CLIENT: Premier Modular Limited

PROJECT TITLE: YIF Manchester OMYOP

DRAWING TITLE: DT1 - DE-03

Visions & Values
C : OMMITMENT
B : ELIEVE
S : USTAINABILITY
O : PPORTUNITY
L : EARNING
www.cbsol.co.uk

DRAWN BY: Chris Page

DATE: 16-03-2026

CONTRACT NUMBER: SO0029995

DRAWING NUMBER: 29995-CIP-003
REV.: C01

Scale: 1:4
